

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Page	1 of 6

Eagle Mountain – Woodfibre Gas Pipeline Project

BCER Waste Discharge Permit Weekly Report

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Page	2 of 6

Contents

Preamble..... 3

Introduction 3

 Sampling Methodology..... 3

Summary-BC Rail Site 5

 Site Activities 5

 Discharge from Water Treatment Plant..... 5

 Receiving Environment Monitoring-Squamish River 5

Summary-Woodfibre Site 6

 Site Activities 6

 Exceedances..... 6

 Discharge from Water Treatment Plant..... 6

 Receiving Environment Monitoring-East Creek..... 6

Appendix A: BC Rail Point of Discharge from Water Treatment System Documentation

Appendix B: BC Rail Receiving Environment Documentation

Appendix C: Woodfibre Point of Discharge from Water Treatment System Documentation

Appendix D: Woodfibre Receiving Environment Documentation

Appendix E: Lab Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Page	3 of 6

Preamble

This weekly report for the British Columbia Energy Regulator (BCER) Waste Discharge Permit (BCER number PE-110163) for the FortisBC Eagle Mountain – Woodfibre Gas Pipeline (EGP) Project includes the results of water quality monitoring and sampling of the receiving environments (upstream and downstream) and points of discharge during the reporting period.

FortisBC has retained Hatfield Consultants as the Qualified Professional to implement and oversee the monitoring and sampling programs. The data represented below, including laboratory reported exceedances, represent conditions measured from final discharge points and the associated receiving environments, as required under the Waste Discharge Permit.

Introduction

The results provided in this document have been submitted to BCER by FortisBC as per the requirements listed in Section 4.2 of the Waste Discharge Permit PE-110163:

The Permittee shall summarize the results of the discharge and receiving environment compliance sampling and monitoring program in a report that shall be submitted weekly over the term of this permit. The sampling and monitoring results shall be suitably tabulated and include comparison to the respective British Columbia Approved and Working Water Quality Guidelines for Freshwater & Marine Aquatic Life, as published by the Ministry of Environment & Climate Change Strategy. Any exceedance of regulatory guidelines shall be clearly highlighted, and any missed sampling events/missing data shall be identified with an explanation provided. Reporting frequency may be reduced upon a history of compliance and by written confirmation from the BCER. These reports shall be submitted to Waste.Management@bc-er.ca. A copy of the reports shall be provided to each First Nation consulted with regarding the subject permit, and also made publicly available on the FortisBC Eagle Mountain-Woodfibre Gas Pipeline Project | Talking Energy webpage.

Sampling Methodology

The monitoring and sampling has been carried out in accordance with the procedures described in the most recent edition of the “British Columbia Field Sampling Manual” using field equipment and laboratory samples to meet daily and real-time requirements for the Waste Discharge Permit.

In the receiving environments, real-time and daily readings were monitored at the same time with one piece of equipment, allowing real-time daily readings. Visible sheen was monitored through visual inspections during times of discharge or sampling.

At the point of discharges, parameters are monitored using field equipment and water quality sondes, as well as discrete weekly water quality sampling events for laboratory analyses. Table 1 and Table 2 below describe this monitoring.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

June 1 to
June 7, 2026

Report #

115

Page

4 of 6

Table 1. Monitor Details for the Point of Discharge from the Water Treatment System-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily (or per batch)	DO	Monitoring using YSI ProDSS
	ORP	Monitoring using YSI ProDSS
	Salinity	Monitoring using YSI ProDSS
Real-time (or per batch)	pH	Monitoring using GF Dryloc pH Series NPT
	Temperature	Monitoring using LevelPro PT100 Temperature and Signet 2350 Temp sensor
	NTU	Monitoring using Observer NEP9504GPI
	Electrical Conductivity	Monitoring using ProCon C450
Weekly (or per batch) Lab Samples	List prescribed in permit	Lab samples*

*indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.

Table 2. Monitor Details for the Receiving Environment (upstream and downstream)-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily	DO	Monitoring using Sonde- AquaTROLL 600 datalogger
	ORP	Monitoring using Sonde- AquaTROLL 600 datalogger
	Salinity	Monitoring using Sonde- AquaTROLL 600 datalogger
Real-time	pH	Monitoring using Sonde- AquaTROLL 600 datalogger
	Temperature	Monitoring using Sonde- AquaTROLL 600 datalogger
	NTU	Monitoring using Sonde- AquaTROLL 600 datalogger
	Electrical Conductivity	Monitoring using Sonde- AquaTROLL 600 datalogger
Weekly Lab Samples	List prescribed in permit	Lab samples*

*indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

June 1 to
June 7, 2026

Report #

115

Page

5 of 6

Summary-BC Rail Site

Site Activities

- The soft ground tunnel has been completed and FortisBC is in the process of demobilizing equipment and preparations for pipe stringing.

Discharge from Water Treatment Plant

- There was no discharges this week from the BC Rail Site.

Receiving Environment Monitoring-Squamish River

Tables 3 and 4 below provide information on water quality monitoring. Lab sampling has been put on hold with permission from BCER as there are no discharges. Appendix B includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit and confirmed by BCER, with additional oversight by the QP.

Table 3. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Upstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

Table 4. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Downstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

**Data gaps in available in-situ continuous monitoring data, included:

- SQU US
 - 2026/06/01: temperature, specific conductivity, dissolved oxygen, and salinity data were missing at 20:00.
- SQU DS
 - No data gaps were observed.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

June 1 to
June 7, 2026

Report #

115

Page

6 of 6

Summary-Woodfibre Site

Site Activities

- Weekly upstream, downstream, and end of pipe water quality sampling performed by the QP.
- On-going tunnelling at WLNG and grouting works to mitigate water ingress.

Exceedances

No reportable exceedances were identified during the June 1 to June 7, 2026, reporting period.

Discharge from Water Treatment Plant

Appendix C includes volume information and real-time/field samples from the discharge.

Receiving Environment Monitoring-East Creek

Tables 5 and 6 below provide information on water quality monitoring. Appendix D includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit with additional oversight by the QP.

Table 5. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Upstream	2026-06-02	Yes *	Full set of results are provided in Appendix D.**

Table 6. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Downstream	2026-06-02	Yes *	Full set of results are provided in Appendix D.**

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

**Data gaps in available in-situ continuous monitoring data, included:

- EAS US
 - No data gaps were observed.
- EAS DS
 - No data gaps were observed.

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix A	A-1

Appendix A:
BCR Site Point of Discharge from Water
Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix A	A-2

BCR Site Batch Sample Analysis
No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix A	A-3

BCR Site WTP Discharge Field Notes and Logs No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix B	B-1

Appendix B:
BCR Site Receiving Environment Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix B	B-2

BCR Site Receiving Environment Sample Analysis No Lab Samples

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix B	B-3

BCR Site Receiving Environment
Field Notes and Logs

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-01 00:00:00	9.72	29.61	575.48	7.30	10.38	10.79	0.01
SQU-DS	2026-06-01 00:15:00	9.66	29.52	574.43	7.32	10.40	10.35	0.01
SQU-DS	2026-06-01 00:30:00	9.59	29.31	575.03	7.30	10.40	10.93	0.01
SQU-DS	2026-06-01 00:45:00	9.54	29.23	574.58	7.31	10.41	10.11	0.01
SQU-DS	2026-06-01 01:00:00	9.48	29.05	574.69	7.31	10.43	10.42	0.01
SQU-DS	2026-06-01 01:15:00	9.42	28.91	575.02	7.30	10.43	9.72	0.01
SQU-DS	2026-06-01 01:30:00	9.35	28.98	576.17	7.29	10.46	10.09	0.01
SQU-DS	2026-06-01 01:45:00	9.30	28.78	575.59	7.30	10.46	10.99	0.01
SQU-DS	2026-06-01 02:00:00	9.24	28.90	574.85	7.31	10.47	11.89	0.01
SQU-DS	2026-06-01 02:15:00	9.18	28.49	575.71	7.30	10.49	10.21	0.01
SQU-DS	2026-06-01 02:30:00	9.12	28.80	577.19	7.29	10.50	11.34	0.01
SQU-DS	2026-06-01 02:45:00	9.06	28.48	576.93	7.30	10.52	10.61	0.01
SQU-DS	2026-06-01 03:00:00	9.01	28.47	577.09	7.31	10.53	11.33	0.01
SQU-DS	2026-06-01 03:15:00	8.93	28.38	576.74	7.32	10.56	8.82	0.01
SQU-DS	2026-06-01 03:30:00	8.88	28.31	577.07	7.31	10.56	9.43	0.01
SQU-DS	2026-06-01 03:45:00	8.82	28.28	577.23	7.31	10.58	9.80	0.01
SQU-DS	2026-06-01 04:00:00	8.76	28.19	577.06	7.31	10.60	10.48	0.01
SQU-DS	2026-06-01 04:15:00	8.72	28.62	576.30	7.32	10.60	9.25	0.01
SQU-DS	2026-06-01 04:30:00	8.67	28.48	575.89	7.32	10.62	8.47	0.01
SQU-DS	2026-06-01 04:45:00	8.61	28.14	576.21	7.31	10.63	9.64	0.01
SQU-DS	2026-06-01 05:00:00	8.57	28.30	575.60	7.32	10.64	9.85	0.01
SQU-DS	2026-06-01 05:15:00	8.53	28.11	574.93	7.33	10.65	8.46	0.01
SQU-DS	2026-06-01 05:30:00	8.49	28.04	575.02	7.33	10.65	8.36	0.01
SQU-DS	2026-06-01 05:45:00	8.44	27.97	576.46	7.31	10.68	11.13	0.01
SQU-DS	2026-06-01 06:00:00	8.42	28.04	575.43	7.33	10.69	8.08	0.01
SQU-DS	2026-06-01 06:15:00	8.39	28.09	574.62	7.34	10.69	8.60	0.01
SQU-DS	2026-06-01 06:30:00	8.35	28.01	574.78	7.33	10.71	9.07	0.01
SQU-DS	2026-06-01 06:45:00	8.34	28.02	575.32	7.32	10.72	8.42	0.01
SQU-DS	2026-06-01 07:00:00	8.34	27.99	574.68	7.32	10.72	7.98	0.01
SQU-DS	2026-06-01 07:15:00	8.33	28.05	573.62	7.33	10.75	8.61	0.01
SQU-DS	2026-06-01 07:30:00	8.32	28.07	575.01	7.30	10.75	9.02	0.01
SQU-DS	2026-06-01 07:45:00	8.33	27.92	573.45	7.32	10.77	8.14	0.01
SQU-DS	2026-06-01 08:00:00	8.34	27.83	573.98	7.31	10.78	10.24	0.01
SQU-DS	2026-06-01 08:15:00	8.37	27.86	574.93	7.29	10.79	10.33	0.01
SQU-DS	2026-06-01 08:30:00	8.39	28.04	572.81	7.32	10.79	8.82	0.01
SQU-DS	2026-06-01 08:45:00	8.44	28.24	572.08	7.32	10.80	15.32	0.01
SQU-DS	2026-06-01 09:00:00	8.50	28.33	573.81	7.29	10.80	18.08	0.01
SQU-DS	2026-06-01 09:15:00	8.57	28.45	571.65	7.32	10.80	14.88	0.01
SQU-DS	2026-06-01 09:30:00	8.63	28.71	570.59	7.33	10.80	14.42	0.01
SQU-DS	2026-06-01 09:45:00	8.70	28.62	570.40	7.33	10.80	13.29	0.01
SQU-DS	2026-06-01 10:00:00	8.76	28.66	569.77	7.34	10.80	12.49	0.01
SQU-DS	2026-06-01 10:15:00	8.83	28.69	569.30	7.33	10.81	13.78	0.01
SQU-DS	2026-06-01 10:30:00	8.91	28.45	569.97	7.31	10.81	13.36	0.01
SQU-DS	2026-06-01 10:45:00	8.98	28.29	568.77	7.33	10.79	11.66	0.01
SQU-DS	2026-06-01 11:00:00	9.07	28.30	568.56	7.33	10.78	14.91	0.01
SQU-DS	2026-06-01 11:15:00	9.14	28.33	568.54	7.32	10.80	12.99	0.01
SQU-DS	2026-06-01 11:30:00	9.22	28.26	568.03	7.33	10.79	12.38	0.01
SQU-DS	2026-06-01 11:45:00	9.31	28.15	567.92	7.32	10.78	12.46	0.01
SQU-DS	2026-06-01 12:00:00	9.39	28.17	566.18	7.35	10.76	12.64	0.01
SQU-DS	2026-06-01 12:15:00	9.48	28.24	567.39	7.33	10.76	14.38	0.01
SQU-DS	2026-06-01 12:30:00	9.57	28.30	567.00	7.34	10.76	12.47	0.01
SQU-DS	2026-06-01 12:45:00	9.65	28.21	565.39	7.37	10.75	11.48	0.01
SQU-DS	2026-06-01 13:00:00	9.73	28.25	566.99	7.34	10.74	12.36	0.01
SQU-DS	2026-06-01 13:15:00	9.81	28.24	566.51	7.34	10.73	10.79	0.01
SQU-DS	2026-06-01 13:30:00	9.90	28.24	565.25	7.36	10.72	11.40	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-01 13:45:00	9.97	28.25	566.02	7.35	10.72	11.00	0.01
SQU-DS	2026-06-01 14:00:00	10.04	28.43	565.71	7.35	10.70	11.13	0.01
SQU-DS	2026-06-01 14:15:00	10.13	28.31	566.78	7.33	10.69	13.51	0.01
SQU-DS	2026-06-01 14:30:00	10.21	28.24	566.35	7.33	10.68	10.47	0.01
SQU-DS	2026-06-01 14:45:00	10.29	28.18	564.98	7.35	10.67	11.56	0.01
SQU-DS	2026-06-01 15:00:00	10.36	28.13	565.04	7.35	10.65	10.05	0.01
SQU-DS	2026-06-01 15:15:00	10.40	28.14	566.12	7.33	10.64	11.73	0.01
SQU-DS	2026-06-01 15:30:00	10.47	28.27	565.15	7.34	10.63	10.73	0.01
SQU-DS	2026-06-01 15:45:00	10.53	28.44	567.03	7.31	10.62	11.25	0.01
SQU-DS	2026-06-01 16:00:00	10.58	28.23	564.68	7.35	10.61	10.66	0.01
SQU-DS	2026-06-01 16:15:00	10.61	28.26	565.17	7.35	10.59	10.44	0.01
SQU-DS	2026-06-01 16:30:00	10.66	28.24	565.66	7.34	10.57	10.49	0.01
SQU-DS	2026-06-01 16:45:00	10.72	28.46	565.49	7.36	10.55	10.34	0.01
SQU-DS	2026-06-01 17:00:00	10.75	28.35	566.90	7.34	10.55	10.27	0.01
SQU-DS	2026-06-01 17:15:00	10.80	28.32	565.22	7.37	10.53	10.32	0.01
SQU-DS	2026-06-01 17:30:00	10.84	28.31	567.36	7.33	10.52	9.87	0.01
SQU-DS	2026-06-01 17:45:00	10.87	28.30	567.34	7.34	10.50	9.42	0.01
SQU-DS	2026-06-01 18:00:00	10.89	28.37	565.36	7.38	10.48	11.33	0.01
SQU-DS	2026-06-01 18:15:00	10.92	28.24	566.75	7.36	10.47	10.86	0.01
SQU-DS	2026-06-01 18:30:00	10.94	28.34	567.13	7.36	10.46	9.54	0.01
SQU-DS	2026-06-01 18:45:00	10.95	28.40	568.10	7.35	10.45	9.33	0.01
SQU-DS	2026-06-01 19:00:00	10.96	28.41	565.68	7.40	10.41	8.04	0.01
SQU-DS	2026-06-01 19:15:00	10.97	28.54	566.31	7.41	10.40	7.37	0.01
SQU-DS	2026-06-01 19:30:00	10.96	28.70	566.48	7.42	10.38	5.65	0.01
SQU-DS	2026-06-01 19:45:00	10.96	28.82	565.83	7.44	10.37	2.58	0.01
SQU-DS	2026-06-01 20:00:00	10.95	28.91	566.80	7.43	10.34	1.24	0.01
SQU-DS	2026-06-01 20:15:00	10.93	29.20	567.11	7.43	10.31	0.29	0.01
SQU-DS	2026-06-01 20:30:00	10.91	29.77	566.78	7.45	10.29	0.00	0.01
SQU-DS	2026-06-01 20:45:00	10.89	30.28	567.92	7.44	10.25	0.00	0.01
SQU-DS	2026-06-01 21:00:00	10.87	29.98	568.08	7.45	10.25	0.00	0.01
SQU-DS	2026-06-01 21:15:00	10.84	30.22	568.69	7.44	10.19	0.00	0.01
SQU-DS	2026-06-01 21:30:00	10.82	30.21	569.51	7.43	10.17	0.00	0.01
SQU-DS	2026-06-01 21:45:00	10.79	30.85	570.38	7.42	10.17	0.00	0.01
SQU-DS	2026-06-01 22:00:00	10.76	30.80	570.69	7.43	10.17	0.00	0.01
SQU-DS	2026-06-01 22:15:00	10.72	30.76	571.24	7.42	10.20	0.00	0.01
SQU-DS	2026-06-01 22:30:00	10.69	30.65	571.63	7.42	10.19	0.71	0.01
SQU-DS	2026-06-01 22:45:00	10.64	30.65	572.97	7.40	10.20	0.12	0.01
SQU-DS	2026-06-01 23:00:00	10.59	30.53	573.11	7.39	10.21	3.18	0.01
SQU-DS	2026-06-01 23:15:00	10.54	30.31	574.29	7.37	10.21	4.08	0.01
SQU-DS	2026-06-01 23:30:00	10.47	30.28	575.66	7.34	10.20	3.50	0.01
SQU-DS	2026-06-01 23:45:00	10.41	30.16	574.48	7.35	10.20	4.16	0.01
SQU-DS	2026-06-02 00:00:00	10.36	29.96	574.41	7.34	10.22	4.82	0.01
SQU-DS	2026-06-02 00:15:00	10.28	29.56	575.45	7.31	10.24	5.06	0.01
SQU-DS	2026-06-02 00:30:00	10.23	29.21	573.95	7.34	10.25	5.19	0.01
SQU-DS	2026-06-02 00:45:00	10.16	29.20	574.01	7.33	10.25	5.22	0.01
SQU-DS	2026-06-02 01:00:00	10.10	28.88	574.41	7.32	10.27	5.66	0.01
SQU-DS	2026-06-02 01:15:00	10.05	28.73	573.69	7.34	10.28	5.70	0.01
SQU-DS	2026-06-02 01:30:00	9.98	28.60	575.58	7.31	10.30	6.02	0.01
SQU-DS	2026-06-02 01:45:00	9.93	28.57	574.82	7.32	10.28	6.06	0.01
SQU-DS	2026-06-02 02:00:00	9.87	28.27	574.72	7.33	10.33	7.53	0.01
SQU-DS	2026-06-02 02:15:00	9.81	28.37	574.10	7.34	10.32	7.07	0.01
SQU-DS	2026-06-02 02:30:00	9.76	28.14	574.64	7.33	10.33	7.54	0.01
SQU-DS	2026-06-02 02:45:00	9.69	27.90	575.45	7.31	10.35	7.47	0.01
SQU-DS	2026-06-02 03:00:00	9.65	27.97	573.95	7.34	10.36	7.15	0.01
SQU-DS	2026-06-02 03:15:00	9.58	27.87	574.63	7.33	10.37	7.80	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-02 03:30:00	9.53	27.65	575.61	7.31	10.39	7.00	0.01
SQU-DS	2026-06-02 03:45:00	9.49	27.69	574.78	7.33	10.41	7.33	0.01
SQU-DS	2026-06-02 04:00:00	9.42	27.68	575.42	7.32	10.41	7.44	0.01
SQU-DS	2026-06-02 04:15:00	9.38	27.53	574.63	7.33	10.42	6.76	0.01
SQU-DS	2026-06-02 04:30:00	9.32	27.64	576.03	7.31	10.43	6.89	0.01
SQU-DS	2026-06-02 04:45:00	9.27	27.60	574.80	7.34	10.44	6.74	0.01
SQU-DS	2026-06-02 05:00:00	9.23	27.25	576.21	7.32	10.46	5.49	0.01
SQU-DS	2026-06-02 05:15:00	9.19	27.23	575.73	7.33	10.47	5.76	0.01
SQU-DS	2026-06-02 05:30:00	9.16	27.28	575.42	7.33	10.48	5.17	0.01
SQU-DS	2026-06-02 05:45:00	9.12	27.23	574.94	7.34	10.50	4.86	0.01
SQU-DS	2026-06-02 06:00:00	9.08	27.17	575.01	7.35	10.51	3.85	0.01
SQU-DS	2026-06-02 06:15:00	9.04	27.28	576.90	7.31	10.51	3.80	0.01
SQU-DS	2026-06-02 06:30:00	9.01	27.18	575.63	7.33	10.52	3.94	0.01
SQU-DS	2026-06-02 06:45:00	9.01	27.19	574.72	7.35	10.55	3.81	0.01
SQU-DS	2026-06-02 07:00:00	8.98	27.07	575.11	7.33	10.56	4.68	0.01
SQU-DS	2026-06-02 07:15:00	8.97	27.23	574.16	7.34	10.56	4.26	0.01
SQU-DS	2026-06-02 07:30:00	8.97	27.25	573.69	7.34	10.57	5.65	0.01
SQU-DS	2026-06-02 07:45:00	8.97	27.16	573.16	7.34	10.58	4.87	0.01
SQU-DS	2026-06-02 08:00:00	8.99	27.20	573.79	7.32	10.60	4.50	0.01
SQU-DS	2026-06-02 08:15:00	9.02	27.10	572.64	7.34	10.59	4.38	0.01
SQU-DS	2026-06-02 08:30:00	9.04	27.32	572.79	7.34	10.60	4.57	0.01
SQU-DS	2026-06-02 08:45:00	9.09	27.09	573.96	7.31	10.61	5.23	0.01
SQU-DS	2026-06-02 09:00:00	9.13	27.23	572.47	7.33	10.61	5.29	0.01
SQU-DS	2026-06-02 09:15:00	9.17	27.22	572.15	7.33	10.62	36.88	0.01
SQU-DS	2026-06-02 09:30:00	9.23	27.17	571.00	7.35	10.62	14.72	0.01
SQU-DS	2026-06-02 09:45:00	9.30	27.22	571.29	7.34	10.61	17.23	0.01
SQU-DS	2026-06-02 10:00:00	9.35	27.14	570.89	7.34	10.62	20.52	0.01
SQU-DS	2026-06-02 10:15:00	9.41	27.15	570.96	7.34	10.61	19.80	0.01
SQU-DS	2026-06-02 10:30:00	9.47	27.36	571.25	7.33	10.61	19.40	0.01
SQU-DS	2026-06-02 10:45:00	9.55	27.25	570.45	7.34	10.62	19.07	0.01
SQU-DS	2026-06-02 11:00:00	9.61	27.22	569.68	7.35	10.61	23.28	0.01
SQU-DS	2026-06-02 11:15:00	9.68	27.02	570.20	7.33	10.61	21.12	0.01
SQU-DS	2026-06-02 11:30:00	9.76	27.01	570.54	7.33	10.61	20.76	0.01
SQU-DS	2026-06-02 11:45:00	9.84	27.03	569.92	7.33	10.60	18.52	0.01
SQU-DS	2026-06-02 12:00:00	9.92	26.98	568.80	7.35	10.60	19.33	0.01
SQU-DS	2026-06-02 12:15:00	10.01	26.86	568.04	7.35	10.60	20.56	0.01
SQU-DS	2026-06-02 12:30:00	10.07	27.15	567.92	7.34	10.59	19.52	0.01
SQU-DS	2026-06-02 12:45:00	10.16	27.02	566.49	7.37	10.57	19.76	0.01
SQU-DS	2026-06-02 13:00:00	10.24	27.04	567.10	7.35	10.57	20.53	0.01
SQU-DS	2026-06-02 13:15:00	10.32	27.00	566.47	7.35	10.56	22.36	0.01
SQU-DS	2026-06-02 13:30:00	10.41	26.80	565.55	7.36	10.54	21.36	0.01
SQU-DS	2026-06-02 13:45:00	10.48	26.87	566.33	7.35	10.54	21.37	0.01
SQU-DS	2026-06-02 14:00:00	10.56	26.96	565.82	7.35	10.53	20.98	0.01
SQU-DS	2026-06-02 14:15:00	10.63	26.92	565.24	7.36	10.51	18.16	0.01
SQU-DS	2026-06-02 14:30:00	10.71	26.91	565.15	7.36	10.50	19.25	0.01
SQU-DS	2026-06-02 14:45:00	10.78	27.27	565.44	7.36	10.49	18.29	0.01
SQU-DS	2026-06-02 15:00:00	10.86	27.09	566.21	7.35	10.47	19.01	0.01
SQU-DS	2026-06-02 15:15:00	10.93	27.02	567.60	7.32	10.46	19.82	0.01
SQU-DS	2026-06-02 15:30:00	11.00	27.18	567.15	7.33	10.46	19.90	0.01
SQU-DS	2026-06-02 15:45:00	11.06	26.99	567.06	7.33	10.47	19.37	0.01
SQU-DS	2026-06-02 16:00:00	11.11	27.16	566.63	7.34	10.44	20.74	0.01
SQU-DS	2026-06-02 16:15:00	11.17	27.24	567.15	7.34	10.42	20.81	0.01
SQU-DS	2026-06-02 16:30:00	11.22	27.48	567.15	7.35	10.41	17.87	0.01
SQU-DS	2026-06-02 16:45:00	11.26	27.33	566.55	7.36	10.39	20.77	0.01
SQU-DS	2026-06-02 17:00:00	11.31	27.53	567.66	7.35	10.37	20.11	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-02 17:15:00	11.35	27.67	567.28	7.36	10.37	20.14	0.01
SQU-DS	2026-06-02 17:30:00	11.38	27.65	567.67	7.35	10.36	22.19	0.01
SQU-DS	2026-06-02 17:45:00	11.40	27.57	567.75	7.36	10.34	21.26	0.01
SQU-DS	2026-06-02 18:00:00	11.42	27.73	566.19	7.39	10.31	20.05	0.01
SQU-DS	2026-06-02 18:15:00	11.44	27.95	567.25	7.38	10.29	21.95	0.01
SQU-DS	2026-06-02 18:30:00	11.44	27.84	567.47	7.38	10.27	21.97	0.01
SQU-DS	2026-06-02 18:45:00	11.45	27.94	567.06	7.40	10.25	20.02	0.01
SQU-DS	2026-06-02 19:00:00	11.45	28.10	567.89	7.39	10.23	18.99	0.01
SQU-DS	2026-06-02 19:15:00	11.45	28.05	567.62	7.40	10.22	25.62	0.01
SQU-DS	2026-06-02 19:30:00	11.45	28.27	566.52	7.42	10.20	19.84	0.01
SQU-DS	2026-06-02 19:45:00	11.44	28.24	567.34	7.42	10.18	17.12	0.01
SQU-DS	2026-06-02 20:00:00	11.42	28.54	567.58	7.43	10.15	11.34	0.01
SQU-DS	2026-06-02 20:15:00	11.40	28.29	567.64	7.44	10.13	6.23	0.01
SQU-DS	2026-06-02 20:30:00	11.38	28.54	567.92	7.44	10.10	4.24	0.01
SQU-DS	2026-06-02 20:45:00	11.35	28.54	568.19	7.45	10.08	4.51	0.01
SQU-DS	2026-06-02 21:00:00	11.33	28.13	571.63	7.46	10.05	0.49	0.01
SQU-DS	2026-06-02 21:15:00	11.30	28.43	573.42	7.45	10.04	0.00	0.01
SQU-DS	2026-06-02 21:30:00	11.26	28.31	574.79	7.45	10.03	0.00	0.01
SQU-DS	2026-06-02 21:45:00	11.21	28.08	575.75	7.45	10.02	0.00	0.01
SQU-DS	2026-06-02 22:00:00	11.16	27.93	576.84	7.45	10.00	0.00	0.01
SQU-DS	2026-06-02 22:15:00	11.10	27.80	577.42	7.45	9.99	0.00	0.01
SQU-DS	2026-06-02 22:30:00	11.04	27.54	576.11	7.43	10.00	0.00	0.01
SQU-DS	2026-06-02 22:45:00	10.98	27.34	577.11	7.43	9.99	0.00	0.01
SQU-DS	2026-06-02 23:00:00	10.91	27.07	576.25	7.41	9.99	0.00	0.01
SQU-DS	2026-06-02 23:15:00	10.83	26.62	576.65	7.40	9.99	0.00	0.01
SQU-DS	2026-06-02 23:30:00	10.76	26.24	576.24	7.40	10.01	0.00	0.01
SQU-DS	2026-06-02 23:45:00	10.69	26.03	575.63	7.41	10.02	0.00	0.01
SQU-DS	2026-06-03 00:00:00	10.62	25.85	575.54	7.41	10.03	0.00	0.01
SQU-DS	2026-06-03 00:15:00	10.54	25.80	575.43	7.40	10.06	0.00	0.01
SQU-DS	2026-06-03 00:30:00	10.48	25.99	576.66	7.37	10.11	0.00	0.01
SQU-DS	2026-06-03 00:45:00	10.40	26.09	576.88	7.37	10.14	2.76	0.01
SQU-DS	2026-06-03 01:00:00	10.33	25.97	577.27	7.36	10.16	3.04	0.01
SQU-DS	2026-06-03 01:15:00	10.27	25.82	577.12	7.36	10.18	5.47	0.01
SQU-DS	2026-06-03 01:30:00	10.21	25.46	576.78	7.36	10.19	8.16	0.01
SQU-DS	2026-06-03 01:45:00	10.15	25.39	577.30	7.35	10.21	10.50	0.01
SQU-DS	2026-06-03 02:00:00	10.08	25.01	576.75	7.35	10.23	15.66	0.01
SQU-DS	2026-06-03 02:15:00	10.01	24.97	578.05	7.32	10.25	16.69	0.01
SQU-DS	2026-06-03 02:30:00	9.94	24.99	577.32	7.33	10.27	14.69	0.01
SQU-DS	2026-06-03 02:45:00	9.87	24.87	576.65	7.35	10.28	12.84	0.01
SQU-DS	2026-06-03 03:00:00	9.82	24.80	576.66	7.35	10.30	16.36	0.01
SQU-DS	2026-06-03 03:15:00	9.75	24.71	576.42	7.35	10.31	12.72	0.01
SQU-DS	2026-06-03 03:30:00	9.69	24.50	575.78	7.36	10.33	8.90	0.01
SQU-DS	2026-06-03 03:45:00	9.66	24.33	576.19	7.35	10.34	8.24	0.01
SQU-DS	2026-06-03 04:00:00	9.60	24.28	576.61	7.34	10.36	7.52	0.01
SQU-DS	2026-06-03 04:15:00	9.56	24.16	576.50	7.34	10.36	12.50	0.01
SQU-DS	2026-06-03 04:30:00	9.50	24.24	575.88	7.35	10.37	6.03	0.01
SQU-DS	2026-06-03 04:45:00	9.47	24.12	576.22	7.35	10.37	5.11	0.01
SQU-DS	2026-06-03 05:00:00	9.44	24.06	575.22	7.36	10.38	4.64	0.01
SQU-DS	2026-06-03 05:15:00	9.40	23.85	574.75	7.37	10.39	3.39	0.01
SQU-DS	2026-06-03 05:30:00	9.36	23.82	575.56	7.36	10.38	0.67	0.01
SQU-DS	2026-06-03 05:45:00	9.33	23.63	575.89	7.36	10.41	0.78	0.01
SQU-DS	2026-06-03 06:00:00	9.31	23.41	575.56	7.37	10.41	0.00	0.01
SQU-DS	2026-06-03 06:15:00	9.28	23.50	576.62	7.35	10.43	0.07	0.01
SQU-DS	2026-06-03 06:30:00	9.24	23.50	576.64	7.35	10.46	0.00	0.01
SQU-DS	2026-06-03 06:45:00	9.24	23.35	576.46	7.35	10.46	0.67	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-03 07:00:00	9.24	23.41	576.03	7.36	10.46	0.00	0.01
SQU-DS	2026-06-03 07:15:00	9.22	23.28	576.05	7.36	10.45	0.00	0.01
SQU-DS	2026-06-03 07:30:00	9.22	22.88	575.38	7.37	10.47	0.00	0.01
SQU-DS	2026-06-03 07:45:00	9.19	23.17	575.18	7.38	10.47	0.00	0.01
SQU-DS	2026-06-03 08:00:00	9.19	23.36	574.80	7.39	10.49	0.00	0.01
SQU-DS	2026-06-03 08:15:00	9.19	23.25	575.56	7.38	10.50	0.00	0.01
SQU-DS	2026-06-03 08:30:00	9.18	23.24	577.24	7.35	10.49	3.30	0.01
SQU-DS	2026-06-03 08:45:00	9.16	23.66	576.93	7.35	10.50	3.70	0.01
SQU-DS	2026-06-03 09:00:00	9.16	23.45	576.26	7.36	10.52	6.14	0.01
SQU-DS	2026-06-03 09:15:00	9.16	23.43	576.50	7.35	10.55	9.75	0.01
SQU-DS	2026-06-03 09:30:00	9.17	23.68	578.78	7.30	10.54	17.86	0.01
SQU-DS	2026-06-03 09:45:00	9.16	23.82	577.74	7.32	10.56	13.50	0.01
SQU-DS	2026-06-03 10:00:00	9.20	23.62	576.25	7.34	10.56	8.90	0.01
SQU-DS	2026-06-03 10:15:00	9.21	23.72	577.78	7.30	10.60	14.17	0.01
SQU-DS	2026-06-03 10:30:00	9.22	23.82	576.54	7.32	10.60	11.71	0.01
SQU-DS	2026-06-03 10:45:00	9.23	23.67	575.35	7.33	10.61	14.74	0.01
SQU-DS	2026-06-03 11:00:00	9.27	23.59	574.79	7.34	10.62	15.32	0.01
SQU-DS	2026-06-03 11:15:00	9.28	23.56	575.79	7.32	10.61	20.04	0.01
SQU-DS	2026-06-03 11:30:00	9.27	23.48	575.46	7.32	10.63	17.91	0.01
SQU-DS	2026-06-03 11:45:00	9.23	23.59	574.77	7.34	10.64	17.96	0.01
SQU-DS	2026-06-03 12:00:00	9.24	23.60	576.41	7.31	10.62	16.68	0.01
SQU-DS	2026-06-03 12:15:00	9.24	23.58	573.86	7.35	10.64	22.43	0.01
SQU-DS	2026-06-03 12:30:00	9.27	23.62	575.25	7.31	10.63	21.22	0.01
SQU-DS	2026-06-03 12:45:00	9.26	23.61	574.01	7.33	10.65	22.33	0.01
SQU-DS	2026-06-03 13:00:00	9.22	23.62	574.28	7.33	10.65	22.98	0.01
SQU-DS	2026-06-03 13:15:00	9.24	23.61	574.34	7.32	10.65	25.91	0.01
SQU-DS	2026-06-03 13:30:00	9.21	23.50	575.82	7.29	10.65	26.22	0.01
SQU-DS	2026-06-03 13:45:00	9.19	23.74	574.39	7.31	10.66	21.49	0.01
SQU-DS	2026-06-03 14:00:00	9.18	23.68	574.51	7.31	10.65	28.85	0.01
SQU-DS	2026-06-03 14:15:00	9.16	23.90	573.99	7.32	10.66	24.11	0.01
SQU-DS	2026-06-03 14:30:00	9.16	23.73	574.92	7.30	10.66	19.95	0.01
SQU-DS	2026-06-03 14:45:00	9.19	23.89	574.15	7.31	10.67	28.42	0.01
SQU-DS	2026-06-03 15:00:00	9.22	23.75	574.50	7.30	10.68	22.93	0.01
SQU-DS	2026-06-03 15:15:00	9.27	23.97	573.90	7.31	10.66	24.91	0.01
SQU-DS	2026-06-03 15:30:00	9.30	24.12	572.77	7.32	10.66	21.77	0.01
SQU-DS	2026-06-03 15:45:00	9.33	24.09	573.09	7.31	10.67	24.23	0.01
SQU-DS	2026-06-03 16:00:00	9.36	23.98	573.03	7.32	10.67	22.68	0.01
SQU-DS	2026-06-03 16:15:00	9.38	23.98	573.75	7.30	10.66	27.87	0.01
SQU-DS	2026-06-03 16:30:00	9.37	24.75	573.89	7.30	10.66	25.12	0.01
SQU-DS	2026-06-03 16:45:00	9.36	24.32	572.72	7.32	10.65	22.14	0.01
SQU-DS	2026-06-03 17:00:00	9.35	24.06	572.53	7.33	10.65	22.91	0.01
SQU-DS	2026-06-03 17:15:00	9.32	24.18	573.13	7.32	10.66	22.37	0.01
SQU-DS	2026-06-03 17:30:00	9.31	24.11	573.50	7.32	10.65	26.21	0.01
SQU-DS	2026-06-03 17:45:00	9.31	24.09	574.26	7.30	10.65	25.33	0.01
SQU-DS	2026-06-03 18:00:00	9.30	24.41	574.78	7.29	10.64	23.88	0.01
SQU-DS	2026-06-03 18:15:00	9.31	24.26	574.72	7.30	10.65	23.30	0.01
SQU-DS	2026-06-03 18:30:00	9.32	24.37	573.36	7.32	10.64	22.73	0.01
SQU-DS	2026-06-03 18:45:00	9.34	24.54	573.84	7.32	10.63	22.59	0.01
SQU-DS	2026-06-03 19:00:00	9.35	24.74	572.96	7.34	10.63	20.59	0.01
SQU-DS	2026-06-03 19:15:00	9.35	24.96	573.25	7.34	10.63	19.11	0.01
SQU-DS	2026-06-03 19:30:00	9.35	24.68	572.92	7.35	10.62	16.64	0.01
SQU-DS	2026-06-03 19:45:00	9.35	24.74	572.52	7.37	10.63	12.10	0.01
SQU-DS	2026-06-03 20:00:00	9.33	24.84	571.72	7.39	10.61	10.74	0.01
SQU-DS	2026-06-03 20:15:00	9.32	24.82	571.22	7.41	10.61	6.53	0.01
SQU-DS	2026-06-03 20:30:00	9.31	25.06	571.30	7.41	10.60	2.46	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-03 20:45:00	9.29	25.13	571.81	7.41	10.59	0.00	0.01
SQU-DS	2026-06-03 21:00:00	9.27	24.89	574.11	7.44	10.57	0.52	0.01
SQU-DS	2026-06-03 21:15:00	9.25	24.80	576.95	7.43	10.56	0.00	0.01
SQU-DS	2026-06-03 21:30:00	9.23	24.71	578.02	7.39	10.56	0.00	0.01
SQU-DS	2026-06-03 21:45:00	9.20	25.09	577.94	7.42	10.55	0.72	0.01
SQU-DS	2026-06-03 22:00:00	9.18	24.97	578.17	7.42	10.55	1.30	0.01
SQU-DS	2026-06-03 22:15:00	9.16	24.86	579.93	7.42	10.53	0.12	0.01
SQU-DS	2026-06-03 22:30:00	9.14	24.80	579.22	7.41	10.53	0.00	0.01
SQU-DS	2026-06-03 22:45:00	9.13	24.82	579.45	7.43	10.52	0.00	0.01
SQU-DS	2026-06-03 23:00:00	9.11	24.66	580.57	7.42	10.53	0.00	0.01
SQU-DS	2026-06-03 23:15:00	9.10	24.60	581.24	7.44	10.51	0.00	0.01
SQU-DS	2026-06-03 23:30:00	9.09	24.62	581.48	7.45	10.52	0.00	0.01
SQU-DS	2026-06-03 23:45:00	9.07	24.24	582.52	7.45	10.51	0.00	0.01
SQU-DS	2026-06-04 00:00:00	9.05	24.00	582.49	7.42	10.52	0.00	0.01
SQU-DS	2026-06-04 00:15:00	9.02	23.84	580.28	7.42	10.54	0.00	0.01
SQU-DS	2026-06-04 00:30:00	9.00	23.46	579.11	7.42	10.54	0.00	0.01
SQU-DS	2026-06-04 00:45:00	8.99	23.67	580.16	7.38	10.54	0.00	0.01
SQU-DS	2026-06-04 01:00:00	8.97	23.64	579.00	7.39	10.54	0.00	0.01
SQU-DS	2026-06-04 01:15:00	8.95	23.68	578.59	7.38	10.55	4.90	0.01
SQU-DS	2026-06-04 01:30:00	8.93	24.13	578.83	7.37	10.57	3.11	0.01
SQU-DS	2026-06-04 01:45:00	8.91	24.30	578.42	7.38	10.54	8.85	0.01
SQU-DS	2026-06-04 02:00:00	8.89	24.09	579.43	7.35	10.56	6.46	0.01
SQU-DS	2026-06-04 02:15:00	8.89	24.10	579.11	7.35	10.57	5.58	0.01
SQU-DS	2026-06-04 02:30:00	8.87	24.61	579.10	7.35	10.57	7.92	0.01
SQU-DS	2026-06-04 02:45:00	8.85	24.57	578.48	7.35	10.58	8.29	0.01
SQU-DS	2026-06-04 03:00:00	8.83	24.64	578.87	7.34	10.58	7.80	0.01
SQU-DS	2026-06-04 03:15:00	8.81	24.57	578.92	7.34	10.58	7.45	0.01
SQU-DS	2026-06-04 03:30:00	8.78	24.65	578.90	7.34	10.59	12.98	0.01
SQU-DS	2026-06-04 03:45:00	8.75	24.48	579.02	7.33	10.59	14.05	0.01
SQU-DS	2026-06-04 04:00:00	8.73	24.54	578.26	7.34	10.61	12.51	0.01
SQU-DS	2026-06-04 04:15:00	8.70	24.50	578.23	7.34	10.61	8.82	0.01
SQU-DS	2026-06-04 04:30:00	8.69	24.50	578.05	7.34	10.60	10.62	0.01
SQU-DS	2026-06-04 04:45:00	8.66	24.45	578.57	7.33	10.61	9.01	0.01
SQU-DS	2026-06-04 05:00:00	8.65	24.39	578.27	7.33	10.62	5.70	0.01
SQU-DS	2026-06-04 05:15:00	8.63	24.32	577.78	7.34	10.63	6.75	0.01
SQU-DS	2026-06-04 05:30:00	8.61	24.23	577.79	7.34	10.65	5.01	0.01
SQU-DS	2026-06-04 05:45:00	8.60	24.12	577.60	7.34	10.64	4.02	0.01
SQU-DS	2026-06-04 06:00:00	8.59	24.25	576.63	7.35	10.65	9.88	0.01
SQU-DS	2026-06-04 06:15:00	8.57	24.21	576.48	7.35	10.67	4.27	0.01
SQU-DS	2026-06-04 06:30:00	8.57	24.70	576.17	7.36	10.66	5.57	0.01
SQU-DS	2026-06-04 06:45:00	8.56	24.04	576.31	7.35	10.66	3.45	0.01
SQU-DS	2026-06-04 07:00:00	8.56	24.08	576.34	7.36	10.67	5.20	0.01
SQU-DS	2026-06-04 07:15:00	8.55	23.84	575.47	7.37	10.70	3.33	0.01
SQU-DS	2026-06-04 07:30:00	8.55	23.95	576.83	7.35	10.71	5.48	0.01
SQU-DS	2026-06-04 07:45:00	8.56	23.99	575.91	7.36	10.71	6.67	0.01
SQU-DS	2026-06-04 08:00:00	8.57	23.97	575.21	7.37	10.73	2.46	0.01
SQU-DS	2026-06-04 08:15:00	8.55	24.13	575.86	7.36	10.73	2.61	0.01
SQU-DS	2026-06-04 08:30:00	8.57	24.03	575.63	7.36	10.73	3.30	0.01
SQU-DS	2026-06-04 08:45:00	8.60	24.44	575.90	7.35	10.73	4.25	0.01
SQU-DS	2026-06-04 09:00:00	8.67	24.43	575.24	7.36	10.75	7.58	0.01
SQU-DS	2026-06-04 09:15:00	8.72	24.38	576.06	7.34	10.76	10.06	0.01
SQU-DS	2026-06-04 09:30:00	8.76	24.44	575.22	7.35	10.75	8.19	0.01
SQU-DS	2026-06-04 09:45:00	8.80	24.89	575.63	7.35	10.76	8.85	0.01
SQU-DS	2026-06-04 10:00:00	8.88	24.80	575.75	7.34	10.75	7.98	0.01
SQU-DS	2026-06-04 10:15:00	8.94	24.93	575.02	7.35	10.76	11.55	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-04 10:30:00	9.04	24.70	574.23	7.36	10.76	12.39	0.01
SQU-DS	2026-06-04 10:45:00	9.12	24.91	574.32	7.35	10.76	11.30	0.01
SQU-DS	2026-06-04 11:00:00	9.18	25.38	573.45	7.36	10.75	16.17	0.01
SQU-DS	2026-06-04 11:15:00	9.21	25.18	573.73	7.35	10.74	11.80	0.01
SQU-DS	2026-06-04 11:30:00	9.23	24.95	573.65	7.35	10.75	13.70	0.01
SQU-DS	2026-06-04 11:45:00	9.29	24.47	573.70	7.35	10.75	12.66	0.01
SQU-DS	2026-06-04 12:00:00	9.33	24.22	573.64	7.35	10.75	10.31	0.01
SQU-DS	2026-06-04 12:15:00	9.40	24.34	572.77	7.36	10.75	20.57	0.01
SQU-DS	2026-06-04 12:30:00	9.47	24.28	573.80	7.34	10.74	13.91	0.01
SQU-DS	2026-06-04 12:45:00	9.58	24.40	573.41	7.35	10.73	12.45	0.01
SQU-DS	2026-06-04 13:00:00	9.62	24.66	573.08	7.36	10.72	11.54	0.01
SQU-DS	2026-06-04 13:15:00	9.67	24.61	572.90	7.36	10.72	9.65	0.01
SQU-DS	2026-06-04 13:30:00	9.72	24.62	572.51	7.37	10.70	11.51	0.01
SQU-DS	2026-06-04 13:45:00	9.71	24.54	572.83	7.36	10.71	8.49	0.01
SQU-DS	2026-06-04 14:00:00	9.75	24.40	572.73	7.36	10.71	7.26	0.01
SQU-DS	2026-06-04 14:15:00	9.74	24.42	573.64	7.34	10.72	14.75	0.01
SQU-DS	2026-06-04 14:30:00	9.73	24.52	572.67	7.36	10.74	11.49	0.01
SQU-DS	2026-06-04 14:45:00	9.69	24.48	572.35	7.37	10.72	11.60	0.01
SQU-DS	2026-06-04 15:00:00	9.70	24.40	571.54	7.38	10.71	12.19	0.01
SQU-DS	2026-06-04 15:15:00	9.76	24.37	571.70	7.38	10.70	8.05	0.01
SQU-DS	2026-06-04 15:30:00	9.81	24.41	572.82	7.36	10.70	12.95	0.01
SQU-DS	2026-06-04 15:45:00	9.88	24.29	572.57	7.37	10.66	4.70	0.01
SQU-DS	2026-06-04 16:00:00	9.93	24.36	571.55	7.39	10.64	0.91	0.01
SQU-DS	2026-06-04 16:15:00	9.99	24.44	572.40	7.37	10.62	5.77	0.01
SQU-DS	2026-06-04 16:30:00	10.03	24.30	572.64	7.36	10.62	5.92	0.01
SQU-DS	2026-06-04 16:45:00	10.04	24.52	572.69	7.36	10.61	9.59	0.01
SQU-DS	2026-06-04 17:00:00	10.04	24.28	573.59	7.35	10.59	10.35	0.01
SQU-DS	2026-06-04 17:15:00	10.08	24.36	572.18	7.37	10.56	8.36	0.01
SQU-DS	2026-06-04 17:30:00	10.10	24.43	572.63	7.37	10.54	6.20	0.01
SQU-DS	2026-06-04 17:45:00	10.09	24.13	573.10	7.36	10.53	4.66	0.01
SQU-DS	2026-06-04 18:00:00	10.05	24.33	573.17	7.37	10.52	8.82	0.01
SQU-DS	2026-06-04 18:15:00	10.03	24.50	572.87	7.37	10.49	7.39	0.01
SQU-DS	2026-06-04 18:30:00	10.02	24.45	572.09	7.39	10.48	8.45	0.01
SQU-DS	2026-06-04 18:45:00	9.97	24.49	573.92	7.36	10.46	6.93	0.01
SQU-DS	2026-06-04 19:00:00	9.91	24.44	573.65	7.38	10.46	5.40	0.01
SQU-DS	2026-06-04 19:15:00	9.87	24.46	574.99	7.36	10.42	1.50	0.01
SQU-DS	2026-06-04 19:30:00	9.83	24.37	574.51	7.37	10.40	3.75	0.01
SQU-DS	2026-06-04 19:45:00	9.78	24.42	575.92	7.35	10.37	1.35	0.01
SQU-DS	2026-06-04 20:00:00	9.73	24.07	575.44	7.37	10.35	0.00	0.01
SQU-DS	2026-06-04 20:15:00	9.68	23.86	576.22	7.36	10.33	0.00	0.01
SQU-DS	2026-06-04 20:30:00	9.63	23.46	575.87	7.40	10.29	0.00	0.01
SQU-DS	2026-06-04 20:45:00	9.59	23.07	578.01	7.44	10.27	0.00	0.01
SQU-DS	2026-06-04 21:00:00	9.55	22.66	581.23	7.40	10.19	0.00	0.01
SQU-DS	2026-06-04 21:15:00	9.50	22.56	581.15	7.43	10.11	0.00	0.01
SQU-DS	2026-06-04 21:30:00	9.44	22.09	581.53	7.44	10.24	0.00	0.01
SQU-DS	2026-06-04 21:45:00	9.40	21.91	580.78	7.42	10.24	0.00	0.01
SQU-DS	2026-06-04 22:00:00	9.35	21.26	581.51	7.38	10.22	0.00	0.01
SQU-DS	2026-06-04 22:15:00	9.33	21.31	582.29	7.37	10.23	0.00	0.01
SQU-DS	2026-06-04 22:30:00	9.28	21.33	580.64	7.38	10.23	0.00	0.01
SQU-DS	2026-06-04 22:45:00	9.24	21.16	580.73	7.37	10.22	0.00	0.01
SQU-DS	2026-06-04 23:00:00	9.21	20.91	580.76	7.36	10.24	0.00	0.01
SQU-DS	2026-06-04 23:15:00	9.17	20.49	580.78	7.36	10.25	0.00	0.01
SQU-DS	2026-06-04 23:30:00	9.12	20.09	580.51	7.36	10.27	0.00	0.01
SQU-DS	2026-06-04 23:45:00	9.08	19.89	581.55	7.36	10.29	0.00	0.01
SQU-DS	2026-06-05 00:00:00	9.04	19.60	581.19	7.35	10.30	0.00	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-05 00:15:00	9.00	19.60	581.02	7.35	10.32	0.00	0.01
SQU-DS	2026-06-05 00:30:00	8.95	19.51	580.79	7.35	10.34	0.00	0.01
SQU-DS	2026-06-05 00:45:00	8.92	19.25	581.92	7.39	10.34	0.00	0.01
SQU-DS	2026-06-05 01:00:00	8.88	19.12	582.93	7.40	10.35	0.00	0.01
SQU-DS	2026-06-05 01:15:00	8.85	19.00	580.01	7.41	10.38	0.00	0.01
SQU-DS	2026-06-05 01:30:00	8.80	18.85	579.19	7.40	10.38	0.00	0.01
SQU-DS	2026-06-05 01:45:00	8.76	18.71	578.18	7.41	10.39	0.00	0.01
SQU-DS	2026-06-05 02:00:00	8.73	19.27	577.97	7.40	10.38	0.00	0.01
SQU-DS	2026-06-05 02:15:00	8.69	18.98	577.03	7.41	10.41	0.00	0.01
SQU-DS	2026-06-05 02:30:00	8.65	19.79	579.60	7.35	10.43	0.00	0.01
SQU-DS	2026-06-05 02:45:00	8.62	20.01	580.91	7.32	10.52	0.00	0.01
SQU-DS	2026-06-05 03:00:00	8.59	20.68	580.96	7.32	10.57	0.00	0.01
SQU-DS	2026-06-05 03:15:00	8.55	20.66	581.03	7.31	10.60	0.00	0.01
SQU-DS	2026-06-05 03:30:00	8.53	21.00	580.85	7.31	10.60	0.00	0.01
SQU-DS	2026-06-05 03:45:00	8.49	21.25	581.34	7.30	10.62	1.76	0.01
SQU-DS	2026-06-05 04:00:00	8.46	21.18	581.94	7.29	10.63	3.37	0.01
SQU-DS	2026-06-05 04:15:00	8.43	21.63	581.61	7.29	10.63	2.64	0.01
SQU-DS	2026-06-05 04:30:00	8.41	21.67	581.25	7.30	10.64	3.22	0.01
SQU-DS	2026-06-05 04:45:00	8.38	21.75	581.23	7.30	10.66	3.58	0.01
SQU-DS	2026-06-05 05:00:00	8.36	22.05	580.66	7.31	10.67	4.39	0.01
SQU-DS	2026-06-05 05:15:00	8.34	22.08	580.56	7.31	10.68	3.05	0.01
SQU-DS	2026-06-05 05:30:00	8.31	21.93	580.35	7.31	10.69	3.07	0.01
SQU-DS	2026-06-05 05:45:00	8.29	21.89	581.01	7.30	10.70	3.21	0.01
SQU-DS	2026-06-05 06:00:00	8.27	22.03	579.26	7.32	10.71	3.56	0.01
SQU-DS	2026-06-05 06:15:00	8.26	22.05	580.92	7.29	10.72	2.87	0.01
SQU-DS	2026-06-05 06:30:00	8.25	22.01	579.40	7.32	10.71	5.50	0.01
SQU-DS	2026-06-05 06:45:00	8.22	22.20	579.91	7.31	10.73	4.29	0.01
SQU-DS	2026-06-05 07:00:00	8.20	21.96	580.10	7.31	10.75	4.18	0.01
SQU-DS	2026-06-05 07:15:00	8.19	22.02	579.50	7.32	10.76	3.98	0.01
SQU-DS	2026-06-05 07:30:00	8.18	22.04	579.85	7.32	10.77	2.92	0.01
SQU-DS	2026-06-05 07:45:00	8.17	22.03	579.67	7.32	10.78	3.82	0.01
SQU-DS	2026-06-05 08:00:00	8.17	21.99	581.02	7.30	10.79	3.14	0.01
SQU-DS	2026-06-05 08:15:00	8.18	22.03	578.14	7.35	10.79	2.68	0.01
SQU-DS	2026-06-05 08:30:00	8.17	22.38	578.47	7.33	10.80	4.24	0.01
SQU-DS	2026-06-05 08:45:00	8.16	22.23	578.06	7.34	10.79	4.81	0.01
SQU-DS	2026-06-05 09:00:00	8.16	22.69	578.04	7.34	10.81	5.09	0.01
SQU-DS	2026-06-05 09:15:00	8.16	22.78	580.02	7.30	10.81	3.38	0.01
SQU-DS	2026-06-05 09:30:00	8.16	23.04	578.54	7.32	10.80	4.60	0.01
SQU-DS	2026-06-05 09:45:00	8.17	23.62	578.69	7.31	10.81	6.93	0.01
SQU-DS	2026-06-05 10:00:00	8.17	23.53	578.48	7.31	10.82	6.43	0.01
SQU-DS	2026-06-05 10:15:00	8.17	23.50	578.40	7.31	10.82	3.54	0.01
SQU-DS	2026-06-05 10:30:00	8.17	23.36	577.79	7.31	10.83	5.27	0.01
SQU-DS	2026-06-05 10:45:00	8.18	23.47	578.73	7.29	10.84	7.62	0.01
SQU-DS	2026-06-05 11:00:00	8.18	23.65	578.64	7.29	10.86	6.23	0.01
SQU-DS	2026-06-05 11:15:00	8.17	24.17	578.05	7.30	10.86	11.48	0.01
SQU-DS	2026-06-05 11:30:00	8.18	24.98	578.44	7.30	10.87	16.75	0.01
SQU-DS	2026-06-05 11:45:00	8.20	24.64	577.83	7.31	10.86	18.43	0.01
SQU-DS	2026-06-05 12:00:00	8.20	24.56	576.93	7.32	10.86	10.33	0.01
SQU-DS	2026-06-05 12:15:00	8.19	24.57	579.16	7.28	10.88	15.40	0.01
SQU-DS	2026-06-05 12:30:00	8.18	24.73	577.82	7.31	10.88	14.76	0.01
SQU-DS	2026-06-05 12:45:00	8.18	24.66	577.69	7.31	10.89	12.31	0.01
SQU-DS	2026-06-05 13:00:00	8.18	24.58	577.03	7.32	10.89	13.11	0.01
SQU-DS	2026-06-05 13:15:00	8.15	24.78	577.65	7.31	10.90	13.24	0.01
SQU-DS	2026-06-05 13:30:00	8.15	24.73	577.82	7.32	10.88	14.51	0.01
SQU-DS	2026-06-05 13:45:00	8.14	24.94	577.58	7.32	10.86	17.30	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-05 14:00:00	8.12	24.91	579.52	7.28	10.87	14.99	0.01
SQU-DS	2026-06-05 14:15:00	8.10	25.08	578.06	7.31	10.88	15.73	0.01
SQU-DS	2026-06-05 14:30:00	8.09	24.94	577.42	7.32	10.89	16.92	0.01
SQU-DS	2026-06-05 14:45:00	8.10	24.95	577.65	7.31	10.89	18.11	0.01
SQU-DS	2026-06-05 15:00:00	8.09	25.12	577.91	7.31	10.89	14.90	0.01
SQU-DS	2026-06-05 15:15:00	8.10	25.13	578.19	7.30	10.88	17.53	0.01
SQU-DS	2026-06-05 15:30:00	8.12	25.21	577.24	7.32	10.90	17.29	0.01
SQU-DS	2026-06-05 15:45:00	8.17	25.30	577.23	7.31	10.91	21.19	0.01
SQU-DS	2026-06-05 16:00:00	8.28	25.16	576.26	7.32	10.91	19.39	0.01
SQU-DS	2026-06-05 16:15:00	8.36	25.41	574.74	7.34	10.91	19.45	0.01
SQU-DS	2026-06-05 16:30:00	8.42	25.73	574.78	7.33	10.90	20.84	0.01
SQU-DS	2026-06-05 16:45:00	8.44	25.35	575.47	7.32	10.89	21.60	0.01
SQU-DS	2026-06-05 17:00:00	8.46	25.88	573.92	7.34	10.90	20.49	0.01
SQU-DS	2026-06-05 17:15:00	8.47	25.71	575.18	7.32	10.88	17.73	0.01
SQU-DS	2026-06-05 17:30:00	8.48	25.94	575.17	7.32	10.90	21.79	0.01
SQU-DS	2026-06-05 17:45:00	8.46	26.07	574.02	7.34	10.89	17.23	0.01
SQU-DS	2026-06-05 18:00:00	8.43	26.13	574.27	7.34	10.89	19.55	0.01
SQU-DS	2026-06-05 18:15:00	8.40	26.19	576.02	7.31	10.88	21.10	0.01
SQU-DS	2026-06-05 18:30:00	8.38	26.28	574.15	7.34	10.87	22.91	0.01
SQU-DS	2026-06-05 18:45:00	8.36	26.33	575.36	7.32	10.85	18.59	0.01
SQU-DS	2026-06-05 19:00:00	8.34	26.20	574.67	7.33	10.85	23.30	0.01
SQU-DS	2026-06-05 19:15:00	8.30	26.47	576.21	7.31	10.84	20.85	0.01
SQU-DS	2026-06-05 19:30:00	8.29	26.40	574.71	7.34	10.84	19.97	0.01
SQU-DS	2026-06-05 19:45:00	8.28	26.06	574.62	7.35	10.84	20.04	0.01
SQU-DS	2026-06-05 20:00:00	8.27	26.19	574.18	7.36	10.83	18.55	0.01
SQU-DS	2026-06-05 20:15:00	8.26	26.08	574.96	7.35	10.81	17.29	0.01
SQU-DS	2026-06-05 20:30:00	8.27	26.17	575.59	7.34	10.80	17.56	0.01
SQU-DS	2026-06-05 20:45:00	8.26	26.42	574.30	7.37	10.78	9.62	0.01
SQU-DS	2026-06-05 21:00:00	8.25	26.35	574.51	7.36	10.77	6.63	0.01
SQU-DS	2026-06-05 21:15:00	8.23	26.20	575.33	7.36	10.77	2.20	0.01
SQU-DS	2026-06-05 21:30:00	8.21	26.27	574.90	7.37	10.77	2.39	0.01
SQU-DS	2026-06-05 21:45:00	8.19	25.90	574.15	7.40	10.78	0.00	0.01
SQU-DS	2026-06-05 22:00:00	8.18	25.86	576.26	7.43	10.78	0.00	0.01
SQU-DS	2026-06-05 22:15:00	8.15	26.03	577.98	7.42	10.76	0.00	0.01
SQU-DS	2026-06-05 22:30:00	8.12	25.13	578.94	7.40	10.76	0.00	0.01
SQU-DS	2026-06-05 22:45:00	8.08	25.15	580.05	7.37	10.76	0.85	0.01
SQU-DS	2026-06-05 23:00:00	8.06	24.93	580.32	7.36	10.77	0.85	0.01
SQU-DS	2026-06-05 23:15:00	8.03	25.02	580.26	7.35	10.77	2.27	0.01
SQU-DS	2026-06-05 23:30:00	8.00	25.28	579.24	7.39	10.77	0.27	0.01
SQU-DS	2026-06-05 23:45:00	7.96	25.14	578.94	7.36	10.77	1.04	0.01
SQU-DS	2026-06-06 00:00:00	7.94	25.31	579.81	7.34	10.77	4.86	0.01
SQU-DS	2026-06-06 00:15:00	7.91	25.29	579.41	7.36	10.78	3.71	0.01
SQU-DS	2026-06-06 00:30:00	7.88	25.41	578.45	7.37	10.78	1.84	0.01
SQU-DS	2026-06-06 00:45:00	7.85	25.16	580.39	7.39	10.79	1.06	0.01
SQU-DS	2026-06-06 01:00:00	7.82	24.96	580.80	7.40	10.79	0.77	0.01
SQU-DS	2026-06-06 01:15:00	7.79	25.08	579.96	7.37	10.78	0.96	0.01
SQU-DS	2026-06-06 01:30:00	7.77	25.15	579.23	7.37	10.77	0.39	0.01
SQU-DS	2026-06-06 01:45:00	7.74	24.91	578.99	7.36	10.80	0.00	0.01
SQU-DS	2026-06-06 02:00:00	7.73	25.03	579.48	7.34	10.81	0.00	0.01
SQU-DS	2026-06-06 02:15:00	7.72	25.45	578.80	7.35	10.81	0.81	0.01
SQU-DS	2026-06-06 02:30:00	7.69	25.62	579.66	7.32	10.80	5.27	0.01
SQU-DS	2026-06-06 02:45:00	7.67	25.86	580.54	7.30	10.81	9.03	0.01
SQU-DS	2026-06-06 03:00:00	7.62	25.91	579.93	7.30	10.81	8.20	0.01
SQU-DS	2026-06-06 03:15:00	7.58	26.03	580.20	7.29	10.81	9.19	0.01
SQU-DS	2026-06-06 03:30:00	7.53	25.79	580.60	7.27	10.82	12.24	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-06 03:45:00	7.50	25.82	579.25	7.29	10.83	24.73	0.01
SQU-DS	2026-06-06 04:00:00	7.46	25.88	579.45	7.28	10.83	20.64	0.01
SQU-DS	2026-06-06 04:15:00	7.42	25.66	580.24	7.26	10.85	25.11	0.01
SQU-DS	2026-06-06 04:30:00	7.39	26.07	580.09	7.26	10.84	21.44	0.01
SQU-DS	2026-06-06 04:45:00	7.36	25.75	580.08	7.25	10.84	24.47	0.01
SQU-DS	2026-06-06 05:00:00	7.34	25.82	579.41	7.26	10.84	24.66	0.01
SQU-DS	2026-06-06 05:15:00	7.32	25.95	579.56	7.26	10.86	24.15	0.01
SQU-DS	2026-06-06 05:30:00	7.30	25.98	580.04	7.24	10.85	26.42	0.01
SQU-DS	2026-06-06 05:45:00	7.29	25.84	579.71	7.25	10.88	24.39	0.01
SQU-DS	2026-06-06 06:00:00	7.27	26.11	579.49	7.25	10.87	26.89	0.01
SQU-DS	2026-06-06 06:15:00	7.25	26.08	579.16	7.26	10.88	26.56	0.01
SQU-DS	2026-06-06 06:30:00	7.24	26.30	579.37	7.25	10.88	31.36	0.01
SQU-DS	2026-06-06 06:45:00	7.24	26.05	581.74	7.21	10.87	27.00	0.01
SQU-DS	2026-06-06 07:00:00	7.23	25.94	579.15	7.26	10.90	28.68	0.01
SQU-DS	2026-06-06 07:15:00	7.22	26.27	579.55	7.24	10.92	28.87	0.01
SQU-DS	2026-06-06 07:30:00	7.20	25.83	579.80	7.24	10.92	27.73	0.01
SQU-DS	2026-06-06 07:45:00	7.19	26.10	579.54	7.24	10.93	27.28	0.01
SQU-DS	2026-06-06 08:00:00	7.18	25.94	578.95	7.25	10.94	29.20	0.01
SQU-DS	2026-06-06 08:15:00	7.16	25.96	578.70	7.26	10.96	28.53	0.01
SQU-DS	2026-06-06 08:30:00	7.15	26.12	579.12	7.24	10.96	28.80	0.01
SQU-DS	2026-06-06 08:45:00	7.14	26.08	578.87	7.25	10.95	28.97	0.01
SQU-DS	2026-06-06 09:00:00	7.14	26.21	578.94	7.25	10.96	27.49	0.01
SQU-DS	2026-06-06 09:15:00	7.15	26.29	578.04	7.25	10.99	29.21	0.01
SQU-DS	2026-06-06 09:30:00	7.20	26.31	577.65	7.25	10.98	28.41	0.01
SQU-DS	2026-06-06 09:45:00	7.26	26.62	576.60	7.26	10.99	28.00	0.01
SQU-DS	2026-06-06 10:00:00	7.29	26.54	575.90	7.27	11.00	28.36	0.01
SQU-DS	2026-06-06 10:15:00	7.34	26.51	576.85	7.25	11.00	27.59	0.01
SQU-DS	2026-06-06 10:30:00	7.39	26.49	577.28	7.23	11.00	27.41	0.01
SQU-DS	2026-06-06 10:45:00	7.46	26.84	575.14	7.26	11.01	30.00	0.01
SQU-DS	2026-06-06 11:00:00	7.54	26.88	574.81	7.26	10.99	30.22	0.01
SQU-DS	2026-06-06 11:15:00	7.65	26.95	574.86	7.24	11.00	32.21	0.01
SQU-DS	2026-06-06 11:30:00	7.77	27.02	575.03	7.22	10.99	24.69	0.01
SQU-DS	2026-06-06 11:45:00	7.88	27.11	572.32	7.26	10.98	35.46	0.01
SQU-DS	2026-06-06 12:00:00	8.00	26.91	571.81	7.26	10.96	35.77	0.01
SQU-DS	2026-06-06 12:15:00	8.10	27.05	573.31	7.22	10.96	24.82	0.01
SQU-DS	2026-06-06 12:30:00	8.22	27.15	571.60	7.24	10.95	37.31	0.01
SQU-DS	2026-06-06 12:45:00	8.35	26.94	571.83	7.24	10.94	31.48	0.01
SQU-DS	2026-06-06 13:00:00	8.46	27.02	570.00	7.26	10.93	37.23	0.01
SQU-DS	2026-06-06 13:15:00	8.49	27.22	569.57	7.27	10.90	36.13	0.01
SQU-DS	2026-06-06 13:30:00	8.50	27.23	570.26	7.26	10.90	35.29	0.01
SQU-DS	2026-06-06 13:45:00	8.54	27.14	569.97	7.26	10.90	34.94	0.01
SQU-DS	2026-06-06 14:00:00	8.49	26.98	570.84	7.25	10.89	37.22	0.01
SQU-DS	2026-06-06 14:15:00	8.37	26.71	571.54	7.25	10.87	36.60	0.01
SQU-DS	2026-06-06 14:30:00	8.44	26.89	571.39	7.26	10.87	35.14	0.01
SQU-DS	2026-06-06 14:45:00	8.56	26.84	570.64	7.26	10.87	38.51	0.01
SQU-DS	2026-06-06 15:00:00	8.63	27.00	570.45	7.27	10.86	29.88	0.01
SQU-DS	2026-06-06 15:15:00	8.66	26.91	570.66	7.26	10.84	39.01	0.01
SQU-DS	2026-06-06 15:30:00	8.63	26.96	572.38	7.24	10.83	29.11	0.01
SQU-DS	2026-06-06 15:45:00	8.63	27.15	570.48	7.29	10.82	37.17	0.01
SQU-DS	2026-06-06 16:00:00	8.69	26.99	572.03	7.25	10.83	33.89	0.01
SQU-DS	2026-06-06 16:15:00	8.76	27.23	571.72	7.26	10.82	33.68	0.01
SQU-DS	2026-06-06 16:30:00	8.83	27.21	571.57	7.26	10.81	35.59	0.01
SQU-DS	2026-06-06 16:45:00	8.86	27.31	571.29	7.27	10.80	34.01	0.01
SQU-DS	2026-06-06 17:00:00	8.91	27.35	570.31	7.29	10.77	33.25	0.01
SQU-DS	2026-06-06 17:15:00	8.96	27.63	570.44	7.29	10.76	36.95	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-06 17:30:00	9.01	27.89	570.80	7.29	10.73	37.84	0.01
SQU-DS	2026-06-06 17:45:00	9.08	27.98	571.35	7.29	10.70	35.49	0.01
SQU-DS	2026-06-06 18:00:00	9.15	28.15	572.34	7.27	10.69	32.14	0.01
SQU-DS	2026-06-06 18:15:00	9.19	28.42	571.79	7.28	10.68	36.18	0.01
SQU-DS	2026-06-06 18:30:00	9.24	28.39	570.05	7.32	10.65	37.49	0.01
SQU-DS	2026-06-06 18:45:00	9.27	28.67	572.06	7.28	10.65	40.57	0.01
SQU-DS	2026-06-06 19:00:00	9.32	28.49	571.08	7.30	10.64	39.25	0.01
SQU-DS	2026-06-06 19:15:00	9.32	28.55	571.39	7.29	10.62	35.56	0.01
SQU-DS	2026-06-06 19:30:00	9.27	28.85	570.42	7.31	10.61	39.95	0.01
SQU-DS	2026-06-06 19:45:00	9.22	28.76	572.35	7.29	10.62	42.57	0.01
SQU-DS	2026-06-06 20:00:00	9.16	29.06	571.16	7.31	10.60	51.24	0.01
SQU-DS	2026-06-06 20:15:00	9.12	29.02	572.27	7.30	10.59	30.63	0.01
SQU-DS	2026-06-06 20:30:00	9.08	29.01	573.64	7.29	10.60	36.51	0.01
SQU-DS	2026-06-06 20:45:00	9.04	28.97	571.56	7.34	10.58	42.19	0.01
SQU-DS	2026-06-06 21:00:00	9.00	28.97	572.62	7.32	10.58	37.70	0.01
SQU-DS	2026-06-06 21:15:00	9.00	28.97	572.58	7.32	10.58	41.19	0.01
SQU-DS	2026-06-06 21:30:00	8.99	29.03	571.89	7.34	10.54	40.28	0.01
SQU-DS	2026-06-06 21:45:00	8.99	29.08	571.46	7.35	10.54	37.93	0.01
SQU-DS	2026-06-06 22:00:00	8.99	29.15	571.35	7.36	10.51	33.32	0.01
SQU-DS	2026-06-06 22:15:00	9.00	28.98	571.30	7.37	10.50	27.91	0.01
SQU-DS	2026-06-06 22:30:00	9.00	29.03	572.25	7.35	10.49	17.01	0.01
SQU-DS	2026-06-06 22:45:00	8.98	28.98	572.38	7.36	10.48	10.25	0.01
SQU-DS	2026-06-06 23:00:00	8.96	29.00	571.73	7.37	10.46	2.09	0.01
SQU-DS	2026-06-06 23:15:00	8.95	28.79	571.89	7.38	10.45	0.37	0.01
SQU-DS	2026-06-06 23:30:00	8.91	28.87	571.52	7.40	10.44	0.00	0.01
SQU-DS	2026-06-06 23:45:00	8.88	28.96	573.28	7.37	10.43	0.00	0.01
SQU-DS	2026-06-07 00:00:00	8.86	29.10	573.32	7.38	10.44	0.00	0.01
SQU-DS	2026-06-07 00:15:00	8.84	29.41	573.96	7.38	10.42	0.00	0.01
SQU-DS	2026-06-07 00:30:00	8.83	29.39	574.12	7.38	10.41	0.00	0.01
SQU-DS	2026-06-07 00:45:00	8.80	29.38	575.34	7.37	10.43	0.00	0.01
SQU-DS	2026-06-07 01:00:00	8.78	29.43	575.62	7.37	10.45	0.00	0.01
SQU-DS	2026-06-07 01:15:00	8.76	29.38	575.77	7.36	10.45	4.12	0.01
SQU-DS	2026-06-07 01:30:00	8.74	29.56	576.46	7.35	10.44	10.38	0.01
SQU-DS	2026-06-07 01:45:00	8.71	29.70	576.28	7.34	10.46	9.06	0.01
SQU-DS	2026-06-07 02:00:00	8.68	29.53	576.20	7.33	10.45	14.56	0.01
SQU-DS	2026-06-07 02:15:00	8.65	29.87	576.21	7.32	10.46	25.84	0.01
SQU-DS	2026-06-07 02:30:00	8.63	29.66	576.37	7.31	10.47	25.84	0.01
SQU-DS	2026-06-07 02:45:00	8.59	29.48	577.34	7.29	10.46	30.62	0.01
SQU-DS	2026-06-07 03:00:00	8.56	29.35	575.76	7.31	10.48	35.99	0.01
SQU-DS	2026-06-07 03:15:00	8.54	29.43	576.12	7.30	10.48	36.32	0.01
SQU-DS	2026-06-07 03:30:00	8.51	29.37	575.59	7.30	10.48	37.92	0.01
SQU-DS	2026-06-07 03:45:00	8.48	29.31	576.49	7.28	10.50	34.53	0.01
SQU-DS	2026-06-07 04:00:00	8.44	29.46	576.60	7.27	10.50	39.23	0.01
SQU-DS	2026-06-07 04:15:00	8.41	29.56	576.69	7.26	10.51	39.57	0.01
SQU-DS	2026-06-07 04:30:00	8.38	29.48	578.86	7.22	10.52	40.46	0.01
SQU-DS	2026-06-07 04:45:00	8.35	29.75	578.81	7.21	10.51	39.15	0.01
SQU-DS	2026-06-07 05:00:00	8.33	29.72	576.87	7.25	10.53	40.87	0.01
SQU-DS	2026-06-07 05:15:00	8.30	29.93	575.80	7.26	10.53	39.44	0.01
SQU-DS	2026-06-07 05:30:00	8.28	30.10	576.48	7.25	10.55	36.47	0.01
SQU-DS	2026-06-07 05:45:00	8.26	30.10	577.64	7.22	10.54	25.10	0.01
SQU-DS	2026-06-07 06:00:00	8.24	30.08	576.19	7.24	10.55	37.55	0.01
SQU-DS	2026-06-07 06:15:00	8.23	30.16	576.03	7.24	10.54	35.06	0.01
SQU-DS	2026-06-07 06:30:00	8.21	30.31	576.52	7.23	10.57	34.21	0.01
SQU-DS	2026-06-07 06:45:00	8.20	30.40	574.68	7.26	10.58	38.50	0.01
SQU-DS	2026-06-07 07:00:00	8.20	30.50	574.53	7.26	10.58	38.13	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-07 07:15:00	8.20	30.60	573.79	7.26	10.59	39.22	0.01
SQU-DS	2026-06-07 07:30:00	8.21	30.81	573.71	7.25	10.59	35.56	0.01
SQU-DS	2026-06-07 07:45:00	8.20	30.53	573.18	7.26	10.61	38.88	0.01
SQU-DS	2026-06-07 08:00:00	8.21	30.49	572.45	7.27	10.61	37.70	0.01
SQU-DS	2026-06-07 08:15:00	8.20	30.44	573.34	7.25	10.62	37.37	0.01
SQU-DS	2026-06-07 08:30:00	8.21	30.36	572.61	7.26	10.63	42.73	0.01
SQU-DS	2026-06-07 08:45:00	8.21	30.61	571.64	7.27	10.64	37.80	0.01
SQU-DS	2026-06-07 09:00:00	8.24	30.48	571.39	7.27	10.66	38.79	0.01
SQU-DS	2026-06-07 09:15:00	8.26	30.51	571.86	7.26	10.67	36.11	0.01
SQU-DS	2026-06-07 09:30:00	8.27	30.56	570.88	7.28	10.67	38.11	0.01
SQU-DS	2026-06-07 09:45:00	8.30	30.75	570.24	7.29	10.67	36.77	0.01
SQU-DS	2026-06-07 10:00:00	8.35	30.78	572.51	7.25	10.68	34.85	0.01
SQU-DS	2026-06-07 10:15:00	8.39	30.71	570.59	7.28	10.69	35.59	0.01
SQU-DS	2026-06-07 10:30:00	8.45	30.68	571.47	7.26	10.67	31.57	0.01
SQU-DS	2026-06-07 10:45:00	8.52	30.70	570.04	7.28	10.67	36.35	0.01
SQU-DS	2026-06-07 11:00:00	8.56	31.09	568.51	7.31	10.67	39.80	0.01
SQU-DS	2026-06-07 11:15:00	8.62	31.01	570.38	7.27	10.65	31.70	0.01
SQU-DS	2026-06-07 11:30:00	8.69	31.26	568.96	7.29	10.67	35.33	0.01
SQU-DS	2026-06-07 11:45:00	8.80	31.13	569.16	7.28	10.65	33.73	0.01
SQU-DS	2026-06-07 12:00:00	8.88	31.22	567.75	7.30	10.65	36.83	0.01
SQU-DS	2026-06-07 12:15:00	8.92	31.09	568.79	7.28	10.64	38.37	0.01
SQU-DS	2026-06-07 12:30:00	8.93	31.22	567.12	7.31	10.65	39.79	0.01
SQU-DS	2026-06-07 12:45:00	8.93	31.35	567.32	7.30	10.64	37.77	0.01
SQU-DS	2026-06-07 13:00:00	8.93	31.37	568.14	7.29	10.64	30.71	0.01
SQU-DS	2026-06-07 13:15:00	8.95	31.31	567.71	7.30	10.63	38.86	0.01
SQU-DS	2026-06-07 13:30:00	9.00	31.38	568.23	7.29	10.62	40.73	0.01
SQU-DS	2026-06-07 13:45:00	9.06	31.35	566.92	7.31	10.62	37.97	0.01
SQU-DS	2026-06-07 14:00:00	9.14	31.35	566.17	7.32	10.61	35.91	0.01
SQU-DS	2026-06-07 14:15:00	9.27	31.34	566.32	7.31	10.62	39.36	0.01
SQU-DS	2026-06-07 14:30:00	9.38	31.27	566.23	7.31	10.61	37.64	0.01
SQU-DS	2026-06-07 14:45:00	9.41	31.47	566.38	7.30	10.59	33.08	0.01
SQU-DS	2026-06-07 15:00:00	9.43	31.37	565.88	7.31	10.60	40.45	0.01
SQU-DS	2026-06-07 15:15:00	9.41	31.58	565.20	7.32	10.58	33.92	0.01
SQU-DS	2026-06-07 15:30:00	9.41	31.29	565.76	7.32	10.57	34.49	0.01
SQU-DS	2026-06-07 15:45:00	9.39	31.51	565.10	7.33	10.58	36.22	0.01
SQU-DS	2026-06-07 16:00:00	9.41	31.61	566.35	7.31	10.57	32.65	0.01
SQU-DS	2026-06-07 16:15:00	9.42	31.93	566.88	7.31	10.55	36.18	0.01
SQU-DS	2026-06-07 16:30:00	9.42	31.90	566.10	7.33	10.55	37.27	0.01
SQU-DS	2026-06-07 16:45:00	9.41	31.64	568.01	7.30	10.55	33.10	0.01
SQU-DS	2026-06-07 17:00:00	9.42	31.78	566.03	7.34	10.54	37.09	0.01
SQU-DS	2026-06-07 17:15:00	9.40	32.00	566.95	7.31	10.55	34.13	0.01
SQU-DS	2026-06-07 17:30:00	9.41	31.84	566.63	7.32	10.54	34.42	0.01
SQU-DS	2026-06-07 17:45:00	9.41	31.99	566.84	7.32	10.53	34.45	0.01
SQU-DS	2026-06-07 18:00:00	9.40	32.21	566.99	7.32	10.55	35.62	0.01
SQU-DS	2026-06-07 18:15:00	9.41	32.01	565.97	7.34	10.53	36.51	0.01
SQU-DS	2026-06-07 18:30:00	9.41	32.27	566.13	7.34	10.52	37.81	0.01
SQU-DS	2026-06-07 18:45:00	9.43	32.31	567.41	7.31	10.52	31.11	0.01
SQU-DS	2026-06-07 19:00:00	9.43	32.41	565.38	7.35	10.50	37.31	0.01
SQU-DS	2026-06-07 19:15:00	9.42	32.13	565.85	7.34	10.49	52.58	0.01
SQU-DS	2026-06-07 19:30:00	9.42	32.22	567.47	7.31	10.49	42.85	0.01
SQU-DS	2026-06-07 19:45:00	9.40	32.35	567.05	7.31	10.49	40.80	0.01
SQU-DS	2026-06-07 20:00:00	9.37	32.57	567.36	7.32	10.50	44.95	0.01
SQU-DS	2026-06-07 20:15:00	9.35	32.43	566.93	7.33	10.47	50.68	0.01
SQU-DS	2026-06-07 20:30:00	9.32	32.54	567.12	7.33	10.45	46.30	0.01
SQU-DS	2026-06-07 20:45:00	9.30	32.57	567.16	7.34	10.46	51.87	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-06-07 21:00:00	9.28	32.37	568.34	7.32	10.45	48.62	0.01
SQU-DS	2026-06-07 21:15:00	9.25	32.35	567.00	7.35	10.44	47.33	0.01
SQU-DS	2026-06-07 21:30:00	9.22	32.35	567.39	7.35	10.43	50.21	0.01
SQU-DS	2026-06-07 21:45:00	9.18	32.11	568.73	7.33	10.44	51.07	0.01
SQU-DS	2026-06-07 22:00:00	9.15	32.02	567.17	7.35	10.44	45.77	0.01
SQU-DS	2026-06-07 22:15:00	9.13	31.93	568.16	7.34	10.41	43.84	0.01
SQU-DS	2026-06-07 22:30:00	9.12	32.17	565.57	7.38	10.39	38.92	0.01
SQU-DS	2026-06-07 22:45:00	9.10	32.41	566.38	7.38	10.37	34.76	0.01
SQU-DS	2026-06-07 23:00:00	9.09	32.39	566.57	7.38	10.39	34.96	0.01
SQU-DS	2026-06-07 23:15:00	9.09	32.14	567.66	7.37	10.38	21.36	0.01
SQU-DS	2026-06-07 23:30:00	9.07	31.98	566.60	7.40	10.37	16.48	0.01
SQU-DS	2026-06-07 23:45:00	9.05	31.94	567.32	7.39	10.37	7.86	0.01
SQU-US	2026-06-01 00:00:00	9.80	32.60	0.42	7.19	11.24	14.06	0.01
SQU-US	2026-06-01 00:15:00	9.73	32.45	0.41	7.22	11.28	13.60	0.01
SQU-US	2026-06-01 00:30:00	9.67	32.55	0.42	7.21	11.30	12.98	0.01
SQU-US	2026-06-01 00:45:00	9.60	32.02	0.42	7.22	11.32	13.56	0.01
SQU-US	2026-06-01 01:00:00	9.53	29.57	0.42	7.19	11.33	13.06	0.01
SQU-US	2026-06-01 01:15:00	9.47	29.05	0.41	7.22	11.34	13.78	0.01
SQU-US	2026-06-01 01:30:00	9.40	29.14	0.42	7.21	11.37	14.63	0.01
SQU-US	2026-06-01 01:45:00	9.34	28.69	0.43	7.21	11.38	14.65	0.01
SQU-US	2026-06-01 02:00:00	9.28	31.11	0.43	7.23	11.39	14.55	0.01
SQU-US	2026-06-01 02:15:00	9.22	30.89	0.43	7.24	11.41	14.72	0.01
SQU-US	2026-06-01 02:30:00	9.16	30.57	0.43	7.23	11.43	13.85	0.01
SQU-US	2026-06-01 02:45:00	9.09	30.54	0.43	7.24	11.45	14.21	0.01
SQU-US	2026-06-01 03:00:00	9.02	30.43	0.44	7.23	11.48	14.82	0.01
SQU-US	2026-06-01 03:15:00	8.96	30.31	0.41	7.25	11.49	15.79	0.01
SQU-US	2026-06-01 03:30:00	8.89	30.17	0.42	7.23	11.51	18.08	0.01
SQU-US	2026-06-01 03:45:00	8.83	30.18	0.42	7.24	11.53	16.16	0.01
SQU-US	2026-06-01 04:00:00	8.78	27.57	0.43	7.22	11.54	16.61	0.01
SQU-US	2026-06-01 04:15:00	8.73	27.36	0.42	7.25	11.56	15.51	0.01
SQU-US	2026-06-01 04:30:00	8.67	27.37	0.42	7.24	11.58	14.68	0.01
SQU-US	2026-06-01 04:45:00	8.60	27.29	0.43	7.27	11.59	14.06	0.01
SQU-US	2026-06-01 05:00:00	8.56	29.91	0.44	7.22	11.60	15.28	0.01
SQU-US	2026-06-01 05:15:00	8.50	29.81	0.41	7.24	11.63	14.59	0.01
SQU-US	2026-06-01 05:30:00	8.47	30.12	0.42	7.23	11.62	14.72	0.01
SQU-US	2026-06-01 05:45:00	8.43	29.86	0.42	7.23	11.64	14.77	0.01
SQU-US	2026-06-01 06:00:00	8.39	27.47	0.43	7.22	11.66	16.03	0.01
SQU-US	2026-06-01 06:15:00	8.36	27.72	0.42	7.21	11.65	15.32	0.01
SQU-US	2026-06-01 06:30:00	8.32	27.62	0.42	7.24	11.67	14.72	0.01
SQU-US	2026-06-01 06:45:00	8.28	27.84	0.43	7.21	11.68	13.93	0.01
SQU-US	2026-06-01 07:00:00	8.30	27.84	0.43	7.20	11.68	15.07	0.01
SQU-US	2026-06-01 07:15:00	8.27	28.00	0.42	7.22	11.70	14.62	0.01
SQU-US	2026-06-01 07:30:00	8.26	28.02	0.42	7.22	11.70	14.57	0.01
SQU-US	2026-06-01 07:45:00	8.26	27.89	0.42	7.24	11.73	14.34	0.01
SQU-US	2026-06-01 08:00:00	8.27	30.24	0.43	7.22	11.75	14.06	0.01
SQU-US	2026-06-01 08:15:00	8.30	30.18	0.43	7.24	11.77	13.89	0.01
SQU-US	2026-06-01 08:30:00	8.33	30.57	0.43	7.20	11.78	13.70	0.01
SQU-US	2026-06-01 08:45:00	8.38	30.58	0.43	7.23	11.79	13.62	0.01
SQU-US	2026-06-01 09:00:00	8.42	28.51	0.43	7.26	11.80	14.98	0.01
SQU-US	2026-06-01 09:15:00	8.50	28.44	0.41	7.26	11.80	15.49	0.01
SQU-US	2026-06-01 09:30:00	8.57	28.42	0.42	7.26	11.81	14.23	0.01
SQU-US	2026-06-01 09:45:00	8.64	28.71	0.42	7.27	11.79	14.36	0.01
SQU-US	2026-06-01 10:00:00	8.72	31.35	0.43	7.26	11.80	15.02	0.01
SQU-US	2026-06-01 10:15:00	8.80	31.22	0.43	7.27	11.79	14.14	0.01
SQU-US	2026-06-01 10:30:00	8.87	31.33	0.43	7.26	11.80	14.08	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-01 10:45:00	8.95	31.26	0.43	7.26	11.78	13.58	0.01
SQU-US	2026-06-01 11:00:00	9.03	28.89	0.43	7.28	11.77	13.78	0.01
SQU-US	2026-06-01 11:15:00	9.11	28.33	0.41	7.28	11.77	14.01	0.01
SQU-US	2026-06-01 11:30:00	9.20	28.21	0.41	7.27	11.78	14.05	0.01
SQU-US	2026-06-01 11:45:00	9.30	28.00	0.42	7.27	11.76	13.14	0.01
SQU-US	2026-06-01 12:00:00	9.39	28.30	0.42	7.28	11.75	13.10	0.01
SQU-US	2026-06-01 12:15:00	9.48	28.24	0.42	7.29	11.77	12.77	0.01
SQU-US	2026-06-01 12:30:00	9.58	28.41	0.42	7.27	11.74	12.68	0.01
SQU-US	2026-06-01 12:45:00	9.67	28.14	0.42	7.28	11.74	13.15	0.01
SQU-US	2026-06-01 13:00:00	9.77	31.14	0.42	7.27	11.74	13.56	0.01
SQU-US	2026-06-01 13:15:00	9.85	31.02	0.38	7.30	11.72	14.41	0.01
SQU-US	2026-06-01 13:30:00	9.94	31.14	0.40	7.30	11.70	13.63	0.01
SQU-US	2026-06-01 13:45:00	10.03	30.94	0.40	7.31	11.69	14.48	0.01
SQU-US	2026-06-01 14:00:00	10.11	28.75	0.41	7.27	11.68	14.01	0.01
SQU-US	2026-06-01 14:15:00	10.19	28.64	0.41	7.28	11.66	12.77	0.01
SQU-US	2026-06-01 14:30:00	10.28	28.59	0.41	7.26	11.64	12.72	0.01
SQU-US	2026-06-01 14:45:00	10.36	28.23	0.42	7.27	11.64	12.71	0.01
SQU-US	2026-06-01 15:00:00	10.46	28.25	0.42	7.28	11.62	13.00	0.01
SQU-US	2026-06-01 15:15:00	10.51	28.28	0.40	7.27	11.61	12.73	0.01
SQU-US	2026-06-01 15:30:00	10.57	28.40	0.41	7.30	11.59	12.83	0.01
SQU-US	2026-06-01 15:45:00	10.64	28.47	0.41	7.29	11.57	12.90	0.01
SQU-US	2026-06-01 16:00:00	10.70	31.05	0.42	7.29	11.54	14.31	0.01
SQU-US	2026-06-01 16:15:00	10.74	30.62	0.41	7.32	11.55	13.98	0.01
SQU-US	2026-06-01 16:30:00	10.77	30.64	0.42	7.33	11.52	13.98	0.01
SQU-US	2026-06-01 16:45:00	10.83	30.87	0.42	7.32	11.52	13.85	0.01
SQU-US	2026-06-01 17:00:00	10.88	28.43	0.42	7.30	11.49	13.86	0.01
SQU-US	2026-06-01 17:15:00	10.91	28.34	0.40	7.29	11.49	13.09	0.01
SQU-US	2026-06-01 17:30:00	10.95	28.32	0.41	7.28	11.46	13.34	0.01
SQU-US	2026-06-01 17:45:00	10.98	28.17	0.42	7.28	11.44	12.65	0.01
SQU-US	2026-06-01 18:00:00	11.01	30.63	0.42	7.28	11.43	13.68	0.01
SQU-US	2026-06-01 18:15:00	11.02	30.40	0.41	7.33	11.41	13.24	0.01
SQU-US	2026-06-01 18:30:00	11.03	30.46	0.42	7.36	11.39	13.31	0.01
SQU-US	2026-06-01 18:45:00	11.05	30.45	0.42	7.35	11.37	13.12	0.01
SQU-US	2026-06-01 19:00:00	11.05	30.66	0.42	7.32	11.36	13.65	0.01
SQU-US	2026-06-01 19:15:00	11.06	30.82	0.38	7.35	11.35	12.92	0.01
SQU-US	2026-06-01 19:30:00	11.05	31.03	0.40	7.37	11.33	13.22	0.01
SQU-US	2026-06-01 19:45:00	11.04	31.15	0.41	7.37	11.31	12.90	0.01
SQU-US	2026-06-01 20:00:00			0.41	7.37		13.54	
SQU-US	2026-06-01 20:15:00	11.02	28.98	0.41	7.33	11.27	13.32	0.01
SQU-US	2026-06-01 20:30:00	10.99	29.63	0.42	7.34	11.23	13.16	0.01
SQU-US	2026-06-01 20:45:00	10.99	30.16	0.42	7.35	11.21	13.28	0.01
SQU-US	2026-06-01 21:00:00	10.95	31.97	0.42	7.35	11.19	13.59	0.01
SQU-US	2026-06-01 21:15:00	10.93	32.39	0.40	7.33	11.17	12.95	0.01
SQU-US	2026-06-01 21:30:00	10.90	32.45	0.41	7.34	11.14	12.60	0.01
SQU-US	2026-06-01 21:45:00	10.87	32.16	0.41	7.35	11.13	12.49	0.01
SQU-US	2026-06-01 22:00:00	10.84	31.12	0.42	7.34	11.12	12.41	0.01
SQU-US	2026-06-01 22:15:00	10.80	30.79	0.42	7.33	11.11	12.66	0.01
SQU-US	2026-06-01 22:30:00	10.76	30.77	0.42	7.32	11.10	12.42	0.01
SQU-US	2026-06-01 22:45:00	10.72	30.64	0.43	7.31	11.09	12.61	0.01
SQU-US	2026-06-01 23:00:00	10.68	33.00	0.40	7.26	11.09	12.21	0.01
SQU-US	2026-06-01 23:15:00	10.62	33.59	0.38	7.24	11.07	12.02	0.01
SQU-US	2026-06-01 23:30:00	10.56	33.70	0.40	7.22	11.08	12.01	0.01
SQU-US	2026-06-01 23:45:00	10.50	33.52	0.41	7.20	11.06	11.86	0.01
SQU-US	2026-06-02 00:00:00	10.44	30.27	0.41	7.23	11.06	11.88	0.01
SQU-US	2026-06-02 00:15:00	10.37	30.40	0.40	7.21	11.09	11.69	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-02 00:30:00	10.29	29.95	0.41	7.22	11.10	11.32	0.01
SQU-US	2026-06-02 00:45:00	10.22	29.48	0.41	7.23	11.12	11.61	0.01
SQU-US	2026-06-02 01:00:00	10.15	31.72	0.42	7.22	11.14	11.80	0.01
SQU-US	2026-06-02 01:15:00	10.08	31.51	0.39	7.26	11.17	11.31	0.01
SQU-US	2026-06-02 01:30:00	10.03	31.10	0.40	7.25	11.19	11.29	0.01
SQU-US	2026-06-02 01:45:00	9.96	30.99	0.41	7.25	11.20	11.24	0.01
SQU-US	2026-06-02 02:00:00	9.89	27.88	0.42	7.24	11.22	11.79	0.01
SQU-US	2026-06-02 02:15:00	9.84	27.77	0.41	7.23	11.24	11.36	0.01
SQU-US	2026-06-02 02:30:00	9.78	27.60	0.42	7.23	11.26	11.22	0.01
SQU-US	2026-06-02 02:45:00	9.72	27.21	0.43	7.22	11.28	11.09	0.01
SQU-US	2026-06-02 03:00:00	9.66	28.66	0.42	7.24	11.29	11.33	0.01
SQU-US	2026-06-02 03:15:00	9.60	28.66	0.39	7.25	11.31	11.12	0.01
SQU-US	2026-06-02 03:30:00	9.53	28.45	0.40	7.26	11.33	11.07	0.01
SQU-US	2026-06-02 03:45:00	9.47	28.28	0.41	7.23	11.35	11.12	0.01
SQU-US	2026-06-02 04:00:00	9.42	27.09	0.42	7.26	11.36	11.02	0.01
SQU-US	2026-06-02 04:15:00	9.36	27.04	0.42	7.23	11.37	10.89	0.01
SQU-US	2026-06-02 04:30:00	9.30	26.84	0.43	7.23	11.39	11.07	0.01
SQU-US	2026-06-02 04:45:00	9.27	26.84	0.43	7.24	11.40	11.07	0.01
SQU-US	2026-06-02 05:00:00	9.21	28.11	0.44	7.25	11.42	10.96	0.01
SQU-US	2026-06-02 05:15:00	9.15	27.88	0.44	7.23	11.43	10.78	0.01
SQU-US	2026-06-02 05:30:00	9.11	28.04	0.44	7.27	11.44	10.83	0.01
SQU-US	2026-06-02 05:45:00	9.06	28.26	0.44	7.24	11.44	10.83	0.01
SQU-US	2026-06-02 06:00:00	9.02	28.73	0.45	7.25	11.46	10.77	0.01
SQU-US	2026-06-02 06:15:00	9.00	29.08	0.44	7.28	11.47	10.49	0.01
SQU-US	2026-06-02 06:30:00	8.95	29.18	0.45	7.28	11.48	10.38	0.01
SQU-US	2026-06-02 06:45:00	8.94	29.30	0.45	7.25	11.49	10.50	0.01
SQU-US	2026-06-02 07:00:00	8.91	27.27	0.45	7.23	11.50	10.29	0.01
SQU-US	2026-06-02 07:15:00	8.90	27.35	0.45	7.20	11.51	10.10	0.01
SQU-US	2026-06-02 07:30:00	8.90	27.41	0.45	7.23	11.52	9.99	0.01
SQU-US	2026-06-02 07:45:00	8.90	27.37	0.45	7.22	11.53	10.20	0.01
SQU-US	2026-06-02 08:00:00	8.90	29.39	0.44	7.23	11.53	9.97	0.01
SQU-US	2026-06-02 08:15:00	8.93	29.23	0.45	7.21	11.54	10.06	0.01
SQU-US	2026-06-02 08:30:00	8.96	29.52	0.44	7.22	11.56	9.99	0.01
SQU-US	2026-06-02 08:45:00	8.99	29.71	0.44	7.22	11.56	10.09	0.01
SQU-US	2026-06-02 09:00:00	9.04	29.58	0.44	7.22	11.58	10.45	0.01
SQU-US	2026-06-02 09:15:00	9.10	29.98	0.40	7.25	11.58	10.82	0.01
SQU-US	2026-06-02 09:30:00	9.16	29.62	0.41	7.27	11.60	10.88	0.01
SQU-US	2026-06-02 09:45:00	9.21	29.48	0.42	7.26	11.60	10.84	0.01
SQU-US	2026-06-02 10:00:00	9.28	27.20	0.42	7.27	11.59	10.54	0.01
SQU-US	2026-06-02 10:15:00	9.36	27.00	0.42	7.22	11.59	10.48	0.01
SQU-US	2026-06-02 10:30:00	9.42	26.80	0.43	7.24	11.59	10.24	0.01
SQU-US	2026-06-02 10:45:00	9.49	26.96	0.43	7.23	11.60	11.11	0.01
SQU-US	2026-06-02 11:00:00	9.56	27.53	0.43	7.26	11.60	10.07	0.01
SQU-US	2026-06-02 11:15:00	9.63	27.34	0.43	7.26	11.60	10.18	0.01
SQU-US	2026-06-02 11:30:00	9.72	27.25	0.43	7.26	11.59	10.24	0.01
SQU-US	2026-06-02 11:45:00	9.81	27.41	0.43	7.28	11.58	10.48	0.01
SQU-US	2026-06-02 12:00:00	9.90	27.78	0.43	7.27	11.58	10.19	0.01
SQU-US	2026-06-02 12:15:00	9.99	27.76	0.43	7.27	11.56	10.22	0.01
SQU-US	2026-06-02 12:30:00	10.08	27.64	0.43	7.28	11.55	10.01	0.01
SQU-US	2026-06-02 12:45:00	10.18	27.56	0.43	7.28	11.54	10.22	0.01
SQU-US	2026-06-02 13:00:00	10.27	26.87	0.43	7.28	11.54	11.16	0.01
SQU-US	2026-06-02 13:15:00	10.35	26.90	0.43	7.28	11.52	11.01	0.01
SQU-US	2026-06-02 13:30:00	10.44	26.88	0.43	7.26	11.52	10.59	0.01
SQU-US	2026-06-02 13:45:00	10.53	26.71	0.43	7.29	11.51	10.33	0.01
SQU-US	2026-06-02 14:00:00	10.62	26.76	0.43	7.30	11.49	11.40	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-02 14:15:00	10.71	26.61	0.43	7.29	11.48	11.36	0.01
SQU-US	2026-06-02 14:30:00	10.79	26.86	0.43	7.29	11.46	11.04	0.01
SQU-US	2026-06-02 14:45:00	10.87	27.02	0.43	7.30	11.46	11.21	0.01
SQU-US	2026-06-02 15:00:00	10.96	27.18	0.43	7.28	11.41	10.90	0.01
SQU-US	2026-06-02 15:15:00	11.04	27.05	0.43	7.29	11.40	11.14	0.01
SQU-US	2026-06-02 15:30:00	11.11	27.14	0.43	7.30	11.39	10.95	0.01
SQU-US	2026-06-02 15:45:00	11.18	26.82	0.43	7.29	11.38	10.93	0.01
SQU-US	2026-06-02 16:00:00	11.24	26.96	0.43	7.30	11.37	11.15	0.01
SQU-US	2026-06-02 16:15:00	11.30	26.96	0.43	7.30	11.34	11.01	0.01
SQU-US	2026-06-02 16:30:00	11.35	27.01	0.43	7.30	11.33	10.79	0.01
SQU-US	2026-06-02 16:45:00	11.40	27.21	0.43	7.28	11.31	10.73	0.01
SQU-US	2026-06-02 17:00:00	11.44	27.21	0.43	7.31	11.30	10.86	0.01
SQU-US	2026-06-02 17:15:00	11.48	27.37	0.43	7.31	11.26	10.58	0.01
SQU-US	2026-06-02 17:30:00	11.51	27.11	0.43	7.31	11.25	11.03	0.01
SQU-US	2026-06-02 17:45:00	11.53	26.94	0.43	7.30	11.24	10.67	0.01
SQU-US	2026-06-02 18:00:00	11.55	27.04	0.43	7.33	11.22	10.72	0.01
SQU-US	2026-06-02 18:15:00	11.55	27.51	0.43	7.33	11.20	10.58	0.01
SQU-US	2026-06-02 18:30:00	11.56	27.53	0.43	7.33	11.17	10.72	0.01
SQU-US	2026-06-02 18:45:00	11.55	27.37	0.43	7.35	11.18	10.52	0.01
SQU-US	2026-06-02 19:00:00	11.55	27.31	0.43	7.36	11.15	10.51	0.01
SQU-US	2026-06-02 19:15:00	11.55	27.34	0.44	7.35	11.12	10.49	0.01
SQU-US	2026-06-02 19:30:00	11.53	27.54	0.44	7.34	11.10	10.79	0.01
SQU-US	2026-06-02 19:45:00	11.53	27.61	0.44	7.35	11.06	10.90	0.01
SQU-US	2026-06-02 20:00:00	11.51	27.95	0.44	7.37	11.05	10.53	0.01
SQU-US	2026-06-02 20:15:00	11.49	27.72	0.44	7.35	11.01	10.58	0.01
SQU-US	2026-06-02 20:30:00	11.47	28.00	0.44	7.36	10.99	10.83	0.01
SQU-US	2026-06-02 20:45:00	11.45	28.09	0.44	7.34	10.97	10.73	0.01
SQU-US	2026-06-02 21:00:00	11.41	28.25	0.44	7.35	10.95	10.78	0.01
SQU-US	2026-06-02 21:15:00	11.38	28.44	0.44	7.35	10.94	10.75	0.01
SQU-US	2026-06-02 21:30:00	11.33	28.57	0.44	7.34	10.93	10.98	0.01
SQU-US	2026-06-02 21:45:00	11.27	28.56	0.44	7.34	10.93	10.88	0.01
SQU-US	2026-06-02 22:00:00	11.22	28.47	0.44	7.34	10.92	10.50	0.01
SQU-US	2026-06-02 22:15:00	11.16	28.26	0.45	7.32	10.91	10.64	0.01
SQU-US	2026-06-02 22:30:00	11.09	28.06	0.45	7.32	10.93	10.78	0.01
SQU-US	2026-06-02 22:45:00	11.02	27.82	0.45	7.33	10.93	10.72	0.01
SQU-US	2026-06-02 23:00:00	10.96	27.99	0.45	7.33	10.94	10.57	0.01
SQU-US	2026-06-02 23:15:00	10.89	27.08	0.45	7.33	10.96	10.43	0.01
SQU-US	2026-06-02 23:30:00	10.79	27.23	0.45	7.30	10.97	10.70	0.01
SQU-US	2026-06-02 23:45:00	10.70	26.92	0.45	7.29	10.98	10.78	0.01
SQU-US	2026-06-03 00:00:00	10.63	26.68	0.45	7.29	11.01	10.45	0.01
SQU-US	2026-06-03 00:15:00	10.56	26.09	0.45	7.27	11.02	10.50	0.01
SQU-US	2026-06-03 00:30:00	10.49	25.97	0.45	7.26	11.03	10.57	0.01
SQU-US	2026-06-03 00:45:00	10.40	25.73	0.45	7.27	11.06	10.31	0.01
SQU-US	2026-06-03 01:00:00	10.32	25.89	0.45	7.26	11.08	10.50	0.01
SQU-US	2026-06-03 01:15:00	10.25	25.51	0.46	7.23	11.10	10.41	0.01
SQU-US	2026-06-03 01:30:00	10.19	25.32	0.46	7.23	11.12	10.75	0.01
SQU-US	2026-06-03 01:45:00	10.09	25.13	0.46	7.23	11.14	10.75	0.01
SQU-US	2026-06-03 02:00:00	10.01	25.25	0.46	7.24	11.15	10.67	0.01
SQU-US	2026-06-03 02:15:00	9.93	24.94	0.46	7.23	11.18	10.58	0.01
SQU-US	2026-06-03 02:30:00	9.86	24.80	0.46	7.22	11.20	10.65	0.01
SQU-US	2026-06-03 02:45:00	9.80	24.49	0.46	7.22	11.23	10.66	0.01
SQU-US	2026-06-03 03:00:00	9.71	24.69	0.46	7.26	11.25	10.52	0.01
SQU-US	2026-06-03 03:15:00	9.63	24.79	0.46	7.25	11.27	10.80	0.01
SQU-US	2026-06-03 03:30:00	9.58	24.35	0.46	7.26	11.30	10.77	0.01
SQU-US	2026-06-03 03:45:00	9.54	24.51	0.46	7.26	11.31	11.02	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-03 04:00:00	9.46	24.31	0.46	7.26	11.33	10.64	0.01
SQU-US	2026-06-03 04:15:00	9.41	24.05	0.46	7.25	11.34	10.48	0.01
SQU-US	2026-06-03 04:30:00	9.36	24.10	0.46	7.25	11.34	10.54	0.01
SQU-US	2026-06-03 04:45:00	9.33	24.15	0.46	7.26	11.34	10.65	0.01
SQU-US	2026-06-03 05:00:00	9.31	23.93	0.46	7.26	11.36	10.41	0.01
SQU-US	2026-06-03 05:15:00	9.24	24.14	0.47	7.25	11.38	10.19	0.01
SQU-US	2026-06-03 05:30:00	9.20	24.16	0.46	7.26	11.39	10.10	0.01
SQU-US	2026-06-03 05:45:00	9.13	24.09	0.46	7.27	11.40	10.24	0.01
SQU-US	2026-06-03 06:00:00	9.12	23.97	0.46	7.25	11.41	10.06	0.01
SQU-US	2026-06-03 06:15:00	9.10	23.90	0.47	7.25	11.42	10.23	0.01
SQU-US	2026-06-03 06:30:00	9.06	23.85	0.47	7.25	11.44	10.13	0.01
SQU-US	2026-06-03 06:45:00	9.08	23.78	0.47	7.25	11.45	9.99	0.01
SQU-US	2026-06-03 07:00:00	9.04	24.09	0.47	7.24	11.46	10.45	0.01
SQU-US	2026-06-03 07:15:00	9.00	23.98	0.47	7.26	11.47	9.98	0.01
SQU-US	2026-06-03 07:30:00	8.99	23.86	0.47	7.24	11.49	10.02	0.01
SQU-US	2026-06-03 07:45:00	8.98	23.62	0.47	7.24	11.51	9.88	0.01
SQU-US	2026-06-03 08:00:00	8.97	24.26	0.46	7.26	11.51	9.99	0.01
SQU-US	2026-06-03 08:15:00	8.97	24.19	0.47	7.25	11.50	9.74	0.01
SQU-US	2026-06-03 08:30:00	8.94	24.10	0.47	7.24	11.51	9.81	0.01
SQU-US	2026-06-03 08:45:00	8.96	24.42	0.47	7.22	11.52	10.10	0.01
SQU-US	2026-06-03 09:00:00	8.99	24.40	0.47	7.19	11.53	9.76	0.01
SQU-US	2026-06-03 09:15:00	8.95	24.51	0.46	7.23	11.55	9.90	0.01
SQU-US	2026-06-03 09:30:00	8.95	24.78	0.46	7.22	11.54	10.47	0.01
SQU-US	2026-06-03 09:45:00	8.94	25.04	0.46	7.19	11.54	9.90	0.01
SQU-US	2026-06-03 10:00:00	8.95	24.66	0.46	7.21	11.55	10.42	0.01
SQU-US	2026-06-03 10:15:00	9.05	24.44	0.46	7.20	11.55	10.39	0.01
SQU-US	2026-06-03 10:30:00	9.05	24.68	0.46	7.21	11.56	10.05	0.01
SQU-US	2026-06-03 10:45:00	9.07	24.87	0.46	7.21	11.57	10.59	0.01
SQU-US	2026-06-03 11:00:00	9.11	24.97	0.45	7.23	11.58	10.27	0.01
SQU-US	2026-06-03 11:15:00	9.15	24.74	0.45	7.23	11.59	10.44	0.01
SQU-US	2026-06-03 11:30:00	9.16	24.48	0.45	7.23	11.60	10.17	0.01
SQU-US	2026-06-03 11:45:00	9.13	24.66	0.45	7.21	11.60	10.07	0.01
SQU-US	2026-06-03 12:00:00	9.13	25.06	0.45	7.22	11.59	9.98	0.01
SQU-US	2026-06-03 12:15:00	9.13	24.92	0.45	7.21	11.59	9.83	0.01
SQU-US	2026-06-03 12:30:00	9.17	24.64	0.45	7.22	11.59	10.06	0.01
SQU-US	2026-06-03 12:45:00	9.20	25.20	0.45	7.21	11.59	10.44	0.01
SQU-US	2026-06-03 13:00:00	9.17	24.81	0.45	7.22	11.59	9.57	0.01
SQU-US	2026-06-03 13:15:00	9.18	24.48	0.45	7.24	11.59	10.11	0.01
SQU-US	2026-06-03 13:30:00	9.18	24.47	0.45	7.22	11.60	9.91	0.01
SQU-US	2026-06-03 13:45:00	9.16	24.70	0.45	7.22	11.59	9.69	0.01
SQU-US	2026-06-03 14:00:00	9.16	24.68	0.45	7.24	11.60	10.21	0.01
SQU-US	2026-06-03 14:15:00	9.13	24.87	0.45	7.23	11.59	9.94	0.01
SQU-US	2026-06-03 14:30:00	9.11	25.00	0.45	7.24	11.59	9.93	0.01
SQU-US	2026-06-03 14:45:00	9.13	25.01	0.45	7.21	11.58	9.86	0.01
SQU-US	2026-06-03 15:00:00	9.18	24.93	0.45	7.24	11.59	9.80	0.01
SQU-US	2026-06-03 15:15:00	9.24	25.17	0.45	7.21	11.59	9.72	0.01
SQU-US	2026-06-03 15:30:00	9.28	25.37	0.45	7.23	11.59	9.55	0.01
SQU-US	2026-06-03 15:45:00	9.33	25.15	0.45	7.23	11.58	9.66	0.01
SQU-US	2026-06-03 16:00:00	9.37	24.84	0.45	7.26	11.59	9.70	0.01
SQU-US	2026-06-03 16:15:00	9.40	25.04	0.45	7.25	11.59	9.64	0.01
SQU-US	2026-06-03 16:30:00	9.41	25.13	0.45	7.25	11.58	10.78	0.01
SQU-US	2026-06-03 16:45:00	9.40	25.33	0.45	7.26	11.58	10.17	0.01
SQU-US	2026-06-03 17:00:00	9.39	24.96	0.45	7.26	11.59	10.23	0.01
SQU-US	2026-06-03 17:15:00	9.38	25.32	0.45	7.25	11.58	10.40	0.01
SQU-US	2026-06-03 17:30:00	9.36	25.29	0.45	7.26	11.58	10.52	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-03 17:45:00	9.34	25.22	0.45	7.27	11.56	11.56	0.01
SQU-US	2026-06-03 18:00:00	9.34	25.57	0.45	7.25	11.56	10.12	0.01
SQU-US	2026-06-03 18:15:00	9.34	25.82	0.46	7.24	11.55	9.96	0.01
SQU-US	2026-06-03 18:30:00	9.36	25.58	0.46	7.25	11.54	9.86	0.01
SQU-US	2026-06-03 18:45:00	9.37	25.98	0.45	7.28	11.54	9.82	0.01
SQU-US	2026-06-03 19:00:00	9.40	25.75	0.45	7.30	11.54	9.82	0.01
SQU-US	2026-06-03 19:15:00	9.41	25.61	0.45	7.30	11.53	10.35	0.01
SQU-US	2026-06-03 19:30:00	9.41	26.13	0.45	7.32	11.54	9.97	0.01
SQU-US	2026-06-03 19:45:00	9.41	25.77	0.46	7.31	11.53	10.04	0.01
SQU-US	2026-06-03 20:00:00	9.41	25.58	0.46	7.29	11.53	9.92	0.01
SQU-US	2026-06-03 20:15:00	9.40	25.82	0.46	7.31	11.53	9.52	0.01
SQU-US	2026-06-03 20:30:00	9.39	25.92	0.46	7.32	11.51	9.71	0.01
SQU-US	2026-06-03 20:45:00	9.37	26.21	0.46	7.31	11.50	9.75	0.01
SQU-US	2026-06-03 21:00:00	9.36	26.23	0.46	7.33	11.47	9.84	0.01
SQU-US	2026-06-03 21:15:00	9.34	26.10	0.46	7.31	11.48	9.78	0.01
SQU-US	2026-06-03 21:30:00	9.30	26.58	0.46	7.31	11.45	9.70	0.01
SQU-US	2026-06-03 21:45:00	9.28	26.89	0.46	7.30	11.46	9.64	0.01
SQU-US	2026-06-03 22:00:00	9.26	26.98	0.46	7.30	11.44	9.73	0.01
SQU-US	2026-06-03 22:15:00	9.24	26.99	0.46	7.30	11.44	9.70	0.01
SQU-US	2026-06-03 22:30:00	9.21	27.15	0.46	7.29	11.45	9.70	0.01
SQU-US	2026-06-03 22:45:00	9.21	27.29	0.46	7.31	11.44	9.63	0.01
SQU-US	2026-06-03 23:00:00	9.18	27.27	0.46	7.32	11.44	9.51	0.01
SQU-US	2026-06-03 23:15:00	9.18	26.61	0.46	7.29	11.43	10.26	0.01
SQU-US	2026-06-03 23:30:00	9.15	27.17	0.46	7.28	11.44	10.06	0.01
SQU-US	2026-06-03 23:45:00	9.14	27.24	0.47	7.27	11.43	10.08	0.01
SQU-US	2026-06-04 00:00:00	9.12	26.58	0.46	7.28	11.44	10.09	0.01
SQU-US	2026-06-04 00:15:00	9.09	26.56	0.47	7.27	11.45	10.09	0.01
SQU-US	2026-06-04 00:30:00	9.07	26.30	0.47	7.27	11.45	10.20	0.01
SQU-US	2026-06-04 00:45:00	9.06	26.17	0.47	7.26	11.45	10.58	0.01
SQU-US	2026-06-04 01:00:00	9.03	26.16	0.47	7.25	11.46	10.61	0.01
SQU-US	2026-06-04 01:15:00	9.00	26.19	0.47	7.23	11.45	10.20	0.01
SQU-US	2026-06-04 01:30:00	8.99	25.94	0.47	7.24	11.46	10.22	0.01
SQU-US	2026-06-04 01:45:00	8.96	26.66	0.47	7.23	11.44	10.15	0.01
SQU-US	2026-06-04 02:00:00	8.95	26.39	0.47	7.21	11.44	10.43	0.01
SQU-US	2026-06-04 02:15:00	8.93	25.77	0.47	7.20	11.44	9.52	0.01
SQU-US	2026-06-04 02:30:00	8.91	26.02	0.47	7.19	11.45	10.04	0.01
SQU-US	2026-06-04 02:45:00	8.91	25.56	0.47	7.20	11.47	9.55	0.01
SQU-US	2026-06-04 03:00:00	8.88	25.75	0.47	7.21	11.46	9.45	0.01
SQU-US	2026-06-04 03:15:00	8.85	25.72	0.47	7.20	11.46	9.43	0.01
SQU-US	2026-06-04 03:30:00	8.81	25.25	0.47	7.23	11.50	9.29	0.01
SQU-US	2026-06-04 03:45:00	8.78	25.40	0.47	7.21	11.51	9.35	0.01
SQU-US	2026-06-04 04:00:00	8.76	25.36	0.47	7.24	11.52	9.26	0.01
SQU-US	2026-06-04 04:15:00	8.72	25.51	0.47	7.23	11.53	9.33	0.01
SQU-US	2026-06-04 04:30:00	8.71	25.15	0.47	7.22	11.55	9.28	0.01
SQU-US	2026-06-04 04:45:00	8.68	25.18	0.47	7.24	11.56	9.33	0.01
SQU-US	2026-06-04 05:00:00	8.64	25.09	0.47	7.26	11.57	9.38	0.01
SQU-US	2026-06-04 05:15:00	8.63	24.96	0.47	7.25	11.59	9.27	0.01
SQU-US	2026-06-04 05:30:00	8.61	24.87	0.47	7.26	11.60	9.23	0.01
SQU-US	2026-06-04 05:45:00	8.60	24.88	0.47	7.25	11.60	9.32	0.01
SQU-US	2026-06-04 06:00:00	8.57	24.86	0.47	7.26	11.61	9.29	0.01
SQU-US	2026-06-04 06:15:00	8.55	24.90	0.47	7.25	11.62	9.18	0.01
SQU-US	2026-06-04 06:30:00	8.55	24.88	0.47	7.25	11.62	9.13	0.01
SQU-US	2026-06-04 06:45:00	8.53	24.92	0.47	7.28	11.62	9.25	0.01
SQU-US	2026-06-04 07:00:00	8.53	24.90	0.47	7.29	11.65	9.16	0.01
SQU-US	2026-06-04 07:15:00	8.51	24.92	0.47	7.29	11.67	9.25	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-04 07:30:00	8.52	25.11	0.47	7.28	11.66	9.09	0.01
SQU-US	2026-06-04 07:45:00	8.52	25.13	0.47	7.28	11.68	9.12	0.01
SQU-US	2026-06-04 08:00:00	8.53	25.28	0.47	7.29	11.69	9.14	0.01
SQU-US	2026-06-04 08:15:00	8.53	25.53	0.47	7.26	11.69	9.15	0.01
SQU-US	2026-06-04 08:30:00	8.54	25.61	0.47	7.27	11.69	9.16	0.01
SQU-US	2026-06-04 08:45:00	8.57	25.93	0.47	7.25	11.69	8.96	0.01
SQU-US	2026-06-04 09:00:00	8.63	25.93	0.47	7.25	11.69	9.00	0.01
SQU-US	2026-06-04 09:15:00	8.74	25.76	0.47	7.26	11.69	8.87	0.01
SQU-US	2026-06-04 09:30:00	8.79	25.72	0.46	7.26	11.70	9.00	0.01
SQU-US	2026-06-04 09:45:00	8.83	26.18	0.46	7.25	11.69	8.96	0.01
SQU-US	2026-06-04 10:00:00	8.89	26.29	0.46	7.25	11.69	9.02	0.01
SQU-US	2026-06-04 10:15:00	8.99	25.80	0.46	7.25	11.70	8.94	0.01
SQU-US	2026-06-04 10:30:00	9.07	25.75	0.46	7.25	11.71	9.09	0.01
SQU-US	2026-06-04 10:45:00	9.18	25.98	0.46	7.26	11.70	9.11	0.01
SQU-US	2026-06-04 11:00:00	9.27	26.27	0.46	7.26	11.70	8.90	0.01
SQU-US	2026-06-04 11:15:00	9.32	25.85	0.46	7.26	11.70	8.94	0.01
SQU-US	2026-06-04 11:30:00	9.35	25.46	0.45	7.29	11.69	9.07	0.01
SQU-US	2026-06-04 11:45:00	9.40	25.60	0.45	7.28	11.71	8.97	0.01
SQU-US	2026-06-04 12:00:00	9.45	25.11	0.45	7.30	11.71	8.90	0.01
SQU-US	2026-06-04 12:15:00	9.48	25.34	0.45	7.27	11.72	9.04	0.01
SQU-US	2026-06-04 12:30:00	9.57	24.82	0.45	7.31	11.71	8.96	0.01
SQU-US	2026-06-04 12:45:00	9.66	24.90	0.45	7.30	11.71	8.92	0.01
SQU-US	2026-06-04 13:00:00	9.75	25.57	0.45	7.30	11.68	8.96	0.01
SQU-US	2026-06-04 13:15:00	9.75	25.78	0.45	7.29	11.67	9.05	0.01
SQU-US	2026-06-04 13:30:00	9.84	25.90	0.45	7.30	11.67	8.95	0.01
SQU-US	2026-06-04 13:45:00	9.83	25.84	0.45	7.31	11.68	9.02	0.01
SQU-US	2026-06-04 14:00:00	9.84	25.69	0.45	7.32	11.67	9.09	0.01
SQU-US	2026-06-04 14:15:00	9.88	25.83	0.45	7.31	11.66	8.94	0.01
SQU-US	2026-06-04 14:30:00	9.86	25.68	0.45	7.31	11.66	9.01	0.01
SQU-US	2026-06-04 14:45:00	9.86	25.83	0.45	7.31	11.66	8.94	0.01
SQU-US	2026-06-04 15:00:00	9.80	25.58	0.45	7.30	11.66	8.92	0.01
SQU-US	2026-06-04 15:15:00	9.85	25.87	0.45	7.31	11.65	8.99	0.01
SQU-US	2026-06-04 15:30:00	9.92	25.82	0.45	7.31	11.65	9.04	0.01
SQU-US	2026-06-04 15:45:00	9.99	25.57	0.45	7.32	11.63	8.82	0.01
SQU-US	2026-06-04 16:00:00	10.05	25.75	0.45	7.33	11.63	8.82	0.01
SQU-US	2026-06-04 16:15:00	10.12	25.92	0.45	7.29	11.61	8.92	0.01
SQU-US	2026-06-04 16:30:00	10.19	25.88	0.45	7.30	11.59	8.84	0.01
SQU-US	2026-06-04 16:45:00	10.20	25.55	0.45	7.30	11.58	8.94	0.01
SQU-US	2026-06-04 17:00:00	10.19	25.93	0.45	7.32	11.56	8.84	0.01
SQU-US	2026-06-04 17:15:00	10.19	25.79	0.45	7.31	11.56	8.90	0.01
SQU-US	2026-06-04 17:30:00	10.20	25.67	0.45	7.30	11.55	9.05	0.01
SQU-US	2026-06-04 17:45:00	10.20	25.70	0.45	7.32	11.55	9.09	0.01
SQU-US	2026-06-04 18:00:00	10.16	25.80	0.45	7.32	11.53	8.97	0.01
SQU-US	2026-06-04 18:15:00	10.12	25.71	0.45	7.32	11.54	8.99	0.01
SQU-US	2026-06-04 18:30:00	10.11	25.89	0.46	7.30	11.51	8.88	0.01
SQU-US	2026-06-04 18:45:00	10.08	26.31	0.46	7.31	11.50	8.91	0.01
SQU-US	2026-06-04 19:00:00	10.01	26.46	0.46	7.32	11.48	9.02	0.01
SQU-US	2026-06-04 19:15:00	9.96	26.05	0.46	7.31	11.48	8.98	0.01
SQU-US	2026-06-04 19:30:00	9.92	25.82	0.46	7.31	11.47	8.95	0.01
SQU-US	2026-06-04 19:45:00	9.86	25.92	0.46	7.31	11.47	8.83	0.01
SQU-US	2026-06-04 20:00:00	9.80	26.12	0.46	7.33	11.48	8.79	0.01
SQU-US	2026-06-04 20:15:00	9.75	26.08	0.46	7.33	11.46	8.96	0.01
SQU-US	2026-06-04 20:30:00	9.70	25.98	0.46	7.32	11.46	8.85	0.01
SQU-US	2026-06-04 20:45:00	9.65	25.80	0.46	7.30	11.45	8.89	0.01
SQU-US	2026-06-04 21:00:00	9.61	26.15	0.46	7.31	11.44	8.84	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-04 21:15:00	9.56	26.14	0.46	7.32	11.43	8.88	0.01
SQU-US	2026-06-04 21:30:00	9.50	26.03	0.47	7.30	11.43	8.81	0.01
SQU-US	2026-06-04 21:45:00	9.46	26.05	0.47	7.30	11.43	8.86	0.01
SQU-US	2026-06-04 22:00:00	9.40	26.76	0.46	7.31	11.42	8.78	0.01
SQU-US	2026-06-04 22:15:00	9.36	26.56	0.47	7.31	11.42	8.82	0.01
SQU-US	2026-06-04 22:30:00	9.32	26.97	0.47	7.31	11.41	8.73	0.01
SQU-US	2026-06-04 22:45:00	9.28	26.82	0.47	7.30	11.41	8.76	0.01
SQU-US	2026-06-04 23:00:00	9.23	26.76	0.47	7.31	11.41	8.74	0.01
SQU-US	2026-06-04 23:15:00	9.19	26.71	0.47	7.29	11.42	8.67	0.01
SQU-US	2026-06-04 23:30:00	9.14	26.36	0.47	7.30	11.43	8.64	0.01
SQU-US	2026-06-04 23:45:00	9.10	25.88	0.47	7.29	11.44	8.58	0.01
SQU-US	2026-06-05 00:00:00	9.05	26.33	0.47	7.29	11.45	8.54	0.01
SQU-US	2026-06-05 00:15:00	9.02	26.09	0.47	7.28	11.45	8.59	0.01
SQU-US	2026-06-05 00:30:00	8.97	25.84	0.47	7.28	11.46	8.63	0.01
SQU-US	2026-06-05 00:45:00	8.92	25.75	0.47	7.28	11.47	8.69	0.01
SQU-US	2026-06-05 01:00:00	8.90	25.88	0.47	7.30	11.47	8.52	0.01
SQU-US	2026-06-05 01:15:00	8.86	25.54	0.47	7.28	11.49	8.61	0.01
SQU-US	2026-06-05 01:30:00	8.85	25.44	0.47	7.27	11.48	8.60	0.01
SQU-US	2026-06-05 01:45:00	8.79	25.43	0.47	7.27	11.49	8.56	0.01
SQU-US	2026-06-05 02:00:00	8.75	25.49	0.47	7.27	11.50	8.59	0.01
SQU-US	2026-06-05 02:15:00	8.72	25.45	0.47	7.23	11.49	8.51	0.01
SQU-US	2026-06-05 02:30:00	8.69	24.76	0.48	7.21	11.49	8.48	0.01
SQU-US	2026-06-05 02:45:00	8.63	25.06	0.48	7.21	11.49	8.49	0.01
SQU-US	2026-06-05 03:00:00	8.60	25.66	0.48	7.21	11.50	8.46	0.01
SQU-US	2026-06-05 03:15:00	8.59	25.71	0.48	7.19	11.49	8.46	0.01
SQU-US	2026-06-05 03:30:00	8.54	25.51	0.48	7.19	11.50	8.47	0.01
SQU-US	2026-06-05 03:45:00	8.50	25.67	0.48	7.18	11.51	8.44	0.01
SQU-US	2026-06-05 04:00:00	8.46	25.58	0.48	7.20	11.52	8.45	0.01
SQU-US	2026-06-05 04:15:00	8.44	24.95	0.48	7.20	11.54	8.44	0.01
SQU-US	2026-06-05 04:30:00	8.38	25.07	0.48	7.20	11.55	8.54	0.01
SQU-US	2026-06-05 04:45:00	8.36	25.13	0.48	7.20	11.57	8.51	0.01
SQU-US	2026-06-05 05:00:00	8.34	24.94	0.48	7.22	11.58	8.46	0.01
SQU-US	2026-06-05 05:15:00	8.31	24.91	0.48	7.22	11.59	8.37	0.01
SQU-US	2026-06-05 05:30:00	8.28	24.99	0.48	7.20	11.60	8.46	0.01
SQU-US	2026-06-05 05:45:00	8.25	24.77	0.48	7.24	11.61	8.52	0.01
SQU-US	2026-06-05 06:00:00	8.23	24.64	0.48	7.23	11.63	8.32	0.01
SQU-US	2026-06-05 06:15:00	8.20	24.85	0.48	7.25	11.64	8.33	0.01
SQU-US	2026-06-05 06:30:00	8.19	24.89	0.48	7.23	11.65	8.85	0.01
SQU-US	2026-06-05 06:45:00	8.16	25.08	0.48	7.24	11.65	8.73	0.01
SQU-US	2026-06-05 07:00:00	8.16	24.74	0.48	7.25	11.66	8.91	0.01
SQU-US	2026-06-05 07:15:00	8.15	24.74	0.48	7.25	11.68	8.56	0.01
SQU-US	2026-06-05 07:30:00	8.12	24.86	0.48	7.27	11.69	8.57	0.01
SQU-US	2026-06-05 07:45:00	8.13	24.89	0.48	7.26	11.69	8.83	0.01
SQU-US	2026-06-05 08:00:00	8.13	24.75	0.48	7.25	11.71	8.84	0.01
SQU-US	2026-06-05 08:15:00	8.12	25.03	0.48	7.24	11.72	8.83	0.01
SQU-US	2026-06-05 08:30:00	8.13	25.20	0.48	7.23	11.72	8.90	0.01
SQU-US	2026-06-05 08:45:00	8.12	25.48	0.48	7.24	11.72	8.88	0.01
SQU-US	2026-06-05 09:00:00	8.11	25.50	0.48	7.25	11.71	8.93	0.01
SQU-US	2026-06-05 09:15:00	8.14	25.17	0.48	7.24	11.72	8.75	0.01
SQU-US	2026-06-05 09:30:00	8.14	25.47	0.48	7.24	11.72	8.64	0.01
SQU-US	2026-06-05 09:45:00	8.14	26.16	0.48	7.24	11.71	8.78	0.01
SQU-US	2026-06-05 10:00:00	8.12	26.32	0.48	7.23	11.71	8.73	0.01
SQU-US	2026-06-05 10:15:00	8.14	26.02	0.48	7.22	11.71	8.81	0.01
SQU-US	2026-06-05 10:30:00	8.14	26.25	0.48	7.21	11.72	8.62	0.01
SQU-US	2026-06-05 10:45:00	8.15	26.09	0.48	7.21	11.72	8.78	0.01


Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-05 11:00:00	8.16	26.20	0.48	7.21	11.72	8.60	0.01
SQU-US	2026-06-05 11:15:00	8.16	25.80	0.48	7.20	11.72	8.66	0.01
SQU-US	2026-06-05 11:30:00	8.16	26.18	0.48	7.22	11.74	8.76	0.01
SQU-US	2026-06-05 11:45:00	8.19	26.12	0.47	7.23	11.75	8.49	0.01
SQU-US	2026-06-05 12:00:00	8.18	26.25	0.47	7.23	11.75	8.57	0.01
SQU-US	2026-06-05 12:15:00	8.19	26.05	0.47	7.24	11.76	8.55	0.01
SQU-US	2026-06-05 12:30:00	8.18	26.37	0.47	7.22	11.77	8.74	0.01
SQU-US	2026-06-05 12:45:00	8.19	26.32	0.47	7.22	11.76	8.37	0.01
SQU-US	2026-06-05 13:00:00	8.18	26.22	0.47	7.24	11.77	8.47	0.01
SQU-US	2026-06-05 13:15:00	8.16	25.99	0.47	7.23	11.77	8.54	0.01
SQU-US	2026-06-05 13:30:00	8.15	26.10	0.47	7.25	11.78	8.38	0.01
SQU-US	2026-06-05 13:45:00	8.14	26.22	0.47	7.23	11.78	8.46	0.01
SQU-US	2026-06-05 14:00:00	8.14	26.96	0.47	7.24	11.77	8.39	0.01
SQU-US	2026-06-05 14:15:00	8.12	26.34	0.47	7.24	11.78	8.39	0.01
SQU-US	2026-06-05 14:30:00	8.10	26.34	0.47	7.24	11.77	8.52	0.01
SQU-US	2026-06-05 14:45:00	8.10	26.67	0.47	7.24	11.79	8.34	0.01
SQU-US	2026-06-05 15:00:00	8.12	26.35	0.47	7.27	11.78	8.33	0.01
SQU-US	2026-06-05 15:15:00	8.11	26.44	0.47	7.24	11.77	8.36	0.01
SQU-US	2026-06-05 15:30:00	8.13	26.46	0.47	7.24	11.78	8.40	0.01
SQU-US	2026-06-05 15:45:00	8.17	26.79	0.47	7.24	11.78	8.34	0.01
SQU-US	2026-06-05 16:00:00	8.26	26.76	0.47	7.28	11.78	8.26	0.01
SQU-US	2026-06-05 16:15:00	8.39	26.72	0.47	7.26	11.78	8.26	0.01
SQU-US	2026-06-05 16:30:00	8.48	26.92	0.47	7.26	11.77	8.28	0.01
SQU-US	2026-06-05 16:45:00	8.53	27.05	0.47	7.26	11.77	8.22	0.01
SQU-US	2026-06-05 17:00:00	8.55	27.03	0.47	7.29	11.76	8.21	0.01
SQU-US	2026-06-05 17:15:00	8.56	27.06	0.47	7.28	11.76	8.24	0.01
SQU-US	2026-06-05 17:30:00	8.56	27.06	0.47	7.28	11.77	8.29	0.01
SQU-US	2026-06-05 17:45:00	8.55	27.03	0.47	7.29	11.76	8.31	0.01
SQU-US	2026-06-05 18:00:00	8.52	27.59	0.47	7.29	11.76	8.17	0.01
SQU-US	2026-06-05 18:15:00	8.48	27.42	0.47	7.27	11.75	8.17	0.01
SQU-US	2026-06-05 18:30:00	8.46	27.25	0.47	7.28	11.73	8.26	0.01
SQU-US	2026-06-05 18:45:00	8.43	27.34	0.47	7.28	11.74	8.30	0.01
SQU-US	2026-06-05 19:00:00	8.40	27.60	0.47	7.29	11.72	8.29	0.01
SQU-US	2026-06-05 19:15:00	8.37	27.44	0.47	7.28	11.71	8.26	0.01
SQU-US	2026-06-05 19:30:00	8.34	27.72	0.47	7.29	11.70	8.17	0.01
SQU-US	2026-06-05 19:45:00	8.31	27.36	0.47	7.29	11.70	8.26	0.01
SQU-US	2026-06-05 20:00:00	8.29	27.13	0.47	7.30	11.70	8.32	0.01
SQU-US	2026-06-05 20:15:00	8.28	27.24	0.47	7.31	11.69	8.22	0.01
SQU-US	2026-06-05 20:30:00	8.27	27.07	0.47	7.32	11.69	8.34	0.01
SQU-US	2026-06-05 20:45:00	8.26	27.18	0.47	7.32	11.67	8.28	0.01
SQU-US	2026-06-05 21:00:00	8.25	26.96	0.47	7.32	11.65	8.21	0.01
SQU-US	2026-06-05 21:15:00	8.24	27.04	0.47	7.30	11.65	8.25	0.01
SQU-US	2026-06-05 21:30:00	8.23	26.77	0.47	7.30	11.64	8.25	0.01
SQU-US	2026-06-05 21:45:00	8.21	26.90	0.47	7.31	11.63	8.25	0.01
SQU-US	2026-06-05 22:00:00	8.17	27.02	0.47	7.31	11.64	8.29	0.01
SQU-US	2026-06-05 22:15:00	8.16	27.26	0.47	7.30	11.63	8.18	0.01
SQU-US	2026-06-05 22:30:00	8.13	27.05	0.48	7.30	11.63	8.32	0.01
SQU-US	2026-06-05 22:45:00	8.10	27.27	0.48	7.30	11.62	8.25	0.01
SQU-US	2026-06-05 23:00:00	8.07	27.32	0.47	7.31	11.62	8.20	0.01
SQU-US	2026-06-05 23:15:00	8.03	27.34	0.47	7.32	11.62	8.33	0.01
SQU-US	2026-06-05 23:30:00	8.00	27.89	0.48	7.30	11.63	8.23	0.01
SQU-US	2026-06-05 23:45:00	7.97	27.58	0.48	7.29	11.62	8.26	0.01
SQU-US	2026-06-06 00:00:00	7.94	27.72	0.48	7.31	11.64	8.13	0.01
SQU-US	2026-06-06 00:15:00	7.90	28.12	0.48	7.30	11.64	8.19	0.01
SQU-US	2026-06-06 00:30:00	7.88	27.82	0.48	7.30	11.64	8.10	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-06 00:45:00	7.85	27.89	0.48	7.29	11.65	8.25	0.01
SQU-US	2026-06-06 01:00:00	7.83	27.58	0.48	7.30	11.67	8.06	0.01
SQU-US	2026-06-06 01:15:00	7.81	27.54	0.48	7.29	11.67	8.19	0.01
SQU-US	2026-06-06 01:30:00	7.77	27.63	0.48	7.28	11.67	8.20	0.01
SQU-US	2026-06-06 01:45:00	7.77	27.70	0.48	7.27	11.66	8.09	0.01
SQU-US	2026-06-06 02:00:00	7.75	27.46	0.48	7.25	11.66	8.14	0.01
SQU-US	2026-06-06 02:15:00	7.75	27.68	0.48	7.22	11.64	8.13	0.01
SQU-US	2026-06-06 02:30:00	7.73	27.88	0.48	7.18	11.62	8.08	0.01
SQU-US	2026-06-06 02:45:00	7.71	28.19	0.48	7.18	11.60	8.14	0.01
SQU-US	2026-06-06 03:00:00	7.68	28.10	0.48	7.17	11.58	8.13	0.01
SQU-US	2026-06-06 03:15:00	7.65	27.88	0.48	7.16	11.58	8.10	0.01
SQU-US	2026-06-06 03:30:00	7.62	28.14	0.48	7.16	11.60	8.22	0.01
SQU-US	2026-06-06 03:45:00	7.57	27.52	0.48	7.16	11.60	8.15	0.01
SQU-US	2026-06-06 04:00:00	7.53	27.58	0.48	7.15	11.62	8.04	0.01
SQU-US	2026-06-06 04:15:00	7.48	27.13	0.48	7.16	11.63	8.05	0.01
SQU-US	2026-06-06 04:30:00	7.46	27.13	0.48	7.16	11.65	8.13	0.01
SQU-US	2026-06-06 04:45:00	7.42	27.03	0.48	7.17	11.65	8.22	0.01
SQU-US	2026-06-06 05:00:00	7.40	26.78	0.48	7.18	11.68	8.13	0.01
SQU-US	2026-06-06 05:15:00	7.38	26.65	0.48	7.17	11.68	8.13	0.01
SQU-US	2026-06-06 05:30:00	7.36	26.61	0.48	7.18	11.68	8.10	0.01
SQU-US	2026-06-06 05:45:00	7.34	26.59	0.48	7.17	11.70	8.08	0.01
SQU-US	2026-06-06 06:00:00	7.32	26.73	0.48	7.19	11.72	8.04	0.01
SQU-US	2026-06-06 06:15:00	7.31	26.61	0.48	7.19	11.71	8.09	0.01
SQU-US	2026-06-06 06:30:00	7.28	26.68	0.48	7.19	11.73	8.03	0.01
SQU-US	2026-06-06 06:45:00	7.29	26.92	0.49	7.18	11.74	8.04	0.01
SQU-US	2026-06-06 07:00:00	7.27	26.43	0.48	7.20	11.74	7.97	0.01
SQU-US	2026-06-06 07:15:00	7.26	26.75	0.48	7.19	11.76	8.00	0.01
SQU-US	2026-06-06 07:30:00	7.25	26.63	0.49	7.19	11.77	8.13	0.01
SQU-US	2026-06-06 07:45:00	7.24	26.54	0.48	7.19	11.78	8.06	0.01
SQU-US	2026-06-06 08:00:00	7.23	26.50	0.48	7.20	11.79	8.03	0.01
SQU-US	2026-06-06 08:15:00	7.21	26.52	0.48	7.21	11.81	8.28	0.01
SQU-US	2026-06-06 08:30:00	7.21	26.61	0.48	7.22	11.82	8.40	0.01
SQU-US	2026-06-06 08:45:00	7.21	26.73	0.48	7.22	11.83	8.31	0.01
SQU-US	2026-06-06 09:00:00	7.20	26.91	0.48	7.23	11.83	8.27	0.01
SQU-US	2026-06-06 09:15:00	7.21	26.92	0.48	7.22	11.84	8.27	0.01
SQU-US	2026-06-06 09:30:00	7.25	27.25	0.48	7.22	11.85	8.16	0.01
SQU-US	2026-06-06 09:45:00	7.32	27.16	0.48	7.21	11.85	8.26	0.01
SQU-US	2026-06-06 10:00:00	7.39	27.46	0.48	7.21	11.85	8.29	0.01
SQU-US	2026-06-06 10:15:00	7.42	27.27	0.48	7.23	11.84	8.28	0.01
SQU-US	2026-06-06 10:30:00	7.48	27.46	0.48	7.22	11.85	8.15	0.01
SQU-US	2026-06-06 10:45:00	7.54	27.55	0.48	7.22	11.86	8.24	0.01
SQU-US	2026-06-06 11:00:00	7.62	27.75	0.48	7.23	11.84	8.20	0.01
SQU-US	2026-06-06 11:15:00	7.71	27.85	0.48	7.24	11.84	8.17	0.01
SQU-US	2026-06-06 11:30:00	7.84	28.14	0.48	7.24	11.84	8.13	0.01
SQU-US	2026-06-06 11:45:00	7.96	28.08	0.47	7.25	11.82	8.20	0.01
SQU-US	2026-06-06 12:00:00	8.08	28.04	0.47	7.24	11.81	8.23	0.01
SQU-US	2026-06-06 12:15:00	8.20	27.93	0.47	7.24	11.80	8.30	0.01
SQU-US	2026-06-06 12:30:00	8.31	28.21	0.47	7.24	11.79	8.29	0.01
SQU-US	2026-06-06 12:45:00	8.44	28.02	0.47	7.25	11.79	8.20	0.01
SQU-US	2026-06-06 13:00:00	8.57	28.02	0.47	7.25	11.76	8.20	0.01
SQU-US	2026-06-06 13:15:00	8.67	28.05	0.47	7.26	11.73	8.32	0.01
SQU-US	2026-06-06 13:30:00	8.68	28.36	0.47	7.24	11.71	8.40	0.01
SQU-US	2026-06-06 13:45:00	8.72	28.28	0.47	7.25	11.70	8.32	0.01
SQU-US	2026-06-06 14:00:00	8.77	28.03	0.47	7.25	11.70	8.28	0.01
SQU-US	2026-06-06 14:15:00	8.67	27.71	0.47	7.26	11.69	8.36	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-06 14:30:00	8.62	27.68	0.47	7.24	11.70	8.41	0.01
SQU-US	2026-06-06 14:45:00	8.73	27.65	0.47	7.26	11.68	8.28	0.01
SQU-US	2026-06-06 15:00:00	8.82	27.91	0.47	7.26	11.68	8.27	0.01
SQU-US	2026-06-06 15:15:00	8.86	27.81	0.47	7.26	11.66	8.38	0.01
SQU-US	2026-06-06 15:30:00	8.83	27.84	0.47	7.26	11.65	8.35	0.01
SQU-US	2026-06-06 15:45:00	8.79	27.84	0.47	7.26	11.64	8.39	0.01
SQU-US	2026-06-06 16:00:00	8.80	27.92	0.47	7.26	11.65	8.36	0.01
SQU-US	2026-06-06 16:15:00	8.84	27.90	0.47	7.27	11.64	8.32	0.01
SQU-US	2026-06-06 16:30:00	8.90	28.12	0.47	7.27	11.64	8.40	0.01
SQU-US	2026-06-06 16:45:00	8.94	28.10	0.47	7.28	11.63	8.29	0.01
SQU-US	2026-06-06 17:00:00	8.97	28.27	0.47	7.28	11.62	8.28	0.01
SQU-US	2026-06-06 17:15:00	9.00	28.36	0.47	7.27	11.60	8.23	0.01
SQU-US	2026-06-06 17:30:00	9.03	28.63	0.47	7.28	11.57	8.22	0.01
SQU-US	2026-06-06 17:45:00	9.08	28.79	0.47	7.28	11.54	8.37	0.01
SQU-US	2026-06-06 18:00:00	9.13	28.91	0.47	7.29	11.51	8.29	0.01
SQU-US	2026-06-06 18:15:00	9.18	29.14	0.47	7.29	11.49	8.33	0.01
SQU-US	2026-06-06 18:30:00	9.22	29.07	0.47	7.29	11.49	8.24	0.01
SQU-US	2026-06-06 18:45:00	9.26	29.11	0.47	7.29	11.48	8.37	0.01
SQU-US	2026-06-06 19:00:00	9.30	29.22	0.47	7.28	11.46	8.40	0.01
SQU-US	2026-06-06 19:15:00	9.32	29.40	0.47	7.29	11.44	8.32	0.01
SQU-US	2026-06-06 19:30:00	9.30	29.54	0.47	7.29	11.44	8.46	0.01
SQU-US	2026-06-06 19:45:00	9.26	29.27	0.47	7.29	11.43	8.34	0.01
SQU-US	2026-06-06 20:00:00	9.19	29.54	0.47	7.28	11.42	8.35	0.01
SQU-US	2026-06-06 20:15:00	9.16	29.42	0.47	7.27	11.41	8.39	0.01
SQU-US	2026-06-06 20:30:00	9.12	29.66	0.47	7.28	11.40	8.46	0.01
SQU-US	2026-06-06 20:45:00	9.07	29.79	0.47	7.27	11.40	8.39	0.01
SQU-US	2026-06-06 21:00:00	9.03	29.70	0.47	7.27	11.38	8.30	0.01
SQU-US	2026-06-06 21:15:00	9.01	29.52	0.47	7.28	11.36	8.39	0.01
SQU-US	2026-06-06 21:30:00	9.00	29.77	0.47	7.28	11.35	8.44	0.01
SQU-US	2026-06-06 21:45:00	8.99	29.60	0.47	7.28	11.34	8.45	0.01
SQU-US	2026-06-06 22:00:00	8.99	29.51	0.48	7.28	11.32	8.34	0.01
SQU-US	2026-06-06 22:15:00	8.99	29.22	0.48	7.30	11.32	8.44	0.01
SQU-US	2026-06-06 22:30:00	8.99	29.44	0.48	7.30	11.30	8.46	0.01
SQU-US	2026-06-06 22:45:00	8.98	29.29	0.48	7.30	11.30	8.49	0.01
SQU-US	2026-06-06 23:00:00	8.95	29.27	0.48	7.29	11.29	8.33	0.01
SQU-US	2026-06-06 23:15:00	8.92	29.59	0.48	7.31	11.28	8.41	0.01
SQU-US	2026-06-06 23:30:00	8.90	29.53	0.48	7.29	11.28	8.45	0.01
SQU-US	2026-06-06 23:45:00	8.85	29.77	0.48	7.30	11.30	8.47	0.01
SQU-US	2026-06-07 00:00:00	8.83	29.92	0.48	7.29	11.30	8.44	0.01
SQU-US	2026-06-07 00:15:00	8.81	30.37	0.48	7.29	11.29	8.45	0.01
SQU-US	2026-06-07 00:30:00	8.80	30.51	0.48	7.29	11.28	8.35	0.01
SQU-US	2026-06-07 00:45:00	8.77	30.65	0.48	7.30	11.27	8.41	0.01
SQU-US	2026-06-07 01:00:00	8.74	30.71	0.48	7.29	11.28	8.45	0.01
SQU-US	2026-06-07 01:15:00	8.73	30.82	0.48	7.27	11.27	8.45	0.01
SQU-US	2026-06-07 01:30:00	8.71	31.17	0.48	7.24	11.25	8.38	0.01
SQU-US	2026-06-07 01:45:00	8.68	31.28	0.48	7.21	11.23	8.23	0.01
SQU-US	2026-06-07 02:00:00	8.66	31.44	0.48	7.19	11.22	8.38	0.01
SQU-US	2026-06-07 02:15:00	8.62	31.25	0.48	7.18	11.22	8.35	0.01
SQU-US	2026-06-07 02:30:00	8.59	31.03	0.48	7.18	11.22	8.38	0.01
SQU-US	2026-06-07 02:45:00	8.56	30.64	0.48	7.20	11.24	8.32	0.01
SQU-US	2026-06-07 03:00:00	8.53	30.08	0.48	7.20	11.28	8.43	0.01
SQU-US	2026-06-07 03:15:00	8.50	29.90	0.48	7.22	11.30	8.30	0.01
SQU-US	2026-06-07 03:30:00	8.48	29.76	0.48	7.22	11.31	8.36	0.01
SQU-US	2026-06-07 03:45:00	8.43	29.28	0.48	7.22	11.33	8.42	0.01
SQU-US	2026-06-07 04:00:00	8.41	29.39	0.48	7.22	11.35	8.21	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-07 04:15:00	8.36	29.39	0.48	7.22	11.35	8.30	0.01
SQU-US	2026-06-07 04:30:00	8.34	29.43	0.48	7.22	11.35	8.38	0.01
SQU-US	2026-06-07 04:45:00	8.32	29.55	0.48	7.22	11.37	8.21	0.01
SQU-US	2026-06-07 05:00:00	8.29	29.49	0.48	7.22	11.36	8.28	0.01
SQU-US	2026-06-07 05:15:00	8.25	29.64	0.48	7.23	11.37	8.41	0.01
SQU-US	2026-06-07 05:30:00	8.22	29.78	0.48	7.23	11.38	8.24	0.01
SQU-US	2026-06-07 05:45:00	8.20	29.79	0.48	7.23	11.38	8.23	0.01
SQU-US	2026-06-07 06:00:00	8.18	29.77	0.48	7.22	11.39	8.27	0.01
SQU-US	2026-06-07 06:15:00	8.16	30.02	0.48	7.22	11.40	8.20	0.01
SQU-US	2026-06-07 06:30:00	8.13	30.29	0.48	7.23	11.41	8.25	0.01
SQU-US	2026-06-07 06:45:00	8.13	20.15	0.48	7.21	11.46	8.62	0.01
SQU-US	2026-06-07 07:00:00	8.11	30.58	0.48	7.21	11.58	8.44	0.01
SQU-US	2026-06-07 07:15:00	8.11	18.10	0.48	7.20	11.69	9.14	0.01
SQU-US	2026-06-07 07:30:00	8.11	21.83	0.48	7.20	11.73	8.33	0.01
SQU-US	2026-06-07 07:45:00	8.12	17.84	0.48	7.22	11.74	8.88	0.01
SQU-US	2026-06-07 08:00:00	8.11	17.65	0.48	7.22	11.77	8.98	0.01
SQU-US	2026-06-07 08:15:00	8.13	25.84	0.48	7.22	11.76	8.53	0.01
SQU-US	2026-06-07 08:30:00	8.13	29.85	0.48	7.23	11.76	8.96	0.01
SQU-US	2026-06-07 08:45:00	8.14	28.22	0.48	7.23	11.74	8.78	0.01
SQU-US	2026-06-07 09:00:00	8.15	27.36	0.48	7.24	11.71	8.26	0.01
SQU-US	2026-06-07 09:15:00	8.18	28.64	0.48	7.25	11.67	8.26	0.01
SQU-US	2026-06-07 09:30:00	8.20	30.01	0.48	7.26	11.66	8.32	0.01
SQU-US	2026-06-07 09:45:00	8.22	29.99	0.48	7.26	11.66	8.29	0.01
SQU-US	2026-06-07 10:00:00	8.28	30.27	0.48	7.27	11.67	8.19	0.01
SQU-US	2026-06-07 10:15:00	8.33	30.37	0.48	7.26	11.67	8.31	0.01
SQU-US	2026-06-07 10:30:00	8.37	30.38	0.48	7.26	11.65	8.25	0.01
SQU-US	2026-06-07 10:45:00	8.43	30.42	0.48	7.27	11.66	8.45	0.01
SQU-US	2026-06-07 11:00:00	8.52	24.58	0.48	7.26	11.65	8.15	0.01
SQU-US	2026-06-07 11:15:00	8.61	18.09	0.48	7.25	11.67	8.63	0.01
SQU-US	2026-06-07 11:30:00	8.69	10.99	0.48	7.23	11.68	8.84	0.00
SQU-US	2026-06-07 11:45:00	8.89	0.34	0.48	7.23	11.64	8.77	0.00
SQU-US	2026-06-07 12:00:00	9.11	0.08	0.47	7.29	11.58	8.97	0.00
SQU-US	2026-06-07 12:15:00	9.28	0.08	0.45	7.30	11.54	8.99	0.00
SQU-US	2026-06-07 12:30:00	9.45	0.08	0.44	7.41	11.48	8.93	0.00
SQU-US	2026-06-07 12:45:00	9.51	0.08	0.45	7.28	11.47	8.77	0.00
SQU-US	2026-06-07 13:00:00	9.70	0.08	0.46	7.39	11.42	8.76	0.00
SQU-US	2026-06-07 13:15:00	9.97	0.08	0.46	7.38	11.36	8.67	0.00
SQU-US	2026-06-07 13:30:00	10.12	0.08	0.46	7.38	11.33	8.68	0.00
SQU-US	2026-06-07 13:45:00	10.42	0.08	0.47	7.38	11.24	8.41	0.00
SQU-US	2026-06-07 14:00:00	10.37	0.08	0.47	7.38	11.25	7.59	0.00
SQU-US	2026-06-07 14:15:00	10.59	0.08	0.46	7.37	11.21	7.93	0.00
SQU-US	2026-06-07 14:30:00	10.97	0.08	0.46	7.36	11.10	8.01	0.00
SQU-US	2026-06-07 14:45:00	11.29	0.07	0.46	7.34	11.01	8.80	0.00
SQU-US	2026-06-07 15:00:00	11.37	0.07	0.46	7.30	10.98	7.78	0.00
SQU-US	2026-06-07 15:15:00	11.45	0.07	0.46	7.27	10.96	7.13	0.00
SQU-US	2026-06-07 15:30:00	11.41	0.07	0.46	7.22	10.96	7.13	0.00
SQU-US	2026-06-07 15:45:00	11.51	0.07	0.46	7.17	10.95	6.88	0.00
SQU-US	2026-06-07 16:00:00	11.66	0.07	0.46	7.13	10.91	7.66	0.00
SQU-US	2026-06-07 16:15:00	12.18	0.07	0.46	7.12	10.78	6.95	0.00
SQU-US	2026-06-07 16:30:00	12.09	0.07	0.46	7.08	10.80	6.94	0.00
SQU-US	2026-06-07 16:45:00	12.06	0.07	0.46	7.02	10.82	6.99	0.00
SQU-US	2026-06-07 17:00:00	11.99	0.07	0.46	6.95	10.83	6.75	0.00
SQU-US	2026-06-07 17:15:00	12.01	0.07	0.46	6.91	10.81	6.88	0.00
SQU-US	2026-06-07 17:30:00	11.94	0.07	0.46	6.88	10.84	6.92	0.00
SQU-US	2026-06-07 17:45:00	11.72	0.07	0.46	6.84	10.89	6.93	0.00

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-06-07 18:00:00	11.51	0.07	0.47	6.81	10.95	6.82	0.00
SQU-US	2026-06-07 18:15:00	11.47	0.07	0.47	6.80	10.96	6.80	0.00
SQU-US	2026-06-07 18:30:00	11.28	0.07	0.47	6.78	10.99	6.95	0.00
SQU-US	2026-06-07 18:45:00	11.26	0.07	0.47	6.77	11.01	6.93	0.00
SQU-US	2026-06-07 19:00:00	11.21	0.07	0.47	6.76	11.01	6.78	0.00
SQU-US	2026-06-07 19:15:00	11.06	0.07	0.47	6.74	11.05	7.00	0.00
SQU-US	2026-06-07 19:30:00	10.69	0.08	0.47	7.29	11.14	7.15	0.00
SQU-US	2026-06-07 19:45:00	10.47	0.08	0.47	7.12	11.20	6.83	0.00
SQU-US	2026-06-07 20:00:00	10.19	0.08	0.47	7.31	11.28	6.78	0.00
SQU-US	2026-06-07 20:15:00	10.06	0.08	0.47	7.19	11.31	6.60	0.00
SQU-US	2026-06-07 20:30:00	9.97	0.08	0.47	7.12	11.34	6.66	0.00
SQU-US	2026-06-07 20:45:00	9.85	0.08	0.47	7.07	11.37	7.10	0.00
SQU-US	2026-06-07 21:00:00	9.64	0.08	0.47	7.06	11.42	8.79	0.00
SQU-US	2026-06-07 21:15:00	9.31	0.19	0.45	7.20	11.52	8.90	0.00
SQU-US	2026-06-07 21:30:00	9.04	31.26	0.45	7.32	11.45	8.26	0.01
SQU-US	2026-06-07 21:45:00	9.00	31.09	0.45	7.31	11.42	8.34	0.01
SQU-US	2026-06-07 22:00:00	8.94	31.06	0.46	7.30	11.42	8.30	0.01
SQU-US	2026-06-07 22:15:00	8.91	30.81	0.46	7.32	11.40	8.38	0.01
SQU-US	2026-06-07 22:30:00	8.88	30.86	0.46	7.30	11.40	8.39	0.01
SQU-US	2026-06-07 22:45:00	8.87	31.16	0.46	7.30	11.39	8.38	0.01
SQU-US	2026-06-07 23:00:00	8.85	31.14	0.46	7.28	11.39	8.28	0.01
SQU-US	2026-06-07 23:15:00	8.85	30.94	0.46	7.30	11.37	8.28	0.01
SQU-US	2026-06-07 23:30:00	8.80	30.79	0.46	7.31	11.40	8.43	0.01
SQU-US	2026-06-07 23:45:00	8.79	30.67	0.46	7.31	11.39	8.37	0.01

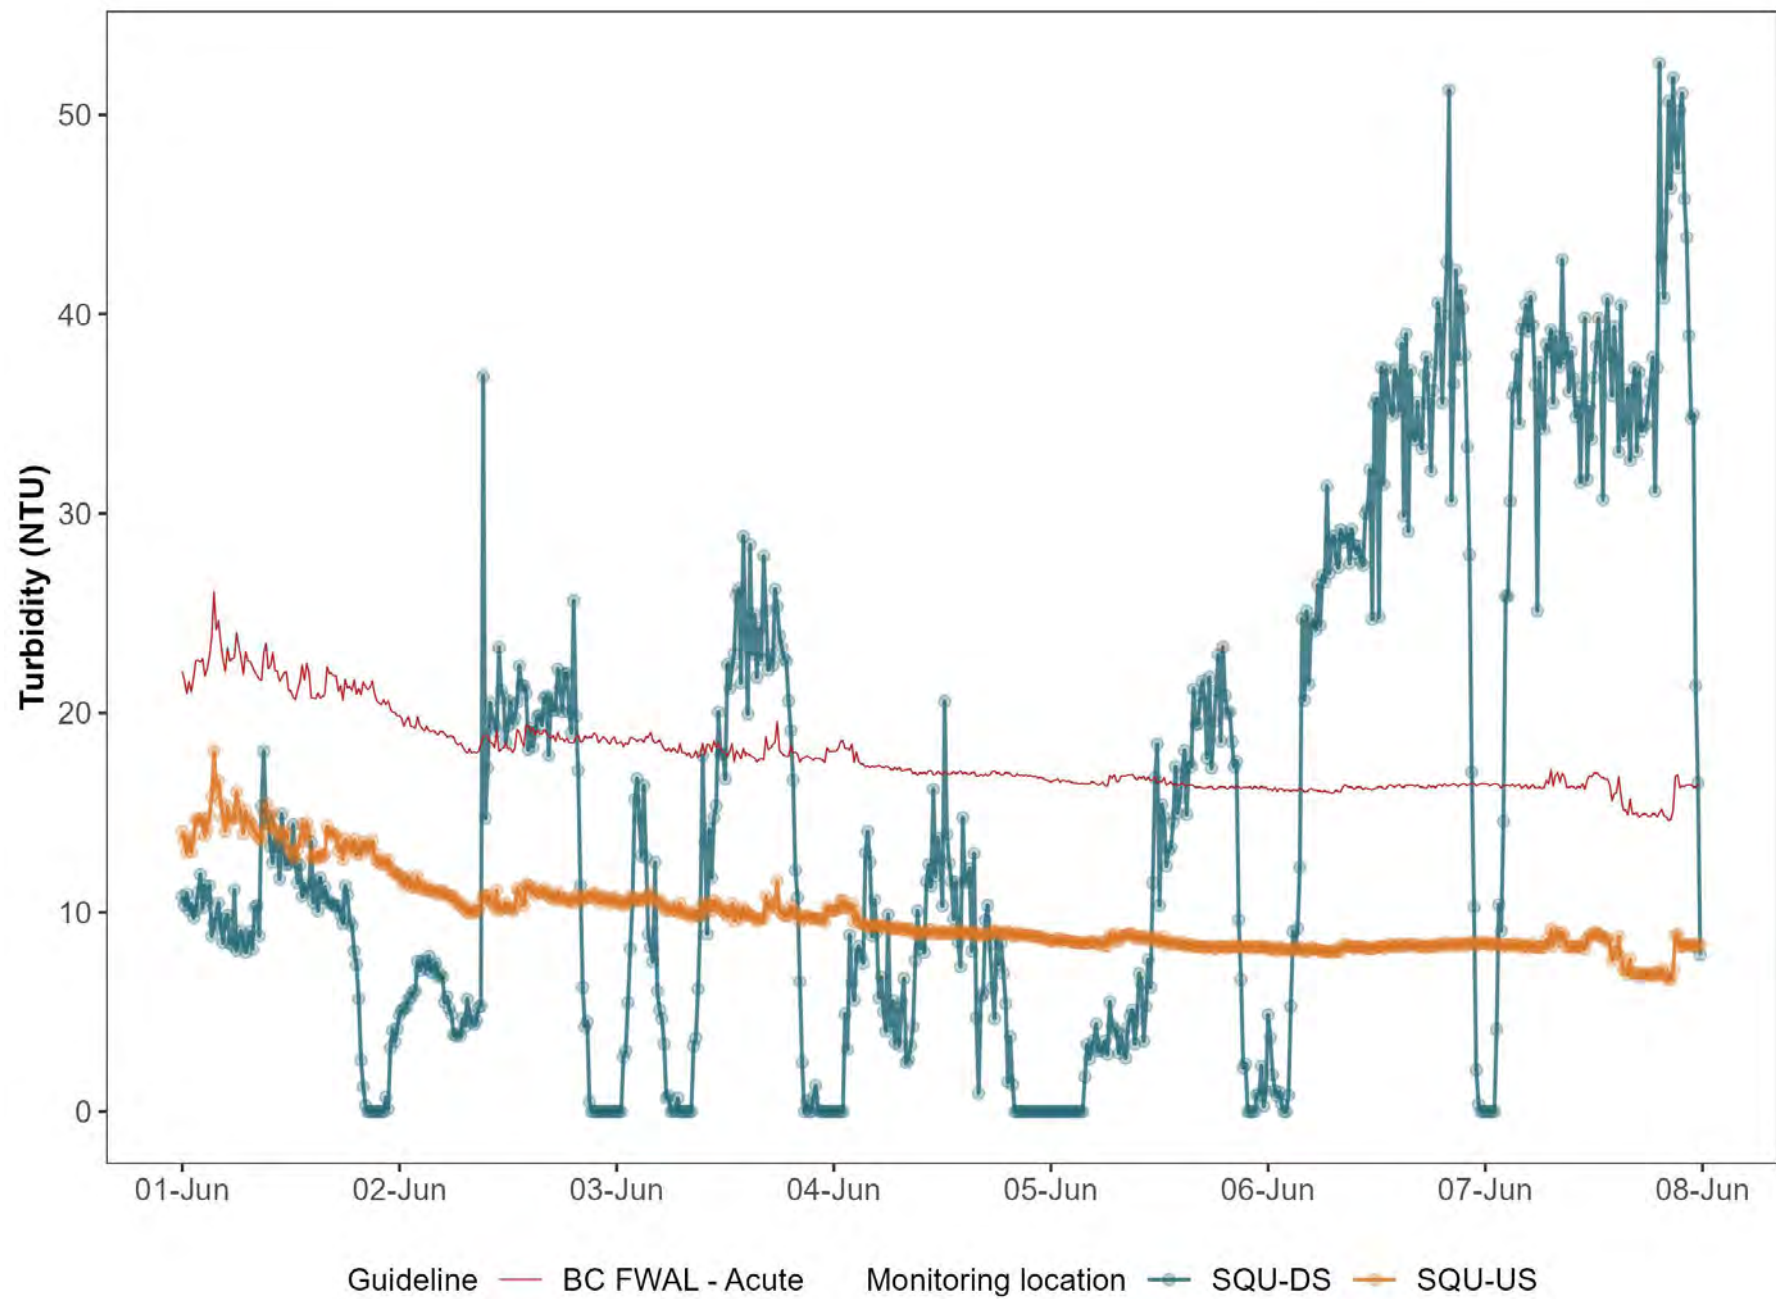

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix C	C-1

Appendix C:

Woodfibre Site Point of Discharge from Water
Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix C	C-2

Woodfibre Site Sample Analysis



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
In situ Parameters								
Field pH	pH Units		6.5 - 9			7 - 8.7		7.3
Field Temperature	°C	18	19					12.9
General Parameters								
pH	pH Units							7.55
Alkalinity (Total as CaCO ₃)	mg/L							46
Alkalinity (PP as CaCO ₃)	mg/L							<1
Hardness (CaCO ₃)-Total	mg/L							63.9
Hardness (CaCO ₃)-Dissolved	mg/L							62.3
Sulphide-Total	mg/L							<0.0018
Sulphide (as H ₂ S)	mg/L			0.002				<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L							<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L							<0.0018
Anions and Nutrients								
Ammonia (N)-Total	mg/L	1.8	15.6		12	83		<0.015
Bicarbonate (HCO ₃)	mg/L							56
Carbonate (CO ₃)	mg/L							<1
Hydroxide (OH)	mg/L							<1
Nitrate (N)	mg/L	3	32.8		3.7			0.081
Nitrite (N)	mg/L	0.2	0.6					<0.005
Nitrate plus Nitrite (N)	mg/L							0.081
Nitrogen (N)-Total	mg/L							0.214
Phosphorus (P)-Total (4500-P)	mg/L							0.0023
Bromide (Br)	mg/L							<0.01
Chloride (Cl)	mg/L	150	600					13
Fluoride (F)	mg/L		1.154052			1.5		0.28
Sulphate (SO ₄)-Dissolved	mg/L	218						16
Total Metals								
Aluminum (Al)-Total	mg/L	0.0801711						0.0646
Antimony (Sb)-Total	mg/L	0.074	0.25					0.000293
Arsenic (As)-Total	mg/L	0.005			0.0125			0.000683
Barium (Ba)-Total	mg/L			1				0.0065
Beryllium (Be)-Total	mg/L			0.00013			0.1	<0.00001
Bismuth (Bi)-Total	mg/L							<0.000005
Boron (B)-Total	mg/L	1.2			1.2			0.012
Cadmium (Cd)-Total	mg/L						0.00012	<0.000005
Calcium (Ca)-Total	mg/L							23.5
Cesium (Cs)-Total	mg/L							<0.00005
Chromium (Cr)-Total	mg/L							0.00014

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
Total Metals (cont'd.)								
Chromium (Cr III)-Total	mg/L			0.0089			0.056	<0.00099
Chromium (Cr VI)-Total	mg/L			0.0025			0.0015	<0.00099
Cobalt (Co)-Total	mg/L							0.0000566
Copper (Cu)-Total	mg/L				0.002	0.003		0.000092
Iron (Fe)-Total	mg/L	0.085	1					0.0152
Lead (Pb)-Total	mg/L				0.002	0.14		<0.000005
Lithium (Li)-Total	mg/L							0.00518
Magnesium (Mg)-Total	mg/L							1.26
Manganese (Mn)-Total	mg/L						0.1	0.0294
Mercury (Hg)-Total	mg/L	0.00002			0.0001			<0.0000019
Molybdenum (Mo)-Total	mg/L	7.6	46					0.0319
Nickel (Ni)-Total	mg/L						0.0083	0.000114
Phosphorus (P)-Total (ICPMS)	mg/L							<0.002
Potassium (K)-Total	mg/L							1.36
Rubidium (Rb)-Total	mg/L							0.00298
Selenium (Se)-Total	mg/L	0.002			0.002			0.000063
Silicon (Si)-Total	mg/L							6.71
Silver (Ag)-Total	mg/L	0.00012			0.0005	0.0037	0.0005	<0.000005
Sodium (Na)-Total	mg/L							6.91
Strontium (Sr)-Total	mg/L							0.0516
Sulphur (S)-Total	mg/L							5.1
Tellurium (Te)-Total	mg/L							<0.00002
Thallium (Tl)-Total	mg/L			0.00003				0.0000086
Thorium (Th)-Total	mg/L							<0.00005
Tin (Sn)-Total	mg/L							<0.0002
Titanium (Ti)-Total	mg/L							0.00067
Uranium (U)-Total	mg/L		0.0165	0.0075				0.000224
Vanadium (V)-Total	mg/L			0.06			0.005	0.00026
Zinc (Zn)-Total	mg/L				0.01	0.055		0.00134
Zirconium (Zr)-Total	mg/L							<0.0001
Dissolved Metals								
Aluminum (Al)-Dissolved	mg/L							0.034
Antimony (Sb)-Dissolved	mg/L							0.000292
Arsenic (As)-Dissolved	mg/L							0.000631
Barium (Ba)-Dissolved	mg/L							0.00596
Beryllium (Be)-Dissolved	mg/L							<0.00001
Bismuth (Bi)-Dissolved	mg/L							<0.000005
Boron (B)-Dissolved	mg/L							<0.01

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
Dissolved Metals (cont'd.)								
Cadmium (Cd)-Dissolved	mg/L	0.0001521	0.0003708					<0.000005
Calcium (Ca)-Dissolved	mg/L							23.1
Cesium (Cs)-Dissolved	mg/L							<0.00005
Chromium (Cr)-Dissolved	mg/L							0.00011
Cobalt (Co)-Dissolved	mg/L	0.0004236						0.0000559
Copper (Cu)-Dissolved	mg/L	0.00023	0.00143					<0.00005
Iron (Fe)-Dissolved	mg/L							<0.001
Lead (Pb)-Dissolved	mg/L	0.0019757						<0.000005
Lithium (Li)-Dissolved	mg/L							0.00354
Manganese (Mn)-Dissolved	mg/L	0.215	2.246164					0.0282
Magnesium (Mg)-Dissolved	mg/L							1.13
Mercury (Hg)-Dissolved	mg/L							<0.0000019
Molybdenum (Mo)-Dissolved	mg/L							0.03
Nickel (Ni)-Dissolved	mg/L	0.0013	0.022					0.000199
Phosphorus (P)-Dissolved	mg/L							0.0026
Potassium (K)-Dissolved	mg/L							1.24
Rubidium (Rb)-Dissolved	mg/L							0.00263
Selenium (Se)-Dissolved	mg/L							0.000071
Silicon (Si)-Dissolved	mg/L							6.64
Silver (Ag)-Dissolved	mg/L							<0.000005
Sodium (Na)-Dissolved	mg/L							6.2
Strontium (Sr)-Dissolved	mg/L			1.25				0.0468
Sulphur (S)-Dissolved	mg/L							4.1
Tellurium (Te)-Dissolved	mg/L							<0.00002
Thallium (Tl)-Dissolved	mg/L							0.0000035
Thorium (Th)-Dissolved	mg/L							<0.000005
Tin (Sn)-Dissolved	mg/L							<0.0002
Titanium (Ti)-Dissolved	mg/L							<0.0005
Uranium (U)-Dissolved	mg/L							0.000212
Vanadium (V)-Dissolved	mg/L							<0.0002
Zinc (Zn)-Dissolved	mg/L	0.00708	0.0276265					0.00127
Zirconium (Zr)-Dissolved	mg/L							<0.0001
Inorganics								
Organic Carbon (C)-Total	mg/L							0.86
Organic Carbon (C)-Dissolved	mg/L							1.1
Solids-Total Dissolved	mg/L							100
Solids-Total Suspended	mg/L	6	26					1.2

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).

Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
Organics								
HEPH (C19-C32 less PAH)	mg/L							<0.2
LEPH (C10-C19 less PAH)	mg/L							<0.2
EPH (C10-C19)	mg/L							<0.2
EPH (C19-C32)	mg/L							<0.2
Ethylene Glycol	mg/L							<3
Diethylene Glycol	mg/L							<5
Triethylene Glycol	mg/L							<5
Propylene Glycol	mg/L							<5
Acenaphthene	mg/L	0.006			0.006			<0.00005
Acenaphthylene	mg/L							<0.00005
Acridine	mg/L	0.003						<0.00005
Anthracene	mg/L	0.004						<0.00001
Benzo(a)anthracene	mg/L	0.0001						<0.00001
Benzo(a)pyrene	mg/L	0.00001			0.00001			<0.000005
Benzo(b&j)fluoranthene	mg/L							<0.00003
Benzo(g,h,i)perylene	mg/L							<0.00005
Benzo(k)fluoranthene	mg/L							<0.00005
Chrysene	mg/L				0.0001			<0.00002
Dibenz(a,h)anthracene	mg/L							<0.000003
Fluoranthene	mg/L	0.004						<0.00002
Fluorene	mg/L	0.012			0.012			<0.00005
Indeno(1,2,3-cd)pyrene	mg/L							<0.00005
1-Methylnaphthalene	mg/L				0.001			<0.00005
2-Methylnaphthalene	mg/L				0.001			<0.0001
Naphthalene	mg/L	0.001	0.001		0.001			<0.0001
Phenanthrene	mg/L	0.0003						<0.00005
Pyrene	mg/L							<0.00002
Quinoline	mg/L							<0.00002
Low Molecular Weight PAH`s	mg/L							<0.0001
High Molecular Weight PAH`s	mg/L							<0.00005
Total PAH	mg/L							<0.0001
VH C6-C10	mg/L							<0.3
1,1,1,2-Tetrachloroethane	mg/L							<0.0005
1,1,1-Trichloroethane	mg/L							<0.0005
1,1,2,2-Tetrachloroethane	mg/L							<0.0005
1,1,2Trichloro-1,2,2Trifluoroethane	mg/L							<0.002
1,1,2-Trichloroethane	mg/L							<0.0005
1,1-Dichloroethane	mg/L							<0.0005

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
Organics (cont'd.)								
1,1-Dichloroethene	mg/L							<0.0005
1,2,3-trichlorobenzene	mg/L			0.008				<0.002
1,2,4-trichlorobenzene	mg/L			0.024			0.0054	<0.002
1,2-dibromoethane	mg/L							<0.0002
1,2-Dichlorobenzene	mg/L			0.0007			0.042	<0.0005
1,2-Dichloroethane	mg/L			0.1				<0.0005
1,2-Dichloropropane	mg/L							<0.0005
1,3,5-trimethylbenzene	mg/L							<0.002
1,3-Butadiene	mg/L							<0.0005
1,3-Dichlorobenzene	mg/L			0.15				<0.0005
1,3-dichloropropane	mg/L							<0.001
1,4-Dichlorobenzene	mg/L			0.026				<0.0005
Benzene	mg/L	0.04			0.11			<0.0004
Bromobenzene	mg/L							<0.002
Bromodichloromethane	mg/L							<0.001
Bromoform	mg/L							<0.001
Bromomethane	mg/L							<0.001
Carbon tetrachloride	mg/L							<0.0005
Chlorobenzene	mg/L			0.0013			0.025	<0.0005
Chloroethane	mg/L							<0.001
Chloroform	mg/L							<0.001
Chloromethane	mg/L							<0.001
cis-1,2-Dichloroethene	mg/L							<0.001
cis-1,3-Dichloropropene	mg/L							<0.001
Dibromochloromethane	mg/L							<0.001
Dichlorodifluoromethane	mg/L							<0.002
Dichloromethane	mg/L			0.0981				<0.002
Ethylbenzene	mg/L	0.2			0.25			<0.0004
Hexachlorobutadiene	mg/L							<0.0005
Isopropylbenzene	mg/L							<0.002
Methyl-tert-butylether (MTBE)	mg/L		3.4			0.44		<0.004
Styrene	mg/L			0.072				<0.0005
Tetrachloroethene	mg/L							<0.0005
Toluene	mg/L	0.0005						<0.0004
trans-1,2-dichloroethene	mg/L							<0.001
trans-1,3-dichloropropene	mg/L							<0.001
Trichloroethene	mg/L							<0.0005
Trichlorofluoromethane	mg/L							<0.004

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-06-02 10:00:00
Organics (cont'd.)								
Vinyl chloride	mg/L							<0.0005
VPH (VH6 to 10 - BTEX)	mg/L							<0.3
Xylenes (Total)	mg/L	0.03						<0.0004
m & p-Xylene	mg/L							<0.0004
o-Xylene	mg/L							<0.0004
Phenols	mg/L		0.05					<0.0015
Rainbow Trout								
LC50 (Daphnia Magna)	% vol/vol							>100%
LC50 (Rainbow Trout)	% vol/vol							>100%

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024).

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix C	C-3

Woodfibre Site WTP Discharge
Field Notes and Logs

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

Table of Contents:

1. Executive Summary and Field Notes
2. Daily Volume Summary
3. Portal Discharge Parameter Summary
4. CP2 Discharge Parameter Summary
5. In-situ Readings
6. WTP Calibration Log

Appendices:

- Appendix A- Portal WTP Data Log
- Appendix B- CP2 WTP Data Log
- Appendix C- Photos

1. Executive Summary and Field Notes:

Parameters, including temperature, NTU, pH, DO, salinity, conductivity, and oxidation-reduction potential (ORP), were monitored throughout the discharge process.

A reading of 522 NTU was recorded on the data log on June 1st at 15:30 at the CP2 water treatment plant (CP2 WTP) while the NTU probe was being calibrated. The discharge water was ~2 NTU at the time of the calibration. On June 5th the NTU, pH and conductivity probes were calibrated between 11:10 and 11:50 at the CP2 WTP. The data logger recorded the following readings while the instrumentation was being calibrated: 523 NTU at 11:15, 750 NTU at 11:30, 6.45 pH at 11:45 and 0 uS/cm conductivity at 11:15, 11:30 and 11:45. The discharge water at the time of these readings was ~0 NTU, 7.4 pH and 158 uS/cm.

Temperature readings >19°C were recorded on the CP2 WTP data logs on June 1st, 2nd, 5th, 6th and 7th due to stagnant water in the temperature probe slip stream being heated up by the conductivity/ temperature probe during low discharge flows. The temperature of the water being discharged varied between 12-16°C. Refer to FKM 2026-05-31 Weekly Report WF for details regarding findings and modifications to rectify the issue. YSI readings were taken of the discharge water at CP2 WTP during routine inspections:

- June 1/ 2026 @ 13:39: 14.1°C
- June 2/ 2026 @ 13:32: 16.0°C
- June 5/ 2026 @ 00:07: 12.0°C
- June 5/ 2026 @ 17:30: 12.7°C
- June 5/ 2026 @ 22:44: 12.5°C

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

- June 6/ 2026 @ 16:52: 12.8°C
- June 6/ 2026 @ 18:53: 13.0°C
- June 7/ 2026 @ 15:56: 12.9°C
- June 7/ 2026 @ 19:24: 12.6°C

No visible sheen was observed on the surface of the WTP tanks or in the discharged water. All relevant parameters were measured using YSI instruments, Hanna NTU meter and WTP's NTU, pH, conductivity and temperature probes.

CP2 WTP received ~350 GPM (1.32 m3/min) and the portal water treatment plant (PWTP) received ~262 GPM (0.99 m3/min) from the tunnel.

The total discharge volume up to June 7th was 1,498,687 m3.

2. Daily Volume Summary:

Table 1: Discharge Volumes Daily Summary

Date	Location	Volume (m3)	Comments
June 1	Woodfibre (WF)	3,557	Exceeded discharge volume limit
June 2	WF	3,368	Exceeded discharge volume limit
June 3	WF	3,412	Exceeded discharge volume limit
June 4	WF	3,314	Exceeded discharge volume limit
June 5	WF	3,262	Exceeded discharge volume limit
June 6	WF	3,286	Exceeded discharge volume limit
June 7	WF	3,154	Exceeded discharge volume limit
Total		23,353	None

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

3. Discharge Parameter Summary:

Table 2: Portal Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	0:00:00	6.9	1.4763	0.5	1,352,926	14.1	269
6/1/2026	0:15:00	6.9	1.4650	0.7	1,352,948	14.1	269
6/1/2026	0:30:00	6.9	1.4460	0.9	1,352,967	14.1	269
6/1/2026	0:45:00	6.9	1.4687	1	1,352,989	14.2	269
6/1/2026	1:00:00	6.9	1.4347	1.2	1,353,011	14.2	271
6/1/2026	1:15:00	6.9	0.2196	1.5	1,353,025	14.5	268
6/1/2026	2:00:00	6.9	1.5558	1.6	1,353,045	14.7	267
6/1/2026	2:15:00	6.9	0.9577	2.1	1,353,065	14.1	268
6/1/2026	2:30:00	6.9	1.4990	2	1,353,087	14.1	268
6/1/2026	2:45:00	6.9	1.4990	1.7	1,353,109	14.2	268
6/1/2026	3:00:00	6.9	1.5104	1.1	1,353,132	14.2	266
6/1/2026	3:15:00	6.9	1.5028	0.5	1,353,146	14.3	266
6/1/2026	3:30:00	6.9	1.5104	0.7	1,353,169	14.3	266
6/1/2026	3:45:00	6.9	1.4990	1.1	1,353,191	14.3	266
6/1/2026	4:15:00	6.9	1.5255	2.1	1,353,206	14.2	266
6/1/2026	4:30:00	6.9	1.3968	2.2	1,353,226	14.5	266
6/1/2026	5:00:00	6.9	1.4763	2.3	1,353,241	14.2	266
6/1/2026	5:15:00	6.9	0.8934	1.7	1,353,251	14.1	264
6/1/2026	5:45:00	6.9	1.5217	1.3	1,353,284	14	263
6/1/2026	6:00:00	6.9	1.4990	0.8	1,353,307	13.9	263
6/1/2026	6:15:00	6.9	1.5028	0.6	1,353,317	14.5	264
6/1/2026	6:45:00	6.9	1.4990	0.5	1,353,340	14	263
6/1/2026	7:15:00	6.9	1.4612	0.7	1,353,362	13.9	263
6/1/2026	7:45:00	6.9	1.4839	0.9	1,353,374	13.7	263
6/1/2026	8:00:00	6.9	1.3741	0.9	1,353,381	13.7	263
6/1/2026	9:45:00	6.8	1.4687	2.2	1,353,400	13.3	264
6/1/2026	10:15:00	6.9	1.4422	1.8	1,353,434	13.6	261
6/1/2026	11:00:00	6.8	1.1281	1.9	1,353,466	13.7	262
6/1/2026	11:15:00	6.8	1.4347	2	1,353,477	13.9	263



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	12:45:00	6.8	1.3892	1.6	1,353,489	14.2	263
6/1/2026	13:15:00	6.8	1.3400	1.7	1,353,489	14.2	265
6/1/2026	14:00:00	6.8	0.8290	1.7	1,353,489	14.3	264
6/1/2026	14:15:00	6.8	0.2725	1.3	1,353,489	14.2	264
6/1/2026	14:45:00	6.7	1.4082	0.9	1,353,489	14.2	264
6/1/2026	15:15:00	6.7	1.4877	0.8	1,353,524	14.3	266
6/1/2026	16:00:00	6.7	1.8056	1	1,353,534	14.2	267
6/1/2026	16:15:00	6.7	1.0258	1.1	1,353,550	14.7	268
6/1/2026	16:30:00	6.7	1.7489	1	1,353,564	14.3	268
6/1/2026	17:15:00	6.7	1.7602	1.1	1,353,607	14.3	267
6/1/2026	17:45:00	6.7	1.7451	1.1	1,353,617	14.2	265
6/1/2026	20:30:00	6.7	1.1621	1	1,353,699	13.7	265
6/1/2026	21:30:00	6.7	1.7602	2.2	1,353,740	13.8	265
6/1/2026	22:15:00	6.7	1.7148	4.1	1,353,785	13.7	265
6/1/2026	22:30:00	6.7	1.7224	4.1	1,353,811	13.7	265
6/1/2026	23:00:00	6.7	1.7224	3.8	1,353,852	13.5	265
6/1/2026	23:30:00	6.8	1.7034	3.3	1,353,878	13.4	265
6/1/2026	23:45:00	6.8	1.1394	3	1,353,903	13.4	266
6/2/2026	0:45:00	6.8	1.7224	4.1	1,353,944	13.1	265
6/2/2026	1:15:00	6.9	1.7186	4.4	1,353,961	13	264
6/2/2026	2:15:00	6.8	1.7072	3.6	1,353,987	13.1	259
6/2/2026	2:45:00	6.9	1.6845	3.6	1,354,012	13	258
6/2/2026	3:00:00	6.9	1.0221	3.3	1,354,029	13.1	258
6/2/2026	3:15:00	6.9	1.7224	3.5	1,354,054	13	258
6/2/2026	3:45:00	6.9	1.1281	2.7	1,354,097	13	255
6/2/2026	4:00:00	6.9	1.7148	2.5	1,354,108	12.9	255
6/2/2026	4:30:00	6.9	1.7186	2.7	1,354,122	12.9	255
6/2/2026	7:15:00	6.9	1.6996	7.5	1,354,177	12.7	255
6/2/2026	7:45:00	6.8	0.5300	5.2	1,354,216	12.7	255
6/2/2026	8:00:00	6.8	1.7261	4.4	1,354,233	12.7	255
6/2/2026	8:30:00	6.8	1.1508	2.7	1,354,275	12.7	256
6/2/2026	9:00:00	6.7	1.7110	2	1,354,292	12.8	259



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	9:15:00	6.7	1.6807	1.7	1,354,317	12.9	258
6/2/2026	9:30:00	6.7	1.5520	1.4	1,354,321	13	258
6/2/2026	9:45:00	6.7	1.6315	1.3	1,354,334	13.5	258
6/2/2026	10:00:00	6.7	1.6996	1.2	1,354,359	13.2	258
6/2/2026	10:15:00	6.7	1.6769	1.1	1,354,384	13.3	258
6/2/2026	10:30:00	6.7	0.8139	1	1,354,405	13.5	259
6/2/2026	10:45:00	6.7	1.5937	1	1,354,421	13.5	259
6/2/2026	11:00:00	6.7	1.6012	1	1,354,445	13.5	258
6/2/2026	11:15:00	6.7	1.0864	1	1,354,468	13.8	258
6/2/2026	11:30:00	6.7	1.5899	1	1,354,484	13.7	258
6/2/2026	12:15:00	6.8	1.5861	0.9	1,354,522	14.2	262
6/2/2026	12:30:00	6.8	1.6012	0.7	1,354,537	14.1	259
6/2/2026	12:45:00	6.8	1.6088	0.8	1,354,561	14.2	259
6/2/2026	13:00:00	6.8	1.6126	0.8	1,354,576	14.3	260
6/2/2026	13:30:00	6.8	1.5974	1	1,354,614	14.2	260
6/2/2026	14:45:00	6.9	1.0675	1	1,354,653	14.5	260
6/2/2026	15:00:00	6.9	1.4801	0.9	1,354,664	14.4	256
6/2/2026	15:15:00	6.9	1.4763	0.9	1,354,664	14.4	256
6/2/2026	16:15:00	6.9	1.3287	0.8	1,354,675	14.6	258
6/2/2026	16:45:00	6.9	1.6277	0.6	1,354,710	14.8	257
6/2/2026	17:00:00	6.9	1.1281	0.6	1,354,721	14.9	257
6/2/2026	17:15:00	6.9	1.6618	0.7	1,354,745	15.1	257
6/2/2026	17:30:00	6.9	1.5937	0.6	1,354,759	14.8	257
6/2/2026	17:45:00	6.9	1.0675	0.6	1,354,774	14.8	257
6/2/2026	18:00:00	6.9	1.6050	0.6	1,354,795	14.7	257
6/2/2026	19:00:00	6.9	1.6239	0.8	1,354,835	14.2	255
6/2/2026	19:30:00	6.9	1.4687	0.9	1,354,850	14	253
6/2/2026	19:45:00	6.9	1.4839	1.1	1,354,850	14	255
6/2/2026	20:00:00	6.9	0.8896	0.9	1,354,850	13.8	255
6/2/2026	20:15:00	6.9	0.7722	0.9	1,354,850	13.7	253
6/2/2026	20:30:00	6.9	1.5520	1	1,354,850	13.8	253
6/2/2026	21:30:00	6.9	1.5672	1	1,354,898	13.7	253



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	21:45:00	6.9	1.7526	1	1,354,912	13.5	255
6/2/2026	22:45:00	6.9	1.7034	1.3	1,354,938	13.1	253
6/2/2026	23:00:00	6.9	1.7451	1.6	1,354,956	13.1	252
6/2/2026	23:15:00	6.9	1.7299	1.4	1,354,981	13	252
6/2/2026	23:30:00	6.9	1.7526	1.4	1,354,998	13.1	252
6/2/2026	23:45:00	6.9	1.1621	1.3	1,355,022	13	253
6/3/2026	0:00:00	6.9	1.7337	1.4	1,355,039	13.1	253
6/3/2026	0:15:00	6.9	1.6580	1.4	1,355,049	13.2	253
6/3/2026	0:30:00	6.9	1.6959	1.4	1,355,069	13.2	252
6/3/2026	0:45:00	6.9	1.7337	1.3	1,355,085	13.3	252
6/3/2026	1:00:00	6.9	1.7261	1.4	1,355,111	13.1	252
6/3/2026	1:15:00	6.9	1.7299	1.2	1,355,126	13.1	252
6/3/2026	1:30:00	6.9	1.7299	1.2	1,355,152	13.1	253
6/3/2026	1:45:00	6.9	1.6883	1.2	1,355,178	13	253
6/3/2026	2:00:00	6.9	1.1697	1.3	1,355,192	13	253
6/3/2026	2:15:00	6.9	1.7034	1.2	1,355,207	13.1	253
6/3/2026	2:45:00	6.9	1.6921	1.2	1,355,233	12.9	255
6/3/2026	3:45:00	6.9	1.7110	1.3	1,355,240	12.7	252
6/3/2026	4:15:00	6.9	1.7299	1.7	1,355,262	12.9	252
6/3/2026	4:30:00	6.9	1.6996	2.1	1,355,287	13.2	255
6/3/2026	5:15:00	6.8	1.7072	2.1	1,355,326	13.2	253
6/3/2026	5:30:00	7	1.7072	5.1	1,355,352	15.2	500
6/3/2026	5:45:00	7.4	1.5974	3.7	1,355,367	13.7	632
6/3/2026	6:00:00	7.7	1.0864	3.5	1,355,389	13.3	699
6/3/2026	6:30:00	7.4	1.6202	1	1,355,404	13.6	668
6/3/2026	6:45:00	7.5	1.5937	1.5	1,355,428	13.5	653
6/3/2026	7:30:00	7.5	1.5899	0.9	1,355,467	13.2	591
6/3/2026	8:15:00	7.4	1.6012	1	1,355,515	13.4	549
6/3/2026	8:45:00	7.5	1.5937	0.9	1,355,531	13.3	530
6/3/2026	9:00:00	7.4	1.5823	1	1,355,554	13.8	525
6/3/2026	10:00:00	7.4	1.5861	1.1	1,355,604	13.5	464
6/3/2026	10:15:00	7.4	1.5974	0.9	1,355,628	13.3	461



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	10:30:00	7	1.5823	1.1	1,355,648	13.3	453
6/3/2026	11:00:00	7.3	1.6277	1.2	1,355,673	13.4	445
6/3/2026	11:15:00	7.3	1.6202	1.2	1,355,697	13.6	438
6/3/2026	11:30:00	7.3	1.5331	1.2	1,355,712	13.7	433
6/3/2026	11:45:00	7.3	1.5937	1.2	1,355,735	13.5	431
6/3/2026	12:00:00	7.3	1.5937	1	1,355,759	13.6	425
6/3/2026	12:15:00	7.3	1.3968	0.7	1,355,780	13.9	423
6/3/2026	12:30:00	7.3	1.5407	0.7	1,355,796	13.9	415
6/3/2026	13:15:00	7.2	1.5974	0.5	1,355,820	15.1	405
6/3/2026	13:45:00	7.2	1.6164	0.5	1,355,859	14.4	392
6/3/2026	14:15:00	7.3	1.5861	0.3	1,355,875	14.3	385
6/3/2026	14:30:00	7.2	1.6012	0.2	1,355,899	14.5	382
6/3/2026	14:45:00	7.3	1.6088	0.1	1,355,913	14.5	379
6/3/2026	15:00:00	7.2	1.5861	0.1	1,355,937	14.7	374
6/3/2026	15:45:00	7.2	1.5823	0	1,355,961	14.7	368
6/3/2026	16:15:00	7	1.1810	0.1	1,355,974	14.6	359
6/3/2026	16:30:00	7.1	1.6088	0.2	1,355,990	15.1	361
6/3/2026	16:45:00	7.2	1.5861	0	1,356,014	15	358
6/3/2026	17:00:00	7.2	1.5407	0.1	1,356,029	14.8	355
6/3/2026	17:15:00	7.3	1.6050	0.2	1,356,049	14.6	351
6/3/2026	17:30:00	7.2	1.5937	0.3	1,356,065	14.4	343
6/3/2026	18:00:00	7.2	1.5369	0.1	1,356,085	14.6	338
6/3/2026	18:45:00	7.2	1.5823	0.4	1,356,122	14.4	335
6/3/2026	19:00:00	7.2	1.0448	0.6	1,356,132	14.7	333
6/3/2026	19:30:00	7.2	1.6202	1	1,356,145	13.9	333
6/3/2026	19:45:00	7.2	1.6315	1.1	1,356,159	13.7	330
6/3/2026	20:00:00	7.2	1.6126	1.2	1,356,184	13.5	328
6/3/2026	20:30:00	7.2	1.5937	1.2	1,356,198	13.5	327
6/3/2026	20:45:00	7.2	1.5974	1.2	1,356,222	13.5	327
6/3/2026	21:15:00	7.2	1.5899	1.3	1,356,246	13.1	323
6/3/2026	21:30:00	7.2	1.5937	1.4	1,356,261	13.4	324
6/3/2026	21:45:00	7.1	1.5861	1.4	1,356,285	13.2	324



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	22:00:00	7.2	1.5709	1.5	1,356,309	12.9	324
6/3/2026	22:15:00	7.2	1.0561	1.5	1,356,323	13	322
6/3/2026	22:30:00	7.1	1.5899	1.5	1,356,346	13.2	322
6/3/2026	22:45:00	7.1	1.6050	1.4	1,356,362	13.2	322
6/3/2026	23:00:00	7.1	1.3173	1.3	1,356,376	13.1	318
6/4/2026	0:00:00	7.1	1.5899	1.3	1,356,413	13.5	315
6/4/2026	1:00:00	7.1	1.4650	0.8	1,356,443	13.3	309
6/4/2026	1:45:00	7.1	1.6277	0.8	1,356,463	13.5	305
6/4/2026	2:15:00	7	1.6088	0.8	1,356,502	13.6	304
6/4/2026	3:15:00	7.1	1.5785	0.7	1,356,516	13.5	300
6/4/2026	3:30:00	7.1	1.0486	0.6	1,356,540	13.6	297
6/4/2026	4:15:00	7	1.5747	0.7	1,356,566	13.6	293
6/4/2026	4:30:00	7	1.4839	0.7	1,356,574	13.6	291
6/4/2026	4:45:00	7	1.5217	0.8	1,356,587	13.7	291
6/4/2026	5:30:00	7	1.5028	0.7	1,356,609	13.6	289
6/4/2026	6:00:00	7	1.0221	0.8	1,356,640	13.6	289
6/4/2026	6:15:00	7	1.4385	0.8	1,356,655	13.7	286
6/4/2026	7:00:00	7	1.5369	0.7	1,356,678	13.3	286
6/4/2026	8:00:00	7	1.5217	0.8	1,356,714	13.7	284
6/4/2026	8:30:00	7	1.5255	0.8	1,356,729	13.4	279
6/4/2026	8:45:00	7	1.5028	0.9	1,356,752	13.6	279
6/4/2026	9:00:00	7	1.5142	0.8	1,356,764	13.4	279
6/4/2026	9:30:00	7	1.5255	0.9	1,356,803	14.1	279
6/4/2026	9:45:00	7	1.0296	0.8	1,356,806	13.7	279
6/4/2026	10:15:00	7	1.5407	0.7	1,356,843	14.2	275
6/4/2026	10:30:00	6.9	1.0145	0.7	1,356,857	14.5	275
6/4/2026	10:45:00	7	1.5066	0.7	1,356,869	14.7	273
6/4/2026	11:00:00	7	1.5142	0.9	1,356,892	14.3	274
6/4/2026	11:15:00	7.1	0.1438	0.8	1,356,904	14.4	270
6/4/2026	11:30:00	7	1.5142	0.7	1,356,914	14.9	271
6/4/2026	11:45:00	6.9	1.6845	0.6	1,356,933	15.7	271
6/4/2026	12:00:00	6.9	1.6845	0.7	1,356,958	15.6	271



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	12:15:00	7	1.1167	0.5	1,356,974	14.9	269
6/4/2026	12:30:00	7	1.6353	0.3	1,356,998	15.6	269
6/4/2026	12:45:00	7	1.6202	0.4	1,357,023	15	269
6/4/2026	13:00:00	7	1.1318	0.3	1,357,039	14.9	269
6/4/2026	13:15:00	7	1.7072	0.3	1,357,056	15.2	269
6/4/2026	13:30:00	7	1.5293	0.6	1,357,072	14.7	268
6/4/2026	14:00:00	7	1.6391	0.5	1,357,099	14.7	268
6/4/2026	14:15:00	7	1.6845	0.6	1,357,124	14.8	266
6/4/2026	15:15:00	7	1.6732	0.7	1,357,132	14.8	268
6/4/2026	15:30:00	7	1.6126	0.7	1,357,173	14.8	268
6/4/2026	15:45:00	7.1	1.6277	0.8	1,357,189	14.8	265
6/4/2026	16:00:00	7	1.1281	0.7	1,357,213	14.8	265
6/4/2026	16:15:00	7	1.6618	0.7	1,357,229	14.7	265
6/4/2026	17:00:00	7	1.4195	0.9	1,357,270	14.6	265
6/4/2026	17:15:00	7	1.6164	0.8	1,357,277	14.7	265
6/4/2026	18:00:00	7	1.5709	0.9	1,357,291	14.7	265
6/4/2026	18:15:00	7	1.1053	1	1,357,304	14.7	264
6/4/2026	18:30:00	7	1.6353	1.2	1,357,319	14.7	263
6/4/2026	18:45:00	7	1.6353	1	1,357,344	14.3	263
6/4/2026	19:00:00	7	1.0978	1.2	1,357,360	14.2	263
6/4/2026	19:30:00	7	1.5974	1	1,357,381	13.8	261
6/4/2026	20:15:00	7	1.6164	1.1	1,357,393	13.5	261
6/4/2026	20:30:00	7	1.6239	1.2	1,357,417	13.3	261
6/4/2026	20:45:00	7	1.5066	1.3	1,357,427	13.3	261
6/4/2026	21:15:00	7	1.6202	1.3	1,357,451	13.2	259
6/4/2026	21:30:00	7	1.5937	1.4	1,357,465	13.1	259
6/4/2026	21:45:00	7	1.0637	1.4	1,357,477	13.1	261
6/4/2026	22:15:00	7	1.5785	1.4	1,357,515	13	260
6/4/2026	22:30:00	7	1.0258	1.4	1,357,528	13.4	260
6/4/2026	23:00:00	7	1.5823	1.2	1,357,544	13.2	260
6/4/2026	23:30:00	7	1.6126	0.7	1,357,582	13.3	260
6/5/2026	0:00:00	7	1.6202	0.3	1,357,596	13.6	259



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	0:30:00	7	1.5558	0.3	1,357,626	13.7	259
6/5/2026	0:45:00	7	1.0902	0.1	1,357,639	13.9	259
6/5/2026	1:45:00	7	1.5785	0.3	1,357,654	14.6	256
6/5/2026	2:00:00	6.9	1.5596	0.5	1,357,678	14.5	258
6/5/2026	2:15:00	7	1.0410	0	1,357,692	14	256
6/5/2026	2:30:00	7	1.6012	0	1,357,705	14	255
6/5/2026	2:45:00	7	1.6050	0	1,357,729	14.1	254
6/5/2026	3:00:00	7	1.6012	0	1,357,744	14.3	253
6/5/2026	3:15:00	6.9	1.5785	0	1,357,757	14.4	252
6/5/2026	4:30:00	6.9	1.0486	1.8	1,357,795	13.8	251
6/5/2026	4:45:00	6.9	1.6088	0.1	1,357,809	13.8	251
6/5/2026	5:00:00	7	1.4952	0.3	1,357,823	13.6	251
6/5/2026	5:30:00	7	1.5785	0.4	1,357,859	13.7	251
6/5/2026	5:45:00	7	1.5634	0.5	1,357,873	13.6	251
6/5/2026	6:15:00	7	1.5974	0.5	1,357,909	13.5	250
6/5/2026	6:30:00	7	1.5974	0.3	1,357,933	13.4	251
6/5/2026	6:45:00	7	1.5937	0	1,357,946	13.8	247
6/5/2026	8:30:00	7	0.1098	0.4	1,357,982	13.3	251
6/5/2026	8:45:00	7	1.0221	0.3	1,357,995	13.3	248
6/5/2026	9:00:00	7	1.5672	0.5	1,358,010	13.2	246
6/5/2026	9:45:00	7	1.5596	0	1,358,047	13.9	242
6/5/2026	10:00:00	7	1.5974	0.3	1,358,062	13.8	245
6/5/2026	10:30:00	7	1.5634	0.5	1,358,086	13.8	246
6/5/2026	10:45:00	7	1.5785	0.6	1,358,101	13.7	246
6/5/2026	11:30:00	7.1	1.5104	1.4	1,358,145	13.6	246
6/5/2026	11:45:00	7.1	0.9766	1.3	1,358,167	13.7	112
6/5/2026	12:15:00	7.1	1.5634	1.3	1,358,180	13.9	243
6/5/2026	12:30:00	7.1	1.5634	1.3	1,358,195	14.1	246
6/5/2026	13:15:00	7.1	1.5596	0.4	1,358,245	13.9	245
6/5/2026	13:45:00	7	1.4347	0.8	1,358,251	14.6	245
6/5/2026	14:15:00	7.1	1.5747	0.3	1,358,255	13.8	243
6/5/2026	14:45:00	7	1.5747	0	1,358,269	14	243



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	15:15:00	7.1	1.5331	0	1,358,305	14.1	242
6/5/2026	15:45:00	7	1.5596	0.2	1,358,321	13.9	112
6/5/2026	16:00:00	7.1	1.5369	0.3	1,358,343	13.7	111
6/5/2026	16:15:00	7	1.5823	0.5	1,358,356	13.8	112
6/5/2026	16:30:00	7.1	1.8624	0.3	1,358,366	13.7	111
6/5/2026	16:45:00	7	1.5255	0.4	1,358,389	14	112
6/5/2026	17:00:00	7.1	1.2113	0.1	1,358,409	13.8	113
6/5/2026	17:15:00	7	1.5709	0.3	1,358,432	14.2	243
6/5/2026	17:30:00	7.1	1.5747	0	1,358,456	14	113
6/5/2026	17:45:00	7.1	1.0599	0.1	1,358,479	14.9	243
6/5/2026	18:30:00	7.1	1.5444	0.3	1,358,498	13.8	112
6/5/2026	18:45:00	7.1	1.6391	0.3	1,358,523	13.7	111
6/5/2026	19:00:00	7	1.6656	0.3	1,358,545	13.9	111
6/5/2026	19:30:00	7.2	1.6542	3	1,358,569	13.5	112
6/5/2026	19:45:00	7.2	1.6088	4.6	1,358,594	13.5	112
6/5/2026	20:15:00	7.1	1.5861	2.2	1,358,606	13.5	112
6/5/2026	20:45:00	7.1	1.6353	2.4	1,358,621	13.4	111
6/5/2026	21:00:00	7.1	1.6050	2.4	1,358,645	13.3	112
6/5/2026	21:15:00	7.1	0.7041	2.6	1,358,668	13.4	111
6/5/2026	21:30:00	7.1	1.5596	2.3	1,358,689	13.3	111
6/5/2026	22:00:00	7.1	1.5520	3	1,358,712	13.5	112
6/5/2026	22:15:00	7.1	1.5634	2.9	1,358,735	14.5	113
6/5/2026	22:30:00	7.1	1.5255	2.3	1,358,755	13.6	113
6/5/2026	23:00:00	7.1	0.4694	2.8	1,358,779	13.6	113
6/5/2026	23:15:00	7.1	1.4498	3.4	1,358,782	13.6	113
6/5/2026	23:30:00	7.1	1.5369	3.6	1,358,795	13.7	111
6/5/2026	23:45:00	7	1.5482	8.4	1,358,819	13.6	111
6/6/2026	0:00:00	7.1	1.0372	4.5	1,358,841	13.7	113
6/6/2026	0:45:00	7	1.5709	2.3	1,358,863	13.8	113
6/6/2026	1:00:00	7	1.5558	2.7	1,358,886	14.4	243
6/6/2026	1:15:00	7.1	1.5558	3.1	1,358,909	13.9	113
6/6/2026	1:30:00	7	1.4536	5.2	1,358,915	13.7	113



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	2:00:00	7	1.6239	3.2	1,358,916	13.5	112
6/6/2026	2:15:00	7	1.5974	6.1	1,358,940	13.5	111
6/6/2026	2:30:00	7.1	1.6126	4.2	1,358,961	13.5	112
6/6/2026	3:15:00	7	1.5482	3.9	1,358,995	14	110
6/6/2026	3:30:00	7	1.0713	4.1	1,359,009	13.5	110
6/6/2026	4:00:00	7	1.5937	4.9	1,359,021	13.3	109
6/6/2026	4:15:00	7	1.5899	4.1	1,359,045	13.6	112
6/6/2026	4:45:00	7	1.5634	4.1	1,359,060	13.4	112
6/6/2026	5:30:00	7	1.5823	0.3	1,359,095	13.4	111
6/6/2026	6:15:00	7	1.5974	0.5	1,359,146	13.4	245
6/6/2026	6:45:00	7.1	1.5520	1	1,359,169	13.3	112
6/6/2026	7:00:00	7	1.0031	0.6	1,359,183	13.3	111
6/6/2026	7:30:00	7	1.5444	0.6	1,359,218	13.4	111
6/6/2026	7:45:00	7	1.5482	0.8	1,359,242	13.4	111
6/6/2026	8:00:00	7	1.5823	1.5	1,359,256	13.5	111
6/6/2026	8:15:00	7	1.5823	0.6	1,359,271	13.3	111
6/6/2026	8:30:00	7	1.5217	0.8	1,359,294	13.3	110
6/6/2026	8:45:00	7	1.5747	0.7	1,359,304	13.2	112
6/6/2026	9:15:00	7	1.5558	1.3	1,359,343	13	110
6/6/2026	10:00:00	7	1.5482	1	1,359,380	13.3	109
6/6/2026	10:30:00	7	1.5066	1.1	1,359,418	13.3	109
6/6/2026	10:45:00	7	1.5293	1.1	1,359,431	13.3	108
6/6/2026	11:00:00	7	1.5747	1.2	1,359,454	13.4	108
6/6/2026	11:15:00	7	1.5596	1	1,359,478	13.5	110
6/6/2026	12:00:00	7	1.4233	1.7	1,359,486	13.4	110
6/6/2026	12:15:00	7	1.0221	2.3	1,359,503	13.4	109
6/6/2026	12:30:00	7	1.6012	3.8	1,359,513	13.7	110
6/6/2026	12:45:00	7	1.5672	3.3	1,359,537	13.5	110
6/6/2026	13:00:00	7.1	1.5179	3.2	1,359,561	13.7	110
6/6/2026	13:30:00	7.1	1.5369	2.8	1,359,580	14	110
6/6/2026	14:00:00	7	1.5482	4.8	1,359,603	14.6	245
6/6/2026	14:15:00	7	1.5520	2.3	1,359,626	14.2	245



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	14:30:00	7	1.4422	2.7	1,359,642	14.2	245
6/6/2026	14:45:00	7.1	1.5861	9	1,359,646	14.5	245
6/6/2026	15:00:00	7.1	1.5331	4.2	1,359,669	14.2	245
6/6/2026	15:15:00	7	1.5142	1.6	1,359,679	14.1	110
6/6/2026	15:30:00	7	1.5785	2	1,359,703	14.7	109
6/6/2026	15:45:00	7	1.5709	2.2	1,359,727	14.1	112
6/6/2026	16:00:00	7	1.5520	2.6	1,359,747	14.1	245
6/6/2026	16:15:00	7.1	1.5823	4.8	1,359,770	14.4	110
6/6/2026	16:30:00	7	1.5785	1.8	1,359,794	14	110
6/6/2026	16:45:00	7	1.5785	1.7	1,359,815	14.1	245
6/6/2026	17:00:00	7	1.5369	6.6	1,359,839	13.7	110
6/6/2026	17:15:00	7	1.6012	1.1	1,359,862	13.7	109
6/6/2026	18:15:00	7.1	1.6202	2.4	1,359,884	13.5	109
6/6/2026	18:45:00	7.1	1.6126	2.6	1,359,908	13.6	109
6/6/2026	19:00:00	7.1	0.6927	2.9	1,359,918	13.5	109
6/6/2026	19:30:00	7.1	1.6429	3.5	1,359,939	13.3	110
6/6/2026	20:15:00	7	1.5937	11.4	1,359,973	13	108
6/6/2026	21:00:00	7	1.4952	3.9	1,359,994	13.3	110
6/6/2026	21:15:00	7	1.6467	3.6	1,360,009	13.8	110
6/6/2026	21:30:00	7	1.6126	3.8	1,360,021	13.8	110
6/6/2026	21:45:00	7	1.6277	3.2	1,360,045	13.2	110
6/6/2026	22:00:00	7	1.6202	1.9	1,360,069	13.3	112
6/6/2026	22:30:00	7	1.6353	0.8	1,360,101	13.6	114
6/6/2026	22:45:00	7.1	1.5709	0.8	1,360,126	14	114
6/6/2026	23:15:00	7.1	1.6126	1	1,360,155	14.2	114
6/6/2026	23:30:00	7	1.6012	0.6	1,360,179	14	245
6/7/2026	0:30:00	7	1.6467	0.3	1,360,195	14.1	245
6/7/2026	0:45:00	7.1	1.6315	1.1	1,360,220	14.4	243
6/7/2026	1:00:00	7	1.6088	0.4	1,360,241	14	245
6/7/2026	1:15:00	7.1	1.5104	2	1,360,243	14.4	243
6/7/2026	1:30:00	7	1.5823	1.1	1,360,266	14	243
6/7/2026	1:45:00	7.1	1.6126	1.8	1,360,275	14.4	243



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	2:00:00	7	1.6504	1.5	1,360,299	14.1	245
6/7/2026	2:30:00	7	1.6429	5.6	1,360,308	14.1	245
6/7/2026	2:45:00	7	1.6315	2.1	1,360,330	14	243
6/7/2026	3:00:00	7	0.4013	5.5	1,360,354	14	243
6/7/2026	3:15:00	7	1.6126	2.4	1,360,357	13.9	243
6/7/2026	3:30:00	7.1	1.6164	5.4	1,360,378	14	243
6/7/2026	3:45:00	7	1.6126	2.5	1,360,402	14.3	243
6/7/2026	4:15:00	7	1.6315	2.4	1,360,423	14	243
6/7/2026	4:30:00	7.1	1.6088	6.1	1,360,448	14.1	245
6/7/2026	4:45:00	7	1.5747	3.4	1,360,471	14.1	243
6/7/2026	5:15:00	7	1.6012	3.2	1,360,503	14	243
6/7/2026	5:30:00	7.1	1.6164	4	1,360,527	14	243
6/7/2026	5:45:00	7	1.6088	3.1	1,360,535	14	245
6/7/2026	6:00:00	7.1	1.5899	7.4	1,360,559	14.1	243
6/7/2026	6:15:00	7	1.6050	3.8	1,360,568	14	243
6/7/2026	6:45:00	7	1.5974	4.6	1,360,590	14	245
6/7/2026	7:00:00	7.1	1.6126	5.2	1,360,600	14.2	245
6/7/2026	7:15:00	7	1.5899	4.3	1,360,624	14.1	245
6/7/2026	7:30:00	7.1	1.6126	5.2	1,360,633	14.4	245
6/7/2026	7:45:00	7	1.6164	6.4	1,360,657	14.2	241
6/7/2026	8:15:00	7	1.6050	6.7	1,360,689	13.9	245
6/7/2026	8:30:00	7	1.5672	6.3	1,360,713	14	243
6/7/2026	8:45:00	7	1.6391	7.6	1,360,721	14	246
6/7/2026	9:15:00	7	0.3445	6.8	1,360,739	14.1	246
6/7/2026	9:30:00	7	1.8738	8.4	1,360,754	14.2	247
6/7/2026	10:00:00	7	1.6959	9.2	1,360,787	14.4	245
6/7/2026	10:30:00	7	1.6618	9.9	1,360,823	14.4	245
6/7/2026	10:45:00	7	1.6769	9.9	1,360,848	15.6	246
6/7/2026	11:00:00	7	1.6921	13.8	1,360,858	14.2	245
6/7/2026	11:15:00	7	1.6580	1.5	1,360,881	15.1	245
6/7/2026	11:45:00	6.9	1.6618	1.5	1,360,910	17.6	247
6/7/2026	12:00:00	7	1.7072	2.5	1,360,920	14.1	246



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	12:15:00	7	1.6694	4	1,360,945	13.9	245
6/7/2026	12:30:00	7	1.6732	2.7	1,360,970	13.9	245
6/7/2026	12:45:00	7	1.6202	2	1,360,990	14	247
6/7/2026	13:00:00	7	1.6012	2	1,361,014	14.3	248
6/7/2026	13:15:00	7	1.5899	1.8	1,361,038	14.5	246
6/7/2026	13:30:00	7.1	1.6202	1.2	1,361,060	14.9	246
6/7/2026	13:45:00	7	1.6126	3.4	1,361,084	14.9	246
6/7/2026	14:15:00	7	1.4536	4.2	1,361,105	14.6	245
6/7/2026	14:30:00	7	1.5596	2.6	1,361,125	14.8	247
6/7/2026	14:45:00	7	1.5747	5.9	1,361,133	14.1	247
6/7/2026	15:00:00	7.1	1.0864	4.9	1,361,155	14.4	245
6/7/2026	15:15:00	7	1.5974	4.7	1,361,178	14	245
6/7/2026	15:45:00	7	1.7072	4.9	1,361,215	14.2	245
6/7/2026	16:00:00	7.1	1.1318	3.8	1,361,239	14.7	245
6/7/2026	16:15:00	7	1.7413	4.4	1,361,263	14.2	247
6/7/2026	16:45:00	7	1.6353	5.3	1,361,303	13.6	245
6/7/2026	17:00:00	7.1	1.6694	4.4	1,361,317	14.3	246
6/7/2026	17:15:00	7	1.7072	6.5	1,361,342	14.1	245
6/7/2026	17:45:00	7	1.6769	6.9	1,361,383	14.1	243
6/7/2026	18:00:00	7.1	1.6580	4.7	1,361,391	14.8	243
6/7/2026	18:30:00	7.1	1.5066	5.3	1,361,420	14.4	245
6/7/2026	19:00:00	7	1.4309	5.8	1,361,447	14.5	245
6/7/2026	19:15:00	7	1.4157	6.8	1,361,465	14	245
6/7/2026	19:30:00	7	1.3892	6.2	1,361,486	14.6	245
6/7/2026	19:45:00	7	1.3892	5.4	1,361,503	13.7	245
6/7/2026	20:00:00	7.1	1.3590	5.1	1,361,524	14	243
6/7/2026	20:15:00	7	1.2340	7.8	1,361,532	13.5	247
6/7/2026	20:30:00	7	1.3552	6.7	1,361,534	14.2	245
6/7/2026	20:45:00	7	1.3362	4.9	1,361,551	13.5	248
6/7/2026	21:00:00	7.1	1.3173	4.5	1,361,571	13.9	246
6/7/2026	21:15:00	7	1.3325	4.9	1,361,588	14.5	246
6/7/2026	21:30:00	7	1.3287	5.5	1,361,608	13.9	246



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	21:45:00	7	1.3627	0.5	1,361,617	14.1	245
6/7/2026	22:00:00	7.1	1.3514	1.1	1,361,637	14.3	245
6/7/2026	22:15:00	7	1.3400	0.4	1,361,654	14.1	244
6/7/2026	22:30:00	7.1	1.3287	1.4	1,361,674	14.1	245
6/7/2026	22:45:00	7.1	1.2113	1	1,361,683	14.2	246
6/7/2026	23:00:00	7.1	1.2000	2.2	1,361,702	14.4	246
6/7/2026	23:30:00	7	1.4195	0.6	1,361,717	15.1	245
6/7/2026	23:45:00	7	1.4195	0.6	1,361,735	14.4	244

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

4. CP2 Discharge Parameter Summary:

Table 3: CP2 Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	0:00:00	7.37	0.3255	2	122198.6	13.5	150
6/1/2026	0:15:00	7.32	0.9417	2	122205.7	14.9	152
6/1/2026	0:30:00	7.36	0.9689	2	122219.4	13.5	151
6/1/2026	0:45:00	7.37	0.7092	2	122240.5	13.4	153
6/1/2026	1:00:00	7.38	2.3989	2	122256.0	12.9	155
6/1/2026	1:15:00	7.39	2.3485	2	122290.0	12.8	158
6/1/2026	1:30:00	7.38	0.6317	3	122312.7	13.4	157
6/1/2026	1:45:00	7.36	0.3333	2	122318.2	14.6	158
6/1/2026	2:00:00	7.34	0.3837	3	122323.8	15.5	158
6/1/2026	2:15:00	7.39	2.3369	4	122352.4	13.3	157
6/1/2026	2:30:00	7.41	2.3175	3	122385.7	13.2	156
6/1/2026	2:45:00	7.4	1.9338	3	122416.3	13.4	156
6/1/2026	3:00:00	7.41	2.1857	6	122432.5	13.4	155
6/1/2026	3:15:00	7.42	2.1625	2	122459.8	14.1	154
6/1/2026	3:30:00	7.41	1.3215	2	122484.1	14.5	154
6/1/2026	3:45:00	7.4	2.0772	2	122509.2	13.6	152
6/1/2026	4:00:00	7.39	0.3565	2	122520.5	14.6	152
6/1/2026	4:15:00	7.37	2.1431	2	122534.7	13.2	151
6/1/2026	4:30:00	7.39	1.4300	2	122561.6	13.2	152
6/1/2026	4:45:00	7.4	1.8912	2	122590.5	13.3	153
6/1/2026	5:00:00	7.37	0.2635	2	122603.1	15.9	153
6/1/2026	5:15:00	7.43	1.6315	2	122617.7	14	155
6/1/2026	5:30:00	7.43	0.8332	2	122642.2	13.7	166
6/1/2026	5:45:00	7.38	0.7557	2	122653.7	14.1	168
6/1/2026	6:00:00	7.37	1.7982	2	122671.6	13.6	167
6/1/2026	6:15:00	7.39	2.3601	2	122697.4	13.3	165
6/1/2026	6:30:00	7.4	0.4999	2	122717.5	14.1	162
6/1/2026	6:45:00	7.4	2.3562	3	122735.0	13.3	159
6/1/2026	7:00:00	7.41	1.5773	2	122765.7	14.4	156



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	7:15:00	7.38	2.3136	2	122797.4	15.4	158
6/1/2026	7:30:00	7.35	0.0969	2	122814.6	17	159
6/1/2026	7:45:00	7.4	1.6742	2	122826.6	13.7	156
6/1/2026	8:00:00	7.37	2.3252	2	122856.9	15.1	155
6/1/2026	8:15:00	7.33	2.2671	2	122890.9	17.2	157
6/1/2026	8:30:00	7.3	2.1896	2	122922.5	18.9	158
6/1/2026	8:45:00	7.35	1.9765	2	122949.5	14.8	146
6/1/2026	9:00:00	7.35	0.3100	2	122963.4	15.1	147
6/1/2026	9:15:00	7.35	1.3835	2	122978.2	13.9	152
6/1/2026	9:30:00	7.35	1.8214	2	123002.4	13.8	150
6/1/2026	9:45:00	7.35	1.4572	2	123027.3	14	149
6/1/2026	10:00:00	7.35	1.4727	2	123051.2	14.2	149
6/1/2026	10:15:00	7.34	1.7246	2	123075.9	15.9	147
6/1/2026	10:30:00	7.3	1.6936	2	123100.1	17.7	150
6/1/2026	10:45:00	7.34	0.3294	2	123116.7	16.5	149
6/1/2026	11:00:00	7.33	1.3060	2	123122.9	15.9	146
6/1/2026	11:15:00	7.28	1.5385	2	123143.6	18	151
6/1/2026	11:30:00	7.29	0.4185	2	123153.9	20	153
6/1/2026	11:45:00	7.31	1.2711	2	123167.4	14.4	150
6/1/2026	12:00:00	7.31	2.0462	2	123194.1	13.6	152
6/1/2026	12:15:00	7.31	2.0191	2	123224.7	13.6	153
6/1/2026	12:30:00	7.3	1.5540	2	123252.0	13.7	153
6/1/2026	12:45:00	7.3	1.5540	2	123274.4	13.9	153
6/1/2026	13:00:00	7.3	1.5424	2	123298.2	14	151
6/1/2026	13:15:00	7.31	1.5153	2	123322.0	14	151
6/1/2026	13:30:00	7.31	1.6742	2	123340.8	14.1	151
6/1/2026	13:45:00	7.31	1.4649	2	123362.4	14	151
6/1/2026	14:00:00	7.31	1.4184	2	123382.9	14	151
6/1/2026	14:15:00	7.3	1.2866	2	123403.8	14.1	151
6/1/2026	14:30:00	7.3	1.3641	2	123423.9	14.2	151
6/1/2026	14:45:00	7.3	1.2828	2	123444.3	14.2	151
6/1/2026	15:00:00	7.31	1.4223	2	123462.0	14.5	151



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	15:15:00	7.25	1.3758	2	123483.5	18.1	151
6/1/2026	15:30:00	7.7	1.2711	522	123501.9	21	0
6/1/2026	15:45:00	7.28	1.0115	2	123518.7	18.1	150
6/1/2026	16:00:00	7.22	0.8836	2	123534.4	20.8	152
6/1/2026	16:15:00	7.3	1.3331	2	123547.9	16.4	147
6/1/2026	16:30:00	7.3	1.8602	2	123567.5	16.2	147
6/1/2026	16:45:00	7.26	1.8524	2	123595.2	19.1	151
6/1/2026	17:00:00	7.32	1.7323	2	123621.0	14.5	149
6/1/2026	17:15:00	7.33	0.6821	2	123639.4	14.7	149
6/1/2026	17:30:00	7.28	0.5232	2	123646.4	18.2	149
6/1/2026	17:45:00	7.25	0.2597	2	123651.0	21	150
6/1/2026	18:00:00	7.31	0.7053	2	123664.9	15.3	148
6/1/2026	18:15:00	7.33	0.8565	6	123681.4	14.5	149
6/1/2026	18:30:00	7.32	2.0850	2	123704.4	13.9	147
6/1/2026	18:45:00	7.33	2.0230	2	123735.1	13.9	148
6/1/2026	19:00:00	7.31	1.7052	2	123765.3	16.4	146
6/1/2026	19:15:00	7.28	1.5153	2	123792.1	18.5	147
6/1/2026	19:30:00	7.25	1.1122	2	123815.2	20	148
6/1/2026	19:45:00	7.28	0.3410	2	123821.9	20.3	148
6/1/2026	20:00:00	7.27	1.6819	2	123832.9	20.8	148
6/1/2026	20:15:00	7.3	0.8138	2	123852.7	18.7	150
6/1/2026	20:30:00	7.31	0.8216	2	123863.5	16.8	150
6/1/2026	20:45:00	7.29	2.0462	2	123886.8	16.6	151
6/1/2026	21:00:00	7.26	0.4728	2	123906.5	18.2	154
6/1/2026	21:15:00	7.28	1.8137	2	123933.8	17	148
6/1/2026	21:30:00	7.24	1.4804	2	123957.6	18.6	150
6/1/2026	21:45:00	7.23	1.8369	2	123982.5	19.8	150
6/1/2026	22:00:00	7.21	1.6005	2	124006.8	20.8	150
6/1/2026	22:15:00	7.28	0.8681	3	124022.7	14.6	143
6/1/2026	22:30:00	7.28	0.9030	2	124044.0	16.7	147
6/1/2026	22:45:00	7.25	1.2828	2	124061.2	18.4	149
6/1/2026	23:00:00	7.27	1.8331	2	124077.4	17.3	146



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	23:15:00	7.24	1.8137	2	124105.5	18.5	148
6/1/2026	23:30:00	7.23	1.8059	2	124133.6	19.6	150
6/1/2026	23:45:00	7.21	1.6897	2	124160.5	20.3	151
6/2/2026	0:00:00	7.17	0.2945	2	124167.7	20.8	151
6/2/2026	0:15:00	7.15	0.3643	2	124171.4	21.2	151
6/2/2026	0:30:00	7.31	1.5230	5	124185.9	15.7	144
6/2/2026	0:45:00	7.31	1.7284	2	124200.8	13.8	146
6/2/2026	1:00:00	7.3	1.7633	2	124221.6	14.9	146
6/2/2026	1:15:00	7.32	1.8447	2	124239.1	14.5	145
6/2/2026	1:30:00	7.29	1.7439	2	124261.7	15.4	147
6/2/2026	1:45:00	7.25	0.3023	2	124268.2	17.2	148
6/2/2026	2:00:00	7.3	1.2944	2	124280.9	12.8	149
6/2/2026	2:15:00	7.3	1.5385	2	124301.9	12.4	149
6/2/2026	2:30:00	7.3	1.2828	2	124322.5	12.4	149
6/2/2026	2:45:00	7.3	1.3215	2	124342.6	12.4	149
6/2/2026	3:00:00	7.3	1.2246	2	124362.5	12.3	149
6/2/2026	3:15:00	7.29	0.5387	2	124381.1	12.4	149
6/2/2026	3:30:00	7.27	0.6239	2	124387.9	14.2	149
6/2/2026	3:45:00	7.29	1.3525	2	124403.0	12.4	149
6/2/2026	4:00:00	7.26	1.5230	2	124420.7	12.3	149
6/2/2026	4:15:00	7.25	1.4184	2	124441.6	12.2	150
6/2/2026	4:30:00	7.24	1.3021	2	124462.0	12.2	150
6/2/2026	4:45:00	7.26	1.8563	2	124484.2	12.8	150
6/2/2026	5:00:00	7.23	2.1392	2	124513.9	14.3	149
6/2/2026	5:15:00	7.21	2.1082	2	124543.4	15.3	149
6/2/2026	5:30:00	7.18	1.5618	2	124569.2	15.9	149
6/2/2026	5:45:00	7.17	1.9261	2	124596.3	16.5	150
6/2/2026	6:00:00	7.21	2.2671	2	124629.7	16.1	149
6/2/2026	6:15:00	7.24	2.2400	2	124663.6	13.3	146
6/2/2026	6:30:00	7.27	2.2012	2	124697.2	13.3	147
6/2/2026	6:45:00	7.24	1.6548	2	124727.1	14.4	147
6/2/2026	7:00:00	7.27	0.0853	2	124732.9	13.7	147



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	7:15:00	7.28	0.9146	3	124737.2	12.5	148
6/2/2026	7:30:00	7.3	1.0270	2	124752.2	12.2	150
6/2/2026	7:45:00	7.3	1.3525	2	124773.6	12.1	149
6/2/2026	8:00:00	7.3	0.1085	2	124783.8	13	149
6/2/2026	8:15:00	7.29	1.0464	2	124789.3	12.6	149
6/2/2026	8:30:00	7.3	1.1006	2	124808.2	12.6	150
6/2/2026	8:45:00	7.3	2.4648	2	124832.6	12.6	149
6/2/2026	9:00:00	7.28	1.9300	2	124866.0	12.7	147
6/2/2026	9:15:00	7.3	0.0000	2	124897.4	13.1	146
6/2/2026	9:30:00	7.28	0.0000	2	124897.4	14.4	146
6/2/2026	9:45:00	7.26	0.2364	2	124913.2	14.9	146
6/2/2026	10:00:00	7.23	0.3798	2	124918.4	16.6	147
6/2/2026	10:15:00	7.24	1.8951	4	124936.7	17.5	146
6/2/2026	10:30:00	7.22	0.0000	4	124958.8	19	147
6/2/2026	10:45:00	7.26	1.8757	2	124978.4	17	144
6/2/2026	11:00:00	7.23	1.7362	2	125004.2	18.7	146
6/2/2026	11:15:00	7.21	1.6819	2	125028.6	20	148
6/2/2026	11:30:00	7.18	0.0853	2	125038.1	21	149
6/2/2026	11:45:00	7.24	1.8447	2	125046.5	19.2	144
6/2/2026	12:00:00	7.21	1.7439	2	125073.7	20.5	149
6/2/2026	12:15:00	7.18	1.6548	2	125097.6	21.7	149
6/2/2026	12:30:00	7.17	1.7517	2	125123.9	22.7	150
6/2/2026	12:45:00	7.32	1.4882	2	125150.5	15.4	150
6/2/2026	13:00:00	7.31	0.7363	2	125170.2	15.3	152
6/2/2026	13:15:00	7.28	0.3410	2	125175.9	17.6	153
6/2/2026	13:30:00	7.27	1.7284	2	125184.6	16.3	152
6/2/2026	13:45:00	7.33	1.2634	3	125208.2	14.6	154
6/2/2026	14:00:00	7.32	1.5967	2	125231.4	14.3	152
6/2/2026	14:15:00	7.31	0.5077	2	125245.8	15	151
6/2/2026	14:30:00	7.31	0.3643	2	125252.3	16.1	151
6/2/2026	14:45:00	7.31	1.4184	2	125264.5	14.9	153
6/2/2026	15:00:00	7.32	1.7594	2	125286.3	14.6	152



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	15:15:00	7.32	1.8021	2	125313.5	14.4	151
6/2/2026	15:30:00	7.32	1.7904	2	125337.5	14.5	150
6/2/2026	15:45:00	7.32	0.6123	3	125354.6	15	149
6/2/2026	16:00:00	7.32	2.0230	2	125375.2	14.3	149
6/2/2026	16:15:00	7.32	1.4727	2	125404.2	14.3	150
6/2/2026	16:30:00	7.32	1.9803	2	125432.2	14.2	149
6/2/2026	16:45:00	7.32	0.5503	2	125447.8	15	148
6/2/2026	17:00:00	7.32	0.5813	2	125454.6	15.6	149
6/2/2026	17:15:00	7.3	2.0346	2	125477.5	16.8	149
6/2/2026	17:30:00	7.27	1.8951	2	125507.6	18.5	151
6/2/2026	17:45:00	7.31	1.8834	2	125536.1	14.8	147
6/2/2026	18:00:00	7.31	1.8912	2	125560.1	15.7	146
6/2/2026	18:15:00	7.33	1.8757	2	125587.4	14.3	149
6/2/2026	18:30:00	7.35	1.3990	2	125613.1	14.8	146
6/2/2026	18:45:00	7.3	0.1473	2	125619.3	16.9	146
6/2/2026	19:00:00	7.27	0.1783	2	125622.7	18.4	149
6/2/2026	19:15:00	7.3	1.7439	2	125637.3	15.4	146
6/2/2026	19:30:00	7.32	1.4610	2	125663.6	14.9	146
6/2/2026	19:45:00	7.28	1.3564	2	125683.9	16.6	147
6/2/2026	20:00:00	7.28	1.5695	2	125706.5	14.9	146
6/2/2026	20:15:00	7.25	1.4804	2	125729.1	16.4	146
6/2/2026	20:30:00	7.23	0.4108	2	125747.1	17.5	149
6/2/2026	20:45:00	7.34	1.2673	2	125763.9	14.7	160
6/2/2026	21:00:00	7.34	1.8408	4	125788.1	14.4	158
6/2/2026	21:15:00	7.32	1.2983	2	125812.5	14	155
6/2/2026	21:30:00	7.3	1.8447	2	125837.6	13.6	154
6/2/2026	21:45:00	7.32	1.9610	3	125861.3	13.3	151
6/2/2026	22:00:00	7.32	1.9532	2	125888.5	12.9	149
6/2/2026	22:15:00	7.31	0.6704	2	125905.5	13.2	148
6/2/2026	22:30:00	7.32	0.3720	2	125912.8	14.1	146
6/2/2026	22:45:00	7.31	1.9377	2	125923.9	13.1	147
6/2/2026	23:00:00	7.32	1.8098	2	125948.2	12.7	148



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	23:15:00	7.32	0.5542	2	125964.2	13	147
6/2/2026	23:30:00	7.33	0.3565	2	125970.0	14	147
6/2/2026	23:45:00	7.31	0.6937	4	125977.5	13.4	147
6/3/2026	0:00:00	7.33	1.9610	2	126001.1	12.6	148
6/3/2026	0:15:00	7.31	1.9610	2	126027.9	12.5	148
6/3/2026	0:30:00	7.31	1.9648	2	126055.0	12.6	149
6/3/2026	0:45:00	7.3	1.9610	2	126079.5	12.7	148
6/3/2026	1:00:00	7.3	1.9648	2	126106.1	12.6	149
6/3/2026	1:15:00	7.31	1.9571	2	126133.4	12.6	147
6/3/2026	1:30:00	7.3	1.9261	2	126157.7	13.3	146
6/3/2026	1:45:00	7.3	1.9338	2	126185.0	12.6	147
6/3/2026	2:00:00	7.32	1.4339	2	126211.7	12.7	147
6/3/2026	2:15:00	7.28	0.1279	2	126218.2	14.3	146
6/3/2026	2:30:00	7.26	0.2868	2	126221.5	15.1	146
6/3/2026	2:45:00	7.29	1.9338	4	126236.5	12.7	148
6/3/2026	3:00:00	7.28	1.9300	2	126263.1	12.6	148
6/3/2026	3:15:00	7.27	1.9222	2	126287.4	12.6	147
6/3/2026	3:30:00	7.28	1.3796	2	126313.7	12.8	146
6/3/2026	3:45:00	7.25	0.2325	2	126320.1	14.2	146
6/3/2026	4:00:00	7.23	0.2907	2	126323.5	15	146
6/3/2026	4:15:00	7.26	0.5852	4	126331.6	13.4	148
6/3/2026	4:30:00	7.24	0.5387	6	126338.6	12.8	148
6/3/2026	4:45:00	7.23	1.6044	2	126365.4	12.5	150
6/3/2026	5:00:00	7.21	2.1082	2	126394.3	12.3	150
6/3/2026	5:15:00	7.23	2.0927	2	126425.0	12.3	150
6/3/2026	5:30:00	7.24	2.0772	2	126454.7	12.3	149
6/3/2026	5:45:00	7.25	2.0578	2	126482.6	12.5	148
6/3/2026	6:00:00	7.27	1.9920	2	126512.1	12.3	148
6/3/2026	6:15:00	7.27	0.7480	2	126536.3	12.5	147
6/3/2026	6:30:00	7.28	0.1666	2	126542.7	14.2	145
6/3/2026	6:45:00	7.25	0.2984	2	126546.1	15.8	145
6/3/2026	7:00:00	7.26	0.2674	2	126549.8	17	146



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	7:15:00	7.24	1.5734	4	126554.2	16	137
6/3/2026	7:30:00	7.27	2.1470	2	126575.4	12.7	146
6/3/2026	7:45:00	7.25	2.1392	2	126606.1	12.6	147
6/3/2026	8:00:00	7.25	2.1392	2	126629.3	12.9	145
6/3/2026	8:15:00	7.25	2.1005	2	126660.0	12.6	146
6/3/2026	8:30:00	7.26	1.7711	2	126689.7	12.6	145
6/3/2026	8:45:00	7.28	1.3951	2	126718.2	12.8	145
6/3/2026	9:00:00	7.29	2.0075	2	126746.4	12.9	145
6/3/2026	9:15:00	7.28	0.1511	2	126755.9	14.6	143
6/3/2026	9:30:00	7.25	0.1511	2	126759.3	15.6	145
6/3/2026	9:45:00	7.25	1.6005	3	126766.5	16.3	146
6/3/2026	10:00:00	7.23	1.9842	2	126794.6	17.1	146
6/3/2026	10:15:00	7.28	1.8757	2	126822.2	13.1	146
6/3/2026	10:30:00	7.28	1.8447	2	126845.4	13.3	146
6/3/2026	10:45:00	7.28	0.1395	2	126859.7	14.5	146
6/3/2026	11:00:00	7.28	1.0890	2	126869.3	13.8	147
6/3/2026	11:15:00	7.29	0.1860	2	126880.9	14.6	147
6/3/2026	11:30:00	7.3	1.7711	2	126896.2	13.5	150
6/3/2026	11:45:00	7.32	1.5734	2	126923.3	13.3	151
6/3/2026	12:00:00	7.33	2.1121	2	126952.8	13.2	153
6/3/2026	12:15:00	7.31	0.8061	2	126976.6	13.5	153
6/3/2026	12:30:00	7.33	0.8216	3	126987.3	13.8	152
6/3/2026	12:45:00	7.34	2.1819	3	127013.5	13.2	154
6/3/2026	13:00:00	7.35	2.1547	3	127044.2	13.1	154
6/3/2026	13:15:00	7.33	0.5077	2	127060.4	14	152
6/3/2026	13:30:00	7.31	0.4612	3	127067.0	15	151
6/3/2026	13:45:00	7.29	0.4418	3	127073.8	16.2	152
6/3/2026	14:00:00	7.29	2.1160	3	127083.7	14.5	150
6/3/2026	14:15:00	7.31	2.1043	2	127114.3	13.4	150
6/3/2026	14:30:00	7.29	2.1276	2	127145.0	13.3	149
6/3/2026	14:45:00	7.27	1.0929	3	127166.6	13.7	148
6/3/2026	15:00:00	7.27	0.5813	2	127182.7	14	146



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	15:15:00	7.24	0.4030	2	127189.6	15.5	146
6/3/2026	15:30:00	7.24	1.0076	3	127197.5	14.6	146
6/3/2026	15:45:00	7.23	2.1198	2	127226.5	13.4	146
6/3/2026	16:00:00	7.22	2.1121	2	127257.2	13.2	146
6/3/2026	16:15:00	7.23	1.5269	2	127286.7	13.2	146
6/3/2026	16:30:00	7.24	0.3759	2	127299.7	14.5	143
6/3/2026	16:45:00	7.21	0.3643	2	127305.6	15.6	146
6/3/2026	17:00:00	7.18	0.3953	2	127312.4	16.6	146
6/3/2026	17:15:00	7.23	1.0502	2	127324.1	14.1	145
6/3/2026	17:30:00	7.23	2.0578	2	127345.2	13.4	148
6/3/2026	17:45:00	7.22	0.7402	2	127370.9	13.3	150
6/3/2026	18:00:00	7.22	0.3914	2	127378.9	14.8	149
6/3/2026	18:15:00	7.21	1.1471	3	127386.9	14.2	150
6/3/2026	18:30:00	7.25	0.6511	3	127414.1	13.2	164
6/3/2026	18:45:00	7.26	2.1664	3	127431.5	13	170
6/3/2026	19:00:00	7.28	2.1857	3	127452.0	13	175
6/3/2026	19:15:00	7.28	1.6083	3	127481.0	13.8	178
6/3/2026	19:30:00	7.3	2.1547	2	127510.6	13.7	181
6/3/2026	19:45:00	7.32	2.1431	2	127540.8	13.7	182
6/3/2026	20:00:00	7.34	2.1315	3	127571.4	13.7	183
6/3/2026	20:15:00	7.33	0.4302	2	127586.4	14.4	182
6/3/2026	20:30:00	7.3	0.4147	2	127593.3	15.3	183
6/3/2026	20:45:00	7.27	0.4495	2	127600.1	16.1	184
6/3/2026	21:00:00	7.28	2.0772	3	127609.9	15.7	181
6/3/2026	21:15:00	7.37	2.0850	3	127640.1	13.9	179
6/3/2026	21:30:00	7.36	1.0502	2	127663.4	14.2	178
6/3/2026	21:45:00	7.35	2.0772	2	127687.1	13.8	177
6/3/2026	22:00:00	7.35	2.0927	3	127717.8	13.6	177
6/3/2026	22:15:00	7.37	2.0772	3	127748.4	12.7	176
6/3/2026	22:30:00	7.38	2.0617	3	127775.5	12.7	174
6/3/2026	22:45:00	7.34	0.3527	2	127788.4	13.8	170
6/3/2026	23:00:00	7.31	0.3604	2	127792.7	14.7	172



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	23:15:00	7.31	0.9689	4	127800.2	14.3	171
6/3/2026	23:30:00	7.35	2.0075	3	127829.4	12.6	168
6/3/2026	23:45:00	7.25	1.4727	4	127855.6	12.8	258
6/4/2026	0:00:00	7.3	1.3138	3	127870.5	12.9	167
6/4/2026	0:15:00	7.29	0.6433	3	127889.5	12.7	164
6/4/2026	0:30:00	7.26	0.3255	3	127895.8	13.9	161
6/4/2026	0:45:00	7.26	1.1510	4	127902.2	13.3	162
6/4/2026	1:00:00	7.28	2.0036	3	127928.1	12.4	160
6/4/2026	1:15:00	7.27	2.0578	3	127958.0	12.3	159
6/4/2026	1:30:00	7.26	2.0152	3	127988.7	12.3	159
6/4/2026	1:45:00	7.26	1.1549	3	128012.8	12.6	157
6/4/2026	2:00:00	7.25	0.1821	3	128022.3	13.5	154
6/4/2026	2:15:00	7.23	0.1783	3	128025.7	14.2	156
6/4/2026	2:30:00	7.25	1.9067	3	128039.8	12.6	156
6/4/2026	2:45:00	7.26	1.8679	3	128062.9	12.5	155
6/4/2026	3:00:00	7.26	1.8214	3	128090.1	12.4	155
6/4/2026	3:15:00	7.16	1.7866	3	128115.8	12.5	162
6/4/2026	3:30:00	7.04	1.2014	3	128139.0	12.9	167
6/4/2026	3:45:00	7.03	1.7401	3	128165.4	12.8	164
6/4/2026	4:00:00	7.09	1.7013	3	128188.6	12.7	161
6/4/2026	4:15:00	7.14	1.2401	3	128212.0	12.7	160
6/4/2026	4:30:00	7.18	0.3759	3	128226.1	13.3	158
6/4/2026	4:45:00	7.15	0.0853	3	128226.7	14	157
6/4/2026	5:00:00	7.18	1.6083	3	128237.2	12.9	158
6/4/2026	5:15:00	7.19	0.9805	3	128251.8	12.8	157
6/4/2026	5:30:00	7.24	2.2787	3	128282.7	12.4	157
6/4/2026	5:45:00	7.24	1.8408	4	128315.9	12.3	157
6/4/2026	6:00:00	7.24	1.2750	3	128344.1	12.4	157
6/4/2026	6:15:00	7.24	1.1859	3	128361.3	12.6	156
6/4/2026	6:30:00	7.25	2.2594	3	128392.5	12.3	156
6/4/2026	6:45:00	7.25	2.2167	4	128426.6	12.3	155
6/4/2026	7:00:00	7.26	2.1198	4	128456.8	12.4	155



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	7:15:00	7.24	0.1899	3	128469.0	13.2	153
6/4/2026	7:30:00	7.2	0.1666	3	128472.4	13.9	154
6/4/2026	7:45:00	7.17	0.2015	3	128475.9	14.5	154
6/4/2026	8:00:00	7.21	0.9960	4	128488.6	13.2	155
6/4/2026	8:15:00	7.25	2.2594	3	128518.8	12.6	155
6/4/2026	8:30:00	7.26	2.2400	4	128552.9	12.7	156
6/4/2026	8:45:00	7.27	1.5967	4	128584.3	12.9	157
6/4/2026	9:00:00	7.28	2.2361	4	128614.5	12.9	158
6/4/2026	9:15:00	7.27	0.2868	3	128628.7	13.8	156
6/4/2026	9:30:00	7.24	0.3178	4	128632.1	14.4	157
6/4/2026	9:45:00	7.26	2.2477	5	128642.6	13.5	159
6/4/2026	10:00:00	7.32	1.7594	4	128676.3	13.2	154
6/4/2026	10:15:00	7.33	1.0657	4	128703.4	13.5	149
6/4/2026	10:30:00	7.29	0.1976	4	128710.1	14.6	149
6/4/2026	10:45:00	7.27	0.4495	4	128713.6	15.3	149
6/4/2026	11:00:00	7.3	0.5348	3	128727.4	14.8	146
6/4/2026	11:15:00	7.33	2.3059	4	128736.1	14.4	138
6/4/2026	11:30:00	7.34	0.0000	4	128755.8	14	138
6/4/2026	11:45:00	7.32	0.3294	4	128761.0	14.9	138
6/4/2026	12:00:00	7.29	0.3565	4	128765.7	15.7	139
6/4/2026	12:15:00	7.36	1.6936	4	128782.6	14.2	136
6/4/2026	12:30:00	7.42	2.3446	4	128814.1	13.8	135
6/4/2026	12:45:00	7.46	2.3175	4	128848.1	13.9	135
6/4/2026	13:00:00	7.47	2.2826	4	128881.0	13.9	136
6/4/2026	13:15:00	7.44	0.6549	4	128903.4	14.4	135
6/4/2026	13:30:00	7.41	0.2480	4	128908.2	15.4	135
6/4/2026	13:45:00	7.38	0.2752	4	128911.6	16.2	135
6/4/2026	14:00:00	7.36	1.1200	4	128918.9	15.1	137
6/4/2026	14:15:00	7.37	1.5075	4	128934.1	14.8	136
6/4/2026	14:30:00	7.44	1.1122	0	128965.1	14.1	135
6/4/2026	14:45:00	7.38	0.2674	0	128972.7	15.2	132
6/4/2026	15:00:00	7.33	0.6046	0	128976.3	16.3	135



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	15:15:00	7.43	1.9803	0	129003.5	14.1	135
6/4/2026	15:30:00	7.44	2.1702	0	129034.4	13.9	133
6/4/2026	15:45:00	7.42	0.3410	0	129052.2	14.9	132
6/4/2026	16:00:00	7.38	0.2325	0	129055.6	16.3	133
6/4/2026	16:15:00	7.35	0.2131	0	129059.0	17.4	133
6/4/2026	16:30:00	7.43	1.4804	0	129082.9	14.3	135
6/4/2026	16:45:00	7.46	0.3372	0	129106.6	14.2	135
6/4/2026	17:00:00	7.4	0.3875	0	129112.5	15.8	134
6/4/2026	17:15:00	7.43	1.2634	0	129129.9	14	135
6/4/2026	17:30:00	7.44	0.6201	0	129148.5	14.3	134
6/4/2026	17:45:00	7.4	0.1705	0	129152.8	15.7	134
6/4/2026	18:00:00	7.44	2.2129	0	129169.3	14.1	135
6/4/2026	18:15:00	7.46	2.1625	0	129196.4	13.6	136
6/4/2026	18:30:00	7.46	1.3641	0	129225.5	13.4	136
6/4/2026	18:45:00	7.42	0.1434	0	129234.5	14.9	134
6/4/2026	19:00:00	7.42	1.2711	0	129245.0	14	135
6/4/2026	19:15:00	7.44	1.3564	0	129270.9	13.4	136
6/4/2026	19:30:00	7.44	1.9648	0	129294.2	13.3	136
6/4/2026	19:45:00	7.44	1.9145	0	129321.4	13	136
6/4/2026	20:00:00	7.44	0.8410	0	129345.3	13.1	136
6/4/2026	20:15:00	7.41	0.0620	0	129348.3	14.5	134
6/4/2026	20:30:00	7.4	1.2634	0	129353.9	13.5	136
6/4/2026	20:45:00	7.43	1.9571	0	129381.1	12.8	136
6/4/2026	21:00:00	7.43	1.2944	0	129407.6	12.7	136
6/4/2026	21:15:00	7.42	1.9261	0	129430.9	12.6	136
6/4/2026	21:30:00	7.42	1.8447	0	129458.2	12.5	136
6/4/2026	21:45:00	7.42	0.5774	0	129479.7	12.8	136
6/4/2026	22:00:00	7.38	0.3565	0	129482.3	14.1	134
6/4/2026	22:15:00	7.42	2.5500	0	129509.7	12.5	136
6/4/2026	22:30:00	7.41	0.2752	0	129538.2	12.5	136
6/4/2026	22:45:00	7.41	0.3720	0	129546.3	13.6	135
6/4/2026	23:00:00	7.38	0.3992	0	129553.1	14.3	135



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	23:15:00	7.38	1.0890	0	129560.7	13.7	135
6/4/2026	23:30:00	7.41	1.5075	0	129588.9	12.4	136
6/4/2026	23:45:00	7.42	1.0231	0	129608.5	12.6	136
6/5/2026	0:00:00	7.4	1.2750	0	129629.0	12.4	136
6/5/2026	0:15:00	7.42	2.3097	0	129661.3	12.2	137
6/5/2026	0:30:00	7.42	0.6782	0	129682.2	12.4	137
6/5/2026	0:45:00	7.4	0.3100	0	129687.1	13.9	135
6/5/2026	1:00:00	7.35	0.9534	0	129692.5	16.7	139
6/5/2026	1:15:00	7.42	2.2826	0	129721.4	12.6	136
6/5/2026	1:30:00	7.43	1.6354	0	129753.9	12.7	136
6/5/2026	1:45:00	7.41	0.8410	0	129771.8	13.4	135
6/5/2026	2:00:00	7.39	0.3372	0	129778.4	15.8	133
6/5/2026	2:15:00	7.35	0.4030	0	129784.7	17.1	134
6/5/2026	2:30:00	7.4	2.2516	0	129801.3	12.8	135
6/5/2026	2:45:00	7.41	2.2400	0	129835.3	12.2	136
6/5/2026	3:00:00	7.4	1.1820	0	129856.2	12.7	135
6/5/2026	3:15:00	7.4	0.6317	0	129874.0	12.6	135
6/5/2026	3:30:00	7.39	0.3643	0	129880.3	13.9	134
6/5/2026	3:45:00	7.34	0.7441	0	129887.2	14.3	136
6/5/2026	4:00:00	7.41	2.2167	0	129916.3	12.1	136
6/5/2026	4:15:00	7.4	2.1896	0	129947.9	12	136
6/5/2026	4:30:00	7.39	0.4185	0	129960.8	12.7	135
6/5/2026	4:45:00	7.37	1.0502	0	129969.5	12.6	134
6/5/2026	5:00:00	7.4	2.1470	0	129989.0	12.2	136
6/5/2026	5:15:00	7.4	0.9844	0	130016.3	12	136
6/5/2026	5:30:00	7.4	0.3178	0	130023.4	12.8	134
6/5/2026	5:45:00	7.38	0.3759	0	130028.5	13.5	134
6/5/2026	6:00:00	7.4	2.2439	0	130043.9	12.1	136
6/5/2026	6:15:00	7.4	2.2167	0	130078.0	11.9	137
6/5/2026	6:30:00	7.4	2.1896	0	130109.5	11.9	137
6/5/2026	6:45:00	7.4	0.9689	0	130135.9	12	137
6/5/2026	7:00:00	7.39	0.2674	0	130142.4	12.9	136



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	7:15:00	7.35	0.3217	0	130145.9	13.5	135
6/5/2026	7:30:00	7.38	1.4068	0	130158.1	12.2	136
6/5/2026	7:45:00	7.37	1.4959	0	130177.3	12.2	136
6/5/2026	8:00:00	7.39	1.5114	0	130209.4	12	136
6/5/2026	8:15:00	7.39	0.3333	0	130220.2	12.7	136
6/5/2026	8:30:00	7.36	0.3449	0	130225.4	13.3	135
6/5/2026	8:45:00	7.39	2.1974	0	130242.8	12.4	136
6/5/2026	9:00:00	7.39	2.1664	0	130272.8	12.4	136
6/5/2026	9:15:00	7.39	2.1431	0	130303.5	12.4	135
6/5/2026	9:30:00	7.38	0.4185	0	130316.6	14.2	133
6/5/2026	9:45:00	7.34	0.2945	0	130320.7	18.3	133
6/5/2026	10:00:00	7.36	2.1509	0	130332.9	13.3	132
6/5/2026	10:15:00	7.38	2.1354	0	130360.7	12.6	135
6/5/2026	10:30:00	7.38	1.1704	0	130382.8	12.8	134
6/5/2026	10:45:00	7.38	0.6588	0	130396.0	12.8	134
6/5/2026	11:00:00	7.32	0.2364	0	130400.4	26.1	117
6/5/2026	11:15:00	7.34	0.2713	523	130403.8	15.7	0
6/5/2026	11:30:00	6.93	0.1938	750	130413.7	16.2	0
6/5/2026	11:45:00	6.45	0.2015	1	130417.1	18.7	0
6/5/2026	12:00:00	7.4	2.2516	0	130448.0	12.3	158
6/5/2026	12:15:00	7.42	2.2129	0	130482.0	12.2	159
6/5/2026	12:30:00	7.43	2.1819	0	130513.5	12.2	159
6/5/2026	12:45:00	7.43	0.7441	0	130538.0	12.3	159
6/5/2026	13:00:00	7.44	0.2597	0	130543.2	13.3	157
6/5/2026	13:15:00	7.41	2.0113	0	130551.1	12.5	159
6/5/2026	13:30:00	7.43	1.1859	0	130565.4	12.3	159
6/5/2026	13:45:00	7.43	2.1160	0	130594.7	12	160
6/5/2026	14:00:00	7.43	2.0811	0	130625.4	12	160
6/5/2026	14:15:00	7.43	1.2440	0	130650.6	12	159
6/5/2026	14:30:00	7.47	0.3604	0	130661.6	12.3	159
6/5/2026	14:45:00	7.44	0.1589	0	130665.0	13	158
6/5/2026	15:00:00	7.44	0.9146	0	130670.4	12.5	159



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	15:15:00	7.44	1.9842	0	130696.5	11.9	161
6/5/2026	15:30:00	7.44	1.9532	0	130724.8	11.9	161
6/5/2026	15:45:00	7.44	1.9261	0	130751.9	12	161
6/5/2026	16:00:00	7.44	0.8526	0	130772.6	12.2	160
6/5/2026	16:15:00	7.47	0.0000	0	130794.6	12.3	160
6/5/2026	16:30:00	7.45	0.0000	0	130794.6	13	159
6/5/2026	16:45:00	7.44	0.0000	0	130794.6	12.6	161
6/5/2026	17:00:00	7.43	1.1355	0	130813.7	12.4	161
6/5/2026	17:15:00	7.43	1.1006	0	130832.4	12.6	159
6/5/2026	17:30:00	7.41	2.1780	0	130858.4	12.4	159
6/5/2026	17:45:00	7.41	1.2208	0	130878.1	12.4	160
6/5/2026	18:00:00	7.43	0.3720	0	130889.0	12.9	159
6/5/2026	18:15:00	7.4	2.1276	0	130900.5	12.5	159
6/5/2026	18:30:00	7.42	2.1160	0	130931.1	12.3	160
6/5/2026	18:45:00	7.42	2.1005	0	130961.8	12.2	160
6/5/2026	19:00:00	7.42	1.2053	0	130988.0	12.2	159
6/5/2026	19:15:00	7.45	0.4185	0	130998.8	12.3	159
6/5/2026	19:30:00	7.45	0.3837	0	131005.6	12.9	158
6/5/2026	19:45:00	7.44	0.3604	0	131012.4	13.2	159
6/5/2026	20:00:00	7.43	2.0850	0	131032.0	12	160
6/5/2026	20:15:00	7.42	0.7635	0	131050.0	12	160
6/5/2026	20:30:00	7.42	1.2169	0	131062.9	11.9	159
6/5/2026	20:45:00	7.42	2.2167	0	131083.3	11.8	161
6/5/2026	21:00:00	7.43	0.5736	0	131102.3	11.8	160
6/5/2026	21:15:00	7.43	0.3527	0	131106.9	12.2	159
6/5/2026	21:30:00	7.42	1.8912	0	131121.8	11.7	161
6/5/2026	21:45:00	7.42	1.8602	0	131149.0	11.7	161
6/5/2026	22:00:00	7.41	1.8098	0	131175.3	11.6	160
6/5/2026	22:15:00	7.43	0.1744	0	131187.5	11.8	160
6/5/2026	22:30:00	7.42	0.2170	0	131190.9	12.6	159
6/5/2026	22:45:00	7.41	0.3062	0	131193.9	14.2	158
6/5/2026	23:00:00	7.41	1.2711	0	131212.3	11.8	159



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	23:15:00	7.41	1.8059	0	131237.1	11.7	159
6/5/2026	23:30:00	7.4	1.9183	0	131263.6	11.8	159
6/5/2026	23:45:00	7.38	1.5967	0	131290.8	11.9	161
6/6/2026	0:00:00	7.4	0.2170	0	131300.5	13.7	159
6/6/2026	0:15:00	7.38	0.1046	0	131302.5	14.8	159
6/6/2026	0:30:00	7.38	0.6937	0	131310.5	12.5	161
6/6/2026	0:45:00	7.39	1.8718	0	131331.0	12.3	161
6/6/2026	1:00:00	7.4	1.8524	0	131358.2	12.2	160
6/6/2026	1:15:00	7.4	1.4145	0	131382.6	12.4	160
6/6/2026	1:30:00	7.41	0.0504	0	131391.6	13.4	159
6/6/2026	1:45:00	7.39	0.3062	0	131393.2	14	161
6/6/2026	2:00:00	7.4	1.4184	0	131408.8	12.2	160
6/6/2026	2:15:00	7.41	2.0191	0	131435.7	13.5	158
6/6/2026	2:30:00	7.38	0.2635	0	131450.1	14.2	160
6/6/2026	2:45:00	7.37	0.2519	0	131453.5	14.9	161
6/6/2026	3:00:00	7.39	1.4494	0	131464.0	12.4	159
6/6/2026	3:15:00	7.39	1.8369	0	131490.0	12.1	158
6/6/2026	3:30:00	7.39	1.8098	0	131512.9	12.2	158
6/6/2026	3:45:00	7.42	0.0543	0	131530.6	13.4	157
6/6/2026	4:00:00	7.4	0.1938	0	131532.2	14.6	157
6/6/2026	4:15:00	7.39	0.1744	0	131535.6	15.2	159
6/6/2026	4:30:00	7.39	0.9030	1	131542.4	12.2	159
6/6/2026	4:45:00	7.4	1.7594	0	131566.8	11.9	160
6/6/2026	5:00:00	7.4	1.7362	0	131593.1	11.8	159
6/6/2026	5:15:00	7.41	1.8176	0	131618.3	11.8	161
6/6/2026	5:30:00	7.4	1.2208	0	131644.0	12.2	160
6/6/2026	5:45:00	7.41	1.5153	0	131668.1	11.9	160
6/6/2026	6:00:00	7.42	0.1666	0	131679.5	12.8	157
6/6/2026	6:15:00	7.41	1.5502	0	131688.5	11.9	160
6/6/2026	6:30:00	7.41	1.8447	0	131715.6	11.6	161
6/6/2026	6:45:00	7.42	1.4029	0	131741.9	11.6	161
6/6/2026	7:00:00	7.41	1.7633	0	131767.4	11.6	161



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	7:15:00	7.43	2.1237	0	131791.6	11.9	161
6/6/2026	7:30:00	7.41	1.9493	0	131821.5	14	159
6/6/2026	7:45:00	7.4	0.1163	0	131834.9	14	157
6/6/2026	8:00:00	7.39	0.0698	0	131834.9	15.7	158
6/6/2026	8:15:00	7.38	0.8138	0	131838.5	12.8	159
6/6/2026	8:30:00	7.39	0.8448	0	131848.9	12.7	161
6/6/2026	8:45:00	7.37	1.4765	0	131865.6	12.2	161
6/6/2026	9:00:00	7.37	2.0307	0	131889.7	14.8	158
6/6/2026	9:15:00	7.35	1.9067	0	131918.7	19.1	159
6/6/2026	9:30:00	7.33	1.7982	0	131944.5	21.1	160
6/6/2026	9:45:00	7.32	1.8718	0	131971.8	21.2	161
6/6/2026	10:00:00	7.3	0.2325	0	131984.5	20.9	161
6/6/2026	10:15:00	7.28	0.1976	0	131987.9	20.8	161
6/6/2026	10:30:00	7.33	1.5308	8	131994.7	13.9	156
6/6/2026	10:45:00	7.35	1.2324	0	132016.9	12.5	159
6/6/2026	11:00:00	7.37	1.3486	0	132036.0	12.7	159
6/6/2026	11:15:00	7.35	0.2364	0	132042.7	15.2	157
6/6/2026	11:30:00	7.33	0.2558	0	132046.1	17.1	157
6/6/2026	11:45:00	7.32	0.9921	0	132051.3	14	157
6/6/2026	12:00:00	7.34	1.1587	0	132071.2	12.8	160
6/6/2026	12:15:00	7.35	0.4147	0	132083.5	13.6	159
6/6/2026	12:30:00	7.36	1.9222	0	132100.8	12.6	160
6/6/2026	12:45:00	7.37	1.8912	0	132126.6	12.6	160
6/6/2026	13:00:00	7.37	1.8563	0	132150.3	12.7	161
6/6/2026	13:15:00	7.39	0.6162	0	132169.8	12.9	160
6/6/2026	13:30:00	7.38	0.2829	0	132173.7	14.7	158
6/6/2026	13:45:00	7.38	1.3138	0	132185.8	13.1	160
6/6/2026	14:00:00	7.39	1.2208	0	132208.1	12.9	160
6/6/2026	14:15:00	7.4	1.7556	0	132232.0	12.7	160
6/6/2026	14:30:00	7.4	1.7401	0	132259.3	12.6	160
6/6/2026	14:45:00	7.41	1.7246	0	132282.8	12.6	160
6/6/2026	15:00:00	7.43	0.3372	0	132296.9	12.9	161



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	15:15:00	7.41	0.1744	0	132300.3	13.8	159
6/6/2026	15:30:00	7.39	0.1705	0	132303.7	14.5	158
6/6/2026	15:45:00	7.38	0.8913	0	132310.0	13.4	159
6/6/2026	16:00:00	7.37	1.7168	0	132330.9	12.7	159
6/6/2026	16:15:00	7.38	1.7749	0	132355.1	12.6	160
6/6/2026	16:30:00	7.41	0.2635	0	132378.6	12.8	159
6/6/2026	16:45:00	7.39	0.3062	0	132382.0	13.8	158
6/6/2026	17:00:00	7.4	0.6549	0	132401.3	12.9	159
6/6/2026	17:15:00	7.38	1.0812	0	132408.8	13.2	159
6/6/2026	17:30:00	7.39	1.4184	0	132427.2	12.8	160
6/6/2026	17:45:00	7.4	2.0772	0	132454.1	13.3	162
6/6/2026	18:00:00	7.39	1.9648	0	132484.2	13.9	161
6/6/2026	18:15:00	7.38	2.0385	0	132512.9	14.3	162
6/6/2026	18:30:00	7.37	0.0000	0	132540.4	14.8	162
6/6/2026	18:45:00	7.36	0.1046	0	132540.4	15.1	162
6/6/2026	19:00:00	7.46	1.7556	0	132559.5	13.3	156
6/6/2026	19:15:00	7.48	1.7207	0	132585.0	13.2	155
6/6/2026	19:30:00	7.49	1.6587	0	132607.6	13.1	154
6/6/2026	19:45:00	7.5	1.6199	0	132631.4	13	155
6/6/2026	20:00:00	7.5	1.5695	0	132655.3	13	155
6/6/2026	20:15:00	7.51	1.4998	0	132676.2	13	154
6/6/2026	20:30:00	7.51	1.8834	0	132697.2	13	154
6/6/2026	20:45:00	7.52	1.7672	0	132724.4	13.2	154
6/6/2026	21:00:00	7.52	1.5657	0	132749.2	13.3	154
6/6/2026	21:15:00	7.5	0.5736	0	132758.5	13.6	154
6/6/2026	21:30:00	7.5	1.2130	0	132776.6	13.8	154
6/6/2026	21:45:00	7.49	1.7711	0	132801.0	14	154
6/6/2026	22:00:00	7.46	1.4882	0	132827.6	14.6	154
6/6/2026	22:15:00	7.46	0.1976	0	132844.0	15.3	155
6/6/2026	22:30:00	7.43	0.2519	0	132845.5	15.8	155
6/6/2026	22:45:00	7.42	0.2597	0	132848.9	16.3	154
6/6/2026	23:00:00	7.41	1.4727	0	132863.5	17.4	154



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	23:15:00	7.39	1.7129	0	132887.3	17.9	155
6/6/2026	23:30:00	7.37	1.7013	0	132903.8	18.1	155
6/6/2026	23:45:00	7.36	1.1122	0	132931.2	18.3	155
6/7/2026	0:00:00	7.33	1.2905	0	132951.0	18.5	155
6/7/2026	0:15:00	7.32	0.9572	0	132973.6	18.8	155
6/7/2026	0:30:00	7.3	0.1976	0	132981.8	20.4	155
6/7/2026	0:45:00	7.29	0.1705	0	132985.3	20.9	155
6/7/2026	1:00:00	7.26	0.1821	0	132988.7	21.3	156
6/7/2026	1:15:00	7.25	1.1587	0	132996.8	21.2	157
6/7/2026	1:30:00	7.25	1.5967	0	133017.7	20.5	157
6/7/2026	1:45:00	7.24	1.1742	0	133037.6	19.5	157
6/7/2026	2:00:00	7.22	1.1510	0	133050.5	18.8	157
6/7/2026	2:15:00	7.21	1.5230	0	133070.8	18.1	157
6/7/2026	2:30:00	7.2	1.3680	0	133093.8	17.5	156
6/7/2026	2:45:00	7.2	1.5889	0	133112.7	17	156
6/7/2026	3:00:00	7.2	1.5928	0	133138.0	16.6	156
6/7/2026	3:15:00	7.19	1.3060	0	133153.9	16.3	156
6/7/2026	3:30:00	7.18	1.2401	0	133172.7	16.2	156
6/7/2026	3:45:00	7.17	1.3409	0	133192.7	16.1	155
6/7/2026	4:00:00	7.16	1.3254	0	133212.9	16.1	156
6/7/2026	4:15:00	7.15	0.1124	0	133223.9	17.7	155
6/7/2026	4:30:00	7.14	0.1085	0	133223.9	18.6	156
6/7/2026	4:45:00	7.13	0.5891	0	133229.9	20.2	156
6/7/2026	5:00:00	7.12	1.4068	0	133246.4	21.9	157
6/7/2026	5:15:00	7.1	0.7712	0	133261.5	23.3	157
6/7/2026	5:30:00	7.49	1.2595	0	133276.7	13.8	146
6/7/2026	5:45:00	7.49	1.2053	0	133293.8	12.7	148
6/7/2026	6:00:00	7.49	0.9417	0	133309.2	12.5	150
6/7/2026	6:15:00	7.49	1.2440	0	133326.0	12.8	149
6/7/2026	6:30:00	7.49	1.6432	0	133347.7	12.4	150
6/7/2026	6:45:00	7.52	1.7904	0	133371.1	13.3	147
6/7/2026	7:00:00	7.54	0.4534	0	133391.2	12.8	151



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	7:15:00	7.49	1.9997	0	133420.7	13.3	150
6/7/2026	7:30:00	7.47	0.0000	0	133445.2	13.9	150
6/7/2026	7:45:00	7.47	0.1008	0	133445.2	14.3	151
6/7/2026	8:00:00	7.46	0.1240	0	133446.5	14.5	151
6/7/2026	8:15:00	7.45	0.2015	0	133449.9	14.8	151
6/7/2026	8:30:00	7.44	0.2093	0	133453.3	15.2	151
6/7/2026	8:45:00	7.43	0.0000	0	133455.4	15.5	151
6/7/2026	9:00:00	7.42	0.2170	0	133457.9	15.6	151
6/7/2026	9:15:00	7.49	0.0000	0	133475.1	12.9	150
6/7/2026	9:30:00	7.48	1.3254	0	133489.2	12.3	150
6/7/2026	9:45:00	7.5	1.9067	0	133513.3	12.2	152
6/7/2026	10:00:00	7.52	1.8602	0	133540.5	12.2	152
6/7/2026	10:15:00	7.52	0.4961	0	133556.2	12.4	152
6/7/2026	10:30:00	7.51	0.2790	0	133560.0	13.4	151
6/7/2026	10:45:00	7.51	1.6819	0	133577.9	12.5	152
6/7/2026	11:00:00	7.53	1.8176	0	133605.1	12.4	153
6/7/2026	11:15:00	7.53	0.8681	0	133628.3	12.5	152
6/7/2026	11:30:00	7.53	0.2286	0	133634.1	13.4	150
6/7/2026	11:45:00	7.52	0.2442	0	133637.5	14	150
6/7/2026	12:00:00	7.49	1.1549	0	133647.9	12.8	152
6/7/2026	12:15:00	7.52	0.0000	0	133657.5	13	151
6/7/2026	12:30:00	7.5	0.4108	0	133661.3	13.2	152
6/7/2026	12:45:00	7.52	1.9338	0	133674.2	12.6	151
6/7/2026	13:00:00	7.53	1.8834	0	133700.5	12.4	151
6/7/2026	13:15:00	7.54	1.4727	0	133723.6	12.4	150
6/7/2026	13:30:00	7.54	1.4455	0	133741.9	12.5	150
6/7/2026	13:45:00	7.55	0.0000	0	133751.7	13.1	148
6/7/2026	14:00:00	7.54	0.5968	1	133754.6	12.9	150
6/7/2026	14:15:00	7.53	1.5812	2	133765.1	12.9	151
6/7/2026	14:30:00	7.55	0.2519	0	133777.8	13.4	150
6/7/2026	14:45:00	7.54	1.1975	4	133792.1	12.8	154
6/7/2026	15:00:00	7.56	0.6278	1	133809.0	12.7	154



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	15:15:00	7.56	0.6549	0	133823.5	12.8	154
6/7/2026	15:30:00	7.56	0.0000	0	133828.5	13.3	152
6/7/2026	15:45:00	7.56	0.7673	0	133836.0	13	153
6/7/2026	16:00:00	7.56	0.9340	0	133854.0	12.8	154
6/7/2026	16:15:00	7.56	0.0000	0	133856.7	13.8	151
6/7/2026	16:30:00	7.55	1.1665	0	133874.1	12.9	153
6/7/2026	16:45:00	7.56	1.6354	0	133895.2	12.8	154
6/7/2026	17:00:00	7.56	1.2053	0	133918.1	13	153
6/7/2026	17:15:00	7.57	0.0000	0	133935.4	13.7	151
6/7/2026	17:30:00	7.55	0.2674	0	133936.0	14.1	153
6/7/2026	17:45:00	7.53	1.5579	2	133943.2	13.4	154
6/7/2026	18:00:00	7.55	1.7129	0	133967.1	12.9	155
6/7/2026	18:15:00	7.57	1.9571	0	133991.9	12.8	154
6/7/2026	18:30:00	7.57	1.0270	0	134017.1	12.8	154
6/7/2026	18:45:00	7.57	0.1860	0	134024.4	13.6	152
6/7/2026	19:00:00	7.55	0.2248	0	134027.8	14.1	153
6/7/2026	19:15:00	7.54	1.4106	0	134032.5	13.9	154
6/7/2026	19:30:00	7.53	0.9417	0	134053.9	13.3	151
6/7/2026	19:45:00	7.54	1.1161	9	134074.5	12.5	153
6/7/2026	20:00:00	7.56	0.0000	0	134081.0	12.8	153
6/7/2026	20:15:00	7.54	0.9301	2	134084.9	12.6	152
6/7/2026	20:30:00	7.56	1.8059	0	134107.4	13.3	151
6/7/2026	20:45:00	7.54	0.2597	0	134113.5	13.7	152
6/7/2026	21:00:00	7.52	0.3255	0	134116.9	14	152
6/7/2026	21:15:00	7.56	1.9300	0	134132.6	13.6	151
6/7/2026	21:30:00	7.55	1.8796	0	134161.1	13.6	151
6/7/2026	21:45:00	7.53	1.9416	0	134170.4	13.7	152
6/7/2026	22:00:00	7.51	1.9842	0	134200.8	13.8	153
6/7/2026	22:15:00	7.5	0.0000	0	134214.5	13.9	152
6/7/2026	22:30:00	7.49	0.0000	0	134214.5	15.3	152
6/7/2026	22:45:00	7.53	2.0036	0	134233.8	16.1	152
6/7/2026	23:00:00	7.51	1.7827	0	134262.0	16.6	152

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	23:15:00	7.54	1.3138	0	134281.0	13.8	150
6/7/2026	23:30:00	7.56	0.5929	0	134306.2	12.7	152
6/7/2026	23:45:00	7.54	0.7208	0	134307.5	13.3	153

5. In-Situ Readings

Table 4. In-Situ Readings

Date	Temperature (C°)	DO mg/L	SAL-ppt	pH	ORP (mV)	NTU
06/01/2026	13.4	9.89	0.09	7.19	164.7	1.44
06/02/2026	12.4	9.61	0.09	7.29	171.2	1.56
06/03/2026	12.8	10.39	0.09	7.36	174.4	1.21
06/04/2026	15.3	9.78	0.09	7.36	166.4	1.18
06/05/2026	12.1	10.29	0.08	7.36	168.5	1.20
06/06/2026	12.4	10.30	0.08	7.55	167.1	1.17
06/07/2026	13.3	10.33	0.08	7.46	165.2	1.61

6. Calibration Log:

Table 5. Calibration Log

Date	Unit	pH	Conductivity	Salinity	NTU
06/05/2026	YSI	✓	✓	✓	✓
06/05/2026	Portal WTP	✓	N/A	N/A	✓
06/01/2026	CP2 WTP	✓	N/A	N/A	✓
06/05/2026	CP2 WTP	✓	✓	N/A	✓

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

APPENDIX A: Portal WTP Data Log



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	0:00:00	6.9	1.4763	0.5	1,352,926	Open	14.1	269
6/1/2026	0:15:00	6.9	1.4650	0.7	1,352,948	Open	14.1	269
6/1/2026	0:30:00	6.9	1.4460	0.9	1,352,967	Open	14.1	269
6/1/2026	0:45:00	6.9	1.4687	1	1,352,989	Open	14.2	269
6/1/2026	1:00:00	6.9	1.4347	1.2	1,353,011	Open	14.2	271
6/1/2026	1:15:00	6.9	0.2196	1.5	1,353,025	Open	14.5	268
6/1/2026	1:30:00	6.9	0.0000	1.4	1,353,041	Closed	14.4	268
6/1/2026	1:45:00	6.9	1.5558	1.6	1,353,045	Open	14.2	268
6/1/2026	2:00:00	6.9	0.9577	1.6	1,353,065	Open	14.7	267
6/1/2026	2:15:00	6.9	1.4990	2.1	1,353,087	Open	14.1	268
6/1/2026	2:30:00	6.9	1.4990	2	1,353,109	Open	14.1	268
6/1/2026	2:45:00	6.9	1.5104	1.7	1,353,132	Open	14.2	268
6/1/2026	3:00:00	6.9	1.5028	1.1	1,353,146	Open	14.2	266
6/1/2026	3:15:00	6.9	1.5104	0.5	1,353,169	Open	14.3	266
6/1/2026	3:30:00	6.9	1.4990	0.7	1,353,191	Open	14.3	266
6/1/2026	3:45:00	6.9	1.5255	1.1	1,353,206	Open	14.3	266
6/1/2026	4:00:00	6.9	1.3968	1.6	1,353,226	Closed	14.2	266
6/1/2026	4:15:00	6.9	1.4763	2.1	1,353,241	Open	14.2	266
6/1/2026	4:30:00	6.9	0.8934	2.2	1,353,251	Open	14.5	266
6/1/2026	4:45:00	6.9	0.0000	2.5	1,353,265	Closed	14.4	266
6/1/2026	5:00:00	6.9	1.5217	2.3	1,353,284	Open	14.2	266
6/1/2026	5:15:00	6.9	1.4990	1.7	1,353,307	Open	14.1	264
6/1/2026	5:30:00	6.9	1.5028	1.3	1,353,317	Open	14.2	265
6/1/2026	5:45:00	6.9	1.4990	1.3	1,353,340	Open	14	263
6/1/2026	6:00:00	6.9	1.4612	0.8	1,353,362	Open	13.9	263
6/1/2026	6:15:00	6.9	1.4839	0.6	1,353,374	Open	14.5	264
6/1/2026	6:30:00	6.9	1.3741	0.6	1,353,381	Closed	13.9	264
6/1/2026	6:45:00	6.9	1.4687	0.5	1,353,400	Open	14	263
6/1/2026	7:00:00	6.9	0.0000	0.4	1,353,418	Closed	14.3	263
6/1/2026	7:15:00	6.9	1.4422	0.7	1,353,434	Open	13.9	263
6/1/2026	7:30:00	6.9	0.0000	0.9	1,353,453	Closed	13.9	263
6/1/2026	7:45:00	6.9	1.1281	0.9	1,353,466	Open	13.7	263



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	8:00:00	6.9	1.4347	0.9	1,353,477	Open	13.7	263
6/1/2026	8:15:00	6.9	1.3892	1.4	1,353,489	Closed	13.9	264
6/1/2026	8:30:00	6.9	1.3400	1.6	1,353,489	Closed	13.2	263
6/1/2026	8:45:00	6.9	0.8290	3.8	1,353,489	Closed	13.3	266
6/1/2026	9:00:00	6.8	0.2725	2	1,353,489	Closed	13.1	263
6/1/2026	9:15:00	6.9	1.4082	2	1,353,489	Closed	13.7	264
6/1/2026	9:30:00	6.8	0.0000	2.1	1,353,504	Closed	13.4	264
6/1/2026	9:45:00	6.8	1.4877	2.2	1,353,524	Open	13.3	264
6/1/2026	10:00:00	6.8	1.8056	1.8	1,353,534	Open	13.3	262
6/1/2026	10:15:00	6.9	1.0258	1.8	1,353,550	Open	13.6	261
6/1/2026	10:30:00	6.9	1.7489	1.9	1,353,564	Open	13.5	262
6/1/2026	10:45:00	6.9	0.0000	1.8	1,353,588	Closed	13.6	261
6/1/2026	11:00:00	6.8	1.7602	1.9	1,353,607	Open	13.7	262
6/1/2026	11:15:00	6.8	1.7451	2	1,353,617	Open	13.9	263
6/1/2026	11:30:00	6.8	0.0000	1.9	1,353,621	Closed	14.3	263
6/1/2026	11:45:00	6.8	0.0000	1.9	1,353,632	Closed	14.2	263
6/1/2026	12:00:00	6.8	0.0000	1.9	1,353,647	Closed	14.2	263
6/1/2026	12:15:00	6.8	0.0000	1.8	1,353,666	Closed	14.1	263
6/1/2026	12:30:00	6.8	0.0000	1.7	1,353,680	Closed	14.2	263
6/1/2026	12:45:00	6.8	1.1621	1.6	1,353,699	Open	14.2	263
6/1/2026	13:00:00	6.8	0.0000	1.8	1,353,716	Closed	14.3	263
6/1/2026	13:15:00	6.8	1.7602	1.7	1,353,740	Open	14.2	265
6/1/2026	13:30:00	6.8	0.0000	1.7	1,353,762	Closed	14.3	266
6/1/2026	13:45:00	6.8	0.0000	1.7	1,353,766	Closed	14.5	265
6/1/2026	14:00:00	6.8	1.7148	1.7	1,353,785	Open	14.3	264
6/1/2026	14:15:00	6.8	1.7224	1.3	1,353,811	Open	14.2	264
6/1/2026	14:30:00	6.8	0.0000	1.1	1,353,833	Closed	14.3	265
6/1/2026	14:45:00	6.7	1.7224	0.9	1,353,852	Open	14.2	264
6/1/2026	15:00:00	6.7	1.7034	0.9	1,353,878	Open	14.3	266
6/1/2026	15:15:00	6.7	1.1394	0.8	1,353,903	Open	14.3	266
6/1/2026	15:30:00	6.7	0.0000	0.8	1,353,910	Closed	14.8	266
6/1/2026	15:45:00	6.7	0.0000	0.8	1,353,920	Closed	14.6	267



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	16:00:00	6.7	1.7224	1	1,353,944	Open	14.2	267
6/1/2026	16:15:00	6.7	1.7186	1.1	1,353,961	Open	14.7	268
6/1/2026	16:30:00	6.7	1.7072	1	1,353,987	Open	14.3	268
6/1/2026	16:45:00	6.7	1.6845	0.7	1,354,012	Open	14.5	266
6/1/2026	17:00:00	6.7	1.0221	0.9	1,354,029	Closed	14.7	266
6/1/2026	17:15:00	6.7	1.7224	1.1	1,354,054	Open	14.3	267
6/1/2026	17:30:00	6.7	0.0000	1.1	1,354,075	Closed	14.3	267
6/1/2026	17:45:00	6.7	1.1281	1.1	1,354,097	Open	14.2	265
6/1/2026	18:00:00	6.7	1.7148	1.2	1,354,108	Open	14.2	266
6/1/2026	18:15:00	6.7	1.7186	1.3	1,354,122	Open	14.1	264
6/1/2026	18:30:00	6.7	0.0000	1.3	1,354,142	Closed	14.2	265
6/1/2026	18:45:00	6.7	0.0000	1.4	1,354,159	Closed	14	264
6/1/2026	19:00:00	6.7	1.6996	1.1	1,354,177	Open	14	265
6/1/2026	19:15:00	6.7	0.0000	1	1,354,197	Closed	14.1	265
6/1/2026	19:30:00	6.7	0.5300	1	1,354,216	Closed	14.2	264
6/1/2026	19:45:00	6.7	1.7261	0.9	1,354,233	Open	13.9	267
6/1/2026	20:00:00	6.7	0.0000	0.9	1,354,251	Closed	13.9	265
6/1/2026	20:15:00	6.7	1.1508	0.9	1,354,275	Open	13.7	265
6/1/2026	20:30:00	6.7	1.7110	1	1,354,292	Open	13.7	265
6/1/2026	20:45:00	6.7	1.6807	1	1,354,317	Open	13.6	266
6/1/2026	21:00:00	6.7	1.5520	1.1	1,354,321	Closed	13.6	267
6/1/2026	21:15:00	6.7	1.6315	1.4	1,354,334	Closed	13.9	266
6/1/2026	21:30:00	6.7	1.6996	2.2	1,354,359	Open	13.8	265
6/1/2026	21:45:00	6.7	1.6769	3	1,354,384	Open	13.8	265
6/1/2026	22:00:00	6.7	0.8139	3.4	1,354,405	Open	13.7	265
6/1/2026	22:15:00	6.7	1.5937	4.1	1,354,421	Open	13.7	265
6/1/2026	22:30:00	6.7	1.6012	4.1	1,354,445	Open	13.7	265
6/1/2026	22:45:00	6.7	1.0864	3.5	1,354,468	Open	13.6	265
6/1/2026	23:00:00	6.7	1.5899	3.8	1,354,484	Open	13.5	265
6/1/2026	23:15:00	6.8	0.0000	3.4	1,354,506	Closed	13.5	265
6/1/2026	23:30:00	6.8	1.5861	3.3	1,354,522	Open	13.4	265
6/1/2026	23:45:00	6.8	1.6012	3	1,354,537	Open	13.4	266



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	0:00:00	6.8	1.6088	2.8	1,354,561	Open	13.2	266
6/2/2026	0:15:00	6.8	1.6126	2.9	1,354,576	Open	13.2	264
6/2/2026	0:30:00	6.8	0.0000	2.9	1,354,595	Closed	13.2	264
6/2/2026	0:45:00	6.8	1.5974	4.1	1,354,614	Open	13.1	265
6/2/2026	1:00:00	6.9	0.0000	4.2	1,354,633	Closed	13.1	264
6/2/2026	1:15:00	6.9	1.0675	4.4	1,354,653	Open	13	264
6/2/2026	1:30:00	6.9	1.4801	4.3	1,354,664	Closed	13	264
6/2/2026	1:45:00	6.9	1.4763	4	1,354,664	Closed	13	263
6/2/2026	2:00:00	6.8	0.0000	8.9	1,354,664	Closed	13.6	259
6/2/2026	2:15:00	6.8	1.3287	3.6	1,354,675	Open	13.1	259
6/2/2026	2:30:00	6.8	0.0000	3.5	1,354,689	Closed	13.2	257
6/2/2026	2:45:00	6.9	1.6277	3.6	1,354,710	Open	13	258
6/2/2026	3:00:00	6.9	1.1281	3.3	1,354,721	Open	13.1	258
6/2/2026	3:15:00	6.9	1.6618	3.5	1,354,745	Open	13	258
6/2/2026	3:30:00	6.9	1.5937	3.1	1,354,759	Open	13	255
6/2/2026	3:45:00	6.9	1.0675	2.7	1,354,774	Open	13	255
6/2/2026	4:00:00	6.9	1.6050	2.5	1,354,795	Open	12.9	255
6/2/2026	4:15:00	6.9	0.0000	2.4	1,354,819	Closed	12.9	255
6/2/2026	4:30:00	6.9	1.6239	2.7	1,354,835	Open	12.9	255
6/2/2026	4:45:00	6.9	0.0000	2.6	1,354,844	Closed	13.2	255
6/2/2026	5:00:00	6.9	1.4687	4	1,354,850	Closed	12.9	255
6/2/2026	5:15:00	6.9	1.4839	5.9	1,354,850	Closed	12.9	258
6/2/2026	5:30:00	6.9	0.8896	6.4	1,354,850	Closed	12.9	258
6/2/2026	5:45:00	6.9	0.7722	234.3	1,354,850	Closed	12.9	258
6/2/2026	6:00:00	6.9	1.5520	10.8	1,354,850	Closed	12.9	257
6/2/2026	6:15:00	6.9	0.0000	10.1	1,354,863	Closed	12.9	256
6/2/2026	6:30:00	6.9	0.0000	9.1	1,354,883	Closed	12.8	255
6/2/2026	6:45:00	6.9	1.5672	9.3	1,354,898	Open	12.8	253
6/2/2026	7:00:00	6.9	1.7526	8.4	1,354,912	Open	12.9	253
6/2/2026	7:15:00	6.9	1.7034	7.5	1,354,938	Open	12.7	255
6/2/2026	7:30:00	6.8	1.7451	6.4	1,354,956	Open	12.8	255
6/2/2026	7:45:00	6.8	1.7299	5.2	1,354,981	Open	12.7	255



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	8:00:00	6.8	1.7526	4.4	1,354,998	Open	12.7	255
6/2/2026	8:15:00	6.8	1.1621	3.4	1,355,022	Open	12.8	255
6/2/2026	8:30:00	6.8	1.7337	2.7	1,355,039	Open	12.7	256
6/2/2026	8:45:00	6.7	1.6580	2.8	1,355,049	Closed	12.9	256
6/2/2026	9:00:00	6.7	1.6959	2	1,355,069	Open	12.8	259
6/2/2026	9:15:00	6.7	1.7337	1.7	1,355,085	Open	12.9	258
6/2/2026	9:30:00	6.7	1.7261	1.4	1,355,111	Open	13	258
6/2/2026	9:45:00	6.7	1.7299	1.3	1,355,126	Open	13.5	258
6/2/2026	10:00:00	6.7	1.7299	1.2	1,355,152	Open	13.2	258
6/2/2026	10:15:00	6.7	1.6883	1.1	1,355,178	Open	13.3	258
6/2/2026	10:30:00	6.7	1.1697	1	1,355,192	Open	13.5	259
6/2/2026	10:45:00	6.7	1.7034	1	1,355,207	Open	13.5	259
6/2/2026	11:00:00	6.7	1.6921	1	1,355,233	Open	13.5	258
6/2/2026	11:15:00	6.7	1.7110	1	1,355,240	Open	13.8	258
6/2/2026	11:30:00	6.7	1.7299	1	1,355,262	Open	13.7	258
6/2/2026	11:45:00	6.8	1.6996	0.9	1,355,287	Open	13.9	258
6/2/2026	12:00:00	6.8	0.0000	0.8	1,355,305	Closed	14.2	261
6/2/2026	12:15:00	6.8	1.7072	0.9	1,355,326	Open	14.2	262
6/2/2026	12:30:00	6.8	1.7072	0.7	1,355,352	Open	14.1	259
6/2/2026	12:45:00	6.8	1.5974	0.8	1,355,367	Open	14.2	259
6/2/2026	13:00:00	6.8	1.0864	0.8	1,355,389	Open	14.3	260
6/2/2026	13:15:00	6.8	1.6202	0.9	1,355,404	Open	14.2	259
6/2/2026	13:30:00	6.8	1.5937	1	1,355,428	Open	14.2	260
6/2/2026	13:45:00	6.9	0.0000	1	1,355,450	Closed	14.2	260
6/2/2026	14:00:00	6.9	1.5899	1	1,355,467	Open	14.2	260
6/2/2026	14:15:00	6.9	0.0000	0.8	1,355,479	Closed	14.4	257
6/2/2026	14:30:00	6.9	0.0000	1	1,355,499	Closed	14.9	258
6/2/2026	14:45:00	6.9	1.6012	1	1,355,515	Open	14.5	260
6/2/2026	15:00:00	6.9	1.5937	0.9	1,355,531	Open	14.4	256
6/2/2026	15:15:00	6.9	1.5823	0.9	1,355,554	Open	14.4	256
6/2/2026	15:30:00	6.9	0.0000	0.9	1,355,573	Closed	14.5	258
6/2/2026	15:45:00	6.9	0.0000	1	1,355,592	Closed	14.4	257



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	16:00:00	6.9	1.5861	0.9	1,355,604	Open	14.5	257
6/2/2026	16:15:00	6.9	1.5974	0.8	1,355,628	Open	14.6	258
6/2/2026	16:30:00	6.9	1.5823	0.9	1,355,648	Open	14.6	257
6/2/2026	16:45:00	6.9	1.6277	0.6	1,355,673	Open	14.8	257
6/2/2026	17:00:00	6.9	1.6202	0.6	1,355,697	Open	14.9	257
6/2/2026	17:15:00	6.9	1.5331	0.7	1,355,712	Open	15.1	257
6/2/2026	17:30:00	6.9	1.5937	0.6	1,355,735	Open	14.8	257
6/2/2026	17:45:00	6.9	1.5937	0.6	1,355,759	Open	14.8	257
6/2/2026	18:00:00	6.9	1.3968	0.6	1,355,780	Open	14.7	257
6/2/2026	18:15:00	6.9	1.5407	0.7	1,355,796	Closed	14.7	257
6/2/2026	18:30:00	6.9	1.5974	0.6	1,355,820	Open	14.4	257
6/2/2026	18:45:00	6.9	0.0000	0.7	1,355,841	Closed	14.4	255
6/2/2026	19:00:00	6.9	1.6164	0.8	1,355,859	Open	14.2	255
6/2/2026	19:15:00	6.9	1.5861	0.8	1,355,875	Open	14.2	253
6/2/2026	19:30:00	6.9	1.6012	0.9	1,355,899	Open	14	253
6/2/2026	19:45:00	6.9	1.6088	1.1	1,355,913	Open	14	255
6/2/2026	20:00:00	6.9	1.5861	0.9	1,355,937	Open	13.8	255
6/2/2026	20:15:00	6.9	1.5823	0.9	1,355,961	Open	13.7	253
6/2/2026	20:30:00	6.9	1.1810	1	1,355,974	Open	13.8	253
6/2/2026	20:45:00	6.9	1.6088	1	1,355,990	Open	13.8	253
6/2/2026	21:00:00	6.9	1.5861	1	1,356,014	Open	13.7	253
6/2/2026	21:15:00	6.9	1.5407	1	1,356,029	Closed	13.9	253
6/2/2026	21:30:00	6.9	1.6050	1	1,356,049	Open	13.7	253
6/2/2026	21:45:00	6.9	1.5937	1	1,356,065	Open	13.5	255
6/2/2026	22:00:00	6.9	0.0000	1.1	1,356,076	Closed	13.7	253
6/2/2026	22:15:00	6.9	1.5369	1.3	1,356,085	Closed	13.6	252
6/2/2026	22:30:00	6.9	0.0000	1.2	1,356,104	Closed	13.3	252
6/2/2026	22:45:00	6.9	1.5823	1.3	1,356,122	Open	13.1	253
6/2/2026	23:00:00	6.9	1.0448	1.6	1,356,132	Open	13.1	252
6/2/2026	23:15:00	6.9	1.6202	1.4	1,356,145	Open	13	252
6/2/2026	23:30:00	6.9	1.6315	1.4	1,356,159	Open	13.1	252
6/2/2026	23:45:00	6.9	1.6126	1.3	1,356,184	Open	13	253



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	0:00:00	6.9	1.5937	1.4	1,356,198	Open	13.1	253
6/3/2026	0:15:00	6.9	1.5974	1.4	1,356,222	Open	13.2	253
6/3/2026	0:30:00	6.9	1.5899	1.4	1,356,246	Open	13.2	252
6/3/2026	0:45:00	6.9	1.5937	1.3	1,356,261	Open	13.3	252
6/3/2026	1:00:00	6.9	1.5861	1.4	1,356,285	Open	13.1	252
6/3/2026	1:15:00	6.9	1.5709	1.2	1,356,309	Open	13.1	252
6/3/2026	1:30:00	6.9	1.0561	1.2	1,356,323	Open	13.1	253
6/3/2026	1:45:00	6.9	1.5899	1.2	1,356,346	Open	13	253
6/3/2026	2:00:00	6.9	1.6050	1.3	1,356,362	Open	13	253
6/3/2026	2:15:00	6.9	1.3173	1.2	1,356,376	Open	13.1	253
6/3/2026	2:30:00	6.9	0.0000	1.3	1,356,392	Closed	13	253
6/3/2026	2:45:00	6.9	1.5899	1.2	1,356,413	Open	12.9	255
6/3/2026	3:00:00	6.9	0.0000	1.2	1,356,430	Closed	12.9	255
6/3/2026	3:15:00	6.9	1.4650	1.2	1,356,443	Closed	12.8	255
6/3/2026	3:30:00	6.9	0.0000	1.2	1,356,443	Closed	12.8	252
6/3/2026	3:45:00	6.9	1.6277	1.3	1,356,463	Open	12.7	252
6/3/2026	4:00:00	6.9	0.0000	1.2	1,356,482	Closed	12.9	252
6/3/2026	4:15:00	6.9	1.6088	1.7	1,356,502	Open	12.9	252
6/3/2026	4:30:00	6.9	1.5785	2.1	1,356,516	Open	13.2	255
6/3/2026	4:45:00	6.8	1.0486	2.6	1,356,540	Open	13.1	255
6/3/2026	5:00:00	6.9	0.0000	2.4	1,356,551	Closed	13.2	253
6/3/2026	5:15:00	6.8	1.5747	2.1	1,356,566	Open	13.2	253
6/3/2026	5:30:00	7	1.4839	5.1	1,356,574	Open	15.2	500
6/3/2026	5:45:00	7.4	1.5217	3.7	1,356,587	Open	13.7	632
6/3/2026	6:00:00	7.7	1.5028	3.5	1,356,609	Open	13.3	699
6/3/2026	6:15:00	7.7	0.0000	4	1,356,631	Closed	13.3	725
6/3/2026	6:30:00	7.4	1.0221	1	1,356,640	Open	13.6	668
6/3/2026	6:45:00	7.5	1.4385	1.5	1,356,655	Open	13.5	653
6/3/2026	7:00:00	7.6	1.5369	1	1,356,678	Open	13.3	630
6/3/2026	7:15:00	7.5	0.0000	1.1	1,356,696	Closed	13.3	615
6/3/2026	7:30:00	7.5	1.5217	0.9	1,356,714	Open	13.2	591
6/3/2026	7:45:00	7.5	1.5255	1	1,356,729	Open	13.3	574



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	8:00:00	7.5	1.5028	0.8	1,356,752	Open	13.3	561
6/3/2026	8:15:00	7.4	1.5142	1	1,356,764	Open	13.4	549
6/3/2026	8:30:00	7.5	0.0000	1	1,356,784	Closed	13.4	537
6/3/2026	8:45:00	7.5	1.5255	0.9	1,356,803	Open	13.3	530
6/3/2026	9:00:00	7.4	1.0296	1	1,356,806	Open	13.8	525
6/3/2026	9:15:00	7.4	0.0000	1	1,356,825	Closed	13.3	513
6/3/2026	9:30:00	7.4	1.5407	1	1,356,843	Open	13.3	510
6/3/2026	9:45:00	7.4	1.0145	1	1,356,857	Open	13.3	500
6/3/2026	10:00:00	7.4	1.5066	1.1	1,356,869	Open	13.5	464
6/3/2026	10:15:00	7.4	1.5142	0.9	1,356,892	Open	13.3	461
6/3/2026	10:30:00	7	0.1438	1.1	1,356,904	Open	13.3	453
6/3/2026	10:45:00	7.4	1.5142	1.4	1,356,914	Closed	13.3	446
6/3/2026	11:00:00	7.3	1.6845	1.2	1,356,933	Open	13.4	445
6/3/2026	11:15:00	7.3	1.6845	1.2	1,356,958	Open	13.6	438
6/3/2026	11:30:00	7.3	1.1167	1.2	1,356,974	Open	13.7	433
6/3/2026	11:45:00	7.3	1.6353	1.2	1,356,998	Open	13.5	431
6/3/2026	12:00:00	7.3	1.6202	1	1,357,023	Open	13.6	425
6/3/2026	12:15:00	7.3	1.1318	0.7	1,357,039	Open	13.9	423
6/3/2026	12:30:00	7.3	1.7072	0.7	1,357,056	Open	13.9	415
6/3/2026	12:45:00	7.2	1.5293	0.7	1,357,072	Closed	14.2	412
6/3/2026	13:00:00	7.2	0.0000	0.6	1,357,088	Closed	14.3	409
6/3/2026	13:15:00	7.2	1.6391	0.5	1,357,099	Open	15.1	405
6/3/2026	13:30:00	7.2	1.6845	0.5	1,357,124	Open	14.7	399
6/3/2026	13:45:00	7.2	1.6732	0.5	1,357,132	Open	14.4	392
6/3/2026	14:15:00	7.3	1.6126	0.3	1,357,173	Open	14.3	385
6/3/2026	14:30:00	7.2	1.6277	0.2	1,357,189	Open	14.5	382
6/3/2026	14:45:00	7.3	1.1281	0.1	1,357,213	Open	14.5	379
6/3/2026	15:00:00	7.2	1.6618	0.1	1,357,229	Open	14.7	374
6/3/2026	15:15:00	7.2	0.0000	0	1,357,246	Closed	14.9	376
6/3/2026	15:30:00	7.2	1.4195	0	1,357,270	Closed	14.8	373
6/3/2026	15:45:00	7.2	1.6164	0	1,357,277	Open	14.7	368
6/3/2026	16:00:00	7.1	0.0000	0.1	1,357,280	Closed	15.4	364



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	16:15:00	7	1.5709	0.1	1,357,291	Open	14.6	359
6/3/2026	16:30:00	7.1	1.1053	0.2	1,357,304	Open	15.1	361
6/3/2026	16:45:00	7.2	1.6353	0	1,357,319	Open	15	358
6/3/2026	17:00:00	7.2	1.6353	0.1	1,357,344	Open	14.8	355
6/3/2026	17:15:00	7.3	1.0978	0.2	1,357,360	Open	14.6	351
6/3/2026	17:30:00	7.2	1.5974	0.3	1,357,381	Open	14.4	343
6/3/2026	17:45:00	7.2	1.6164	0.3	1,357,393	Open	14.3	338
6/3/2026	18:00:00	7.2	1.6239	0.1	1,357,417	Open	14.6	338
6/3/2026	18:15:00	7.1	1.5066	0.2	1,357,427	Closed	15.2	338
6/3/2026	18:30:00	7.2	1.6202	0.1	1,357,451	Open	14.6	332
6/3/2026	18:45:00	7.2	1.5937	0.4	1,357,465	Open	14.4	335
6/3/2026	19:00:00	7.2	1.0637	0.6	1,357,477	Open	14.7	333
6/3/2026	19:15:00	7.3	0.0000	0.8	1,357,497	Closed	14.1	330
6/3/2026	19:30:00	7.2	1.5785	1	1,357,515	Open	13.9	333
6/3/2026	19:45:00	7.2	1.0258	1.1	1,357,528	Open	13.7	330
6/3/2026	20:00:00	7.2	1.5823	1.2	1,357,544	Open	13.5	328
6/3/2026	20:30:00	7.2	1.6126	1.2	1,357,582	Open	13.5	327
6/3/2026	20:45:00	7.2	1.6202	1.2	1,357,596	Open	13.5	327
6/3/2026	21:00:00	7.3	0.0000	1.2	1,357,612	Closed	13.4	323
6/3/2026	21:15:00	7.2	1.5558	1.3	1,357,626	Open	13.1	323
6/3/2026	21:30:00	7.2	1.0902	1.4	1,357,639	Open	13.4	324
6/3/2026	21:45:00	7.1	1.5785	1.4	1,357,654	Open	13.2	324
6/3/2026	22:00:00	7.2	1.5596	1.5	1,357,678	Open	12.9	324
6/3/2026	22:15:00	7.2	1.0410	1.5	1,357,692	Open	13	322
6/3/2026	22:30:00	7.1	1.6012	1.5	1,357,705	Open	13.2	322
6/3/2026	22:45:00	7.1	1.6050	1.4	1,357,729	Open	13.2	322
6/3/2026	23:00:00	7.1	1.6012	1.3	1,357,744	Open	13.1	318
6/3/2026	23:15:00	7.1	1.5785	1.5	1,357,757	Open	13.1	320
6/3/2026	23:30:00	7.2	0.0000	1.4	1,357,774	Closed	13	319
6/3/2026	23:45:00	7.2	0.0000	1.2	1,357,788	Closed	13	315
6/4/2026	0:00:00	7.1	1.0486	1.3	1,357,795	Open	13.5	315
6/4/2026	0:15:00	7.1	1.6088	1.1	1,357,809	Open	13.3	315



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	0:30:00	7.1	1.4952	0.9	1,357,823	Closed	13.6	314
6/4/2026	0:45:00	7.2	0.0000	0.9	1,357,844	Closed	13.4	312
6/4/2026	1:00:00	7.1	1.5785	0.8	1,357,859	Open	13.3	309
6/4/2026	1:15:00	7.1	1.5634	0.9	1,357,873	Open	13.3	309
6/4/2026	1:30:00	7.1	0.0000	0.8	1,357,893	Closed	13.3	307
6/4/2026	1:45:00	7.1	1.5974	0.8	1,357,909	Open	13.5	305
6/4/2026	2:00:00	7	1.5974	0.8	1,357,933	Open	13.6	305
6/4/2026	2:15:00	7	1.5937	0.8	1,357,946	Open	13.6	304
6/4/2026	2:30:00	7	0.0000	0.8	1,357,951	Closed	13.7	300
6/4/2026	2:45:00	7.1	0.0000	0.8	1,357,962	Closed	13.6	299
6/4/2026	3:00:00	7.1	0.1098	0.6	1,357,982	Closed	13.5	300
6/4/2026	3:15:00	7.1	1.0221	0.7	1,357,995	Open	13.5	300
6/4/2026	3:30:00	7.1	1.5672	0.6	1,358,010	Open	13.6	297
6/4/2026	3:45:00	7.1	0.0000	0.7	1,358,025	Closed	13.6	296
6/4/2026	4:00:00	7.1	1.5596	0.7	1,358,047	Open	13.4	294
6/4/2026	4:15:00	7	1.5974	0.7	1,358,062	Open	13.6	293
6/4/2026	4:30:00	7	1.5634	0.7	1,358,086	Open	13.6	291
6/4/2026	4:45:00	7	1.5785	0.8	1,358,101	Open	13.7	291
6/4/2026	5:00:00	6.9	0.0000	0.9	1,358,111	Closed	13.9	291
6/4/2026	5:15:00	7.1	0.0000	0.7	1,358,125	Closed	13.8	289
6/4/2026	5:30:00	7	1.5104	0.7	1,358,145	Open	13.6	289
6/4/2026	5:45:00	7.1	0.9766	0.7	1,358,167	Open	13.6	288
6/4/2026	6:00:00	7	1.5634	0.8	1,358,180	Open	13.6	289
6/4/2026	6:15:00	7	1.5634	0.8	1,358,195	Open	13.7	286
6/4/2026	6:30:00	7.1	0.0000	0.8	1,358,213	Closed	13.5	286
6/4/2026	6:45:00	7.1	0.0000	0.8	1,358,226	Closed	13.4	286
6/4/2026	7:00:00	7	1.5596	0.7	1,358,245	Open	13.3	286
6/4/2026	7:15:00	7	1.4347	0.9	1,358,251	Closed	13.4	284
6/4/2026	7:30:00	7.1	0.0000	0.9	1,358,251	Closed	13.2	284
6/4/2026	7:45:00	7	1.5747	0.7	1,358,255	Open	13.3	284
6/4/2026	8:00:00	7	1.5747	0.8	1,358,269	Open	13.7	284
6/4/2026	8:15:00	7.1	0.0000	0.7	1,358,287	Closed	13.4	279



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	8:30:00	7	1.5331	0.8	1,358,305	Open	13.4	279
6/4/2026	8:45:00	7	1.5596	0.9	1,358,321	Open	13.6	279
6/4/2026	9:00:00	7	1.5369	0.8	1,358,343	Open	13.4	279
6/4/2026	9:15:00	7	1.5823	0.8	1,358,356	Open	14	279
6/4/2026	9:30:00	7	1.8624	0.9	1,358,366	Open	14.1	279
6/4/2026	9:45:00	7	1.5255	0.8	1,358,389	Open	13.7	279
6/4/2026	10:00:00	7	1.2113	0.8	1,358,409	Open	14.3	278
6/4/2026	10:15:00	7	1.5709	0.7	1,358,432	Open	14.2	275
6/4/2026	10:30:00	6.9	1.5747	0.7	1,358,456	Open	14.5	275
6/4/2026	10:45:00	7	1.0599	0.7	1,358,479	Open	14.7	273
6/4/2026	11:00:00	7	0.0000	0.9	1,358,497	Open	14.3	274
6/4/2026	11:15:00	7.1	1.5444	0.8	1,358,498	Open	14.4	270
6/4/2026	11:30:00	7	1.6391	0.7	1,358,523	Open	14.9	271
6/4/2026	11:45:00	6.9	1.6656	0.6	1,358,545	Open	15.7	271
6/4/2026	12:00:00	6.9	1.6542	0.7	1,358,569	Open	15.6	271
6/4/2026	12:15:00	7	1.6088	0.5	1,358,594	Open	14.9	269
6/4/2026	12:30:00	7	1.5861	0.3	1,358,606	Open	15.6	269
6/4/2026	12:45:00	7	1.6353	0.4	1,358,621	Open	15	269
6/4/2026	13:00:00	7	1.6050	0.3	1,358,645	Open	14.9	269
6/4/2026	13:15:00	7	0.7041	0.3	1,358,668	Open	15.2	269
6/4/2026	13:30:00	7	1.5596	0.6	1,358,689	Open	14.7	268
6/4/2026	13:45:00	7	1.5520	0.5	1,358,712	Open	14.7	268
6/4/2026	14:00:00	7	1.5634	0.5	1,358,735	Open	14.7	268
6/4/2026	14:15:00	7	1.5255	0.6	1,358,755	Open	14.8	266
6/4/2026	14:30:00	7.1	0.0000	0.7	1,358,764	Closed	14.9	266
6/4/2026	14:45:00	7	0.4694	0.8	1,358,779	Closed	14.9	266
6/4/2026	15:00:00	7	1.4498	0.8	1,358,782	Closed	14.9	268
6/4/2026	15:15:00	7	1.5369	0.7	1,358,795	Open	14.8	268
6/4/2026	15:30:00	7	1.5482	0.7	1,358,819	Open	14.8	268
6/4/2026	15:45:00	7.1	1.0372	0.8	1,358,841	Open	14.8	265
6/4/2026	16:00:00	7	1.5709	0.7	1,358,863	Open	14.8	265
6/4/2026	16:15:00	7	1.5558	0.7	1,358,886	Open	14.7	265



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	16:30:00	7	1.5558	0.7	1,358,909	Open	14.7	265
6/4/2026	16:45:00	7	1.4536	0.8	1,358,915	Closed	14.6	265
6/4/2026	17:00:00	7	1.6239	0.9	1,358,916	Open	14.6	265
6/4/2026	17:15:00	7	1.5974	0.8	1,358,940	Open	14.7	265
6/4/2026	17:30:00	6.9	1.6126	0.9	1,358,961	Open	15.1	265
6/4/2026	17:45:00	7.1	0.0000	0.9	1,358,982	Closed	14.8	265
6/4/2026	18:00:00	7	1.5482	0.9	1,358,995	Open	14.7	265
6/4/2026	18:15:00	7	1.0713	1	1,359,009	Open	14.7	264
6/4/2026	18:30:00	7	1.5937	1.2	1,359,021	Open	14.7	263
6/4/2026	18:45:00	7	1.5899	1	1,359,045	Open	14.3	263
6/4/2026	19:00:00	7	1.5634	1.2	1,359,060	Open	14.2	263
6/4/2026	19:15:00	7	0.0000	1	1,359,074	Closed	14.1	264
6/4/2026	19:30:00	7	1.5823	1	1,359,095	Open	13.8	261
6/4/2026	19:45:00	7	0.0000	1.1	1,359,111	Closed	13.8	261
6/4/2026	20:00:00	7	0.0000	1.1	1,359,126	Closed	13.9	263
6/4/2026	20:15:00	7	1.5974	1.1	1,359,146	Open	13.5	261
6/4/2026	20:30:00	7	1.5520	1.2	1,359,169	Open	13.3	261
6/4/2026	20:45:00	7	1.0031	1.3	1,359,183	Open	13.3	261
6/4/2026	21:00:00	7	0.0000	1.1	1,359,200	Closed	13.3	261
6/4/2026	21:15:00	7	1.5444	1.3	1,359,218	Open	13.2	259
6/4/2026	21:30:00	7	1.5482	1.4	1,359,242	Open	13.1	259
6/4/2026	21:45:00	7	1.5823	1.4	1,359,256	Open	13.1	261
6/4/2026	22:00:00	7	1.5823	1.6	1,359,271	Open	13.3	260
6/4/2026	22:15:00	7	1.5217	1.4	1,359,294	Open	13	260
6/4/2026	22:30:00	7	1.5747	1.4	1,359,304	Open	13.4	260
6/4/2026	22:45:00	7	0.0000	1.2	1,359,325	Closed	13.2	260
6/4/2026	23:00:00	7	1.5558	1.2	1,359,343	Open	13.2	260
6/4/2026	23:15:00	7	0.0000	0.7	1,359,363	Closed	13.4	259
6/4/2026	23:30:00	7	1.5482	0.7	1,359,380	Open	13.3	260
6/4/2026	23:45:00	7	0.0000	0.5	1,359,401	Closed	13.4	259
6/5/2026	0:00:00	7	1.5066	0.3	1,359,418	Open	13.6	259
6/5/2026	0:15:00	6.9	1.5293	0.7	1,359,431	Open	13.9	259



FRONTIER-KEMPER
MICHELS® joint venture

Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	0:30:00	7	1.5747	0.3	1,359,454	Open	13.7	259
6/5/2026	0:45:00	7	1.5596	0.1	1,359,478	Open	13.9	259
6/5/2026	1:00:00	6.9	0.0000	0.3	1,359,485	Closed	14.2	258
6/5/2026	1:15:00	6.8	0.0000	0.2	1,359,485	Closed	14.8	258
6/5/2026	1:30:00	6.9	1.4233	0	1,359,486	Closed	14	256
6/5/2026	1:45:00	7	1.0221	0.3	1,359,503	Open	14.6	256
6/5/2026	2:00:00	6.9	1.6012	0.5	1,359,513	Open	14.5	258
6/5/2026	2:15:00	7	1.5672	0	1,359,537	Open	14	256
6/5/2026	2:30:00	7	1.5179	0	1,359,561	Open	14	255
6/5/2026	2:45:00	7	1.5369	0	1,359,580	Open	14.1	254
6/5/2026	3:00:00	7	1.5482	0	1,359,603	Open	14.3	253
6/5/2026	3:15:00	6.9	1.5520	0	1,359,626	Open	14.4	252
6/5/2026	3:30:00	6.9	1.4422	0	1,359,642	Closed	14.3	253
6/5/2026	3:45:00	7	1.5861	0	1,359,646	Open	14.4	254
6/5/2026	4:00:00	6.9	1.5331	0	1,359,669	Open	14.2	252
6/5/2026	4:15:00	6.9	1.5142	0.3	1,359,679	Closed	14.5	255
6/5/2026	4:30:00	6.9	1.5785	1.8	1,359,703	Open	13.8	251
6/5/2026	4:45:00	6.9	1.5709	0.1	1,359,727	Open	13.8	251
6/5/2026	5:00:00	7	1.5520	0.3	1,359,747	Open	13.6	251
6/5/2026	5:15:00	7	1.5823	0.5	1,359,770	Open	13.5	250
6/5/2026	5:30:00	7	1.5785	0.4	1,359,794	Open	13.7	251
6/5/2026	5:45:00	7	1.5785	0.5	1,359,815	Open	13.6	251
6/5/2026	6:00:00	7	1.5369	0.5	1,359,839	Open	13.5	250
6/5/2026	6:15:00	7	1.6012	0.5	1,359,862	Open	13.5	250
6/5/2026	6:30:00	7	1.6202	0.3	1,359,884	Open	13.4	251
6/5/2026	6:45:00	7	1.6126	0	1,359,908	Open	13.8	247
6/5/2026	7:00:00	7	0.6927	0.3	1,359,918	Closed	14.3	249
6/5/2026	7:15:00	7	1.6429	0.5	1,359,939	Open	13.6	250
6/5/2026	7:30:00	7	0.0000	0.1	1,359,956	Closed	13.8	247
6/5/2026	7:45:00	7	1.5937	0	1,359,973	Open	13.7	247
6/5/2026	8:00:00	7	0.0000	1.6	1,359,994	Closed	13.5	245
6/5/2026	8:15:00	7	1.4952	0.6	1,359,994	Closed	13.2	246



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	8:30:00	7	1.6467	0.4	1,360,009	Open	13.3	251
6/5/2026	8:45:00	7	1.6126	0.3	1,360,021	Open	13.3	248
6/5/2026	9:00:00	7	1.6277	0.5	1,360,045	Open	13.2	246
6/5/2026	9:15:00	7.1	1.6202	0	1,360,069	Open	13.3	246
6/5/2026	9:30:00	7	0.0000	0	1,360,080	Closed	14.6	246
6/5/2026	9:45:00	7	1.6353	0	1,360,101	Open	13.9	242
6/5/2026	10:00:00	7	1.5709	0.3	1,360,126	Open	13.8	245
6/5/2026	10:15:00	6.9	0.0000	0.4	1,360,131	Closed	14.3	246
6/5/2026	10:30:00	7	1.6126	0.5	1,360,155	Open	13.8	246
6/5/2026	10:45:00	7	1.6012	0.6	1,360,179	Open	13.7	246
6/5/2026	11:00:00	7.2	0.0000	2.3	1,360,184	Open	13.8	246
6/5/2026	11:15:00	7.1	1.6467	1.6	1,360,195	Open	13.6	247
6/5/2026	11:30:00	7.1	1.6315	1.4	1,360,220	Open	13.6	246
6/5/2026	11:45:00	7.1	1.6088	1.3	1,360,241	Open	13.7	112
6/5/2026	12:00:00	7.1	1.5104	1.2	1,360,243	Closed	13.7	246
6/5/2026	12:15:00	7.1	1.5823	1.3	1,360,266	Open	13.9	243
6/5/2026	12:30:00	7.1	1.6126	1.3	1,360,275	Open	14.1	246
6/5/2026	12:45:00	7.1	1.6504	1.4	1,360,299	Open	14	243
6/5/2026	13:00:00	7.1	1.6429	1.6	1,360,308	Open	15.1	245
6/5/2026	13:15:00	7.1	1.6315	0.4	1,360,330	Open	13.9	245
6/5/2026	13:30:00	7.1	0.4013	0.9	1,360,354	Closed	13.8	112
6/5/2026	13:45:00	7	1.6126	0.8	1,360,357	Open	14.6	245
6/5/2026	14:00:00	7.1	1.6164	0.2	1,360,378	Open	13.7	112
6/5/2026	14:15:00	7.1	1.6126	0.3	1,360,402	Open	13.8	243
6/5/2026	14:30:00	7	0.0000	0.1	1,360,415	Closed	14.7	243
6/5/2026	14:45:00	7	1.6315	0	1,360,423	Open	14	243
6/5/2026	15:00:00	7.1	1.6088	0	1,360,448	Open	14	243
6/5/2026	15:15:00	7.1	1.5747	0	1,360,471	Open	14.1	242
6/5/2026	15:30:00	7.1	0.0000	0	1,360,490	Closed	14.1	112
6/5/2026	15:45:00	7	1.6012	0.2	1,360,503	Open	13.9	112
6/5/2026	16:00:00	7.1	1.6164	0.3	1,360,527	Open	13.7	111
6/5/2026	16:15:00	7	1.6088	0.5	1,360,535	Open	13.8	112



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	16:30:00	7.1	1.5899	0.3	1,360,559	Open	13.7	111
6/5/2026	16:45:00	7	1.6050	0.4	1,360,568	Open	14	112
6/5/2026	17:00:00	7.1	1.5974	0.1	1,360,590	Open	13.8	113
6/5/2026	17:15:00	7	1.6126	0.3	1,360,600	Open	14.2	243
6/5/2026	17:30:00	7.1	1.5899	0	1,360,624	Open	14	113
6/5/2026	17:45:00	7.1	1.6126	0.1	1,360,633	Open	14.9	243
6/5/2026	18:00:00	7.1	1.6164	0.2	1,360,657	Open	14	112
6/5/2026	18:15:00	7	0.0000	0.2	1,360,674	Closed	14.2	112
6/5/2026	18:30:00	7.1	1.6050	0.3	1,360,689	Open	13.8	112
6/5/2026	18:45:00	7.1	1.5672	0.3	1,360,713	Open	13.7	111
6/5/2026	19:00:00	7	1.6391	0.3	1,360,721	Open	13.9	111
6/5/2026	19:15:00	7	0.0000	0.1	1,360,732	Closed	14.1	112
6/5/2026	19:30:00	7.2	0.3445	3	1,360,739	Open	13.5	112
6/5/2026	19:45:00	7.2	1.8738	4.6	1,360,754	Open	13.5	112
6/5/2026	20:00:00	7.1	0.0000	1.3	1,360,765	Closed	13.6	112
6/5/2026	20:15:00	7.1	1.6959	2.2	1,360,787	Open	13.5	112
6/5/2026	20:30:00	7.1	0.0000	1	1,360,808	Closed	13.5	112
6/5/2026	20:45:00	7.1	1.6618	2.4	1,360,823	Open	13.4	111
6/5/2026	21:00:00	7.1	1.6769	2.4	1,360,848	Open	13.3	112
6/5/2026	21:15:00	7.1	1.6921	2.6	1,360,858	Open	13.4	111
6/5/2026	21:30:00	7.1	1.6580	2.3	1,360,881	Open	13.3	111
6/5/2026	21:45:00	7	0.0000	2.1	1,360,889	Closed	13.9	112
6/5/2026	22:00:00	7.1	1.6618	3	1,360,910	Open	13.5	112
6/5/2026	22:15:00	7.1	1.7072	2.9	1,360,920	Open	14.5	113
6/5/2026	22:30:00	7.1	1.6694	2.3	1,360,945	Open	13.6	113
6/5/2026	22:45:00	7.1	1.6732	2.7	1,360,970	Open	13.7	113
6/5/2026	23:00:00	7.1	1.6202	2.8	1,360,990	Open	13.6	113
6/5/2026	23:15:00	7.1	1.6012	3.4	1,361,014	Open	13.6	113
6/5/2026	23:30:00	7.1	1.5899	3.6	1,361,038	Open	13.7	111
6/5/2026	23:45:00	7	1.6202	8.4	1,361,060	Open	13.6	111
6/6/2026	0:00:00	7.1	1.6126	4.5	1,361,084	Open	13.7	113
6/6/2026	0:15:00	7.1	0.0000	3.1	1,361,105	Closed	13.7	113



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	0:30:00	7	1.4536	2.7	1,361,105	Closed	13.8	114
6/6/2026	0:45:00	7	1.5596	2.3	1,361,125	Open	13.8	113
6/6/2026	1:00:00	7	1.5747	2.7	1,361,133	Open	14.4	243
6/6/2026	1:15:00	7.1	1.0864	3.1	1,361,155	Open	13.9	113
6/6/2026	1:30:00	7	1.5974	5.2	1,361,178	Open	13.7	113
6/6/2026	1:45:00	7	0.0000	3.4	1,361,198	Closed	13.8	113
6/6/2026	2:00:00	7	1.7072	3.2	1,361,215	Open	13.5	112
6/6/2026	2:15:00	7	1.1318	6.1	1,361,239	Open	13.5	111
6/6/2026	2:30:00	7.1	1.7413	4.2	1,361,263	Open	13.5	112
6/6/2026	2:45:00	7	0.0000	4.2	1,361,284	Closed	13.5	112
6/6/2026	3:00:00	7.1	1.6353	4	1,361,303	Open	13.4	112
6/6/2026	3:15:00	7	1.6694	3.9	1,361,317	Open	14	110
6/6/2026	3:30:00	7	1.7072	4.1	1,361,342	Open	13.5	110
6/6/2026	3:45:00	7.1	0.0000	4.4	1,361,364	Closed	13.4	110
6/6/2026	4:00:00	7	1.6769	4.9	1,361,383	Open	13.3	109
6/6/2026	4:15:00	7	1.6580	4.1	1,361,391	Open	13.6	112
6/6/2026	4:30:00	7	0.0000	3.9	1,361,398	Closed	14.2	246
6/6/2026	4:45:00	7	1.5066	4.1	1,361,420	Open	13.4	112
6/6/2026	5:00:00	7.1	0.0000	1.3	1,361,428	Closed	13.9	111
6/6/2026	5:15:00	7	1.4309	0.4	1,361,447	Open	13.4	111
6/6/2026	5:30:00	7	1.4157	0.3	1,361,465	Open	13.4	111
6/6/2026	5:45:00	7	1.3892	0.5	1,361,486	Open	13.4	111
6/6/2026	6:00:00	7	1.3892	0.5	1,361,503	Open	13.4	112
6/6/2026	6:15:00	7	1.3590	0.5	1,361,524	Open	13.4	245
6/6/2026	6:30:00	7	1.2340	0.6	1,361,532	Closed	13.3	111
6/6/2026	6:45:00	7.1	1.3552	1	1,361,534	Open	13.3	112
6/6/2026	7:00:00	7	1.3362	0.6	1,361,551	Open	13.3	111
6/6/2026	7:15:00	7	1.3173	0.9	1,361,571	Open	13.4	111
6/6/2026	7:30:00	7	1.3325	0.6	1,361,588	Open	13.4	111
6/6/2026	7:45:00	7	1.3287	0.8	1,361,608	Open	13.4	111
6/6/2026	8:00:00	7	1.3627	1.5	1,361,617	Open	13.5	111
6/6/2026	8:15:00	7	1.3514	0.6	1,361,637	Open	13.3	111



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	8:30:00	7	1.3400	0.8	1,361,654	Open	13.3	110
6/6/2026	8:45:00	7	1.3287	0.7	1,361,674	Open	13.2	112
6/6/2026	9:00:00	7	1.2113	1.6	1,361,683	Open	13.1	110
6/6/2026	9:15:00	7	1.2000	1.3	1,361,702	Open	13	110
6/6/2026	9:30:00	7.1	0.0000	1.3	1,361,709	Closed	13.5	109
6/6/2026	9:45:00	7.1	1.4195	1.5	1,361,717	Open	13.4	109
6/6/2026	10:00:00	7	1.4195	1	1,361,735	Open	13.3	109
6/6/2026	10:15:00	7	1.4195	1	1,361,757	Open	13.3	110
6/6/2026	10:30:00	7	1.4195	1.1	1,361,774	Open	13.3	109
6/6/2026	10:45:00	7	1.4044	1.1	1,361,795	Open	13.3	108
6/6/2026	11:00:00	7	1.4082	1.2	1,361,813	Open	13.4	108
6/6/2026	11:15:00	7	1.4271	1	1,361,834	Open	13.5	110
6/6/2026	11:30:00	7	1.4044	0.9	1,361,854	Open	13.5	108
6/6/2026	11:45:00	7	1.5444	8.5	1,361,872	Open	13.6	108
6/6/2026	12:00:00	7	1.5369	1.7	1,361,896	Open	13.4	110
6/6/2026	12:15:00	7	1.5331	2.3	1,361,919	Open	13.4	109
6/6/2026	12:30:00	7	1.5179	3.8	1,361,938	Open	13.7	110
6/6/2026	12:45:00	7	1.5104	3.3	1,361,961	Open	13.5	110
6/6/2026	13:00:00	7.1	1.5066	3.2	1,361,984	Open	13.7	110
6/6/2026	13:15:00	7.1	0.0000	4.7	1,362,003	Closed	14.3	110
6/6/2026	13:30:00	7.1	1.5482	2.8	1,362,016	Open	14	110
6/6/2026	13:45:00	7.1	1.4309	5.8	1,362,037	Closed	14	243
6/6/2026	14:00:00	7	1.5331	4.8	1,362,046	Open	14.6	245
6/6/2026	14:15:00	7	1.5179	2.3	1,362,069	Open	14.2	245
6/6/2026	14:30:00	7	1.4990	2.7	1,362,091	Open	14.2	245
6/6/2026	14:45:00	7.1	1.5066	9	1,362,110	Open	14.5	245
6/6/2026	15:00:00	7.1	1.5520	4.2	1,362,123	Open	14.2	245
6/6/2026	15:15:00	7	1.5331	1.6	1,362,146	Open	14.1	110
6/6/2026	15:30:00	7	1.5293	2	1,362,166	Open	14.7	109
6/6/2026	15:45:00	7	1.5179	2.2	1,362,189	Open	14.1	112
6/6/2026	16:00:00	7	1.4877	2.6	1,362,211	Open	14.1	245
6/6/2026	16:15:00	7.1	1.5104	4.8	1,362,231	Open	14.4	110



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	16:30:00	7	1.5066	1.8	1,362,253	Open	14	110
6/6/2026	16:45:00	7	1.4877	1.7	1,362,262	Open	14.1	245
6/6/2026	17:00:00	7	1.5369	6.6	1,362,280	Open	13.7	110
6/6/2026	17:15:00	7	1.5104	1.1	1,362,303	Open	13.7	109
6/6/2026	17:30:00	7.1	0.0000	1.6	1,362,316	Closed	14.1	109
6/6/2026	17:45:00	7.1	1.4082	3.5	1,362,316	Closed	13.7	110
6/6/2026	18:00:00	7.1	1.4044	2.1	1,362,316	Closed	13.6	109
6/6/2026	18:15:00	7.1	1.5066	2.4	1,362,334	Open	13.5	109
6/6/2026	18:30:00	7.1	0.0000	5.9	1,362,348	Closed	13.9	109
6/6/2026	18:45:00	7.1	1.4082	2.6	1,362,366	Open	13.6	109
6/6/2026	19:00:00	7.1	1.4990	2.9	1,362,388	Open	13.5	109
6/6/2026	19:15:00	7	0.0000	3.4	1,362,400	Closed	14	109
6/6/2026	19:30:00	7.1	1.5028	3.5	1,362,420	Open	13.3	110
6/6/2026	19:45:00	7.1	1.4990	3.9	1,362,442	Open	13.1	108
6/6/2026	20:00:00	7.1	0.0000	5.2	1,362,453	Closed	13.6	108
6/6/2026	20:15:00	7	1.5634	11.4	1,362,473	Open	13	108
6/6/2026	20:30:00	7.1	0.0000	4.7	1,362,492	Closed	13.1	108
6/6/2026	20:45:00	7	1.0486	6.3	1,362,503	Open	13.6	110
6/6/2026	21:00:00	7	1.6050	3.9	1,362,526	Open	13.3	110
6/6/2026	21:15:00	7	1.0826	3.6	1,362,535	Open	13.8	110
6/6/2026	21:30:00	7	1.6315	3.8	1,362,543	Open	13.8	110
6/6/2026	21:45:00	7	0.5981	3.2	1,362,562	Open	13.2	110
6/6/2026	22:00:00	7	1.5785	1.9	1,362,584	Open	13.3	112
6/6/2026	22:15:00	7.1	1.0410	2.1	1,362,605	Open	13.9	112
6/6/2026	22:30:00	7	1.5899	0.8	1,362,629	Open	13.6	114
6/6/2026	22:45:00	7.1	1.0410	0.8	1,362,650	Open	14	114
6/6/2026	23:00:00	7	1.5747	1.1	1,362,673	Open	13.8	114
6/6/2026	23:15:00	7.1	1.0145	1	1,362,693	Open	14.2	114
6/6/2026	23:30:00	7	1.5444	0.6	1,362,716	Open	14	245
6/6/2026	23:45:00	7.1	0.0000	0.5	1,362,730	Closed	14.3	243
6/7/2026	0:00:00	7	1.5444	0.6	1,362,747	Open	14.1	245
6/7/2026	0:15:00	7.1	0.0000	0.4	1,362,755	Closed	14.6	245



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	0:30:00	7	1.5709	0.3	1,362,778	Open	14.1	245
6/7/2026	0:45:00	7.1	1.0296	1.1	1,362,798	Open	14.4	243
6/7/2026	1:00:00	7	1.5596	0.4	1,362,821	Open	14	245
6/7/2026	1:15:00	7.1	1.0107	2	1,362,842	Open	14.4	243
6/7/2026	1:30:00	7	1.5369	1.1	1,362,864	Open	14	243
6/7/2026	1:45:00	7.1	1.0334	1.8	1,362,885	Open	14.4	243
6/7/2026	2:00:00	7	1.5369	1.5	1,362,907	Open	14.1	245
6/7/2026	2:15:00	7.1	0.0000	3.7	1,362,927	Closed	14.4	243
6/7/2026	2:30:00	7	0.5830	5.6	1,362,939	Open	14.1	245
6/7/2026	2:45:00	7	1.5028	2.1	1,362,958	Open	14	243
6/7/2026	3:00:00	7	1.0221	5.5	1,362,968	Open	14	243
6/7/2026	3:15:00	7	1.5217	2.4	1,362,988	Open	13.9	243
6/7/2026	3:30:00	7.1	0.9993	5.4	1,363,010	Open	14	243
6/7/2026	3:45:00	7	1.5482	2.5	1,363,017	Open	14.3	243
6/7/2026	4:00:00	7.1	0.9804	4	1,363,039	Open	14.1	244
6/7/2026	4:15:00	7	1.5369	2.4	1,363,060	Open	14	243
6/7/2026	4:30:00	7.1	1.0145	6.1	1,363,082	Open	14.1	245
6/7/2026	4:45:00	7	1.5520	3.4	1,363,094	Open	14.1	243
6/7/2026	5:00:00	7.1	0.9842	3.9	1,363,116	Open	14.1	243
6/7/2026	5:15:00	7	1.5444	3.2	1,363,137	Open	14	243
6/7/2026	5:30:00	7.1	0.9918	4	1,363,155	Open	14	243
6/7/2026	5:45:00	7	1.5369	3.1	1,363,176	Open	14	245
6/7/2026	6:00:00	7.1	0.9956	7.4	1,363,198	Open	14.1	243
6/7/2026	6:15:00	7	1.5142	3.8	1,363,218	Open	14	243
6/7/2026	6:30:00	7.1	0.0000	3.7	1,363,233	Closed	14.1	247
6/7/2026	6:45:00	7	1.5104	4.6	1,363,245	Open	14	245
6/7/2026	7:00:00	7.1	1.1167	5.2	1,363,269	Open	14.2	245
6/7/2026	7:15:00	7	1.7072	4.3	1,363,292	Open	14.1	245
6/7/2026	7:30:00	7.1	0.1514	5.2	1,363,310	Open	14.4	245
6/7/2026	7:45:00	7	1.7451	6.4	1,363,331	Open	14.2	241
6/7/2026	8:00:00	7	1.1432	5.9	1,363,356	Open	14.1	243
6/7/2026	8:15:00	7	1.7526	6.7	1,363,380	Open	13.9	245



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	8:30:00	7	1.1848	6.3	1,363,405	Open	14	243
6/7/2026	8:45:00	7	1.7337	7.6	1,363,429	Open	14	246
6/7/2026	9:00:00	7	1.1167	7.1	1,363,454	Open	14.1	246
6/7/2026	9:15:00	7	1.7261	6.8	1,363,477	Open	14.1	246
6/7/2026	9:30:00	7	1.1281	8.4	1,363,501	Open	14.2	247
6/7/2026	9:45:00	7	1.7224	7.8	1,363,514	Open	14.6	247
6/7/2026	10:00:00	7	1.1281	9.2	1,363,538	Open	14.4	245
6/7/2026	10:15:00	7	1.7602	8.8	1,363,551	Open	14.8	246
6/7/2026	10:30:00	7	1.1697	9.9	1,363,576	Open	14.4	245
6/7/2026	10:45:00	7	0.2158	9.9	1,363,583	Open	15.6	246
6/7/2026	11:00:00	7	0.2915	13.8	1,363,592	Open	14.2	245
6/7/2026	11:15:00	7	1.1470	1.5	1,363,607	Open	15.1	245
6/7/2026	11:30:00	6.9	0.7268	1.3	1,363,623	Open	16.1	245
6/7/2026	11:45:00	6.9	1.8094	1.5	1,363,640	Open	17.6	247
6/7/2026	12:00:00	7	1.3098	2.5	1,363,667	Open	14.1	246
6/7/2026	12:15:00	7	1.9003	4	1,363,694	Open	13.9	245
6/7/2026	12:30:00	7	1.3135	2.7	1,363,721	Open	13.9	245
6/7/2026	12:45:00	7	1.8738	2	1,363,738	Open	14	247
6/7/2026	13:00:00	7	1.2303	2	1,363,764	Open	14.3	248
6/7/2026	13:15:00	7	1.8776	1.8	1,363,779	Open	14.5	246
6/7/2026	13:30:00	7.1	0.3407	1.2	1,363,805	Open	14.9	246
6/7/2026	13:45:00	7	1.8813	3.4	1,363,820	Open	14.9	246
6/7/2026	14:00:00	7.1	0.2120	2.9	1,363,840	Open	14.9	245
6/7/2026	14:15:00	7	1.7829	4.2	1,363,859	Open	14.6	245
6/7/2026	14:30:00	7	0.1287	2.6	1,363,877	Open	14.8	247
6/7/2026	14:45:00	7	0.6284	5.9	1,363,888	Open	14.1	247
6/7/2026	15:00:00	7.1	1.1583	4.9	1,363,906	Open	14.4	245
6/7/2026	15:15:00	7	1.8132	4.7	1,363,930	Open	14	245
6/7/2026	15:30:00	7	1.2000	5.3	1,363,945	Open	14.5	245
6/7/2026	15:45:00	7	1.8397	4.9	1,363,971	Open	14.2	245
6/7/2026	16:00:00	7.1	0.2423	3.8	1,363,985	Open	14.7	245
6/7/2026	16:15:00	7	1.8397	4.4	1,364,009	Open	14.2	247



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	16:30:00	7	0.2536	4.1	1,364,022	Open	14.3	244
6/7/2026	16:45:00	7	1.8246	5.3	1,364,045	Open	13.6	245
6/7/2026	17:00:00	7.1	0.2006	4.4	1,364,058	Open	14.3	246
6/7/2026	17:15:00	7	1.8435	6.5	1,364,082	Open	14.1	245
6/7/2026	17:30:00	7.1	0.2347	4.1	1,364,095	Open	14.6	245
6/7/2026	17:45:00	7	1.8132	6.9	1,364,119	Open	14.1	243
6/7/2026	18:00:00	7.1	0.2839	4.7	1,364,130	Open	14.8	243
6/7/2026	18:15:00	7	1.8208	8.4	1,364,154	Open	13.9	245
6/7/2026	18:30:00	7.1	0.2574	5.3	1,364,167	Open	14.4	245
6/7/2026	18:45:00	7	1.8586	7	1,364,191	Open	13.8	245
6/7/2026	19:00:00	7	1.2000	5.8	1,364,202	Open	14.5	245
6/7/2026	19:15:00	7	1.8208	6.8	1,364,227	Open	14	245
6/7/2026	19:30:00	7	1.2189	6.2	1,364,238	Open	14.6	245
6/7/2026	19:45:00	7	1.8397	5.4	1,364,263	Open	13.7	245
6/7/2026	20:00:00	7.1	0.2196	5.1	1,364,278	Open	14	243
6/7/2026	20:15:00	7	1.8473	7.8	1,364,302	Open	13.5	247
6/7/2026	20:30:00	7	1.2492	6.7	1,364,312	Open	14.2	245
6/7/2026	20:45:00	7	1.7602	4.9	1,364,337	Open	13.5	248
6/7/2026	21:00:00	7.1	0.1590	4.5	1,364,351	Open	13.9	246
6/7/2026	21:15:00	7	1.6353	4.9	1,364,357	Open	14.5	246
6/7/2026	21:30:00	7	0.3975	5.5	1,364,379	Open	13.9	246
6/7/2026	21:45:00	7	1.6277	0.5	1,364,400	Open	14.1	245
6/7/2026	22:00:00	7.1	1.0258	1.1	1,364,423	Open	14.3	245
6/7/2026	22:15:00	7	1.6239	0.4	1,364,444	Open	14.1	244
6/7/2026	22:30:00	7.1	1.0864	1.4	1,364,466	Open	14.1	245
6/7/2026	22:45:00	7.1	0.2309	1	1,364,484	Open	14.2	246
6/7/2026	23:00:00	7.1	1.2757	2.2	1,364,498	Open	14.4	246
6/7/2026	23:15:00	7	1.6012	0.4	1,364,521	Open	14.4	245
6/7/2026	23:30:00	7	0.2612	0.6	1,364,534	Open	15.1	245
6/7/2026	23:45:00	7	1.6315	0.6	1,364,556	Open	14.4	244

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

Appendix B: CP2 WTP Data Logs



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	0:00:00	7.37	0.3255	2	122198.6	ON	13.5	150
6/1/2026	0:15:00	7.32	0.9417	2	122205.7	ON	14.9	152
6/1/2026	0:30:00	7.36	0.9689	2	122219.4	ON	13.5	151
6/1/2026	0:45:00	7.37	0.7092	2	122240.5	ON	13.4	153
6/1/2026	1:00:00	7.38	2.3989	2	122256.0	ON	12.9	155
6/1/2026	1:15:00	7.39	2.3485	2	122290.0	ON	12.8	158
6/1/2026	1:30:00	7.38	0.6317	3	122312.7	ON	13.4	157
6/1/2026	1:45:00	7.36	0.3333	2	122318.2	ON	14.6	158
6/1/2026	2:00:00	7.34	0.3837	3	122323.8	ON	15.5	158
6/1/2026	2:15:00	7.39	2.3369	4	122352.4	ON	13.3	157
6/1/2026	2:30:00	7.41	2.3175	3	122385.7	ON	13.2	156
6/1/2026	2:45:00	7.4	1.9338	3	122416.3	ON	13.4	156
6/1/2026	3:00:00	7.41	2.1857	6	122432.5	ON	13.4	155
6/1/2026	3:15:00	7.42	2.1625	2	122459.8	ON	14.1	154
6/1/2026	3:30:00	7.41	1.3215	2	122484.1	ON	14.5	154
6/1/2026	3:45:00	7.4	2.0772	2	122509.2	ON	13.6	152
6/1/2026	4:00:00	7.39	0.3565	2	122520.5	ON	14.6	152
6/1/2026	4:15:00	7.37	2.1431	2	122534.7	ON	13.2	151
6/1/2026	4:30:00	7.39	1.4300	2	122561.6	ON	13.2	152
6/1/2026	4:45:00	7.4	1.8912	2	122590.5	ON	13.3	153
6/1/2026	5:00:00	7.37	0.2635	2	122603.1	ON	15.9	153
6/1/2026	5:15:00	7.43	1.6315	2	122617.7	ON	14	155
6/1/2026	5:30:00	7.43	0.8332	2	122642.2	ON	13.7	166
6/1/2026	5:45:00	7.38	0.7557	2	122653.7	ON	14.1	168
6/1/2026	6:00:00	7.37	1.7982	2	122671.6	ON	13.6	167
6/1/2026	6:15:00	7.39	2.3601	2	122697.4	ON	13.3	165
6/1/2026	6:30:00	7.4	0.4999	2	122717.5	ON	14.1	162
6/1/2026	6:45:00	7.4	2.3562	3	122735.0	ON	13.3	159
6/1/2026	7:00:00	7.41	1.5773	2	122765.7	ON	14.4	156
6/1/2026	7:15:00	7.38	2.3136	2	122797.4	ON	15.4	158
6/1/2026	7:30:00	7.35	0.0969	2	122814.6	ON	17	159
6/1/2026	7:45:00	7.4	1.6742	2	122826.6	ON	13.7	156



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	8:00:00	7.37	2.3252	2	122856.9	ON	15.1	155
6/1/2026	8:15:00	7.33	2.2671	2	122890.9	ON	17.2	157
6/1/2026	8:30:00	7.3	2.1896	2	122922.5	ON	18.9	158
6/1/2026	8:45:00	7.35	1.9765	2	122949.5	ON	14.8	146
6/1/2026	9:00:00	7.35	0.3100	2	122963.4	ON	15.1	147
6/1/2026	9:15:00	7.35	1.3835	2	122978.2	ON	13.9	152
6/1/2026	9:30:00	7.35	1.8214	2	123002.4	ON	13.8	150
6/1/2026	9:45:00	7.35	1.4572	2	123027.3	ON	14	149
6/1/2026	10:00:00	7.35	1.4727	2	123051.2	ON	14.2	149
6/1/2026	10:15:00	7.34	1.7246	2	123075.9	ON	15.9	147
6/1/2026	10:30:00	7.3	1.6936	2	123100.1	ON	17.7	150
6/1/2026	10:45:00	7.34	0.3294	2	123116.7	ON	16.5	149
6/1/2026	11:00:00	7.33	1.3060	2	123122.9	ON	15.9	146
6/1/2026	11:15:00	7.28	1.5385	2	123143.6	ON	18	151
6/1/2026	11:30:00	7.29	0.4185	2	123153.9	ON	20	153
6/1/2026	11:45:00	7.31	1.2711	2	123167.4	ON	14.4	150
6/1/2026	12:00:00	7.31	2.0462	2	123194.1	ON	13.6	152
6/1/2026	12:15:00	7.31	2.0191	2	123224.7	ON	13.6	153
6/1/2026	12:30:00	7.3	1.5540	2	123252.0	ON	13.7	153
6/1/2026	12:45:00	7.3	1.5540	2	123274.4	ON	13.9	153
6/1/2026	13:00:00	7.3	1.5424	2	123298.2	ON	14	151
6/1/2026	13:15:00	7.31	1.5153	2	123322.0	ON	14	151
6/1/2026	13:30:00	7.31	1.6742	2	123340.8	ON	14.1	151
6/1/2026	13:45:00	7.31	1.4649	2	123362.4	ON	14	151
6/1/2026	14:00:00	7.31	1.4184	2	123382.9	ON	14	151
6/1/2026	14:15:00	7.3	1.2866	2	123403.8	ON	14.1	151
6/1/2026	14:30:00	7.3	1.3641	2	123423.9	ON	14.2	151
6/1/2026	14:45:00	7.3	1.2828	2	123444.3	ON	14.2	151
6/1/2026	15:00:00	7.31	1.4223	2	123462.0	ON	14.5	151
6/1/2026	15:15:00	7.25	1.3758	2	123483.5	ON	18.1	151
6/1/2026	15:30:00	7.7	1.2711	522	123501.9	ON	21	0
6/1/2026	15:45:00	7.28	1.0115	2	123518.7	ON	18.1	150



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/1/2026	16:00:00	7.22	0.8836	2	123534.4	ON	20.8	152
6/1/2026	16:15:00	7.3	1.3331	2	123547.9	ON	16.4	147
6/1/2026	16:30:00	7.3	1.8602	2	123567.5	ON	16.2	147
6/1/2026	16:45:00	7.26	1.8524	2	123595.2	ON	19.1	151
6/1/2026	17:00:00	7.32	1.7323	2	123621.0	ON	14.5	149
6/1/2026	17:15:00	7.33	0.6821	2	123639.4	ON	14.7	149
6/1/2026	17:30:00	7.28	0.5232	2	123646.4	ON	18.2	149
6/1/2026	17:45:00	7.25	0.2597	2	123651.0	ON	21	150
6/1/2026	18:00:00	7.31	0.7053	2	123664.9	ON	15.3	148
6/1/2026	18:15:00	7.33	0.8565	6	123681.4	ON	14.5	149
6/1/2026	18:30:00	7.32	2.0850	2	123704.4	ON	13.9	147
6/1/2026	18:45:00	7.33	2.0230	2	123735.1	ON	13.9	148
6/1/2026	19:00:00	7.31	1.7052	2	123765.3	ON	16.4	146
6/1/2026	19:15:00	7.28	1.5153	2	123792.1	ON	18.5	147
6/1/2026	19:30:00	7.25	1.1122	2	123815.2	ON	20	148
6/1/2026	19:45:00	7.28	0.3410	2	123821.9	ON	20.3	148
6/1/2026	20:00:00	7.27	1.6819	2	123832.9	ON	20.8	148
6/1/2026	20:15:00	7.3	0.8138	2	123852.7	ON	18.7	150
6/1/2026	20:30:00	7.31	0.8216	2	123863.5	ON	16.8	150
6/1/2026	20:45:00	7.29	2.0462	2	123886.8	ON	16.6	151
6/1/2026	21:00:00	7.26	0.4728	2	123906.5	ON	18.2	154
6/1/2026	21:15:00	7.28	1.8137	2	123933.8	ON	17	148
6/1/2026	21:30:00	7.24	1.4804	2	123957.6	ON	18.6	150
6/1/2026	21:45:00	7.23	1.8369	2	123982.5	ON	19.8	150
6/1/2026	22:00:00	7.21	1.6005	2	124006.8	ON	20.8	150
6/1/2026	22:15:00	7.28	0.8681	3	124022.7	ON	14.6	143
6/1/2026	22:30:00	7.28	0.9030	2	124044.0	ON	16.7	147
6/1/2026	22:45:00	7.25	1.2828	2	124061.2	ON	18.4	149
6/1/2026	23:00:00	7.27	1.8331	2	124077.4	ON	17.3	146
6/1/2026	23:15:00	7.24	1.8137	2	124105.5	ON	18.5	148
6/1/2026	23:30:00	7.23	1.8059	2	124133.6	ON	19.6	150
6/1/2026	23:45:00	7.21	1.6897	2	124160.5	ON	20.3	151



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	0:00:00	7.17	0.2945	2	124167.7	ON	20.8	151
6/2/2026	0:15:00	7.15	0.3643	2	124171.4	ON	21.2	151
6/2/2026	0:30:00	7.31	1.5230	5	124185.9	ON	15.7	144
6/2/2026	0:45:00	7.31	1.7284	2	124200.8	ON	13.8	146
6/2/2026	1:00:00	7.3	1.7633	2	124221.6	ON	14.9	146
6/2/2026	1:15:00	7.32	1.8447	2	124239.1	ON	14.5	145
6/2/2026	1:30:00	7.29	1.7439	2	124261.7	ON	15.4	147
6/2/2026	1:45:00	7.25	0.3023	2	124268.2	ON	17.2	148
6/2/2026	2:00:00	7.3	1.2944	2	124280.9	ON	12.8	149
6/2/2026	2:15:00	7.3	1.5385	2	124301.9	ON	12.4	149
6/2/2026	2:30:00	7.3	1.2828	2	124322.5	ON	12.4	149
6/2/2026	2:45:00	7.3	1.3215	2	124342.6	ON	12.4	149
6/2/2026	3:00:00	7.3	1.2246	2	124362.5	ON	12.3	149
6/2/2026	3:15:00	7.29	0.5387	2	124381.1	ON	12.4	149
6/2/2026	3:30:00	7.27	0.6239	2	124387.9	ON	14.2	149
6/2/2026	3:45:00	7.29	1.3525	2	124403.0	ON	12.4	149
6/2/2026	4:00:00	7.26	1.5230	2	124420.7	ON	12.3	149
6/2/2026	4:15:00	7.25	1.4184	2	124441.6	ON	12.2	150
6/2/2026	4:30:00	7.24	1.3021	2	124462.0	ON	12.2	150
6/2/2026	4:45:00	7.26	1.8563	2	124484.2	ON	12.8	150
6/2/2026	5:00:00	7.23	2.1392	2	124513.9	ON	14.3	149
6/2/2026	5:15:00	7.21	2.1082	2	124543.4	ON	15.3	149
6/2/2026	5:30:00	7.18	1.5618	2	124569.2	ON	15.9	149
6/2/2026	5:45:00	7.17	1.9261	2	124596.3	ON	16.5	150
6/2/2026	6:00:00	7.21	2.2671	2	124629.7	ON	16.1	149
6/2/2026	6:15:00	7.24	2.2400	2	124663.6	ON	13.3	146
6/2/2026	6:30:00	7.27	2.2012	2	124697.2	ON	13.3	147
6/2/2026	6:45:00	7.24	1.6548	2	124727.1	ON	14.4	147
6/2/2026	7:00:00	7.27	0.0853	2	124732.9	ON	13.7	147
6/2/2026	7:15:00	7.28	0.9146	3	124737.2	ON	12.5	148
6/2/2026	7:30:00	7.3	1.0270	2	124752.2	ON	12.2	150
6/2/2026	7:45:00	7.3	1.3525	2	124773.6	ON	12.1	149



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	8:00:00	7.3	0.1085	2	124783.8	ON	13	149
6/2/2026	8:15:00	7.29	1.0464	2	124789.3	ON	12.6	149
6/2/2026	8:30:00	7.3	1.1006	2	124808.2	ON	12.6	150
6/2/2026	8:45:00	7.3	2.4648	2	124832.6	ON	12.6	149
6/2/2026	9:00:00	7.28	1.9300	2	124866.0	ON	12.7	147
6/2/2026	9:15:00	7.3	0.0000	2	124897.4	ON	13.1	146
6/2/2026	9:30:00	7.28	0.0000	2	124897.4	ON	14.4	146
6/2/2026	9:45:00	7.26	0.2364	2	124913.2	ON	14.9	146
6/2/2026	10:00:00	7.23	0.3798	2	124918.4	ON	16.6	147
6/2/2026	10:15:00	7.24	1.8951	4	124936.7	ON	17.5	146
6/2/2026	10:30:00	7.22	0.0000	4	124958.8	ON	19	147
6/2/2026	10:45:00	7.26	1.8757	2	124978.4	ON	17	144
6/2/2026	11:00:00	7.23	1.7362	2	125004.2	ON	18.7	146
6/2/2026	11:15:00	7.21	1.6819	2	125028.6	ON	20	148
6/2/2026	11:30:00	7.18	0.0853	2	125038.1	ON	21	149
6/2/2026	11:45:00	7.24	1.8447	2	125046.5	ON	19.2	144
6/2/2026	12:00:00	7.21	1.7439	2	125073.7	ON	20.5	149
6/2/2026	12:15:00	7.18	1.6548	2	125097.6	ON	21.7	149
6/2/2026	12:30:00	7.17	1.7517	2	125123.9	ON	22.7	150
6/2/2026	12:45:00	7.32	1.4882	2	125150.5	ON	15.4	150
6/2/2026	13:00:00	7.31	0.7363	2	125170.2	ON	15.3	152
6/2/2026	13:15:00	7.28	0.3410	2	125175.9	ON	17.6	153
6/2/2026	13:30:00	7.27	1.7284	2	125184.6	ON	16.3	152
6/2/2026	13:45:00	7.33	1.2634	3	125208.2	ON	14.6	154
6/2/2026	14:00:00	7.32	1.5967	2	125231.4	ON	14.3	152
6/2/2026	14:15:00	7.31	0.5077	2	125245.8	ON	15	151
6/2/2026	14:30:00	7.31	0.3643	2	125252.3	ON	16.1	151
6/2/2026	14:45:00	7.31	1.4184	2	125264.5	ON	14.9	153
6/2/2026	15:00:00	7.32	1.7594	2	125286.3	ON	14.6	152
6/2/2026	15:15:00	7.32	1.8021	2	125313.5	ON	14.4	151
6/2/2026	15:30:00	7.32	1.7904	2	125337.5	ON	14.5	150
6/2/2026	15:45:00	7.32	0.6123	3	125354.6	ON	15	149



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/2/2026	16:00:00	7.32	2.0230	2	125375.2	ON	14.3	149
6/2/2026	16:15:00	7.32	1.4727	2	125404.2	ON	14.3	150
6/2/2026	16:30:00	7.32	1.9803	2	125432.2	ON	14.2	149
6/2/2026	16:45:00	7.32	0.5503	2	125447.8	ON	15	148
6/2/2026	17:00:00	7.32	0.5813	2	125454.6	ON	15.6	149
6/2/2026	17:15:00	7.3	2.0346	2	125477.5	ON	16.8	149
6/2/2026	17:30:00	7.27	1.8951	2	125507.6	ON	18.5	151
6/2/2026	17:45:00	7.31	1.8834	2	125536.1	ON	14.8	147
6/2/2026	18:00:00	7.31	1.8912	2	125560.1	ON	15.7	146
6/2/2026	18:15:00	7.33	1.8757	2	125587.4	ON	14.3	149
6/2/2026	18:30:00	7.35	1.3990	2	125613.1	ON	14.8	146
6/2/2026	18:45:00	7.3	0.1473	2	125619.3	ON	16.9	146
6/2/2026	19:00:00	7.27	0.1783	2	125622.7	ON	18.4	149
6/2/2026	19:15:00	7.3	1.7439	2	125637.3	ON	15.4	146
6/2/2026	19:30:00	7.32	1.4610	2	125663.6	ON	14.9	146
6/2/2026	19:45:00	7.28	1.3564	2	125683.9	ON	16.6	147
6/2/2026	20:00:00	7.28	1.5695	2	125706.5	ON	14.9	146
6/2/2026	20:15:00	7.25	1.4804	2	125729.1	ON	16.4	146
6/2/2026	20:30:00	7.23	0.4108	2	125747.1	ON	17.5	149
6/2/2026	20:45:00	7.34	1.2673	2	125763.9	ON	14.7	160
6/2/2026	21:00:00	7.34	1.8408	4	125788.1	ON	14.4	158
6/2/2026	21:15:00	7.32	1.2983	2	125812.5	ON	14	155
6/2/2026	21:30:00	7.3	1.8447	2	125837.6	ON	13.6	154
6/2/2026	21:45:00	7.32	1.9610	3	125861.3	ON	13.3	151
6/2/2026	22:00:00	7.32	1.9532	2	125888.5	ON	12.9	149
6/2/2026	22:15:00	7.31	0.6704	2	125905.5	ON	13.2	148
6/2/2026	22:30:00	7.32	0.3720	2	125912.8	ON	14.1	146
6/2/2026	22:45:00	7.31	1.9377	2	125923.9	ON	13.1	147
6/2/2026	23:00:00	7.32	1.8098	2	125948.2	ON	12.7	148
6/2/2026	23:15:00	7.32	0.5542	2	125964.2	ON	13	147
6/2/2026	23:30:00	7.33	0.3565	2	125970.0	ON	14	147
6/2/2026	23:45:00	7.31	0.6937	4	125977.5	ON	13.4	147



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	0:00:00	7.33	1.9610	2	126001.1	ON	12.6	148
6/3/2026	0:15:00	7.31	1.9610	2	126027.9	ON	12.5	148
6/3/2026	0:30:00	7.31	1.9648	2	126055.0	ON	12.6	149
6/3/2026	0:45:00	7.3	1.9610	2	126079.5	ON	12.7	148
6/3/2026	1:00:00	7.3	1.9648	2	126106.1	ON	12.6	149
6/3/2026	1:15:00	7.31	1.9571	2	126133.4	ON	12.6	147
6/3/2026	1:30:00	7.3	1.9261	2	126157.7	ON	13.3	146
6/3/2026	1:45:00	7.3	1.9338	2	126185.0	ON	12.6	147
6/3/2026	2:00:00	7.32	1.4339	2	126211.7	ON	12.7	147
6/3/2026	2:15:00	7.28	0.1279	2	126218.2	ON	14.3	146
6/3/2026	2:30:00	7.26	0.2868	2	126221.5	ON	15.1	146
6/3/2026	2:45:00	7.29	1.9338	4	126236.5	ON	12.7	148
6/3/2026	3:00:00	7.28	1.9300	2	126263.1	ON	12.6	148
6/3/2026	3:15:00	7.27	1.9222	2	126287.4	ON	12.6	147
6/3/2026	3:30:00	7.28	1.3796	2	126313.7	ON	12.8	146
6/3/2026	3:45:00	7.25	0.2325	2	126320.1	ON	14.2	146
6/3/2026	4:00:00	7.23	0.2907	2	126323.5	ON	15	146
6/3/2026	4:15:00	7.26	0.5852	4	126331.6	ON	13.4	148
6/3/2026	4:30:00	7.24	0.5387	6	126338.6	ON	12.8	148
6/3/2026	4:45:00	7.23	1.6044	2	126365.4	ON	12.5	150
6/3/2026	5:00:00	7.21	2.1082	2	126394.3	ON	12.3	150
6/3/2026	5:15:00	7.23	2.0927	2	126425.0	ON	12.3	150
6/3/2026	5:30:00	7.24	2.0772	2	126454.7	ON	12.3	149
6/3/2026	5:45:00	7.25	2.0578	2	126482.6	ON	12.5	148
6/3/2026	6:00:00	7.27	1.9920	2	126512.1	ON	12.3	148
6/3/2026	6:15:00	7.27	0.7480	2	126536.3	ON	12.5	147
6/3/2026	6:30:00	7.28	0.1666	2	126542.7	ON	14.2	145
6/3/2026	6:45:00	7.25	0.2984	2	126546.1	ON	15.8	145
6/3/2026	7:00:00	7.26	0.2674	2	126549.8	ON	17	146
6/3/2026	7:15:00	7.24	1.5734	4	126554.2	ON	16	137
6/3/2026	7:30:00	7.27	2.1470	2	126575.4	ON	12.7	146
6/3/2026	7:45:00	7.25	2.1392	2	126606.1	ON	12.6	147



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	8:00:00	7.25	2.1392	2	126629.3	ON	12.9	145
6/3/2026	8:15:00	7.25	2.1005	2	126660.0	ON	12.6	146
6/3/2026	8:30:00	7.26	1.7711	2	126689.7	ON	12.6	145
6/3/2026	8:45:00	7.28	1.3951	2	126718.2	ON	12.8	145
6/3/2026	9:00:00	7.29	2.0075	2	126746.4	ON	12.9	145
6/3/2026	9:15:00	7.28	0.1511	2	126755.9	ON	14.6	143
6/3/2026	9:30:00	7.25	0.1511	2	126759.3	ON	15.6	145
6/3/2026	9:45:00	7.25	1.6005	3	126766.5	ON	16.3	146
6/3/2026	10:00:00	7.23	1.9842	2	126794.6	ON	17.1	146
6/3/2026	10:15:00	7.28	1.8757	2	126822.2	ON	13.1	146
6/3/2026	10:30:00	7.28	1.8447	2	126845.4	ON	13.3	146
6/3/2026	10:45:00	7.28	0.1395	2	126859.7	ON	14.5	146
6/3/2026	11:00:00	7.28	1.0890	2	126869.3	ON	13.8	147
6/3/2026	11:15:00	7.29	0.1860	2	126880.9	ON	14.6	147
6/3/2026	11:30:00	7.3	1.7711	2	126896.2	ON	13.5	150
6/3/2026	11:45:00	7.32	1.5734	2	126923.3	ON	13.3	151
6/3/2026	12:00:00	7.33	2.1121	2	126952.8	ON	13.2	153
6/3/2026	12:15:00	7.31	0.8061	2	126976.6	ON	13.5	153
6/3/2026	12:30:00	7.33	0.8216	3	126987.3	ON	13.8	152
6/3/2026	12:45:00	7.34	2.1819	3	127013.5	ON	13.2	154
6/3/2026	13:00:00	7.35	2.1547	3	127044.2	ON	13.1	154
6/3/2026	13:15:00	7.33	0.5077	2	127060.4	ON	14	152
6/3/2026	13:30:00	7.31	0.4612	3	127067.0	ON	15	151
6/3/2026	13:45:00	7.29	0.4418	3	127073.8	ON	16.2	152
6/3/2026	14:00:00	7.29	2.1160	3	127083.7	ON	14.5	150
6/3/2026	14:15:00	7.31	2.1043	2	127114.3	ON	13.4	150
6/3/2026	14:30:00	7.29	2.1276	2	127145.0	ON	13.3	149
6/3/2026	14:45:00	7.27	1.0929	3	127166.6	ON	13.7	148
6/3/2026	15:00:00	7.27	0.5813	2	127182.7	ON	14	146
6/3/2026	15:15:00	7.24	0.4030	2	127189.6	ON	15.5	146
6/3/2026	15:30:00	7.24	1.0076	3	127197.5	ON	14.6	146
6/3/2026	15:45:00	7.23	2.1198	2	127226.5	ON	13.4	146



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/3/2026	16:00:00	7.22	2.1121	2	127257.2	ON	13.2	146
6/3/2026	16:15:00	7.23	1.5269	2	127286.7	ON	13.2	146
6/3/2026	16:30:00	7.24	0.3759	2	127299.7	ON	14.5	143
6/3/2026	16:45:00	7.21	0.3643	2	127305.6	ON	15.6	146
6/3/2026	17:00:00	7.18	0.3953	2	127312.4	ON	16.6	146
6/3/2026	17:15:00	7.23	1.0502	2	127324.1	ON	14.1	145
6/3/2026	17:30:00	7.23	2.0578	2	127345.2	ON	13.4	148
6/3/2026	17:45:00	7.22	0.7402	2	127370.9	ON	13.3	150
6/3/2026	18:00:00	7.22	0.3914	2	127378.9	ON	14.8	149
6/3/2026	18:15:00	7.21	1.1471	3	127386.9	ON	14.2	150
6/3/2026	18:30:00	7.25	0.6511	3	127414.1	ON	13.2	164
6/3/2026	18:45:00	7.26	2.1664	3	127431.5	ON	13	170
6/3/2026	19:00:00	7.28	2.1857	3	127452.0	ON	13	175
6/3/2026	19:15:00	7.28	1.6083	3	127481.0	ON	13.8	178
6/3/2026	19:30:00	7.3	2.1547	2	127510.6	ON	13.7	181
6/3/2026	19:45:00	7.32	2.1431	2	127540.8	ON	13.7	182
6/3/2026	20:00:00	7.34	2.1315	3	127571.4	ON	13.7	183
6/3/2026	20:15:00	7.33	0.4302	2	127586.4	ON	14.4	182
6/3/2026	20:30:00	7.3	0.4147	2	127593.3	ON	15.3	183
6/3/2026	20:45:00	7.27	0.4495	2	127600.1	ON	16.1	184
6/3/2026	21:00:00	7.28	2.0772	3	127609.9	ON	15.7	181
6/3/2026	21:15:00	7.37	2.0850	3	127640.1	ON	13.9	179
6/3/2026	21:30:00	7.36	1.0502	2	127663.4	ON	14.2	178
6/3/2026	21:45:00	7.35	2.0772	2	127687.1	ON	13.8	177
6/3/2026	22:00:00	7.35	2.0927	3	127717.8	ON	13.6	177
6/3/2026	22:15:00	7.37	2.0772	3	127748.4	ON	12.7	176
6/3/2026	22:30:00	7.38	2.0617	3	127775.5	ON	12.7	174
6/3/2026	22:45:00	7.34	0.3527	2	127788.4	ON	13.8	170
6/3/2026	23:00:00	7.31	0.3604	2	127792.7	ON	14.7	172
6/3/2026	23:15:00	7.31	0.9689	4	127800.2	ON	14.3	171
6/3/2026	23:30:00	7.35	2.0075	3	127829.4	ON	12.6	168
6/3/2026	23:45:00	7.25	1.4727	4	127855.6	ON	12.8	258



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	0:00:00	7.3	1.3138	3	127870.5	ON	12.9	167
6/4/2026	0:15:00	7.29	0.6433	3	127889.5	ON	12.7	164
6/4/2026	0:30:00	7.26	0.3255	3	127895.8	ON	13.9	161
6/4/2026	0:45:00	7.26	1.1510	4	127902.2	ON	13.3	162
6/4/2026	1:00:00	7.28	2.0036	3	127928.1	ON	12.4	160
6/4/2026	1:15:00	7.27	2.0578	3	127958.0	ON	12.3	159
6/4/2026	1:30:00	7.26	2.0152	3	127988.7	ON	12.3	159
6/4/2026	1:45:00	7.26	1.1549	3	128012.8	ON	12.6	157
6/4/2026	2:00:00	7.25	0.1821	3	128022.3	ON	13.5	154
6/4/2026	2:15:00	7.23	0.1783	3	128025.7	ON	14.2	156
6/4/2026	2:30:00	7.25	1.9067	3	128039.8	ON	12.6	156
6/4/2026	2:45:00	7.26	1.8679	3	128062.9	ON	12.5	155
6/4/2026	3:00:00	7.26	1.8214	3	128090.1	ON	12.4	155
6/4/2026	3:15:00	7.16	1.7866	3	128115.8	ON	12.5	162
6/4/2026	3:30:00	7.04	1.2014	3	128139.0	ON	12.9	167
6/4/2026	3:45:00	7.03	1.7401	3	128165.4	ON	12.8	164
6/4/2026	4:00:00	7.09	1.7013	3	128188.6	ON	12.7	161
6/4/2026	4:15:00	7.14	1.2401	3	128212.0	ON	12.7	160
6/4/2026	4:30:00	7.18	0.3759	3	128226.1	ON	13.3	158
6/4/2026	4:45:00	7.15	0.0853	3	128226.7	ON	14	157
6/4/2026	5:00:00	7.18	1.6083	3	128237.2	ON	12.9	158
6/4/2026	5:15:00	7.19	0.9805	3	128251.8	ON	12.8	157
6/4/2026	5:30:00	7.24	2.2787	3	128282.7	ON	12.4	157
6/4/2026	5:45:00	7.24	1.8408	4	128315.9	ON	12.3	157
6/4/2026	6:00:00	7.24	1.2750	3	128344.1	ON	12.4	157
6/4/2026	6:15:00	7.24	1.1859	3	128361.3	ON	12.6	156
6/4/2026	6:30:00	7.25	2.2594	3	128392.5	ON	12.3	156
6/4/2026	6:45:00	7.25	2.2167	4	128426.6	ON	12.3	155
6/4/2026	7:00:00	7.26	2.1198	4	128456.8	ON	12.4	155
6/4/2026	7:15:00	7.24	0.1899	3	128469.0	ON	13.2	153
6/4/2026	7:30:00	7.2	0.1666	3	128472.4	ON	13.9	154
6/4/2026	7:45:00	7.17	0.2015	3	128475.9	ON	14.5	154



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	8:00:00	7.21	0.9960	4	128488.6	ON	13.2	155
6/4/2026	8:15:00	7.25	2.2594	3	128518.8	ON	12.6	155
6/4/2026	8:30:00	7.26	2.2400	4	128552.9	ON	12.7	156
6/4/2026	8:45:00	7.27	1.5967	4	128584.3	ON	12.9	157
6/4/2026	9:00:00	7.28	2.2361	4	128614.5	ON	12.9	158
6/4/2026	9:15:00	7.27	0.2868	3	128628.7	ON	13.8	156
6/4/2026	9:30:00	7.24	0.3178	4	128632.1	ON	14.4	157
6/4/2026	9:45:00	7.26	2.2477	5	128642.6	ON	13.5	159
6/4/2026	10:00:00	7.32	1.7594	4	128676.3	ON	13.2	154
6/4/2026	10:15:00	7.33	1.0657	4	128703.4	ON	13.5	149
6/4/2026	10:30:00	7.29	0.1976	4	128710.1	ON	14.6	149
6/4/2026	10:45:00	7.27	0.4495	4	128713.6	ON	15.3	149
6/4/2026	11:00:00	7.3	0.5348	3	128727.4	ON	14.8	146
6/4/2026	11:15:00	7.33	2.3059	4	128736.1	ON	14.4	138
6/4/2026	11:30:00	7.34	0.0000	4	128755.8	ON	14	138
6/4/2026	11:45:00	7.32	0.3294	4	128761.0	ON	14.9	138
6/4/2026	12:00:00	7.29	0.3565	4	128765.7	ON	15.7	139
6/4/2026	12:15:00	7.36	1.6936	4	128782.6	ON	14.2	136
6/4/2026	12:30:00	7.42	2.3446	4	128814.1	ON	13.8	135
6/4/2026	12:45:00	7.46	2.3175	4	128848.1	ON	13.9	135
6/4/2026	13:00:00	7.47	2.2826	4	128881.0	ON	13.9	136
6/4/2026	13:15:00	7.44	0.6549	4	128903.4	ON	14.4	135
6/4/2026	13:30:00	7.41	0.2480	4	128908.2	ON	15.4	135
6/4/2026	13:45:00	7.38	0.2752	4	128911.6	ON	16.2	135
6/4/2026	14:00:00	7.36	1.1200	4	128918.9	ON	15.1	137
6/4/2026	14:15:00	7.37	1.5075	4	128934.1	ON	14.8	136
6/4/2026	14:30:00	7.44	1.1122	0	128965.1	ON	14.1	135
6/4/2026	14:45:00	7.38	0.2674	0	128972.7	ON	15.2	132
6/4/2026	15:00:00	7.33	0.6046	0	128976.3	ON	16.3	135
6/4/2026	15:15:00	7.43	1.9803	0	129003.5	ON	14.1	135
6/4/2026	15:30:00	7.44	2.1702	0	129034.4	ON	13.9	133
6/4/2026	15:45:00	7.42	0.3410	0	129052.2	ON	14.9	132



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/4/2026	16:00:00	7.38	0.2325	0	129055.6	ON	16.3	133
6/4/2026	16:15:00	7.35	0.2131	0	129059.0	ON	17.4	133
6/4/2026	16:30:00	7.43	1.4804	0	129082.9	ON	14.3	135
6/4/2026	16:45:00	7.46	0.3372	0	129106.6	ON	14.2	135
6/4/2026	17:00:00	7.4	0.3875	0	129112.5	ON	15.8	134
6/4/2026	17:15:00	7.43	1.2634	0	129129.9	ON	14	135
6/4/2026	17:30:00	7.44	0.6201	0	129148.5	ON	14.3	134
6/4/2026	17:45:00	7.4	0.1705	0	129152.8	ON	15.7	134
6/4/2026	18:00:00	7.44	2.2129	0	129169.3	ON	14.1	135
6/4/2026	18:15:00	7.46	2.1625	0	129196.4	ON	13.6	136
6/4/2026	18:30:00	7.46	1.3641	0	129225.5	ON	13.4	136
6/4/2026	18:45:00	7.42	0.1434	0	129234.5	ON	14.9	134
6/4/2026	19:00:00	7.42	1.2711	0	129245.0	ON	14	135
6/4/2026	19:15:00	7.44	1.3564	0	129270.9	ON	13.4	136
6/4/2026	19:30:00	7.44	1.9648	0	129294.2	ON	13.3	136
6/4/2026	19:45:00	7.44	1.9145	0	129321.4	ON	13	136
6/4/2026	20:00:00	7.44	0.8410	0	129345.3	ON	13.1	136
6/4/2026	20:15:00	7.41	0.0620	0	129348.3	ON	14.5	134
6/4/2026	20:30:00	7.4	1.2634	0	129353.9	ON	13.5	136
6/4/2026	20:45:00	7.43	1.9571	0	129381.1	ON	12.8	136
6/4/2026	21:00:00	7.43	1.2944	0	129407.6	ON	12.7	136
6/4/2026	21:15:00	7.42	1.9261	0	129430.9	ON	12.6	136
6/4/2026	21:30:00	7.42	1.8447	0	129458.2	ON	12.5	136
6/4/2026	21:45:00	7.42	0.5774	0	129479.7	ON	12.8	136
6/4/2026	22:00:00	7.38	0.3565	0	129482.3	ON	14.1	134
6/4/2026	22:15:00	7.42	2.5500	0	129509.7	ON	12.5	136
6/4/2026	22:30:00	7.41	0.2752	0	129538.2	ON	12.5	136
6/4/2026	22:45:00	7.41	0.3720	0	129546.3	ON	13.6	135
6/4/2026	23:00:00	7.38	0.3992	0	129553.1	ON	14.3	135
6/4/2026	23:15:00	7.38	1.0890	0	129560.7	ON	13.7	135
6/4/2026	23:30:00	7.41	1.5075	0	129588.9	ON	12.4	136
6/4/2026	23:45:00	7.42	1.0231	0	129608.5	ON	12.6	136



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	0:00:00	7.4	1.2750	0	129629.0	ON	12.4	136
6/5/2026	0:15:00	7.42	2.3097	0	129661.3	ON	12.2	137
6/5/2026	0:30:00	7.42	0.6782	0	129682.2	ON	12.4	137
6/5/2026	0:45:00	7.4	0.3100	0	129687.1	ON	13.9	135
6/5/2026	1:00:00	7.35	0.9534	0	129692.5	ON	16.7	139
6/5/2026	1:15:00	7.42	2.2826	0	129721.4	ON	12.6	136
6/5/2026	1:30:00	7.43	1.6354	0	129753.9	ON	12.7	136
6/5/2026	1:45:00	7.41	0.8410	0	129771.8	ON	13.4	135
6/5/2026	2:00:00	7.39	0.3372	0	129778.4	ON	15.8	133
6/5/2026	2:15:00	7.35	0.4030	0	129784.7	ON	17.1	134
6/5/2026	2:30:00	7.4	2.2516	0	129801.3	ON	12.8	135
6/5/2026	2:45:00	7.41	2.2400	0	129835.3	ON	12.2	136
6/5/2026	3:00:00	7.4	1.1820	0	129856.2	ON	12.7	135
6/5/2026	3:15:00	7.4	0.6317	0	129874.0	ON	12.6	135
6/5/2026	3:30:00	7.39	0.3643	0	129880.3	ON	13.9	134
6/5/2026	3:45:00	7.34	0.7441	0	129887.2	ON	14.3	136
6/5/2026	4:00:00	7.41	2.2167	0	129916.3	ON	12.1	136
6/5/2026	4:15:00	7.4	2.1896	0	129947.9	ON	12	136
6/5/2026	4:30:00	7.39	0.4185	0	129960.8	ON	12.7	135
6/5/2026	4:45:00	7.37	1.0502	0	129969.5	ON	12.6	134
6/5/2026	5:00:00	7.4	2.1470	0	129989.0	ON	12.2	136
6/5/2026	5:15:00	7.4	0.9844	0	130016.3	ON	12	136
6/5/2026	5:30:00	7.4	0.3178	0	130023.4	ON	12.8	134
6/5/2026	5:45:00	7.38	0.3759	0	130028.5	ON	13.5	134
6/5/2026	6:00:00	7.4	2.2439	0	130043.9	ON	12.1	136
6/5/2026	6:15:00	7.4	2.2167	0	130078.0	ON	11.9	137
6/5/2026	6:30:00	7.4	2.1896	0	130109.5	ON	11.9	137
6/5/2026	6:45:00	7.4	0.9689	0	130135.9	ON	12	137
6/5/2026	7:00:00	7.39	0.2674	0	130142.4	ON	12.9	136
6/5/2026	7:15:00	7.35	0.3217	0	130145.9	ON	13.5	135
6/5/2026	7:30:00	7.38	1.4068	0	130158.1	ON	12.2	136
6/5/2026	7:45:00	7.37	1.4959	0	130177.3	ON	12.2	136



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	8:00:00	7.39	1.5114	0	130209.4	ON	12	136
6/5/2026	8:15:00	7.39	0.3333	0	130220.2	ON	12.7	136
6/5/2026	8:30:00	7.36	0.3449	0	130225.4	ON	13.3	135
6/5/2026	8:45:00	7.39	2.1974	0	130242.8	ON	12.4	136
6/5/2026	9:00:00	7.39	2.1664	0	130272.8	ON	12.4	136
6/5/2026	9:15:00	7.39	2.1431	0	130303.5	ON	12.4	135
6/5/2026	9:30:00	7.38	0.4185	0	130316.6	ON	14.2	133
6/5/2026	9:45:00	7.34	0.2945	0	130320.7	ON	18.3	133
6/5/2026	10:00:00	7.36	2.1509	0	130332.9	ON	13.3	132
6/5/2026	10:15:00	7.38	2.1354	0	130360.7	ON	12.6	135
6/5/2026	10:30:00	7.38	1.1704	0	130382.8	ON	12.8	134
6/5/2026	10:45:00	7.38	0.6588	0	130396.0	ON	12.8	134
6/5/2026	11:00:00	7.32	0.2364	0	130400.4	ON	26.1	117
6/5/2026	11:15:00	7.34	0.2713	523	130403.8	ON	15.7	0
6/5/2026	11:30:00	6.93	0.1938	750	130413.7	ON	16.2	0
6/5/2026	11:45:00	6.45	0.2015	1	130417.1	ON	18.7	0
6/5/2026	12:00:00	7.4	2.2516	0	130448.0	ON	12.3	158
6/5/2026	12:15:00	7.42	2.2129	0	130482.0	ON	12.2	159
6/5/2026	12:30:00	7.43	2.1819	0	130513.5	ON	12.2	159
6/5/2026	12:45:00	7.43	0.7441	0	130538.0	ON	12.3	159
6/5/2026	13:00:00	7.44	0.2597	0	130543.2	ON	13.3	157
6/5/2026	13:15:00	7.41	2.0113	0	130551.1	ON	12.5	159
6/5/2026	13:30:00	7.43	1.1859	0	130565.4	ON	12.3	159
6/5/2026	13:45:00	7.43	2.1160	0	130594.7	ON	12	160
6/5/2026	14:00:00	7.43	2.0811	0	130625.4	ON	12	160
6/5/2026	14:15:00	7.43	1.2440	0	130650.6	ON	12	159
6/5/2026	14:30:00	7.47	0.3604	0	130661.6	ON	12.3	159
6/5/2026	14:45:00	7.44	0.1589	0	130665.0	ON	13	158
6/5/2026	15:00:00	7.44	0.9146	0	130670.4	ON	12.5	159
6/5/2026	15:15:00	7.44	1.9842	0	130696.5	ON	11.9	161
6/5/2026	15:30:00	7.44	1.9532	0	130724.8	ON	11.9	161
6/5/2026	15:45:00	7.44	1.9261	0	130751.9	ON	12	161



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/5/2026	16:00:00	7.44	0.8526	0	130772.6	ON	12.2	160
6/5/2026	16:15:00	7.47	0.0000	0	130794.6	ON	12.3	160
6/5/2026	16:30:00	7.45	0.0000	0	130794.6	ON	13	159
6/5/2026	16:45:00	7.44	0.0000	0	130794.6	ON	12.6	161
6/5/2026	17:00:00	7.43	1.1355	0	130813.7	ON	12.4	161
6/5/2026	17:15:00	7.43	1.1006	0	130832.4	ON	12.6	159
6/5/2026	17:30:00	7.41	2.1780	0	130858.4	ON	12.4	159
6/5/2026	17:45:00	7.41	1.2208	0	130878.1	ON	12.4	160
6/5/2026	18:00:00	7.43	0.3720	0	130889.0	ON	12.9	159
6/5/2026	18:15:00	7.4	2.1276	0	130900.5	ON	12.5	159
6/5/2026	18:30:00	7.42	2.1160	0	130931.1	ON	12.3	160
6/5/2026	18:45:00	7.42	2.1005	0	130961.8	ON	12.2	160
6/5/2026	19:00:00	7.42	1.2053	0	130988.0	ON	12.2	159
6/5/2026	19:15:00	7.45	0.4185	0	130998.8	ON	12.3	159
6/5/2026	19:30:00	7.45	0.3837	0	131005.6	ON	12.9	158
6/5/2026	19:45:00	7.44	0.3604	0	131012.4	ON	13.2	159
6/5/2026	20:00:00	7.43	2.0850	0	131032.0	ON	12	160
6/5/2026	20:15:00	7.42	0.7635	0	131050.0	ON	12	160
6/5/2026	20:30:00	7.42	1.2169	0	131062.9	ON	11.9	159
6/5/2026	20:45:00	7.42	2.2167	0	131083.3	ON	11.8	161
6/5/2026	21:00:00	7.43	0.5736	0	131102.3	ON	11.8	160
6/5/2026	21:15:00	7.43	0.3527	0	131106.9	ON	12.2	159
6/5/2026	21:30:00	7.42	1.8912	0	131121.8	ON	11.7	161
6/5/2026	21:45:00	7.42	1.8602	0	131149.0	ON	11.7	161
6/5/2026	22:00:00	7.41	1.8098	0	131175.3	ON	11.6	160
6/5/2026	22:15:00	7.43	0.1744	0	131187.5	ON	11.8	160
6/5/2026	22:30:00	7.42	0.2170	0	131190.9	ON	12.6	159
6/5/2026	22:45:00	7.41	0.3062	0	131193.9	ON	14.2	158
6/5/2026	23:00:00	7.41	1.2711	0	131212.3	ON	11.8	159
6/5/2026	23:15:00	7.41	1.8059	0	131237.1	ON	11.7	159
6/5/2026	23:30:00	7.4	1.9183	0	131263.6	ON	11.8	159
6/5/2026	23:45:00	7.38	1.5967	0	131290.8	ON	11.9	161



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	0:00:00	7.4	0.2170	0	131300.5	ON	13.7	159
6/6/2026	0:15:00	7.38	0.1046	0	131302.5	ON	14.8	159
6/6/2026	0:30:00	7.38	0.6937	0	131310.5	ON	12.5	161
6/6/2026	0:45:00	7.39	1.8718	0	131331.0	ON	12.3	161
6/6/2026	1:00:00	7.4	1.8524	0	131358.2	ON	12.2	160
6/6/2026	1:15:00	7.4	1.4145	0	131382.6	ON	12.4	160
6/6/2026	1:30:00	7.41	0.0504	0	131391.6	ON	13.4	159
6/6/2026	1:45:00	7.39	0.3062	0	131393.2	ON	14	161
6/6/2026	2:00:00	7.4	1.4184	0	131408.8	ON	12.2	160
6/6/2026	2:15:00	7.41	2.0191	0	131435.7	ON	13.5	158
6/6/2026	2:30:00	7.38	0.2635	0	131450.1	ON	14.2	160
6/6/2026	2:45:00	7.37	0.2519	0	131453.5	ON	14.9	161
6/6/2026	3:00:00	7.39	1.4494	0	131464.0	ON	12.4	159
6/6/2026	3:15:00	7.39	1.8369	0	131490.0	ON	12.1	158
6/6/2026	3:30:00	7.39	1.8098	0	131512.9	ON	12.2	158
6/6/2026	3:45:00	7.42	0.0543	0	131530.6	ON	13.4	157
6/6/2026	4:00:00	7.4	0.1938	0	131532.2	ON	14.6	157
6/6/2026	4:15:00	7.39	0.1744	0	131535.6	ON	15.2	159
6/6/2026	4:30:00	7.39	0.9030	1	131542.4	ON	12.2	159
6/6/2026	4:45:00	7.4	1.7594	0	131566.8	ON	11.9	160
6/6/2026	5:00:00	7.4	1.7362	0	131593.1	ON	11.8	159
6/6/2026	5:15:00	7.41	1.8176	0	131618.3	ON	11.8	161
6/6/2026	5:30:00	7.4	1.2208	0	131644.0	ON	12.2	160
6/6/2026	5:45:00	7.41	1.5153	0	131668.1	ON	11.9	160
6/6/2026	6:00:00	7.42	0.1666	0	131679.5	ON	12.8	157
6/6/2026	6:15:00	7.41	1.5502	0	131688.5	ON	11.9	160
6/6/2026	6:30:00	7.41	1.8447	0	131715.6	ON	11.6	161
6/6/2026	6:45:00	7.42	1.4029	0	131741.9	ON	11.6	161
6/6/2026	7:00:00	7.41	1.7633	0	131767.4	ON	11.6	161
6/6/2026	7:15:00	7.43	2.1237	0	131791.6	ON	11.9	161
6/6/2026	7:30:00	7.41	1.9493	0	131821.5	ON	14	159
6/6/2026	7:45:00	7.4	0.1163	0	131834.9	ON	14	157



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	8:00:00	7.39	0.0698	0	131834.9	ON	15.7	158
6/6/2026	8:15:00	7.38	0.8138	0	131838.5	ON	12.8	159
6/6/2026	8:30:00	7.39	0.8448	0	131848.9	ON	12.7	161
6/6/2026	8:45:00	7.37	1.4765	0	131865.6	ON	12.2	161
6/6/2026	9:00:00	7.37	2.0307	0	131889.7	ON	14.8	158
6/6/2026	9:15:00	7.35	1.9067	0	131918.7	ON	19.1	159
6/6/2026	9:30:00	7.33	1.7982	0	131944.5	ON	21.1	160
6/6/2026	9:45:00	7.32	1.8718	0	131971.8	ON	21.2	161
6/6/2026	10:00:00	7.3	0.2325	0	131984.5	ON	20.9	161
6/6/2026	10:15:00	7.28	0.1976	0	131987.9	ON	20.8	161
6/6/2026	10:30:00	7.33	1.5308	8	131994.7	ON	13.9	156
6/6/2026	10:45:00	7.35	1.2324	0	132016.9	ON	12.5	159
6/6/2026	11:00:00	7.37	1.3486	0	132036.0	ON	12.7	159
6/6/2026	11:15:00	7.35	0.2364	0	132042.7	ON	15.2	157
6/6/2026	11:30:00	7.33	0.2558	0	132046.1	ON	17.1	157
6/6/2026	11:45:00	7.32	0.9921	0	132051.3	ON	14	157
6/6/2026	12:00:00	7.34	1.1587	0	132071.2	ON	12.8	160
6/6/2026	12:15:00	7.35	0.4147	0	132083.5	ON	13.6	159
6/6/2026	12:30:00	7.36	1.9222	0	132100.8	ON	12.6	160
6/6/2026	12:45:00	7.37	1.8912	0	132126.6	ON	12.6	160
6/6/2026	13:00:00	7.37	1.8563	0	132150.3	ON	12.7	161
6/6/2026	13:15:00	7.39	0.6162	0	132169.8	ON	12.9	160
6/6/2026	13:30:00	7.38	0.2829	0	132173.7	ON	14.7	158
6/6/2026	13:45:00	7.38	1.3138	0	132185.8	ON	13.1	160
6/6/2026	14:00:00	7.39	1.2208	0	132208.1	ON	12.9	160
6/6/2026	14:15:00	7.4	1.7556	0	132232.0	ON	12.7	160
6/6/2026	14:30:00	7.4	1.7401	0	132259.3	ON	12.6	160
6/6/2026	14:45:00	7.41	1.7246	0	132282.8	ON	12.6	160
6/6/2026	15:00:00	7.43	0.3372	0	132296.9	ON	12.9	161
6/6/2026	15:15:00	7.41	0.1744	0	132300.3	ON	13.8	159
6/6/2026	15:30:00	7.39	0.1705	0	132303.7	ON	14.5	158
6/6/2026	15:45:00	7.38	0.8913	0	132310.0	ON	13.4	159



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/6/2026	16:00:00	7.37	1.7168	0	132330.9	ON	12.7	159
6/6/2026	16:15:00	7.38	1.7749	0	132355.1	ON	12.6	160
6/6/2026	16:30:00	7.41	0.2635	0	132378.6	ON	12.8	159
6/6/2026	16:45:00	7.39	0.3062	0	132382.0	ON	13.8	158
6/6/2026	17:00:00	7.4	0.6549	0	132401.3	ON	12.9	159
6/6/2026	17:15:00	7.38	1.0812	0	132408.8	ON	13.2	159
6/6/2026	17:30:00	7.39	1.4184	0	132427.2	ON	12.8	160
6/6/2026	17:45:00	7.4	2.0772	0	132454.1	ON	13.3	162
6/6/2026	18:00:00	7.39	1.9648	0	132484.2	ON	13.9	161
6/6/2026	18:15:00	7.38	2.0385	0	132512.9	ON	14.3	162
6/6/2026	18:30:00	7.37	0.0000	0	132540.4	ON	14.8	162
6/6/2026	18:45:00	7.36	0.1046	0	132540.4	ON	15.1	162
6/6/2026	19:00:00	7.46	1.7556	0	132559.5	ON	13.3	156
6/6/2026	19:15:00	7.48	1.7207	0	132585.0	ON	13.2	155
6/6/2026	19:30:00	7.49	1.6587	0	132607.6	ON	13.1	154
6/6/2026	19:45:00	7.5	1.6199	0	132631.4	ON	13	155
6/6/2026	20:00:00	7.5	1.5695	0	132655.3	ON	13	155
6/6/2026	20:15:00	7.51	1.4998	0	132676.2	ON	13	154
6/6/2026	20:30:00	7.51	1.8834	0	132697.2	ON	13	154
6/6/2026	20:45:00	7.52	1.7672	0	132724.4	ON	13.2	154
6/6/2026	21:00:00	7.52	1.5657	0	132749.2	ON	13.3	154
6/6/2026	21:15:00	7.5	0.5736	0	132758.5	ON	13.6	154
6/6/2026	21:30:00	7.5	1.2130	0	132776.6	ON	13.8	154
6/6/2026	21:45:00	7.49	1.7711	0	132801.0	ON	14	154
6/6/2026	22:00:00	7.46	1.4882	0	132827.6	ON	14.6	154
6/6/2026	22:15:00	7.46	0.1976	0	132844.0	ON	15.3	155
6/6/2026	22:30:00	7.43	0.2519	0	132845.5	ON	15.8	155
6/6/2026	22:45:00	7.42	0.2597	0	132848.9	ON	16.3	154
6/6/2026	23:00:00	7.41	1.4727	0	132863.5	ON	17.4	154
6/6/2026	23:15:00	7.39	1.7129	0	132887.3	ON	17.9	155
6/6/2026	23:30:00	7.37	1.7013	0	132903.8	ON	18.1	155
6/6/2026	23:45:00	7.36	1.1122	0	132931.2	ON	18.3	155



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	0:00:00	7.33	1.2905	0	132951.0	ON	18.5	155
6/7/2026	0:15:00	7.32	0.9572	0	132973.6	ON	18.8	155
6/7/2026	0:30:00	7.3	0.1976	0	132981.8	ON	20.4	155
6/7/2026	0:45:00	7.29	0.1705	0	132985.3	ON	20.9	155
6/7/2026	1:00:00	7.26	0.1821	0	132988.7	ON	21.3	156
6/7/2026	1:15:00	7.25	1.1587	0	132996.8	ON	21.2	157
6/7/2026	1:30:00	7.25	1.5967	0	133017.7	ON	20.5	157
6/7/2026	1:45:00	7.24	1.1742	0	133037.6	ON	19.5	157
6/7/2026	2:00:00	7.22	1.1510	0	133050.5	ON	18.8	157
6/7/2026	2:15:00	7.21	1.5230	0	133070.8	ON	18.1	157
6/7/2026	2:30:00	7.2	1.3680	0	133093.8	ON	17.5	156
6/7/2026	2:45:00	7.2	1.5889	0	133112.7	ON	17	156
6/7/2026	3:00:00	7.2	1.5928	0	133138.0	ON	16.6	156
6/7/2026	3:15:00	7.19	1.3060	0	133153.9	ON	16.3	156
6/7/2026	3:30:00	7.18	1.2401	0	133172.7	ON	16.2	156
6/7/2026	3:45:00	7.17	1.3409	0	133192.7	ON	16.1	155
6/7/2026	4:00:00	7.16	1.3254	0	133212.9	ON	16.1	156
6/7/2026	4:15:00	7.15	0.1124	0	133223.9	ON	17.7	155
6/7/2026	4:30:00	7.14	0.1085	0	133223.9	ON	18.6	156
6/7/2026	4:45:00	7.13	0.5891	0	133229.9	ON	20.2	156
6/7/2026	5:00:00	7.12	1.4068	0	133246.4	ON	21.9	157
6/7/2026	5:15:00	7.1	0.7712	0	133261.5	ON	23.3	157
6/7/2026	5:30:00	7.49	1.2595	0	133276.7	ON	13.8	146
6/7/2026	5:45:00	7.49	1.2053	0	133293.8	ON	12.7	148
6/7/2026	6:00:00	7.49	0.9417	0	133309.2	ON	12.5	150
6/7/2026	6:15:00	7.49	1.2440	0	133326.0	ON	12.8	149
6/7/2026	6:30:00	7.49	1.6432	0	133347.7	ON	12.4	150
6/7/2026	6:45:00	7.52	1.7904	0	133371.1	ON	13.3	147
6/7/2026	7:00:00	7.54	0.4534	0	133391.2	ON	12.8	151
6/7/2026	7:15:00	7.49	1.9997	0	133420.7	ON	13.3	150
6/7/2026	7:30:00	7.47	0.0000	0	133445.2	ON	13.9	150
6/7/2026	7:45:00	7.47	0.1008	0	133445.2	ON	14.3	151



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	8:00:00	7.46	0.1240	0	133446.5	ON	14.5	151
6/7/2026	8:15:00	7.45	0.2015	0	133449.9	ON	14.8	151
6/7/2026	8:30:00	7.44	0.2093	0	133453.3	ON	15.2	151
6/7/2026	8:45:00	7.43	0.0000	0	133455.4	ON	15.5	151
6/7/2026	9:00:00	7.42	0.2170	0	133457.9	ON	15.6	151
6/7/2026	9:15:00	7.49	0.0000	0	133475.1	ON	12.9	150
6/7/2026	9:30:00	7.48	1.3254	0	133489.2	ON	12.3	150
6/7/2026	9:45:00	7.5	1.9067	0	133513.3	ON	12.2	152
6/7/2026	10:00:00	7.52	1.8602	0	133540.5	ON	12.2	152
6/7/2026	10:15:00	7.52	0.4961	0	133556.2	ON	12.4	152
6/7/2026	10:30:00	7.51	0.2790	0	133560.0	ON	13.4	151
6/7/2026	10:45:00	7.51	1.6819	0	133577.9	ON	12.5	152
6/7/2026	11:00:00	7.53	1.8176	0	133605.1	ON	12.4	153
6/7/2026	11:15:00	7.53	0.8681	0	133628.3	ON	12.5	152
6/7/2026	11:30:00	7.53	0.2286	0	133634.1	ON	13.4	150
6/7/2026	11:45:00	7.52	0.2442	0	133637.5	ON	14	150
6/7/2026	12:00:00	7.49	1.1549	0	133647.9	ON	12.8	152
6/7/2026	12:15:00	7.52	0.0000	0	133657.5	ON	13	151
6/7/2026	12:30:00	7.5	0.4108	0	133661.3	ON	13.2	152
6/7/2026	12:45:00	7.52	1.9338	0	133674.2	ON	12.6	151
6/7/2026	13:00:00	7.53	1.8834	0	133700.5	ON	12.4	151
6/7/2026	13:15:00	7.54	1.4727	0	133723.6	ON	12.4	150
6/7/2026	13:30:00	7.54	1.4455	0	133741.9	ON	12.5	150
6/7/2026	13:45:00	7.55	0.0000	0	133751.7	ON	13.1	148
6/7/2026	14:00:00	7.54	0.5968	1	133754.6	ON	12.9	150
6/7/2026	14:15:00	7.53	1.5812	2	133765.1	ON	12.9	151
6/7/2026	14:30:00	7.55	0.2519	0	133777.8	ON	13.4	150
6/7/2026	14:45:00	7.54	1.1975	4	133792.1	ON	12.8	154
6/7/2026	15:00:00	7.56	0.6278	1	133809.0	ON	12.7	154
6/7/2026	15:15:00	7.56	0.6549	0	133823.5	ON	12.8	154
6/7/2026	15:30:00	7.56	0.0000	0	133828.5	ON	13.3	152
6/7/2026	15:45:00	7.56	0.7673	0	133836.0	ON	13	153



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope


Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (C°)	Discharge Conductivity (uS/cm)
6/7/2026	16:00:00	7.56	0.9340	0	133854.0	ON	12.8	154
6/7/2026	16:15:00	7.56	0.0000	0	133856.7	ON	13.8	151
6/7/2026	16:30:00	7.55	1.1665	0	133874.1	ON	12.9	153
6/7/2026	16:45:00	7.56	1.6354	0	133895.2	ON	12.8	154
6/7/2026	17:00:00	7.56	1.2053	0	133918.1	ON	13	153
6/7/2026	17:15:00	7.57	0.0000	0	133935.4	ON	13.7	151
6/7/2026	17:30:00	7.55	0.2674	0	133936.0	ON	14.1	153
6/7/2026	17:45:00	7.53	1.5579	2	133943.2	ON	13.4	154
6/7/2026	18:00:00	7.55	1.7129	0	133967.1	ON	12.9	155
6/7/2026	18:15:00	7.57	1.9571	0	133991.9	ON	12.8	154
6/7/2026	18:30:00	7.57	1.0270	0	134017.1	ON	12.8	154
6/7/2026	18:45:00	7.57	0.1860	0	134024.4	ON	13.6	152
6/7/2026	19:00:00	7.55	0.2248	0	134027.8	ON	14.1	153
6/7/2026	19:15:00	7.54	1.4106	0	134032.5	ON	13.9	154
6/7/2026	19:30:00	7.53	0.9417	0	134053.9	ON	13.3	151
6/7/2026	19:45:00	7.54	1.1161	9	134074.5	ON	12.5	153
6/7/2026	20:00:00	7.56	0.0000	0	134081.0	ON	12.8	153
6/7/2026	20:15:00	7.54	0.9301	2	134084.9	ON	12.6	152
6/7/2026	20:30:00	7.56	1.8059	0	134107.4	ON	13.3	151
6/7/2026	20:45:00	7.54	0.2597	0	134113.5	ON	13.7	152
6/7/2026	21:00:00	7.52	0.3255	0	134116.9	ON	14	152
6/7/2026	21:15:00	7.56	1.9300	0	134132.6	ON	13.6	151
6/7/2026	21:30:00	7.55	1.8796	0	134161.1	ON	13.6	151
6/7/2026	21:45:00	7.53	1.9416	0	134170.4	ON	13.7	152
6/7/2026	22:00:00	7.51	1.9842	0	134200.8	ON	13.8	153
6/7/2026	22:15:00	7.5	0.0000	0	134214.5	ON	13.9	152
6/7/2026	22:30:00	7.49	0.0000	0	134214.5	ON	15.3	152
6/7/2026	22:45:00	7.53	2.0036	0	134233.8	ON	16.1	152
6/7/2026	23:00:00	7.51	1.7827	0	134262.0	ON	16.6	152
6/7/2026	23:15:00	7.54	1.3138	0	134281.0	ON	13.8	150
6/7/2026	23:30:00	7.56	0.5929	0	134306.2	ON	12.7	152
6/7/2026	23:45:00	7.54	0.7208	0	134307.5	ON	13.3	153


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

Appendix C: Photos

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

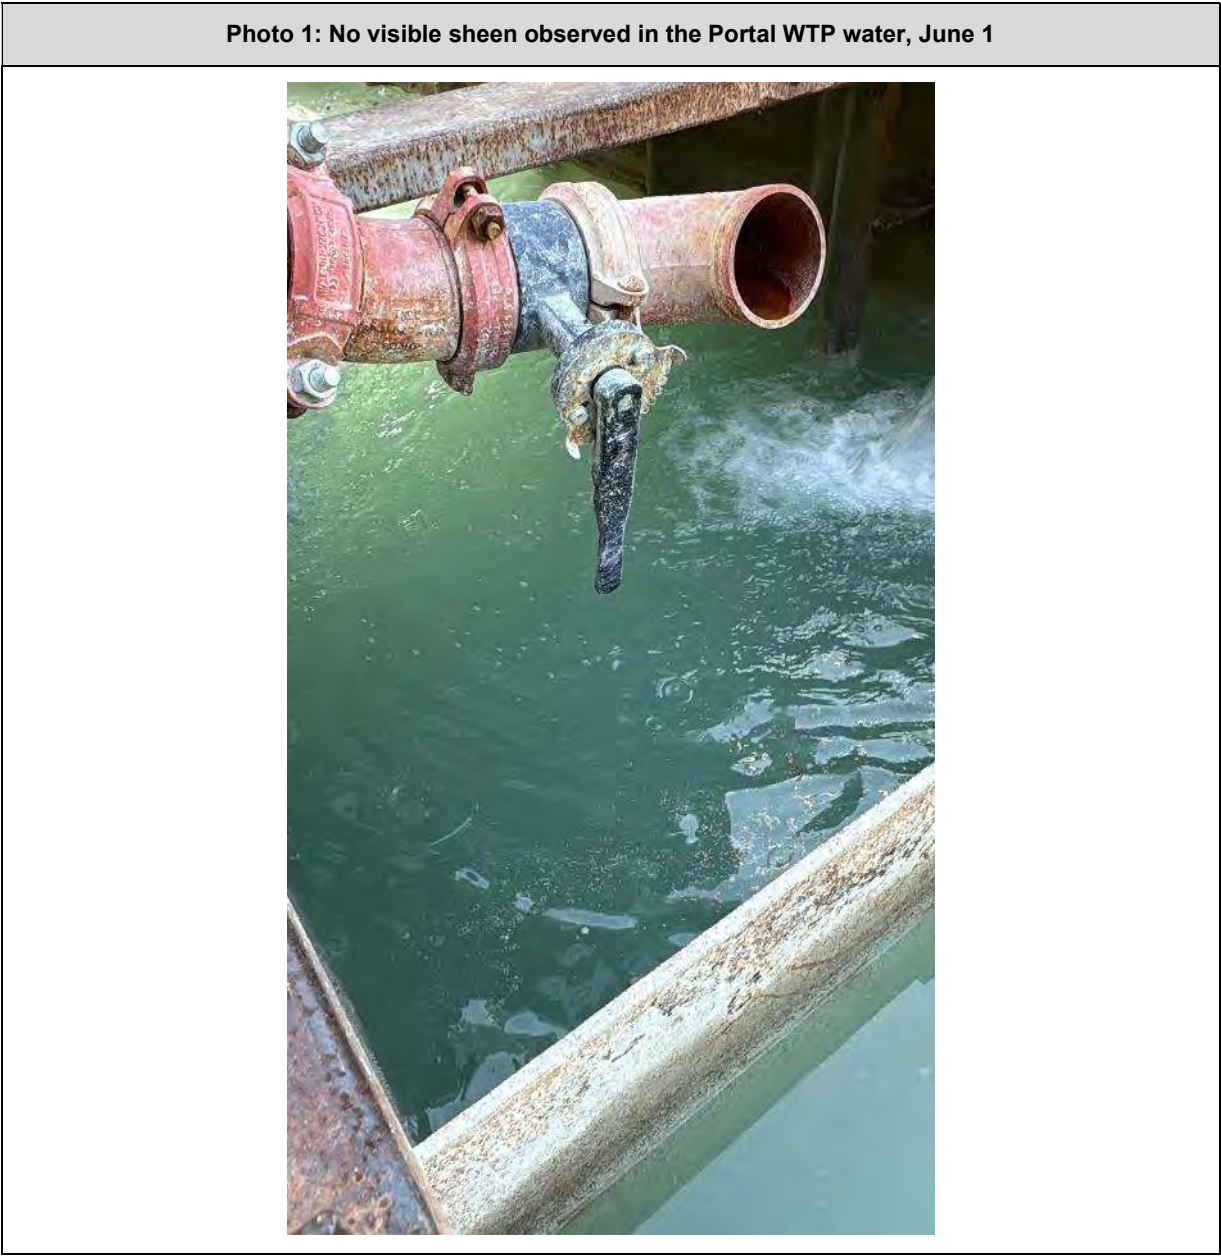

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

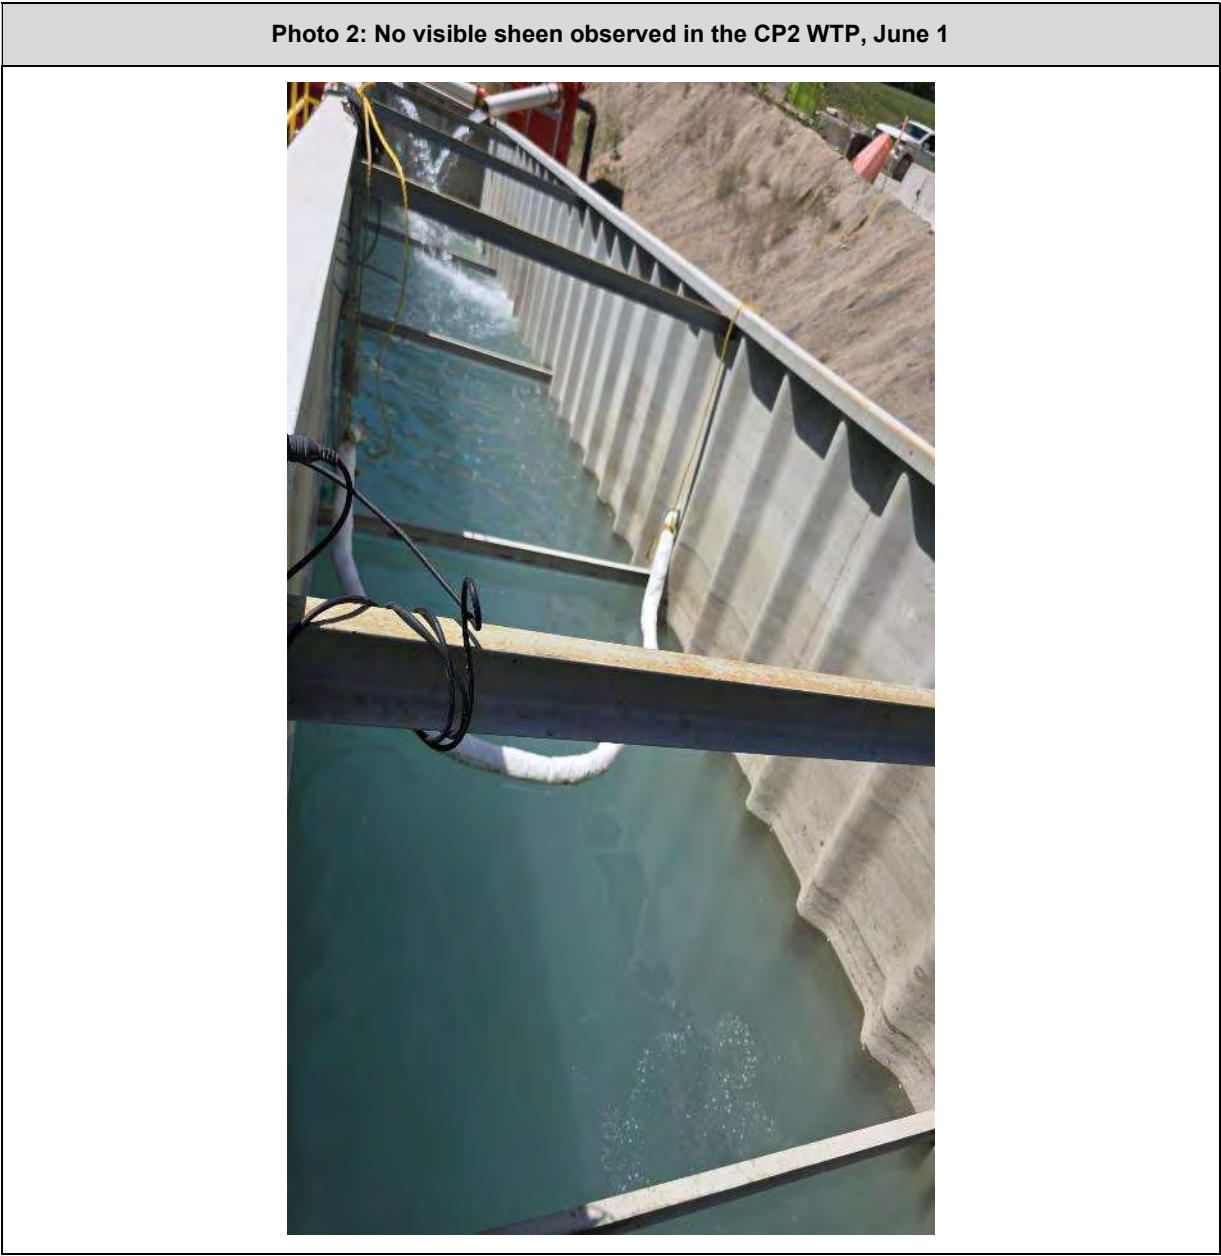



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Photo 3: No visible sheen observed in the Portal WTP water, June 2





Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Photo 4: No visible sheen observed in the CP2 WTP water, June 2



		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	






Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026


Photo 6: No visible sheen observed in the CP2 WTP water, June 3




		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

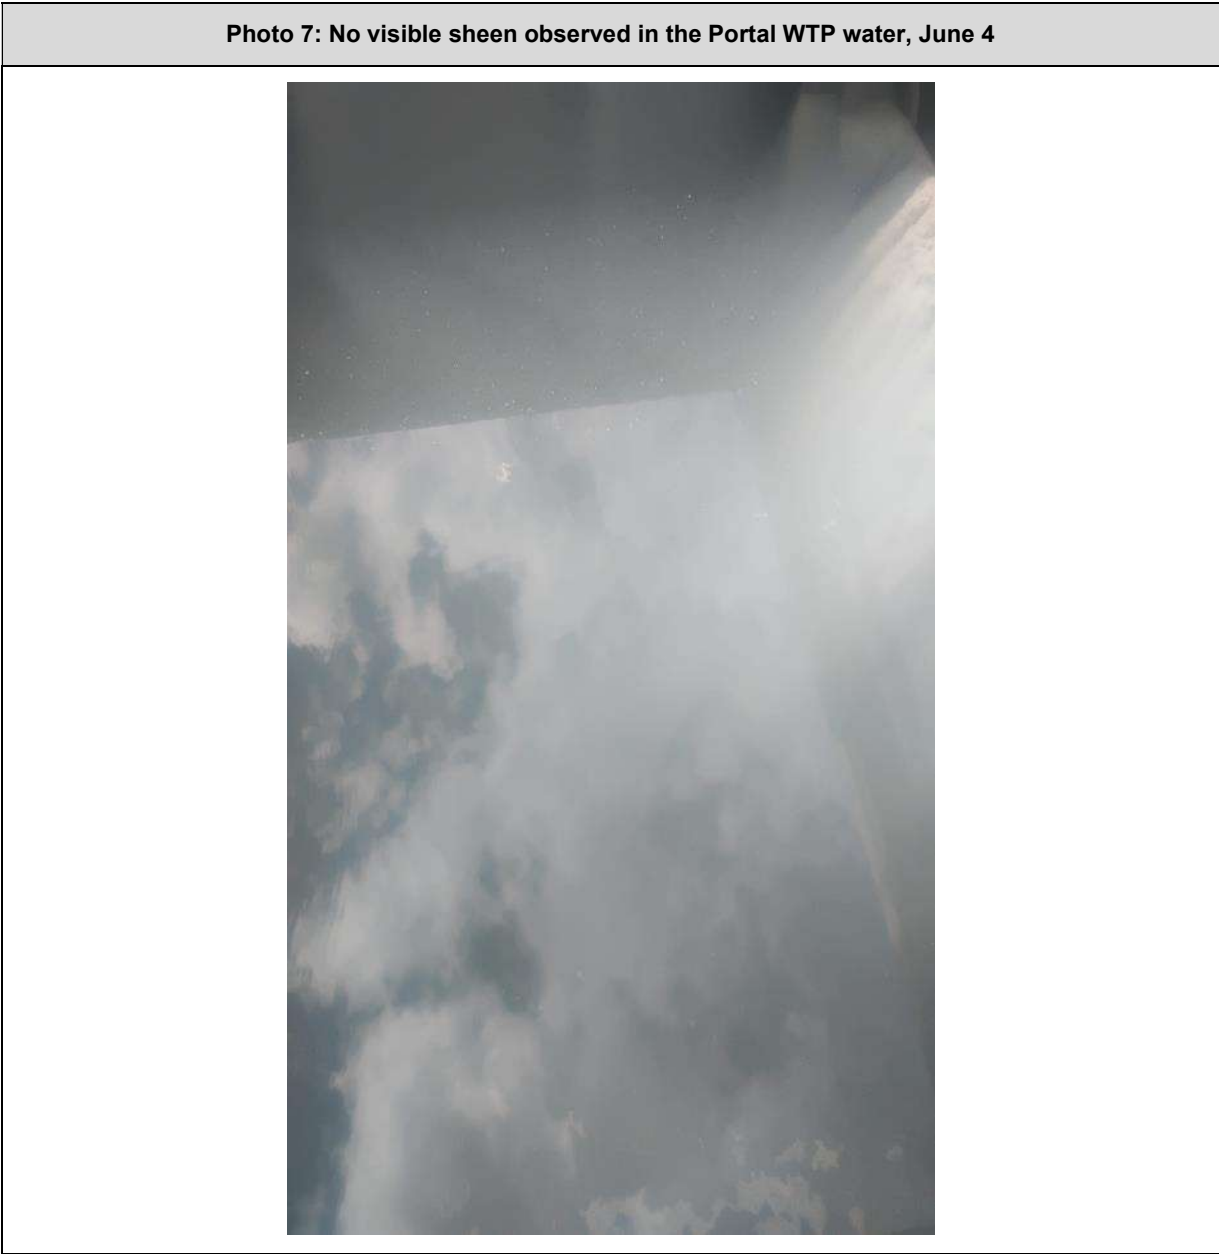

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

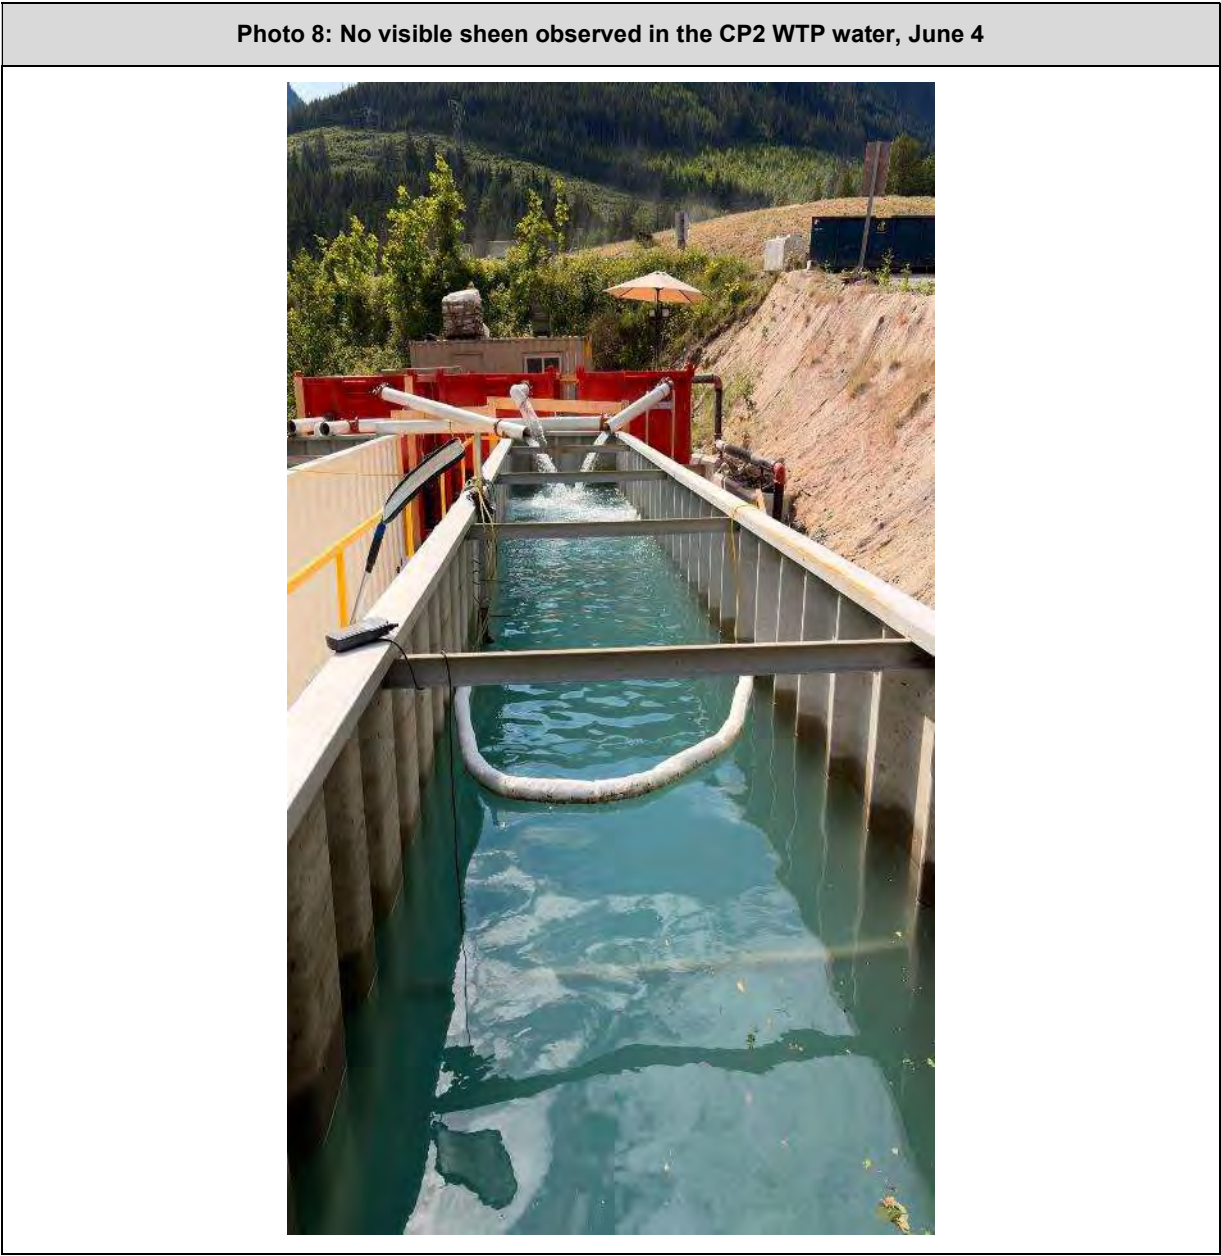

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

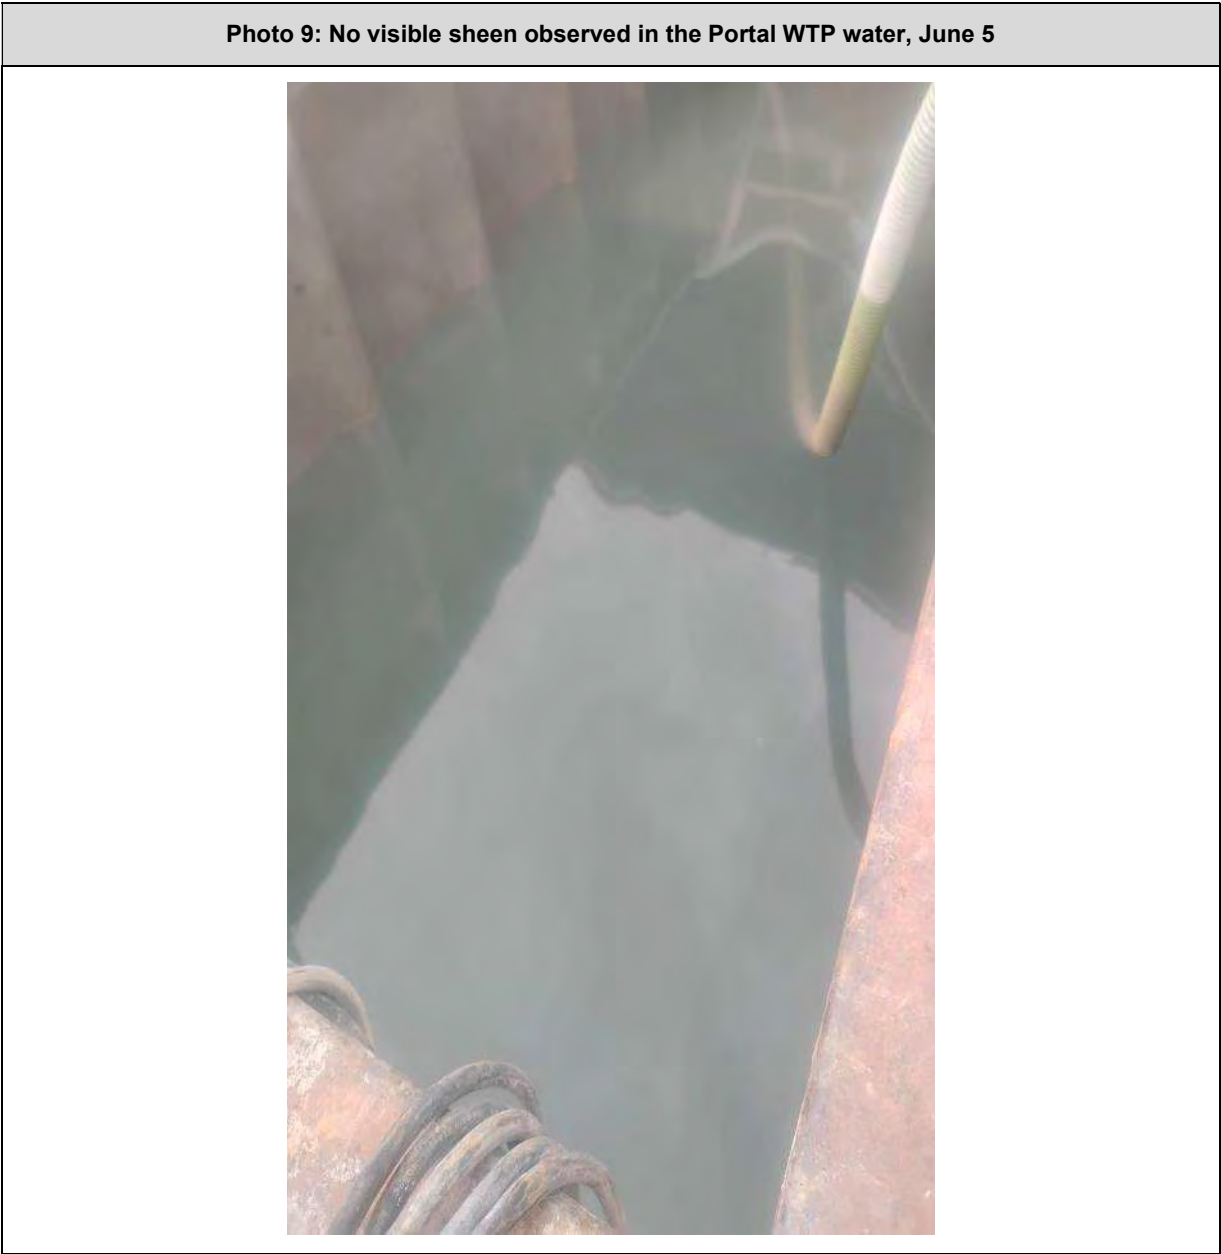




Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Photo 10: No visible sheen observed in the CP2 WTP water, June 5



		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: BC1 Approved by: BC2 Date: July 16, 2026	

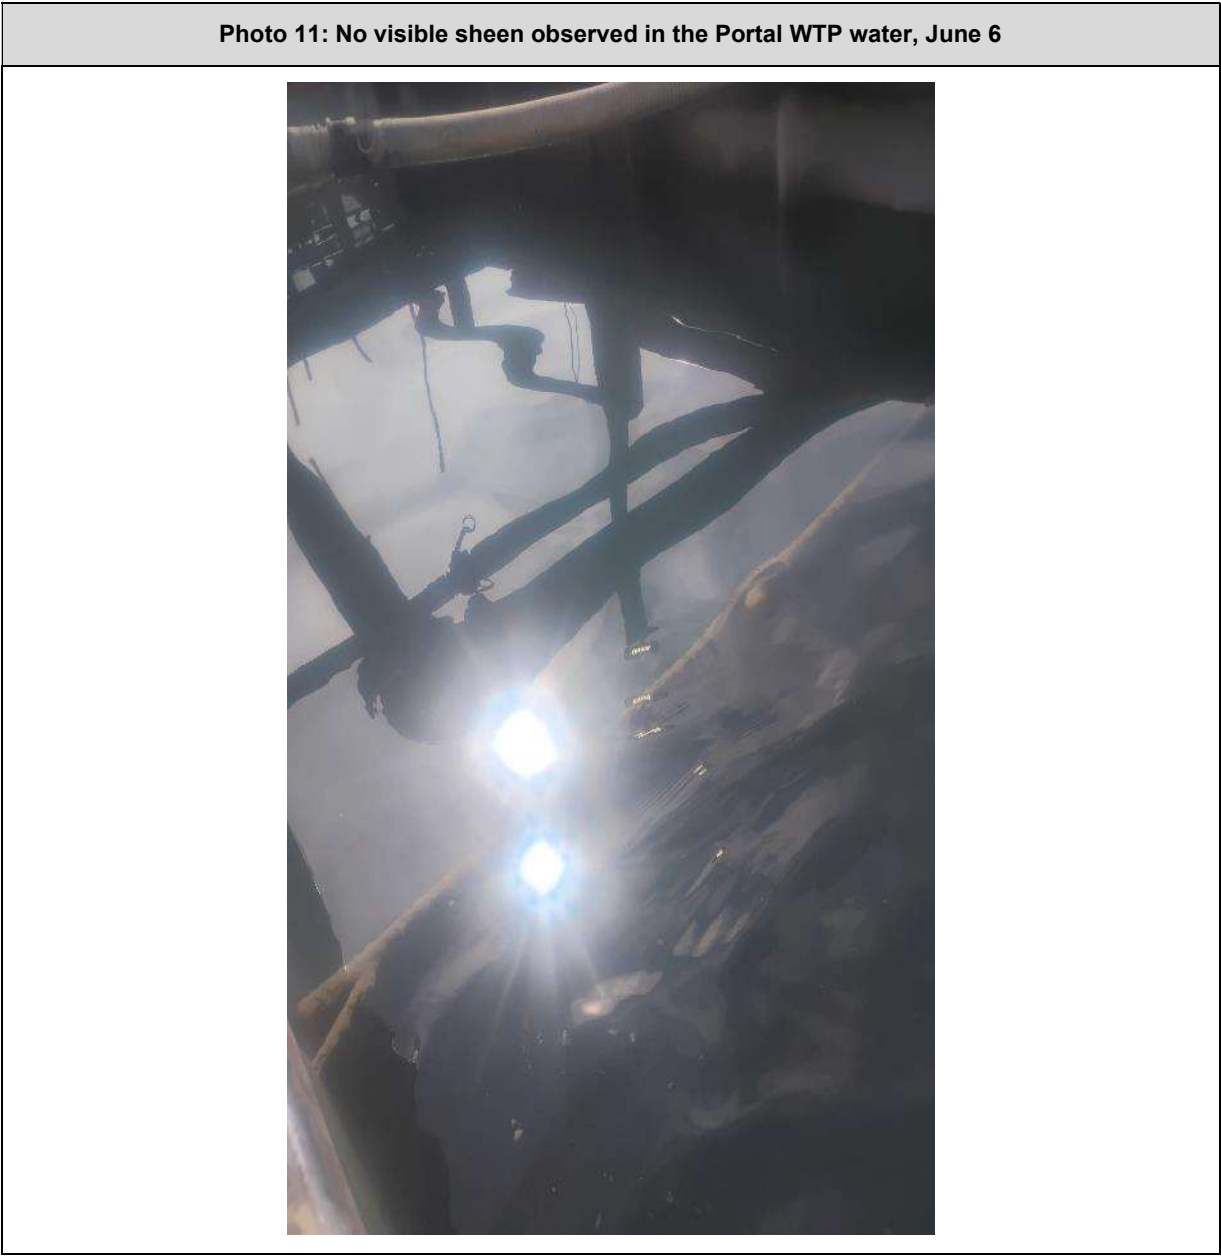





Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Photo 12: No visible sheen observed in the CP2 WTP water, June 6

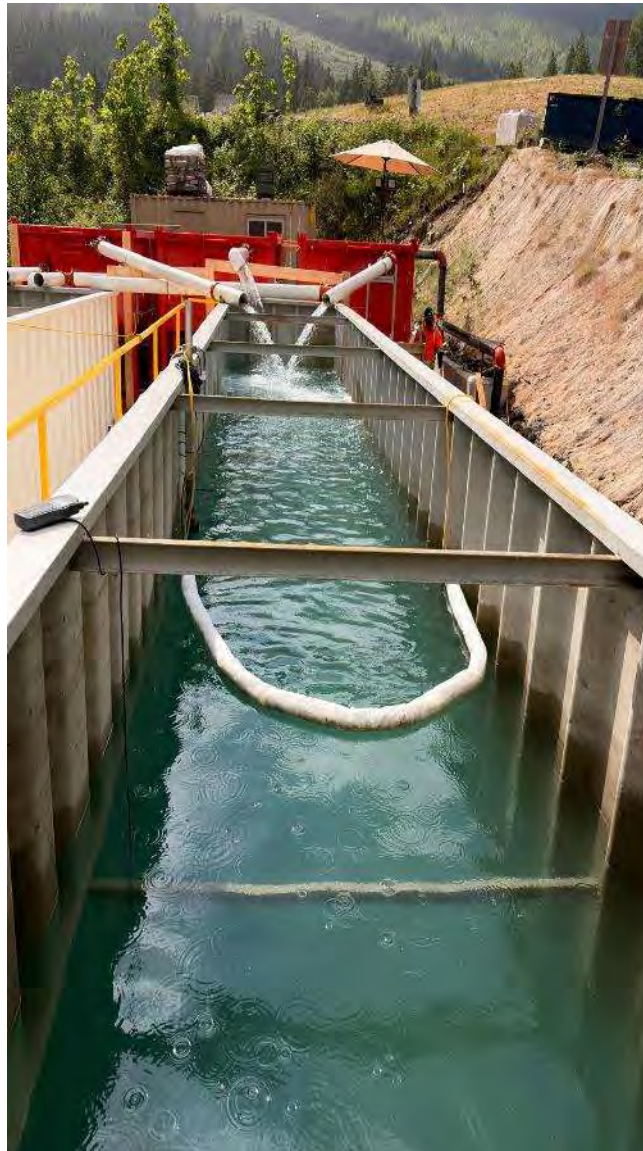

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

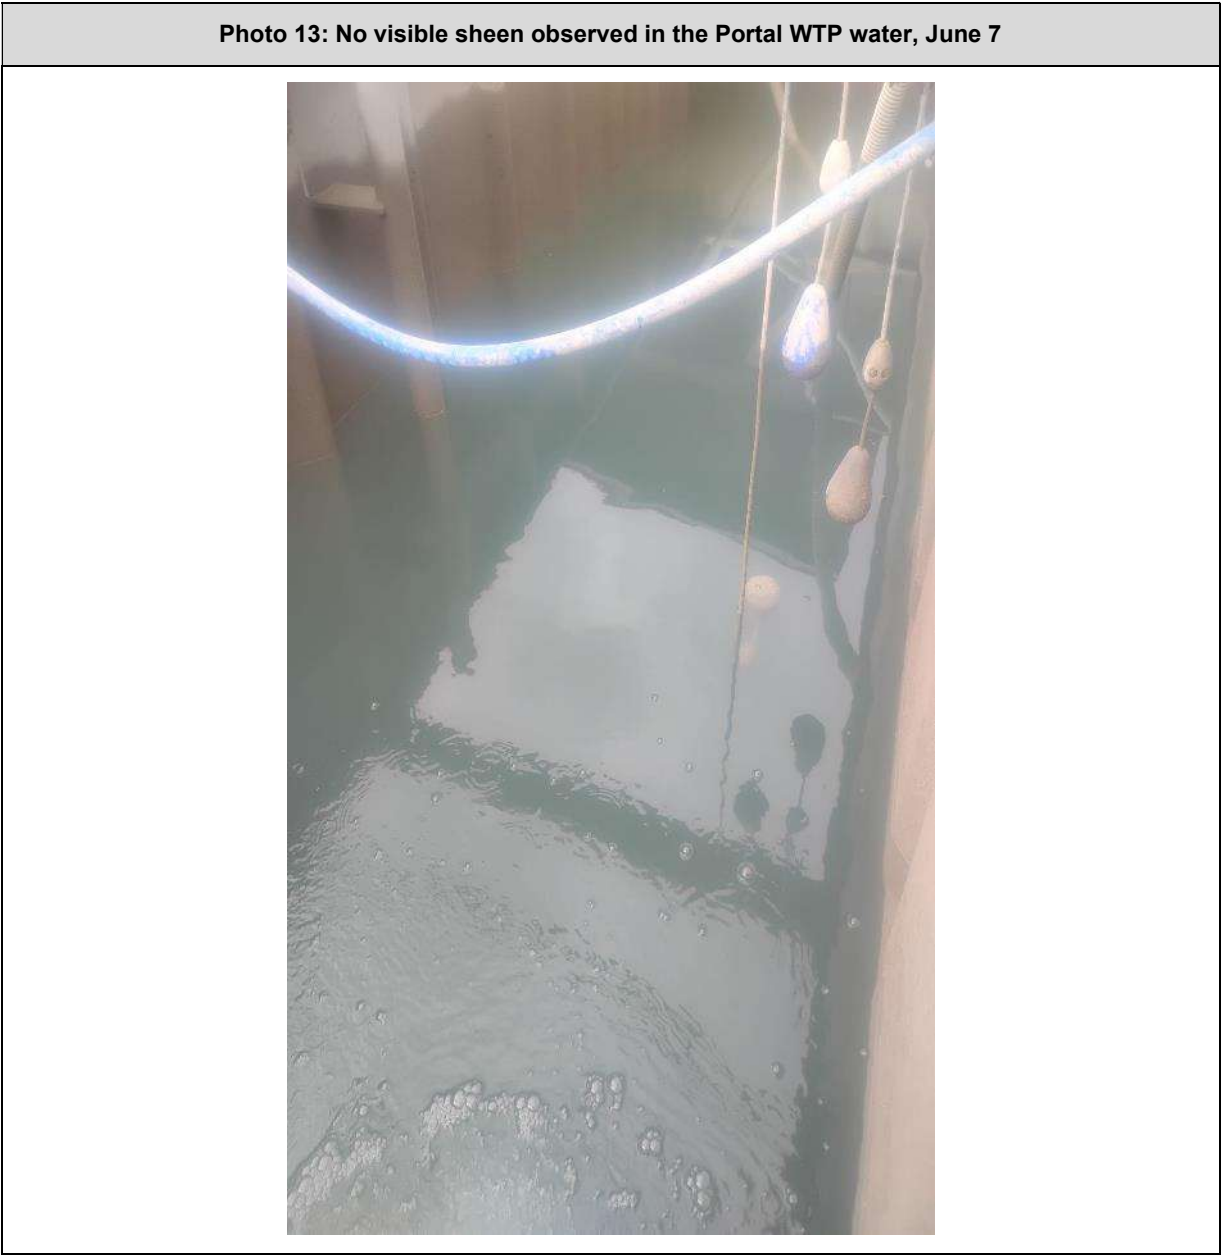



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	1
Data Range	June 1, 2026 to June 7, 2026	Prepared by: Approved by: Date:	BC1 BC2 July 16, 2026

Photo 14: No visible sheen observed in the CP2 WTP water, June 7



Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	<u>WLNG EOP</u>	Date:	<u>June 2, 2026</u>
Site Name:	<u>East Creek</u>	Time:	<u>10:00</u>
Crew:	<u>HM</u>		
Weather:	<u>Sun</u>		

In Situ Parameters

pH:	<u>7.28</u>	DO:	<u>4.5</u> (mg/L)
Temp:	<u>12.9</u> (°C)	Cond:	<u>207.4</u> (us/cm)
Turbidity:	<u>2.87</u> NTU	Salinity:	<u>0.1</u> (ppt)
		ORP:	<u>177.1</u> (mV)

Visible Sheen: N

Water Surface Condition: Clear

Photo Record



Observations

No issues observed, trip blank and field blank retrieved from lab during drop off - not completed in the field

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix D	D-1

Appendix D:
Woodfibre Site Receiving Environment
Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix D	D-2

Woodfibre Site Receiving Environment Sample Analysis



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-06-02 09:30:00	WLNG DS 2026-06-02 10:20:00
In situ Parameters									
Field pH	pH Units		6.5 - 9			7 - 8.7		7.2	7.4
Field Temperature	°C	18	19					12.1	12.5
General Parameters									
pH	pH Units							6.71	7.53
Alkalinity (Total as CaCO ₃)	mg/L							7.2	44
Alkalinity (PP as CaCO ₃)	mg/L							<1	<1
Hardness (CaCO ₃)-Total	mg/L							7.11	55.9
Hardness (CaCO ₃)-Dissolved	mg/L							7	56.8
Sulphide-Total	mg/L							<0.0018	<0.0018
Sulphide (as H ₂ S)	mg/L			0.002				<0.002	<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L							<0.0019	<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L							<0.0018	<0.0018
Anions and Nutrients									
Ammonia (N)-Total	mg/L	1.8	14		12	52		<0.015	<0.015
Bicarbonate (HCO ₃)	mg/L							8.8	53
Carbonate (CO ₃)	mg/L							<1	<1
Hydroxide (OH)	mg/L							<1	<1
Nitrate (N)	mg/L	3	32.8		3.7			<0.02	0.078
Nitrite (N)	mg/L	0.02	0.06					<0.005	<0.005
Nitrate plus Nitrite (N)	mg/L							<0.02	0.078
Nitrogen (N)-Total	mg/L							0.049	0.254
Phosphorus (P)-Total (4500-P)	mg/L							0.01	0.0037
Bromide (Br)	mg/L							<0.01	<0.01
Chloride (Cl)	mg/L	150	600					<1	12
Fluoride (F)	mg/L		0.4			1.5		<0.05	0.23
Sulphate (SO ₄)-Dissolved	mg/L	128						2.2	15
Total Metals									
Aluminum (Al)-Total	mg/L	0.0637229						0.04	0.073
Antimony (Sb)-Total	mg/L	0.074	0.25					<0.00002	0.000277
Arsenic (As)-Total	mg/L	0.005			0.0125			0.000083	0.000647
Barium (Ba)-Total	mg/L			1				0.00418	0.00483
Beryllium (Be)-Total	mg/L			0.00013			0.1	<0.00001	<0.00001
Bismuth (Bi)-Total	mg/L							<0.000005	<0.00001
Boron (B)-Total	mg/L	1.2			1.2			<0.01	<0.01
Cadmium (Cd)-Total	mg/L						0.00012	<0.000005	<0.000005
Calcium (Ca)-Total	mg/L							2.43	20.6
Cesium (Cs)-Total	mg/L							<0.00005	<0.00005
Chromium (Cr)-Total	mg/L							<0.0001	0.00036

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024)



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-06-02 09:30:00	WLNG DS 2026-06-02 10:20:00
Total Metals (cont'd.)									
Chromium (Cr III)-Total	mg/L			0.0089			0.056	<0.0099	<0.0099
Chromium (Cr VI)-Total	mg/L			0.0025			0.0015	<0.0099	<0.0099
Cobalt (Co)-Total	mg/L							0.0000161	0.000039
Copper (Cu)-Total	mg/L				0.002	0.003		0.000505	0.00017
Iron (Fe)-Total	mg/L	0.055	1					0.0283	0.026
Lead (Pb)-Total	mg/L				0.002	0.14		0.0000116	0.000021
Lithium (Li)-Total	mg/L							<0.0005	0.00412
Magnesium (Mg)-Total	mg/L							0.253	1.09
Manganese (Mn)-Total	mg/L						0.1	0.00105	0.0197
Mercury (Hg)-Total	mg/L	0.00002			0.0001			<0.0000019	<0.0000019
Molybdenum (Mo)-Total	mg/L	7.6	46					0.00038	0.0292
Nickel (Ni)-Total	mg/L						0.0083	0.0002	0.00013
Phosphorus (P)-Total (ICPMS)	mg/L							0.0067	<0.005
Potassium (K)-Total	mg/L							0.159	1.39
Rubidium (Rb)-Total	mg/L							0.000328	0.00318
Selenium (Se)-Total	mg/L	0.002			0.002			<0.00004	0.000051
Silicon (Si)-Total	mg/L							4.3	6.66
Silver (Ag)-Total	mg/L	0.00012			0.0005	0.0037	0.0005	<0.000005	<0.00001
Sodium (Na)-Total	mg/L							1.63	5.83
Strontium (Sr)-Total	mg/L							0.0134	0.0473
Sulphur (S)-Total	mg/L							<3	4.2
Tellurium (Te)-Total	mg/L							<0.00002	<0.00002
Thallium (Tl)-Total	mg/L			0.00003				<0.000002	0.0000083
Thorium (Th)-Total	mg/L							<0.00005	<0.00005
Tin (Sn)-Total	mg/L							<0.0002	<0.0002
Titanium (Ti)-Total	mg/L							<0.0005	<0.002
Uranium (U)-Total	mg/L		0.0165	0.0075				0.0000516	0.000266
Vanadium (V)-Total	mg/L			0.06			0.005	<0.0002	0.00022
Zinc (Zn)-Total	mg/L				0.01	0.055		0.00078	0.0016
Zirconium (Zr)-Total	mg/L							<0.0001	<0.0001
Dissolved Metals									
Aluminum (Al)-Dissolved	mg/L							0.0317	0.0414
Antimony (Sb)-Dissolved	mg/L							<0.00002	0.000258
Arsenic (As)-Dissolved	mg/L							0.000083	0.000624
Barium (Ba)-Dissolved	mg/L							0.00384	0.00433
Beryllium (Be)-Dissolved	mg/L							<0.00001	<0.00001
Bismuth (Bi)-Dissolved	mg/L							<0.000005	<0.000005
Boron (B)-Dissolved	mg/L							<0.01	<0.01

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024)



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-06-02 09:30:00	WLNG DS 2026-06-02 10:20:00
Dissolved Metals (cont'd.)									
Cadmium (Cd)-Dissolved	mg/L	0.0000302	0.0000386					<0.000005	<0.000005
Calcium (Ca)-Dissolved	mg/L							2.42	21
Cesium (Cs)-Dissolved	mg/L							<0.00005	<0.00005
Chromium (Cr)-Dissolved	mg/L							<0.0001	0.00014
Cobalt (Co)-Dissolved	mg/L	0.0003889						0.0000161	0.0000304
Copper (Cu)-Dissolved	mg/L	0.00022	0.00134					0.000453	0.000078
Iron (Fe)-Dissolved	mg/L							0.0194	0.0017
Lead (Pb)-Dissolved	mg/L	0.0014972						0.0000061	<0.000005
Lithium (Li)-Dissolved	mg/L							<0.0005	0.00319
Manganese (Mn)-Dissolved	mg/L	0.215	0.3267031					0.000715	0.018
Magnesium (Mg)-Dissolved	mg/L							0.231	1.07
Mercury (Hg)-Dissolved	mg/L							<0.0000019	<0.0000019
Molybdenum (Mo)-Dissolved	mg/L							0.000401	0.0281
Nickel (Ni)-Dissolved	mg/L	0.0006	0.0096					0.0002	0.00011
Phosphorus (P)-Dissolved	mg/L							0.0068	<0.002
Potassium (K)-Dissolved	mg/L							0.148	1.31
Rubidium (Rb)-Dissolved	mg/L							0.000299	0.00298
Selenium (Se)-Dissolved	mg/L							<0.00004	0.000052
Silicon (Si)-Dissolved	mg/L							4.38	6.62
Silver (Ag)-Dissolved	mg/L							<0.000005	<0.000005
Sodium (Na)-Dissolved	mg/L							1.48	5.99
Strontium (Sr)-Dissolved	mg/L			1.25				0.0124	0.0442
Sulphur (S)-Dissolved	mg/L							<3	4.6
Tellurium (Te)-Dissolved	mg/L							<0.00002	<0.00002
Thallium (Tl)-Dissolved	mg/L							<0.000002	0.0000043
Thorium (Th)-Dissolved	mg/L							<0.000005	<0.000005
Tin (Sn)-Dissolved	mg/L							<0.0002	<0.0002
Titanium (Ti)-Dissolved	mg/L							<0.0005	<0.0005
Uranium (U)-Dissolved	mg/L							0.0000421	0.000246
Vanadium (V)-Dissolved	mg/L							<0.0002	<0.0002
Zinc (Zn)-Dissolved	mg/L	0.0034437	0.0084317					0.00092	0.00094
Zirconium (Zr)-Dissolved	mg/L							<0.0001	<0.0001

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (2024)



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-06-02 09:30:00	WLNG DS 2026-06-02 10:20:00
Inorganics									
Organic Carbon (C)-Total	mg/L							1.5	0.98
Organic Carbon (C)-Dissolved	mg/L							1.6	0.98
Solids-Total Dissolved	mg/L							<10	110
Solids-Total Suspended	mg/L	6	26					<1	1.6

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor consideration

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), consistent with recommendations outlined in Hatfield (202

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix D	D-3

Woodfibre Site Receiving Environment
Field Notes and Logs

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-01 00:00:00	12.10	171.16	0.34	7.83	10.09	0.00	0.08
EAS-DS	2026-06-01 00:15:00	12.26	168.92	0.34	7.79	9.78	0.00	0.08
EAS-DS	2026-06-01 00:30:00	12.18	170.54	0.34	7.82	9.98	0.00	0.08
EAS-DS	2026-06-01 00:45:00	12.17	172.60	0.34	7.82	9.95	0.00	0.08
EAS-DS	2026-06-01 01:00:00	12.14	172.58	0.34	7.84	10.03	0.00	0.08
EAS-DS	2026-06-01 01:15:00	12.07	174.57	0.34	7.83	10.09	0.00	0.08
EAS-DS	2026-06-01 01:30:00	12.13	174.38	0.34	7.82	9.95	0.00	0.08
EAS-DS	2026-06-01 01:45:00	12.15	158.19	0.35	7.53	8.76	0.00	0.07
EAS-DS	2026-06-01 02:00:00	12.15	171.57	0.35	7.78	9.71	6.64	0.08
EAS-DS	2026-06-01 02:15:00	12.03	176.40	0.34	7.83	10.07	0.00	0.08
EAS-DS	2026-06-01 02:30:00	12.00	176.65	0.34	7.85	10.13	0.00	0.08
EAS-DS	2026-06-01 02:45:00	11.99	176.97	0.34	7.84	10.12	0.00	0.08
EAS-DS	2026-06-01 03:00:00	12.01	172.22	0.35	7.81	9.90	0.00	0.08
EAS-DS	2026-06-01 03:15:00	11.98	176.04	0.34	7.84	10.09	0.00	0.08
EAS-DS	2026-06-01 03:30:00	11.95	175.73	0.34	7.85	10.10	0.00	0.08
EAS-DS	2026-06-01 03:45:00	11.86	169.69	0.34	7.74	9.77	0.00	0.08
EAS-DS	2026-06-01 04:00:00	11.96	171.85	0.34	7.82	9.98	0.00	0.08
EAS-DS	2026-06-01 04:15:00	11.87	171.20	0.35	7.81	10.08	0.00	0.08
EAS-DS	2026-06-01 04:30:00	11.75	167.73	0.35	7.81	10.10	0.00	0.08
EAS-DS	2026-06-01 04:45:00	11.85	171.78	0.35	7.81	10.13	0.00	0.08
EAS-DS	2026-06-01 05:00:00	11.87	168.30	0.35	7.79	9.94	0.00	0.08
EAS-DS	2026-06-01 05:15:00	11.80	171.44	0.35	7.82	10.13	0.00	0.08
EAS-DS	2026-06-01 05:30:00	11.79	175.31	0.35	7.79	9.90	0.00	0.08
EAS-DS	2026-06-01 05:45:00	11.85	173.80	0.34	7.80	9.93	0.00	0.08
EAS-DS	2026-06-01 06:00:00	11.83	177.82	0.34	7.83	10.02	0.00	0.08
EAS-DS	2026-06-01 06:15:00	11.79	175.08	0.34	7.78	9.79	0.00	0.08
EAS-DS	2026-06-01 06:30:00	11.79	175.29	0.35	7.65	9.32	0.00	0.08
EAS-DS	2026-06-01 06:45:00	11.71	174.37	0.35	7.81	10.08	0.00	0.08
EAS-DS	2026-06-01 07:00:00	11.70	173.91	0.35	7.82	10.10	0.00	0.08
EAS-DS	2026-06-01 07:15:00	11.67	171.93	0.35	7.81	10.12	0.00	0.08
EAS-DS	2026-06-01 07:30:00	11.73	171.05	0.35	7.75	9.79	0.00	0.08
EAS-DS	2026-06-01 07:45:00	11.71	168.78	0.35	7.80	9.96	0.00	0.08
EAS-DS	2026-06-01 08:00:00	11.71	168.80	0.35	7.83	10.11	0.00	0.08
EAS-DS	2026-06-01 08:15:00	11.78	170.00	0.35	7.79	10.04	0.00	0.08
EAS-DS	2026-06-01 08:30:00	11.80	165.20	0.35	7.78	10.00	0.00	0.08
EAS-DS	2026-06-01 08:45:00	11.86	163.12	0.35	7.73	9.78	0.00	0.08
EAS-DS	2026-06-01 09:00:00	11.89	159.95	0.36	7.58	9.27	0.00	0.08
EAS-DS	2026-06-01 09:15:00	12.03	158.76	0.36	7.73	9.63	0.00	0.08
EAS-DS	2026-06-01 09:30:00	12.22	167.54	0.35	7.80	9.99	0.00	0.08
EAS-DS	2026-06-01 09:45:00	12.28	168.10	0.35	7.82	10.03	0.00	0.08
EAS-DS	2026-06-01 10:00:00	12.34	161.04	0.35	7.78	9.67	0.00	0.08
EAS-DS	2026-06-01 10:15:00	12.41	168.80	0.35	7.78	9.82	0.00	0.08
EAS-DS	2026-06-01 10:30:00	12.50	165.76	0.35	7.77	9.76	0.00	0.08
EAS-DS	2026-06-01 10:45:00	12.66	170.47	0.35	7.83	9.87	0.00	0.08
EAS-DS	2026-06-01 11:00:00	12.82	172.20	0.35	7.83	9.73	0.00	0.08
EAS-DS	2026-06-01 11:15:00	12.89	161.68	0.35	7.72	9.40	104.55	0.08
EAS-DS	2026-06-01 11:30:00	12.82	163.65	0.36	7.55	8.92	0.00	0.08
EAS-DS	2026-06-01 11:45:00	13.34	174.77	0.35	7.82	9.73	0.00	0.08
EAS-DS	2026-06-01 12:00:00	13.34	176.18	0.35	7.85	9.74	0.00	0.08
EAS-DS	2026-06-01 12:15:00	13.35	177.87	0.35	7.84	9.78	0.00	0.08
EAS-DS	2026-06-01 12:30:00	13.44	178.61	0.35	7.85	9.72	0.00	0.08
EAS-DS	2026-06-01 12:45:00	13.55	178.74	0.35	7.84	9.70	0.00	0.08
EAS-DS	2026-06-01 13:00:00	13.62	177.46	0.35	7.85	9.69	0.00	0.08
EAS-DS	2026-06-01 13:15:00	13.64	176.46	0.35	7.83	9.71	0.00	0.08
EAS-DS	2026-06-01 13:30:00	13.65	175.40	0.35	7.84	9.68	0.00	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-01 13:45:00	13.78	170.16	0.35	7.78	9.55	0.00	0.08
EAS-DS	2026-06-01 14:00:00	13.80	173.78	0.35	7.85	9.63	0.00	0.08
EAS-DS	2026-06-01 14:15:00	13.72	173.03	0.35	7.82	9.66	0.00	0.08
EAS-DS	2026-06-01 14:30:00	13.71	172.52	0.35	7.82	9.61	0.00	0.08
EAS-DS	2026-06-01 14:45:00	13.79	172.20	0.35	7.82	9.64	0.00	0.08
EAS-DS	2026-06-01 15:00:00	13.75	171.69	0.35	7.83	9.63	0.00	0.08
EAS-DS	2026-06-01 15:15:00	13.81	171.48	0.35	7.81	9.65	0.00	0.08
EAS-DS	2026-06-01 15:30:00	13.90	166.11	0.35	7.67	9.03	0.00	0.08
EAS-DS	2026-06-01 15:45:00	13.96	171.01	0.35	7.72	9.35	0.00	0.08
EAS-DS	2026-06-01 16:00:00	13.88	170.09	0.35	7.81	9.56	0.00	0.08
EAS-DS	2026-06-01 16:15:00	13.87	166.98	0.35	7.76	9.45	0.00	0.08
EAS-DS	2026-06-01 16:30:00	13.86	169.67	0.35	7.82	9.62	0.00	0.08
EAS-DS	2026-06-01 16:45:00	13.76	171.89	0.35	7.82	9.65	0.00	0.08
EAS-DS	2026-06-01 17:00:00	13.68	170.57	0.35	7.81	9.66	0.00	0.08
EAS-DS	2026-06-01 17:15:00	13.62	170.43	0.35	7.80	9.61	0.00	0.08
EAS-DS	2026-06-01 17:30:00	13.47	168.68	0.35	7.78	9.50	0.00	0.08
EAS-DS	2026-06-01 17:45:00	13.45	168.08	0.35	7.77	9.57	0.00	0.08
EAS-DS	2026-06-01 18:00:00	13.88	163.04	0.36	7.67	9.08	0.00	0.08
EAS-DS	2026-06-01 18:15:00	13.69	166.64	0.36	7.79	9.62	0.00	0.08
EAS-DS	2026-06-01 18:30:00	13.40	167.85	0.35	7.80	9.74	0.00	0.08
EAS-DS	2026-06-01 18:45:00	13.29	167.81	0.35	7.80	9.76	0.00	0.08
EAS-DS	2026-06-01 19:00:00	13.21	168.78	0.35	7.80	9.79	0.00	0.08
EAS-DS	2026-06-01 19:15:00	13.09	168.77	0.35	7.79	9.79	0.00	0.08
EAS-DS	2026-06-01 19:30:00	13.01	168.82	0.35	7.78	9.79	0.00	0.08
EAS-DS	2026-06-01 19:45:00	13.04	167.94	0.35	7.76	9.65	0.00	0.08
EAS-DS	2026-06-01 20:00:00	12.95	168.50	0.34	7.78	9.78	73.38	0.08
EAS-DS	2026-06-01 20:15:00	13.00	170.01	0.35	7.79	9.77	0.00	0.08
EAS-DS	2026-06-01 20:30:00	13.05	169.60	0.35	7.81	9.62	0.00	0.08
EAS-DS	2026-06-01 20:45:00	12.97	169.99	0.34	7.80	9.85	0.00	0.08
EAS-DS	2026-06-01 21:00:00	12.98	163.03	0.35	7.67	9.16	0.00	0.08
EAS-DS	2026-06-01 21:15:00	12.74	167.54	0.35	7.77	9.86	0.00	0.08
EAS-DS	2026-06-01 21:30:00	12.72	168.75	0.35	7.80	9.86	0.00	0.08
EAS-DS	2026-06-01 21:45:00	12.71	169.03	0.35	7.79	9.92	0.00	0.08
EAS-DS	2026-06-01 22:00:00	12.70	168.38	0.34	7.78	9.86	0.00	0.08
EAS-DS	2026-06-01 22:15:00	12.74	168.29	0.35	7.77	9.80	0.00	0.08
EAS-DS	2026-06-01 22:30:00	12.67	169.59	0.34	7.78	9.88	0.00	0.08
EAS-DS	2026-06-01 22:45:00	12.65	169.27	0.34	7.77	9.89	0.00	0.08
EAS-DS	2026-06-01 23:00:00	12.63	168.75	0.34	7.78	9.90	0.00	0.08
EAS-DS	2026-06-01 23:15:00	12.48	168.84	0.34	7.79	9.96	0.00	0.08
EAS-DS	2026-06-01 23:30:00	12.42	166.95	0.34	7.81	9.98	0.00	0.08
EAS-DS	2026-06-01 23:45:00	12.39	162.36	0.34	7.72	9.64	0.00	0.08
EAS-DS	2026-06-02 00:00:00	12.44	161.29	0.34	7.76	9.70	0.00	0.08
EAS-DS	2026-06-02 00:15:00	12.51	160.55	0.35	7.56	8.89	0.00	0.08
EAS-DS	2026-06-02 00:30:00	12.29	163.01	0.34	7.81	9.96	0.00	0.08
EAS-DS	2026-06-02 00:45:00	12.24	163.09	0.34	7.78	9.96	0.00	0.08
EAS-DS	2026-06-02 01:00:00	12.19	162.26	0.34	7.81	10.02	0.00	0.08
EAS-DS	2026-06-02 01:15:00	12.16	163.15	0.34	7.80	10.03	0.00	0.08
EAS-DS	2026-06-02 01:30:00	12.13	162.84	0.34	7.80	10.05	0.00	0.08
EAS-DS	2026-06-02 01:45:00	12.35	150.76	0.35	7.48	8.57	0.00	0.07
EAS-DS	2026-06-02 02:00:00	12.22	150.01	0.36	7.66	9.51	0.00	0.07
EAS-DS	2026-06-02 02:15:00	12.13	158.98	0.35	7.71	9.71	0.00	0.08
EAS-DS	2026-06-02 02:30:00	12.09	161.31	0.34	7.79	10.02	0.00	0.08
EAS-DS	2026-06-02 02:45:00	12.07	162.13	0.35	7.79	10.05	0.00	0.08
EAS-DS	2026-06-02 03:00:00	12.03	157.30	0.35	7.72	9.70	0.00	0.07
EAS-DS	2026-06-02 03:15:00	12.04	161.75	0.34	7.80	10.05	0.00	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-02 03:30:00	12.09	151.97	0.35	7.75	9.75	0.00	0.07
EAS-DS	2026-06-02 03:45:00	12.04	158.17	0.35	7.70	9.67	0.00	0.07
EAS-DS	2026-06-02 04:00:00	11.99	162.00	0.34	7.80	10.04	0.00	0.08
EAS-DS	2026-06-02 04:15:00	11.95	162.82	0.34	7.79	10.06	0.00	0.08
EAS-DS	2026-06-02 04:30:00	11.94	163.24	0.35	7.80	10.05	0.00	0.08
EAS-DS	2026-06-02 04:45:00	11.94	160.38	0.35	7.71	9.72	0.00	0.08
EAS-DS	2026-06-02 05:00:00	11.88	164.76	0.35	7.76	9.98	0.00	0.08
EAS-DS	2026-06-02 05:15:00	11.84	162.16	0.35	7.71	9.89	0.00	0.08
EAS-DS	2026-06-02 05:30:00	11.83	159.41	0.35	7.70	9.75	0.00	0.08
EAS-DS	2026-06-02 05:45:00	11.81	160.91	0.35	7.71	9.87	0.00	0.08
EAS-DS	2026-06-02 06:00:00	11.78	161.79	0.35	7.75	10.04	0.00	0.08
EAS-DS	2026-06-02 06:15:00	11.86	165.04	0.35	7.79	10.11	0.00	0.08
EAS-DS	2026-06-02 06:30:00	11.86	165.12	0.34	7.80	10.12	0.00	0.08
EAS-DS	2026-06-02 06:45:00	11.85	163.77	0.35	7.79	10.12	0.00	0.08
EAS-DS	2026-06-02 07:00:00	11.96	162.32	0.35	7.59	9.22	0.00	0.08
EAS-DS	2026-06-02 07:15:00	11.96	162.24	0.35	7.78	9.99	0.00	0.08
EAS-DS	2026-06-02 07:30:00	11.92	162.35	0.35	7.60	9.37	0.00	0.08
EAS-DS	2026-06-02 07:45:00	11.85	165.93	0.34	7.77	10.12	0.00	0.08
EAS-DS	2026-06-02 08:00:00	11.92	164.74	0.35	7.60	9.52	0.00	0.08
EAS-DS	2026-06-02 08:15:00	11.95	165.67	0.35	7.73	10.00	0.00	0.08
EAS-DS	2026-06-02 08:30:00	12.02	165.96	0.34	7.75	10.04	0.00	0.08
EAS-DS	2026-06-02 08:45:00	12.13	161.63	0.34	7.75	9.98	0.00	0.08
EAS-DS	2026-06-02 09:00:00	12.09	164.31	0.34	7.76	10.08	0.00	0.08
EAS-DS	2026-06-02 09:15:00	12.18	164.76	0.34	7.76	10.04	0.00	0.08
EAS-DS	2026-06-02 09:30:00	12.17	163.96	0.34	7.68	9.70	0.00	0.08
EAS-DS	2026-06-02 09:45:00	12.39	165.38	0.34	7.72	9.85	0.00	0.08
EAS-DS	2026-06-02 10:00:00	12.46	162.75	0.34	7.74	9.80	0.00	0.08
EAS-DS	2026-06-02 10:15:00	12.67	164.81	0.34	7.79	9.93	0.00	0.08
EAS-DS	2026-06-02 10:30:00	12.76	160.54	0.24	7.82	10.00	44.73	0.08
EAS-DS	2026-06-02 10:45:00	12.94	160.69	0.25	7.83	9.84	0.00	0.08
EAS-DS	2026-06-02 11:00:00	12.86	163.77	0.25	7.81	9.85	0.00	0.08
EAS-DS	2026-06-02 11:15:00	13.01	151.29	0.26	7.80	9.83	0.00	0.07
EAS-DS	2026-06-02 11:30:00	13.02	159.14	0.27	7.81	9.82	0.00	0.08
EAS-DS	2026-06-02 11:45:00	13.23	159.72	0.27	7.86	9.86	0.00	0.08
EAS-DS	2026-06-02 12:00:00	13.40	164.26	0.27	7.86	9.85	0.00	0.08
EAS-DS	2026-06-02 12:15:00	13.49	161.40	0.28	7.87	9.83	0.00	0.08
EAS-DS	2026-06-02 12:30:00	13.49	166.16	0.28	7.87	9.82	0.00	0.08
EAS-DS	2026-06-02 12:45:00	13.81	165.45	0.28	7.88	9.73	560.53	0.08
EAS-DS	2026-06-02 13:00:00	13.71	166.03	0.28	7.89	9.76	0.00	0.08
EAS-DS	2026-06-02 13:15:00	14.00	153.56	0.29	7.84	9.50	0.00	0.07
EAS-DS	2026-06-02 13:30:00	13.85	159.01	0.28	7.89	9.71	0.00	0.08
EAS-DS	2026-06-02 13:45:00	13.95	165.39	0.28	7.90	9.72	0.00	0.08
EAS-DS	2026-06-02 14:00:00	13.94	163.24	0.28	7.90	9.73	0.00	0.08
EAS-DS	2026-06-02 14:15:00	13.71	160.74	0.29	7.71	9.20	0.00	0.08
EAS-DS	2026-06-02 14:30:00	14.09	157.00	0.29	7.89	9.56	0.00	0.07
EAS-DS	2026-06-02 14:45:00	14.45	163.08	0.29	7.88	9.49	0.00	0.08
EAS-DS	2026-06-02 15:00:00	14.33	163.05	0.29	7.89	9.62	0.00	0.08
EAS-DS	2026-06-02 15:15:00	14.02	164.41	0.29	7.89	9.67	0.00	0.08
EAS-DS	2026-06-02 15:30:00	13.96	163.07	0.29	7.89	9.70	0.00	0.08
EAS-DS	2026-06-02 15:45:00	14.01	160.42	0.29	7.88	9.62	0.00	0.08
EAS-DS	2026-06-02 16:00:00	14.21	162.55	0.30	7.87	9.60	0.00	0.08
EAS-DS	2026-06-02 16:15:00	13.95	164.14	0.30	7.88	9.69	0.00	0.08
EAS-DS	2026-06-02 16:30:00	13.93	163.74	0.29	7.88	9.69	0.00	0.08
EAS-DS	2026-06-02 16:45:00	13.97	161.69	0.30	7.88	9.61	0.00	0.08
EAS-DS	2026-06-02 17:00:00	14.13	161.66	0.29	7.89	9.57	0.00	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-02 17:15:00	14.19	165.01	0.30	7.88	9.56	0.00	0.08
EAS-DS	2026-06-02 17:30:00	13.99	165.41	0.29	7.88	9.66	0.00	0.08
EAS-DS	2026-06-02 17:45:00	13.91	165.22	0.30	7.88	9.67	0.00	0.08
EAS-DS	2026-06-02 18:00:00	13.81	164.42	0.30	7.88	9.70	0.00	0.08
EAS-DS	2026-06-02 18:15:00	13.67	164.53	0.30	7.88	9.74	0.00	0.08
EAS-DS	2026-06-02 18:30:00	13.54	163.83	0.29	7.88	9.76	0.00	0.08
EAS-DS	2026-06-02 18:45:00	13.47	157.56	0.30	7.82	9.52	0.00	0.07
EAS-DS	2026-06-02 19:00:00	13.51	153.27	0.30	7.82	9.48	343.66	0.07
EAS-DS	2026-06-02 19:15:00	13.43	161.51	0.30	7.83	9.67	0.00	0.08
EAS-DS	2026-06-02 19:30:00	13.21	162.54	0.30	7.86	9.82	0.00	0.08
EAS-DS	2026-06-02 19:45:00	13.14	161.63	0.30	7.75	9.58	0.00	0.08
EAS-DS	2026-06-02 20:00:00	12.94	161.64	0.30	7.86	9.89	0.00	0.08
EAS-DS	2026-06-02 20:15:00	12.84	161.32	0.30	7.86	9.90	0.00	0.08
EAS-DS	2026-06-02 20:30:00	13.01	161.26	0.30	7.83	9.73	0.00	0.08
EAS-DS	2026-06-02 20:45:00	13.16	164.54	0.30	7.74	9.53	0.00	0.08
EAS-DS	2026-06-02 21:00:00	13.42	168.12	0.30	7.86	9.76	0.00	0.08
EAS-DS	2026-06-02 21:15:00	13.25	166.33	0.30	7.85	9.71	0.00	0.08
EAS-DS	2026-06-02 21:30:00	13.10	165.47	0.30	7.85	9.83	0.00	0.08
EAS-DS	2026-06-02 21:45:00	12.93	164.25	0.30	7.85	9.85	213.87	0.08
EAS-DS	2026-06-02 22:00:00	12.72	163.56	0.30	7.82	9.86	0.00	0.08
EAS-DS	2026-06-02 22:15:00	12.66	161.00	0.30	7.71	9.57	0.00	0.08
EAS-DS	2026-06-02 22:30:00	12.54	158.06	0.30	7.82	9.87	0.00	0.07
EAS-DS	2026-06-02 22:45:00	12.52	156.83	0.31	7.84	9.89	0.00	0.07
EAS-DS	2026-06-02 23:00:00	12.43	160.61	0.31	7.81	9.82	0.00	0.08
EAS-DS	2026-06-02 23:15:00	12.40	155.62	0.31	7.79	9.81	0.00	0.07
EAS-DS	2026-06-02 23:30:00	12.49	157.66	0.31	7.58	9.48	0.00	0.07
EAS-DS	2026-06-02 23:45:00	12.33	156.59	0.31	7.82	9.93	130.05	0.07
EAS-DS	2026-06-03 00:00:00	12.34	160.43	0.31	7.82	9.94	0.00	0.08
EAS-DS	2026-06-03 00:15:00	12.27	162.46	0.31	7.84	10.02	0.00	0.08
EAS-DS	2026-06-03 00:30:00	12.25	162.48	0.31	7.82	9.95	0.00	0.08
EAS-DS	2026-06-03 00:45:00	12.24	160.79	0.31	7.82	9.98	0.00	0.08
EAS-DS	2026-06-03 01:00:00	12.22	162.25	0.30	7.83	10.03	0.00	0.08
EAS-DS	2026-06-03 01:15:00	12.21	162.23	0.31	7.83	10.05	0.00	0.08
EAS-DS	2026-06-03 01:30:00	12.21	161.85	0.31	7.77	9.91	0.00	0.08
EAS-DS	2026-06-03 01:45:00	12.17	161.74	0.31	7.84	10.07	0.00	0.08
EAS-DS	2026-06-03 02:00:00	12.15	161.39	0.31	7.81	10.03	0.00	0.08
EAS-DS	2026-06-03 02:15:00	12.29	158.48	0.31	7.62	9.43	0.00	0.08
EAS-DS	2026-06-03 02:30:00	12.30	152.70	0.31	7.78	9.79	0.00	0.07
EAS-DS	2026-06-03 02:45:00	12.17	160.31	0.31	7.81	10.02	0.00	0.08
EAS-DS	2026-06-03 03:00:00	12.05	161.18	0.31	7.81	10.10	278.23	0.08
EAS-DS	2026-06-03 03:15:00	12.00	160.22	0.31	7.81	10.07	0.00	0.08
EAS-DS	2026-06-03 03:30:00	11.97	159.86	0.31	7.77	10.00	0.00	0.08
EAS-DS	2026-06-03 03:45:00	12.04	154.00	0.31	7.79	9.98	0.00	0.07
EAS-DS	2026-06-03 04:00:00	12.05	154.12	0.31	7.77	9.92	0.00	0.07
EAS-DS	2026-06-03 04:15:00	12.08	155.49	0.31	7.80	9.96	0.00	0.07
EAS-DS	2026-06-03 04:30:00	12.15	156.52	0.31	7.70	9.87	0.00	0.07
EAS-DS	2026-06-03 04:45:00	12.04	162.65	0.31	7.81	10.07	0.00	0.08
EAS-DS	2026-06-03 05:00:00	12.00	162.70	0.31	7.80	10.07	0.00	0.08
EAS-DS	2026-06-03 05:15:00	12.03	162.99	0.31	7.82	10.07	0.00	0.08
EAS-DS	2026-06-03 05:30:00	11.96	161.84	0.31	7.79	10.03	0.00	0.08
EAS-DS	2026-06-03 05:45:00	12.18	184.25	0.30	7.88	9.91	0.00	0.09
EAS-DS	2026-06-03 06:00:00	12.05	174.40	0.31	7.87	10.03	0.00	0.08
EAS-DS	2026-06-03 06:15:00	12.04	169.24	0.31	7.86	10.02	0.00	0.08
EAS-DS	2026-06-03 06:30:00	12.13	155.60	0.32	7.72	9.13	0.00	0.07
EAS-DS	2026-06-03 06:45:00	12.23	162.52	0.31	7.85	9.87	175.30	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-03 07:00:00	12.27	161.38	0.31	7.86	9.80	0.00	0.08
EAS-DS	2026-06-03 07:15:00	12.28	160.85	0.31	7.84	9.89	0.00	0.08
EAS-DS	2026-06-03 07:30:00	12.12	163.91	0.31	7.81	10.00	0.00	0.08
EAS-DS	2026-06-03 07:45:00	12.00	161.92	0.32	7.78	10.00	0.00	0.08
EAS-DS	2026-06-03 08:00:00	12.11	162.76	0.31	7.85	10.03	0.00	0.08
EAS-DS	2026-06-03 08:15:00	12.02	161.39	0.32	7.80	10.07	0.00	0.08
EAS-DS	2026-06-03 08:30:00	12.09	162.67	0.31	7.82	10.04	0.00	0.08
EAS-DS	2026-06-03 08:45:00	12.11	162.20	0.32	7.84	10.07	0.00	0.08
EAS-DS	2026-06-03 09:00:00	12.09	159.30	0.32	7.77	9.96	0.00	0.08
EAS-DS	2026-06-03 09:15:00	12.21	157.89	0.32	7.83	9.92	0.00	0.07
EAS-DS	2026-06-03 09:30:00	12.32	154.40	0.19	7.80	9.95	0.00	0.07
EAS-DS	2026-06-03 09:45:00	12.34	154.20	0.19	7.77	9.70	0.00	0.07
EAS-DS	2026-06-03 10:00:00	12.35	159.43	0.20	7.79	9.97	0.00	0.08
EAS-DS	2026-06-03 10:15:00	12.37	162.62	0.21	7.86	10.11	0.00	0.08
EAS-DS	2026-06-03 10:30:00	12.38	162.14	0.22	7.82	9.90	0.00	0.08
EAS-DS	2026-06-03 10:45:00	12.44	161.61	0.23	7.78	9.83	0.00	0.08
EAS-DS	2026-06-03 11:00:00	12.60	160.84	0.23	7.88	10.03	0.00	0.08
EAS-DS	2026-06-03 11:15:00	12.66	161.23	0.23	7.88	10.00	0.00	0.08
EAS-DS	2026-06-03 11:30:00	12.71	163.14	0.24	7.86	9.92	0.00	0.08
EAS-DS	2026-06-03 11:45:00	12.69	166.12	0.24	7.87	10.03	0.00	0.08
EAS-DS	2026-06-03 12:00:00	12.65	166.78	0.25	7.88	10.05	0.00	0.08
EAS-DS	2026-06-03 12:15:00	12.65	167.38	0.25	7.88	10.02	0.00	0.08
EAS-DS	2026-06-03 12:30:00	12.73	165.76	0.25	7.90	10.00	0.00	0.08
EAS-DS	2026-06-03 12:45:00	12.71	169.46	0.26	7.87	10.01	0.00	0.08
EAS-DS	2026-06-03 13:00:00	12.71	169.98	0.26	7.88	10.03	0.00	0.08
EAS-DS	2026-06-03 13:15:00	12.79	166.85	0.26	7.84	9.86	0.00	0.08
EAS-DS	2026-06-03 13:30:00	12.87	167.03	0.26	7.90	9.91	0.00	0.08
EAS-DS	2026-06-03 13:45:00	12.86	162.02	0.27	7.76	9.67	0.00	0.08
EAS-DS	2026-06-03 14:00:00	12.85	163.37	0.27	7.88	9.90	0.00	0.08
EAS-DS	2026-06-03 14:15:00	12.82	166.38	0.27	7.88	9.99	0.00	0.08
EAS-DS	2026-06-03 14:30:00	12.76	164.96	0.27	7.86	9.99	0.00	0.08
EAS-DS	2026-06-03 14:45:00	12.74	162.89	0.27	7.91	10.02	0.00	0.08
EAS-DS	2026-06-03 15:00:00	12.83	161.52	0.27	7.87	9.97	0.00	0.08
EAS-DS	2026-06-03 15:15:00	12.86	160.17	0.27	7.89	9.94	0.00	0.08
EAS-DS	2026-06-03 15:30:00	12.92	160.63	0.28	7.89	9.93	0.00	0.08
EAS-DS	2026-06-03 15:45:00	12.94	160.98	0.28	7.84	9.96	0.00	0.08
EAS-DS	2026-06-03 16:00:00	12.76	160.44	0.28	7.83	9.95	0.00	0.08
EAS-DS	2026-06-03 16:15:00	12.71	161.10	0.28	7.84	10.00	0.00	0.08
EAS-DS	2026-06-03 16:30:00	12.77	156.70	0.28	7.77	9.84	0.00	0.07
EAS-DS	2026-06-03 16:45:00	12.83	159.70	0.28	7.78	9.62	0.00	0.08
EAS-DS	2026-06-03 17:00:00	12.77	160.24	0.28	7.86	9.89	0.00	0.08
EAS-DS	2026-06-03 17:15:00	12.77	159.82	0.29	7.86	10.00	0.00	0.08
EAS-DS	2026-06-03 17:30:00	12.65	162.37	0.28	7.88	10.04	0.00	0.08
EAS-DS	2026-06-03 17:45:00	12.55	164.67	0.29	7.81	9.96	0.00	0.08
EAS-DS	2026-06-03 18:00:00	12.57	167.48	0.29	7.86	9.95	0.00	0.08
EAS-DS	2026-06-03 18:15:00	12.62	170.42	0.29	7.76	9.60	0.00	0.08
EAS-DS	2026-06-03 18:30:00	12.56	179.92	0.29	7.89	10.06	0.00	0.09
EAS-DS	2026-06-03 18:45:00	12.62	180.98	0.29	7.86	10.05	0.00	0.09
EAS-DS	2026-06-03 19:00:00	12.61	182.07	0.29	7.75	9.55	0.00	0.09
EAS-DS	2026-06-03 19:15:00	12.51	193.62	0.29	7.89	10.07	0.00	0.09
EAS-DS	2026-06-03 19:30:00	12.45	196.07	0.29	7.89	10.08	0.00	0.09
EAS-DS	2026-06-03 19:45:00	12.39	197.21	0.29	7.88	10.09	0.00	0.09
EAS-DS	2026-06-03 20:00:00	12.37	197.94	0.29	7.89	10.11	0.00	0.09
EAS-DS	2026-06-03 20:15:00	12.35	194.26	0.29	7.92	10.09	0.00	0.09
EAS-DS	2026-06-03 20:30:00	12.43	183.70	0.29	7.80	9.76	0.00	0.09

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-03 20:45:00	12.39	188.63	0.29	7.78	9.73	0.00	0.09
EAS-DS	2026-06-03 21:00:00	12.32	188.65	0.29	7.92	10.07	0.00	0.09
EAS-DS	2026-06-03 21:15:00	12.32	193.43	0.29	7.89	10.12	0.00	0.09
EAS-DS	2026-06-03 21:30:00	12.31	191.71	0.29	7.80	9.80	0.00	0.09
EAS-DS	2026-06-03 21:45:00	12.22	191.07	0.29	7.89	10.12	0.00	0.09
EAS-DS	2026-06-03 22:00:00	12.16	189.94	0.29	7.89	10.16	0.00	0.09
EAS-DS	2026-06-03 22:15:00	12.19	189.90	0.29	7.86	10.12	0.00	0.09
EAS-DS	2026-06-03 22:30:00	12.15	186.42	0.29	7.88	10.13	0.00	0.09
EAS-DS	2026-06-03 22:45:00	12.17	180.77	0.29	7.89	10.13	0.00	0.09
EAS-DS	2026-06-03 23:00:00	12.26	170.89	0.30	7.80	9.81	0.00	0.08
EAS-DS	2026-06-03 23:15:00	12.21	176.39	0.30	7.77	9.86	0.00	0.08
EAS-DS	2026-06-03 23:30:00	12.10	181.85	0.30	7.88	10.18	0.00	0.09
EAS-DS	2026-06-03 23:45:00	12.05	182.62	0.30	7.87	10.19	0.00	0.09
EAS-DS	2026-06-04 00:00:00	12.21	188.40	0.30	7.74	9.79	0.00	0.09
EAS-DS	2026-06-04 00:15:00	12.02	176.91	0.30	7.86	10.14	0.00	0.08
EAS-DS	2026-06-04 00:30:00	12.04	171.71	0.30	7.82	9.94	0.00	0.08
EAS-DS	2026-06-04 00:45:00	12.00	167.17	0.30	7.86	10.14	0.00	0.08
EAS-DS	2026-06-04 01:00:00	11.95	172.34	0.30	7.85	10.20	0.00	0.08
EAS-DS	2026-06-04 01:15:00	11.93	171.42	0.30	7.83	10.21	0.00	0.08
EAS-DS	2026-06-04 01:30:00	11.88	170.61	0.30	7.85	10.25	0.00	0.08
EAS-DS	2026-06-04 01:45:00	11.88	168.73	0.30	7.84	10.23	0.00	0.08
EAS-DS	2026-06-04 02:00:00	11.90	163.88	0.30	7.87	10.17	0.00	0.08
EAS-DS	2026-06-04 02:15:00	12.00	152.16	0.30	7.79	10.03	0.00	0.07
EAS-DS	2026-06-04 02:30:00	11.99	162.35	0.30	7.75	9.94	0.00	0.08
EAS-DS	2026-06-04 02:45:00	11.92	166.25	0.30	7.85	10.23	0.00	0.08
EAS-DS	2026-06-04 03:00:00	11.90	167.74	0.30	7.86	10.25	0.00	0.08
EAS-DS	2026-06-04 03:15:00	11.92	168.20	0.30	7.82	10.25	0.00	0.08
EAS-DS	2026-06-04 03:30:00	12.07	171.35	0.30	7.79	10.15	0.00	0.08
EAS-DS	2026-06-04 03:45:00	12.06	171.48	0.30	7.79	10.15	0.00	0.08
EAS-DS	2026-06-04 04:00:00	12.03	169.55	0.30	7.80	10.17	0.00	0.08
EAS-DS	2026-06-04 04:15:00	12.05	169.75	0.30	7.78	10.07	0.00	0.08
EAS-DS	2026-06-04 04:30:00	11.95	164.66	0.30	7.82	10.16	0.00	0.08
EAS-DS	2026-06-04 04:45:00	11.97	161.35	0.30	7.77	9.85	0.00	0.08
EAS-DS	2026-06-04 05:00:00	12.05	163.80	0.30	7.74	9.82	0.00	0.08
EAS-DS	2026-06-04 05:15:00	12.07	166.42	0.30	7.83	10.09	0.00	0.08
EAS-DS	2026-06-04 05:30:00	12.07	170.62	0.30	7.81	10.13	0.00	0.08
EAS-DS	2026-06-04 05:45:00	12.05	170.75	0.30	7.81	10.13	0.00	0.08
EAS-DS	2026-06-04 06:00:00	12.03	168.79	0.30	7.82	10.13	0.00	0.08
EAS-DS	2026-06-04 06:15:00	12.06	166.99	0.30	7.81	10.04	0.00	0.08
EAS-DS	2026-06-04 06:30:00	12.00	168.75	0.30	7.82	10.16	0.00	0.08
EAS-DS	2026-06-04 06:45:00	11.98	168.38	0.30	7.81	10.16	0.00	0.08
EAS-DS	2026-06-04 07:00:00	11.98	167.48	0.30	7.83	10.18	0.00	0.08
EAS-DS	2026-06-04 07:15:00	12.01	163.38	0.31	7.69	9.63	0.00	0.08
EAS-DS	2026-06-04 07:30:00	12.12	144.71	0.31	7.72	9.38	0.00	0.07
EAS-DS	2026-06-04 07:45:00	12.23	129.02	0.31	7.68	9.52	0.00	0.06
EAS-DS	2026-06-04 08:00:00	12.07	159.95	0.31	7.78	9.92	0.00	0.08
EAS-DS	2026-06-04 08:15:00	12.06	165.87	0.31	7.83	10.16	0.00	0.08
EAS-DS	2026-06-04 08:30:00	12.07	166.91	0.30	7.85	10.17	0.00	0.08
EAS-DS	2026-06-04 08:45:00	12.09	167.15	0.30	7.83	10.09	0.00	0.08
EAS-DS	2026-06-04 09:00:00	12.11	167.94	0.30	7.85	10.15	0.00	0.08
EAS-DS	2026-06-04 09:15:00	12.10	163.85	0.30	7.76	9.83	0.00	0.08
EAS-DS	2026-06-04 09:30:00	12.15	158.75	0.31	7.76	9.77	0.00	0.08
EAS-DS	2026-06-04 09:45:00	12.35	164.15	0.31	7.85	10.07	0.00	0.08
EAS-DS	2026-06-04 10:00:00	12.41	168.72	0.30	7.85	10.08	0.00	0.08
EAS-DS	2026-06-04 10:15:00	12.49	167.32	0.30	7.86	10.04	0.00	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-04 10:30:00	12.65	165.00	0.30	7.88	9.93	0.00	0.08
EAS-DS	2026-06-04 10:45:00	12.85	166.52	0.30	7.89	9.84	0.00	0.08
EAS-DS	2026-06-04 11:00:00	12.99	167.77	0.30	7.89	9.86	0.00	0.08
EAS-DS	2026-06-04 11:15:00	12.93	155.42	0.30	7.72	9.43	0.00	0.07
EAS-DS	2026-06-04 11:30:00	13.08	166.80	0.30	7.91	9.89	0.00	0.08
EAS-DS	2026-06-04 11:45:00	13.17	166.39	0.30	7.86	9.64	0.00	0.08
EAS-DS	2026-06-04 12:00:00	13.36	167.53	0.30	7.89	9.70	0.00	0.08
EAS-DS	2026-06-04 12:15:00	13.44	163.86	0.30	7.90	9.85	0.00	0.08
EAS-DS	2026-06-04 12:30:00	13.35	158.37	0.30	7.92	9.88	0.00	0.07
EAS-DS	2026-06-04 12:45:00	13.29	156.88	0.30	7.91	9.91	0.00	0.07
EAS-DS	2026-06-04 13:00:00	13.23	160.20	0.30	7.93	9.93	0.00	0.08
EAS-DS	2026-06-04 13:15:00	13.27	160.54	0.30	7.92	9.86	0.00	0.08
EAS-DS	2026-06-04 13:30:00	13.43	159.46	0.30	7.91	9.79	0.00	0.08
EAS-DS	2026-06-04 13:45:00	13.52	160.30	0.30	7.90	9.76	0.00	0.08
EAS-DS	2026-06-04 14:00:00	13.72	160.77	0.30	7.92	9.72	0.00	0.08
EAS-DS	2026-06-04 14:15:00	13.83	158.38	0.30	7.90	9.64	0.00	0.07
EAS-DS	2026-06-04 14:30:00	13.80	155.50	0.30	7.91	9.75	0.00	0.07
EAS-DS	2026-06-04 14:45:00	13.89	160.36	0.30	7.90	9.63	0.00	0.08
EAS-DS	2026-06-04 15:00:00	13.94	151.16	0.31	7.79	8.95	0.00	0.07
EAS-DS	2026-06-04 15:15:00	14.11	157.08	0.30	7.89	9.67	0.00	0.07
EAS-DS	2026-06-04 15:30:00	13.71	158.00	0.30	7.93	9.79	0.00	0.07
EAS-DS	2026-06-04 15:45:00	13.79	158.78	0.30	7.92	9.67	0.00	0.08
EAS-DS	2026-06-04 16:00:00	13.91	158.24	0.30	7.90	9.61	0.00	0.07
EAS-DS	2026-06-04 16:15:00	13.87	158.88	0.30	7.90	9.64	0.00	0.08
EAS-DS	2026-06-04 16:30:00	13.95	157.47	0.30	7.91	9.68	0.00	0.07
EAS-DS	2026-06-04 16:45:00	13.79	151.90	0.31	7.90	9.65	0.00	0.07
EAS-DS	2026-06-04 17:00:00	13.80	144.59	0.31	7.73	9.34	0.00	0.07
EAS-DS	2026-06-04 17:15:00	13.67	157.68	0.31	7.90	9.74	0.00	0.07
EAS-DS	2026-06-04 17:30:00	13.59	158.22	0.31	7.90	9.73	0.00	0.07
EAS-DS	2026-06-04 17:45:00	13.63	159.82	0.31	7.90	9.67	0.00	0.08
EAS-DS	2026-06-04 18:00:00	13.67	155.94	0.31	7.91	9.77	0.00	0.07
EAS-DS	2026-06-04 18:15:00	13.37	152.77	0.31	7.89	9.82	0.00	0.07
EAS-DS	2026-06-04 18:30:00	13.25	156.80	0.31	7.90	9.78	0.00	0.07
EAS-DS	2026-06-04 18:45:00	13.22	157.77	0.31	7.89	9.79	0.00	0.07
EAS-DS	2026-06-04 19:00:00	13.15	155.40	0.31	7.87	9.75	0.00	0.07
EAS-DS	2026-06-04 19:15:00	12.91	156.30	0.31	7.89	9.95	0.00	0.07
EAS-DS	2026-06-04 19:30:00	12.79	156.33	0.31	7.90	9.98	0.00	0.07
EAS-DS	2026-06-04 19:45:00	12.64	156.28	0.31	7.88	9.96	0.00	0.07
EAS-DS	2026-06-04 20:00:00	12.55	155.80	0.31	7.89	10.00	0.00	0.07
EAS-DS	2026-06-04 20:15:00	12.59	154.77	0.31	7.86	9.94	0.00	0.07
EAS-DS	2026-06-04 20:30:00	12.48	153.18	0.31	7.87	10.00	0.00	0.07
EAS-DS	2026-06-04 20:45:00	12.42	153.45	0.31	7.86	10.06	0.00	0.07
EAS-DS	2026-06-04 21:00:00	12.30	155.98	0.31	7.89	10.09	0.00	0.07
EAS-DS	2026-06-04 21:15:00	12.28	156.11	0.31	7.87	10.09	0.00	0.07
EAS-DS	2026-06-04 21:30:00	12.20	155.89	0.31	7.88	10.12	0.00	0.07
EAS-DS	2026-06-04 21:45:00	12.16	152.41	0.31	7.86	10.05	0.00	0.07
EAS-DS	2026-06-04 22:00:00	12.15	155.59	0.31	7.86	10.02	0.00	0.07
EAS-DS	2026-06-04 22:15:00	12.12	155.38	0.31	7.86	10.12	0.00	0.07
EAS-DS	2026-06-04 22:30:00	12.08	151.75	0.31	7.85	10.04	0.00	0.07
EAS-DS	2026-06-04 22:45:00	12.13	154.36	0.31	7.87	10.04	0.00	0.07
EAS-DS	2026-06-04 23:00:00	12.20	152.78	0.31	7.83	9.99	0.00	0.07
EAS-DS	2026-06-04 23:15:00	12.18	154.79	0.31	7.86	9.99	0.00	0.07
EAS-DS	2026-06-04 23:30:00	12.05	155.73	0.31	7.87	10.11	0.00	0.07
EAS-DS	2026-06-04 23:45:00	12.03	155.56	0.31	7.87	10.06	0.00	0.07
EAS-DS	2026-06-05 00:00:00	12.00	154.60	0.31	7.87	10.15	0.00	0.07

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-05 00:15:00	11.92	154.53	0.31	7.87	10.12	0.00	0.07
EAS-DS	2026-06-05 00:30:00	11.95	154.75	0.31	7.87	10.10	0.00	0.07
EAS-DS	2026-06-05 00:45:00	12.02	154.10	0.31	7.87	10.05	0.00	0.07
EAS-DS	2026-06-05 01:00:00	12.05	152.65	0.31	7.78	9.84	0.00	0.07
EAS-DS	2026-06-05 01:15:00	11.87	150.66	0.31	7.86	10.07	0.00	0.07
EAS-DS	2026-06-05 01:30:00	11.81	151.47	0.31	7.87	10.16	0.00	0.07
EAS-DS	2026-06-05 01:45:00	12.06	160.50	0.31	7.87	10.06	0.00	0.08
EAS-DS	2026-06-05 02:00:00	12.27	155.19	0.31	7.75	9.70	0.00	0.07
EAS-DS	2026-06-05 02:15:00	12.39	159.71	0.31	7.88	9.93	0.00	0.08
EAS-DS	2026-06-05 02:30:00	12.04	157.48	0.31	7.89	10.12	0.00	0.07
EAS-DS	2026-06-05 02:45:00	11.84	156.05	0.31	7.86	10.18	0.00	0.07
EAS-DS	2026-06-05 03:00:00	11.84	155.90	0.31	7.87	10.11	0.00	0.07
EAS-DS	2026-06-05 03:15:00	11.82	155.85	0.31	7.86	10.09	0.00	0.07
EAS-DS	2026-06-05 03:30:00	11.87	152.82	0.31	7.82	10.01	0.00	0.07
EAS-DS	2026-06-05 03:45:00	11.91	142.70	0.31	7.75	9.83	0.00	0.07
EAS-DS	2026-06-05 04:00:00	11.73	154.81	0.31	7.85	10.17	0.00	0.07
EAS-DS	2026-06-05 04:15:00	11.68	153.18	0.30	7.85	10.11	0.00	0.07
EAS-DS	2026-06-05 04:30:00	11.74	153.20	0.30	7.84	10.07	0.00	0.07
EAS-DS	2026-06-05 04:45:00	11.77	151.92	0.31	7.84	10.05	0.00	0.07
EAS-DS	2026-06-05 05:00:00	11.70	152.20	0.30	7.85	10.18	0.00	0.07
EAS-DS	2026-06-05 05:15:00	11.65	152.93	0.30	7.86	10.19	0.00	0.07
EAS-DS	2026-06-05 05:30:00	11.76	150.55	0.30	7.85	10.00	0.00	0.07
EAS-DS	2026-06-05 05:45:00	11.83	149.66	0.30	7.83	10.00	0.00	0.07
EAS-DS	2026-06-05 06:00:00	11.80	152.70	0.30	7.88	10.14	0.00	0.07
EAS-DS	2026-06-05 06:15:00	11.70	153.66	0.30	7.88	10.19	0.00	0.07
EAS-DS	2026-06-05 06:30:00	11.69	153.45	0.30	7.88	10.19	0.00	0.07
EAS-DS	2026-06-05 06:45:00	11.70	153.79	0.30	7.87	10.13	0.00	0.07
EAS-DS	2026-06-05 07:00:00	11.80	150.48	0.30	7.78	9.81	0.00	0.07
EAS-DS	2026-06-05 07:15:00	11.83	147.61	0.31	7.84	9.95	0.00	0.07
EAS-DS	2026-06-05 07:30:00	11.78	151.28	0.30	7.89	10.10	0.00	0.07
EAS-DS	2026-06-05 07:45:00	11.70	151.72	0.31	7.88	10.14	0.00	0.07
EAS-DS	2026-06-05 08:00:00	11.67	151.90	0.31	7.89	10.23	0.00	0.07
EAS-DS	2026-06-05 08:15:00	11.71	146.36	0.31	7.69	9.69	0.00	0.07
EAS-DS	2026-06-05 08:30:00	11.71	139.41	0.31	7.76	9.87	0.00	0.07
EAS-DS	2026-06-05 08:45:00	11.63	146.91	0.31	7.83	10.05	0.00	0.07
EAS-DS	2026-06-05 09:00:00	11.60	150.86	0.31	7.88	10.19	0.00	0.07
EAS-DS	2026-06-05 09:15:00	11.61	151.06	0.31	7.89	10.23	0.00	0.07
EAS-DS	2026-06-05 09:30:00	11.67	148.19	0.31	7.83	9.99	0.00	0.07
EAS-DS	2026-06-05 09:45:00	11.76	146.04	0.31	7.87	10.00	0.00	0.07
EAS-DS	2026-06-05 10:00:00	11.88	149.79	0.31	7.90	10.12	0.00	0.07
EAS-DS	2026-06-05 10:15:00	11.82	149.90	0.31	7.86	10.08	0.00	0.07
EAS-DS	2026-06-05 10:30:00	11.90	150.99	0.31	7.89	10.10	0.00	0.07
EAS-DS	2026-06-05 10:45:00	11.91	149.58	0.31	7.88	10.04	0.00	0.07
EAS-DS	2026-06-05 11:00:00	11.94	146.38	0.31	7.75	9.72	0.00	0.07
EAS-DS	2026-06-05 11:15:00	11.96	129.36	0.31	7.75	9.84	0.00	0.06
EAS-DS	2026-06-05 11:30:00	11.93	149.08	0.31	7.87	9.99	0.00	0.07
EAS-DS	2026-06-05 11:45:00	11.97	144.19	0.31	7.85	9.98	0.00	0.07
EAS-DS	2026-06-05 12:00:00	11.91	148.80	0.31	7.86	9.99	0.00	0.07
EAS-DS	2026-06-05 12:15:00	11.92	151.30	0.31	7.90	10.13	0.00	0.07
EAS-DS	2026-06-05 12:30:00	11.88	150.03	0.31	7.87	10.03	0.00	0.07
EAS-DS	2026-06-05 12:45:00	11.92	150.97	0.31	7.89	10.11	0.00	0.07
EAS-DS	2026-06-05 13:00:00	11.94	146.66	0.31	7.80	9.84	0.00	0.07
EAS-DS	2026-06-05 13:15:00	11.94	144.19	0.31	7.88	10.05	0.00	0.07
EAS-DS	2026-06-05 13:30:00	11.84	147.77	0.31	7.89	10.11	0.00	0.07
EAS-DS	2026-06-05 13:45:00	11.74	149.02	0.31	7.86	9.97	0.00	0.07

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-05 14:00:00	11.73	150.08	0.31	7.89	10.16	0.00	0.07
EAS-DS	2026-06-05 14:15:00	11.74	149.12	0.31	7.90	10.13	0.00	0.07
EAS-DS	2026-06-05 14:30:00	11.80	147.10	0.31	7.85	9.99	0.00	0.07
EAS-DS	2026-06-05 14:45:00	11.76	134.67	0.32	7.77	9.32	0.00	0.06
EAS-DS	2026-06-05 15:00:00	11.86	144.29	0.32	7.89	10.00	0.00	0.07
EAS-DS	2026-06-05 15:15:00	11.76	150.80	0.31	7.88	10.16	0.00	0.07
EAS-DS	2026-06-05 15:30:00	11.75	150.22	0.31	7.89	10.18	0.00	0.07
EAS-DS	2026-06-05 15:45:00	11.79	150.90	0.31	7.88	10.16	0.00	0.07
EAS-DS	2026-06-05 16:00:00	11.86	149.38	0.31	7.89	9.86	0.00	0.07
EAS-DS	2026-06-05 16:15:00	11.94	148.45	0.31	7.84	9.82	0.00	0.07
EAS-DS	2026-06-05 16:30:00	11.96	142.60	0.31	7.87	9.96	0.00	0.07
EAS-DS	2026-06-05 16:45:00	11.95	141.25	0.31	7.79	9.75	0.00	0.07
EAS-DS	2026-06-05 17:00:00	12.01	148.74	0.30	7.87	9.91	0.00	0.07
EAS-DS	2026-06-05 17:15:00	12.04	145.91	0.30	7.81	9.89	0.00	0.07
EAS-DS	2026-06-05 17:30:00	12.04	150.09	0.29	7.89	9.90	0.00	0.07
EAS-DS	2026-06-05 17:45:00	11.99	146.25	0.29	7.79	9.82	0.00	0.07
EAS-DS	2026-06-05 18:00:00	12.00	145.70	0.29	7.87	9.97	0.00	0.07
EAS-DS	2026-06-05 18:15:00	11.98	145.01	0.29	7.87	9.96	0.00	0.07
EAS-DS	2026-06-05 18:30:00	11.98	149.84	0.29	7.88	10.12	0.00	0.07
EAS-DS	2026-06-05 18:45:00	11.91	150.04	0.29	7.88	10.15	0.00	0.07
EAS-DS	2026-06-05 19:00:00	11.87	147.44	0.29	7.85	10.00	0.00	0.07
EAS-DS	2026-06-05 19:15:00	11.81	145.70	0.29	7.86	10.01	0.00	0.07
EAS-DS	2026-06-05 19:30:00	11.84	140.26	0.29	7.66	9.59	0.00	0.07
EAS-DS	2026-06-05 19:45:00	11.74	138.30	0.30	7.77	9.80	0.00	0.07
EAS-DS	2026-06-05 20:00:00	11.64	147.87	0.29	7.84	10.02	0.00	0.07
EAS-DS	2026-06-05 20:15:00	11.62	147.37	0.29	7.88	10.09	0.00	0.07
EAS-DS	2026-06-05 20:30:00	11.59	147.06	0.29	7.88	10.09	0.00	0.07
EAS-DS	2026-06-05 20:45:00	11.54	147.71	0.29	7.86	10.15	0.00	0.07
EAS-DS	2026-06-05 21:00:00	11.53	147.18	0.29	7.88	10.14	624.44	0.07
EAS-DS	2026-06-05 21:15:00	11.57	140.26	0.29	7.80	9.94	0.00	0.07
EAS-DS	2026-06-05 21:30:00	11.46	147.16	0.29	7.87	10.17	0.00	0.07
EAS-DS	2026-06-05 21:45:00	11.42	148.64	0.29	7.84	10.13	0.00	0.07
EAS-DS	2026-06-05 22:00:00	11.43	150.12	0.29	7.87	10.25	0.00	0.07
EAS-DS	2026-06-05 22:15:00	11.48	146.10	0.29	7.76	9.91	0.00	0.07
EAS-DS	2026-06-05 22:30:00	11.48	144.90	0.29	7.85	10.02	0.00	0.07
EAS-DS	2026-06-05 22:45:00	11.49	145.65	0.29	7.87	10.04	0.00	0.07
EAS-DS	2026-06-05 23:00:00	11.38	150.53	0.29	7.86	10.22	0.00	0.07
EAS-DS	2026-06-05 23:15:00	11.40	151.50	0.29	7.86	10.22	0.00	0.07
EAS-DS	2026-06-05 23:30:00	11.42	152.10	0.29	7.87	10.18	0.00	0.07
EAS-DS	2026-06-05 23:45:00	11.42	153.67	0.29	7.85	10.21	0.00	0.07
EAS-DS	2026-06-06 00:00:00	11.52	151.94	0.29	7.86	10.06	0.00	0.07
EAS-DS	2026-06-06 00:15:00	11.60	151.57	0.29	7.86	9.99	0.00	0.07
EAS-DS	2026-06-06 00:30:00	11.42	139.47	0.30	7.70	9.79	0.00	0.07
EAS-DS	2026-06-06 00:45:00	11.40	154.13	0.30	7.83	10.19	0.00	0.07
EAS-DS	2026-06-06 01:00:00	11.31	150.66	0.30	7.83	10.07	0.00	0.07
EAS-DS	2026-06-06 01:15:00	11.42	153.54	0.30	7.84	10.16	0.00	0.07
EAS-DS	2026-06-06 01:30:00	11.46	149.35	0.30	7.86	10.02	0.00	0.07
EAS-DS	2026-06-06 01:45:00	11.46	146.03	0.30	7.85	10.00	0.00	0.07
EAS-DS	2026-06-06 02:00:00	11.32	149.98	0.30	7.84	10.12	0.00	0.07
EAS-DS	2026-06-06 02:15:00	11.33	151.72	0.30	7.86	10.23	0.00	0.07
EAS-DS	2026-06-06 02:30:00	11.42	148.26	0.30	7.88	10.06	0.00	0.07
EAS-DS	2026-06-06 02:45:00	11.47	148.31	0.30	7.87	10.02	0.00	0.07
EAS-DS	2026-06-06 03:00:00	11.41	151.06	0.30	7.87	10.12	0.00	0.07
EAS-DS	2026-06-06 03:15:00	11.36	155.68	0.30	7.85	10.12	0.00	0.07
EAS-DS	2026-06-06 03:30:00	11.59	160.11	0.29	7.88	10.05	0.00	0.08

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-06 03:45:00	11.49	154.68	0.29	7.87	10.08	0.00	0.07
EAS-DS	2026-06-06 04:00:00	11.48	147.47	0.30	7.80	9.87	0.00	0.07
EAS-DS	2026-06-06 04:15:00	11.46	148.09	0.30	7.77	9.70	0.00	0.07
EAS-DS	2026-06-06 04:30:00	11.40	144.39	0.30	7.71	9.72	0.00	0.07
EAS-DS	2026-06-06 04:45:00	11.29	153.08	0.30	7.85	10.19	0.00	0.07
EAS-DS	2026-06-06 05:00:00	11.24	150.40	0.30	7.84	10.08	0.00	0.07
EAS-DS	2026-06-06 05:15:00	11.27	152.45	0.30	7.85	10.18	0.00	0.07
EAS-DS	2026-06-06 05:30:00	11.25	151.71	0.29	7.85	10.19	0.00	0.07
EAS-DS	2026-06-06 05:45:00	11.25	151.54	0.30	7.85	10.24	0.00	0.07
EAS-DS	2026-06-06 06:00:00	11.23	145.59	0.30	7.84	10.08	0.00	0.07
EAS-DS	2026-06-06 06:15:00	11.25	148.29	0.30	7.86	10.18	0.00	0.07
EAS-DS	2026-06-06 06:30:00	11.21	149.99	0.30	7.84	10.12	0.00	0.07
EAS-DS	2026-06-06 06:45:00	11.18	148.94	0.30	7.82	10.00	0.00	0.07
EAS-DS	2026-06-06 07:00:00	11.23	150.33	0.30	7.84	10.15	0.00	0.07
EAS-DS	2026-06-06 07:15:00	11.26	149.86	0.30	7.85	10.19	0.00	0.07
EAS-DS	2026-06-06 07:30:00	11.24	150.14	0.30	7.85	10.20	0.00	0.07
EAS-DS	2026-06-06 07:45:00	11.27	146.71	0.30	7.84	10.03	0.00	0.07
EAS-DS	2026-06-06 08:00:00	11.27	139.92	0.30	7.74	9.76	0.00	0.07
EAS-DS	2026-06-06 08:15:00	11.28	137.92	0.30	7.83	10.09	0.00	0.07
EAS-DS	2026-06-06 08:30:00	11.22	140.49	0.30	7.83	10.02	0.00	0.07
EAS-DS	2026-06-06 08:45:00	11.28	144.98	0.30	7.84	10.19	0.00	0.07
EAS-DS	2026-06-06 09:00:00	11.28	143.47	0.30	7.82	10.04	0.00	0.07
EAS-DS	2026-06-06 09:15:00	11.33	147.37	0.30	7.83	10.23	0.00	0.07
EAS-DS	2026-06-06 09:30:00	11.39	146.20	0.30	7.84	10.07	0.00	0.07
EAS-DS	2026-06-06 09:45:00	11.47	145.23	0.31	7.83	10.02	0.00	0.07
EAS-DS	2026-06-06 10:00:00	11.50	140.09	0.31	7.81	9.99	0.00	0.07
EAS-DS	2026-06-06 10:15:00	11.63	140.67	0.31	7.83	9.91	0.00	0.07
EAS-DS	2026-06-06 10:30:00	11.75	139.01	0.30	7.80	9.93	0.00	0.07
EAS-DS	2026-06-06 10:45:00	11.93	149.29	0.30	7.86	10.06	0.00	0.07
EAS-DS	2026-06-06 11:00:00	12.00	148.11	0.30	7.86	9.98	0.00	0.07
EAS-DS	2026-06-06 11:15:00	12.11	145.66	0.28	7.86	9.91	0.00	0.07
EAS-DS	2026-06-06 11:30:00	12.18	144.79	0.28	7.85	9.86	0.00	0.07
EAS-DS	2026-06-06 11:45:00	12.15	145.27	0.29	7.86	9.88	0.00	0.07
EAS-DS	2026-06-06 12:00:00	12.19	149.74	0.28	7.90	10.09	0.00	0.07
EAS-DS	2026-06-06 12:15:00	12.19	148.47	0.29	7.89	9.95	0.00	0.07
EAS-DS	2026-06-06 12:30:00	12.31	150.68	0.29	7.90	10.09	0.00	0.07
EAS-DS	2026-06-06 12:45:00	12.35	151.27	0.29	7.91	10.09	0.00	0.07
EAS-DS	2026-06-06 13:00:00	12.39	150.80	0.29	7.91	10.06	0.00	0.07
EAS-DS	2026-06-06 13:15:00	12.44	149.40	0.29	7.91	9.98	0.00	0.07
EAS-DS	2026-06-06 13:30:00	12.59	136.31	0.29	7.81	9.66	0.00	0.06
EAS-DS	2026-06-06 13:45:00	12.66	149.90	0.29	7.93	9.99	0.00	0.07
EAS-DS	2026-06-06 14:00:00	12.63	148.47	0.29	7.91	10.00	0.00	0.07
EAS-DS	2026-06-06 14:15:00	12.49	151.42	0.29	7.91	10.02	0.00	0.07
EAS-DS	2026-06-06 14:30:00	12.43	150.99	0.29	7.91	10.05	0.00	0.07
EAS-DS	2026-06-06 14:45:00	12.44	149.92	0.29	7.92	10.06	0.00	0.07
EAS-DS	2026-06-06 15:00:00	12.58	144.05	0.29	7.91	9.99	0.00	0.07
EAS-DS	2026-06-06 15:15:00	12.52	144.70	0.30	7.89	9.79	0.00	0.07
EAS-DS	2026-06-06 15:30:00	12.47	144.26	0.30	7.86	9.76	0.00	0.07
EAS-DS	2026-06-06 15:45:00	12.52	147.16	0.30	7.92	10.00	0.00	0.07
EAS-DS	2026-06-06 16:00:00	12.49	150.20	0.29	7.91	10.04	0.00	0.07
EAS-DS	2026-06-06 16:15:00	12.37	150.23	0.29	7.91	10.05	0.00	0.07
EAS-DS	2026-06-06 16:30:00	12.41	150.98	0.29	7.92	10.05	0.00	0.07
EAS-DS	2026-06-06 16:45:00	12.43	142.34	0.30	7.72	9.38	0.00	0.07
EAS-DS	2026-06-06 17:00:00	12.37	149.76	0.29	7.91	10.02	0.00	0.07
EAS-DS	2026-06-06 17:15:00	12.32	145.85	0.30	7.92	10.06	0.00	0.07

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-06 17:30:00	12.27	148.85	0.29	7.91	10.05	0.00	0.07
EAS-DS	2026-06-06 17:45:00	12.37	151.05	0.30	7.87	9.88	0.00	0.07
EAS-DS	2026-06-06 18:00:00	12.28	149.59	0.30	7.88	9.97	0.00	0.07
EAS-DS	2026-06-06 18:15:00	12.15	149.54	0.30	7.92	10.12	0.00	0.07
EAS-DS	2026-06-06 18:30:00	12.10	148.64	0.29	7.92	10.12	0.00	0.07
EAS-DS	2026-06-06 18:45:00	12.08	140.68	0.30	7.84	9.86	0.00	0.07
EAS-DS	2026-06-06 19:00:00	12.07	148.34	0.29	7.91	10.14	0.00	0.07
EAS-DS	2026-06-06 19:15:00	12.05	147.13	0.30	7.92	10.10	0.00	0.07
EAS-DS	2026-06-06 19:30:00	11.99	147.34	0.29	7.92	10.15	0.00	0.07
EAS-DS	2026-06-06 19:45:00	11.95	147.48	0.30	7.91	10.17	0.00	0.07
EAS-DS	2026-06-06 20:00:00	11.96	146.05	0.30	7.88	10.05	0.00	0.07
EAS-DS	2026-06-06 20:15:00	11.91	147.30	0.30	7.92	10.18	0.00	0.07
EAS-DS	2026-06-06 20:30:00	11.88	146.94	0.30	7.91	10.19	0.00	0.07
EAS-DS	2026-06-06 20:45:00	11.92	147.64	0.30	7.90	10.18	0.00	0.07
EAS-DS	2026-06-06 21:00:00	11.86	147.26	0.30	7.91	10.19	0.00	0.07
EAS-DS	2026-06-06 21:15:00	11.90	135.24	0.30	7.82	9.98	0.00	0.06
EAS-DS	2026-06-06 21:30:00	11.90	143.42	0.30	7.84	9.96	0.00	0.07
EAS-DS	2026-06-06 21:45:00	11.78	147.40	0.30	7.91	10.21	0.00	0.07
EAS-DS	2026-06-06 22:00:00	11.76	147.45	0.30	7.91	10.23	0.00	0.07
EAS-DS	2026-06-06 22:15:00	11.76	146.60	0.30	7.91	10.20	0.00	0.07
EAS-DS	2026-06-06 22:30:00	11.78	143.62	0.30	7.87	9.96	0.00	0.07
EAS-DS	2026-06-06 22:45:00	11.83	145.02	0.31	7.87	10.03	0.00	0.07
EAS-DS	2026-06-06 23:00:00	11.81	148.19	0.30	7.92	10.21	0.00	0.07
EAS-DS	2026-06-06 23:15:00	11.75	148.29	0.30	7.92	10.21	0.00	0.07
EAS-DS	2026-06-06 23:30:00	11.74	147.58	0.30	7.89	10.18	0.00	0.07
EAS-DS	2026-06-06 23:45:00	11.67	147.47	0.30	7.93	10.23	0.00	0.07
EAS-DS	2026-06-07 00:00:00	11.68	147.92	0.30	7.91	10.23	0.00	0.07
EAS-DS	2026-06-07 00:15:00	11.56	144.94	0.30	7.91	10.22	0.00	0.07
EAS-DS	2026-06-07 00:30:00	11.71	146.06	0.30	7.89	10.10	0.00	0.07
EAS-DS	2026-06-07 00:45:00	11.73	144.77	0.31	7.87	10.03	0.00	0.07
EAS-DS	2026-06-07 01:00:00	11.70	144.39	0.31	7.86	10.04	0.00	0.07
EAS-DS	2026-06-07 01:15:00	11.65	145.98	0.31	7.91	10.21	0.00	0.07
EAS-DS	2026-06-07 01:30:00	11.58	147.34	0.30	7.90	10.27	0.00	0.07
EAS-DS	2026-06-07 01:45:00	11.60	146.82	0.30	7.91	10.24	0.00	0.07
EAS-DS	2026-06-07 02:00:00	11.65	146.00	0.30	7.90	10.24	0.00	0.07
EAS-DS	2026-06-07 02:15:00	11.59	146.92	0.30	7.91	10.24	0.00	0.07
EAS-DS	2026-06-07 02:30:00	11.56	147.28	0.30	7.91	10.26	0.00	0.07
EAS-DS	2026-06-07 02:45:00	11.58	147.07	0.30	7.90	10.26	0.00	0.07
EAS-DS	2026-06-07 03:00:00	11.43	143.64	0.30	7.88	10.29	0.00	0.07
EAS-DS	2026-06-07 03:15:00	11.62	145.50	0.30	7.91	10.23	0.00	0.07
EAS-DS	2026-06-07 03:30:00	11.57	147.03	0.30	7.91	10.27	0.00	0.07
EAS-DS	2026-06-07 03:45:00	11.46	142.23	0.30	7.82	10.03	0.00	0.07
EAS-DS	2026-06-07 04:00:00	11.54	147.27	0.30	7.90	10.27	0.00	0.07
EAS-DS	2026-06-07 04:15:00	11.56	146.17	0.30	7.89	10.19	0.00	0.07
EAS-DS	2026-06-07 04:30:00	11.63	145.01	0.30	7.87	10.03	0.00	0.07
EAS-DS	2026-06-07 04:45:00	11.50	135.71	0.31	7.83	10.00	0.00	0.06
EAS-DS	2026-06-07 05:00:00	11.52	147.34	0.30	7.90	10.29	0.00	0.07
EAS-DS	2026-06-07 05:15:00	11.54	146.95	0.30	7.90	10.27	0.00	0.07
EAS-DS	2026-06-07 05:30:00	11.54	147.05	0.30	7.89	10.26	0.00	0.07
EAS-DS	2026-06-07 05:45:00	11.54	147.35	0.30	7.90	10.27	0.00	0.07
EAS-DS	2026-06-07 06:00:00	11.56	147.13	0.30	7.89	10.26	0.00	0.07
EAS-DS	2026-06-07 06:15:00	11.54	147.02	0.30	7.90	10.29	0.00	0.07
EAS-DS	2026-06-07 06:30:00	11.53	147.17	0.30	7.91	10.27	0.00	0.07
EAS-DS	2026-06-07 06:45:00	11.49	146.83	0.31	7.89	10.31	0.00	0.07
EAS-DS	2026-06-07 07:00:00	11.53	147.06	0.30	7.91	10.30	0.00	0.07

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-07 07:15:00	11.51	147.19	0.31	7.89	10.31	0.00	0.07
EAS-DS	2026-06-07 07:30:00	11.49	146.47	0.30	7.91	10.29	0.00	0.07
EAS-DS	2026-06-07 07:45:00	11.55	142.70	0.31	7.89	10.22	0.00	0.07
EAS-DS	2026-06-07 08:00:00	11.55	143.42	0.31	7.90	10.20	0.00	0.07
EAS-DS	2026-06-07 08:15:00	11.56	144.11	0.31	7.92	10.25	0.00	0.07
EAS-DS	2026-06-07 08:30:00	11.59	144.12	0.30	7.93	10.25	0.00	0.07
EAS-DS	2026-06-07 08:45:00	11.60	144.65	0.31	7.91	10.22	0.00	0.07
EAS-DS	2026-06-07 09:00:00	11.64	144.16	0.31	7.93	10.23	0.00	0.07
EAS-DS	2026-06-07 09:15:00	11.69	146.89	0.30	7.91	10.25	0.00	0.07
EAS-DS	2026-06-07 09:30:00	11.77	146.61	0.30	7.91	10.26	0.00	0.07
EAS-DS	2026-06-07 09:45:00	11.77	144.26	0.30	7.92	10.22	0.00	0.07
EAS-DS	2026-06-07 10:00:00	11.81	147.52	0.30	7.92	10.24	0.00	0.07
EAS-DS	2026-06-07 10:15:00	11.81	142.46	0.30	7.86	9.99	0.00	0.07
EAS-DS	2026-06-07 10:30:00	11.98	145.65	0.30	7.95	10.19	0.00	0.07
EAS-DS	2026-06-07 10:45:00	12.08	143.02	0.30	7.92	10.09	0.00	0.07
EAS-DS	2026-06-07 11:00:00	12.06	147.80	0.30	7.93	10.17	0.00	0.07
EAS-DS	2026-06-07 11:15:00	12.06	146.80	0.30	7.93	10.16	0.00	0.07
EAS-DS	2026-06-07 11:30:00	12.04	143.11	0.31	7.86	9.94	0.00	0.07
EAS-DS	2026-06-07 11:45:00	12.02	142.50	0.31	7.85	9.90	0.00	0.07
EAS-DS	2026-06-07 12:00:00	11.99	147.29	0.30	7.92	10.18	0.00	0.07
EAS-DS	2026-06-07 12:15:00	11.99	146.93	0.30	7.94	10.18	0.00	0.07
EAS-DS	2026-06-07 12:30:00	11.96	145.78	0.30	7.93	10.19	0.00	0.07
EAS-DS	2026-06-07 12:45:00	12.16	144.31	0.18	7.90	10.04	10.02	0.07
EAS-DS	2026-06-07 13:00:00	12.02	147.74	0.19	7.89	9.99	9.71	0.07
EAS-DS	2026-06-07 13:15:00	12.05	144.00	0.20	7.93	9.99	9.97	0.07
EAS-DS	2026-06-07 13:30:00	12.07	147.41	0.21	7.93	9.88	9.16	0.07
EAS-DS	2026-06-07 13:45:00	12.07	140.86	0.22	7.92	10.07	10.18	0.07
EAS-DS	2026-06-07 14:00:00	12.22	145.94	0.23	7.94	9.86	9.60	0.07
EAS-DS	2026-06-07 14:15:00	12.36	146.32	0.23	7.93	9.97	9.61	0.07
EAS-DS	2026-06-07 14:30:00	12.26	146.91	0.24	7.93	9.78	9.59	0.07
EAS-DS	2026-06-07 14:45:00	12.31	144.27	0.24	7.93	9.98	9.68	0.07
EAS-DS	2026-06-07 15:00:00	12.22	145.99	0.25	7.94	9.67	9.32	0.07
EAS-DS	2026-06-07 15:15:00	12.18	146.50	0.25	7.94	10.06	9.48	0.07
EAS-DS	2026-06-07 15:30:00	12.19	140.26	0.26	7.92	9.69	9.13	0.07
EAS-DS	2026-06-07 15:45:00	12.15	145.43	0.26	7.93	10.05	9.21	0.07
EAS-DS	2026-06-07 16:00:00	12.24	145.09	0.26	7.92	9.67	13.59	0.07
EAS-DS	2026-06-07 16:15:00	12.13	143.75	0.27	7.94	10.01	10.09	0.07
EAS-DS	2026-06-07 16:30:00	12.31	145.67	0.27	7.92	9.63	9.14	0.07
EAS-DS	2026-06-07 16:45:00	12.24	147.53	0.27	7.91	10.04	9.41	0.07
EAS-DS	2026-06-07 17:00:00	12.30	145.97	0.27	7.92	9.65	9.19	0.07
EAS-DS	2026-06-07 17:15:00	12.20	147.23	0.28	7.94	10.07	9.24	0.07
EAS-DS	2026-06-07 17:30:00	12.12	142.29	0.28	7.92	9.83	9.82	0.07
EAS-DS	2026-06-07 17:45:00	12.17	144.11	0.28	7.93	9.90	9.40	0.07
EAS-DS	2026-06-07 18:00:00	12.36	144.93	0.28	7.91	9.66	9.24	0.07
EAS-DS	2026-06-07 18:15:00	12.23	147.93	0.28	7.90	9.85	9.26	0.07
EAS-DS	2026-06-07 18:30:00	12.28	146.20	0.28	7.92	9.73	9.33	0.07
EAS-DS	2026-06-07 18:45:00	12.08	145.49	0.29	7.92	8.71	23.55	0.07
EAS-DS	2026-06-07 19:00:00	12.02	139.91	0.29	7.91	9.68	9.25	0.07
EAS-DS	2026-06-07 19:15:00	11.95	144.32	0.29	7.89	9.00	9.14	0.07
EAS-DS	2026-06-07 19:30:00	12.13	144.42	0.29	7.92	9.86	9.93	0.07
EAS-DS	2026-06-07 19:45:00	11.96	147.53	0.29	7.89	9.44	9.22	0.07
EAS-DS	2026-06-07 20:00:00	11.86	145.00	0.29	7.91	10.01	9.14	0.07
EAS-DS	2026-06-07 20:15:00	11.79	143.53	0.30	7.88	9.82	9.71	0.07
EAS-DS	2026-06-07 20:30:00	11.86	144.56	0.29	7.93	10.04	9.21	0.07
EAS-DS	2026-06-07 20:45:00	11.75	144.62	0.30	7.90	9.47	9.24	0.07

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-06-07 21:00:00	11.72	143.63	0.30	7.90	10.02	9.23	0.07
EAS-DS	2026-06-07 21:15:00	11.77	141.02	0.30	7.87	9.36	9.09	0.07
EAS-DS	2026-06-07 21:30:00	11.70	147.13	0.30	7.89	10.12	9.29	0.07
EAS-DS	2026-06-07 21:45:00	11.63	144.06	0.30	7.88	9.66	9.16	0.07
EAS-DS	2026-06-07 22:00:00	11.66	147.76	0.30	7.90	10.10	9.31	0.07
EAS-DS	2026-06-07 22:15:00	11.64	146.08	0.30	7.90	9.57	9.10	0.07
EAS-DS	2026-06-07 22:30:00	11.65	145.20	0.30	7.90	10.03	9.07	0.07
EAS-DS	2026-06-07 22:45:00	11.65	149.01	0.30	7.87	9.50	9.12	0.07
EAS-DS	2026-06-07 23:00:00	11.64	149.24	0.30	7.89	10.04	9.29	0.07
EAS-DS	2026-06-07 23:15:00	11.65	148.56	0.30	7.88	9.21	9.12	0.07
EAS-DS	2026-06-07 23:30:00	11.62	147.49	0.30	7.90	10.01	9.05	0.07
EAS-DS	2026-06-07 23:45:00	11.62	145.97	0.30	7.88	9.17	9.16	0.07
EAS-US	2026-06-01 00:00:00	12.15	28.88	0.12	6.78	10.02	1.80	0.01
EAS-US	2026-06-01 00:15:00	12.10	28.85	0.23	6.99	10.06	1.44	0.01
EAS-US	2026-06-01 00:30:00	12.05	28.83	0.23	7.00	10.06	1.41	0.01
EAS-US	2026-06-01 00:45:00	12.00	28.77	0.22	6.98	10.09	1.34	0.01
EAS-US	2026-06-01 01:00:00	11.96	28.80	0.13	6.69	10.09	1.33	0.01
EAS-US	2026-06-01 01:15:00	11.91	28.76	0.23	6.80	10.10	1.35	0.01
EAS-US	2026-06-01 01:30:00	11.87	28.74	0.23	6.78	10.13	1.31	0.01
EAS-US	2026-06-01 01:45:00	11.82	28.74	0.23	6.76	10.13	1.33	0.01
EAS-US	2026-06-01 02:00:00	11.78	28.75	0.12	6.75	10.15	1.39	0.01
EAS-US	2026-06-01 02:15:00	11.74	28.82	0.23	6.99	10.17	1.42	0.01
EAS-US	2026-06-01 02:30:00	11.70	28.88	0.22	6.99	10.17	1.34	0.01
EAS-US	2026-06-01 02:45:00	11.66	28.81	0.22	6.94	10.19	1.40	0.01
EAS-US	2026-06-01 03:00:00	11.61	28.79	0.12	6.68	10.19	1.30	0.01
EAS-US	2026-06-01 03:15:00	11.57	28.70	0.23	6.78	10.20	1.36	0.01
EAS-US	2026-06-01 03:30:00	11.53	28.66	0.23	6.74	10.22	1.38	0.01
EAS-US	2026-06-01 03:45:00	11.49	28.63	0.22	6.79	10.23	1.36	0.01
EAS-US	2026-06-01 04:00:00	11.45	28.63	0.12	6.81	10.24	1.33	0.01
EAS-US	2026-06-01 04:15:00	11.41	28.58	0.23	6.95	10.26	1.31	0.01
EAS-US	2026-06-01 04:30:00	11.38	28.58	0.23	6.97	10.26	1.29	0.01
EAS-US	2026-06-01 04:45:00	11.34	28.55	0.22	6.99	10.28	1.32	0.01
EAS-US	2026-06-01 05:00:00	11.30	28.53	0.13	6.70	10.28	1.39	0.01
EAS-US	2026-06-01 05:15:00	11.27	28.49	0.23	6.80	10.29	1.35	0.01
EAS-US	2026-06-01 05:30:00	11.23	28.48	0.23	6.76	10.31	1.31	0.01
EAS-US	2026-06-01 05:45:00	11.20	28.45	0.23	6.77	10.34	1.32	0.01
EAS-US	2026-06-01 06:00:00	11.17	28.42	0.12	6.82	10.34	1.31	0.01
EAS-US	2026-06-01 06:15:00	11.14	28.35	0.23	6.98	10.35	1.25	0.01
EAS-US	2026-06-01 06:30:00	11.12	28.32	0.23	6.97	10.37	1.29	0.01
EAS-US	2026-06-01 06:45:00	11.10	28.26	0.22	7.00	10.37	1.30	0.01
EAS-US	2026-06-01 07:00:00	11.09	28.26	0.12	6.71	10.40	1.32	0.01
EAS-US	2026-06-01 07:15:00	11.08	28.18	0.23	6.82	10.41	1.28	0.01
EAS-US	2026-06-01 07:30:00	11.08	28.17	0.23	6.80	10.40	1.23	0.01
EAS-US	2026-06-01 07:45:00	11.08	28.10	0.23	6.82	10.42	1.28	0.01
EAS-US	2026-06-01 08:00:00	11.10	28.09	0.11	6.81	10.43	1.30	0.01
EAS-US	2026-06-01 08:15:00	11.12	28.05	0.23	7.00	10.44	1.28	0.01
EAS-US	2026-06-01 08:30:00	11.16	28.00	0.23	7.00	10.44	1.30	0.01
EAS-US	2026-06-01 08:45:00	11.21	27.98	0.22	7.02	10.42	1.35	0.01
EAS-US	2026-06-01 09:00:00	11.29	27.97	0.12	6.74	10.44	1.33	0.01
EAS-US	2026-06-01 09:15:00	11.35	27.93	0.23	6.80	10.44	1.27	0.01
EAS-US	2026-06-01 09:30:00	11.40	27.96	0.23	6.84	10.44	1.35	0.01
EAS-US	2026-06-01 09:45:00	11.44	27.98	0.23	6.83	10.44	1.31	0.01
EAS-US	2026-06-01 10:00:00	11.49	28.01	0.12	6.87	10.43	1.28	0.01
EAS-US	2026-06-01 10:15:00	11.56	27.92	0.23	7.05	10.42	1.34	0.01
EAS-US	2026-06-01 10:30:00	11.71	27.82	0.23	7.06	10.45	1.32	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-01 10:45:00	11.90	27.77	0.22	7.09	10.45	1.37	0.01
EAS-US	2026-06-01 11:00:00	12.15	27.74	0.13	6.83	10.43	1.32	0.01
EAS-US	2026-06-01 11:15:00	12.36	27.74	0.23	6.91	10.43	1.34	0.01
EAS-US	2026-06-01 11:30:00	12.52	27.72	0.22	6.88	10.40	1.36	0.01
EAS-US	2026-06-01 11:45:00	12.75	27.71	0.22	6.93	10.39	1.45	0.01
EAS-US	2026-06-01 12:00:00	12.93	27.73	0.12	6.93	10.36	1.41	0.01
EAS-US	2026-06-01 12:15:00	12.96	27.72	0.22	7.13	10.30	1.38	0.01
EAS-US	2026-06-01 12:30:00	13.03	27.73	0.21	7.14	10.26	1.40	0.01
EAS-US	2026-06-01 12:45:00	13.16	27.76	0.21	7.13	10.18	1.41	0.01
EAS-US	2026-06-01 13:00:00	13.28	27.80	0.12	6.85	10.12	1.36	0.01
EAS-US	2026-06-01 13:15:00	13.43	27.79	0.22	6.89	10.06	1.43	0.01
EAS-US	2026-06-01 13:30:00	13.59	27.79	0.22	6.91	10.02	1.40	0.01
EAS-US	2026-06-01 13:45:00	13.74	27.84	0.22	6.86	9.96	1.43	0.01
EAS-US	2026-06-01 14:00:00	13.83	27.84	0.12	6.91	9.92	1.44	0.01
EAS-US	2026-06-01 14:15:00	13.97	27.86	0.22	7.09	9.90	1.41	0.01
EAS-US	2026-06-01 14:30:00	14.07	27.87	0.22	7.08	9.86	1.46	0.01
EAS-US	2026-06-01 14:45:00	14.19	27.89	0.22	7.10	9.85	1.47	0.01
EAS-US	2026-06-01 15:00:00	14.26	27.90	0.13	6.84	9.84	1.39	0.01
EAS-US	2026-06-01 15:15:00	14.32	27.90	0.23	6.86	9.81	1.44	0.01
EAS-US	2026-06-01 15:30:00	14.38	27.93	0.22	6.91	9.79	1.45	0.01
EAS-US	2026-06-01 15:45:00	14.46	27.98	0.22	6.90	9.78	1.49	0.01
EAS-US	2026-06-01 16:00:00	14.52	28.07	0.13	6.93	9.76	1.49	0.01
EAS-US	2026-06-01 16:15:00	14.55	28.05	0.22	7.11	9.76	1.48	0.01
EAS-US	2026-06-01 16:30:00	14.58	28.15	0.22	7.10	9.73	1.48	0.01
EAS-US	2026-06-01 16:45:00	14.52	28.27	0.22	7.08	9.69	1.50	0.01
EAS-US	2026-06-01 17:00:00	14.46	28.42	0.13	6.80	9.67	1.43	0.01
EAS-US	2026-06-01 17:15:00	14.40	28.51	0.23	6.87	9.67	1.48	0.01
EAS-US	2026-06-01 17:30:00	14.28	28.61	0.22	6.80	9.68	1.51	0.01
EAS-US	2026-06-01 17:45:00	14.18	28.69	0.22	6.80	9.67	1.46	0.01
EAS-US	2026-06-01 18:00:00	14.10	28.87	0.12	6.81	9.66	1.55	0.01
EAS-US	2026-06-01 18:15:00	14.01	28.91	0.23	7.02	9.67	1.48	0.01
EAS-US	2026-06-01 18:30:00	13.94	28.96	0.22	7.02	9.66	1.42	0.01
EAS-US	2026-06-01 18:45:00	13.86	29.03	0.22	7.01	9.68	1.46	0.01
EAS-US	2026-06-01 19:00:00	13.80	29.11	0.13	6.73	9.70	1.38	0.01
EAS-US	2026-06-01 19:15:00	13.74	29.04	0.23	6.76	9.71	1.44	0.01
EAS-US	2026-06-01 19:30:00	13.69	29.03	0.23	6.81	9.73	1.55	0.01
EAS-US	2026-06-01 19:45:00	13.65	29.05	0.23	6.79	9.73	1.37	0.01
EAS-US	2026-06-01 20:00:00	13.61	29.12	0.12	6.80	9.73	1.42	0.01
EAS-US	2026-06-01 20:15:00	13.56	29.17	0.23	7.02	9.73	1.40	0.01
EAS-US	2026-06-01 20:30:00	13.52	29.24	0.23	7.02	9.72	1.47	0.01
EAS-US	2026-06-01 20:45:00	13.48	29.27	0.23	7.02	9.73	1.45	0.01
EAS-US	2026-06-01 21:00:00	13.44	29.36	0.13	6.73	9.73	1.41	0.01
EAS-US	2026-06-01 21:15:00	13.39	29.37	0.24	6.80	9.71	1.79	0.01
EAS-US	2026-06-01 21:30:00	13.35	29.41	0.23	6.78	9.72	1.44	0.01
EAS-US	2026-06-01 21:45:00	13.30	29.43	0.23	6.76	9.73	1.43	0.01
EAS-US	2026-06-01 22:00:00	13.26	29.47	0.12	6.80	9.73	1.43	0.01
EAS-US	2026-06-01 22:15:00	13.22	29.45	0.23	7.00	9.75	1.42	0.01
EAS-US	2026-06-01 22:30:00	13.19	29.41	0.23	6.99	9.74	1.42	0.01
EAS-US	2026-06-01 22:45:00	13.15	29.41	0.23	6.98	9.75	1.43	0.01
EAS-US	2026-06-01 23:00:00	13.12	29.46	0.13	6.71	9.77	1.35	0.01
EAS-US	2026-06-01 23:15:00	13.08	29.44	0.24	6.76	9.78	1.42	0.01
EAS-US	2026-06-01 23:30:00	13.05	29.41	0.23	6.79	9.78	1.42	0.01
EAS-US	2026-06-01 23:45:00	13.01	29.44	0.23	6.77	9.79	1.40	0.01
EAS-US	2026-06-02 00:00:00	12.98	29.47	0.13	6.82	9.80	1.53	0.01
EAS-US	2026-06-02 00:15:00	12.94	29.46	0.23	6.98	9.81	1.39	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-02 00:30:00	12.90	29.46	0.23	6.99	9.83	1.41	0.01
EAS-US	2026-06-02 00:45:00	12.86	29.45	0.22	6.98	9.84	1.35	0.01
EAS-US	2026-06-02 01:00:00	12.83	29.50	0.13	6.66	9.84	1.40	0.01
EAS-US	2026-06-02 01:15:00	12.80	29.71	0.23	6.81	9.85	1.40	0.01
EAS-US	2026-06-02 01:30:00	12.77	29.62	0.23	6.77	9.85	1.38	0.01
EAS-US	2026-06-02 01:45:00	12.74	29.56	0.23	6.77	9.88	1.40	0.01
EAS-US	2026-06-02 02:00:00	12.71	29.51	0.13	6.75	9.87	1.45	0.01
EAS-US	2026-06-02 02:15:00	12.68	29.47	0.23	6.98	9.87	1.43	0.01
EAS-US	2026-06-02 02:30:00	12.64	29.47	0.23	6.94	9.88	1.42	0.01
EAS-US	2026-06-02 02:45:00	12.60	29.46	0.22	6.98	9.90	1.37	0.01
EAS-US	2026-06-02 03:00:00	12.56	29.46	0.13	6.71	9.90	1.40	0.01
EAS-US	2026-06-02 03:15:00	12.52	29.42	0.23	6.77	9.92	1.39	0.01
EAS-US	2026-06-02 03:30:00	12.49	29.38	0.23	6.78	9.92	1.41	0.01
EAS-US	2026-06-02 03:45:00	12.45	29.38	0.23	6.77	9.93	1.41	0.01
EAS-US	2026-06-02 04:00:00	12.41	29.37	0.12	6.77	9.95	1.36	0.01
EAS-US	2026-06-02 04:15:00	12.37	29.33	0.23	6.98	9.97	1.38	0.01
EAS-US	2026-06-02 04:30:00	12.33	29.30	0.23	6.99	9.96	1.35	0.01
EAS-US	2026-06-02 04:45:00	12.29	29.30	0.23	6.99	9.98	1.43	0.01
EAS-US	2026-06-02 05:00:00	12.25	29.28	0.13	6.73	9.98	1.35	0.01
EAS-US	2026-06-02 05:15:00	12.21	29.22	0.23	6.77	10.00	1.37	0.01
EAS-US	2026-06-02 05:30:00	12.17	29.20	0.23	6.77	10.02	1.35	0.01
EAS-US	2026-06-02 05:45:00	12.13	29.15	0.23	6.79	10.03	1.38	0.01
EAS-US	2026-06-02 06:00:00	12.09	29.12	0.13	6.79	10.04	1.35	0.01
EAS-US	2026-06-02 06:15:00	12.06	29.05	0.23	6.99	10.07	1.36	0.01
EAS-US	2026-06-02 06:30:00	12.03	28.99	0.23	7.01	10.08	1.34	0.01
EAS-US	2026-06-02 06:45:00	12.01	28.94	0.23	7.02	10.09	1.33	0.01
EAS-US	2026-06-02 07:00:00	11.99	28.94	0.14	6.73	10.10	1.28	0.01
EAS-US	2026-06-02 07:15:00	11.98	28.90	0.23	6.76	10.11	1.37	0.01
EAS-US	2026-06-02 07:30:00	11.98	28.85	0.23	6.82	10.12	1.37	0.01
EAS-US	2026-06-02 07:45:00	11.98	28.82	0.23	6.80	10.12	1.39	0.01
EAS-US	2026-06-02 08:00:00	11.98	28.81	0.13	6.85	10.14	1.39	0.01
EAS-US	2026-06-02 08:15:00	12.00	28.76	0.23	7.01	10.13	1.38	0.01
EAS-US	2026-06-02 08:30:00	12.02	28.74	0.22	7.01	10.15	1.43	0.01
EAS-US	2026-06-02 08:45:00	12.06	28.71	0.22	7.02	10.15	1.36	0.01
EAS-US	2026-06-02 09:00:00	12.13	28.68	0.13	6.73	10.16	1.31	0.01
EAS-US	2026-06-02 09:15:00	12.18	28.60	0.23	6.82	10.16	1.40	0.01
EAS-US	2026-06-02 09:30:00	12.23	28.61	0.23	6.82	10.16	1.36	0.01
EAS-US	2026-06-02 09:45:00	12.26	28.73	0.23	6.79	10.15	1.63	0.01
EAS-US	2026-06-02 10:00:00	12.30	28.70	0.13	6.84	10.15	1.37	0.01
EAS-US	2026-06-02 10:15:00	12.37	28.63	0.23	7.04	10.16	1.42	0.01
EAS-US	2026-06-02 10:30:00	12.53	28.54	0.22	7.07	10.19	1.40	0.01
EAS-US	2026-06-02 10:45:00	12.73	28.47	0.22	7.07	10.18	1.45	0.01
EAS-US	2026-06-02 11:00:00	12.97	28.38	0.13	6.85	10.18	1.39	0.01
EAS-US	2026-06-02 11:15:00	13.19	28.34	0.23	6.89	10.17	1.41	0.01
EAS-US	2026-06-02 11:30:00	13.39	28.34	0.22	6.92	10.16	1.41	0.01
EAS-US	2026-06-02 11:45:00	13.61	28.30	0.22	6.91	10.13	1.52	0.01
EAS-US	2026-06-02 12:00:00	13.85	28.30	0.13	6.96	10.10	1.45	0.01
EAS-US	2026-06-02 12:15:00	13.94	28.31	0.22	7.15	10.06	1.53	0.01
EAS-US	2026-06-02 12:30:00	13.98	28.30	0.22	7.16	10.00	1.48	0.01
EAS-US	2026-06-02 12:45:00	14.12	28.35	0.22	7.11	9.95	1.50	0.01
EAS-US	2026-06-02 13:00:00	14.24	28.39	0.12	6.86	9.85	1.51	0.01
EAS-US	2026-06-02 13:15:00	14.36	28.32	0.22	6.90	9.80	1.56	0.01
EAS-US	2026-06-02 13:30:00	14.50	28.33	0.22	6.94	9.76	1.53	0.01
EAS-US	2026-06-02 13:45:00	14.63	28.41	0.22	6.92	9.71	1.54	0.01
EAS-US	2026-06-02 14:00:00	14.71	28.42	0.13	6.93	9.64	1.50	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-02 14:15:00	14.86	28.41	0.22	7.12	9.63	1.54	0.01
EAS-US	2026-06-02 14:30:00	14.97	28.43	0.22	7.09	9.60	1.60	0.01
EAS-US	2026-06-02 14:45:00	15.11	28.46	0.22	7.12	9.58	1.51	0.01
EAS-US	2026-06-02 15:00:00	15.20	28.47	0.13	6.85	9.56	1.54	0.01
EAS-US	2026-06-02 15:15:00	15.28	28.50	0.22	6.92	9.53	1.55	0.01
EAS-US	2026-06-02 15:30:00	15.33	28.52	0.22	6.90	9.52	1.56	0.01
EAS-US	2026-06-02 15:45:00	15.37	28.55	0.22	6.87	9.49	1.60	0.01
EAS-US	2026-06-02 16:00:00	15.41	28.61	0.12	6.93	9.50	1.64	0.01
EAS-US	2026-06-02 16:15:00	15.41	28.66	0.22	7.11	9.47	1.61	0.01
EAS-US	2026-06-02 16:30:00	15.42	28.90	0.21	7.09	9.46	1.55	0.01
EAS-US	2026-06-02 16:45:00	15.40	29.08	0.21	7.08	9.44	1.60	0.01
EAS-US	2026-06-02 17:00:00	15.36	29.23	0.13	6.81	9.42	1.56	0.01
EAS-US	2026-06-02 17:15:00	15.27	29.26	0.22	6.88	9.42	1.54	0.01
EAS-US	2026-06-02 17:30:00	15.14	29.31	0.22	6.82	9.41	1.58	0.01
EAS-US	2026-06-02 17:45:00	15.03	29.36	0.22	6.82	9.41	1.50	0.01
EAS-US	2026-06-02 18:00:00	14.93	29.43	0.13	6.86	9.41	1.58	0.01
EAS-US	2026-06-02 18:15:00	14.82	29.48	0.23	7.04	9.41	1.49	0.01
EAS-US	2026-06-02 18:30:00	14.72	29.58	0.22	7.00	9.43	1.54	0.01
EAS-US	2026-06-02 18:45:00	14.63	29.59	0.22	7.02	9.43	1.54	0.01
EAS-US	2026-06-02 19:00:00	14.55	29.69	0.13	6.72	9.44	1.46	0.01
EAS-US	2026-06-02 19:15:00	14.48	29.67	0.23	6.79	9.46	1.49	0.01
EAS-US	2026-06-02 19:30:00	14.41	29.69	0.23	6.76	9.47	1.47	0.01
EAS-US	2026-06-02 19:45:00	14.34	29.69	0.23	6.82	9.47	1.47	0.01
EAS-US	2026-06-02 20:00:00	14.29	29.72	0.13	6.81	9.48	1.52	0.01
EAS-US	2026-06-02 20:15:00	14.23	29.76	0.23	7.00	9.49	1.44	0.01
EAS-US	2026-06-02 20:30:00	14.17	29.85	0.23	6.98	9.49	3.01	0.01
EAS-US	2026-06-02 20:45:00	14.12	29.91	0.22	6.99	9.49	1.43	0.01
EAS-US	2026-06-02 21:00:00	14.06	29.94	0.14	6.70	9.51	1.42	0.01
EAS-US	2026-06-02 21:15:00	14.01	29.92	0.23	6.75	9.51	1.49	0.01
EAS-US	2026-06-02 21:30:00	13.97	29.92	0.23	6.77	9.52	1.48	0.01
EAS-US	2026-06-02 21:45:00	13.92	29.90	0.23	6.78	9.52	1.48	0.01
EAS-US	2026-06-02 22:00:00	13.87	29.93	0.13	6.74	9.54	1.48	0.01
EAS-US	2026-06-02 22:15:00	13.83	29.92	0.23	6.98	9.54	1.46	0.01
EAS-US	2026-06-02 22:30:00	13.78	30.05	0.23	6.98	9.57	1.81	0.01
EAS-US	2026-06-02 22:45:00	13.74	29.94	0.22	6.95	9.57	1.42	0.01
EAS-US	2026-06-02 23:00:00	13.70	29.94	0.13	6.71	9.57	1.44	0.01
EAS-US	2026-06-02 23:15:00	13.66	29.90	0.23	6.81	9.59	1.48	0.01
EAS-US	2026-06-02 23:30:00	13.62	29.99	0.23	6.77	9.59	1.46	0.01
EAS-US	2026-06-02 23:45:00	13.59	29.89	0.23	6.81	9.59	12.42	0.01
EAS-US	2026-06-03 00:00:00	13.55	29.88	0.13	6.76	9.63	1.46	0.01
EAS-US	2026-06-03 00:15:00	13.51	29.89	0.23	6.98	9.63	1.48	0.01
EAS-US	2026-06-03 00:30:00	13.48	30.52	0.23	6.98	9.63	1.48	0.01
EAS-US	2026-06-03 00:45:00	13.44	29.88	0.23	6.98	9.64	1.48	0.01
EAS-US	2026-06-03 01:00:00	13.40	29.88	0.13	6.70	9.65	1.44	0.01
EAS-US	2026-06-03 01:15:00	13.36	29.89	0.24	6.74	9.67	1.61	0.01
EAS-US	2026-06-03 01:30:00	13.33	29.85	0.23	6.79	9.67	1.63	0.01
EAS-US	2026-06-03 01:45:00	13.30	29.85	0.23	6.79	9.67	1.43	0.01
EAS-US	2026-06-03 02:00:00	13.27	29.88	0.13	6.77	9.68	1.41	0.01
EAS-US	2026-06-03 02:15:00	13.24	29.85	0.23	6.98	9.69	1.45	0.01
EAS-US	2026-06-03 02:30:00	13.20	29.87	0.23	6.95	9.69	1.44	0.01
EAS-US	2026-06-03 02:45:00	13.17	29.87	0.23	6.97	9.70	1.46	0.01
EAS-US	2026-06-03 03:00:00	13.14	29.90	0.13	6.70	9.71	1.65	0.01
EAS-US	2026-06-03 03:15:00	13.11	29.91	0.24	6.80	9.72	1.42	0.01
EAS-US	2026-06-03 03:30:00	13.08	29.93	0.23	6.78	9.73	1.40	0.01
EAS-US	2026-06-03 03:45:00	13.05	29.91	0.23	6.78	9.74	1.43	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-03 04:00:00	13.03	29.93	0.14	6.79	9.74	1.42	0.01
EAS-US	2026-06-03 04:15:00	13.00	29.94	0.23	6.97	9.76	1.53	0.01
EAS-US	2026-06-03 04:30:00	12.98	29.95	0.23	6.90	9.76	1.53	0.01
EAS-US	2026-06-03 04:45:00	12.96	29.91	0.22	7.00	9.76	1.43	0.01
EAS-US	2026-06-03 05:00:00	12.94	29.96	0.13	6.71	9.78	1.47	0.01
EAS-US	2026-06-03 05:15:00	12.92	29.93	0.24	6.81	9.78	1.50	0.01
EAS-US	2026-06-03 05:30:00	12.90	29.92	0.23	6.75	9.79	1.39	0.01
EAS-US	2026-06-03 05:45:00	12.89	29.88	0.23	6.82	9.79	1.40	0.01
EAS-US	2026-06-03 06:00:00	12.88	29.88	0.13	6.79	9.80	1.46	0.01
EAS-US	2026-06-03 06:15:00	12.87	29.86	0.23	6.98	9.81	1.44	0.01
EAS-US	2026-06-03 06:30:00	12.87	29.83	0.23	6.89	9.84	1.47	0.01
EAS-US	2026-06-03 06:45:00	12.86	29.79	0.23	6.94	9.83	1.46	0.01
EAS-US	2026-06-03 07:00:00	12.86	29.75	0.13	6.70	9.85	1.36	0.01
EAS-US	2026-06-03 07:15:00	12.85	29.72	0.24	6.80	9.85	1.38	0.01
EAS-US	2026-06-03 07:30:00	12.85	29.75	0.23	6.77	9.85	1.43	0.01
EAS-US	2026-06-03 07:45:00	12.86	29.75	0.23	6.80	9.87	1.43	0.01
EAS-US	2026-06-03 08:00:00	12.88	29.71	0.12	6.84	9.89	1.38	0.01
EAS-US	2026-06-03 08:15:00	12.88	29.68	0.23	7.01	9.90	1.42	0.01
EAS-US	2026-06-03 08:30:00	12.91	29.59	0.23	6.99	9.94	1.44	0.01
EAS-US	2026-06-03 08:45:00	12.92	29.58	0.23	6.96	9.94	1.44	0.01
EAS-US	2026-06-03 09:00:00	12.95	29.56	0.13	6.74	9.95	1.41	0.01
EAS-US	2026-06-03 09:15:00	12.97	29.52	0.24	6.78	9.97	1.44	0.01
EAS-US	2026-06-03 09:30:00	12.99	29.45	0.23	6.84	9.98	1.48	0.01
EAS-US	2026-06-03 09:45:00	13.04	29.31	0.23	6.83	10.00	1.46	0.01
EAS-US	2026-06-03 10:00:00	13.11	29.20	0.13	6.90	10.05	1.59	0.01
EAS-US	2026-06-03 10:15:00	13.16	29.06	0.23	7.09	10.07	1.51	0.01
EAS-US	2026-06-03 10:30:00	13.23	28.98	0.22	7.11	10.07	1.53	0.01
EAS-US	2026-06-03 10:45:00	13.28	28.96	0.22	7.05	10.05	1.50	0.01
EAS-US	2026-06-03 11:00:00	13.35	28.91	0.13	6.81	10.05	1.42	0.01
EAS-US	2026-06-03 11:15:00	13.36	29.03	0.23	6.90	9.94	1.51	0.01
EAS-US	2026-06-03 11:30:00	13.35	29.20	0.23	6.80	9.85	1.49	0.01
EAS-US	2026-06-03 11:45:00	13.33	29.37	0.23	6.85	9.83	1.51	0.01
EAS-US	2026-06-03 12:00:00	13.31	29.47	0.13	6.83	9.87	1.57	0.01
EAS-US	2026-06-03 12:15:00	13.30	29.53	0.23	7.05	9.87	1.53	0.01
EAS-US	2026-06-03 12:30:00	13.32	29.38	0.22	7.06	9.95	1.63	0.01
EAS-US	2026-06-03 12:45:00	13.33	29.27	0.22	7.04	9.93	1.52	0.01
EAS-US	2026-06-03 13:00:00	13.38	29.19	0.13	6.82	9.97	1.47	0.01
EAS-US	2026-06-03 13:15:00	13.44	29.05	0.24	6.88	10.00	1.57	0.01
EAS-US	2026-06-03 13:30:00	13.47	29.03	0.23	6.89	9.98	1.49	0.01
EAS-US	2026-06-03 13:45:00	13.52	28.98	0.22	6.91	9.96	1.54	0.01
EAS-US	2026-06-03 14:00:00	13.56	29.00	0.13	6.93	9.91	1.54	0.01
EAS-US	2026-06-03 14:15:00	13.58	28.96	0.23	7.07	9.89	1.50	0.01
EAS-US	2026-06-03 14:30:00	13.62	28.94	0.22	7.11	9.92	1.50	0.01
EAS-US	2026-06-03 14:45:00	13.65	28.89	0.22	7.09	9.92	1.50	0.01
EAS-US	2026-06-03 15:00:00	13.68	28.84	0.13	6.84	9.92	2.33	0.01
EAS-US	2026-06-03 15:15:00	13.72	28.77	0.23	6.91	9.93	1.44	0.01
EAS-US	2026-06-03 15:30:00	13.75	28.78	0.23	6.91	9.90	1.48	0.01
EAS-US	2026-06-03 15:45:00	13.78	28.79	0.22	6.94	9.87	1.45	0.01
EAS-US	2026-06-03 16:00:00	13.78	28.87	0.12	6.92	9.84	1.57	0.01
EAS-US	2026-06-03 16:15:00	13.76	28.98	0.23	7.07	9.79	1.53	0.01
EAS-US	2026-06-03 16:30:00	13.73	29.17	0.23	7.04	9.77	1.50	0.01
EAS-US	2026-06-03 16:45:00	13.69	29.26	0.22	7.04	9.75	1.50	0.01
EAS-US	2026-06-03 17:00:00	13.66	29.41	0.13	6.79	9.74	1.43	0.01
EAS-US	2026-06-03 17:15:00	13.63	29.38	0.23	6.87	9.77	1.49	0.01
EAS-US	2026-06-03 17:30:00	13.61	29.40	0.23	6.86	9.78	1.53	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-03 17:45:00	13.60	29.41	0.23	6.82	9.77	1.49	0.01
EAS-US	2026-06-03 18:00:00	13.58	29.51	0.13	6.82	9.77	1.54	0.01
EAS-US	2026-06-03 18:15:00	13.56	29.51	0.23	7.03	9.76	1.56	0.01
EAS-US	2026-06-03 18:30:00	13.54	29.50	0.23	7.05	9.78	1.55	0.01
EAS-US	2026-06-03 18:45:00	13.53	29.45	0.22	7.06	9.78	1.49	0.01
EAS-US	2026-06-03 19:00:00	13.53	29.48	0.13	6.78	9.78	1.46	0.01
EAS-US	2026-06-03 19:15:00	13.51	29.55	0.23	6.82	9.76	1.49	0.01
EAS-US	2026-06-03 19:30:00	13.49	29.67	0.23	6.83	9.72	1.50	0.01
EAS-US	2026-06-03 19:45:00	13.46	29.80	0.23	6.82	9.71	1.51	0.01
EAS-US	2026-06-03 20:00:00	13.43	29.92	0.13	6.85	9.70	1.45	0.01
EAS-US	2026-06-03 20:15:00	13.40	29.95	0.23	7.01	9.71	1.47	0.01
EAS-US	2026-06-03 20:30:00	13.37	29.93	0.23	7.02	9.72	1.50	0.01
EAS-US	2026-06-03 20:45:00	13.34	29.90	0.23	7.02	9.71	1.48	0.01
EAS-US	2026-06-03 21:00:00	13.32	29.91	0.13	6.77	9.71	1.47	0.01
EAS-US	2026-06-03 21:15:00	13.29	29.90	0.24	6.81	9.74	1.48	0.01
EAS-US	2026-06-03 21:30:00	13.26	29.95	0.23	6.83	9.72	1.49	0.01
EAS-US	2026-06-03 21:45:00	13.24	29.95	0.23	6.78	9.73	1.52	0.01
EAS-US	2026-06-03 22:00:00	13.21	29.95	0.14	6.77	9.74	1.70	0.01
EAS-US	2026-06-03 22:15:00	13.19	29.99	0.23	7.02	9.74	1.48	0.01
EAS-US	2026-06-03 22:30:00	13.17	29.89	0.23	6.99	9.74	1.54	0.01
EAS-US	2026-06-03 22:45:00	13.15	29.90	0.23	7.02	9.75	1.49	0.01
EAS-US	2026-06-03 23:00:00	13.13	29.90	0.14	6.73	9.76	1.45	0.01
EAS-US	2026-06-03 23:15:00	13.11	29.82	0.24	6.83	9.76	1.43	0.01
EAS-US	2026-06-03 23:30:00	13.08	29.78	0.23	6.82	9.77	1.54	0.01
EAS-US	2026-06-03 23:45:00	13.05	29.74	0.23	6.83	9.78	1.45	0.01
EAS-US	2026-06-04 00:00:00	13.03	29.76	0.13	6.77	9.79	1.50	0.01
EAS-US	2026-06-04 00:15:00	13.00	29.73	0.23	7.02	9.79	1.42	0.01
EAS-US	2026-06-04 00:30:00	12.97	29.71	0.23	7.01	9.79	1.50	0.01
EAS-US	2026-06-04 00:45:00	12.95	29.70	0.22	7.00	9.80	1.49	0.01
EAS-US	2026-06-04 01:00:00	12.93	29.72	0.13	6.74	9.81	1.41	0.01
EAS-US	2026-06-04 01:15:00	12.92	29.63	0.24	6.81	9.81	1.45	0.01
EAS-US	2026-06-04 01:30:00	12.90	29.60	0.23	6.83	9.82	1.48	0.01
EAS-US	2026-06-04 01:45:00	12.89	29.57	0.23	6.77	9.83	2.04	0.01
EAS-US	2026-06-04 02:00:00	12.87	29.61	0.13	6.84	9.83	1.42	0.01
EAS-US	2026-06-04 02:15:00	12.86	29.56	0.23	6.99	9.83	1.46	0.01
EAS-US	2026-06-04 02:30:00	12.84	29.55	0.23	7.01	9.85	1.54	0.01
EAS-US	2026-06-04 02:45:00	12.83	29.55	0.23	7.01	9.86	1.48	0.01
EAS-US	2026-06-04 03:00:00	12.81	29.54	0.13	6.76	9.85	1.48	0.01
EAS-US	2026-06-04 03:15:00	12.80	29.51	0.24	6.78	9.85	1.67	0.01
EAS-US	2026-06-04 03:30:00	12.79	29.49	0.23	6.81	9.85	1.47	0.01
EAS-US	2026-06-04 03:45:00	12.77	29.51	0.23	6.77	9.86	1.45	0.01
EAS-US	2026-06-04 04:00:00	12.76	29.47	0.13	6.80	9.86	1.49	0.01
EAS-US	2026-06-04 04:15:00	12.75	29.49	0.23	6.99	9.86	1.45	0.01
EAS-US	2026-06-04 04:30:00	12.74	29.48	0.22	7.01	9.87	1.48	0.01
EAS-US	2026-06-04 04:45:00	12.73	29.49	0.22	6.99	9.87	1.49	0.01
EAS-US	2026-06-04 05:00:00	12.72	29.48	0.13	6.74	9.88	1.41	0.01
EAS-US	2026-06-04 05:15:00	12.71	29.46	0.24	6.85	9.89	1.45	0.01
EAS-US	2026-06-04 05:30:00	12.70	29.45	0.23	6.82	9.88	1.50	0.01
EAS-US	2026-06-04 05:45:00	12.69	29.46	0.23	6.78	9.90	1.42	0.01
EAS-US	2026-06-04 06:00:00	12.68	29.44	0.14	6.79	9.91	1.45	0.01
EAS-US	2026-06-04 06:15:00	12.67	29.38	0.23	6.99	9.93	1.46	0.01
EAS-US	2026-06-04 06:30:00	12.67	29.31	0.23	7.01	9.95	1.47	0.01
EAS-US	2026-06-04 06:45:00	12.68	29.27	0.22	7.01	9.97	1.50	0.01
EAS-US	2026-06-04 07:00:00	12.69	29.22	0.13	6.77	10.00	1.43	0.01
EAS-US	2026-06-04 07:15:00	12.70	29.14	0.23	6.83	10.01	1.46	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-04 07:30:00	12.71	29.09	0.23	6.85	10.01	1.42	0.01
EAS-US	2026-06-04 07:45:00	12.72	29.08	0.23	6.87	10.01	1.45	0.01
EAS-US	2026-06-04 08:00:00	12.72	29.04	0.12	6.87	10.04	1.49	0.01
EAS-US	2026-06-04 08:15:00	12.72	28.92	0.23	7.09	10.06	1.46	0.01
EAS-US	2026-06-04 08:30:00	12.73	28.85	0.23	7.08	10.07	1.59	0.01
EAS-US	2026-06-04 08:45:00	12.73	28.77	0.22	7.11	10.08	1.50	0.01
EAS-US	2026-06-04 09:00:00	12.73	28.72	0.13	6.81	10.10	1.43	0.01
EAS-US	2026-06-04 09:15:00	12.73	28.66	0.24	6.88	10.09	1.52	0.01
EAS-US	2026-06-04 09:30:00	12.76	28.60	0.23	6.93	10.13	1.51	0.01
EAS-US	2026-06-04 09:45:00	12.78	28.57	0.23	6.89	10.14	1.45	0.01
EAS-US	2026-06-04 10:00:00	12.80	28.51	0.13	6.92	10.14	1.50	0.01
EAS-US	2026-06-04 10:15:00	12.88	28.43	0.23	7.14	10.17	1.49	0.01
EAS-US	2026-06-04 10:30:00	13.03	28.29	0.22	7.16	10.18	1.47	0.01
EAS-US	2026-06-04 10:45:00	13.21	28.25	0.22	7.19	10.19	1.43	0.01
EAS-US	2026-06-04 11:00:00	13.25	28.29	0.13	6.90	10.15	1.63	0.01
EAS-US	2026-06-04 11:15:00	13.40	28.31	0.23	6.95	10.10	1.46	0.01
EAS-US	2026-06-04 11:30:00	13.55	28.29	0.23	6.95	10.11	1.50	0.01
EAS-US	2026-06-04 11:45:00	13.71	28.31	0.22	6.96	10.12	1.54	0.01
EAS-US	2026-06-04 12:00:00	13.85	28.38	0.13	7.02	10.10	1.54	0.01
EAS-US	2026-06-04 12:15:00	14.00	28.32	0.22	7.21	10.08	1.52	0.01
EAS-US	2026-06-04 12:30:00	14.05	28.33	0.21	7.22	10.06	1.52	0.01
EAS-US	2026-06-04 12:45:00	13.98	28.37	0.21	7.18	9.96	1.50	0.01
EAS-US	2026-06-04 13:00:00	14.10	28.38	0.13	6.91	9.97	1.53	0.01
EAS-US	2026-06-04 13:15:00	14.23	28.32	0.22	6.97	9.94	1.58	0.01
EAS-US	2026-06-04 13:30:00	14.31	28.36	0.22	6.99	9.94	1.55	0.01
EAS-US	2026-06-04 13:45:00	14.43	28.44	0.22	6.98	9.91	1.52	0.01
EAS-US	2026-06-04 14:00:00	14.59	28.46	0.13	7.00	9.84	1.56	0.01
EAS-US	2026-06-04 14:15:00	14.70	28.53	0.22	7.17	9.77	1.60	0.01
EAS-US	2026-06-04 14:30:00	14.85	28.56	0.21	7.19	9.74	1.56	0.01
EAS-US	2026-06-04 14:45:00	14.97	28.61	0.21	7.18	9.68	1.59	0.01
EAS-US	2026-06-04 15:00:00	15.05	28.75	0.13	6.88	9.64	1.58	0.01
EAS-US	2026-06-04 15:15:00	15.11	28.71	0.22	6.90	9.62	1.66	0.01
EAS-US	2026-06-04 15:30:00	15.09	28.74	0.22	6.91	9.62	1.59	0.01
EAS-US	2026-06-04 15:45:00	15.16	28.67	0.22	6.90	9.63	1.59	0.01
EAS-US	2026-06-04 16:00:00	15.16	28.69	0.14	6.96	9.63	1.58	0.01
EAS-US	2026-06-04 16:15:00	15.14	28.77	0.22	7.16	9.60	1.67	0.01
EAS-US	2026-06-04 16:30:00	15.09	28.82	0.21	7.11	9.59	21.77	0.01
EAS-US	2026-06-04 16:45:00	14.98	28.61	0.21	7.04	9.55	38.94	0.01
EAS-US	2026-06-04 17:00:00	14.84	28.75	0.14	6.83	9.56	47.08	0.01
EAS-US	2026-06-04 17:15:00	14.69	29.06	0.23	6.92	9.62	8.14	0.01
EAS-US	2026-06-04 17:30:00	14.56	28.96	0.23	6.90	9.61	4.30	0.01
EAS-US	2026-06-04 17:45:00	14.40	29.07	0.22	6.92	9.61	3.66	0.01
EAS-US	2026-06-04 18:00:00	14.28	29.14	0.13	6.93	9.65	4.79	0.01
EAS-US	2026-06-04 18:15:00	14.17	29.18	0.23	7.07	9.65	3.10	0.01
EAS-US	2026-06-04 18:30:00	14.09	29.25	0.22	7.11	9.66	3.07	0.01
EAS-US	2026-06-04 18:45:00	14.02	29.35	0.22	7.07	9.65	3.10	0.01
EAS-US	2026-06-04 19:00:00	13.97	29.50	0.13	6.79	9.64	3.69	0.01
EAS-US	2026-06-04 19:15:00	13.90	29.56	0.23	6.85	9.63	2.98	0.01
EAS-US	2026-06-04 19:30:00	13.84	29.63	0.23	6.84	9.63	2.74	0.01
EAS-US	2026-06-04 19:45:00	13.77	29.66	0.23	6.87	9.64	2.83	0.01
EAS-US	2026-06-04 20:00:00	13.71	29.72	0.13	6.87	9.64	3.19	0.01
EAS-US	2026-06-04 20:15:00	13.67	29.80	0.23	7.02	9.62	2.91	0.01
EAS-US	2026-06-04 20:30:00	13.63	29.88	0.22	7.04	9.63	2.87	0.01
EAS-US	2026-06-04 20:45:00	13.59	29.96	0.22	7.03	9.61	2.78	0.01
EAS-US	2026-06-04 21:00:00	13.55	30.02	0.14	6.76	9.62	3.07	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-04 21:15:00	13.51	30.03	0.24	6.78	9.63	3.18	0.01
EAS-US	2026-06-04 21:30:00	13.47	30.05	0.23	6.81	9.64	3.20	0.01
EAS-US	2026-06-04 21:45:00	13.43	30.06	0.23	6.80	9.64	2.69	0.01
EAS-US	2026-06-04 22:00:00	13.39	30.07	0.13	6.85	9.64	3.00	0.01
EAS-US	2026-06-04 22:15:00	13.36	30.05	0.23	7.01	9.67	2.72	0.01
EAS-US	2026-06-04 22:30:00	13.31	30.01	0.23	7.02	9.67	2.97	0.01
EAS-US	2026-06-04 22:45:00	13.26	29.97	0.22	7.00	9.66	3.06	0.01
EAS-US	2026-06-04 23:00:00	13.22	29.99	0.13	6.76	9.69	2.81	0.01
EAS-US	2026-06-04 23:15:00	13.18	29.95	0.24	6.82	9.69	2.73	0.01
EAS-US	2026-06-04 23:30:00	13.15	29.93	0.23	6.88	9.71	2.70	0.01
EAS-US	2026-06-04 23:45:00	13.11	29.90	0.23	6.79	9.71	2.63	0.01
EAS-US	2026-06-05 00:00:00	13.07	29.87	0.13	6.85	9.71	3.01	0.01
EAS-US	2026-06-05 00:15:00	13.02	29.77	0.23	7.04	9.74	2.88	0.01
EAS-US	2026-06-05 00:30:00	12.97	29.74	0.23	7.04	9.75	2.64	0.01
EAS-US	2026-06-05 00:45:00	12.93	29.71	0.22	7.04	9.74	2.96	0.01
EAS-US	2026-06-05 01:00:00	12.87	29.70	0.14	6.77	9.75	2.46	0.01
EAS-US	2026-06-05 01:15:00	12.81	29.64	0.24	6.79	9.76	2.67	0.01
EAS-US	2026-06-05 01:30:00	12.74	29.62	0.23	6.83	9.78	2.56	0.01
EAS-US	2026-06-05 01:45:00	12.70	29.63	0.23	6.84	9.81	2.69	0.01
EAS-US	2026-06-05 02:00:00	12.68	29.67	0.13	6.84	9.81	5.40	0.01
EAS-US	2026-06-05 02:15:00	12.65	29.64	0.23	7.04	9.82	2.43	0.01
EAS-US	2026-06-05 02:30:00	12.63	29.63	0.23	7.03	9.82	2.65	0.01
EAS-US	2026-06-05 02:45:00	12.61	29.63	0.23	7.02	9.83	2.71	0.01
EAS-US	2026-06-05 03:00:00	12.59	29.68	0.14	6.74	9.84	2.89	0.01
EAS-US	2026-06-05 03:15:00	12.56	29.61	0.23	6.82	9.84	2.57	0.01
EAS-US	2026-06-05 03:30:00	12.54	29.60	0.23	6.82	9.84	2.79	0.01
EAS-US	2026-06-05 03:45:00	12.51	29.60	0.23	6.82	9.85	2.44	0.01
EAS-US	2026-06-05 04:00:00	12.49	29.61	0.12	6.88	9.86	2.55	0.01
EAS-US	2026-06-05 04:15:00	12.46	29.55	0.23	7.02	9.87	2.65	0.01
EAS-US	2026-06-05 04:30:00	12.43	29.54	0.23	6.98	9.88	2.47	0.01
EAS-US	2026-06-05 04:45:00	12.41	29.53	0.23	7.02	9.88	2.59	0.01
EAS-US	2026-06-05 05:00:00	12.38	29.54	0.13	6.74	9.89	2.51	0.01
EAS-US	2026-06-05 05:15:00	12.35	29.45	0.24	6.83	9.90	2.50	0.01
EAS-US	2026-06-05 05:30:00	12.32	29.43	0.23	6.84	9.91	2.52	0.01
EAS-US	2026-06-05 05:45:00	12.29	29.39	0.23	6.83	9.93	2.57	0.01
EAS-US	2026-06-05 06:00:00	12.27	29.39	0.13	6.82	9.93	2.58	0.01
EAS-US	2026-06-05 06:15:00	12.24	29.33	0.23	7.01	9.93	2.63	0.01
EAS-US	2026-06-05 06:30:00	12.22	29.31	0.23	7.05	9.96	2.70	0.01
EAS-US	2026-06-05 06:45:00	12.20	29.29	0.23	7.03	9.96	2.36	0.01
EAS-US	2026-06-05 07:00:00	12.19	29.38	0.13	6.77	9.99	2.82	0.01
EAS-US	2026-06-05 07:15:00	12.17	29.45	0.23	6.85	10.00	2.61	0.01
EAS-US	2026-06-05 07:30:00	12.16	29.39	0.23	6.82	10.02	2.61	0.01
EAS-US	2026-06-05 07:45:00	12.16	29.26	0.23	6.84	10.05	2.64	0.01
EAS-US	2026-06-05 08:00:00	12.16	29.28	0.12	6.90	10.04	2.83	0.01
EAS-US	2026-06-05 08:15:00	12.14	29.17	0.23	7.06	10.03	2.66	0.01
EAS-US	2026-06-05 08:30:00	12.13	29.16	0.23	7.07	10.05	2.69	0.01
EAS-US	2026-06-05 08:45:00	12.12	29.12	0.22	7.07	10.05	2.49	0.01
EAS-US	2026-06-05 09:00:00	12.11	29.05	0.13	6.83	10.11	4.18	0.01
EAS-US	2026-06-05 09:15:00	12.11	28.89	0.24	6.85	10.13	2.78	0.01
EAS-US	2026-06-05 09:30:00	12.12	28.72	0.23	6.88	10.16	2.82	0.01
EAS-US	2026-06-05 09:45:00	12.14	28.59	0.23	6.92	10.21	2.39	0.01
EAS-US	2026-06-05 10:00:00	12.17	28.47	0.13	6.95	10.23	2.47	0.01
EAS-US	2026-06-05 10:15:00	12.21	28.37	0.23	7.14	10.25	2.44	0.01
EAS-US	2026-06-05 10:30:00	12.21	28.49	0.22	7.08	10.15	2.42	0.01
EAS-US	2026-06-05 10:45:00	12.20	28.56	0.22	7.10	10.13	2.80	0.01


Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-05 11:00:00	12.20	28.60	0.13	6.85	10.16	2.54	0.01
EAS-US	2026-06-05 11:15:00	12.19	28.60	0.23	6.88	10.13	4.34	0.01
EAS-US	2026-06-05 11:30:00	12.20	28.54	0.23	6.86	10.16	2.82	0.01
EAS-US	2026-06-05 11:45:00	12.21	28.52	0.23	6.88	10.17	2.78	0.01
EAS-US	2026-06-05 12:00:00	12.27	28.36	0.13	6.97	10.23	2.79	0.01
EAS-US	2026-06-05 12:15:00	12.28	28.28	0.23	7.13	10.21	2.72	0.01
EAS-US	2026-06-05 12:30:00	12.28	28.30	0.22	7.13	10.16	2.76	0.01
EAS-US	2026-06-05 12:45:00	12.24	28.45	0.22	7.10	10.14	2.65	0.01
EAS-US	2026-06-05 13:00:00	12.19	28.84	0.14	6.79	10.06	5.30	0.01
EAS-US	2026-06-05 13:15:00	12.13	29.22	0.23	6.92	10.05	4.44	0.01
EAS-US	2026-06-05 13:30:00	12.06	29.57	0.23	6.87	10.05	3.01	0.01
EAS-US	2026-06-05 13:45:00	12.00	29.76	0.23	6.87	10.05	3.03	0.01
EAS-US	2026-06-05 14:00:00	11.97	29.83	0.13	6.91	10.13	3.57	0.01
EAS-US	2026-06-05 14:15:00	11.95	29.85	0.23	7.09	10.16	3.18	0.01
EAS-US	2026-06-05 14:30:00	11.94	29.72	0.22	7.11	10.18	3.09	0.01
EAS-US	2026-06-05 14:45:00	11.92	29.59	0.22	7.11	10.17	2.98	0.01
EAS-US	2026-06-05 15:00:00	11.88	29.49	0.14	6.84	10.18	3.18	0.01
EAS-US	2026-06-05 15:15:00	11.86	29.52	0.24	6.88	10.22	3.10	0.01
EAS-US	2026-06-05 15:30:00	11.84	29.52	0.23	6.91	10.22	2.90	0.01
EAS-US	2026-06-05 15:45:00	11.87	29.34	0.23	6.90	10.26	2.88	0.01
EAS-US	2026-06-05 16:00:00	11.96	29.20	0.13	6.91	10.27	3.08	0.01
EAS-US	2026-06-05 16:15:00	12.04	29.05	0.23	7.14	10.28	2.90	0.01
EAS-US	2026-06-05 16:30:00	12.09	28.92	0.22	7.14	10.24	2.87	0.01
EAS-US	2026-06-05 16:45:00	12.14	28.79	0.22	7.14	10.20	2.91	0.01
EAS-US	2026-06-05 17:00:00	12.15	28.74	0.14	6.86	10.18	5.31	0.01
EAS-US	2026-06-05 17:15:00	12.16	28.60	0.23	6.95	10.18	2.75	0.01
EAS-US	2026-06-05 17:30:00	12.18	28.52	0.23	6.90	10.16	2.72	0.01
EAS-US	2026-06-05 17:45:00	12.18	28.52	0.23	6.93	10.16	2.75	0.01
EAS-US	2026-06-05 18:00:00	12.18	28.49	0.13	6.90	10.14	2.72	0.01
EAS-US	2026-06-05 18:15:00	12.18	28.54	0.23	7.11	10.12	2.91	0.01
EAS-US	2026-06-05 18:30:00	12.18	28.59	0.22	7.12	10.12	2.77	0.01
EAS-US	2026-06-05 18:45:00	12.15	28.71	0.22	7.09	10.04	2.82	0.01
EAS-US	2026-06-05 19:00:00	12.12	28.88	0.13	6.81	10.01	2.80	0.01
EAS-US	2026-06-05 19:15:00	12.08	28.80	0.23	6.84	10.03	2.71	0.01
EAS-US	2026-06-05 19:30:00	12.03	28.79	0.23	6.87	10.04	2.73	0.01
EAS-US	2026-06-05 19:45:00	11.98	28.76	0.23	6.84	10.03	2.86	0.01
EAS-US	2026-06-05 20:00:00	11.91	28.82	0.14	6.83	10.02	2.77	0.01
EAS-US	2026-06-05 20:15:00	11.84	28.77	0.23	7.07	10.01	2.90	0.01
EAS-US	2026-06-05 20:30:00	11.76	28.78	0.23	7.07	10.04	4.17	0.01
EAS-US	2026-06-05 20:45:00	11.70	28.85	0.23	7.06	10.03	2.99	0.01
EAS-US	2026-06-05 21:00:00	11.66	28.89	0.13	6.77	10.05	2.93	0.01
EAS-US	2026-06-05 21:15:00	11.61	28.83	0.24	6.77	10.07	2.79	0.01
EAS-US	2026-06-05 21:30:00	11.58	28.80	0.24	6.81	10.08	2.82	0.01
EAS-US	2026-06-05 21:45:00	11.54	28.77	0.24	6.84	10.09	2.95	0.01
EAS-US	2026-06-05 22:00:00	11.50	28.73	0.13	6.82	10.09	2.90	0.01
EAS-US	2026-06-05 22:15:00	11.46	28.65	0.23	7.06	10.11	2.89	0.01
EAS-US	2026-06-05 22:30:00	11.43	28.59	0.23	7.04	10.12	2.76	0.01
EAS-US	2026-06-05 22:45:00	11.39	28.65	0.23	7.05	10.09	3.00	0.01
EAS-US	2026-06-05 23:00:00	11.35	28.53	0.13	6.76	10.14	2.84	0.01
EAS-US	2026-06-05 23:15:00	11.32	28.50	0.24	6.84	10.16	2.72	0.01
EAS-US	2026-06-05 23:30:00	11.29	28.48	0.23	6.84	10.14	2.61	0.01
EAS-US	2026-06-05 23:45:00	11.26	28.44	0.24	6.79	10.15	2.66	0.01
EAS-US	2026-06-06 00:00:00	11.23	28.46	0.13	6.79	10.15	2.72	0.01
EAS-US	2026-06-06 00:15:00	11.21	28.45	0.23	7.04	10.15	2.57	0.01
EAS-US	2026-06-06 00:30:00	11.19	28.49	0.23	7.03	10.16	2.69	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-06 00:45:00	11.17	28.54	0.23	7.04	10.14	2.67	0.01
EAS-US	2026-06-06 01:00:00	11.15	28.52	0.15	6.73	10.16	2.61	0.01
EAS-US	2026-06-06 01:15:00	11.13	28.47	0.24	6.82	10.18	2.51	0.01
EAS-US	2026-06-06 01:30:00	11.11	28.44	0.24	6.82	10.18	2.63	0.01
EAS-US	2026-06-06 01:45:00	11.10	28.44	0.24	6.78	10.19	2.68	0.01
EAS-US	2026-06-06 02:00:00	11.07	28.42	0.12	6.80	10.19	2.71	0.01
EAS-US	2026-06-06 02:15:00	11.06	28.37	0.24	7.03	10.20	2.64	0.01
EAS-US	2026-06-06 02:30:00	11.04	28.39	0.23	7.04	10.21	2.74	0.01
EAS-US	2026-06-06 02:45:00	11.02	28.37	0.23	7.03	10.19	2.70	0.01
EAS-US	2026-06-06 03:00:00	11.00	28.35	0.14	6.74	10.19	2.58	0.01
EAS-US	2026-06-06 03:15:00	10.98	28.35	0.24	6.80	10.21	2.61	0.01
EAS-US	2026-06-06 03:30:00	10.96	28.33	0.24	6.81	10.22	2.63	0.01
EAS-US	2026-06-06 03:45:00	10.94	28.38	0.24	6.78	10.22	2.71	0.01
EAS-US	2026-06-06 04:00:00	10.92	28.35	0.13	6.79	10.24	3.47	0.01
EAS-US	2026-06-06 04:15:00	10.91	28.35	0.23	7.04	10.21	2.66	0.01
EAS-US	2026-06-06 04:30:00	10.89	28.49	0.23	7.04	10.23	2.61	0.01
EAS-US	2026-06-06 04:45:00	10.88	28.40	0.23	7.04	10.14	2.77	0.01
EAS-US	2026-06-06 05:00:00	10.85	28.38	0.14	6.74	10.23	2.65	0.01
EAS-US	2026-06-06 05:15:00	10.83	28.36	0.24	6.82	10.18	2.57	0.01
EAS-US	2026-06-06 05:30:00	10.80	28.34	0.24	6.83	10.14	2.64	0.01
EAS-US	2026-06-06 05:45:00	10.78	28.34	0.24	6.80	10.18	2.56	0.01
EAS-US	2026-06-06 06:00:00	10.76	28.13	0.13	6.80	10.23	2.58	0.01
EAS-US	2026-06-06 06:15:00	10.75	28.23	0.24	7.05	10.24	2.57	0.01
EAS-US	2026-06-06 06:30:00	10.74	28.34	0.23	7.05	10.31	2.51	0.01
EAS-US	2026-06-06 06:45:00	10.74	28.26	0.23	7.05	10.32	2.59	0.01
EAS-US	2026-06-06 07:00:00	10.73	28.08	0.13	6.75	10.32	2.54	0.01
EAS-US	2026-06-06 07:15:00	10.73	28.19	0.24	6.82	10.29	2.48	0.01
EAS-US	2026-06-06 07:30:00	10.70	28.13	0.24	6.83	10.19	2.71	0.01
EAS-US	2026-06-06 07:45:00	10.66	28.03	0.24	6.79	10.34	3.19	0.01
EAS-US	2026-06-06 08:00:00	10.64	28.35	0.13	6.80	10.38	3.08	0.01
EAS-US	2026-06-06 08:15:00	10.65	28.36	0.24	7.02	10.43	3.04	0.01
EAS-US	2026-06-06 08:30:00	10.68	31.74	0.23	7.03	10.47	4.17	0.02
EAS-US	2026-06-06 08:45:00	10.73	47.75	0.23	7.09	10.53	3.54	0.02
EAS-US	2026-06-06 09:00:00	10.79	57.92	0.12	6.97	10.54	3.96	0.03
EAS-US	2026-06-06 09:15:00	10.85	58.60	0.23	7.05	10.54	3.61	0.03
EAS-US	2026-06-06 09:30:00	10.91	54.15	0.22	7.09	10.59	3.90	0.03
EAS-US	2026-06-06 09:45:00	10.96	49.58	0.22	7.07	10.56	4.25	0.03
EAS-US	2026-06-06 10:00:00	11.00	46.71	0.11	7.10	10.52	4.70	0.02
EAS-US	2026-06-06 10:15:00	11.05	43.98	0.22	7.22	10.53	4.72	0.02
EAS-US	2026-06-06 10:30:00	11.11	41.19	0.22	7.24	10.56	4.60	0.02
EAS-US	2026-06-06 10:45:00	11.22	38.78	0.22	7.24	10.56	4.11	0.02
EAS-US	2026-06-06 11:00:00	11.36	36.88	0.11	6.99	10.54	3.73	0.02
EAS-US	2026-06-06 11:15:00	11.56	34.91	0.23	7.08	10.54	3.46	0.02
EAS-US	2026-06-06 11:30:00	11.47	33.31	0.23	7.08	10.50	2.38	0.02
EAS-US	2026-06-06 11:45:00	11.45	32.03	0.23	7.03	10.45	2.40	0.02
EAS-US	2026-06-06 12:00:00	11.42	30.96	0.12	7.04	10.47	2.39	0.02
EAS-US	2026-06-06 12:15:00	11.45	29.91	0.23	7.23	10.51	2.14	0.01
EAS-US	2026-06-06 12:30:00	11.60	29.22	0.22	7.23	10.53	2.15	0.01
EAS-US	2026-06-06 12:45:00	11.71	28.79	0.22	7.22	10.50	2.06	0.01
EAS-US	2026-06-06 13:00:00	11.77	28.57	0.12	6.94	10.39	1.95	0.01
EAS-US	2026-06-06 13:15:00	11.96	28.33	0.23	7.00	10.38	2.10	0.01
EAS-US	2026-06-06 13:30:00	12.00	28.14	0.23	6.92	10.36	2.06	0.01
EAS-US	2026-06-06 13:45:00	12.09	28.00	0.23	6.99	10.35	2.02	0.01
EAS-US	2026-06-06 14:00:00	12.10	28.04	0.13	7.00	10.29	2.19	0.01
EAS-US	2026-06-06 14:15:00	12.04	28.00	0.23	7.16	10.23	2.05	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-06 14:30:00	11.94	27.98	0.22	7.16	10.27	2.12	0.01
EAS-US	2026-06-06 14:45:00	11.90	27.94	0.22	7.17	10.31	2.14	0.01
EAS-US	2026-06-06 15:00:00	11.90	27.95	0.13	6.89	10.32	2.29	0.01
EAS-US	2026-06-06 15:15:00	12.02	27.84	0.23	6.98	10.30	2.00	0.01
EAS-US	2026-06-06 15:30:00	12.09	27.80	0.23	6.95	10.26	2.03	0.01
EAS-US	2026-06-06 15:45:00	12.12	27.94	0.23	6.94	10.25	2.02	0.01
EAS-US	2026-06-06 16:00:00	12.11	27.83	0.13	7.00	10.24	2.22	0.01
EAS-US	2026-06-06 16:15:00	12.07	27.82	0.23	7.17	10.25	2.02	0.01
EAS-US	2026-06-06 16:30:00	12.12	27.77	0.23	7.15	10.27	2.04	0.01
EAS-US	2026-06-06 16:45:00	12.12	27.82	0.22	7.16	10.25	2.02	0.01
EAS-US	2026-06-06 17:00:00	12.11	27.91	0.14	6.86	10.20	2.07	0.01
EAS-US	2026-06-06 17:15:00	12.09	27.94	0.23	6.96	10.19	1.99	0.01
EAS-US	2026-06-06 17:30:00	12.05	27.97	0.23	6.91	10.20	2.04	0.01
EAS-US	2026-06-06 17:45:00	12.02	28.04	0.23	6.90	10.19	2.01	0.01
EAS-US	2026-06-06 18:00:00	11.99	28.12	0.13	6.95	10.19	2.15	0.01
EAS-US	2026-06-06 18:15:00	11.99	28.02	0.24	7.11	10.21	2.05	0.01
EAS-US	2026-06-06 18:30:00	11.97	28.09	0.23	7.10	10.19	2.07	0.01
EAS-US	2026-06-06 18:45:00	11.96	28.20	0.23	7.08	10.16	2.12	0.01
EAS-US	2026-06-06 19:00:00	11.94	28.24	0.14	6.85	10.18	2.04	0.01
EAS-US	2026-06-06 19:15:00	11.92	28.30	0.24	6.88	10.14	2.01	0.01
EAS-US	2026-06-06 19:30:00	11.88	28.40	0.23	6.88	10.13	1.98	0.01
EAS-US	2026-06-06 19:45:00	11.85	28.47	0.23	6.89	10.13	1.94	0.01
EAS-US	2026-06-06 20:00:00	11.82	28.51	0.13	6.92	10.12	2.06	0.01
EAS-US	2026-06-06 20:15:00	11.80	28.54	0.23	7.08	10.13	2.09	0.01
EAS-US	2026-06-06 20:30:00	11.77	28.59	0.23	7.07	10.10	1.99	0.01
EAS-US	2026-06-06 20:45:00	11.74	28.68	0.23	7.07	10.10	2.06	0.01
EAS-US	2026-06-06 21:00:00	11.72	28.79	0.14	6.79	10.09	2.02	0.01
EAS-US	2026-06-06 21:15:00	11.70	28.75	0.24	6.88	10.09	1.96	0.01
EAS-US	2026-06-06 21:30:00	11.67	28.76	0.24	6.86	10.09	2.00	0.01
EAS-US	2026-06-06 21:45:00	11.65	28.76	0.24	6.85	10.08	1.96	0.01
EAS-US	2026-06-06 22:00:00	11.62	28.80	0.13	6.90	10.10	2.01	0.01
EAS-US	2026-06-06 22:15:00	11.59	28.76	0.23	7.03	10.11	2.20	0.01
EAS-US	2026-06-06 22:30:00	11.57	28.75	0.23	7.03	10.12	2.00	0.01
EAS-US	2026-06-06 22:45:00	11.54	28.74	0.23	7.03	10.11	2.89	0.01
EAS-US	2026-06-06 23:00:00	11.52	28.76	0.13	6.77	10.12	2.00	0.01
EAS-US	2026-06-06 23:15:00	11.50	28.73	0.24	6.83	10.13	1.99	0.01
EAS-US	2026-06-06 23:30:00	11.48	28.70	0.24	6.83	10.14	2.16	0.01
EAS-US	2026-06-06 23:45:00	11.46	28.67	0.24	6.85	10.14	2.02	0.01
EAS-US	2026-06-07 00:00:00	11.44	28.70	0.13	6.88	10.15	1.96	0.01
EAS-US	2026-06-07 00:15:00	11.42	28.68	0.23	7.04	10.15	2.07	0.01
EAS-US	2026-06-07 00:30:00	11.40	28.67	0.23	6.99	10.16	2.00	0.01
EAS-US	2026-06-07 00:45:00	11.39	28.67	0.23	7.00	10.16	2.13	0.01
EAS-US	2026-06-07 01:00:00	11.38	28.70	0.14	6.76	10.15	2.45	0.01
EAS-US	2026-06-07 01:15:00	11.36	28.66	0.24	6.82	10.16	1.94	0.01
EAS-US	2026-06-07 01:30:00	11.35	28.63	0.24	6.81	10.17	2.05	0.01
EAS-US	2026-06-07 01:45:00	11.34	28.64	0.24	6.81	10.17	2.01	0.01
EAS-US	2026-06-07 02:00:00	11.33	28.66	0.14	6.87	10.17	2.24	0.01
EAS-US	2026-06-07 02:15:00	11.32	28.64	0.24	6.99	10.18	2.12	0.01
EAS-US	2026-06-07 02:30:00	11.31	28.64	0.23	7.03	10.19	2.01	0.01
EAS-US	2026-06-07 02:45:00	11.30	29.08	0.23	7.03	10.18	2.11	0.01
EAS-US	2026-06-07 03:00:00	11.29	28.64	0.13	6.76	10.18	1.96	0.01
EAS-US	2026-06-07 03:15:00	11.28	28.58	0.24	6.85	10.19	2.13	0.01
EAS-US	2026-06-07 03:30:00	11.26	28.58	0.24	6.77	10.19	2.00	0.01
EAS-US	2026-06-07 03:45:00	11.25	28.59	0.23	6.87	10.21	1.95	0.01
EAS-US	2026-06-07 04:00:00	11.24	28.62	0.13	6.87	10.20	2.02	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-07 04:15:00	11.23	28.61	0.24	6.97	10.21	2.12	0.01
EAS-US	2026-06-07 04:30:00	11.21	28.57	0.23	7.01	10.21	2.25	0.01
EAS-US	2026-06-07 04:45:00	11.21	28.57	0.23	7.02	10.22	2.05	0.01
EAS-US	2026-06-07 05:00:00	11.20	28.59	0.13	6.75	10.21	2.36	0.01
EAS-US	2026-06-07 05:15:00	11.19	28.56	0.24	6.82	10.23	1.98	0.01
EAS-US	2026-06-07 05:30:00	11.18	28.58	0.24	6.84	10.22	1.92	0.01
EAS-US	2026-06-07 05:45:00	11.17	28.55	0.24	6.84	10.22	1.97	0.01
EAS-US	2026-06-07 06:00:00	11.16	28.58	0.13	6.86	10.25	1.93	0.01
EAS-US	2026-06-07 06:15:00	11.15	28.49	0.24	7.00	10.26	2.01	0.01
EAS-US	2026-06-07 06:30:00	11.15	28.44	0.23	7.04	10.29	1.94	0.01
EAS-US	2026-06-07 06:45:00	11.15	28.37	0.23	7.03	10.29	1.97	0.01
EAS-US	2026-06-07 07:00:00	11.16	28.34	0.14	6.78	10.32	2.99	0.01
EAS-US	2026-06-07 07:15:00	11.16	28.27	0.24	6.85	10.32	2.00	0.01
EAS-US	2026-06-07 07:30:00	11.17	28.24	0.24	6.86	10.32	1.91	0.01
EAS-US	2026-06-07 07:45:00	11.20	28.17	0.23	6.91	10.37	1.92	0.01
EAS-US	2026-06-07 08:00:00	11.23	28.18	0.13	6.93	10.37	1.97	0.01
EAS-US	2026-06-07 08:15:00	11.28	28.30	0.23	7.07	10.38	1.96	0.01
EAS-US	2026-06-07 08:30:00	11.33	27.98	0.22	7.02	10.41	1.92	0.01
EAS-US	2026-06-07 08:45:00	11.35	27.96	0.23	7.09	10.38	1.96	0.01
EAS-US	2026-06-07 09:00:00	11.37	28.02	0.13	6.83	10.34	1.95	0.01
EAS-US	2026-06-07 09:15:00	11.40	27.99	0.24	6.88	10.38	1.97	0.01
EAS-US	2026-06-07 09:30:00	11.46	27.89	0.24	6.94	10.42	2.01	0.01
EAS-US	2026-06-07 09:45:00	11.48	27.86	0.24	6.88	10.38	2.30	0.01
EAS-US	2026-06-07 10:00:00	11.51	27.90	0.14	6.93	10.38	2.19	0.01
EAS-US	2026-06-07 10:15:00	11.55	27.81	0.23	7.11	10.39	2.12	0.01
EAS-US	2026-06-07 10:30:00	11.65	27.78	0.23	7.12	10.44	2.08	0.01
EAS-US	2026-06-07 10:45:00	11.70	27.75	0.23	7.11	10.41	2.02	0.01
EAS-US	2026-06-07 11:00:00	11.73	27.77	0.14	6.89	10.37	1.98	0.01
EAS-US	2026-06-07 11:15:00	11.78	27.71	0.24	6.93	10.39	2.06	0.01
EAS-US	2026-06-07 11:30:00	11.77	27.81	0.24	6.94	10.33	2.00	0.01
EAS-US	2026-06-07 11:45:00	11.75	27.90	0.24	6.96	10.29	1.97	0.01
EAS-US	2026-06-07 12:00:00	11.74	27.97	0.13	6.97	10.30	2.15	0.01
EAS-US	2026-06-07 12:15:00	11.74	27.88	0.23	7.12	10.34	2.02	0.01
EAS-US	2026-06-07 12:30:00	11.74	27.87	0.23	7.15	10.34	2.02	0.01
EAS-US	2026-06-07 12:45:00	11.75	27.89	0.23	7.15	10.31	2.05	0.01
EAS-US	2026-06-07 13:00:00	11.77	27.87	0.14	6.87	10.33	1.97	0.01
EAS-US	2026-06-07 13:15:00	11.78	27.85	0.24	6.97	10.32	1.98	0.01
EAS-US	2026-06-07 13:30:00	11.79	27.87	0.24	6.97	10.32	1.99	0.01
EAS-US	2026-06-07 13:45:00	11.80	27.89	0.24	6.93	10.29	1.99	0.01
EAS-US	2026-06-07 14:00:00	11.89	27.81	0.13	6.97	10.36	5.82	0.01
EAS-US	2026-06-07 14:15:00	11.99	27.71	0.23	7.17	10.37	1.98	0.01
EAS-US	2026-06-07 14:30:00	12.10	27.75	0.23	7.14	10.27	2.07	0.01
EAS-US	2026-06-07 14:45:00	12.19	27.87	0.23	7.06	10.20	1.96	0.01
EAS-US	2026-06-07 15:00:00	12.16	27.97	0.14	6.87	10.20	7.96	0.01
EAS-US	2026-06-07 15:15:00	12.11	27.95	0.24	6.96	10.20	1.87	0.01
EAS-US	2026-06-07 15:30:00	12.08	27.95	0.24	6.94	10.22	2.02	0.01
EAS-US	2026-06-07 15:45:00	12.07	27.93	0.23	6.97	10.25	1.99	0.01
EAS-US	2026-06-07 16:00:00	12.08	27.86	0.13	6.99	10.26	13.17	0.01
EAS-US	2026-06-07 16:15:00	12.09	27.83	0.23	7.13	10.27	2.03	0.01
EAS-US	2026-06-07 16:30:00	12.13	27.82	0.23	7.14	10.27	2.05	0.01
EAS-US	2026-06-07 16:45:00	12.13	27.86	0.23	7.06	10.22	1.99	0.01
EAS-US	2026-06-07 17:00:00	12.12	27.98	0.14	6.90	10.19	2.02	0.01
EAS-US	2026-06-07 17:15:00	12.11	27.97	0.24	6.93	10.20	2.01	0.01
EAS-US	2026-06-07 17:30:00	12.15	27.92	0.24	6.94	10.23	2.05	0.01
EAS-US	2026-06-07 17:45:00	12.13	28.03	0.23	6.93	10.16	2.15	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-06-07 18:00:00	12.14	28.14	0.13	6.95	10.14	2.53	0.01
EAS-US	2026-06-07 18:15:00	12.12	28.25	0.24	7.04	10.12	2.04	0.01
EAS-US	2026-06-07 18:30:00	12.10	28.25	0.24	7.03	10.12	2.07	0.01
EAS-US	2026-06-07 18:45:00	12.08	28.25	0.23	7.05	10.10	2.15	0.01
EAS-US	2026-06-07 19:00:00	12.05	28.37	0.14	6.84	10.10	2.18	0.01
EAS-US	2026-06-07 19:15:00	12.02	28.26	0.24	6.90	10.10	2.04	0.01
EAS-US	2026-06-07 19:30:00	12.00	28.32	0.24	6.91	10.11	2.05	0.01
EAS-US	2026-06-07 19:45:00	11.98	28.41	0.24	6.90	10.12	1.98	0.01
EAS-US	2026-06-07 20:00:00	11.97	28.43	0.14	6.90	10.10	2.06	0.01
EAS-US	2026-06-07 20:15:00	11.94	28.39	0.24	7.03	10.10	2.17	0.01
EAS-US	2026-06-07 20:30:00	11.91	28.40	0.23	7.02	10.09	2.11	0.01
EAS-US	2026-06-07 20:45:00	11.87	28.38	0.23	7.03	10.08	2.06	0.01
EAS-US	2026-06-07 21:00:00	11.83	28.48	0.14	6.83	10.08	2.13	0.01
EAS-US	2026-06-07 21:15:00	11.79	28.43	0.24	6.86	10.08	2.36	0.01
EAS-US	2026-06-07 21:30:00	11.76	28.44	0.24	6.85	10.09	2.34	0.01
EAS-US	2026-06-07 21:45:00	11.72	28.46	0.24	6.88	10.10	2.26	0.01
EAS-US	2026-06-07 22:00:00	11.68	28.49	0.14	6.87	10.10	2.33	0.01
EAS-US	2026-06-07 22:15:00	11.64	28.44	0.24	7.00	10.11	2.40	0.01
EAS-US	2026-06-07 22:30:00	11.61	28.44	0.24	6.99	10.11	3.77	0.01
EAS-US	2026-06-07 22:45:00	11.57	28.41	0.24	7.01	10.13	2.24	0.01
EAS-US	2026-06-07 23:00:00	11.53	28.44	0.14	6.80	10.13	2.48	0.01
EAS-US	2026-06-07 23:15:00	11.50	28.41	0.24	6.89	10.14	2.30	0.01
EAS-US	2026-06-07 23:30:00	11.46	28.38	0.24	6.81	10.14	2.41	0.01
EAS-US	2026-06-07 23:45:00	11.43	28.39	0.24	6.85	10.16	2.33	0.01

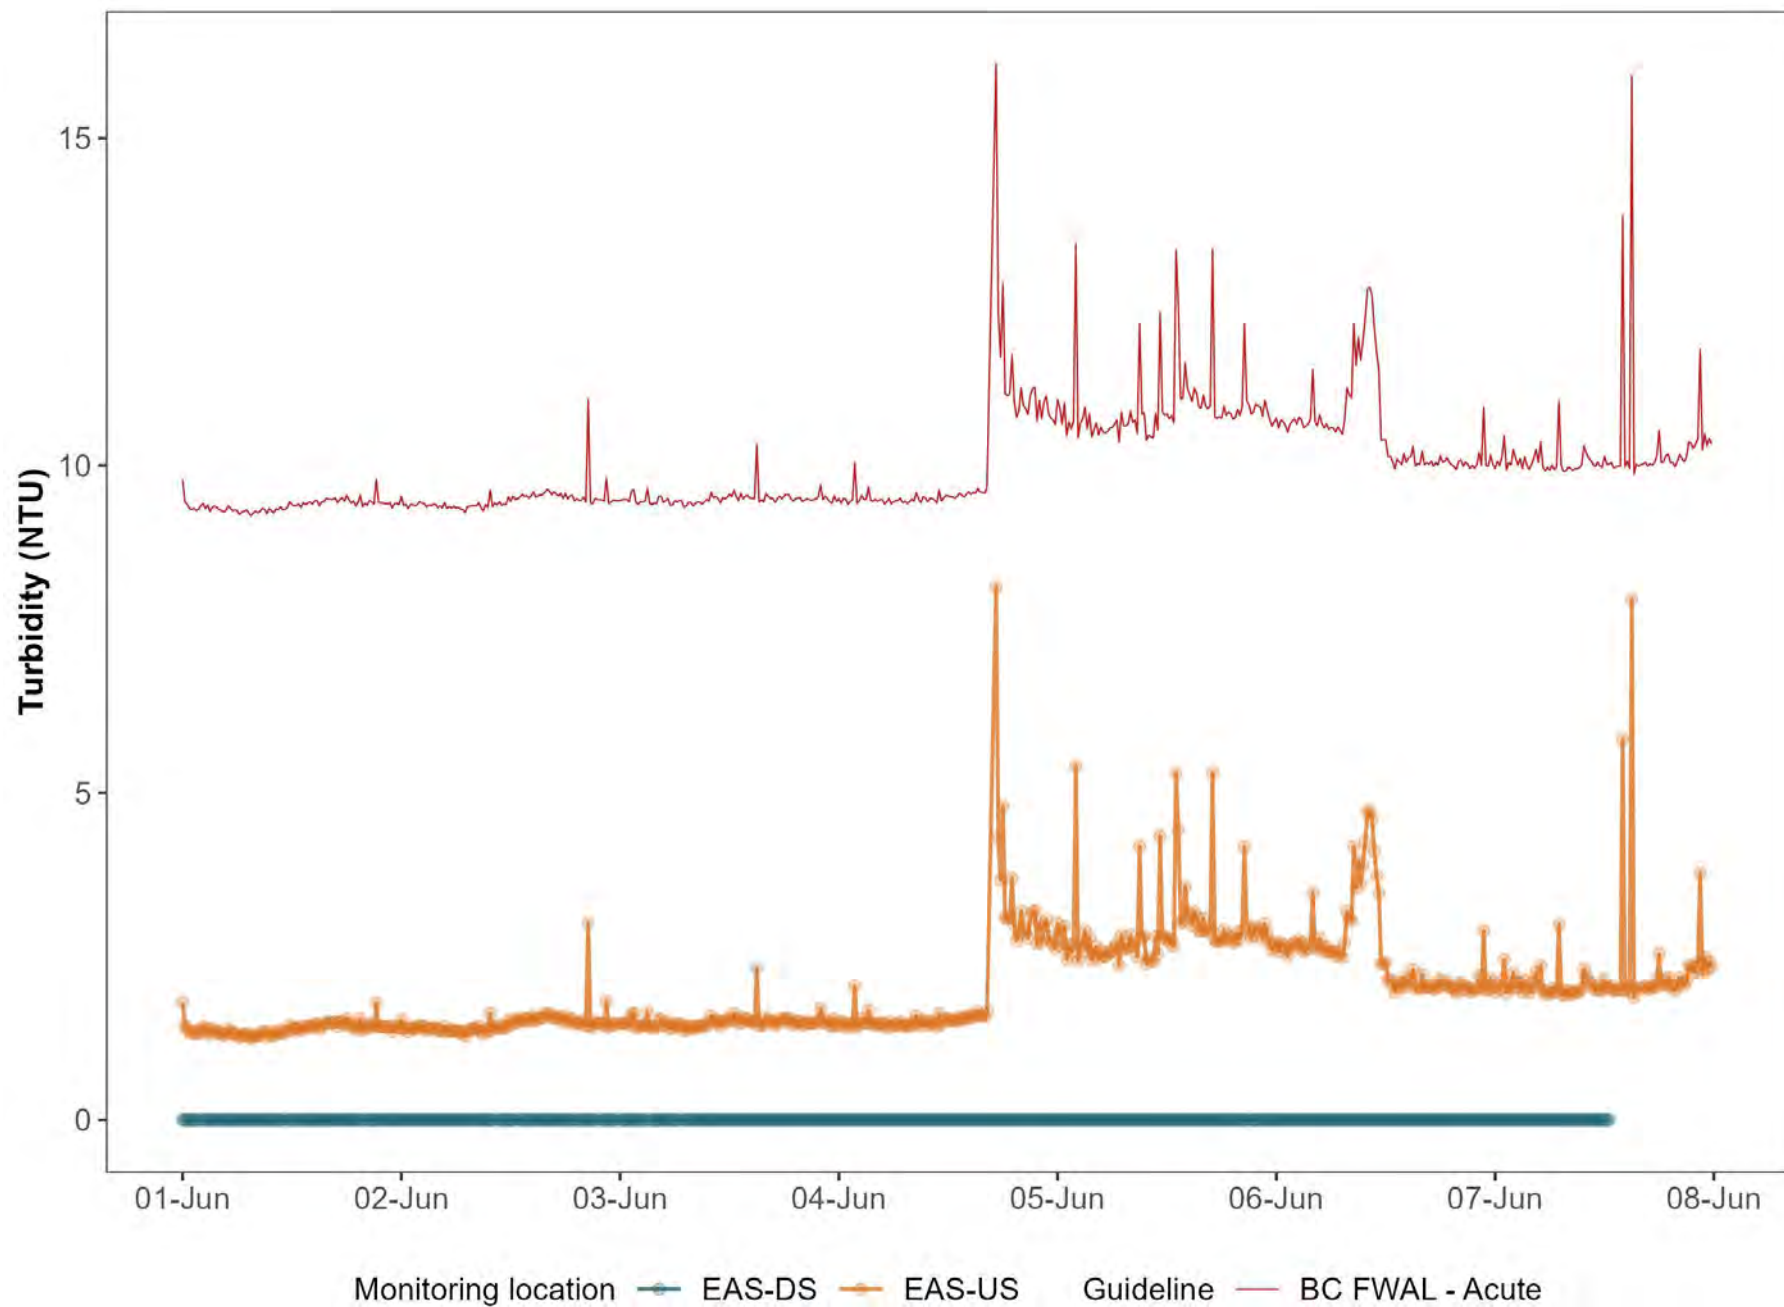

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	<u>WLNG (EAS) DS</u>	Date:	<u>June 2, 2026</u>
Site Name:	<u>East Creek</u>	Time:	<u>10:20</u>
Site UTM:	Zone: 10U E: <u>482092</u>	Crew:	<u>HM</u>
(NAD83)	N: <u>5501875</u>	Weather:	<u>Sun</u>

In Situ Parameters

pH:	<u>7.39</u>	DO:	<u>4.11</u>	(mg/L)
Temp:	<u>12.5</u>	Cond:	<u>198</u>	(us/cm)
Turbidity:	<u>0</u>	Salinity:	<u>0.1</u>	(ppt)
Visible Sheen:	<u>N</u>	ORP:	<u>151.9</u>	(mV)
Water Surface Condition:	<u>Clear</u>			

Photo Record



Observations

No issues observed

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	<u>WLNG (EAS) US</u>	Date:	<u>June 2, 2026</u>
Site Name:	<u>East Creek</u>	Time:	<u>9:30</u>
Site UTM:	Zone:10U E: <u>481908</u>	Crew:	<u>HM</u>
(NAD83)	N: <u>5501909</u>	Weather:	<u>Sun</u>

In Situ Parameters

pH:	<u>7.19</u>	DO:	<u>4.49</u>	(mg/L)
Temp.:	<u>12.1</u>	Cond:	<u>61.1</u>	(us)
Turbidity:	<u>0</u>	Salinity:	<u>0.03</u>	(ppt)
Visible Sheen:	<u>N</u>	ORP:	<u>170.6</u>	(mV)
Water Surface Condition:	<u>Clear</u>			

Photo Record



Observations

No issues observed

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	June 1 to June 7, 2026
	Report #	115
	Appendix E	E-1

Appendix E: Lab Documentation



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 131162

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/06/15
 Report #: R3794185
 Version: 4 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C631926

Received: 2026/06/02, 17:45

Sample Matrix: Water
 # Samples Received: 6

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
Alkalinity @25C (pp, total), CO ₃ ,HCO ₃ ,OH	6	N/A	2026/06/04	BBY6SOP-00026	SM 24 2320 B m
Chloride/Sulphate by Auto Colourimetry	6	N/A	2026/06/04	BBY6SOP-00011 / BBY6SOP-00017	SM24-4500-Cl/SO ₄ -E m
Chromium III (Calc'd)	1	N/A	2026/06/10		
Chromium III (Calc'd)	5	N/A	2026/06/08		
Total Hexavalent Chromium	6	N/A	2026/06/05	BBY6SOP-00054	SM 24 3500-Cr B m
Daphnia Magna LC50 Multi-concentration	1	N/A	2026/06/03	BBY2SOP-00007	EC EPS 1/RM/14 R2
Carbon (DOC) -Lab Filtered (2)	6	N/A	2026/06/04	BBY6SOP-00053	SM 24 5310 B m
Fluoride	1	N/A	2026/06/04	BBY6SOP-00037	SM 24 4500-F C m
Fluoride	5	N/A	2026/06/05	BBY6SOP-00037	SM 24 4500-F C m
Glycols in Water by GC/FID (1)	2	N/A	2026/06/09	CAL SOP-00093	BCMOE Glycols 09/17
Sulphide (as H ₂ S) (1)	6	N/A	2026/06/09		Auto Calc
Un-ionized Hydrogen Sulphide as S Calc	4	N/A	2026/06/09	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	1	N/A	2026/06/10	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	1	N/A	2026/06/04	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	4	N/A	2026/06/08	BBY WI-00033	Auto Calc
Hardness (calculated as CaCO ₃)	6	N/A	2026/06/04	BBY WI-00033	Auto Calc
Mercury (Dissolved) by CV-Lab Filtered	6	2026/06/03	2026/06/03	BBY7SOP-00032	BCMOE LMAug2023 C m
Mercury (Total) by CV	6	2026/06/03	2026/06/04	BBY7SOP-00032	BCMOE LMAug2023 C m
Bromide as Bromine (Br) by ICPMS	6	N/A	2026/06/09	BBY7SOP-00002	EPA 6020B R2 m
EPH in Water when PAH required	2	2026/06/08	2026/06/08	BBY8SOP-00029	BCMOE BCLM Sep2017 m
Na, K, Ca, Mg, S by CRC ICPMS (diss.)	6	N/A	2026/06/04	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (lab filter) (4)	6	N/A	2026/06/04	BBY7SOP-00002	EPA 6020b R2 m
Elements by ICPMS Digested LL (total)	1	2026/06/09	2026/06/09	BBY7SOP-00003 / BBY7SOP-00002	EPA 6020b R2 m
Na, K, Ca, Mg, S by CRC ICPMS (total)	1	N/A	2026/06/10	BBY WI-00033	Auto Calc
Na, K, Ca, Mg, S by CRC ICPMS (total)	1	N/A	2026/06/04	BBY WI-00033	Auto Calc
Na, K, Ca, Mg, S by CRC ICPMS (total)	4	N/A	2026/06/08	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (total)	1	N/A	2026/06/04	BBY7SOP-00002	EPA 6020b R2 m
Elements by ICPMS Low Level (total)	4	N/A	2026/06/06	BBY7SOP-00002	EPA 6020b R2 m
Nitrogen (Total)	6	N/A	2026/06/08	BBY6SOP-00016	SM 24 4500-N C m



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 131162

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/06/15
 Report #: R3794185
 Version: 4 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C631926

Received: 2026/06/02, 17:45

Sample Matrix: Water
 # Samples Received: 6

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
Ammonia-N (Total)	6	N/A	2026/06/05	AB SOP-00007	SM 24 4500 NH3 A G m
Nitrate + Nitrite (N)	6	N/A	2026/06/03	BBY6SOP-00010	SM 24 4500-NO3- H m
Nitrite (N) Regular Level Water	6	N/A	2026/06/03	BBY6SOP-00010	SM 24 4500-NO2- m
Nitrogen - Nitrate (as N)	6	N/A	2026/06/04	BBY WI-00033	Auto Calc
PAH in Water by GC/MS (SIM)	2	2026/06/08	2026/06/08	BBY8SOP-00021	BCMOE BCLM Jul2017m
Total LMW, HMW, Total PAH Calc (5)	2	N/A	2026/06/09	BBY WI-00033	Auto Calc
pH @25°C (6)	6	N/A	2026/06/04	BBY6SOP-00026	SM 24 4500-H+ B m
Phenols (4-AAP) (1)	2	N/A	2026/06/05	AB SOP-00088	EPA 9066 R0 m
Rainbow Trout LC50 Multi-concentration	1	N/A	2026/06/04	BBY2SOP-00004	EPS1/RM/13(2nd)&RM/9
Total Sulphide (1)	6	2026/06/08	2026/06/09	AB SOP-00080	SM 24 4500 S2-A D Fm
Total Dissolved Solids (Filt. Residue)	6	2026/06/03	2026/06/04	BBY6SOP-00033	SM 24 2540 C m
EPH less PAH in Water by GC/FID (7)	2	N/A	2026/06/09	BBY WI-00033	Auto Calc
Carbon (Total Organic) (8)	6	N/A	2026/06/04	BBY6SOP-00053	SM 24 5310 B m
Total Phosphorus Low Level Total	6	2026/06/08	2026/06/09	BBY6SOP-00013	SM 24 4500-P E m
Total Suspended Solids (NFR)	6	2026/06/03	2026/06/04	BBY6SOP-00034	SM 24 2540 D m
Field pH	4	N/A	2026/06/03	Field Test	Field Test
Field Temperature	4	N/A	2026/06/03	Field Test	Field Test
VOCs, VH, F1, LH in Water by HS GC/MS	2	N/A	2026/06/06	BBY8SOP-00009 / BBY8SOP-00011 / BBY8SOP-00012	BCMOE BCLM Jul2017 m
Volatile HC-BTEX (9)	2	N/A	2026/06/08	BBY WI-00033	Auto Calc

Remarks:

Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation. Unless otherwise noted, procedures used by Bureau Veritas are based upon recognized Provincial, Federal or US method compendia such as CCME, EPA, APHA or the Quebec Ministry of Environment.

All work recorded herein has been done in accordance with procedures and practices ordinarily exercised by professionals in Bureau Veritas' profession using accepted testing methodologies, quality assurance and quality control procedures (except where otherwise agreed by the client and Bureau Veritas in writing). All data is in statistical control and has met quality control and method performance criteria unless otherwise noted. All method blanks are reported; unless indicated otherwise, associated sample data are not blank corrected. Where applicable, unless otherwise noted, Measurement Uncertainty has not been accounted for when stating conformity to the referenced standard.



Your P.O. #: 4800010213
Your Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your C.O.C. #: 131162

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
N. VANCOUVER
200-850 Harbourside Dr
North Vancouver, BC
Canada V7P 0A3

Report Date: 2026/06/15

Report #: R3794185

Version: 4 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C631926

Received: 2026/06/02, 17:45

Bureau Veritas liability is limited to the actual cost of the requested analyses, unless otherwise agreed in writing. There is no other warranty expressed or implied. Bureau Veritas has been retained to provide analysis of samples provided by the Client using the testing methodology referenced in this report. Interpretation and use of test results are the sole responsibility of the Client and are not within the scope of services provided by Bureau Veritas, unless otherwise agreed in writing. Bureau Veritas is not responsible for the accuracy or any data impacts, that result from the information provided by the customer or their agent.

Solid sample results, except biota, are based on dry weight unless otherwise indicated. Organic analyses are not recovery corrected except for isotope dilution methods.

Results relate to samples tested. When sampling is not conducted by Bureau Veritas, results relate to the supplied samples tested.

This Certificate shall not be reproduced except in full, without the written approval of the laboratory.

Reference Method suffix "m" indicates test methods incorporate validated modifications from specific reference methods to improve performance.

* RPDs calculated using raw data. The rounding of final results may result in the apparent difference.

(1) This test was performed by Bureau Veritas Calgary, 4000 - 19 St. , Calgary, AB, T2E 6P8

(2) DOC present in the sample should be considered as non-purgeable DOC. Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(3) "Total Hardness" was calculated from Total Ca and Mg concentrations and may be biased high (Hardness, or Dissolved Hardness, calculated from Dissolved Ca and Mg, should be used for compliance if available).

(4) Samples were filtered and preserved at the lab. Values may not reflect concentrations at the time of sampling.

For Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(5) Total PAHs in Water include: Quinoline, Naphthalene, 1-Methylnaphthalene, 2-Methylnaphthalene, Acenaphthylene, Acenaphthene, Fluorene, Phenanthrene, Anthracene, Acridine, Fluoranthene, Pyrene, Benzo(a)anthracene, Chrysene, Benzo(b&j)fluoranthene, Benzo(k)fluoranthene, Benzo(a)pyrene, Indeno(1,2,3-cd)pyrene, Dibenz(a,h)anthracene, and Benzo(g,h,i)perylene.

(6) The CCME method requires pH to be analysed within 15 minutes of sampling and therefore field analysis is required for compliance. All Laboratory pH analyses in this report are reported past the CCME holding time. Bureau Veritas endeavours to analyze samples as soon as possible after receipt.

(7) LEPH = EPH (C10 to C19) - (Acenaphthene + Acridine + Anthracene + Fluorene + Naphthalene + Phenanthrene)

HEPH = EPH (C19 to C32) - (Benzo(a)anthracene + Benzo(a)pyrene + Fluoranthene + Pyrene)

(8) TOC present in the sample should be considered as non-purgeable TOC.

(9) VPH = VH - (Benzene + Toluene + Ethylbenzene + m & p-Xylene + o-Xylene + Styrene)

Encryption Key

Please direct all questions regarding this Certificate of Analysis to:

Levi Manchak, Project Manager SR

Email: Levi.MANCHAK@bureauveritas.com

Phone# (780)862-5634

=====

Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports. For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.

Total Cover Pages : 3

Page 3 of 53



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ440			EFZ440			EFZ441		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch

ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C303397				ND	0.0050	C303397
Calculated Parameters										
Total Chromium III	mg/L	ND	0.0099	C302849				ND	0.00099	C302849
Dissolved Hardness (CaCO ₃)	mg/L	56.8	0.50	C302396				62.3	0.50	C302396
Total Hardness (CaCO ₃)	mg/L	55.9	0.50	C302360				63.9	0.50	C302360
Nitrate (N)	mg/L	0.078	0.020	C302368				0.081	0.020	C302368
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C302929				ND	0.0020	C302929
Daphnia Magna										
LC50	% vol/vol							ATTACHED	N/A	C303268
Field Parameters										
Field pH	pH	7.4	N/A	ONSITE				7.3	N/A	ONSITE
Field Temperature	°C	12.5	N/A	ONSITE				12.9	N/A	ONSITE
Misc. Inorganics										
pH	pH	7.53	N/A	C304013				7.55	N/A	C304013
Total Organic Carbon (C)	mg/L	0.98 (1)	0.50	C304074	1.0	0.50	C304074	0.86	0.50	C304074
Total Dissolved Solids	mg/L	110	10	C303398				100	10	C303398
Total Suspended Solids	mg/L	1.6	1.0	C303355	1.6	1.0	C303355	1.2	1.0	C303355
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L	0.98	0.50	C303210				1.1	0.50	C303210
Anions										
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C304011				ND	1.0	C304011
Alkalinity (Total as CaCO ₃)	mg/L	44	1.0	C304011				46	1.0	C304011
Bicarbonate (HCO ₃)	mg/L	53	1.0	C304011				56	1.0	C304011
Carbonate (CO ₃)	mg/L	ND	1.0	C304011				ND	1.0	C304011
Fluoride (F)	mg/L	0.23	0.050	C304639				0.28	0.050	C304639
Hydroxide (OH)	mg/L	ND	1.0	C304011				ND	1.0	C304011

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.

N/A = Not Applicable

(1) Matrix spike exceeds acceptance limits due to matrix interference. Unable to reanalyze due to insufficient sample.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ440			EFZ440			EFZ441		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Total Sulphide	mg/L	ND	0.0018	C307725	ND	0.0018	C307725	ND	0.0018	C307725
Chloride (Cl)	mg/L	12	1.0	C304198				13	1.0	C304198
Sulphate (SO4)	mg/L	15	1.0	C304198				16	1.0	C304198
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.0099	C304846				ND	0.00099	C304846
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C304746	ND	0.015	C304746	ND	0.015	C304746
Total Phosphorus (P)	mg/L	0.0037	0.0010	C307079	0.0048	0.0010	C307079	0.0023	0.0010	C307079
Nitrate plus Nitrite (N)	mg/L	0.078	0.020	C303392				0.081	0.020	C303392
Total Nitrogen (N)	mg/L	0.254	0.020	C305521	0.252	0.020	C305521	0.214	0.020	C305521
Misc. Organics										
Phenols	mg/L							ND	0.0015	C305451
Rainbow Trout										
LC50	% vol/vol							ATTACHED	N/A	C306706
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ442			EFZ442			EFZ443		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-US	RDL	QC Batch	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C303397	ND	0.0050	C303397	ND	0.0050	C303397
Calculated Parameters										
Total Chromium III	mg/L	ND	0.0099	C302849				ND	0.00099	C302849
Dissolved Hardness (CaCO ₃)	mg/L	7.00	0.50	C302396				ND	0.50	C302396
Total Hardness (CaCO ₃)	mg/L	7.11	0.50	C302360				ND	0.50	C302360
Nitrate (N)	mg/L	ND	0.020	C302368				ND	0.020	C302368
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C302929				ND	0.0020	C302929
Field Parameters										
Field pH	pH	7.2	N/A	ONSITE						
Field Temperature	°C	12.1	N/A	ONSITE						
Misc. Inorganics										
pH	pH	6.71	N/A	C304013				6.05	N/A	C304013
Total Organic Carbon (C)	mg/L	1.5	0.50	C304074				ND	0.50	C304074
Total Dissolved Solids	mg/L	ND	10	C303398				ND	10	C303398
Total Suspended Solids	mg/L	ND	1.0	C303364				ND	1.0	C303355
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L	1.6	0.50	C303210				ND	0.50	C303210
Anions										
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C304011				ND	1.0	C304011
Alkalinity (Total as CaCO ₃)	mg/L	7.2	1.0	C304011				ND	1.0	C304011
Bicarbonate (HCO ₃)	mg/L	8.8	1.0	C304011				ND	1.0	C304011
Carbonate (CO ₃)	mg/L	ND	1.0	C304011				ND	1.0	C304011
Fluoride (F)	mg/L	ND	0.050	C304639				ND	0.050	C304639
Hydroxide (OH)	mg/L	ND	1.0	C304011				ND	1.0	C304011
Total Sulphide	mg/L	ND	0.0018	C307725				ND	0.0018	C307725
Chloride (Cl)	mg/L	ND	1.0	C304198				ND	1.0	C304198
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ442			EFZ442			EFZ443		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-US	RDL	QC Batch	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch
Sulphate (SO4)	mg/L	2.2	1.0	C304198				ND	1.0	C304198
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.0099	C304846				0.0014	0.00099	C304846
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C304746				ND	0.015	C304746
Total Phosphorus (P)	mg/L	0.010	0.0010	C307079				ND	0.0010	C307079
Nitrate plus Nitrite (N)	mg/L	ND	0.020	C303392	ND	0.020	C303392	ND	0.020	C303392
Total Nitrogen (N)	mg/L	0.049	0.020	C305521				ND	0.020	C305521
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C631926

Report Date: 2026/06/15

HATFIELD CONSULTANTS

Client Project #: FORTIS11234/PE110163

Site Location: WOODFIBRE PIPELINE PROJECT

Your P.O. #: 4800010213

Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ443			EFZ444			EFZ444		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L				ND	0.0050	C303397			
Calculated Parameters										
Total Chromium III	mg/L				ND	0.0099	C302849			
Dissolved Hardness (CaCO ₃)	mg/L				ND	0.50	C302396			
Total Hardness (CaCO ₃)	mg/L				ND	0.50	C302360			
Nitrate (N)	mg/L				ND	0.020	C302368			
Sulphide (as H ₂ S)	mg/L				ND	0.0020	C302339			
Misc. Inorganics										
pH	pH				5.87	N/A	C304013			
Total Organic Carbon (C)	mg/L				ND	0.50	C304074			
Total Dissolved Solids	mg/L				ND	10	C303398	ND	10	C303398
Total Suspended Solids	mg/L				ND	1.0	C303355			
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L				ND	0.50	C303210			
Anions										
Alkalinity (PP as CaCO ₃)	mg/L				ND	1.0	C304011			
Alkalinity (Total as CaCO ₃)	mg/L				ND	1.0	C304011			
Bicarbonate (HCO ₃)	mg/L				ND	1.0	C304011			
Carbonate (CO ₃)	mg/L				ND	1.0	C304011			
Fluoride (F)	mg/L				ND	0.050	C304639			
Hydroxide (OH)	mg/L				ND	1.0	C304011			
Total Sulphide	mg/L				ND	0.0018	C307725			
Chloride (Cl)	mg/L	ND	1.0	C304198	ND	1.0	C304198			
Sulphate (SO ₄)	mg/L	ND	1.0	C304198	ND	1.0	C304198			
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										
N/A = Not Applicable										



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ443			EFZ444			EFZ444		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch
Metals										
Total Hex. Chromium (Cr 6+)	mg/L				ND	0.0099	C304844			
Nutrients										
Total Ammonia (N)	mg/L				ND	0.015	C304746			
Total Phosphorus (P)	mg/L				ND	0.0010	C307079			
Nitrate plus Nitrite (N)	mg/L				ND	0.020	C303392			
Total Nitrogen (N)	mg/L				ND	0.020	C305521			
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ445		
Sampling Date		2026/06/02 09:30		
COC Number		131162		
	UNITS	DUP	RDL	QC Batch
ANIONS				
Nitrite (N)	mg/L	ND	0.0050	C303397
Calculated Parameters				
Total Chromium III	mg/L	ND	0.0099	C302849
Dissolved Hardness (CaCO ₃)	mg/L	63.9	0.50	C302396
Total Hardness (CaCO ₃)	mg/L	65.1	0.50	C302360
Nitrate (N)	mg/L	0.086	0.020	C302368
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C302339
Field Parameters				
Field pH	pH	7.3	N/A	ONSITE
Field Temperature	°C	12.5	N/A	ONSITE
Misc. Inorganics				
pH	pH	7.38	N/A	C304013
Total Organic Carbon (C)	mg/L	0.85	0.50	C304074
Total Dissolved Solids	mg/L	68	10	C303398
Total Suspended Solids	mg/L	ND	1.0	C303355
Lab Filtered Inorganics				
Dissolved Organic Carbon (C)	mg/L	1.0	0.50	C303210
Anions				
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C304011
Alkalinity (Total as CaCO ₃)	mg/L	46	1.0	C304011
Bicarbonate (HCO ₃)	mg/L	56	1.0	C304011
Carbonate (CO ₃)	mg/L	ND	1.0	C304011
Fluoride (F)	mg/L	0.27	0.050	C304646
Hydroxide (OH)	mg/L	ND	1.0	C304011
Total Sulphide	mg/L	ND	0.0018	C307725
Chloride (Cl)	mg/L	14	1.0	C304198
RDL = Reportable Detection Limit				
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				
N/A = Not Applicable				



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EFZ445		
Sampling Date		2026/06/02 09:30		
COC Number		131162		
	UNITS	DUP	RDL	QC Batch
Sulphate (SO4)	mg/L	16	1.0	C304198
Metals				
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.0099	C304846
Nutrients				
Total Ammonia (N)	mg/L	ND	0.015	C304746
Total Phosphorus (P)	mg/L	0.0022	0.0010	C307079
Nitrate plus Nitrite (N)	mg/L	0.086	0.020	C303392
Total Nitrogen (N)	mg/L	0.229	0.020	C305521
Misc. Organics				
Phenols	mg/L	ND	0.0015	C305451
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

GLYCOLS BY GC-FID (WATER)

Bureau Veritas ID		EFZ441	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Glycols					
Ethylene Glycol	mg/L	ND	ND	3.0	C307509
Diethylene Glycol	mg/L	ND	ND	5.0	C307509
Triethylene Glycol	mg/L	ND	ND	5.0	C307509
Propylene Glycol	mg/L	ND	ND	5.0	C307509
Surrogate Recovery (%)					
Methyl Sulfone (sur.)	%	99	96		C307509
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

MERCURY BY COLD VAPOR (WATER)

Bureau Veritas ID		EFZ440	EFZ441	EFZ442	EFZ443	EFZ444	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162	131162	131162	131162	131162		
	UNITS	WLNG-DS	WLNG -EOP	WLNG-US	Field Blank	Trip Blank	DUP	RDL	QC Batch
Elements									
Total Mercury (Hg)	ug/L	ND	ND	ND	ND	ND	ND	0.0019	C303060
Lab Filtered Elements									
Dissolved Mercury (Hg)	ug/L	ND	ND	ND	ND	ND	ND	0.0019	C303051
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.									



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ440			EFZ440			EFZ441		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch

ANIONS										
Bromide (Br)	mg/L	ND	0.010	C307634				ND	0.010	C307634
Dissolved Metals by ICPMS										
Dissolved Calcium (Ca)	mg/L	21.0	0.050	C302862				23.1	0.050	C302862
Dissolved Magnesium (Mg)	mg/L	1.07	0.050	C302862				1.13	0.050	C302862
Dissolved Potassium (K)	mg/L	1.31	0.050	C302862				1.24	0.050	C302862
Dissolved Sodium (Na)	mg/L	5.99	0.050	C302862				6.20	0.050	C302862
Dissolved Sulphur (S)	mg/L	4.6	3.0	C302862				4.1	3.0	C302862
Lab Filtered Metals										
Dissolved Aluminum (Al)	ug/L	41.4	0.50	C303792	41.2	0.50	C303792	34.0	0.50	C303792
Dissolved Antimony (Sb)	ug/L	0.258	0.020	C303792	0.263	0.020	C303792	0.292	0.020	C303792
Dissolved Arsenic (As)	ug/L	0.624	0.020	C303792	0.589	0.020	C303792	0.631	0.020	C303792
Dissolved Barium (Ba)	ug/L	4.33	0.020	C303792	4.52	0.020	C303792	5.96	0.020	C303792
Dissolved Beryllium (Be)	ug/L	ND	0.010	C303792	ND	0.010	C303792	ND	0.010	C303792
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Boron (B)	ug/L	ND	10	C303792	ND	10	C303792	ND	10	C303792
Dissolved Cadmium (Cd)	ug/L	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Cesium (Cs)	ug/L	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Chromium (Cr)	ug/L	0.14	0.10	C303792	0.14	0.10	C303792	0.11	0.10	C303792
Dissolved Cobalt (Co)	ug/L	0.0304	0.0050	C303792	0.0280	0.0050	C303792	0.0559	0.0050	C303792
Dissolved Copper (Cu)	ug/L	0.078	0.050	C303792	0.073	0.050	C303792	ND	0.050	C303792
Dissolved Iron (Fe)	ug/L	1.7	1.0	C303792	1.7	1.0	C303792	ND	1.0	C303792
Dissolved Lead (Pb)	ug/L	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Lithium (Li)	ug/L	3.19 (1)	0.50	C303792	3.28	0.50	C303792	3.54	0.50	C303792
Dissolved Manganese (Mn)	ug/L	18.0	0.050	C303792	18.1	0.050	C303792	28.2	0.050	C303792
Dissolved Molybdenum (Mo)	ug/L	28.1	0.050	C303792	28.2	0.050	C303792	30.0	0.050	C303792
Dissolved Nickel (Ni)	ug/L	0.110	0.020	C303792	0.126	0.020	C303792	0.199	0.020	C303792
Dissolved Phosphorus (P)	ug/L	ND	2.0	C303792	2.1	2.0	C303792	2.6	2.0	C303792

RDL = Reportable Detection Limit
Lab-Dup = Laboratory Initiated Duplicate
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.
(1) Matrix spike exceeds acceptance limits due to matrix interference.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ440			EFZ440			EFZ441		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Dissolved Rubidium (Rb)	ug/L	2.98	0.050	C303792	2.98	0.050	C303792	2.63	0.050	C303792
Dissolved Selenium (Se)	ug/L	0.052	0.040	C303792	0.050	0.040	C303792	0.071	0.040	C303792
Dissolved Silicon (Si)	ug/L	6620	50	C303792	6820	50	C303792	6640	50	C303792
Dissolved Silver (Ag)	ug/L	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Strontium (Sr)	ug/L	44.2	0.050	C303792	44.8	0.050	C303792	46.8	0.050	C303792
Dissolved Tellurium (Te)	ug/L	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Thallium (Tl)	ug/L	0.0043	0.0020	C303792	0.0038	0.0020	C303792	0.0035	0.0020	C303792
Dissolved Thorium (Th)	ug/L	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Tin (Sn)	ug/L	ND	0.20	C303792	ND	0.20	C303792	ND	0.20	C303792
Dissolved Titanium (Ti)	ug/L	ND	0.50	C303792	ND	0.50	C303792	ND	0.50	C303792
Dissolved Uranium (U)	ug/L	0.246	0.0020	C303792	0.248	0.0020	C303792	0.212	0.0020	C303792
Dissolved Vanadium (V)	ug/L	0.20	0.20	C303792	ND	0.20	C303792	ND	0.20	C303792
Dissolved Zinc (Zn)	ug/L	0.94	0.10	C303792	0.87	0.10	C303792	1.27	0.10	C303792
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C303792	ND	0.10	C303792	ND	0.10	C303792
Total Metals by ICPMS										
Total Aluminum (Al)	ug/L	73.0	3.0	C308119				64.6	0.50	C304119
Total Antimony (Sb)	ug/L	0.277	0.020	C308119				0.293	0.020	C304119
Total Arsenic (As)	ug/L	0.647	0.020	C308119				0.683	0.020	C304119
Total Barium (Ba)	ug/L	4.83	0.050	C308119				6.50	0.020	C304119
Total Beryllium (Be)	ug/L	ND	0.010	C308119				ND	0.010	C304119
Total Bismuth (Bi)	ug/L	ND	0.010	C308119				ND	0.0050	C304119
Total Boron (B)	ug/L	ND	10	C308119				12	10	C304119
Total Cadmium (Cd)	ug/L	ND	0.0050	C308119				ND	0.0050	C304119
Total Cesium (Cs)	ug/L	ND	0.050	C308119				ND	0.050	C304119
Total Chromium (Cr)	ug/L	0.36	0.10	C308119				0.14	0.10	C304119
Total Cobalt (Co)	ug/L	0.039	0.010	C308119				0.0566	0.0050	C304119
Total Copper (Cu)	ug/L	0.17	0.10	C308119				0.092	0.050	C304119
Total Iron (Fe)	ug/L	26.0	5.0	C308119				15.2	1.0	C304119
Total Lead (Pb)	ug/L	0.021	0.020	C308119				ND	0.0050	C304119
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ440			EFZ440			EFZ441		
Sampling Date		2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162			131162			131162		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Total Lithium (Li)	ug/L	4.12	0.50	C308119				5.18	0.50	C304119
Total Manganese (Mn)	ug/L	19.7	0.10	C308119				29.4	0.050	C304119
Total Molybdenum (Mo)	ug/L	29.2	0.050	C308119				31.9	0.050	C304119
Total Nickel (Ni)	ug/L	0.13	0.10	C308119				0.114	0.020	C304119
Total Phosphorus (P)	ug/L	ND	5.0	C308119				ND	2.0	C304119
Total Rubidium (Rb)	ug/L	3.18	0.050	C308119				2.98	0.050	C304119
Total Selenium (Se)	ug/L	0.051	0.040	C308119				0.063	0.040	C304119
Total Silicon (Si)	ug/L	6660	50	C308119				6710	50	C304119
Total Silver (Ag)	ug/L	ND	0.010	C308119				ND	0.0050	C304119
Total Strontium (Sr)	ug/L	47.3	0.050	C308119				51.6	0.050	C304119
Total Tellurium (Te)	ug/L	ND	0.020	C308119				ND	0.020	C304119
Total Thallium (Tl)	ug/L	0.0083	0.0020	C308119				0.0086	0.0020	C304119
Total Thorium (Th)	ug/L	ND	0.050	C308119				ND	0.050	C304119
Total Tin (Sn)	ug/L	ND	0.20	C308119				ND	0.20	C304119
Total Titanium (Ti)	ug/L	ND	2.0	C308119				0.67	0.50	C304119
Total Uranium (U)	ug/L	0.266	0.0050	C308119				0.224	0.0020	C304119
Total Vanadium (V)	ug/L	0.22	0.20	C308119				0.26	0.20	C304119
Total Zinc (Zn)	ug/L	1.6	1.0	C308119				1.34	0.10	C304119
Total Zirconium (Zr)	ug/L	ND	0.10	C308119				ND	0.10	C304119
Total Calcium (Ca)	mg/L	20.6	0.25	C302864				23.5	0.050	C302864
Total Magnesium (Mg)	mg/L	1.09	0.25	C302864				1.26	0.050	C302864
Total Potassium (K)	mg/L	1.39	0.25	C302864				1.36	0.050	C302864
Total Sodium (Na)	mg/L	5.83	0.25	C302864				6.91	0.050	C302864
Total Sulphur (S)	mg/L	4.2	3.0	C302864				5.1	3.0	C302864
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ442	EFZ443			EFZ443			EFZ444		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162	131162			131162			131162		
	UNITS	WLNG-US	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch

ANIONS											
Bromide (Br)	mg/L	ND	ND	0.010	C307634				ND	0.010	C307634
Dissolved Metals by ICPMS											
Dissolved Calcium (Ca)	mg/L	2.42	ND	0.050	C302862				ND	0.050	C302862
Dissolved Magnesium (Mg)	mg/L	0.231	ND	0.050	C302862				ND	0.050	C302862
Dissolved Potassium (K)	mg/L	0.148	ND	0.050	C302862				ND	0.050	C302862
Dissolved Sodium (Na)	mg/L	1.48	ND	0.050	C302862				ND	0.050	C302862
Dissolved Sulphur (S)	mg/L	ND	ND	3.0	C302862				ND	3.0	C302862
Lab Filtered Metals											
Dissolved Aluminum (Al)	ug/L	31.7	ND	0.50	C303792	ND	0.50	C303792	ND	0.50	C303792
Dissolved Antimony (Sb)	ug/L	ND	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Arsenic (As)	ug/L	0.083	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Barium (Ba)	ug/L	3.84	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Beryllium (Be)	ug/L	ND	ND	0.010	C303792	ND	0.010	C303792	ND	0.010	C303792
Dissolved Bismuth (Bi)	ug/L	ND	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Boron (B)	ug/L	ND	ND	10	C303792	ND	10	C303792	ND	10	C303792
Dissolved Cadmium (Cd)	ug/L	ND	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Cesium (Cs)	ug/L	ND	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Chromium (Cr)	ug/L	ND	ND	0.10	C303792	ND	0.10	C303792	ND	0.10	C303792
Dissolved Cobalt (Co)	ug/L	0.0161	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Copper (Cu)	ug/L	0.453	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Iron (Fe)	ug/L	19.4	ND	1.0	C303792	ND	1.0	C303792	ND	1.0	C303792
Dissolved Lead (Pb)	ug/L	0.0061	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Lithium (Li)	ug/L	ND	ND	0.50	C303792	ND	0.50	C303792	ND	0.50	C303792
Dissolved Manganese (Mn)	ug/L	0.715	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Molybdenum (Mo)	ug/L	0.401	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Nickel (Ni)	ug/L	0.200	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Phosphorus (P)	ug/L	6.8	ND	2.0	C303792	ND	2.0	C303792	ND	2.0	C303792
Dissolved Rubidium (Rb)	ug/L	0.299	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ442	EFZ443			EFZ443			EFZ444		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162	131162			131162			131162		
	UNITS	WLNG-US	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch
Dissolved Selenium (Se)	ug/L	ND	ND	0.040	C303792	ND	0.040	C303792	ND	0.040	C303792
Dissolved Silicon (Si)	ug/L	4380	ND	50	C303792	ND	50	C303792	ND	50	C303792
Dissolved Silver (Ag)	ug/L	ND	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Strontium (Sr)	ug/L	12.4	ND	0.050	C303792	ND	0.050	C303792	ND	0.050	C303792
Dissolved Tellurium (Te)	ug/L	ND	ND	0.020	C303792	ND	0.020	C303792	ND	0.020	C303792
Dissolved Thallium (Tl)	ug/L	ND	ND	0.0020	C303792	ND	0.0020	C303792	0.0037	0.0020	C303792
Dissolved Thorium (Th)	ug/L	ND	ND	0.0050	C303792	ND	0.0050	C303792	ND	0.0050	C303792
Dissolved Tin (Sn)	ug/L	ND	ND	0.20	C303792	ND	0.20	C303792	ND	0.20	C303792
Dissolved Titanium (Ti)	ug/L	ND	ND	0.50	C303792	ND	0.50	C303792	ND	0.50	C303792
Dissolved Uranium (U)	ug/L	0.0421	ND	0.0020	C303792	ND	0.0020	C303792	ND	0.0020	C303792
Dissolved Vanadium (V)	ug/L	ND	ND	0.20	C303792	ND	0.20	C303792	ND	0.20	C303792
Dissolved Zinc (Zn)	ug/L	0.92	ND	0.10	C303792	ND	0.10	C303792	ND	0.10	C303792
Dissolved Zirconium (Zr)	ug/L	ND	0.29	0.10	C303792	0.27	0.10	C303792	ND	0.10	C303792
Total Metals by ICPMS											
Total Aluminum (Al)	ug/L	40.0	0.91	0.50	C305396				ND	0.50	C305396
Total Antimony (Sb)	ug/L	ND	ND	0.020	C305396				ND	0.020	C305396
Total Arsenic (As)	ug/L	0.083	ND	0.020	C305396				ND	0.020	C305396
Total Barium (Ba)	ug/L	4.18	0.021	0.020	C305396				ND	0.020	C305396
Total Beryllium (Be)	ug/L	ND	ND	0.010	C305396				ND	0.010	C305396
Total Bismuth (Bi)	ug/L	ND	ND	0.0050	C305396				ND	0.0050	C305396
Total Boron (B)	ug/L	ND	ND	10	C305396				ND	10	C305396
Total Cadmium (Cd)	ug/L	ND	ND	0.0050	C305396				ND	0.0050	C305396
Total Cesium (Cs)	ug/L	ND	ND	0.050	C305396				ND	0.050	C305396
Total Chromium (Cr)	ug/L	ND	ND	0.10	C305396				ND	0.10	C305396
Total Cobalt (Co)	ug/L	0.0161	ND	0.0050	C305396				ND	0.0050	C305396
Total Copper (Cu)	ug/L	0.505	ND	0.050	C305396				ND	0.050	C305396
Total Iron (Fe)	ug/L	28.3	ND	1.0	C305396				ND	1.0	C305396
Total Lead (Pb)	ug/L	0.0116	ND	0.0050	C305396				ND	0.0050	C305396
Total Lithium (Li)	ug/L	ND	ND	0.50	C305396				ND	0.50	C305396

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ442	EFZ443			EFZ443			EFZ444		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30			2026/06/02 09:30			2026/06/02 09:30		
COC Number		131162	131162			131162			131162		
	UNITS	WLNG-US	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch
Total Manganese (Mn)	ug/L	1.05	ND	0.050	C305396				ND	0.050	C305396
Total Molybdenum (Mo)	ug/L	0.380	ND	0.050	C305396				ND	0.050	C305396
Total Nickel (Ni)	ug/L	0.200	ND	0.020	C305396				ND	0.020	C305396
Total Phosphorus (P)	ug/L	6.7	ND	2.0	C305396				ND	2.0	C305396
Total Rubidium (Rb)	ug/L	0.328	ND	0.050	C305396				ND	0.050	C305396
Total Selenium (Se)	ug/L	ND	ND	0.040	C305396				ND	0.040	C305396
Total Silicon (Si)	ug/L	4300	ND	50	C305396				ND	50	C305396
Total Silver (Ag)	ug/L	ND	ND	0.0050	C305396				ND	0.0050	C305396
Total Strontium (Sr)	ug/L	13.4	ND	0.050	C305396				ND	0.050	C305396
Total Tellurium (Te)	ug/L	ND	ND	0.020	C305396				ND	0.020	C305396
Total Thallium (Tl)	ug/L	ND	ND	0.0020	C305396				0.0038	0.0020	C305396
Total Thorium (Th)	ug/L	ND	ND	0.050	C305396				ND	0.050	C305396
Total Tin (Sn)	ug/L	ND	ND	0.20	C305396				ND	0.20	C305396
Total Titanium (Ti)	ug/L	ND	ND	0.50	C305396				ND	0.50	C305396
Total Uranium (U)	ug/L	0.0516	ND	0.0020	C305396				ND	0.0020	C305396
Total Vanadium (V)	ug/L	ND	ND	0.20	C305396				ND	0.20	C305396
Total Zinc (Zn)	ug/L	0.78	ND	0.10	C305396				ND	0.10	C305396
Total Zirconium (Zr)	ug/L	ND	ND	0.10	C305396				ND	0.10	C305396
Total Calcium (Ca)	mg/L	2.43	ND	0.050	C302864				ND	0.050	C302864
Total Magnesium (Mg)	mg/L	0.253	ND	0.050	C302864				ND	0.050	C302864
Total Potassium (K)	mg/L	0.159	ND	0.050	C302864				ND	0.050	C302864
Total Sodium (Na)	mg/L	1.63	ND	0.050	C302864				ND	0.050	C302864
Total Sulphur (S)	mg/L	ND	ND	3.0	C302864				ND	3.0	C302864

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ445		
Sampling Date		2026/06/02 09:30		
COC Number		131162		
	UNITS	DUP	RDL	QC Batch
ANIONS				
Bromide (Br)	mg/L	ND	0.010	C307634
Dissolved Metals by ICPMS				
Dissolved Calcium (Ca)	mg/L	23.7	0.050	C302862
Dissolved Magnesium (Mg)	mg/L	1.13	0.050	C302862
Dissolved Potassium (K)	mg/L	1.24	0.050	C302862
Dissolved Sodium (Na)	mg/L	6.35	0.050	C302862
Dissolved Sulphur (S)	mg/L	4.7	3.0	C302862
Lab Filtered Metals				
Dissolved Aluminum (Al)	ug/L	33.7	0.50	C303792
Dissolved Antimony (Sb)	ug/L	0.312	0.020	C303792
Dissolved Arsenic (As)	ug/L	0.629	0.020	C303792
Dissolved Barium (Ba)	ug/L	6.24	0.020	C303792
Dissolved Beryllium (Be)	ug/L	ND	0.010	C303792
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C303792
Dissolved Boron (B)	ug/L	ND	10	C303792
Dissolved Cadmium (Cd)	ug/L	ND	0.0050	C303792
Dissolved Cesium (Cs)	ug/L	ND	0.050	C303792
Dissolved Chromium (Cr)	ug/L	0.10	0.10	C303792
Dissolved Cobalt (Co)	ug/L	0.0592	0.0050	C303792
Dissolved Copper (Cu)	ug/L	ND	0.050	C303792
Dissolved Iron (Fe)	ug/L	ND	1.0	C303792
Dissolved Lead (Pb)	ug/L	ND	0.0050	C303792
Dissolved Lithium (Li)	ug/L	3.23	0.50	C303792
Dissolved Manganese (Mn)	ug/L	29.8	0.050	C303792
Dissolved Molybdenum (Mo)	ug/L	30.3	0.050	C303792
Dissolved Nickel (Ni)	ug/L	0.171	0.020	C303792
Dissolved Phosphorus (P)	ug/L	ND	2.0	C303792
Dissolved Rubidium (Rb)	ug/L	2.71	0.050	C303792
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ445		
Sampling Date		2026/06/02 09:30		
COC Number		131162		
	UNITS	DUP	RDL	QC Batch
Dissolved Selenium (Se)	ug/L	0.054	0.040	C303792
Dissolved Silicon (Si)	ug/L	6780	50	C303792
Dissolved Silver (Ag)	ug/L	ND	0.0050	C303792
Dissolved Strontium (Sr)	ug/L	48.5	0.050	C303792
Dissolved Tellurium (Te)	ug/L	ND	0.020	C303792
Dissolved Thallium (Tl)	ug/L	0.0041	0.0020	C303792
Dissolved Thorium (Th)	ug/L	ND	0.0050	C303792
Dissolved Tin (Sn)	ug/L	ND	0.20	C303792
Dissolved Titanium (Ti)	ug/L	ND	0.50	C303792
Dissolved Uranium (U)	ug/L	0.192	0.0020	C303792
Dissolved Vanadium (V)	ug/L	ND	0.20	C303792
Dissolved Zinc (Zn)	ug/L	1.23	0.10	C303792
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C303792
Total Metals by ICPMS				
Total Aluminum (Al)	ug/L	51.8	0.50	C305396
Total Antimony (Sb)	ug/L	0.331	0.020	C305396
Total Arsenic (As)	ug/L	0.691	0.020	C305396
Total Barium (Ba)	ug/L	6.70	0.020	C305396
Total Beryllium (Be)	ug/L	ND	0.010	C305396
Total Bismuth (Bi)	ug/L	ND	0.0050	C305396
Total Boron (B)	ug/L	ND	10	C305396
Total Cadmium (Cd)	ug/L	ND	0.0050	C305396
Total Cesium (Cs)	ug/L	ND	0.050	C305396
Total Chromium (Cr)	ug/L	0.12	0.10	C305396
Total Cobalt (Co)	ug/L	0.0609	0.0050	C305396
Total Copper (Cu)	ug/L	0.078	0.050	C305396
Total Iron (Fe)	ug/L	6.2	1.0	C305396
Total Lead (Pb)	ug/L	ND	0.0050	C305396
Total Lithium (Li)	ug/L	4.61	0.50	C305396
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EFZ445		
Sampling Date		2026/06/02 09:30		
COC Number		131162		
	UNITS	DUP	RDL	QC Batch
Total Manganese (Mn)	ug/L	30.2	0.050	C305396
Total Molybdenum (Mo)	ug/L	32.2	0.050	C305396
Total Nickel (Ni)	ug/L	0.153	0.020	C305396
Total Phosphorus (P)	ug/L	ND	2.0	C305396
Total Rubidium (Rb)	ug/L	2.98	0.050	C305396
Total Selenium (Se)	ug/L	0.062	0.040	C305396
Total Silicon (Si)	ug/L	6800	50	C305396
Total Silver (Ag)	ug/L	ND	0.0050	C305396
Total Strontium (Sr)	ug/L	52.8	0.050	C305396
Total Tellurium (Te)	ug/L	ND	0.020	C305396
Total Thallium (Tl)	ug/L	0.0066	0.0020	C305396
Total Thorium (Th)	ug/L	ND	0.050	C305396
Total Tin (Sn)	ug/L	ND	0.20	C305396
Total Titanium (Ti)	ug/L	ND	0.50	C305396
Total Uranium (U)	ug/L	0.233	0.0020	C305396
Total Vanadium (V)	ug/L	ND	0.20	C305396
Total Zinc (Zn)	ug/L	1.71	0.10	C305396
Total Zirconium (Zr)	ug/L	ND	0.10	C305396
Total Calcium (Ca)	mg/L	24.0	0.050	C302864
Total Magnesium (Mg)	mg/L	1.27	0.050	C302864
Total Potassium (K)	mg/L	1.35	0.050	C302864
Total Sodium (Na)	mg/L	7.13	0.050	C302864
Total Sulphur (S)	mg/L	4.8	3.0	C302864
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

MISCELLANEOUS (WATER)

Bureau Veritas ID		EFZ440	EFZ441	EFZ442	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162	131162	131162		
	UNITS	WLNG-DS	WLNG -EOP	WLNG-US	DUP	RDL	QC Batch
Calculated Parameters							
Total Un-ionized Hydrogen Sulfide as S	mg/L	ND	ND	ND	ND	0.0018	C303117
Total Un-ionized Hydrogen Sulfide as H2S	mg/L	ND	ND	ND	ND	0.0019	C303117
RDL = Reportable Detection Limit							
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.							



Bureau Veritas Job #: C631926

Report Date: 2026/06/15

HATFIELD CONSULTANTS

Client Project #: FORTIS11234/PE110163

Site Location: WOODFIBRE PIPELINE PROJECT

Your P.O. #: 4800010213

Sampler Initials: 5.4

LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)

Bureau Veritas ID		EFZ441	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Calculated Parameters					
Low Molecular Weight PAH's	ug/L	ND	ND	0.10	C302457
High Molecular Weight PAH's	ug/L	ND	ND	0.050	C302457
Total PAH	ug/L	ND	ND	0.10	C302457
Polycyclic Aromatics					
Quinoline	ug/L	ND	ND	0.020	C307285
Naphthalene	ug/L	ND	ND	0.10	C307285
1-Methylnaphthalene	ug/L	ND	ND	0.050	C307285
2-Methylnaphthalene	ug/L	ND	ND	0.10	C307285
Acenaphthylene	ug/L	ND	ND	0.050	C307285
Acenaphthene	ug/L	ND	ND	0.050	C307285
Fluorene	ug/L	ND	ND	0.050	C307285
Phenanthrene	ug/L	ND	ND	0.050	C307285
Anthracene	ug/L	ND	ND	0.010	C307285
Acridine	ug/L	ND	ND	0.050	C307285
Fluoranthene	ug/L	ND	ND	0.020	C307285
Pyrene	ug/L	ND	ND	0.020	C307285
Benzo(a)anthracene	ug/L	ND	ND	0.010	C307285
Chrysene	ug/L	ND	ND	0.020	C307285
Benzo(b&j)fluoranthene	ug/L	ND	ND	0.030	C307285
Benzo(k)fluoranthene	ug/L	ND	ND	0.050	C307285
Benzo(a)pyrene	ug/L	ND	ND	0.0050	C307285
Indeno(1,2,3-cd)pyrene	ug/L	ND	ND	0.050	C307285
Dibenz(a,h)anthracene	ug/L	ND	ND	0.0030	C307285
Benzo(g,h,i)perylene	ug/L	ND	ND	0.050	C307285
Calculated Parameters					
LEPH (C10-C19 less PAH)	mg/L	ND	ND	0.20	C302459
HEPH (C19-C32 less PAH)	mg/L	ND	ND	0.20	C302459
Ext. Pet. Hydrocarbon					
EPH (C10-C19)	mg/L	ND	ND	0.20	C307287
RDL = Reportable Detection Limit					
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)

Bureau Veritas ID		EFZ441	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
EPH (C19-C32)	mg/L	ND	ND	0.20	C307287
Surrogate Recovery (%)					
O-TERPHENYL (sur.)	%	111	105		C307287
D10-ANTHRACENE (sur.)	%	112	115		C307285
D8-ACENAPHTHYLENE (sur.)	%	89	91		C307285
D8-NAPHTHALENE (sur.)	%	64	67		C307285
TERPHENYL-D14 (sur.)	%	85	87		C307285
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		EFZ441	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Calculated Parameters					
VPH (VH6 to 10 - BTEX)	ug/L	ND	ND	300	C302458
Volatiles					
VH C6-C10	ug/L	ND	ND	300	C305547
1,1,1,2-tetrachloroethane	ug/L	ND	ND	0.50	C305547
1,1,1-trichloroethane	ug/L	ND	ND	0.50	C305547
1,1,2,2-tetrachloroethane	ug/L	ND	ND	0.50	C305547
1,1,2Trichloro-1,2,2Trifluoroethane	ug/L	ND	ND	2.0	C305547
1,1,2-trichloroethane	ug/L	ND	ND	0.50	C305547
1,1-dichloroethane	ug/L	ND	ND	0.50	C305547
1,1-dichloroethene	ug/L	ND	ND	0.50	C305547
1,2,3-trichlorobenzene	ug/L	ND	ND	2.0	C305547
1,2,4-trichlorobenzene	ug/L	ND	ND	2.0	C305547
1,2-dibromoethane	ug/L	ND	ND	0.20	C305547
1,2-dichlorobenzene	ug/L	ND	ND	0.50	C305547
1,2-dichloroethane	ug/L	ND	ND	0.50	C305547
1,2-dichloropropane	ug/L	ND	ND	0.50	C305547
1,3,5-trimethylbenzene	ug/L	ND	ND	2.0	C305547
1,3-Butadiene	ug/L	ND	ND	0.50	C305547
1,3-dichlorobenzene	ug/L	ND	ND	0.50	C305547
1,3-dichloropropane	ug/L	ND	ND	1.0	C305547
1,4-dichlorobenzene	ug/L	ND	ND	0.50	C305547
Benzene	ug/L	ND	ND	0.40	C305547
Bromobenzene	ug/L	ND	ND	2.0	C305547
Bromodichloromethane	ug/L	ND	ND	1.0	C305547
Bromoform	ug/L	ND	ND	1.0	C305547
Bromomethane	ug/L	ND	ND	1.0	C305547
Carbon tetrachloride	ug/L	ND	ND	0.50	C305547
Chlorobenzene	ug/L	ND	ND	0.50	C305547
Dibromochloromethane	ug/L	ND	ND	1.0	C305547
RDL = Reportable Detection Limit					
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		EFZ441	EFZ445		
Sampling Date		2026/06/02 09:30	2026/06/02 09:30		
COC Number		131162	131162		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Chloroethane	ug/L	ND	ND	1.0	C305547
Chloroform	ug/L	ND	ND	1.0	C305547
Chloromethane	ug/L	ND	ND	1.0	C305547
cis-1,2-dichloroethene	ug/L	ND	ND	1.0	C305547
cis-1,3-dichloropropene	ug/L	ND	ND	1.0	C305547
Dichlorodifluoromethane	ug/L	ND	ND	2.0	C305547
Dichloromethane	ug/L	ND	ND	2.0	C305547
Ethylbenzene	ug/L	ND	ND	0.40	C305547
Hexachlorobutadiene	ug/L	ND	ND	0.50	C305547
Isopropylbenzene	ug/L	ND	ND	2.0	C305547
Methyl-tert-butylether (MTBE)	ug/L	ND	ND	4.0	C305547
Styrene	ug/L	ND	ND	0.50	C305547
Tetrachloroethene	ug/L	ND	ND	0.50	C305547
Toluene	ug/L	ND	ND	0.40	C305547
trans-1,2-dichloroethene	ug/L	ND	ND	1.0	C305547
trans-1,3-dichloropropene	ug/L	ND	ND	1.0	C305547
Trichloroethene	ug/L	ND	ND	0.50	C305547
Trichlorofluoromethane	ug/L	ND	ND	4.0	C305547
Vinyl chloride	ug/L	ND	ND	0.50	C305547
m & p-Xylene	ug/L	ND	ND	0.40	C305547
o-Xylene	ug/L	ND	ND	0.40	C305547
Xylenes (Total)	ug/L	ND	ND	0.40	C305547
Surrogate Recovery (%)					
1,4-Difluorobenzene (sur.)	%	103	103		C305547
4-Bromofluorobenzene (sur.)	%	87	87		C305547
D4-1,2-Dichloroethane (sur.)	%	117	113		C305547
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

GENERAL COMMENTS

Sample EFZ443 [Field Blank] : Total Chromium < Total Hexavalent Chromium. High Hexavalent result is likely due to matrix interference.

Results relate only to the items tested.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C303051	IC4	Matrix Spike	Dissolved Mercury (Hg)	2026/06/03		92	%	80 - 120
C303051	IC4	Spiked Blank	Dissolved Mercury (Hg)	2026/06/03		92	%	80 - 120
C303051	IC4	Method Blank	Dissolved Mercury (Hg)	2026/06/03	ND, RDL=0.0019		ug/L	
C303051	IC4	RPD	Dissolved Mercury (Hg)	2026/06/03	NC		%	20
C303060	IC4	Matrix Spike	Total Mercury (Hg)	2026/06/04		98	%	80 - 120
C303060	IC4	Spiked Blank	Total Mercury (Hg)	2026/06/04		97	%	80 - 120
C303060	IC4	Method Blank	Total Mercury (Hg)	2026/06/04	ND, RDL=0.0019		ug/L	
C303060	IC4	RPD	Total Mercury (Hg)	2026/06/04	NC		%	20
C303210	CJY	Spiked Blank	Dissolved Organic Carbon (C)	2026/06/04		102	%	80 - 120
C303210	CJY	Method Blank	Dissolved Organic Carbon (C)	2026/06/04	ND, RDL=0.50		mg/L	
C303355	SPP	Matrix Spike	Total Suspended Solids	2026/06/04		104	%	80 - 120
C303355	SPP	Spiked Blank	Total Suspended Solids	2026/06/04		102	%	80 - 120
C303355	SPP	Method Blank	Total Suspended Solids	2026/06/04	ND, RDL=1.0		mg/L	
C303355	SPP	RPD [EFZ440-01]	Total Suspended Solids	2026/06/04	0		%	20
C303364	SPP	Matrix Spike [EFZ442-01]	Total Suspended Solids	2026/06/04		107	%	80 - 120
C303364	SPP	Spiked Blank	Total Suspended Solids	2026/06/04		101	%	80 - 120
C303364	SPP	Method Blank	Total Suspended Solids	2026/06/04	ND, RDL=1.0		mg/L	
C303364	SPP	RPD	Total Suspended Solids	2026/06/04	NC		%	20
C303392	RLZ	Matrix Spike [EFZ442-01]	Nitrate plus Nitrite (N)	2026/06/03		102	%	80 - 120
C303392	RLZ	Spiked Blank	Nitrate plus Nitrite (N)	2026/06/03		105	%	80 - 120
C303392	RLZ	Method Blank	Nitrate plus Nitrite (N)	2026/06/03	ND, RDL=0.020		mg/L	
C303392	RLZ	RPD [EFZ442-01]	Nitrate plus Nitrite (N)	2026/06/03	NC		%	20
C303397	RLZ	Matrix Spike [EFZ442-01]	Nitrite (N)	2026/06/03		98	%	80 - 120
C303397	RLZ	Spiked Blank	Nitrite (N)	2026/06/03		104	%	80 - 120
C303397	RLZ	Method Blank	Nitrite (N)	2026/06/03	ND, RDL=0.0050		mg/L	
C303397	RLZ	RPD [EFZ442-01]	Nitrite (N)	2026/06/03	NC		%	20
C303398	SPP	Matrix Spike [EFZ445-03]	Total Dissolved Solids	2026/06/04		106	%	80 - 120
C303398	SPP	Spiked Blank	Total Dissolved Solids	2026/06/04		104	%	80 - 120
C303398	SPP	Method Blank	Total Dissolved Solids	2026/06/04	ND, RDL=10		mg/L	
C303398	SPP	RPD [EFZ444-03]	Total Dissolved Solids	2026/06/04	NC		%	20
C303792	MEM	Matrix Spike [EFZ440-05]	Dissolved Aluminum (Al)	2026/06/04		92	%	80 - 120
			Dissolved Antimony (Sb)	2026/06/04		99	%	80 - 120
			Dissolved Arsenic (As)	2026/06/04		100	%	80 - 120
			Dissolved Barium (Ba)	2026/06/04		96	%	80 - 120
			Dissolved Beryllium (Be)	2026/06/04		86	%	80 - 120
			Dissolved Bismuth (Bi)	2026/06/04		93	%	80 - 120
			Dissolved Boron (B)	2026/06/04		92	%	80 - 120
			Dissolved Cadmium (Cd)	2026/06/04		100	%	80 - 120
			Dissolved Cesium (Cs)	2026/06/04		95	%	80 - 120
			Dissolved Chromium (Cr)	2026/06/04		95	%	80 - 120
			Dissolved Cobalt (Co)	2026/06/04		94	%	80 - 120
			Dissolved Copper (Cu)	2026/06/04		93	%	80 - 120
			Dissolved Iron (Fe)	2026/06/04		98	%	80 - 120
			Dissolved Lead (Pb)	2026/06/04		91	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C303792	MEM	Spiked Blank	Dissolved Lithium (Li)	2026/06/04		75 (1)	%	80 - 120
			Dissolved Manganese (Mn)	2026/06/04		91	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/06/04		NC	%	80 - 120
			Dissolved Nickel (Ni)	2026/06/04		94	%	80 - 120
			Dissolved Phosphorus (P)	2026/06/04		93	%	80 - 120
			Dissolved Rubidium (Rb)	2026/06/04		98	%	80 - 120
			Dissolved Selenium (Se)	2026/06/04		98	%	80 - 120
			Dissolved Silicon (Si)	2026/06/04		NC	%	80 - 120
			Dissolved Silver (Ag)	2026/06/04		97	%	80 - 120
			Dissolved Strontium (Sr)	2026/06/04		99	%	80 - 120
			Dissolved Tellurium (Te)	2026/06/04		98	%	80 - 120
			Dissolved Thallium (Tl)	2026/06/04		97	%	80 - 120
			Dissolved Thorium (Th)	2026/06/04		97	%	80 - 120
			Dissolved Tin (Sn)	2026/06/04		98	%	80 - 120
			Dissolved Titanium (Ti)	2026/06/04		97	%	80 - 120
			Dissolved Uranium (U)	2026/06/04		100	%	80 - 120
			Dissolved Vanadium (V)	2026/06/04		96	%	80 - 120
			Dissolved Zinc (Zn)	2026/06/04		98	%	80 - 120
			Dissolved Zirconium (Zr)	2026/06/04		99	%	80 - 120
			Dissolved Aluminum (Al)	2026/06/04		99	%	80 - 120
			Dissolved Antimony (Sb)	2026/06/04		104	%	80 - 120
			Dissolved Arsenic (As)	2026/06/04		103	%	80 - 120
			Dissolved Barium (Ba)	2026/06/04		101	%	80 - 120
			Dissolved Beryllium (Be)	2026/06/04		92	%	80 - 120
			Dissolved Bismuth (Bi)	2026/06/04		99	%	80 - 120
			Dissolved Boron (B)	2026/06/04		96	%	80 - 120
			Dissolved Cadmium (Cd)	2026/06/04		104	%	80 - 120
			Dissolved Cesium (Cs)	2026/06/04		99	%	80 - 120
			Dissolved Chromium (Cr)	2026/06/04		103	%	80 - 120
			Dissolved Cobalt (Co)	2026/06/04		102	%	80 - 120
			Dissolved Copper (Cu)	2026/06/04		101	%	80 - 120
			Dissolved Iron (Fe)	2026/06/04		107	%	80 - 120
			Dissolved Lead (Pb)	2026/06/04		99	%	80 - 120
			Dissolved Lithium (Li)	2026/06/04		81	%	80 - 120
			Dissolved Manganese (Mn)	2026/06/04		101	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/06/04		104	%	80 - 120
			Dissolved Nickel (Ni)	2026/06/04		101	%	80 - 120
			Dissolved Phosphorus (P)	2026/06/04		95	%	80 - 120
			Dissolved Rubidium (Rb)	2026/06/04		99	%	80 - 120
			Dissolved Selenium (Se)	2026/06/04		103	%	80 - 120
			Dissolved Silicon (Si)	2026/06/04		106	%	80 - 120
			Dissolved Silver (Ag)	2026/06/04		100	%	80 - 120
			Dissolved Strontium (Sr)	2026/06/04		101	%	80 - 120
			Dissolved Tellurium (Te)	2026/06/04		100	%	80 - 120
			Dissolved Thallium (Tl)	2026/06/04		98	%	80 - 120
			Dissolved Thorium (Th)	2026/06/04		102	%	80 - 120
			Dissolved Tin (Sn)	2026/06/04		104	%	80 - 120
			Dissolved Titanium (Ti)	2026/06/04		104	%	80 - 120
			Dissolved Uranium (U)	2026/06/04		101	%	80 - 120
			Dissolved Vanadium (V)	2026/06/04		102	%	80 - 120
			Dissolved Zinc (Zn)	2026/06/04		104	%	80 - 120
			Dissolved Zirconium (Zr)	2026/06/04		101	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C303792	MEM	Method Blank	Dissolved Aluminum (Al)	2026/06/04	ND, RDL=0.50		ug/L	
			Dissolved Antimony (Sb)	2026/06/04	ND, RDL=0.020		ug/L	
			Dissolved Arsenic (As)	2026/06/04	ND, RDL=0.020		ug/L	
			Dissolved Barium (Ba)	2026/06/04	ND, RDL=0.020		ug/L	
			Dissolved Beryllium (Be)	2026/06/04	ND, RDL=0.010		ug/L	
			Dissolved Bismuth (Bi)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Boron (B)	2026/06/04	ND, RDL=10		ug/L	
			Dissolved Cadmium (Cd)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Cesium (Cs)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Chromium (Cr)	2026/06/04	ND, RDL=0.10		ug/L	
			Dissolved Cobalt (Co)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Copper (Cu)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Iron (Fe)	2026/06/04	ND, RDL=1.0		ug/L	
			Dissolved Lead (Pb)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Lithium (Li)	2026/06/04	ND, RDL=0.50		ug/L	
			Dissolved Manganese (Mn)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Molybdenum (Mo)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Nickel (Ni)	2026/06/04	ND, RDL=0.020		ug/L	
			Dissolved Phosphorus (P)	2026/06/04	ND, RDL=2.0		ug/L	
			Dissolved Rubidium (Rb)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Selenium (Se)	2026/06/04	ND, RDL=0.040		ug/L	
			Dissolved Silicon (Si)	2026/06/04	ND, RDL=50		ug/L	
			Dissolved Silver (Ag)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Strontium (Sr)	2026/06/04	ND, RDL=0.050		ug/L	
			Dissolved Tellurium (Te)	2026/06/04	ND, RDL=0.020		ug/L	
			Dissolved Thallium (Tl)	2026/06/04	ND, RDL=0.0020		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C303792	MEM	RPD [EFZ440-05]	Dissolved Thorium (Th)	2026/06/04	ND, RDL=0.0050		ug/L	
			Dissolved Tin (Sn)	2026/06/04	ND, RDL=0.20		ug/L	
			Dissolved Titanium (Ti)	2026/06/04	ND, RDL=0.50		ug/L	
			Dissolved Uranium (U)	2026/06/04	ND, RDL=0.0020		ug/L	
			Dissolved Vanadium (V)	2026/06/04	ND, RDL=0.20		ug/L	
			Dissolved Zinc (Zn)	2026/06/04	ND, RDL=0.10		ug/L	
			Dissolved Zirconium (Zr)	2026/06/04	ND, RDL=0.10		ug/L	
			Dissolved Aluminum (Al)	2026/06/04	0.37		%	20
			Dissolved Antimony (Sb)	2026/06/04	2.1		%	20
			Dissolved Arsenic (As)	2026/06/04	5.8		%	20
			Dissolved Barium (Ba)	2026/06/04	4.3		%	20
			Dissolved Beryllium (Be)	2026/06/04	NC		%	20
			Dissolved Bismuth (Bi)	2026/06/04	NC		%	20
			Dissolved Boron (B)	2026/06/04	NC		%	20
			Dissolved Cadmium (Cd)	2026/06/04	NC		%	20
			Dissolved Cesium (Cs)	2026/06/04	NC		%	20
			Dissolved Chromium (Cr)	2026/06/04	0.58		%	20
			Dissolved Cobalt (Co)	2026/06/04	8.2		%	20
			Dissolved Copper (Cu)	2026/06/04	5.7		%	20
			Dissolved Iron (Fe)	2026/06/04	0.99		%	20
			Dissolved Lead (Pb)	2026/06/04	NC		%	20
			Dissolved Lithium (Li)	2026/06/04	3.0		%	20
			Dissolved Manganese (Mn)	2026/06/04	0.83		%	20
			Dissolved Molybdenum (Mo)	2026/06/04	0.22		%	20
			Dissolved Nickel (Ni)	2026/06/04	13		%	20
			Dissolved Phosphorus (P)	2026/06/04	4.2		%	20
			Dissolved Rubidium (Rb)	2026/06/04	0.0034		%	20
			Dissolved Selenium (Se)	2026/06/04	3.9		%	20
			Dissolved Silicon (Si)	2026/06/04	2.9		%	20
			Dissolved Silver (Ag)	2026/06/04	NC		%	20
			Dissolved Strontium (Sr)	2026/06/04	1.3		%	20
			Dissolved Tellurium (Te)	2026/06/04	NC		%	20
			Dissolved Thallium (Tl)	2026/06/04	12		%	20
			Dissolved Thorium (Th)	2026/06/04	NC		%	20
			Dissolved Tin (Sn)	2026/06/04	NC		%	20
			Dissolved Titanium (Ti)	2026/06/04	NC		%	20
			Dissolved Uranium (U)	2026/06/04	0.65		%	20
			Dissolved Vanadium (V)	2026/06/04	1.6		%	20
			Dissolved Zinc (Zn)	2026/06/04	7.5		%	20
			Dissolved Zirconium (Zr)	2026/06/04	NC		%	20
C303792	MEM	RPD [EFZ443-05]	Dissolved Aluminum (Al)	2026/06/04	NC		%	20
			Dissolved Antimony (Sb)	2026/06/04	NC		%	20
			Dissolved Arsenic (As)	2026/06/04	NC		%	20
			Dissolved Barium (Ba)	2026/06/04	NC		%	20
			Dissolved Beryllium (Be)	2026/06/04	NC		%	20



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Dissolved Bismuth (Bi)	2026/06/04	NC		%	20
			Dissolved Boron (B)	2026/06/04	NC		%	20
			Dissolved Cadmium (Cd)	2026/06/04	NC		%	20
			Dissolved Cesium (Cs)	2026/06/04	NC		%	20
			Dissolved Chromium (Cr)	2026/06/04	NC		%	20
			Dissolved Cobalt (Co)	2026/06/04	NC		%	20
			Dissolved Copper (Cu)	2026/06/04	NC		%	20
			Dissolved Iron (Fe)	2026/06/04	NC		%	20
			Dissolved Lead (Pb)	2026/06/04	NC		%	20
			Dissolved Lithium (Li)	2026/06/04	NC		%	20
			Dissolved Manganese (Mn)	2026/06/04	NC		%	20
			Dissolved Molybdenum (Mo)	2026/06/04	NC		%	20
			Dissolved Nickel (Ni)	2026/06/04	NC		%	20
			Dissolved Phosphorus (P)	2026/06/04	NC		%	20
			Dissolved Rubidium (Rb)	2026/06/04	NC		%	20
			Dissolved Selenium (Se)	2026/06/04	NC		%	20
			Dissolved Silicon (Si)	2026/06/04	NC		%	20
			Dissolved Silver (Ag)	2026/06/04	NC		%	20
			Dissolved Strontium (Sr)	2026/06/04	NC		%	20
			Dissolved Tellurium (Te)	2026/06/04	NC		%	20
			Dissolved Thallium (Tl)	2026/06/04	NC		%	20
			Dissolved Thorium (Th)	2026/06/04	NC		%	20
			Dissolved Tin (Sn)	2026/06/04	NC		%	20
			Dissolved Titanium (Ti)	2026/06/04	NC		%	20
			Dissolved Uranium (U)	2026/06/04	NC		%	20
			Dissolved Vanadium (V)	2026/06/04	NC		%	20
			Dissolved Zinc (Zn)	2026/06/04	NC		%	20
			Dissolved Zirconium (Zr)	2026/06/04	6.2		%	20
C304011	BTM	Spiked Blank	Alkalinity (Total as CaCO ₃)	2026/06/04		102	%	80 - 120
C304011	BTM	Method Blank	Alkalinity (PP as CaCO ₃)	2026/06/04	ND, RDL=1.0		mg/L	
			Alkalinity (Total as CaCO ₃)	2026/06/04	ND, RDL=1.0		mg/L	
			Bicarbonate (HCO ₃)	2026/06/04	ND, RDL=1.0		mg/L	
			Carbonate (CO ₃)	2026/06/04	ND, RDL=1.0		mg/L	
			Hydroxide (OH)	2026/06/04	ND, RDL=1.0		mg/L	
C304011	BTM	RPD	Alkalinity (PP as CaCO ₃)	2026/06/04	NC		%	20
			Alkalinity (Total as CaCO ₃)	2026/06/04	0.68		%	20
			Bicarbonate (HCO ₃)	2026/06/04	0.68		%	20
			Carbonate (CO ₃)	2026/06/04	NC		%	20
			Hydroxide (OH)	2026/06/04	NC		%	20
C304013	BTM	Spiked Blank	pH	2026/06/04		100	%	97 - 103
C304074	CJY	Matrix Spike [EFZ440-09]	Total Organic Carbon (C)	2026/06/04		143 (1)	%	80 - 120
C304074	CJY	Spiked Blank	Total Organic Carbon (C)	2026/06/04		110	%	80 - 120
C304074	CJY	Method Blank	Total Organic Carbon (C)	2026/06/04	ND, RDL=0.50		mg/L	
C304074	CJY	RPD [EFZ440-09]	Total Organic Carbon (C)	2026/06/04	3.2		%	20
C304119	MEM	Matrix Spike	Total Aluminum (Al)	2026/06/04		103	%	80 - 120
			Total Antimony (Sb)	2026/06/04		101	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C304119	MEM	Spiked Blank	Total Arsenic (As)	2026/06/04		104	%	80 - 120
			Total Barium (Ba)	2026/06/04		100	%	80 - 120
			Total Beryllium (Be)	2026/06/04		102	%	80 - 120
			Total Bismuth (Bi)	2026/06/04		97	%	80 - 120
			Total Boron (B)	2026/06/04		117	%	80 - 120
			Total Cadmium (Cd)	2026/06/04		100	%	80 - 120
			Total Cesium (Cs)	2026/06/04		98	%	80 - 120
			Total Chromium (Cr)	2026/06/04		98	%	80 - 120
			Total Cobalt (Co)	2026/06/04		95	%	80 - 120
			Total Copper (Cu)	2026/06/04		92	%	80 - 120
			Total Iron (Fe)	2026/06/04		100	%	80 - 120
			Total Lead (Pb)	2026/06/04		95	%	80 - 120
			Total Lithium (Li)	2026/06/04		96	%	80 - 120
			Total Manganese (Mn)	2026/06/04		96	%	80 - 120
			Total Molybdenum (Mo)	2026/06/04		105	%	80 - 120
			Total Nickel (Ni)	2026/06/04		93	%	80 - 120
			Total Phosphorus (P)	2026/06/04		106	%	80 - 120
			Total Rubidium (Rb)	2026/06/04		101	%	80 - 120
			Total Selenium (Se)	2026/06/04		101	%	80 - 120
			Total Silicon (Si)	2026/06/04		104	%	80 - 120
			Total Silver (Ag)	2026/06/04		97	%	80 - 120
			Total Strontium (Sr)	2026/06/04		103	%	80 - 120
			Total Tellurium (Te)	2026/06/04		103	%	80 - 120
			Total Thallium (Tl)	2026/06/04		97	%	80 - 120
			Total Thorium (Th)	2026/06/04		99	%	80 - 120
			Total Tin (Sn)	2026/06/04		102	%	80 - 120
			Total Titanium (Ti)	2026/06/04		100	%	80 - 120
			Total Uranium (U)	2026/06/04		102	%	80 - 120
			Total Vanadium (V)	2026/06/04		101	%	80 - 120
			Total Zinc (Zn)	2026/06/04		97	%	80 - 120
			Total Zirconium (Zr)	2026/06/04		102	%	80 - 120
			Total Aluminum (Al)	2026/06/04		109	%	80 - 120
			Total Antimony (Sb)	2026/06/04		105	%	80 - 120
			Total Arsenic (As)	2026/06/04		106	%	80 - 120
			Total Barium (Ba)	2026/06/04		104	%	80 - 120
			Total Beryllium (Be)	2026/06/04		109	%	80 - 120
			Total Bismuth (Bi)	2026/06/04		101	%	80 - 120
			Total Boron (B)	2026/06/04		126 (2)	%	80 - 120
			Total Cadmium (Cd)	2026/06/04		105	%	80 - 120
			Total Cesium (Cs)	2026/06/04		104	%	80 - 120
			Total Chromium (Cr)	2026/06/04		103	%	80 - 120
			Total Cobalt (Co)	2026/06/04		102	%	80 - 120
			Total Copper (Cu)	2026/06/04		101	%	80 - 120
			Total Iron (Fe)	2026/06/04		106	%	80 - 120
			Total Lead (Pb)	2026/06/04		100	%	80 - 120
			Total Lithium (Li)	2026/06/04		107	%	80 - 120
			Total Manganese (Mn)	2026/06/04		102	%	80 - 120
			Total Molybdenum (Mo)	2026/06/04		105	%	80 - 120
			Total Nickel (Ni)	2026/06/04		101	%	80 - 120
			Total Phosphorus (P)	2026/06/04		106	%	80 - 120
			Total Rubidium (Rb)	2026/06/04		104	%	80 - 120
			Total Selenium (Se)	2026/06/04		104	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C304119	MEM	Method Blank	Total Silicon (Si)	2026/06/04		108	%	80 - 120
			Total Silver (Ag)	2026/06/04		101	%	80 - 120
			Total Strontium (Sr)	2026/06/04		105	%	80 - 120
			Total Tellurium (Te)	2026/06/04		106	%	80 - 120
			Total Thallium (Tl)	2026/06/04		100	%	80 - 120
			Total Thorium (Th)	2026/06/04		101	%	80 - 120
			Total Tin (Sn)	2026/06/04		106	%	80 - 120
			Total Titanium (Ti)	2026/06/04		106	%	80 - 120
			Total Uranium (U)	2026/06/04		106	%	80 - 120
			Total Vanadium (V)	2026/06/04		104	%	80 - 120
			Total Zinc (Zn)	2026/06/04		105	%	80 - 120
			Total Zirconium (Zr)	2026/06/04		102	%	80 - 120
			Total Aluminum (Al)	2026/06/04	ND, RDL=0.50		ug/L	
			Total Antimony (Sb)	2026/06/04	ND, RDL=0.020		ug/L	
			Total Arsenic (As)	2026/06/04	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/06/04	ND, RDL=0.020		ug/L	
			Total Beryllium (Be)	2026/06/04	ND, RDL=0.010		ug/L	
			Total Bismuth (Bi)	2026/06/04	ND, RDL=0.0050		ug/L	
			Total Boron (B)	2026/06/04	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/06/04	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/06/04	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/06/04	ND, RDL=0.0050		ug/L	
			Total Copper (Cu)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Iron (Fe)	2026/06/04	ND, RDL=1.0		ug/L	
			Total Lead (Pb)	2026/06/04	ND, RDL=0.0050		ug/L	
			Total Lithium (Li)	2026/06/04	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Molybdenum (Mo)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/06/04	ND, RDL=0.020		ug/L	
			Total Phosphorus (P)	2026/06/04	ND, RDL=2.0		ug/L	
			Total Rubidium (Rb)	2026/06/04	ND, RDL=0.050		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Selenium (Se)	2026/06/04	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/06/04	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/06/04	ND, RDL=0.0050		ug/L	
			Total Strontium (Sr)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/06/04	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/06/04	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/06/04	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/06/04	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/06/04	ND, RDL=0.50		ug/L	
			Total Uranium (U)	2026/06/04	ND, RDL=0.0020		ug/L	
			Total Vanadium (V)	2026/06/04	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/06/04	ND, RDL=0.10		ug/L	
			Total Zirconium (Zr)	2026/06/04	ND, RDL=0.10		ug/L	
C304119	MEM	RPD	Total Aluminum (Al)	2026/06/04	NC		%	20
			Total Arsenic (As)	2026/06/04	2.7		%	20
			Total Cadmium (Cd)	2026/06/04	NC		%	20
			Total Cobalt (Co)	2026/06/04	0.61		%	20
			Total Copper (Cu)	2026/06/04	NC		%	20
			Total Lead (Pb)	2026/06/04	NC		%	20
			Total Molybdenum (Mo)	2026/06/04	1.5		%	20
			Total Phosphorus (P)	2026/06/04	NC		%	20
			Total Selenium (Se)	2026/06/04	NC		%	20
			Total Thallium (Tl)	2026/06/04	NC		%	20
			Total Uranium (U)	2026/06/04	0.57		%	20
			Total Vanadium (V)	2026/06/04	NC		%	20
			Total Zinc (Zn)	2026/06/04	12		%	20
C304198	BB3	Matrix Spike [EFZ443-01]	Chloride (Cl)	2026/06/04		110	%	80 - 120
			Sulphate (SO4)	2026/06/04		108	%	80 - 120
C304198	BB3	Spiked Blank	Chloride (Cl)	2026/06/04		97	%	80 - 120
			Sulphate (SO4)	2026/06/04		100	%	80 - 120
C304198	BB3	Method Blank	Chloride (Cl)	2026/06/04	ND, RDL=1.0		mg/L	
			Sulphate (SO4)	2026/06/04	ND, RDL=1.0		mg/L	
C304198	BB3	RPD [EFZ443-01]	Chloride (Cl)	2026/06/04	NC		%	20
			Sulphate (SO4)	2026/06/04	NC		%	20
C304639	JLP	Matrix Spike	Dissolved Fluoride (F)	2026/06/04		99	%	80 - 120
C304639	JLP	Spiked Blank	Dissolved Fluoride (F)	2026/06/04		96	%	80 - 120
C304639	JLP	Method Blank	Dissolved Fluoride (F)	2026/06/04	ND, RDL=0.050		mg/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C304639	JLP	RPD	Fluoride (F)	2026/06/04	3.3		%	20
C304646	JLP	Matrix Spike	Dissolved Fluoride (F)	2026/06/05		83	%	80 - 120
C304646	JLP	Spiked Blank	Dissolved Fluoride (F)	2026/06/05		96	%	80 - 120
C304646	JLP	Method Blank	Dissolved Fluoride (F)	2026/06/05	ND, RDL=0.050		mg/L	
C304646	JLP	RPD	Fluoride (F)	2026/06/05	NC		%	20
C304746	TSO	Matrix Spike [EFZ440-10]	Total Ammonia (N)	2026/06/05		102	%	80 - 120
C304746	TSO	Spiked Blank	Total Ammonia (N)	2026/06/05		106	%	80 - 120
C304746	TSO	Method Blank	Total Ammonia (N)	2026/06/05	ND, RDL=0.015		mg/L	
C304746	TSO	RPD [EFZ440-10]	Total Ammonia (N)	2026/06/05	NC		%	20
C304844	JGL	Matrix Spike	Total Hex. Chromium (Cr 6+)	2026/06/05		110	%	80 - 120
C304844	JGL	Spiked Blank	Total Hex. Chromium (Cr 6+)	2026/06/05		97	%	80 - 120
C304844	JGL	Method Blank	Total Hex. Chromium (Cr 6+)	2026/06/05	ND, RDL=0.00099		mg/L	
C304844	JGL	RPD	Total Hex. Chromium (Cr 6+)	2026/06/05	NC		%	20
C304846	JGL	Matrix Spike	Total Hex. Chromium (Cr 6+)	2026/06/05		109	%	80 - 120
C304846	JGL	Spiked Blank	Total Hex. Chromium (Cr 6+)	2026/06/05		97	%	80 - 120
C304846	JGL	Method Blank	Total Hex. Chromium (Cr 6+)	2026/06/05	ND, RDL=0.00099		mg/L	
C304846	JGL	RPD	Total Hex. Chromium (Cr 6+)	2026/06/05	NC		%	20
C305396	MEM	Matrix Spike	Total Aluminum (Al)	2026/06/06		98	%	80 - 120
			Total Antimony (Sb)	2026/06/06		102	%	80 - 120
			Total Arsenic (As)	2026/06/06		104	%	80 - 120
			Total Barium (Ba)	2026/06/06		NC	%	80 - 120
			Total Beryllium (Be)	2026/06/06		104	%	80 - 120
			Total Bismuth (Bi)	2026/06/06		98	%	80 - 120
			Total Boron (B)	2026/06/06		105	%	80 - 120
			Total Cadmium (Cd)	2026/06/06		102	%	80 - 120
			Total Cesium (Cs)	2026/06/06		92	%	80 - 120
			Total Chromium (Cr)	2026/06/06		97	%	80 - 120
			Total Cobalt (Co)	2026/06/06		91	%	80 - 120
			Total Copper (Cu)	2026/06/06		93	%	80 - 120
			Total Iron (Fe)	2026/06/06		101	%	80 - 120
			Total Lead (Pb)	2026/06/06		98	%	80 - 120
			Total Lithium (Li)	2026/06/06		91	%	80 - 120
			Total Manganese (Mn)	2026/06/06		96	%	80 - 120
			Total Molybdenum (Mo)	2026/06/06		111	%	80 - 120
			Total Nickel (Ni)	2026/06/06		94	%	80 - 120
			Total Phosphorus (P)	2026/06/06		101	%	80 - 120
			Total Rubidium (Rb)	2026/06/06		104	%	80 - 120
			Total Selenium (Se)	2026/06/06		102	%	80 - 120
			Total Silicon (Si)	2026/06/06		99	%	80 - 120
			Total Silver (Ag)	2026/06/06		100	%	80 - 120
			Total Strontium (Sr)	2026/06/06		NC	%	80 - 120
			Total Tellurium (Te)	2026/06/06		105	%	80 - 120
			Total Thallium (Tl)	2026/06/06		102	%	80 - 120
			Total Thorium (Th)	2026/06/06		105	%	80 - 120
			Total Tin (Sn)	2026/06/06		101	%	80 - 120
			Total Titanium (Ti)	2026/06/06		100	%	80 - 120
			Total Uranium (U)	2026/06/06		110	%	80 - 120
			Total Vanadium (V)	2026/06/06		100	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC	Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C305396	MEM	Spiked Blank		Total Zinc (Zn)	2026/06/06		96	%	80 - 120
				Total Zirconium (Zr)	2026/06/06		105	%	80 - 120
				Total Aluminum (Al)	2026/06/06		103	%	80 - 120
				Total Antimony (Sb)	2026/06/06		103	%	80 - 120
				Total Arsenic (As)	2026/06/06		104	%	80 - 120
				Total Barium (Ba)	2026/06/06		102	%	80 - 120
				Total Beryllium (Be)	2026/06/06		100	%	80 - 120
				Total Bismuth (Bi)	2026/06/06		101	%	80 - 120
				Total Boron (B)	2026/06/06		104	%	80 - 120
				Total Cadmium (Cd)	2026/06/06		104	%	80 - 120
				Total Cesium (Cs)	2026/06/06		95	%	80 - 120
				Total Chromium (Cr)	2026/06/06		102	%	80 - 120
				Total Cobalt (Co)	2026/06/06		96	%	80 - 120
				Total Copper (Cu)	2026/06/06		101	%	80 - 120
				Total Iron (Fe)	2026/06/06		106	%	80 - 120
				Total Lead (Pb)	2026/06/06		100	%	80 - 120
				Total Lithium (Li)	2026/06/06		94	%	80 - 120
				Total Manganese (Mn)	2026/06/06		102	%	80 - 120
				Total Molybdenum (Mo)	2026/06/06		107	%	80 - 120
				Total Nickel (Ni)	2026/06/06		100	%	80 - 120
				Total Phosphorus (P)	2026/06/06		102	%	80 - 120
				Total Rubidium (Rb)	2026/06/06		102	%	80 - 120
				Total Selenium (Se)	2026/06/06		104	%	80 - 120
				Total Silicon (Si)	2026/06/06		107	%	80 - 120
				Total Silver (Ag)	2026/06/06		100	%	80 - 120
				Total Strontium (Sr)	2026/06/06		103	%	80 - 120
				Total Tellurium (Te)	2026/06/06		108	%	80 - 120
				Total Thallium (Tl)	2026/06/06		102	%	80 - 120
				Total Thorium (Th)	2026/06/06		106	%	80 - 120
				Total Tin (Sn)	2026/06/06		102	%	80 - 120
				Total Titanium (Ti)	2026/06/06		104	%	80 - 120
				Total Uranium (U)	2026/06/06		111	%	80 - 120
				Total Vanadium (V)	2026/06/06		102	%	80 - 120
				Total Zinc (Zn)	2026/06/06		103	%	80 - 120
				Total Zirconium (Zr)	2026/06/06		102	%	80 - 120
C305396	MEM	Method Blank		Total Aluminum (Al)	2026/06/06	ND, RDL=0.50		ug/L	
				Total Antimony (Sb)	2026/06/06	ND, RDL=0.020		ug/L	
				Total Arsenic (As)	2026/06/06	ND, RDL=0.020		ug/L	
				Total Barium (Ba)	2026/06/06	ND, RDL=0.020		ug/L	
				Total Beryllium (Be)	2026/06/06	0.016, RDL=0.010 (3)		ug/L	
				Total Bismuth (Bi)	2026/06/06	ND, RDL=0.0050		ug/L	
				Total Boron (B)	2026/06/06	ND, RDL=10		ug/L	
				Total Cadmium (Cd)	2026/06/06	ND, RDL=0.0050		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Cesium (Cs)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/06/06	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/06/06	ND, RDL=0.0050		ug/L	
			Total Copper (Cu)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Iron (Fe)	2026/06/06	ND, RDL=1.0		ug/L	
			Total Lead (Pb)	2026/06/06	ND, RDL=0.0050		ug/L	
			Total Lithium (Li)	2026/06/06	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Molybdenum (Mo)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/06/06	ND, RDL=0.020		ug/L	
			Total Phosphorus (P)	2026/06/06	ND, RDL=2.0		ug/L	
			Total Rubidium (Rb)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/06/06	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/06/06	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/06/06	ND, RDL=0.0050		ug/L	
			Total Strontium (Sr)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/06/06	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/06/06	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/06/06	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/06/06	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/06/06	ND, RDL=0.50		ug/L	
			Total Uranium (U)	2026/06/06	0.0029, RDL=0.0020 (3)		ug/L	
			Total Vanadium (V)	2026/06/06	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/06/06	ND, RDL=0.10		ug/L	
			Total Zirconium (Zr)	2026/06/06	ND, RDL=0.10		ug/L	
C305396	MEM	RPD	Total Aluminum (Al)	2026/06/06	4.8		%	20
			Total Antimony (Sb)	2026/06/06	4.8		%	20
			Total Arsenic (As)	2026/06/06	4.1		%	20



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Barium (Ba)	2026/06/06	0.55		%	20
			Total Beryllium (Be)	2026/06/06	NC		%	20
			Total Bismuth (Bi)	2026/06/06	NC		%	20
			Total Boron (B)	2026/06/06	NC		%	20
			Total Cadmium (Cd)	2026/06/06	NC		%	20
			Total Chromium (Cr)	2026/06/06	NC		%	20
			Total Cobalt (Co)	2026/06/06	NC		%	20
			Total Copper (Cu)	2026/06/06	0.66		%	20
			Total Iron (Fe)	2026/06/06	1.5		%	20
			Total Lead (Pb)	2026/06/06	1.7		%	20
			Total Lithium (Li)	2026/06/06	0.38		%	20
			Total Manganese (Mn)	2026/06/06	4.2		%	20
			Total Molybdenum (Mo)	2026/06/06	3.2		%	20
			Total Nickel (Ni)	2026/06/06	9.4		%	20
			Total Selenium (Se)	2026/06/06	0.66		%	20
			Total Silicon (Si)	2026/06/06	3.4		%	20
			Total Silver (Ag)	2026/06/06	NC		%	20
			Total Strontium (Sr)	2026/06/06	2.2		%	20
			Total Thallium (Tl)	2026/06/06	NC		%	20
			Total Tin (Sn)	2026/06/06	NC		%	20
			Total Titanium (Ti)	2026/06/06	NC		%	20
			Total Uranium (U)	2026/06/06	1.8		%	20
			Total Vanadium (V)	2026/06/06	NC		%	20
			Total Zinc (Zn)	2026/06/06	1.7		%	20
			Total Zirconium (Zr)	2026/06/06	NC		%	20
C305451	STB	Matrix Spike	Phenols	2026/06/05		101	%	80 - 120
C305451	STB	Spiked Blank	Phenols	2026/06/05		103	%	80 - 120
C305451	STB	Method Blank	Phenols	2026/06/05	ND, RDL=0.0015		mg/L	
C305451	STB	RPD	Phenols	2026/06/05	1.3 (4)		%	20
C305521	TSO	Matrix Spike [EFZ440-09]	Total Nitrogen (N)	2026/06/08		100	%	80 - 120
C305521	TSO	Spiked Blank	Total Nitrogen (N)	2026/06/08		100	%	80 - 120
C305521	TSO	Method Blank	Total Nitrogen (N)	2026/06/08	ND, RDL=0.020		mg/L	
C305521	TSO	RPD [EFZ440-09]	Total Nitrogen (N)	2026/06/08	0.76		%	20
C305547	DWL	Matrix Spike	1,4-Difluorobenzene (sur.)	2026/06/06		99	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/06/06		107	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/06/06		106	%	50 - 140
			1,1,1,2-tetrachloroethane	2026/06/06		101	%	50 - 140
			1,1,1-trichloroethane	2026/06/06		109	%	50 - 140
			1,1,2,2-tetrachloroethane	2026/06/06		97	%	50 - 140
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/06/06		106	%	50 - 140
			1,1,2-trichloroethane	2026/06/06		105	%	50 - 140
			1,1-dichloroethane	2026/06/06		115	%	50 - 140
			1,1-dichloroethene	2026/06/06		128	%	50 - 140
			1,2,3-trichlorobenzene	2026/06/06		102	%	50 - 140
			1,2,4-trichlorobenzene	2026/06/06		101	%	50 - 140
			1,2-dibromoethane	2026/06/06		94	%	50 - 140
			1,2-dichlorobenzene	2026/06/06		106	%	50 - 140
			1,2-dichloroethane	2026/06/06		100	%	50 - 140
			1,2-dichloropropane	2026/06/06		109	%	50 - 140
			1,3,5-trimethylbenzene	2026/06/06		118	%	50 - 140



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C305547	DWL	Spiked Blank	1,3-Butadiene	2026/06/06		145 (1)	%	50 - 140
			1,3-dichlorobenzene	2026/06/06		108	%	50 - 140
			1,3-dichloropropane	2026/06/06		103	%	50 - 140
			1,4-dichlorobenzene	2026/06/06		98	%	50 - 140
			Benzene	2026/06/06		109	%	50 - 140
			Bromobenzene	2026/06/06		105	%	50 - 140
			Bromodichloromethane	2026/06/06		102	%	50 - 140
			Bromoform	2026/06/06		99	%	50 - 140
			Bromomethane	2026/06/06		84	%	50 - 140
			Carbon tetrachloride	2026/06/06		108	%	50 - 140
			Chlorobenzene	2026/06/06		101	%	50 - 140
			Dibromochloromethane	2026/06/06		99	%	50 - 140
			Chloroethane	2026/06/06		86	%	50 - 140
			Chloroform	2026/06/06		103	%	50 - 140
			Chloromethane	2026/06/06		101	%	50 - 140
			cis-1,2-dichloroethene	2026/06/06		105	%	50 - 140
			cis-1,3-dichloropropene	2026/06/06		75	%	50 - 140
			Dichlorodifluoromethane	2026/06/06		83	%	50 - 140
			Dichloromethane	2026/06/06		101	%	50 - 140
			Ethylbenzene	2026/06/06		95	%	50 - 140
			Hexachlorobutadiene	2026/06/06		102	%	50 - 140
			Isopropylbenzene	2026/06/06		105	%	50 - 140
			Methyl-tert-butylether (MTBE)	2026/06/06		92	%	50 - 140
			Styrene	2026/06/06		91	%	50 - 140
			Tetrachloroethene	2026/06/06		105	%	50 - 140
			Toluene	2026/06/06		93	%	50 - 140
			trans-1,2-dichloroethene	2026/06/06		111	%	50 - 140
			trans-1,3-dichloropropene	2026/06/06		82	%	50 - 140
			Trichloroethene	2026/06/06		102	%	50 - 140
			Trichlorofluoromethane	2026/06/06		104	%	50 - 140
			Vinyl chloride	2026/06/06		106	%	50 - 140
			m & p-Xylene	2026/06/06		91	%	50 - 140
			o-Xylene	2026/06/06		93	%	50 - 140
			1,4-Difluorobenzene (sur.)	2026/06/06		98	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/06/06		84	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/06/06		104	%	50 - 140
			VH C6-C10	2026/06/06		114	%	70 - 130
			1,1,1,2-tetrachloroethane	2026/06/06		97	%	60 - 130
			1,1,1-trichloroethane	2026/06/06		107	%	60 - 130
			1,1,2,2-tetrachloroethane	2026/06/06		95	%	60 - 130
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/06/06		102	%	60 - 130
			1,1,2-trichloroethane	2026/06/06		103	%	60 - 130
			1,1-dichloroethane	2026/06/06		113	%	60 - 130
			1,1-dichloroethene	2026/06/06		124	%	60 - 130
			1,2,3-trichlorobenzene	2026/06/06		99	%	60 - 130
			1,2,4-trichlorobenzene	2026/06/06		100	%	60 - 130
			1,2-dibromoethane	2026/06/06		93	%	60 - 130
			1,2-dichlorobenzene	2026/06/06		104	%	60 - 130
			1,2-dichloroethane	2026/06/06		101	%	60 - 130
			1,2-dichloropropane	2026/06/06		106	%	60 - 130
			1,3,5-trimethylbenzene	2026/06/06		114	%	60 - 130
			1,3-Butadiene	2026/06/06		144 (5)	%	50 - 140



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC	Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
				1,3-dichlorobenzene	2026/06/06		105	%	60 - 130
				1,3-dichloropropane	2026/06/06		102	%	60 - 130
				1,4-dichlorobenzene	2026/06/06		96	%	60 - 130
				Benzene	2026/06/06		105	%	60 - 130
				Bromobenzene	2026/06/06		102	%	60 - 130
				Bromodichloromethane	2026/06/06		100	%	60 - 130
				Bromoform	2026/06/06		97	%	60 - 130
				Bromomethane	2026/06/06		94	%	50 - 140
				Carbon tetrachloride	2026/06/06		105	%	60 - 130
				Chlorobenzene	2026/06/06		99	%	60 - 130
				Dibromochloromethane	2026/06/06		97	%	60 - 130
				Chloroethane	2026/06/06		89	%	50 - 140
				Chloroform	2026/06/06		101	%	60 - 130
				Chloromethane	2026/06/06		99	%	50 - 140
				cis-1,2-dichloroethene	2026/06/06		103	%	60 - 130
				cis-1,3-dichloropropene	2026/06/06		75	%	50 - 140
				Dichlorodifluoromethane	2026/06/06		82	%	50 - 140
				Dichloromethane	2026/06/06		99	%	60 - 130
				Ethylbenzene	2026/06/06		93	%	60 - 130
				Hexachlorobutadiene	2026/06/06		98	%	60 - 130
				Isopropylbenzene	2026/06/06		103	%	60 - 130
				Methyl-tert-butylether (MTBE)	2026/06/06		92	%	60 - 130
				Styrene	2026/06/06		90	%	60 - 130
				Tetrachloroethene	2026/06/06		101	%	60 - 130
				Toluene	2026/06/06		92	%	60 - 130
				trans-1,2-dichloroethene	2026/06/06		109	%	60 - 130
				trans-1,3-dichloropropene	2026/06/06		83	%	50 - 140
				Trichloroethene	2026/06/06		99	%	60 - 130
				Trichlorofluoromethane	2026/06/06		100	%	60 - 130
				Vinyl chloride	2026/06/06		105	%	50 - 140
				m & p-Xylene	2026/06/06		90	%	60 - 130
				o-Xylene	2026/06/06		91	%	60 - 130
C305547	DWL	Method Blank		1,4-Difluorobenzene (sur.)	2026/06/06		103	%	50 - 140
				4-Bromofluorobenzene (sur.)	2026/06/06		85	%	50 - 140
				D4-1,2-Dichloroethane (sur.)	2026/06/06		114	%	50 - 140
				VH C6-C10	2026/06/06	ND, RDL=300		ug/L	
				1,1,1,2-tetrachloroethane	2026/06/06	ND, RDL=0.50		ug/L	
				1,1,1-trichloroethane	2026/06/06	ND, RDL=0.50		ug/L	
				1,1,2,2-tetrachloroethane	2026/06/06	ND, RDL=0.50		ug/L	
				1,1,2Trichloro-1,2,2Trifluoroethane	2026/06/06	ND, RDL=2.0		ug/L	
				1,1,2-trichloroethane	2026/06/06	ND, RDL=0.50		ug/L	
				1,1-dichloroethane	2026/06/06	ND, RDL=0.50		ug/L	
				1,1-dichloroethene	2026/06/06	ND, RDL=0.50		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			1,2,3-trichlorobenzene	2026/06/06	ND, RDL=2.0		ug/L	
			1,2,4-trichlorobenzene	2026/06/06	ND, RDL=2.0		ug/L	
			1,2-dibromoethane	2026/06/06	ND, RDL=0.20		ug/L	
			1,2-dichlorobenzene	2026/06/06	ND, RDL=0.50		ug/L	
			1,2-dichloroethane	2026/06/06	ND, RDL=0.50		ug/L	
			1,2-dichloropropane	2026/06/06	ND, RDL=0.50		ug/L	
			1,3,5-trimethylbenzene	2026/06/06	ND, RDL=2.0		ug/L	
			1,3-Butadiene	2026/06/06	ND, RDL=0.50		ug/L	
			1,3-dichlorobenzene	2026/06/06	ND, RDL=0.50		ug/L	
			1,3-dichloropropane	2026/06/06	ND, RDL=1.0		ug/L	
			1,4-dichlorobenzene	2026/06/06	ND, RDL=0.50		ug/L	
			Benzene	2026/06/06	ND, RDL=0.40		ug/L	
			Bromobenzene	2026/06/06	ND, RDL=2.0		ug/L	
			Bromodichloromethane	2026/06/06	ND, RDL=1.0		ug/L	
			Bromoform	2026/06/06	ND, RDL=1.0		ug/L	
			Bromomethane	2026/06/06	ND, RDL=1.0		ug/L	
			Carbon tetrachloride	2026/06/06	ND, RDL=0.50		ug/L	
			Chlorobenzene	2026/06/06	ND, RDL=0.50		ug/L	
			Dibromochloromethane	2026/06/06	ND, RDL=1.0		ug/L	
			Chloroethane	2026/06/06	ND, RDL=1.0		ug/L	
			Chloroform	2026/06/06	ND, RDL=1.0		ug/L	
			Chloromethane	2026/06/06	ND, RDL=1.0		ug/L	
			cis-1,2-dichloroethene	2026/06/06	ND, RDL=1.0		ug/L	
			cis-1,3-dichloropropene	2026/06/06	ND, RDL=1.0		ug/L	
			Dichlorodifluoromethane	2026/06/06	ND, RDL=2.0		ug/L	
			Dichloromethane	2026/06/06	ND, RDL=2.0		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Ethylbenzene	2026/06/06	ND, RDL=0.40		ug/L	
			Hexachlorobutadiene	2026/06/06	ND, RDL=0.50		ug/L	
			Isopropylbenzene	2026/06/06	ND, RDL=2.0		ug/L	
			Methyl-tert-butylether (MTBE)	2026/06/06	ND, RDL=4.0		ug/L	
			Styrene	2026/06/06	ND, RDL=0.50		ug/L	
			Tetrachloroethene	2026/06/06	ND, RDL=0.50		ug/L	
			Toluene	2026/06/06	ND, RDL=0.40		ug/L	
			trans-1,2-dichloroethene	2026/06/06	ND, RDL=1.0		ug/L	
			trans-1,3-dichloropropene	2026/06/06	ND, RDL=1.0		ug/L	
			Trichloroethene	2026/06/06	ND, RDL=0.50		ug/L	
			Trichlorofluoromethane	2026/06/06	ND, RDL=4.0		ug/L	
			Vinyl chloride	2026/06/06	ND, RDL=0.50		ug/L	
			m & p-Xylene	2026/06/06	ND, RDL=0.40		ug/L	
			o-Xylene	2026/06/06	ND, RDL=0.40		ug/L	
			Xylenes (Total)	2026/06/06	ND, RDL=0.40		ug/L	
C305547	DWL	RPD	VH C6-C10	2026/06/06	NC		%	30
			1,2-dibromoethane	2026/06/06	NC		%	30
			1,2-dichloroethane	2026/06/06	NC		%	30
			1,3,5-trimethylbenzene	2026/06/06	NC		%	30
			1,3-Butadiene	2026/06/06	NC		%	30
			Benzene	2026/06/06	NC		%	30
			Ethylbenzene	2026/06/06	NC		%	30
			Isopropylbenzene	2026/06/06	NC		%	30
			Methyl-tert-butylether (MTBE)	2026/06/06	NC		%	30
			Styrene	2026/06/06	NC		%	30
			Toluene	2026/06/06	NC		%	30
			m & p-Xylene	2026/06/06	NC		%	30
			o-Xylene	2026/06/06	NC		%	30
			Xylenes (Total)	2026/06/06	NC		%	30
C307079	KA5	Matrix Spike [EFZ440-09]	Total Phosphorus (P)	2026/06/09		111	%	N/A
C307079	KA5	Spiked Blank	Total Phosphorus (P)	2026/06/09		113	%	80 - 120
C307079	KA5	Method Blank	Total Phosphorus (P)	2026/06/09	ND, RDL=0.0010		mg/L	
C307079	KA5	RPD [EFZ440-09]	Total Phosphorus (P)	2026/06/09	NC		%	20
C307285	JP1	Spiked Blank	D10-ANTHRACENE (sur.)	2026/06/08		108	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/06/08		92	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/06/08		68	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/06/08		86	%	50 - 140



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C307285	JP1	Method Blank	Quinoline	2026/06/08		100	%	50 - 140
			Naphthalene	2026/06/08		65	%	50 - 140
			1-Methylnaphthalene	2026/06/08		68	%	50 - 140
			2-Methylnaphthalene	2026/06/08		67	%	50 - 140
			Acenaphthylene	2026/06/08		83	%	50 - 140
			Acenaphthene	2026/06/08		82	%	50 - 140
			Fluorene	2026/06/08		88	%	50 - 140
			Phenanthrene	2026/06/08		87	%	50 - 140
			Anthracene	2026/06/08		91	%	50 - 140
			Acridine	2026/06/08		72	%	50 - 140
			Fluoranthene	2026/06/08		78	%	50 - 140
			Pyrene	2026/06/08		83	%	50 - 140
			Benzo(a)anthracene	2026/06/08		88	%	50 - 140
			Chrysene	2026/06/08		89	%	50 - 140
			Benzo(b&j)fluoranthene	2026/06/08		91	%	50 - 140
			Benzo(k)fluoranthene	2026/06/08		95	%	50 - 140
			Benzo(a)pyrene	2026/06/08		94	%	50 - 140
			Indeno(1,2,3-cd)pyrene	2026/06/08		94	%	50 - 140
			Dibenz(a,h)anthracene	2026/06/08		93	%	50 - 140
			Benzo(g,h,i)perylene	2026/06/08		93	%	50 - 140
			D10-ANTHRACENE (sur.)	2026/06/08		115	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/06/08		91	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/06/08		62	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/06/08		89	%	50 - 140
			Quinoline	2026/06/08	ND, RDL=0.020		ug/L	
			Naphthalene	2026/06/08	ND, RDL=0.10		ug/L	
			1-Methylnaphthalene	2026/06/08	ND, RDL=0.050		ug/L	
			2-Methylnaphthalene	2026/06/08	ND, RDL=0.10		ug/L	
			Acenaphthylene	2026/06/08	ND, RDL=0.050		ug/L	
			Acenaphthene	2026/06/08	ND, RDL=0.050		ug/L	
			Fluorene	2026/06/08	ND, RDL=0.050		ug/L	
			Phenanthrene	2026/06/08	ND, RDL=0.050		ug/L	
			Anthracene	2026/06/08	ND, RDL=0.010		ug/L	
			Acridine	2026/06/08	ND, RDL=0.050		ug/L	
			Fluoranthene	2026/06/08	ND, RDL=0.020		ug/L	
			Pyrene	2026/06/08	ND, RDL=0.020		ug/L	
			Benzo(a)anthracene	2026/06/08	ND, RDL=0.010		ug/L	
			Chrysene	2026/06/08	ND, RDL=0.020		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Benzo(b&j)fluoranthene	2026/06/08	ND, RDL=0.030		ug/L	
			Benzo(k)fluoranthene	2026/06/08	ND, RDL=0.050		ug/L	
			Benzo(a)pyrene	2026/06/08	ND, RDL=0.0050		ug/L	
			Indeno(1,2,3-cd)pyrene	2026/06/08	ND, RDL=0.050		ug/L	
			Dibenz(a,h)anthracene	2026/06/08	ND, RDL=0.0030		ug/L	
			Benzo(g,h,i)perylene	2026/06/08	ND, RDL=0.050		ug/L	
C307287	IT1	Spiked Blank	O-TERPHENYL (sur.)	2026/06/08		109	%	60 - 140
			EPH (C10-C19)	2026/06/08		101	%	70 - 130
			EPH (C19-C32)	2026/06/08		104	%	70 - 130
C307287	IT1	Method Blank	O-TERPHENYL (sur.)	2026/06/08		101	%	60 - 140
			EPH (C10-C19)	2026/06/08	ND, RDL=0.20		mg/L	
			EPH (C19-C32)	2026/06/08	ND, RDL=0.20		mg/L	
C307509	AAX	Matrix Spike	Methyl Sulfone (sur.)	2026/06/09		100	%	50 - 140
			Ethylene Glycol	2026/06/09		95	%	60 - 140
			Diethylene Glycol	2026/06/09		114	%	60 - 140
			Triethylene Glycol	2026/06/09		104	%	60 - 140
			Propylene Glycol	2026/06/09		98	%	60 - 140
C307509	AAX	Spiked Blank	Methyl Sulfone (sur.)	2026/06/09		100	%	50 - 140
			Ethylene Glycol	2026/06/09		88	%	70 - 130
			Diethylene Glycol	2026/06/09		105	%	70 - 130
			Triethylene Glycol	2026/06/09		96	%	70 - 130
			Propylene Glycol	2026/06/09		90	%	70 - 130
C307509	AAX	Method Blank	Methyl Sulfone (sur.)	2026/06/09		97	%	50 - 140
			Ethylene Glycol	2026/06/09	ND, RDL=3.0		mg/L	
			Diethylene Glycol	2026/06/09	ND, RDL=5.0		mg/L	
			Triethylene Glycol	2026/06/09	ND, RDL=5.0		mg/L	
			Propylene Glycol	2026/06/09	ND, RDL=5.0		mg/L	
C307509	AAX	RPD	Ethylene Glycol	2026/06/09	NC		%	30
			Diethylene Glycol	2026/06/09	NC		%	30
			Triethylene Glycol	2026/06/09	NC		%	30
			Propylene Glycol	2026/06/09	NC		%	30
C307634	MWU	Matrix Spike	Bromide (Br)	2026/06/09		97	%	78 - 120
C307634	MWU	Spiked Blank	Bromide (Br)	2026/06/09		106	%	80 - 120
C307634	MWU	Method Blank	Bromide (Br)	2026/06/09	ND, RDL=0.010		mg/L	
C307634	MWU	RPD	Bromide (Br)	2026/06/09	NC		%	20
C307725	NJD	Matrix Spike [EFZ441-11]	Total Sulphide	2026/06/09		112	%	80 - 120
C307725	NJD	Spiked Blank	Total Sulphide	2026/06/09		84	%	80 - 120
C307725	NJD	Method Blank	Total Sulphide	2026/06/09	ND, RDL=0.0018		mg/L	
C307725	NJD	RPD [EFZ440-11]	Total Sulphide	2026/06/09	NC		%	20



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC		QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
Batch	Init							
C308119	MEM	Matrix Spike	Total Aluminum (Al)	2026/06/09		88	%	80 - 120
			Total Antimony (Sb)	2026/06/09		101	%	80 - 120
			Total Arsenic (As)	2026/06/09		100	%	80 - 120
			Total Barium (Ba)	2026/06/09		96	%	80 - 120
			Total Beryllium (Be)	2026/06/09		86	%	80 - 120
			Total Bismuth (Bi)	2026/06/09		94	%	80 - 120
			Total Boron (B)	2026/06/09		92	%	80 - 120
			Total Cadmium (Cd)	2026/06/09		100	%	80 - 120
			Total Cesium (Cs)	2026/06/09		90	%	80 - 120
			Total Chromium (Cr)	2026/06/09		97	%	80 - 120
			Total Cobalt (Co)	2026/06/09		92	%	80 - 120
			Total Copper (Cu)	2026/06/09		91	%	80 - 120
			Total Iron (Fe)	2026/06/09		98	%	80 - 120
			Total Lead (Pb)	2026/06/09		97	%	80 - 120
			Total Lithium (Li)	2026/06/09		82	%	80 - 120
			Total Manganese (Mn)	2026/06/09		96	%	80 - 120
			Total Molybdenum (Mo)	2026/06/09		105	%	80 - 120
			Total Nickel (Ni)	2026/06/09		96	%	80 - 120
			Total Phosphorus (P)	2026/06/09		92	%	80 - 120
			Total Rubidium (Rb)	2026/06/09		99	%	80 - 120
			Total Selenium (Se)	2026/06/09		105	%	80 - 120
			Total Silicon (Si)	2026/06/09		92	%	80 - 120
			Total Silver (Ag)	2026/06/09		97	%	80 - 120
			Total Strontium (Sr)	2026/06/09		NC	%	80 - 120
			Total Tellurium (Te)	2026/06/09		99	%	80 - 120
			Total Thallium (Tl)	2026/06/09		100	%	80 - 120
			Total Thorium (Th)	2026/06/09		108	%	80 - 120
			Total Tin (Sn)	2026/06/09		102	%	80 - 120
			Total Titanium (Ti)	2026/06/09		100	%	80 - 120
			Total Uranium (U)	2026/06/09		107	%	80 - 120
			Total Vanadium (V)	2026/06/09		99	%	80 - 120
			Total Zinc (Zn)	2026/06/09		99	%	80 - 120
			Total Zirconium (Zr)	2026/06/09		101	%	80 - 120
C308119	MEM	Spiked Blank	Total Aluminum (Al)	2026/06/09		91	%	80 - 120
			Total Antimony (Sb)	2026/06/09		103	%	80 - 120
			Total Arsenic (As)	2026/06/09		102	%	80 - 120
			Total Barium (Ba)	2026/06/09		99	%	80 - 120
			Total Beryllium (Be)	2026/06/09		87	%	80 - 120
			Total Bismuth (Bi)	2026/06/09		99	%	80 - 120
			Total Boron (B)	2026/06/09		94	%	80 - 120
			Total Cadmium (Cd)	2026/06/09		103	%	80 - 120
			Total Cesium (Cs)	2026/06/09		91	%	80 - 120
			Total Chromium (Cr)	2026/06/09		104	%	80 - 120
			Total Cobalt (Co)	2026/06/09		98	%	80 - 120
			Total Copper (Cu)	2026/06/09		102	%	80 - 120
			Total Iron (Fe)	2026/06/09		99	%	80 - 120
			Total Lead (Pb)	2026/06/09		101	%	80 - 120
			Total Lithium (Li)	2026/06/09		83	%	80 - 120
			Total Manganese (Mn)	2026/06/09		103	%	80 - 120
			Total Molybdenum (Mo)	2026/06/09		104	%	80 - 120
			Total Nickel (Ni)	2026/06/09		102	%	80 - 120
			Total Phosphorus (P)	2026/06/09		95	%	80 - 120



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C308119	MEM	Method Blank	Total Rubidium (Rb)	2026/06/09		100	%	80 - 120
			Total Selenium (Se)	2026/06/09		108	%	80 - 120
			Total Silicon (Si)	2026/06/09		98	%	80 - 120
			Total Silver (Ag)	2026/06/09		100	%	80 - 120
			Total Strontium (Sr)	2026/06/09		99	%	80 - 120
			Total Tellurium (Te)	2026/06/09		99	%	80 - 120
			Total Thallium (Tl)	2026/06/09		101	%	80 - 120
			Total Thorium (Th)	2026/06/09		112	%	80 - 120
			Total Tin (Sn)	2026/06/09		105	%	80 - 120
			Total Titanium (Ti)	2026/06/09		106	%	80 - 120
			Total Uranium (U)	2026/06/09		115	%	80 - 120
			Total Vanadium (V)	2026/06/09		105	%	80 - 120
			Total Zinc (Zn)	2026/06/09		106	%	80 - 120
			Total Zirconium (Zr)	2026/06/09		110	%	80 - 120
			Total Aluminum (Al)	2026/06/09	ND, RDL=3.0		ug/L	
			Total Antimony (Sb)	2026/06/09	0.024, RDL=0.020 (3)		ug/L	
			Total Arsenic (As)	2026/06/09	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Beryllium (Be)	2026/06/09	ND, RDL=0.010		ug/L	
			Total Bismuth (Bi)	2026/06/09	ND, RDL=0.010		ug/L	
			Total Boron (B)	2026/06/09	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/06/09	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/06/09	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/06/09	ND, RDL=0.010		ug/L	
			Total Copper (Cu)	2026/06/09	ND, RDL=0.10		ug/L	
			Total Iron (Fe)	2026/06/09	ND, RDL=5.0		ug/L	
			Total Lead (Pb)	2026/06/09	ND, RDL=0.020		ug/L	
			Total Lithium (Li)	2026/06/09	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/06/09	ND, RDL=0.10		ug/L	
			Total Molybdenum (Mo)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/06/09	ND, RDL=0.10		ug/L	
			Total Phosphorus (P)	2026/06/09	ND, RDL=5.0		ug/L	



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C308119	MEM	RPD	Total Rubidium (Rb)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/06/09	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/06/09	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/06/09	ND, RDL=0.010		ug/L	
			Total Strontium (Sr)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/06/09	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/06/09	0.0036, RDL=0.0020 (3)		ug/L	
			Total Thorium (Th)	2026/06/09	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/06/09	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/06/09	ND, RDL=2.0		ug/L	
			Total Uranium (U)	2026/06/09	ND, RDL=0.0050		ug/L	
			Total Vanadium (V)	2026/06/09	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/06/09	ND, RDL=1.0		ug/L	
			Total Zirconium (Zr)	2026/06/09	ND, RDL=0.10		ug/L	
			Total Aluminum (Al)	2026/06/09	0.95		%	20
			Total Antimony (Sb)	2026/06/09	4.2		%	20
			Total Arsenic (As)	2026/06/09	8.6		%	20
			Total Barium (Ba)	2026/06/09	0.59		%	20
			Total Beryllium (Be)	2026/06/09	NC		%	20
			Total Bismuth (Bi)	2026/06/09	NC		%	20
			Total Boron (B)	2026/06/09	NC		%	20
			Total Cadmium (Cd)	2026/06/09	17		%	20
			Total Chromium (Cr)	2026/06/09	NC		%	20
			Total Cobalt (Co)	2026/06/09	NC		%	20
			Total Copper (Cu)	2026/06/09	7.9		%	20
			Total Iron (Fe)	2026/06/09	2.2		%	20
			Total Lead (Pb)	2026/06/09	NC		%	20
			Total Lithium (Li)	2026/06/09	3.4		%	20
			Total Manganese (Mn)	2026/06/09	3.1		%	20
			Total Molybdenum (Mo)	2026/06/09	1.7		%	20
			Total Nickel (Ni)	2026/06/09	16		%	20
			Total Phosphorus (P)	2026/06/09	8.1		%	20
			Total Selenium (Se)	2026/06/09	0.059		%	20
			Total Silicon (Si)	2026/06/09	2.4		%	20
			Total Silver (Ag)	2026/06/09	NC		%	20
			Total Strontium (Sr)	2026/06/09	1.4		%	20
			Total Thallium (Tl)	2026/06/09	7.2		%	20
			Total Tin (Sn)	2026/06/09	NC		%	20
			Total Titanium (Ti)	2026/06/09	NC		%	20



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Uranium (U)	2026/06/09	0.83		%	20
			Total Vanadium (V)	2026/06/09	NC		%	20
			Total Zinc (Zn)	2026/06/09	NC		%	20
			Total Zirconium (Zr)	2026/06/09	NC		%	20

Duplicate: Paired analysis of a separate portion of the same sample. Used to evaluate the variance in the measurement.

Matrix Spike: A sample to which a known amount of the analyte of interest has been added. Used to evaluate sample matrix interference.

Spiked Blank: A blank matrix sample to which a known amount of the analyte, usually from a second source, has been added. Used to evaluate method accuracy.

Method Blank: A blank matrix containing all reagents used in the analytical procedure. Used to identify laboratory contamination.

Surrogate: A pure or isotopically labeled compound whose behavior mirrors the analytes of interest. Used to evaluate extraction efficiency.

NC (Matrix Spike): The recovery in the matrix spike was not calculated. The relative difference between the concentration in the parent sample and the spike amount was too small to permit a reliable recovery calculation (matrix spike concentration was less than the native sample concentration)

NC (Duplicate RPD): The duplicate RPD was not calculated. The concentration in the sample and/or duplicate was too low to permit a reliable RPD calculation (absolute difference $\leq 2 \times \text{RDL}$).

(1) Recovery or RPD for this parameter is outside control limits. The overall quality control for this analysis meets acceptability criteria.

(2) Blank Spike outside acceptance criteria (10% of analytes failure allowed).

(3) Method Blank exceeds acceptance limits - $2 \times \text{RDL}$ acceptable for low level metals determination.

(4) Detection limits raised due to sample matrix.

(5) Spike recovery exceeds acceptance criteria (high recovery). As results are non-detect, there is no impact on data quality.



Bureau Veritas Job #: C631926
Report Date: 2026/06/15

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213
Sampler Initials: 5.4

VALIDATION SIGNATURE PAGE

The analytical data and all QC contained in this report were reviewed and validated by:

David Huang, M.Sc., P.Chem., QP, Scientific Services Manager

Kimberly Tamaki, Scientist, Ecotoxicology

Levi Manchak, Project Manager SR



Melissa Thompson, Scientist

Pushpa Gurung, Laboratory Supervisor

Suwan (Sze Yeung) Fock, B.Sc., Scientific Specialist



Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports. For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.

EPH in Water when PAH required Chromatogram

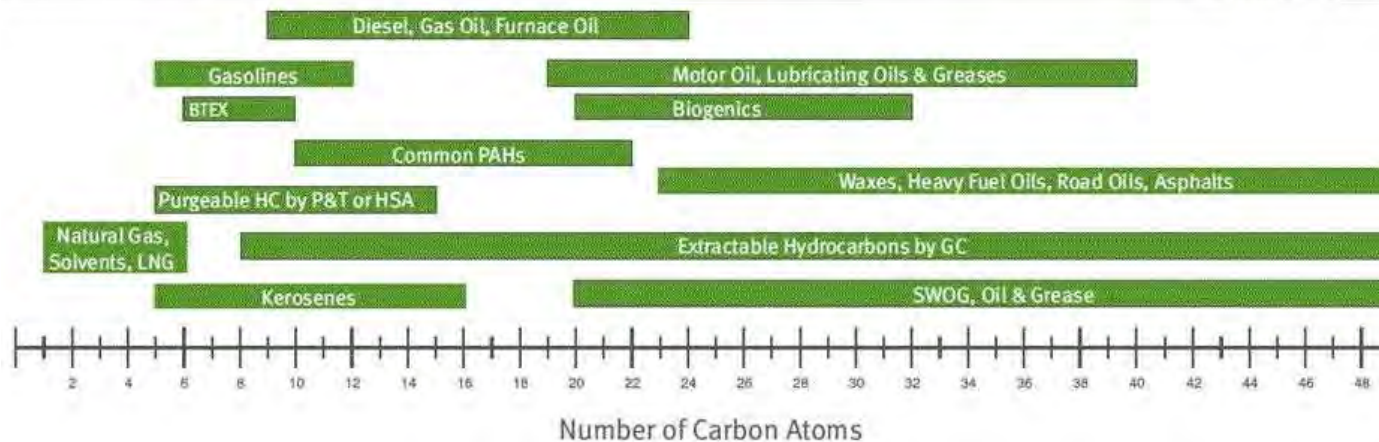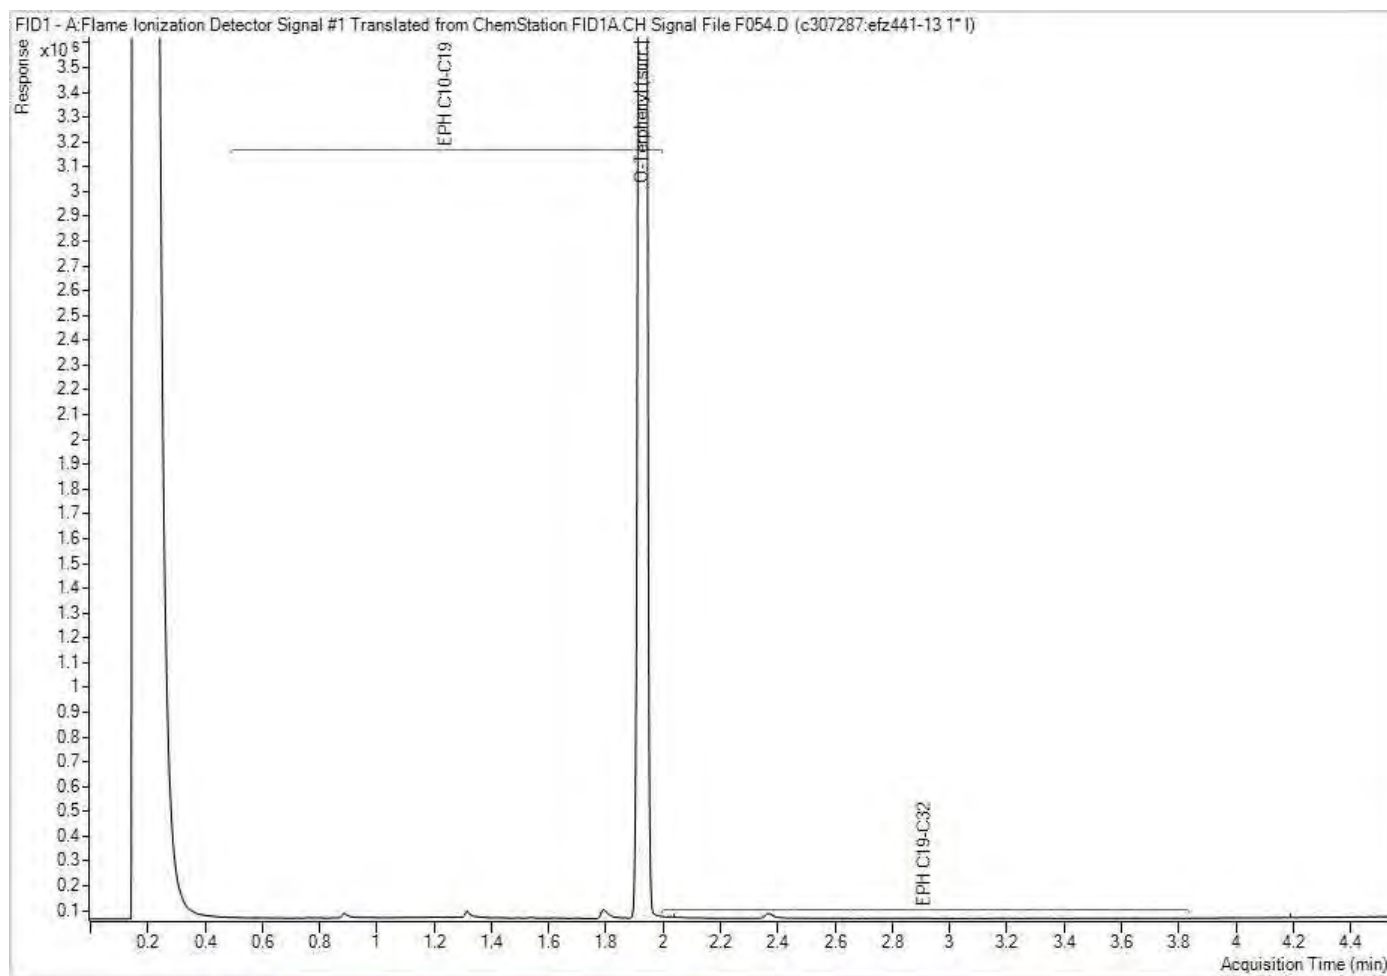

Note: This information is provided for reference purposes only. Should detailed chemist interpretation or fingerprinting be required, please contact the laboratory.


EPH in Water when PAH required Chromatogram

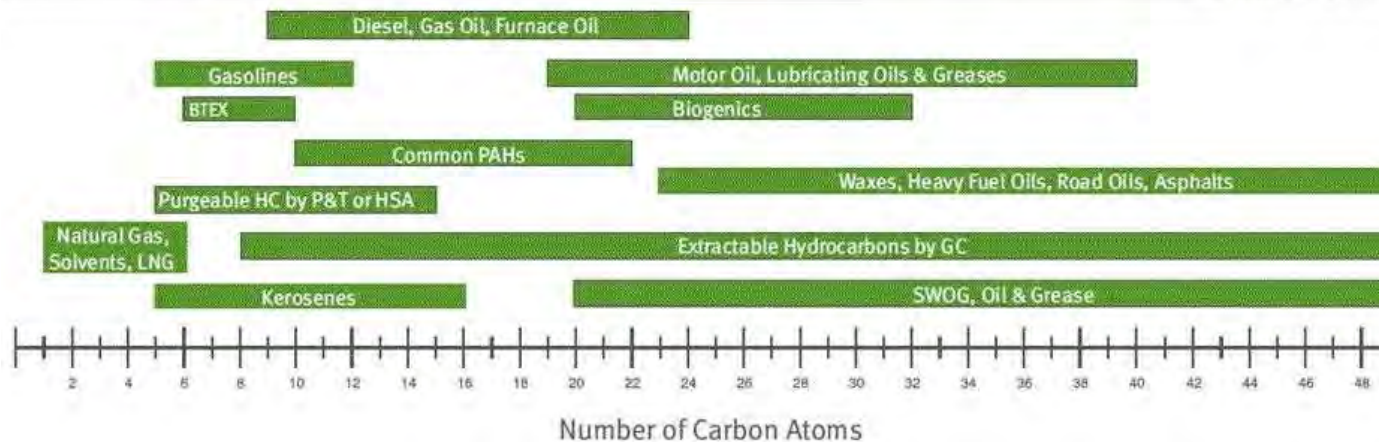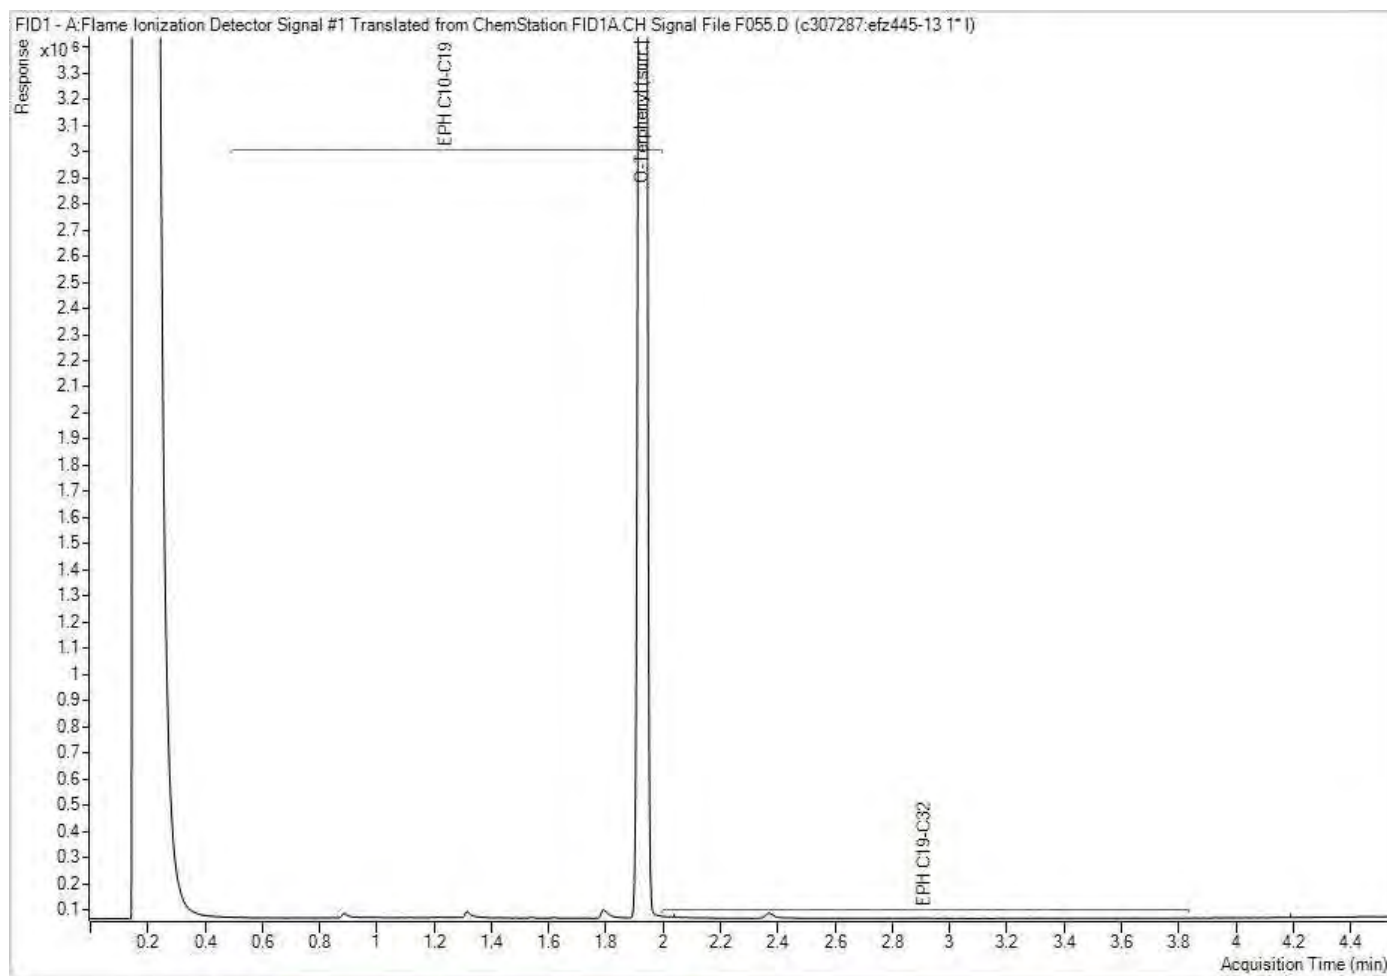

Note: This information is provided for reference purposes only. Should detailed chemist interpretation or fingerprinting be required, please contact the laboratory.



eCOC: W131162



Project Information: C631926
Job Received: 2026/06/02 17:45
Expected TAT: Standard TAT
Expected Arrival: 2026/06/02 17:30
Submitted By: Jackson Macpherson
Submitted To: Burnaby ENV: 4606
Canada Way

Invoice Information

Attn: Accounts Payable
Fortis BC Energy Inc
16705 Fraser Hwy
Surrey, BC, V4N 0E8
Email to:
einvoices@fortisbc.com

Report Information

Attn: Brett Lucas
HATFIELD CONSULTANTS
200-850 Harbourside Dr
North Vancouver, BC, V7P 0A3
Email to:
blucas@hatfieldgroup.com
danielle.samels@fortisbc.com
smangwani@hatfieldgroup.com
jmacpherson@hatfieldgroup.com
swolf@hatfieldgroup.com

Project Information

Quote #: C50083
PO/AFE#: 4800010213
Project #: Fortis11234/PE-110163
Site Location: Woodfibre Pipeline Project

Analytical Summary

A: Standard TAT

Client Sample ID	Clnt Ref	Sampling Date/Time	Matrix	#Cont	Woodfibre	Woodfibre Additional	Woodfibre Blank	Daphnia Magna LC50 Multi-concentration	Rainbow Trout LC50 Multi-concentration	Set Number
WLNG-DS	1	2026/06/02 09:30	WATER	14	A					1
WLNG -EOP	2	2026/06/02 09:30	WATER	23	A	A		A	A	2
WLNG-US	3	2026/06/02 09:30	WATER	14	A					1
Field Blank	4	2026/06/02 09:30	WATER	14			A			3
Trip Blank	5	2026/06/02 09:30	WATER	14			A			3
DUP	6	2026/06/02 09:30	WATER	18	A	A				4

Deadlines are estimates only and are subject to change. Please refer to your Job Confirmation report for final due dates.

Submission Information

of Samples: 6

Details: *RUSH turn around time on WLNG EOP metals and WLNG EOP daphnia magna LC50 tests, all other tests/samples regular TAT.

eCOC Change Log

Modified By	Date Modified	Changes	Comments
Jackson Macpherson	02 Jun 26 09:37:05	Notes/Comments, Sample Information	Updates
Levi Manchak	02 Jun 26 09:45:53	Notes/Comments, Sample Information	LM1 add note
Jackson Macpherson	02 Jun 26 13:56:11	Notes/Comments, Sample Information	Updates
Jackson Macpherson	02 Jun 26 13:56:21	Shipping Information	Updates
Linsay Sunderman	27 May 26 16:02:51	Tests Requested	testing update
Jackson Macpherson	27 May 26 16:21:29	Sample Information	Review



eCOC: W131162



Project Information: C631926
Job Received: 2026/06/02 17:45
Expected TAT: Standard TAT
Expected Arrival: 2026/06/02 17:30
Submitted By: Jackson Macpherson
Submitted To: Burnaby ENV: 4606
Canada Way

Sample Set Listing

Set 1 (2 samples)	Set 2 (1 sample)	Set 3 (2 samples)	Set 4 (1 sample)
WLNG-DS WLNG-US	WLNG -EOP	Field Blank Trip Blank	DUP



RESULTS OF RAINBOW TROUT LC50 MULTI-CONCENTRATION

Client : 12239 Fortis BC Energy Inc, Surrey **Job Number:** C631926
Client Project Name & Number: WOODFIBRE PIPELINE PROJECT FORTIS11234/PE110163

Test Result:

96 hrs LC50 % vol/vol (95% CL): >100% (N/A) **Statistical Method:** Visual

Sample Name : WLNG -EOP

Description: Clear and colourless. **Sample Number:** EFZ441-16
Sample Collected: Jun 02, 2026 09:30 AM **Sampling Method :** N/A **Site Collection:** N/A
Sample Collected By: 5.4 **Volume Received:** 5 x ECO10 **Avg Temp Arrival:** 6 °C **Storage:** 2-6°C
Sample Received: Jun 02, 2026 05:45 PM **pH:** 7.6 **Dissolved Oxygen:** 9.9 mg/L
Analysis Start : Jun 04, 2026 01:31 PM **Temperature :** 16 °C **Sample Conductance:** 181 µS/cm

Concentration	Temperature (°C)	Temperature (°C)	Dissolved Oxygen (mg/L)	Dissolved Oxygen (mg/L)	pH	pH	Conductivity (uS/cm)	Mortality (#)	Mortality (%)	Atypical Behaviour (#)
% vol/vol	Initial	96 hrs	Initial	96 hrs	Initial	96 hrs	Initial	96 hrs	96 hrs	96 hrs
0	15	16	10.0	9.8	7.7	7.8	59	0	0	0
6.25	15	16	10.0	9.7	7.7	7.8	68	0	0	0
12.5	15	16	10.0	9.6	7.7	7.8	78	0	0	0
25	15	15	10.0	9.8	7.7	7.8	93	0	0	0
50	15	16	10.0	9.6	7.7	7.7	124	0	0	0
100	16	16	9.9	9.6	7.9	7.9	181	0	0	0

Comments : All fish appeared and behaved normally at 24 hours, 48 hours, 72 hours, and 96 hours into testing.

Culture/Control/Dilution Water

Burnaby Municipal Dechlorinated Water

Hardness: 23 mg/L CaCO₃ Other parameters available on request.

Test Conditions

Test concentration : 0,6.25,12.5,25,50,100 (% vol/vol)

Organisms per Vessel : 10 **Test Temperature :** 15 ± 1 °C **Solution Depth :** >15 cm
Total # of Organisms Used : 60 **Pre-aeration Time :** 120 min. **Rate of Aeration** 6.5±1 mL/(min*L)
Test Volume : 15 L **Vessel Volume :** 20L **Test pH Adjusted:** No
Loading Density : 0.2 g/L **Photoperiod :** 16:8 (light: dark)

Test Organism :

Rainbow Trout (*Oncorhynchus mykiss*) **Source :** Aqua Farm

Culture Temperature : 15 ± 2 °C **Weight (Mean) +- SD :** 0.3 ± 0.1 g **Length (Mean) +- SD :** 3.47 ± 0.22 cm
Culture Water Renewal : ≥ 1L/min/kg fish **Weight (Range) :** 0.3 – 0.5 g **Length (Range) :** 3.20 – 3.90 cm
Culture Photoperiod : 16:8 (light: dark) **% Mortality within 7 days :** 0%
Feeding rate and frequency : daily: 1-5% biomass of trout. **Acclimation Time:** >14 days

Reference chemical:

Zinc **Test Date:** Jun 03, 2026
Test Endpoint 96 hrs LC50 (95% confidence interval) : 0.17 (0.12, 0.24)mg/L **Statistical Method :** Probit
Historical Mean LC50 (warning limits) : 0.23 (0.12, 0.46) mg/L **Concentration :** 0,0.04,0.08,0.16,0.32,0.64 mg/L

Test Method

BV Lab's BBY2SOP-00004 is based on the latest version of EPS 1/RM9 and EPS 1 /RM13.

Method Deviations : None.

Note: The results contained in this report refer only to the testing of the sample submitted. Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation, including the toxicity parameters reported herein. The conductivity, dissolved oxygen and pH data contained within the toxicity report are provided for information purposes and are not individually accredited parameters. This report may not be reproduced, except in its entirety, without the written approval of the laboratory.

Analyst : Dayna Lee, Melanie Mazzotti, Sara McLean

Kimberly Tamaki

Verified By : Kimberly Tamaki, Scientist, Ecotoxicology

Date: Jun 15, 2026 09:35 AM
