

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Page	1 of 6

Eagle Mountain – Woodfibre Gas Pipeline Project

BCER Waste Discharge Permit Weekly Report

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Page	2 of 6

Contents

Preamble 3

Introduction 3

 Sampling Methodology 3

Summary-BC Rail Site 5

 Site Activities 5

 Discharge from Water Treatment Plant..... 5

 Receiving Environment Monitoring-Squamish River 5

 Site Activities 5

 Exceedances..... 6

 Discharge from Water Treatment Plant..... 6

 Receiving Environment Monitoring-East Creek..... 6

Appendix A: BC Rail Point of Discharge from Water Treatment System Documentation

Appendix B: BC Rail Receiving Environment Documentation

Appendix C: Woodfibre Point of Discharge from Water Treatment System Documentation

Appendix D: Woodfibre Receiving Environment Documentation

Appendix E: Lab Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Page	3 of 6

Preamble

This weekly report for the British Columbia Energy Regulator (BCER) Waste Discharge Permit (BCER number PE-110163) for the FortisBC Eagle Mountain – Woodfibre Gas Pipeline (EGP) Project includes the results of water quality monitoring and sampling of the receiving environments (upstream and downstream) and points of discharge during the reporting period.

FortisBC has retained Hatfield Consultants as the Qualified Professional to implement and oversee the monitoring and sampling programs. The data represented below, including laboratory reported exceedances, represent conditions measured from final discharge points and the associated receiving environments, as required under the Waste Discharge Permit.

Introduction

The results provided in this document have been submitted to BCER by FortisBC as per the requirements listed in Section 4.2 of the Waste Discharge Permit PE-110163:

The Permittee shall summarize the results of the discharge and receiving environment compliance sampling and monitoring program in a report that shall be submitted weekly over the term of this permit. The sampling and monitoring results shall be suitably tabulated and include comparison to the respective British Columbia Approved and Working Water Quality Guidelines for Freshwater & Marine Aquatic Life, as published by the Ministry of Environment & Climate Change Strategy. Any exceedance of regulatory guidelines shall be clearly highlighted, and any missed sampling events/missing data shall be identified with an explanation provided. Reporting frequency may be reduced upon a history of compliance and by written confirmation from the BCER. These reports shall be submitted to Waste.Management@bc-er.ca. A copy of the reports shall be provided to each First Nation consulted with regarding the subject permit, and also made publicly available on the FortisBC Eagle Mountain-Woodfibre Gas Pipeline Project | Talking Energy webpage.

Sampling Methodology

The monitoring and sampling has been carried out in accordance with the procedures described in the most recent edition of the “British Columbia Field Sampling Manual” using field equipment and laboratory samples to meet daily and real-time requirements for the Waste Discharge Permit.

In the receiving environments, real-time and daily readings were monitored at the same time with one piece of equipment, allowing real-time daily readings. Visible sheen was monitored through visual inspections during times of discharge or sampling.

At the point of discharges, parameters are monitored using field equipment and water quality sondes, as well as discrete weekly water quality sampling events for laboratory analyses. Table 1 and Table 2 below describe this monitoring.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

August 03 to
August 09, 2026

Report #

124

Page

4 of 6

Table 1. Monitor Details for the Point of Discharge from the Water Treatment System-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily (or per batch)	DO	Monitoring using YSI ProDSS
	ORP	Monitoring using YSI ProDSS
	Salinity	Monitoring using YSI ProDSS
Real-time (or per batch)	pH	Monitoring using GF Dryloc pH Series NPT
	Temperature	Monitoring using LevelPro PT100 Temperature and Signet 2350 Temp sensor
	NTU	Monitoring using Observer NEP9504GPI
	Electrical Conductivity	Monitoring using ProCon C450
Weekly (or per batch) Lab Samples	List prescribed in permit	Lab samples*

*Indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.

Table 2. Monitor Details for the Receiving Environment (upstream and downstream)-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily	DO	Monitoring using Sonde- AquaTROLL 600 datalogger
	ORP	Monitoring using Sonde- AquaTROLL 600 datalogger
	Salinity	Monitoring using Sonde- AquaTROLL 600 datalogger
Real-time	pH	Monitoring using Sonde- AquaTROLL 600 datalogger
	Temperature	Monitoring using Sonde- AquaTROLL 600 datalogger
	NTU	Monitoring using Sonde- AquaTROLL 600 datalogger
	Electrical Conductivity	Monitoring using Sonde- AquaTROLL 600 datalogger
Weekly Lab Samples	List prescribed in permit	Lab samples*

*Indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.



Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report

Reporting Week

August 03 to
August 09, 2026

Report #

124

Page

5 of 6

Summary-BC Rail Site

Site Activities

- The soft ground tunnel has been completed and FortisBC is in the process of demobilizing equipment and preparations for pipe stringing.

Discharge from Water Treatment Plant

- There was no discharge this week from the BC Rail Site.

Receiving Environment Monitoring-Squamish River

Tables 3 and 4 below provide information on water quality monitoring. Lab sampling has been put on hold with permission from BCER as there are currently no discharges. Appendix B includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit and confirmed by BCER, with additional oversight by the QP.

Table 3. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Upstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

Table 4. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Downstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

** Data gaps in available in-situ continuous monitoring data, included:

- SQU US
 - 2026/08/03 at 00:00 to 2026/08/09 at 23:45: Due to sonde maintenance, no data available.
- SQU DS
 - 2026/08/05 at 14:45 to 2026/08/06 at 15:45: Due to sonde maintenance, no data available.

Summary-Woodfibre Site

Site Activities

- Weekly upstream, downstream, and end of pipe water quality sampling performed by the QP.
- On-going tunnelling at WLNG and grouting works to mitigate water ingress.

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Page	6 of 6

Exceedances

There were no reportable exceedance identified during the August 3 to August 9, 2026 reporting period.

Discharge from Water Treatment Plant

Appendix C includes volume information and real-time/field samples from the discharge.

Receiving Environment Monitoring-East Creek

Tables 5 and 6 below provide information on water quality monitoring. Appendix D includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit with additional oversight by the QP.

Table 5. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Upstream	2026-08-05	Yes *	Full set of results are provided in Appendix D.**

Table 6. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Downstream	2026-08-05	Yes *	Full set of results are provided in Appendix D.**

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

**Data gaps in available in-situ continuous monitoring data, included:

- EAS US
 - 2026/08/03 at 00:00 to 2026/08/09 at 23:45: Sonde sensor set to 60-minute recording interval rather than 15-minute recording interval, therefore creating three data gaps an hour.
- EAS DS
 - No data gaps reported.

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix A	A-1

Appendix A:
BCR Site Point of Discharge from Water
Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix A	A-2

BCR Site Batch Sample Analysis
No discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix A	A-3

BCR Site WTP Discharge Field Notes and Logs

No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix B	B-1

Appendix B:
BCR Site Receiving Environment Documentation
No Sample

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix B	B-2

BCR Site Receiving Environment Sample Analysis
No Sample

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix B	B-3

BCR Site Receiving Environment
Field Notes and Logs

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-03 00:00:00	11.40	24.42	0.53	7.36	9.96	4.01	0.01
SQU-DS	2026-08-03 00:15:00	11.37	24.63	0.53	7.32	9.96	7.16	0.01
SQU-DS	2026-08-03 00:30:00	11.35	24.76	0.53	7.32	9.96	8.67	0.01
SQU-DS	2026-08-03 00:45:00	11.32	24.77	0.53	7.32	9.96	11.48	0.01
SQU-DS	2026-08-03 01:00:00	11.29	24.77	0.54	7.29	9.97	14.47	0.01
SQU-DS	2026-08-03 01:15:00	11.26	24.89	0.54	7.30	9.97	13.01	0.01
SQU-DS	2026-08-03 01:30:00	11.23	24.72	0.53	7.32	9.97	12.71	0.01
SQU-DS	2026-08-03 01:45:00	11.19	24.59	0.54	7.29	9.97	15.44	0.01
SQU-DS	2026-08-03 02:00:00	11.16	24.73	0.54	7.32	9.98	14.16	0.01
SQU-DS	2026-08-03 02:15:00	11.12	24.67	0.54	7.33	10.00	14.01	0.01
SQU-DS	2026-08-03 02:30:00	11.08	24.64	0.54	7.32	9.99	13.90	0.01
SQU-DS	2026-08-03 02:45:00	11.03	24.62	0.54	7.31	10.00	14.76	0.01
SQU-DS	2026-08-03 03:00:00	10.99	24.73	0.54	7.32	10.01	18.05	0.01
SQU-DS	2026-08-03 03:15:00	10.95	24.68	0.54	7.31	10.02	16.37	0.01
SQU-DS	2026-08-03 03:30:00	10.92	24.50	0.54	7.32	10.02	13.68	0.01
SQU-DS	2026-08-03 03:45:00	10.88	24.56	0.54	7.32	10.02	15.91	0.01
SQU-DS	2026-08-03 04:00:00	10.84	24.72	0.54	7.30	10.03	15.68	0.01
SQU-DS	2026-08-03 04:15:00	10.79	24.15	0.54	7.30	10.05	15.26	0.01
SQU-DS	2026-08-03 04:30:00	10.74	24.08	0.54	7.31	10.05	15.15	0.01
SQU-DS	2026-08-03 04:45:00	10.69	24.11	0.54	7.30	10.06	15.97	0.01
SQU-DS	2026-08-03 05:00:00	10.63	23.96	0.54	7.29	10.07	15.48	0.01
SQU-DS	2026-08-03 05:15:00	10.57	24.03	0.54	7.30	10.07	16.09	0.01
SQU-DS	2026-08-03 05:30:00	10.52	24.12	0.54	7.29	10.09	15.09	0.01
SQU-DS	2026-08-03 05:45:00	10.49	23.91	0.54	7.29	10.10	15.17	0.01
SQU-DS	2026-08-03 06:00:00	10.45	23.87	0.54	7.29	10.10	15.34	0.01
SQU-DS	2026-08-03 06:15:00	10.41	23.89	0.54	7.29	10.12	16.20	0.01
SQU-DS	2026-08-03 06:30:00	10.38	23.88	0.54	7.30	10.13	15.41	0.01
SQU-DS	2026-08-03 06:45:00	10.35	23.75	0.54	7.28	10.13	17.20	0.01
SQU-DS	2026-08-03 07:00:00	10.32	23.74	0.54	7.28	10.14	13.93	0.01
SQU-DS	2026-08-03 07:15:00	10.31	23.62	0.54	7.29	10.14	14.48	0.01
SQU-DS	2026-08-03 07:30:00	10.29	23.62	0.54	7.27	10.15	17.34	0.01
SQU-DS	2026-08-03 07:45:00	10.28	23.50	0.54	7.29	10.16	13.06	0.01
SQU-DS	2026-08-03 08:00:00	10.29	23.56	0.54	7.29	10.17	14.67	0.01
SQU-DS	2026-08-03 08:15:00	10.29	22.66	0.54	7.29	10.18	20.50	0.01
SQU-DS	2026-08-03 08:30:00	10.30	22.50	0.54	7.30	10.18	19.39	0.01
SQU-DS	2026-08-03 08:45:00	10.32	22.42	0.54	7.31	10.19	15.09	0.01
SQU-DS	2026-08-03 09:00:00	10.35	22.76	0.54	7.32	10.20	16.61	0.01
SQU-DS	2026-08-03 09:15:00	10.38	22.17	0.54	7.33	10.20	15.17	0.01
SQU-DS	2026-08-03 09:30:00	10.43	22.56	0.54	7.33	10.20	15.51	0.01
SQU-DS	2026-08-03 09:45:00	10.48	22.04	0.54	7.31	10.20	20.38	0.01
SQU-DS	2026-08-03 10:00:00	10.53	21.29	0.54	7.32	10.21	15.55	0.01
SQU-DS	2026-08-03 10:15:00	10.58	21.44	0.54	7.32	10.20	14.14	0.01
SQU-DS	2026-08-03 10:30:00	10.64	20.57	0.54	7.32	10.19	16.70	0.01
SQU-DS	2026-08-03 10:45:00	10.71	20.83	0.54	7.31	10.19	18.80	0.01
SQU-DS	2026-08-03 11:00:00	10.78	20.87	0.54	7.31	10.18	18.32	0.01
SQU-DS	2026-08-03 11:15:00	10.85	21.32	0.54	7.31	10.16	21.43	0.01
SQU-DS	2026-08-03 11:30:00	10.91	21.36	0.54	7.31	10.16	17.34	0.01
SQU-DS	2026-08-03 11:45:00	10.98	21.44	0.54	7.31	10.16	18.30	0.01
SQU-DS	2026-08-03 12:00:00	11.06	21.48	0.54	7.30	10.15	18.74	0.01
SQU-DS	2026-08-03 12:15:00	11.14	21.61	0.54	7.30	10.13	19.78	0.01
SQU-DS	2026-08-03 12:30:00	11.22	21.27	0.54	7.29	10.16	24.24	0.01
SQU-DS	2026-08-03 12:45:00	11.30	21.26	0.54	7.31	10.13	22.01	0.01
SQU-DS	2026-08-03 13:00:00	11.38	21.33	0.54	7.31	10.12	20.60	0.01
SQU-DS	2026-08-03 13:15:00	11.46	21.41	0.54	7.30	10.12	24.42	0.01
SQU-DS	2026-08-03 13:30:00	11.54	21.56	0.54	7.30	10.10	21.05	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-03 13:45:00	11.62	21.61	0.54	7.32	10.09	21.00	0.01
SQU-DS	2026-08-03 14:00:00	11.71	21.81	0.54	7.30	10.08	21.49	0.01
SQU-DS	2026-08-03 14:15:00	11.79	21.95	0.54	7.31	10.07	20.26	0.01
SQU-DS	2026-08-03 14:30:00	11.87	21.90	0.54	7.32	10.08	22.96	0.01
SQU-DS	2026-08-03 14:45:00	11.95	23.02	0.54	7.31	10.06	23.42	0.01
SQU-DS	2026-08-03 15:00:00	12.02	22.89	0.54	7.33	10.05	23.04	0.01
SQU-DS	2026-08-03 15:15:00	12.10	23.57	0.54	7.31	10.03	27.64	0.01
SQU-DS	2026-08-03 15:30:00							
SQU-DS	2026-08-03 15:45:00	12.23	28.36	0.51	7.36	10.02	24.00	0.01
SQU-DS	2026-08-03 16:00:00	12.28	28.26	0.51	7.36	9.99	24.78	0.01
SQU-DS	2026-08-03 16:15:00	12.34	28.42	0.52	7.37	10.00	24.04	0.01
SQU-DS	2026-08-03 16:30:00	12.40	28.66	0.52	7.32	9.98	23.35	0.01
SQU-DS	2026-08-03 16:45:00	12.44	29.08	0.52	7.38	9.96	25.32	0.01
SQU-DS	2026-08-03 17:00:00	12.48	28.92	0.52	7.39	9.96	22.17	0.01
SQU-DS	2026-08-03 17:15:00	12.52	29.18	0.52	7.37	9.93	20.27	0.01
SQU-DS	2026-08-03 17:30:00	12.55	29.20	0.53	7.30	9.91	25.25	0.01
SQU-DS	2026-08-03 17:45:00	12.58	29.50	0.52	7.38	9.92	21.64	0.01
SQU-DS	2026-08-03 18:00:00	12.58	29.73	0.52	7.39	9.89	20.38	0.01
SQU-DS	2026-08-03 18:15:00	12.59	29.98	0.53	7.35	9.86	22.35	0.01
SQU-DS	2026-08-03 18:30:00	12.59	30.20	0.53	7.39	9.84	20.32	0.01
SQU-DS	2026-08-03 18:45:00	12.60	30.28	0.53	7.36	9.84	22.00	0.01
SQU-DS	2026-08-03 19:00:00	12.60	30.65	0.53	7.40	9.81	25.85	0.01
SQU-DS	2026-08-03 19:15:00	12.60	30.77	0.53	7.38	9.81	26.23	0.01
SQU-DS	2026-08-03 19:30:00	12.58	30.57	0.53	7.38	9.80	23.06	0.01
SQU-DS	2026-08-03 19:45:00	12.56	30.80	0.53	7.40	9.78	21.99	0.01
SQU-DS	2026-08-03 20:00:00	12.55	30.68	0.53	7.41	9.77	23.68	0.01
SQU-DS	2026-08-03 20:15:00	12.54	30.75	0.53	7.42	9.77	25.65	0.01
SQU-DS	2026-08-03 20:30:00	12.53	30.51	0.53	7.33	9.75	25.80	0.01
SQU-DS	2026-08-03 20:45:00	12.52	30.56	0.53	7.41	9.73	22.91	0.01
SQU-DS	2026-08-03 21:00:00	12.51	30.66	0.53	7.42	9.73	24.49	0.01
SQU-DS	2026-08-03 21:15:00	12.51	30.67	0.53	7.38	9.71	27.54	0.01
SQU-DS	2026-08-03 21:30:00	12.50	30.87	0.53	7.43	9.68	26.42	0.01
SQU-DS	2026-08-03 21:45:00	12.50	31.07	0.53	7.42	9.67	23.62	0.01
SQU-DS	2026-08-03 22:00:00	12.49	31.47	0.53	7.41	9.65	28.90	0.01
SQU-DS	2026-08-03 22:15:00	12.48	31.53	0.53	7.41	9.64	26.43	0.01
SQU-DS	2026-08-03 22:30:00	12.48	31.83	0.53	7.41	9.63	26.62	0.01
SQU-DS	2026-08-03 22:45:00	12.47	32.06	0.53	7.40	9.61	29.74	0.01
SQU-DS	2026-08-03 23:00:00	12.46	32.41	0.53	7.36	9.59	27.61	0.01
SQU-DS	2026-08-03 23:15:00	12.45	32.25	0.53	7.38	9.57	33.49	0.01
SQU-DS	2026-08-03 23:30:00	12.43	32.12	0.53	7.38	9.58	31.79	0.01
SQU-DS	2026-08-03 23:45:00	12.41	32.37	0.53	7.33	9.58	32.84	0.01
SQU-DS	2026-08-04 00:00:00	12.38	31.93	0.53	7.35	9.55	31.89	0.01
SQU-DS	2026-08-04 00:15:00	12.34	31.83	0.53	7.33	9.57	33.87	0.01
SQU-DS	2026-08-04 00:30:00	12.30	31.61	0.54	7.29	9.58	34.41	0.01
SQU-DS	2026-08-04 00:45:00	12.26	31.27	0.53	7.32	9.56	32.22	0.01
SQU-DS	2026-08-04 01:00:00	12.20	31.59	0.54	7.27	9.58	37.94	0.01
SQU-DS	2026-08-04 01:15:00	12.14	31.10	0.54	7.27	9.60	35.48	0.01
SQU-DS	2026-08-04 01:30:00	12.08	30.92	0.54	7.30	9.58	35.39	0.01
SQU-DS	2026-08-04 01:45:00	12.02	30.25	0.54	7.26	9.61	36.00	0.01
SQU-DS	2026-08-04 02:00:00	11.95	30.30	0.54	7.27	9.62	35.47	0.01
SQU-DS	2026-08-04 02:15:00	11.90	30.61	0.54	7.29	9.62	37.57	0.01
SQU-DS	2026-08-04 02:30:00	11.84	29.99	0.54	7.31	9.68	37.32	0.01
SQU-DS	2026-08-04 02:45:00	11.79	29.93	0.54	7.30	9.67	37.54	0.01
SQU-DS	2026-08-04 03:00:00	11.73	29.42	0.54	7.28	9.70	36.65	0.01
SQU-DS	2026-08-04 03:15:00	11.67	29.50	0.54	7.31	9.70	37.54	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-04 03:30:00	11.62	29.80	0.54	7.32	9.71	38.42	0.01
SQU-DS	2026-08-04 03:45:00	11.56	29.29	0.54	7.31	9.73	33.83	0.01
SQU-DS	2026-08-04 04:00:00	11.50	29.46	0.54	7.31	9.72	36.59	0.01
SQU-DS	2026-08-04 04:15:00	11.44	29.11	0.54	7.34	9.76	36.89	0.01
SQU-DS	2026-08-04 04:30:00	11.38	29.02	0.54	7.34	9.74	36.50	0.01
SQU-DS	2026-08-04 04:45:00	11.32	29.01	0.54	7.32	9.78	40.58	0.01
SQU-DS	2026-08-04 05:00:00	11.27	28.87	0.54	7.31	9.79	39.83	0.01
SQU-DS	2026-08-04 05:15:00	11.22	28.99	0.54	7.34	9.81	37.07	0.01
SQU-DS	2026-08-04 05:30:00	11.17	28.72	0.54	7.32	9.81	31.45	0.01
SQU-DS	2026-08-04 05:45:00	11.13	28.66	0.54	7.29	9.84	39.62	0.01
SQU-DS	2026-08-04 06:00:00	11.09	28.71	0.54	7.34	9.84	40.25	0.01
SQU-DS	2026-08-04 06:15:00	11.05	28.50	0.54	7.32	9.85	42.66	0.01
SQU-DS	2026-08-04 06:30:00	11.02	28.74	0.54	7.34	9.87	37.66	0.01
SQU-DS	2026-08-04 06:45:00	10.98	28.54	0.54	7.34	9.87	36.83	0.01
SQU-DS	2026-08-04 07:00:00	10.95	28.45	0.54	7.34	9.88	36.22	0.01
SQU-DS	2026-08-04 07:15:00	10.93	28.60	0.54	7.26	9.89	41.16	0.01
SQU-DS	2026-08-04 07:30:00	10.91	28.24	0.54	7.36	9.90	36.29	0.01
SQU-DS	2026-08-04 07:45:00	10.89	28.45	0.54	7.34	9.90	38.85	0.01
SQU-DS	2026-08-04 08:00:00	10.89	28.16	0.54	7.35	9.91	34.22	0.01
SQU-DS	2026-08-04 08:15:00	10.88	28.45	0.54	7.34	9.92	36.44	0.01
SQU-DS	2026-08-04 08:30:00	10.89	28.46	0.54	7.33	9.93	34.72	0.01
SQU-DS	2026-08-04 08:45:00	10.90	28.27	0.54	7.33	9.95	34.61	0.01
SQU-DS	2026-08-04 09:00:00	10.92	28.17	0.54	7.29	9.96	37.28	0.01
SQU-DS	2026-08-04 09:15:00	10.95	28.26	0.54	7.32	9.97	37.75	0.01
SQU-DS	2026-08-04 09:30:00	10.98	28.43	0.54	7.32	9.96	37.26	0.01
SQU-DS	2026-08-04 09:45:00	11.02	28.19	0.54	7.35	9.97	32.91	0.01
SQU-DS	2026-08-04 10:00:00	11.07	28.39	0.54	7.35	9.95	41.15	0.01
SQU-DS	2026-08-04 10:15:00	11.13	28.01	0.54	7.35	9.95	36.90	0.01
SQU-DS	2026-08-04 10:30:00	11.19	28.22	0.54	7.36	9.95	32.45	0.01
SQU-DS	2026-08-04 10:45:00	11.27	27.95	0.54	7.31	9.94	36.48	0.01
SQU-DS	2026-08-04 11:00:00	11.34	27.79	0.54	7.36	9.93	35.70	0.01
SQU-DS	2026-08-04 11:15:00	11.43	27.86	0.54	7.34	9.93	34.90	0.01
SQU-DS	2026-08-04 11:30:00	11.51	27.54	0.54	7.32	9.93	32.37	0.01
SQU-DS	2026-08-04 11:45:00	11.60	27.65	0.54	7.33	9.92	31.90	0.01
SQU-DS	2026-08-04 12:00:00	11.69	27.64	0.54	7.33	9.89	28.92	0.01
SQU-DS	2026-08-04 12:15:00	11.79	27.69	0.54	7.36	9.90	32.23	0.01
SQU-DS	2026-08-04 12:30:00	11.89	28.24	0.54	7.35	9.89	30.33	0.01
SQU-DS	2026-08-04 12:45:00	11.98	29.07	0.54	7.37	9.88	31.70	0.01
SQU-DS	2026-08-04 13:00:00	12.07	29.74	0.54	7.39	9.86	31.31	0.01
SQU-DS	2026-08-04 13:15:00	12.16	29.88	0.54	7.38	9.88	32.77	0.01
SQU-DS	2026-08-04 13:30:00	12.24	30.17	0.54	7.37	9.88	31.59	0.01
SQU-DS	2026-08-04 13:45:00	12.29	30.48	0.54	7.32	9.84	31.13	0.01
SQU-DS	2026-08-04 14:00:00	12.35	30.16	0.54	7.33	9.86	31.13	0.01
SQU-DS	2026-08-04 14:15:00	12.40	30.19	0.54	7.40	9.85	32.80	0.01
SQU-DS	2026-08-04 14:30:00	12.47	30.38	0.54	7.38	9.81	36.14	0.01
SQU-DS	2026-08-04 14:45:00	12.54	30.05	0.54	7.39	9.82	31.41	0.01
SQU-DS	2026-08-04 15:00:00	12.60	30.51	0.54	7.39	9.80	29.05	0.01
SQU-DS	2026-08-04 15:15:00	12.68	30.51	0.54	7.37	9.80	32.47	0.01
SQU-DS	2026-08-04 15:30:00	12.75	29.97	0.54	7.31	9.79	28.60	0.01
SQU-DS	2026-08-04 15:45:00	12.82	30.30	0.54	7.39	9.77	27.94	0.01
SQU-DS	2026-08-04 16:00:00	12.89	30.65	0.54	7.38	9.75	29.84	0.01
SQU-DS	2026-08-04 16:15:00	12.96	30.68	0.54	7.39	9.75	28.87	0.01
SQU-DS	2026-08-04 16:30:00	13.01	30.67	0.54	7.41	9.73	27.67	0.01
SQU-DS	2026-08-04 16:45:00	13.05	30.52	0.54	7.39	9.74	30.43	0.01
SQU-DS	2026-08-04 17:00:00	13.08	30.58	0.53	7.43	9.72	29.41	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-04 17:15:00	13.11	30.43	0.54	7.41	9.71	31.37	0.01
SQU-DS	2026-08-04 17:30:00	13.12	31.06	0.54	7.40	9.69	29.93	0.01
SQU-DS	2026-08-04 17:45:00	13.12	31.11	0.54	7.38	9.67	32.25	0.01
SQU-DS	2026-08-04 18:00:00	13.11	30.86	0.54	7.38	9.67	34.85	0.01
SQU-DS	2026-08-04 18:15:00	13.10	30.73	0.54	7.35	9.65	31.43	0.01
SQU-DS	2026-08-04 18:30:00	13.09	30.99	0.54	7.37	9.64	32.31	0.01
SQU-DS	2026-08-04 18:45:00	13.08	31.00	0.54	7.35	9.63	36.66	0.01
SQU-DS	2026-08-04 19:00:00	13.09	31.07	0.54	7.40	9.61	30.98	0.01
SQU-DS	2026-08-04 19:15:00	13.10	30.85	0.54	7.39	9.61	32.51	0.01
SQU-DS	2026-08-04 19:30:00	13.10	30.92	0.53	7.42	9.59	34.57	0.01
SQU-DS	2026-08-04 19:45:00	13.09	30.75	0.54	7.39	9.59	31.79	0.01
SQU-DS	2026-08-04 20:00:00	13.10	30.52	0.54	7.37	9.57	31.99	0.01
SQU-DS	2026-08-04 20:15:00	13.10	30.34	0.54	7.38	9.57	34.49	0.01
SQU-DS	2026-08-04 20:30:00	13.10	30.35	0.54	7.40	9.56	30.49	0.01
SQU-DS	2026-08-04 20:45:00	13.10	30.06	0.53	7.41	9.55	32.00	0.01
SQU-DS	2026-08-04 21:00:00	13.09	30.22	0.54	7.39	9.54	32.10	0.01
SQU-DS	2026-08-04 21:15:00	13.10	30.20	0.53	7.44	9.52	33.67	0.01
SQU-DS	2026-08-04 21:30:00	13.10	30.20	0.53	7.42	9.51	31.59	0.01
SQU-DS	2026-08-04 21:45:00	13.11	30.45	0.53	7.42	9.48	29.96	0.01
SQU-DS	2026-08-04 22:00:00	13.12	30.57	0.53	7.44	9.48	33.76	0.01
SQU-DS	2026-08-04 22:15:00	13.12	30.61	0.53	7.45	9.47	35.72	0.01
SQU-DS	2026-08-04 22:30:00	13.13	30.72	0.53	7.43	9.45	39.81	0.01
SQU-DS	2026-08-04 22:45:00	13.14	31.25	0.53	7.42	9.44	38.18	0.01
SQU-DS	2026-08-04 23:00:00	13.14	31.34	0.53	7.40	9.43	45.22	0.01
SQU-DS	2026-08-04 23:15:00	13.14	31.37	0.53	7.39	9.42	45.34	0.01
SQU-DS	2026-08-04 23:30:00	13.13	31.58	0.53	7.43	9.39	52.26	0.01
SQU-DS	2026-08-04 23:45:00	13.11	31.85	0.53	7.41	9.38	51.14	0.01
SQU-DS	2026-08-05 00:00:00	13.09	32.12	0.53	7.41	9.38	50.71	0.01
SQU-DS	2026-08-05 00:15:00	13.06	32.09	0.53	7.43	9.37	48.83	0.01
SQU-DS	2026-08-05 00:30:00	13.01	32.30	0.53	7.39	9.39	58.05	0.01
SQU-DS	2026-08-05 00:45:00	12.97	32.31	0.53	7.42	9.39	61.00	0.01
SQU-DS	2026-08-05 01:00:00	12.92	31.95	0.54	7.36	9.44	71.08	0.01
SQU-DS	2026-08-05 01:15:00	12.86	32.18	0.54	7.35	9.41	72.05	0.01
SQU-DS	2026-08-05 01:30:00	12.81	31.39	0.54	7.36	9.45	63.91	0.01
SQU-DS	2026-08-05 01:45:00	12.75	31.12	0.53	7.38	9.44	64.15	0.01
SQU-DS	2026-08-05 02:00:00	12.68	30.80	0.53	7.36	9.46	61.86	0.01
SQU-DS	2026-08-05 02:15:00	12.61	30.36	0.53	7.38	9.48	63.41	0.01
SQU-DS	2026-08-05 02:30:00	12.55	30.15	0.53	7.37	9.47	60.69	0.01
SQU-DS	2026-08-05 02:45:00	12.47	29.50	0.54	7.30	9.52	63.93	0.01
SQU-DS	2026-08-05 03:00:00	12.41	28.86	0.54	7.30	9.51	68.23	0.01
SQU-DS	2026-08-05 03:15:00	12.34	28.78	0.54	7.36	9.55	70.61	0.01
SQU-DS	2026-08-05 03:30:00	12.27	28.66	0.54	7.35	9.56	68.64	0.01
SQU-DS	2026-08-05 03:45:00	12.18	28.25	0.54	7.29	9.59	61.45	0.01
SQU-DS	2026-08-05 04:00:00	12.10	28.03	0.54	7.33	9.60	60.44	0.01
SQU-DS	2026-08-05 04:15:00	12.02	27.70	0.54	7.36	9.61	59.74	0.01
SQU-DS	2026-08-05 04:30:00	11.93	27.40	0.54	7.33	9.65	61.57	0.01
SQU-DS	2026-08-05 04:45:00	11.85	27.36	0.54	7.36	9.67	61.37	0.01
SQU-DS	2026-08-05 05:00:00	11.78	27.00	0.54	7.34	9.68	55.98	0.01
SQU-DS	2026-08-05 05:15:00	11.71	26.91	0.54	7.33	9.70	54.97	0.01
SQU-DS	2026-08-05 05:30:00	11.64	26.79	0.54	7.28	9.72	57.59	0.01
SQU-DS	2026-08-05 05:45:00	11.59	26.93	0.54	7.36	9.74	53.53	0.01
SQU-DS	2026-08-05 06:00:00	11.54	26.65	0.54	7.28	9.73	59.52	0.01
SQU-DS	2026-08-05 06:15:00	11.49	26.52	0.54	7.33	9.75	55.92	0.01
SQU-DS	2026-08-05 06:30:00	11.45	26.52	0.54	7.33	9.76	55.34	0.01
SQU-DS	2026-08-05 06:45:00	11.42	26.56	0.54	7.35	9.77	53.68	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-05 07:00:00	11.38	26.46	0.55	7.27	9.77	55.56	0.01
SQU-DS	2026-08-05 07:15:00	11.35	26.39	0.54	7.31	9.79	54.26	0.01
SQU-DS	2026-08-05 07:30:00	11.33	26.19	0.54	7.36	9.80	45.99	0.01
SQU-DS	2026-08-05 07:45:00	11.31	26.27	0.54	7.34	9.80	47.51	0.01
SQU-DS	2026-08-05 08:00:00	11.30	26.26	0.54	7.35	9.82	51.55	0.01
SQU-DS	2026-08-05 08:15:00	11.29	26.08	0.54	7.34	9.82	54.14	0.01
SQU-DS	2026-08-05 08:30:00	11.29	26.20	0.54	7.34	9.84	51.10	0.01
SQU-DS	2026-08-05 08:45:00	11.30	26.07	0.54	7.34	9.84	49.46	0.01
SQU-DS	2026-08-05 09:00:00	11.32	25.93	0.54	7.34	9.85	50.88	0.01
SQU-DS	2026-08-05 09:15:00	11.34	26.11	0.54	7.35	9.85	53.10	0.01
SQU-DS	2026-08-05 09:30:00	11.37	26.04	0.54	7.33	9.85	47.46	0.01
SQU-DS	2026-08-05 09:45:00	11.41	26.13	0.54	7.35	9.86	42.82	0.01
SQU-DS	2026-08-05 10:00:00	11.46	26.23	0.54	7.36	9.86	43.05	0.01
SQU-DS	2026-08-05 10:15:00	11.51	26.16	0.54	7.35	9.86	43.84	0.01
SQU-DS	2026-08-05 10:30:00	11.57	26.32	0.54	7.36	9.86	41.49	0.01
SQU-DS	2026-08-05 10:45:00	11.63	26.29	0.54	7.36	9.86	48.77	0.01
SQU-DS	2026-08-05 11:00:00	11.70	26.37	0.54	7.34	9.86	45.99	0.01
SQU-DS	2026-08-05 11:15:00	11.77	26.30	0.54	7.37	9.87	44.37	0.01
SQU-DS	2026-08-05 11:30:00	11.84	26.56	0.54	7.38	9.85	44.37	0.01
SQU-DS	2026-08-05 11:45:00	11.92	26.62	0.54	7.38	9.83	45.13	0.01
SQU-DS	2026-08-05 12:00:00	12.00	26.67	0.54	7.36	9.84	45.85	0.01
SQU-DS	2026-08-05 12:15:00	12.06	26.68	0.54	7.37	9.84	41.80	0.01
SQU-DS	2026-08-05 12:30:00	12.13	26.97	0.54	7.39	9.82	44.20	0.01
SQU-DS	2026-08-05 12:45:00	12.21	26.93	0.54	7.37	9.82	44.69	0.01
SQU-DS	2026-08-05 13:00:00	12.29	27.05	0.54	7.37	9.80	47.97	0.01
SQU-DS	2026-08-05 13:15:00	12.36	27.00	0.54	7.35	9.81	38.68	0.01
SQU-DS	2026-08-05 13:30:00	12.44	27.08	0.54	7.35	9.80	38.31	0.01
SQU-DS	2026-08-05 13:45:00	12.51	27.16	0.54	7.35	9.78	42.89	0.01
SQU-DS	2026-08-05 14:00:00	12.59	27.19	0.54	7.38	9.80	42.16	0.01
SQU-DS	2026-08-05 14:15:00	12.67	27.42	0.54	7.37	9.79	37.12	0.01
SQU-DS	2026-08-05 14:30:00	15.38	0.07	0.51	6.99	9.19	0.00	0.00
SQU-DS	2026-08-05 14:45:00							
SQU-DS	2026-08-05 15:00:00							
SQU-DS	2026-08-05 15:15:00							
SQU-DS	2026-08-05 15:30:00							
SQU-DS	2026-08-05 15:45:00							
SQU-DS	2026-08-05 16:00:00							
SQU-DS	2026-08-05 16:15:00							
SQU-DS	2026-08-05 16:30:00							
SQU-DS	2026-08-05 16:45:00							
SQU-DS	2026-08-05 17:00:00							
SQU-DS	2026-08-05 17:15:00							
SQU-DS	2026-08-05 17:30:00							
SQU-DS	2026-08-05 17:45:00							
SQU-DS	2026-08-05 18:00:00							
SQU-DS	2026-08-05 18:15:00							
SQU-DS	2026-08-05 18:30:00							
SQU-DS	2026-08-05 18:45:00							
SQU-DS	2026-08-05 19:00:00							
SQU-DS	2026-08-05 19:15:00							
SQU-DS	2026-08-05 19:30:00							
SQU-DS	2026-08-05 19:45:00							
SQU-DS	2026-08-05 20:00:00							
SQU-DS	2026-08-05 20:15:00							
SQU-DS	2026-08-05 20:30:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-05 20:45:00							
SQU-DS	2026-08-05 21:00:00							
SQU-DS	2026-08-05 21:15:00							
SQU-DS	2026-08-05 21:30:00							
SQU-DS	2026-08-05 21:45:00							
SQU-DS	2026-08-05 22:00:00							
SQU-DS	2026-08-05 22:15:00							
SQU-DS	2026-08-05 22:30:00							
SQU-DS	2026-08-05 22:45:00							
SQU-DS	2026-08-05 23:00:00							
SQU-DS	2026-08-05 23:15:00							
SQU-DS	2026-08-05 23:30:00							
SQU-DS	2026-08-05 23:45:00							
SQU-DS	2026-08-06 00:00:00							
SQU-DS	2026-08-06 00:15:00							
SQU-DS	2026-08-06 00:30:00							
SQU-DS	2026-08-06 00:45:00							
SQU-DS	2026-08-06 01:00:00							
SQU-DS	2026-08-06 01:15:00							
SQU-DS	2026-08-06 01:30:00							
SQU-DS	2026-08-06 01:45:00							
SQU-DS	2026-08-06 02:00:00							
SQU-DS	2026-08-06 02:15:00							
SQU-DS	2026-08-06 02:30:00							
SQU-DS	2026-08-06 02:45:00							
SQU-DS	2026-08-06 03:00:00							
SQU-DS	2026-08-06 03:15:00							
SQU-DS	2026-08-06 03:30:00							
SQU-DS	2026-08-06 03:45:00							
SQU-DS	2026-08-06 04:00:00							
SQU-DS	2026-08-06 04:15:00							
SQU-DS	2026-08-06 04:30:00							
SQU-DS	2026-08-06 04:45:00							
SQU-DS	2026-08-06 05:00:00							
SQU-DS	2026-08-06 05:15:00							
SQU-DS	2026-08-06 05:30:00							
SQU-DS	2026-08-06 05:45:00							
SQU-DS	2026-08-06 06:00:00							
SQU-DS	2026-08-06 06:15:00							
SQU-DS	2026-08-06 06:30:00							
SQU-DS	2026-08-06 06:45:00							
SQU-DS	2026-08-06 07:00:00							
SQU-DS	2026-08-06 07:15:00							
SQU-DS	2026-08-06 07:30:00							
SQU-DS	2026-08-06 07:45:00							
SQU-DS	2026-08-06 08:00:00							
SQU-DS	2026-08-06 08:15:00							
SQU-DS	2026-08-06 08:30:00							
SQU-DS	2026-08-06 08:45:00							
SQU-DS	2026-08-06 09:00:00							
SQU-DS	2026-08-06 09:15:00							
SQU-DS	2026-08-06 09:30:00							
SQU-DS	2026-08-06 09:45:00							
SQU-DS	2026-08-06 10:00:00							
SQU-DS	2026-08-06 10:15:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-06 10:30:00							
SQU-DS	2026-08-06 10:45:00							
SQU-DS	2026-08-06 11:00:00							
SQU-DS	2026-08-06 11:15:00							
SQU-DS	2026-08-06 11:30:00							
SQU-DS	2026-08-06 11:45:00							
SQU-DS	2026-08-06 12:00:00							
SQU-DS	2026-08-06 12:15:00							
SQU-DS	2026-08-06 12:30:00							
SQU-DS	2026-08-06 12:45:00							
SQU-DS	2026-08-06 13:00:00							
SQU-DS	2026-08-06 13:15:00							
SQU-DS	2026-08-06 13:30:00							
SQU-DS	2026-08-06 13:45:00							
SQU-DS	2026-08-06 14:00:00							
SQU-DS	2026-08-06 14:15:00							
SQU-DS	2026-08-06 14:30:00							
SQU-DS	2026-08-06 14:45:00							
SQU-DS	2026-08-06 15:00:00							
SQU-DS	2026-08-06 15:15:00							
SQU-DS	2026-08-06 15:30:00							
SQU-DS	2026-08-06 15:45:00							
SQU-DS	2026-08-06 16:00:00	27.99	0.00	0.41	7.30	7.16	0.00	0.00
SQU-DS	2026-08-06 16:15:00	13.53	26.96	0.35	6.81	9.69	56.69	0.01
SQU-DS	2026-08-06 16:30:00	13.55	27.09	0.36	6.63	9.69	68.54	0.01
SQU-DS	2026-08-06 16:45:00	13.54	27.17	0.38	6.45	9.70	50.00	0.01
SQU-DS	2026-08-06 17:00:00	13.58	27.07	0.38	6.51	9.69	45.35	0.01
SQU-DS	2026-08-06 17:15:00	13.59	27.19	0.38	6.50	9.70	66.17	0.01
SQU-DS	2026-08-06 17:30:00	13.61	27.60	0.39	6.49	9.67	52.29	0.01
SQU-DS	2026-08-06 17:45:00	13.62	27.65	0.39	6.49	9.67	37.49	0.01
SQU-DS	2026-08-06 18:00:00	13.61	27.65	0.39	6.51	9.66	44.72	0.01
SQU-DS	2026-08-06 18:15:00	13.60	27.60	0.39	6.53	9.65	39.12	0.01
SQU-DS	2026-08-06 18:30:00	13.60	28.00	0.39	6.56	9.63	56.04	0.01
SQU-DS	2026-08-06 18:45:00	13.59	28.17	0.39	6.58	9.61	42.89	0.01
SQU-DS	2026-08-06 19:00:00	13.59	28.23	0.39	6.58	9.60	44.91	0.01
SQU-DS	2026-08-06 19:15:00	13.58	28.19	0.39	6.57	9.59	44.02	0.01
SQU-DS	2026-08-06 19:30:00	13.57	28.28	0.39	6.63	9.59	59.22	0.01
SQU-DS	2026-08-06 19:45:00	13.56	28.41	0.39	6.61	9.58	40.17	0.01
SQU-DS	2026-08-06 20:00:00	13.54	28.40	0.39	6.60	9.57	48.08	0.01
SQU-DS	2026-08-06 20:15:00	13.53	28.55	0.39	6.63	9.55	48.51	0.01
SQU-DS	2026-08-06 20:30:00	13.52	28.50	0.39	6.64	9.54	48.43	0.01
SQU-DS	2026-08-06 20:45:00	13.52	28.62	0.39	6.64	9.54	43.68	0.01
SQU-DS	2026-08-06 21:00:00	13.51	28.64	0.39	6.62	9.53	57.90	0.01
SQU-DS	2026-08-06 21:15:00	13.51	28.51	0.39	6.64	9.51	43.73	0.01
SQU-DS	2026-08-06 21:30:00	13.51	28.39	0.40	6.62	9.50	43.53	0.01
SQU-DS	2026-08-06 21:45:00	13.52	28.27	0.40	6.61	9.50	49.69	0.01
SQU-DS	2026-08-06 22:00:00	13.52	28.33	0.40	6.64	9.50	55.38	0.01
SQU-DS	2026-08-06 22:15:00	13.52	28.34	0.40	6.64	9.47	45.71	0.01
SQU-DS	2026-08-06 22:30:00	13.52	28.36	0.40	6.65	9.47	55.28	0.01
SQU-DS	2026-08-06 22:45:00	13.52	28.54	0.40	6.68	9.46	53.34	0.01
SQU-DS	2026-08-06 23:00:00	13.52	28.29	0.40	6.67	9.46	52.81	0.01
SQU-DS	2026-08-06 23:15:00	13.51	28.39	0.40	6.67	9.45	52.33	0.01
SQU-DS	2026-08-06 23:30:00	13.50	28.67	0.40	6.68	9.44	62.41	0.01
SQU-DS	2026-08-06 23:45:00	13.48	28.62	0.40	6.71	9.44	61.98	0.01
SQU-DS	2026-08-07 00:00:00	13.46	28.65	0.39	6.74	9.44	63.35	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-07 00:15:00	13.43	28.73	0.39	6.75	9.43	65.46	0.01
SQU-DS	2026-08-07 00:30:00	13.39	28.99	0.40	6.74	9.42	77.15	0.01
SQU-DS	2026-08-07 00:45:00	13.36	29.09	0.40	6.72	9.42	73.02	0.01
SQU-DS	2026-08-07 01:00:00	13.31	29.23	0.40	6.70	9.41	73.02	0.01
SQU-DS	2026-08-07 01:15:00	13.26	29.20	0.40	6.68	9.42	79.27	0.01
SQU-DS	2026-08-07 01:30:00	13.20	29.04	0.40	6.66	9.42	68.96	0.01
SQU-DS	2026-08-07 01:45:00	13.14	28.59	0.40	6.56	9.43	93.65	0.01
SQU-DS	2026-08-07 02:00:00	13.08	28.08	0.40	6.61	9.46	81.86	0.01
SQU-DS	2026-08-07 02:15:00	13.02	28.08	0.40	6.59	9.47	92.26	0.01
SQU-DS	2026-08-07 02:30:00	12.96	27.48	0.40	6.59	9.49	103.42	0.01
SQU-DS	2026-08-07 02:45:00	12.90	27.41	0.40	6.55	9.50	102.38	0.01
SQU-DS	2026-08-07 03:00:00	12.84	27.49	0.40	6.60	9.50	96.06	0.01
SQU-DS	2026-08-07 03:15:00	12.77	27.08	0.40	6.53	9.53	83.41	0.01
SQU-DS	2026-08-07 03:30:00	12.71	27.15	0.41	6.48	9.54	85.17	0.01
SQU-DS	2026-08-07 03:45:00	12.64	26.72	0.40	6.56	9.56	96.76	0.01
SQU-DS	2026-08-07 04:00:00	12.57	26.47	0.40	6.57	9.58	87.41	0.01
SQU-DS	2026-08-07 04:15:00	12.50	26.46	0.40	6.58	9.59	82.00	0.01
SQU-DS	2026-08-07 04:30:00	12.44	26.23	0.40	6.59	9.62	104.23	0.01
SQU-DS	2026-08-07 04:45:00	12.37	26.20	0.40	6.57	9.61	85.24	0.01
SQU-DS	2026-08-07 05:00:00	12.31	26.13	0.40	6.55	9.64	83.38	0.01
SQU-DS	2026-08-07 05:15:00	12.25	25.43	0.40	6.61	9.66	92.09	0.01
SQU-DS	2026-08-07 05:30:00	12.20	25.73	0.41	6.44	9.67	96.58	0.01
SQU-DS	2026-08-07 05:45:00	12.14	25.61	0.40	6.60	9.68	75.46	0.01
SQU-DS	2026-08-07 06:00:00	12.09	25.42	0.41	6.46	9.70	94.36	0.01
SQU-DS	2026-08-07 06:15:00	12.04	25.28	0.41	6.52	9.70	80.63	0.01
SQU-DS	2026-08-07 06:30:00	12.00	25.19	0.41	6.54	9.71	91.86	0.01
SQU-DS	2026-08-07 06:45:00	11.95	25.00	0.40	6.59	9.74	84.10	0.01
SQU-DS	2026-08-07 07:00:00	11.92	24.99	0.40	6.57	9.74	83.50	0.01
SQU-DS	2026-08-07 07:15:00	11.89	24.83	0.41	6.46	9.75	91.43	0.01
SQU-DS	2026-08-07 07:30:00	11.87	24.87	0.41	6.47	9.77	80.72	0.01
SQU-DS	2026-08-07 07:45:00	11.85	24.85	0.41	6.55	9.78	70.93	0.01
SQU-DS	2026-08-07 08:00:00	11.84	24.67	0.41	6.52	9.79	80.75	0.01
SQU-DS	2026-08-07 08:15:00	11.84	24.61	0.40	6.58	9.79	73.69	0.01
SQU-DS	2026-08-07 08:30:00	11.85	24.77	0.41	6.45	9.78	75.66	0.01
SQU-DS	2026-08-07 08:45:00	11.87	24.66	0.40	6.58	9.80	82.60	0.01
SQU-DS	2026-08-07 09:00:00	11.90	24.39	0.40	6.60	9.80	64.36	0.01
SQU-DS	2026-08-07 09:15:00	11.94	24.54	0.41	6.55	9.81	71.23	0.01
SQU-DS	2026-08-07 09:30:00	11.98	24.79	0.40	6.59	9.80	64.94	0.01
SQU-DS	2026-08-07 09:45:00	12.04	24.88	0.41	6.50	9.81	61.05	0.01
SQU-DS	2026-08-07 10:00:00	12.10	24.65	0.40	6.58	9.82	74.66	0.01
SQU-DS	2026-08-07 10:15:00	12.17	24.78	0.40	6.58	9.81	58.29	0.01
SQU-DS	2026-08-07 10:30:00	12.24	24.94	0.40	6.58	9.80	67.17	0.01
SQU-DS	2026-08-07 10:45:00	12.32	25.06	0.40	6.56	9.81	59.87	0.01
SQU-DS	2026-08-07 11:00:00	12.40	24.93	0.41	6.49	9.79	57.73	0.01
SQU-DS	2026-08-07 11:15:00	12.49	24.76	0.40	6.62	9.80	74.04	0.01
SQU-DS	2026-08-07 11:30:00	12.58	25.07	0.40	6.59	9.78	63.07	0.01
SQU-DS	2026-08-07 11:45:00	12.67	25.16	0.40	6.59	9.78	64.01	0.01
SQU-DS	2026-08-07 12:00:00	12.76	25.33	0.40	6.61	9.78	57.23	0.01
SQU-DS	2026-08-07 12:15:00	12.84	25.27	0.40	6.61	9.79	67.35	0.01
SQU-DS	2026-08-07 12:30:00	12.92	25.09	0.40	6.59	9.78	48.80	0.01
SQU-DS	2026-08-07 12:45:00	13.01	25.32	0.39	6.63	9.77	51.58	0.01
SQU-DS	2026-08-07 13:00:00	13.09	25.19	0.40	6.61	9.76	52.20	0.01
SQU-DS	2026-08-07 13:15:00	13.17	25.07	0.40	6.60	9.77	53.34	0.01
SQU-DS	2026-08-07 13:30:00	13.26	25.09	0.40	6.55	9.76	63.50	0.01
SQU-DS	2026-08-07 13:45:00	13.34	25.07	0.39	6.64	9.77	50.54	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-07 14:00:00	13.42	25.39	0.40	6.63	9.76	49.23	0.01
SQU-DS	2026-08-07 14:15:00	13.49	25.51	0.40	6.63	9.76	45.16	0.01
SQU-DS	2026-08-07 14:30:00	13.56	25.50	0.40	6.63	9.76	46.76	0.01
SQU-DS	2026-08-07 14:45:00	13.61	25.66	0.39	6.69	9.74	46.18	0.01
SQU-DS	2026-08-07 15:00:00	13.67	25.71	0.39	6.67	9.74	45.82	0.01
SQU-DS	2026-08-07 15:15:00	13.71	25.72	0.39	6.69	9.74	53.77	0.01
SQU-DS	2026-08-07 15:30:00	13.77	26.00	0.39	6.67	9.73	45.49	0.01
SQU-DS	2026-08-07 15:45:00	13.81	26.16	0.39	6.74	9.71	55.64	0.01
SQU-DS	2026-08-07 16:00:00	13.86	26.25	0.39	6.74	9.72	53.44	0.01
SQU-DS	2026-08-07 16:15:00	13.90	26.47	0.39	6.72	9.70	50.92	0.01
SQU-DS	2026-08-07 16:30:00	13.94	26.85	0.39	6.70	9.68	39.41	0.01
SQU-DS	2026-08-07 16:45:00	13.97	26.83	0.39	6.67	9.67	38.31	0.01
SQU-DS	2026-08-07 17:00:00	13.99	26.93	0.39	6.68	9.66	46.47	0.01
SQU-DS	2026-08-07 17:15:00	14.01	27.24	0.39	6.70	9.64	46.83	0.01
SQU-DS	2026-08-07 17:30:00	14.03	27.52	0.39	6.68	9.61	42.19	0.01
SQU-DS	2026-08-07 17:45:00	14.04	27.75	0.39	6.66	9.61	46.12	0.01
SQU-DS	2026-08-07 18:00:00	14.03	27.80	0.39	6.63	9.59	48.82	0.01
SQU-DS	2026-08-07 18:15:00	14.03	27.90	0.39	6.65	9.57	43.73	0.01
SQU-DS	2026-08-07 18:30:00	14.03	27.84	0.40	6.62	9.55	46.93	0.01
SQU-DS	2026-08-07 18:45:00	14.02	28.07	0.40	6.53	9.53	45.26	0.01
SQU-DS	2026-08-07 19:00:00	14.02	28.00	0.40	6.56	9.52	41.36	0.01
SQU-DS	2026-08-07 19:15:00	14.01	28.00	0.40	6.60	9.52	44.75	0.01
SQU-DS	2026-08-07 19:30:00	13.99	27.66	0.39	6.64	9.50	47.21	0.01
SQU-DS	2026-08-07 19:45:00	13.97	27.99	0.39	6.65	9.48	44.49	0.01
SQU-DS	2026-08-07 20:00:00	13.96	27.76	0.39	6.66	9.47	48.10	0.01
SQU-DS	2026-08-07 20:15:00	13.95	27.58	0.40	6.55	9.45	42.42	0.01
SQU-DS	2026-08-07 20:30:00	13.94	27.83	0.39	6.64	9.43	55.12	0.01
SQU-DS	2026-08-07 20:45:00	13.94	27.64	0.40	6.64	9.43	48.93	0.01
SQU-DS	2026-08-07 21:00:00	13.94	27.53	0.40	6.61	9.41	42.84	0.01
SQU-DS	2026-08-07 21:15:00	13.94	27.56	0.40	6.57	9.40	56.01	0.01
SQU-DS	2026-08-07 21:30:00	13.94	27.61	0.40	6.61	9.37	46.07	0.01
SQU-DS	2026-08-07 21:45:00	13.94	27.23	0.40	6.55	9.36	48.61	0.01
SQU-DS	2026-08-07 22:00:00	13.94	27.16	0.39	6.66	9.32	52.30	0.01
SQU-DS	2026-08-07 22:15:00	13.95	27.20	0.40	6.58	9.29	51.92	0.01
SQU-DS	2026-08-07 22:30:00	13.95	27.32	0.40	6.62	9.26	50.54	0.01
SQU-DS	2026-08-07 22:45:00	13.94	27.19	0.40	6.63	9.11	68.07	0.01
SQU-DS	2026-08-07 23:00:00	13.93	26.90	0.40	6.61	9.28	54.79	0.01
SQU-DS	2026-08-07 23:15:00	13.91	26.92	0.40	6.64	9.27	48.87	0.01
SQU-DS	2026-08-07 23:30:00	13.89	26.88	0.40	6.62	9.26	72.75	0.01
SQU-DS	2026-08-07 23:45:00	13.86	26.91	0.40	6.63	9.27	64.72	0.01
SQU-DS	2026-08-08 00:00:00	13.82	26.63	0.40	6.63	9.27	61.65	0.01
SQU-DS	2026-08-08 00:15:00	13.77	26.46	0.40	6.63	9.27	65.57	0.01
SQU-DS	2026-08-08 00:30:00	13.73	26.58	0.40	6.63	9.27	61.18	0.01
SQU-DS	2026-08-08 00:45:00	13.67	26.45	0.40	6.61	9.30	73.21	0.01
SQU-DS	2026-08-08 01:00:00	13.61	26.35	0.40	6.57	9.30	71.24	0.01
SQU-DS	2026-08-08 01:15:00	13.55	26.50	0.40	6.55	9.31	67.83	0.01
SQU-DS	2026-08-08 01:30:00	13.50	26.62	0.40	6.53	9.31	82.09	0.01
SQU-DS	2026-08-08 01:45:00	13.43	26.41	0.41	6.50	9.34	84.06	0.01
SQU-DS	2026-08-08 02:00:00	13.37	26.29	0.41	6.48	9.35	94.09	0.01
SQU-DS	2026-08-08 02:15:00	13.31	26.20	0.41	6.47	9.37	92.92	0.01
SQU-DS	2026-08-08 02:30:00	13.23	26.11	0.42	6.34	9.39	102.28	0.01
SQU-DS	2026-08-08 02:45:00	13.16	25.72	0.42	6.35	9.42	101.98	0.01
SQU-DS	2026-08-08 03:00:00	13.09	25.47	0.41	6.41	9.45	110.61	0.01
SQU-DS	2026-08-08 03:15:00	13.01	25.25	0.41	6.44	9.51	101.69	0.01
SQU-DS	2026-08-08 03:30:00	12.93	24.99	0.41	6.43	9.53	97.98	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-08 03:45:00	12.86	24.72	0.41	6.49	9.55	97.72	0.01
SQU-DS	2026-08-08 04:00:00	12.79	24.66	0.41	6.44	9.55	105.18	0.01
SQU-DS	2026-08-08 04:15:00	12.71	24.03	0.41	6.38	9.59	100.52	0.01
SQU-DS	2026-08-08 04:30:00	12.64	24.12	0.41	6.43	9.60	92.83	0.01
SQU-DS	2026-08-08 04:45:00	12.58	23.91	0.42	6.34	9.62	108.36	0.01
SQU-DS	2026-08-08 05:00:00	12.51	23.54	0.42	6.34	9.64	112.88	0.01
SQU-DS	2026-08-08 05:15:00	12.46	23.73	0.41	6.44	9.65	88.07	0.01
SQU-DS	2026-08-08 05:30:00	12.40	23.40	0.41	6.43	9.67	102.14	0.01
SQU-DS	2026-08-08 05:45:00	12.34	23.30	0.42	6.39	9.68	113.07	0.01
SQU-DS	2026-08-08 06:00:00	12.29	23.10	0.41	6.42	9.69	108.03	0.01
SQU-DS	2026-08-08 06:15:00	12.25	23.35	0.41	6.49	9.69	93.34	0.01
SQU-DS	2026-08-08 06:30:00	12.21	23.10	0.41	6.42	9.71	108.07	0.01
SQU-DS	2026-08-08 06:45:00	12.17	22.95	0.41	6.43	9.73	99.95	0.01
SQU-DS	2026-08-08 07:00:00	12.15	23.05	0.41	6.46	9.73	127.24	0.01
SQU-DS	2026-08-08 07:15:00	12.13	22.75	0.41	6.49	9.73	105.02	0.01
SQU-DS	2026-08-08 07:30:00	12.12	22.86	0.41	6.40	9.74	107.19	0.01
SQU-DS	2026-08-08 07:45:00	12.12	22.79	0.41	6.49	9.76	100.04	0.01
SQU-DS	2026-08-08 08:00:00	12.12	22.84	0.41	6.40	9.75	87.41	0.01
SQU-DS	2026-08-08 08:15:00	12.13	22.64	0.41	6.48	9.77	93.29	0.01
SQU-DS	2026-08-08 08:30:00	12.15	22.66	0.41	6.47	9.76	83.31	0.01
SQU-DS	2026-08-08 08:45:00	12.17	22.53	0.41	6.46	9.77	85.97	0.01
SQU-DS	2026-08-08 09:00:00	12.20	22.48	0.41	6.43	9.78	96.70	0.01
SQU-DS	2026-08-08 09:15:00	12.21	22.56	0.41	6.46	9.78	126.27	0.01
SQU-DS	2026-08-08 09:30:00	12.26	22.43	0.42	6.29	9.77	77.65	0.01
SQU-DS	2026-08-08 09:45:00	12.29	22.53	0.41	6.44	9.77	89.49	0.01
SQU-DS	2026-08-08 10:00:00	12.32	22.51	0.41	6.42	9.78	97.43	0.01
SQU-DS	2026-08-08 10:15:00	12.37	22.70	0.41	6.42	9.77	93.43	0.01
SQU-DS	2026-08-08 10:30:00	12.43	23.01	0.41	6.42	9.77	78.55	0.01
SQU-DS	2026-08-08 10:45:00	12.51	23.08	0.41	6.40	9.76	115.95	0.01
SQU-DS	2026-08-08 11:00:00	12.58	23.01	0.40	6.45	9.78	84.27	0.01
SQU-DS	2026-08-08 11:15:00	12.65	23.04	0.41	6.40	9.76	94.03	0.01
SQU-DS	2026-08-08 11:30:00	12.72	23.01	0.41	6.24	9.78	106.88	0.01
SQU-DS	2026-08-08 11:45:00	12.79	23.00	0.41	6.37	9.78	70.07	0.01
SQU-DS	2026-08-08 12:00:00	12.84	23.02	0.41	6.29	9.78	104.16	0.01
SQU-DS	2026-08-08 12:15:00	12.91	23.41	0.40	6.38	9.77	104.35	0.01
SQU-DS	2026-08-08 12:30:00	12.99	23.34	0.41	6.31	9.76	65.45	0.01
SQU-DS	2026-08-08 12:45:00	13.06	23.12	0.41	6.30	9.77	83.63	0.01
SQU-DS	2026-08-08 13:00:00	13.12	23.42	0.40	6.39	9.77	86.91	0.01
SQU-DS	2026-08-08 13:15:00	13.19	23.11	0.40	6.38	9.77	77.17	0.01
SQU-DS	2026-08-08 13:30:00	13.25	23.27	0.40	6.39	9.76	79.81	0.01
SQU-DS	2026-08-08 13:45:00	13.31	23.23	0.40	6.39	9.77	79.74	0.01
SQU-DS	2026-08-08 14:00:00	13.37	23.34	0.40	6.39	9.76	72.41	0.01
SQU-DS	2026-08-08 14:15:00	13.42	23.37	0.40	6.37	9.76	68.57	0.01
SQU-DS	2026-08-08 14:30:00	13.47	23.31	0.40	6.42	9.74	62.62	0.01
SQU-DS	2026-08-08 14:45:00	13.51	23.34	0.40	6.42	9.76	76.82	0.01
SQU-DS	2026-08-08 15:00:00	13.56	23.31	0.40	6.39	9.76	67.62	0.01
SQU-DS	2026-08-08 15:15:00	13.60	23.47	0.40	6.41	9.75	59.89	0.01
SQU-DS	2026-08-08 15:30:00	13.65	23.57	0.40	6.41	9.75	61.77	0.01
SQU-DS	2026-08-08 15:45:00	13.69	23.60	0.40	6.40	9.74	69.20	0.01
SQU-DS	2026-08-08 16:00:00	13.72	23.77	0.40	6.42	9.73	52.81	0.01
SQU-DS	2026-08-08 16:15:00	13.76	24.05	0.40	6.40	9.71	68.22	0.01
SQU-DS	2026-08-08 16:30:00	13.79	24.21	0.40	6.41	9.70	55.48	0.01
SQU-DS	2026-08-08 16:45:00	13.82	24.44	0.40	6.42	9.69	58.79	0.01
SQU-DS	2026-08-08 17:00:00	13.85	24.62	0.40	6.41	9.67	47.13	0.01
SQU-DS	2026-08-08 17:15:00	13.86	24.91	0.40	6.41	9.67	59.27	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-08 17:30:00	13.85	25.09	0.40	6.41	9.67	56.71	0.01
SQU-DS	2026-08-08 17:45:00	13.86	25.16	0.41	6.40	9.65	56.36	0.01
SQU-DS	2026-08-08 18:00:00	13.85	25.59	0.41	6.37	9.63	64.86	0.01
SQU-DS	2026-08-08 18:15:00	13.84	25.87	0.41	6.37	9.62	55.83	0.01
SQU-DS	2026-08-08 18:30:00	13.82	25.88	0.41	6.36	9.62	67.77	0.01
SQU-DS	2026-08-08 18:45:00	13.82	26.52	0.41	6.33	9.59	56.85	0.01
SQU-DS	2026-08-08 19:00:00	13.81	26.70	0.42	6.31	9.58	66.12	0.01
SQU-DS	2026-08-08 19:15:00	13.80	26.67	0.42	6.30	9.58	62.96	0.01
SQU-DS	2026-08-08 19:30:00	13.77	26.54	0.42	6.31	9.57	52.92	0.01
SQU-DS	2026-08-08 19:45:00	13.73	26.76	0.42	6.32	9.55	68.16	0.01
SQU-DS	2026-08-08 20:00:00	13.68	26.55	0.42	6.30	9.57	63.40	0.01
SQU-DS	2026-08-08 20:15:00	13.66	26.70	0.42	6.31	9.55	69.54	0.01
SQU-DS	2026-08-08 20:30:00	13.63	26.66	0.42	6.32	9.54	55.15	0.01
SQU-DS	2026-08-08 20:45:00	13.62	26.38	0.42	6.30	9.55	56.60	0.01
SQU-DS	2026-08-08 21:00:00	13.62	26.00	0.42	6.32	9.54	54.68	0.01
SQU-DS	2026-08-08 21:15:00	13.62	25.80	0.42	6.29	9.53	62.21	0.01
SQU-DS	2026-08-08 21:30:00	13.63	25.68	0.42	6.31	9.52	61.67	0.01
SQU-DS	2026-08-08 21:45:00	13.62	25.55	0.43	6.11	9.53	105.70	0.01
SQU-DS	2026-08-08 22:00:00	13.62	25.48	0.42	6.33	9.52	55.05	0.01
SQU-DS	2026-08-08 22:15:00	13.61	25.41	0.42	6.35	9.51	56.82	0.01
SQU-DS	2026-08-08 22:30:00	13.59	25.20	0.42	6.33	9.50	59.24	0.01
SQU-DS	2026-08-08 22:45:00	13.57	25.32	0.42	6.31	9.51	68.30	0.01
SQU-DS	2026-08-08 23:00:00	13.56	25.50	0.42	6.38	9.50	63.15	0.01
SQU-DS	2026-08-08 23:15:00	13.54	25.59	0.42	6.39	9.50	68.45	0.01
SQU-DS	2026-08-08 23:30:00	13.52	25.78	0.42	6.41	9.50	71.61	0.01
SQU-DS	2026-08-08 23:45:00	13.49	26.06	0.42	6.39	9.48	67.49	0.01
SQU-DS	2026-08-09 00:00:00	13.46	26.31	0.42	6.42	9.49	68.58	0.01
SQU-DS	2026-08-09 00:15:00	13.42	26.65	0.42	6.43	9.47	65.00	0.01
SQU-DS	2026-08-09 00:30:00	13.37	26.80	0.42	6.44	9.47	70.12	0.01
SQU-DS	2026-08-09 00:45:00	13.33	27.13	0.42	6.46	9.45	67.81	0.01
SQU-DS	2026-08-09 01:00:00	13.29	27.08	0.42	6.48	9.46	62.45	0.01
SQU-DS	2026-08-09 01:15:00	13.24	27.29	0.42	6.48	9.47	77.85	0.01
SQU-DS	2026-08-09 01:30:00	13.20	27.69	0.42	6.47	9.46	77.43	0.01
SQU-DS	2026-08-09 01:45:00	13.15	27.70	0.42	6.46	9.48	81.02	0.01
SQU-DS	2026-08-09 02:00:00	13.11	27.59	0.42	6.42	9.48	80.44	0.01
SQU-DS	2026-08-09 02:15:00	13.07	27.59	0.43	6.41	9.49	81.39	0.01
SQU-DS	2026-08-09 02:30:00	13.01	27.31	0.43	6.39	9.51	76.19	0.01
SQU-DS	2026-08-09 02:45:00	12.95	27.04	0.43	6.37	9.52	82.09	0.01
SQU-DS	2026-08-09 03:00:00	12.88	26.98	0.43	6.38	9.53	81.20	0.01
SQU-DS	2026-08-09 03:15:00	12.80	26.63	0.43	6.34	9.54	87.92	0.01
SQU-DS	2026-08-09 03:30:00	12.72	26.06	0.43	6.32	9.57	86.63	0.01
SQU-DS	2026-08-09 03:45:00	12.64	25.80	0.44	6.26	9.59	84.41	0.01
SQU-DS	2026-08-09 04:00:00	12.55	25.23	0.44	6.26	9.61	84.93	0.01
SQU-DS	2026-08-09 04:15:00	12.46	24.93	0.43	6.30	9.64	93.82	0.01
SQU-DS	2026-08-09 04:30:00	12.39	24.85	0.43	6.32	9.63	106.73	0.01
SQU-DS	2026-08-09 04:45:00	12.32	24.46	0.43	6.33	9.66	84.53	0.01
SQU-DS	2026-08-09 05:00:00	12.25	24.29	0.44	6.14	9.68	96.06	0.01
SQU-DS	2026-08-09 05:15:00	12.19	24.05	0.44	6.29	9.69	93.34	0.01
SQU-DS	2026-08-09 05:30:00	12.13	23.74	0.43	6.32	9.71	103.01	0.01
SQU-DS	2026-08-09 05:45:00	12.08	23.72	0.43	6.31	9.72	98.05	0.01
SQU-DS	2026-08-09 06:00:00	12.02	23.41	0.43	6.34	9.73	80.39	0.01
SQU-DS	2026-08-09 06:15:00	11.97	23.32	0.43	6.40	9.76	95.45	0.01
SQU-DS	2026-08-09 06:30:00	11.92	23.39	0.43	6.35	9.76	98.32	0.01
SQU-DS	2026-08-09 06:45:00	11.87	23.14	0.43	6.35	9.77	77.21	0.01
SQU-DS	2026-08-09 07:00:00	11.83	23.07	0.43	6.35	9.78	101.22	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-09 07:15:00	11.80	22.77	0.43	6.38	9.80	85.49	0.01
SQU-DS	2026-08-09 07:30:00	11.77	22.89	0.42	6.39	9.80	87.18	0.01
SQU-DS	2026-08-09 07:45:00	11.76	22.88	0.42	6.38	9.81	91.19	0.01
SQU-DS	2026-08-09 08:00:00	11.74	22.77	0.43	6.33	9.83	79.95	0.01
SQU-DS	2026-08-09 08:15:00	11.75	22.71	0.43	6.27	9.83	82.79	0.01
SQU-DS	2026-08-09 08:30:00	11.76	22.82	0.42	6.38	9.85	75.07	0.01
SQU-DS	2026-08-09 08:45:00	11.77	22.86	0.42	6.32	9.84	71.27	0.01
SQU-DS	2026-08-09 09:00:00	11.80	22.77	0.42	6.37	9.84	76.35	0.01
SQU-DS	2026-08-09 09:15:00	11.83	22.81	0.42	6.39	9.85	80.25	0.01
SQU-DS	2026-08-09 09:30:00	11.87	22.81	0.42	6.35	9.86	78.36	0.01
SQU-DS	2026-08-09 09:45:00	11.92	22.69	0.42	6.38	9.86	64.10	0.01
SQU-DS	2026-08-09 10:00:00	11.96	22.70	0.42	6.38	9.87	82.87	0.01
SQU-DS	2026-08-09 10:15:00	11.99	23.04	0.42	6.36	9.86	62.23	0.01
SQU-DS	2026-08-09 10:30:00	12.05	23.07	0.41	6.40	9.85	77.19	0.01
SQU-DS	2026-08-09 10:45:00	12.10	22.79	0.41	6.35	9.87	61.63	0.01
SQU-DS	2026-08-09 11:00:00	12.16	23.25	0.41	6.34	9.86	67.39	0.01
SQU-DS	2026-08-09 11:15:00	12.22	23.62	0.41	6.30	9.86	72.60	0.01
SQU-DS	2026-08-09 11:30:00	12.26	23.26	0.41	6.36	9.87	54.99	0.01
SQU-DS	2026-08-09 11:45:00	12.33	23.37	0.41	6.37	9.86	71.32	0.01
SQU-DS	2026-08-09 12:00:00	12.39	23.64	0.41	6.38	9.85	55.07	0.01
SQU-DS	2026-08-09 12:15:00	12.44	23.57	0.41	6.41	9.86	68.37	0.01
SQU-DS	2026-08-09 12:30:00	12.52	23.47	0.41	6.39	9.86	69.18	0.01
SQU-DS	2026-08-09 12:45:00	12.59	23.72	0.41	6.38	9.85	53.47	0.01
SQU-DS	2026-08-09 13:00:00	12.65	23.96	0.40	6.41	9.85	65.63	0.01
SQU-DS	2026-08-09 13:15:00	12.68	24.17	0.40	6.40	9.86	53.49	0.01
SQU-DS	2026-08-09 13:30:00	12.73	24.16	0.41	6.35	9.84	70.59	0.01
SQU-DS	2026-08-09 13:45:00	12.79	24.28	0.40	6.37	9.85	67.33	0.01
SQU-DS	2026-08-09 14:00:00	12.83	24.09	0.40	6.35	9.84	48.40	0.01
SQU-DS	2026-08-09 14:15:00	12.86	23.77	0.40	6.37	9.85	60.49	0.01
SQU-DS	2026-08-09 14:30:00	12.88	23.67	0.40	6.37	9.86	48.45	0.01
SQU-DS	2026-08-09 14:45:00	12.89	23.83	0.40	6.38	9.86	55.97	0.01
SQU-DS	2026-08-09 15:00:00	12.91	23.80	0.40	6.40	9.85	64.79	0.01
SQU-DS	2026-08-09 15:15:00	12.92	23.85	0.40	6.40	9.85	54.75	0.01
SQU-DS	2026-08-09 15:30:00	12.92	23.91	0.40	6.35	9.86	63.31	0.01
SQU-DS	2026-08-09 15:45:00	12.93	24.05	0.41	6.31	9.86	50.48	0.01
SQU-DS	2026-08-09 16:00:00	12.93	24.02	0.40	6.36	9.85	47.48	0.01
SQU-DS	2026-08-09 16:15:00	12.92	24.14	0.40	6.40	9.87	51.70	0.01
SQU-DS	2026-08-09 16:30:00	12.90	24.35	0.40	6.43	9.86	42.18	0.01
SQU-DS	2026-08-09 16:45:00	12.89	24.49	0.40	6.39	9.86	43.15	0.01
SQU-DS	2026-08-09 17:00:00	12.91	24.89	0.41	6.36	9.85	40.92	0.01
SQU-DS	2026-08-09 17:15:00	12.91	25.05	0.41	6.39	9.84	41.30	0.01
SQU-DS	2026-08-09 17:30:00	12.90	25.26	0.41	6.42	9.84	35.01	0.01
SQU-DS	2026-08-09 17:45:00	12.89	25.62	0.41	6.44	9.82	41.71	0.01
SQU-DS	2026-08-09 18:00:00	12.88	25.94	0.41	6.45	9.80	39.15	0.01
SQU-DS	2026-08-09 18:15:00	12.89	26.34	0.41	6.44	9.78	40.86	0.01
SQU-DS	2026-08-09 18:30:00	12.90	26.30	0.41	6.43	9.77	42.21	0.01
SQU-DS	2026-08-09 18:45:00	12.92	26.55	0.41	6.42	9.77	37.26	0.01
SQU-DS	2026-08-09 19:00:00	12.93	26.55	0.41	6.42	9.75	33.42	0.01
SQU-DS	2026-08-09 19:15:00	12.94	26.51	0.41	6.42	9.75	33.09	0.01
SQU-DS	2026-08-09 19:30:00	12.95	26.81	0.42	6.40	9.73	34.97	0.01
SQU-DS	2026-08-09 19:45:00	12.95	26.85	0.42	6.32	9.72	33.89	0.01
SQU-DS	2026-08-09 20:00:00	12.95	26.94	0.42	6.29	9.70	37.77	0.01
SQU-DS	2026-08-09 20:15:00	12.94	26.54	0.42	6.27	9.71	44.02	0.01
SQU-DS	2026-08-09 20:30:00	12.92	26.77	0.42	6.33	9.70	43.52	0.01
SQU-DS	2026-08-09 20:45:00	12.91	26.64	0.42	6.33	9.69	35.93	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-09 21:00:00	12.90	26.58	0.42	6.37	9.67	43.14	0.01
SQU-DS	2026-08-09 21:15:00	12.90	26.49	0.42	6.34	9.64	45.63	0.01
SQU-DS	2026-08-09 21:30:00	12.91	26.72	0.42	6.32	9.64	54.93	0.01
SQU-DS	2026-08-09 21:45:00	12.92	26.72	0.42	6.33	9.61	51.52	0.01
SQU-DS	2026-08-09 22:00:00	12.94	26.80	0.42	6.36	9.60	51.63	0.01
SQU-DS	2026-08-09 22:15:00	12.96	26.96	0.42	6.36	9.57	48.97	0.01
SQU-DS	2026-08-09 22:30:00	12.98	27.09	0.42	6.35	9.59	46.47	0.01
SQU-DS	2026-08-09 22:45:00	12.99	27.08	0.42	6.41	9.59	55.55	0.01
SQU-DS	2026-08-09 23:00:00	12.99	26.88	0.42	6.39	9.57	47.60	0.01
SQU-DS	2026-08-09 23:15:00	12.98	26.91	0.42	6.40	9.58	55.50	0.01
SQU-DS	2026-08-09 23:30:00	12.97	26.99	0.42	6.44	9.57	53.79	0.01
SQU-DS	2026-08-09 23:45:00	12.95	26.90	0.42	6.43	9.58	47.57	0.01
SQU-US	2026-08-03 00:00:00							
SQU-US	2026-08-03 00:15:00							
SQU-US	2026-08-03 00:30:00							
SQU-US	2026-08-03 00:45:00							
SQU-US	2026-08-03 01:00:00							
SQU-US	2026-08-03 01:15:00							
SQU-US	2026-08-03 01:30:00							
SQU-US	2026-08-03 01:45:00							
SQU-US	2026-08-03 02:00:00							
SQU-US	2026-08-03 02:15:00							
SQU-US	2026-08-03 02:30:00							
SQU-US	2026-08-03 02:45:00							
SQU-US	2026-08-03 03:00:00							
SQU-US	2026-08-03 03:15:00							
SQU-US	2026-08-03 03:30:00							
SQU-US	2026-08-03 03:45:00							
SQU-US	2026-08-03 04:00:00							
SQU-US	2026-08-03 04:15:00							
SQU-US	2026-08-03 04:30:00							
SQU-US	2026-08-03 04:45:00							
SQU-US	2026-08-03 05:00:00							
SQU-US	2026-08-03 05:15:00							
SQU-US	2026-08-03 05:30:00							
SQU-US	2026-08-03 05:45:00							
SQU-US	2026-08-03 06:00:00							
SQU-US	2026-08-03 06:15:00							
SQU-US	2026-08-03 06:30:00							
SQU-US	2026-08-03 06:45:00							
SQU-US	2026-08-03 07:00:00							
SQU-US	2026-08-03 07:15:00							
SQU-US	2026-08-03 07:30:00							
SQU-US	2026-08-03 07:45:00							
SQU-US	2026-08-03 08:00:00							
SQU-US	2026-08-03 08:15:00							
SQU-US	2026-08-03 08:30:00							
SQU-US	2026-08-03 08:45:00							
SQU-US	2026-08-03 09:00:00							
SQU-US	2026-08-03 09:15:00							
SQU-US	2026-08-03 09:30:00							
SQU-US	2026-08-03 09:45:00							
SQU-US	2026-08-03 10:00:00							
SQU-US	2026-08-03 10:15:00							
SQU-US	2026-08-03 10:30:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-03 10:45:00							
SQU-US	2026-08-03 11:00:00							
SQU-US	2026-08-03 11:15:00							
SQU-US	2026-08-03 11:30:00							
SQU-US	2026-08-03 11:45:00							
SQU-US	2026-08-03 12:00:00							
SQU-US	2026-08-03 12:15:00							
SQU-US	2026-08-03 12:30:00							
SQU-US	2026-08-03 12:45:00							
SQU-US	2026-08-03 13:00:00							
SQU-US	2026-08-03 13:15:00							
SQU-US	2026-08-03 13:30:00							
SQU-US	2026-08-03 13:45:00							
SQU-US	2026-08-03 14:00:00							
SQU-US	2026-08-03 14:15:00							
SQU-US	2026-08-03 14:30:00							
SQU-US	2026-08-03 14:45:00							
SQU-US	2026-08-03 15:00:00							
SQU-US	2026-08-03 15:15:00							
SQU-US	2026-08-03 15:30:00							
SQU-US	2026-08-03 15:45:00							
SQU-US	2026-08-03 16:00:00							
SQU-US	2026-08-03 16:15:00							
SQU-US	2026-08-03 16:30:00							
SQU-US	2026-08-03 16:45:00							
SQU-US	2026-08-03 17:00:00							
SQU-US	2026-08-03 17:15:00							
SQU-US	2026-08-03 17:30:00							
SQU-US	2026-08-03 17:45:00							
SQU-US	2026-08-03 18:00:00							
SQU-US	2026-08-03 18:15:00							
SQU-US	2026-08-03 18:30:00							
SQU-US	2026-08-03 18:45:00							
SQU-US	2026-08-03 19:00:00							
SQU-US	2026-08-03 19:15:00							
SQU-US	2026-08-03 19:30:00							
SQU-US	2026-08-03 19:45:00							
SQU-US	2026-08-03 20:00:00							
SQU-US	2026-08-03 20:15:00							
SQU-US	2026-08-03 20:30:00							
SQU-US	2026-08-03 20:45:00							
SQU-US	2026-08-03 21:00:00							
SQU-US	2026-08-03 21:15:00							
SQU-US	2026-08-03 21:30:00							
SQU-US	2026-08-03 21:45:00							
SQU-US	2026-08-03 22:00:00							
SQU-US	2026-08-03 22:15:00							
SQU-US	2026-08-03 22:30:00							
SQU-US	2026-08-03 22:45:00							
SQU-US	2026-08-03 23:00:00							
SQU-US	2026-08-03 23:15:00							
SQU-US	2026-08-03 23:30:00							
SQU-US	2026-08-03 23:45:00							
SQU-US	2026-08-04 00:00:00							
SQU-US	2026-08-04 00:15:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-04 00:30:00							
SQU-US	2026-08-04 00:45:00							
SQU-US	2026-08-04 01:00:00							
SQU-US	2026-08-04 01:15:00							
SQU-US	2026-08-04 01:30:00							
SQU-US	2026-08-04 01:45:00							
SQU-US	2026-08-04 02:00:00							
SQU-US	2026-08-04 02:15:00							
SQU-US	2026-08-04 02:30:00							
SQU-US	2026-08-04 02:45:00							
SQU-US	2026-08-04 03:00:00							
SQU-US	2026-08-04 03:15:00							
SQU-US	2026-08-04 03:30:00							
SQU-US	2026-08-04 03:45:00							
SQU-US	2026-08-04 04:00:00							
SQU-US	2026-08-04 04:15:00							
SQU-US	2026-08-04 04:30:00							
SQU-US	2026-08-04 04:45:00							
SQU-US	2026-08-04 05:00:00							
SQU-US	2026-08-04 05:15:00							
SQU-US	2026-08-04 05:30:00							
SQU-US	2026-08-04 05:45:00							
SQU-US	2026-08-04 06:00:00							
SQU-US	2026-08-04 06:15:00							
SQU-US	2026-08-04 06:30:00							
SQU-US	2026-08-04 06:45:00							
SQU-US	2026-08-04 07:00:00							
SQU-US	2026-08-04 07:15:00							
SQU-US	2026-08-04 07:30:00							
SQU-US	2026-08-04 07:45:00							
SQU-US	2026-08-04 08:00:00							
SQU-US	2026-08-04 08:15:00							
SQU-US	2026-08-04 08:30:00							
SQU-US	2026-08-04 08:45:00							
SQU-US	2026-08-04 09:00:00							
SQU-US	2026-08-04 09:15:00							
SQU-US	2026-08-04 09:30:00							
SQU-US	2026-08-04 09:45:00							
SQU-US	2026-08-04 10:00:00							
SQU-US	2026-08-04 10:15:00							
SQU-US	2026-08-04 10:30:00							
SQU-US	2026-08-04 10:45:00							
SQU-US	2026-08-04 11:00:00							
SQU-US	2026-08-04 11:15:00							
SQU-US	2026-08-04 11:30:00							
SQU-US	2026-08-04 11:45:00							
SQU-US	2026-08-04 12:00:00							
SQU-US	2026-08-04 12:15:00							
SQU-US	2026-08-04 12:30:00							
SQU-US	2026-08-04 12:45:00							
SQU-US	2026-08-04 13:00:00							
SQU-US	2026-08-04 13:15:00							
SQU-US	2026-08-04 13:30:00							
SQU-US	2026-08-04 13:45:00							
SQU-US	2026-08-04 14:00:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-04 14:15:00							
SQU-US	2026-08-04 14:30:00							
SQU-US	2026-08-04 14:45:00							
SQU-US	2026-08-04 15:00:00							
SQU-US	2026-08-04 15:15:00							
SQU-US	2026-08-04 15:30:00							
SQU-US	2026-08-04 15:45:00							
SQU-US	2026-08-04 16:00:00							
SQU-US	2026-08-04 16:15:00							
SQU-US	2026-08-04 16:30:00							
SQU-US	2026-08-04 16:45:00							
SQU-US	2026-08-04 17:00:00							
SQU-US	2026-08-04 17:15:00							
SQU-US	2026-08-04 17:30:00							
SQU-US	2026-08-04 17:45:00							
SQU-US	2026-08-04 18:00:00							
SQU-US	2026-08-04 18:15:00							
SQU-US	2026-08-04 18:30:00							
SQU-US	2026-08-04 18:45:00							
SQU-US	2026-08-04 19:00:00							
SQU-US	2026-08-04 19:15:00							
SQU-US	2026-08-04 19:30:00							
SQU-US	2026-08-04 19:45:00							
SQU-US	2026-08-04 20:00:00							
SQU-US	2026-08-04 20:15:00							
SQU-US	2026-08-04 20:30:00							
SQU-US	2026-08-04 20:45:00							
SQU-US	2026-08-04 21:00:00							
SQU-US	2026-08-04 21:15:00							
SQU-US	2026-08-04 21:30:00							
SQU-US	2026-08-04 21:45:00							
SQU-US	2026-08-04 22:00:00							
SQU-US	2026-08-04 22:15:00							
SQU-US	2026-08-04 22:30:00							
SQU-US	2026-08-04 22:45:00							
SQU-US	2026-08-04 23:00:00							
SQU-US	2026-08-04 23:15:00							
SQU-US	2026-08-04 23:30:00							
SQU-US	2026-08-04 23:45:00							
SQU-US	2026-08-05 00:00:00							
SQU-US	2026-08-05 00:15:00							
SQU-US	2026-08-05 00:30:00							
SQU-US	2026-08-05 00:45:00							
SQU-US	2026-08-05 01:00:00							
SQU-US	2026-08-05 01:15:00							
SQU-US	2026-08-05 01:30:00							
SQU-US	2026-08-05 01:45:00							
SQU-US	2026-08-05 02:00:00							
SQU-US	2026-08-05 02:15:00							
SQU-US	2026-08-05 02:30:00							
SQU-US	2026-08-05 02:45:00							
SQU-US	2026-08-05 03:00:00							
SQU-US	2026-08-05 03:15:00							
SQU-US	2026-08-05 03:30:00							
SQU-US	2026-08-05 03:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-05 04:00:00							
SQU-US	2026-08-05 04:15:00							
SQU-US	2026-08-05 04:30:00							
SQU-US	2026-08-05 04:45:00							
SQU-US	2026-08-05 05:00:00							
SQU-US	2026-08-05 05:15:00							
SQU-US	2026-08-05 05:30:00							
SQU-US	2026-08-05 05:45:00							
SQU-US	2026-08-05 06:00:00							
SQU-US	2026-08-05 06:15:00							
SQU-US	2026-08-05 06:30:00							
SQU-US	2026-08-05 06:45:00							
SQU-US	2026-08-05 07:00:00							
SQU-US	2026-08-05 07:15:00							
SQU-US	2026-08-05 07:30:00							
SQU-US	2026-08-05 07:45:00							
SQU-US	2026-08-05 08:00:00							
SQU-US	2026-08-05 08:15:00							
SQU-US	2026-08-05 08:30:00							
SQU-US	2026-08-05 08:45:00							
SQU-US	2026-08-05 09:00:00							
SQU-US	2026-08-05 09:15:00							
SQU-US	2026-08-05 09:30:00							
SQU-US	2026-08-05 09:45:00							
SQU-US	2026-08-05 10:00:00							
SQU-US	2026-08-05 10:15:00							
SQU-US	2026-08-05 10:30:00							
SQU-US	2026-08-05 10:45:00							
SQU-US	2026-08-05 11:00:00							
SQU-US	2026-08-05 11:15:00							
SQU-US	2026-08-05 11:30:00							
SQU-US	2026-08-05 11:45:00							
SQU-US	2026-08-05 12:00:00							
SQU-US	2026-08-05 12:15:00							
SQU-US	2026-08-05 12:30:00							
SQU-US	2026-08-05 12:45:00							
SQU-US	2026-08-05 13:00:00							
SQU-US	2026-08-05 13:15:00							
SQU-US	2026-08-05 13:30:00							
SQU-US	2026-08-05 13:45:00							
SQU-US	2026-08-05 14:00:00							
SQU-US	2026-08-05 14:15:00							
SQU-US	2026-08-05 14:30:00							
SQU-US	2026-08-05 14:45:00							
SQU-US	2026-08-05 15:00:00							
SQU-US	2026-08-05 15:15:00							
SQU-US	2026-08-05 15:30:00							
SQU-US	2026-08-05 15:45:00							
SQU-US	2026-08-05 16:00:00							
SQU-US	2026-08-05 16:15:00							
SQU-US	2026-08-05 16:30:00							
SQU-US	2026-08-05 16:45:00							
SQU-US	2026-08-05 17:00:00							
SQU-US	2026-08-05 17:15:00							
SQU-US	2026-08-05 17:30:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-05 17:45:00							
SQU-US	2026-08-05 18:00:00							
SQU-US	2026-08-05 18:15:00							
SQU-US	2026-08-05 18:30:00							
SQU-US	2026-08-05 18:45:00							
SQU-US	2026-08-05 19:00:00							
SQU-US	2026-08-05 19:15:00							
SQU-US	2026-08-05 19:30:00							
SQU-US	2026-08-05 19:45:00							
SQU-US	2026-08-05 20:00:00							
SQU-US	2026-08-05 20:15:00							
SQU-US	2026-08-05 20:30:00							
SQU-US	2026-08-05 20:45:00							
SQU-US	2026-08-05 21:00:00							
SQU-US	2026-08-05 21:15:00							
SQU-US	2026-08-05 21:30:00							
SQU-US	2026-08-05 21:45:00							
SQU-US	2026-08-05 22:00:00							
SQU-US	2026-08-05 22:15:00							
SQU-US	2026-08-05 22:30:00							
SQU-US	2026-08-05 22:45:00							
SQU-US	2026-08-05 23:00:00							
SQU-US	2026-08-05 23:15:00							
SQU-US	2026-08-05 23:30:00							
SQU-US	2026-08-05 23:45:00							
SQU-US	2026-08-06 00:00:00							
SQU-US	2026-08-06 00:15:00							
SQU-US	2026-08-06 00:30:00							
SQU-US	2026-08-06 00:45:00							
SQU-US	2026-08-06 01:00:00							
SQU-US	2026-08-06 01:15:00							
SQU-US	2026-08-06 01:30:00							
SQU-US	2026-08-06 01:45:00							
SQU-US	2026-08-06 02:00:00							
SQU-US	2026-08-06 02:15:00							
SQU-US	2026-08-06 02:30:00							
SQU-US	2026-08-06 02:45:00							
SQU-US	2026-08-06 03:00:00							
SQU-US	2026-08-06 03:15:00							
SQU-US	2026-08-06 03:30:00							
SQU-US	2026-08-06 03:45:00							
SQU-US	2026-08-06 04:00:00							
SQU-US	2026-08-06 04:15:00							
SQU-US	2026-08-06 04:30:00							
SQU-US	2026-08-06 04:45:00							
SQU-US	2026-08-06 05:00:00							
SQU-US	2026-08-06 05:15:00							
SQU-US	2026-08-06 05:30:00							
SQU-US	2026-08-06 05:45:00							
SQU-US	2026-08-06 06:00:00							
SQU-US	2026-08-06 06:15:00							
SQU-US	2026-08-06 06:30:00							
SQU-US	2026-08-06 06:45:00							
SQU-US	2026-08-06 07:00:00							
SQU-US	2026-08-06 07:15:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-06 07:30:00							
SQU-US	2026-08-06 07:45:00							
SQU-US	2026-08-06 08:00:00							
SQU-US	2026-08-06 08:15:00							
SQU-US	2026-08-06 08:30:00							
SQU-US	2026-08-06 08:45:00							
SQU-US	2026-08-06 09:00:00							
SQU-US	2026-08-06 09:15:00							
SQU-US	2026-08-06 09:30:00							
SQU-US	2026-08-06 09:45:00							
SQU-US	2026-08-06 10:00:00							
SQU-US	2026-08-06 10:15:00							
SQU-US	2026-08-06 10:30:00							
SQU-US	2026-08-06 10:45:00							
SQU-US	2026-08-06 11:00:00							
SQU-US	2026-08-06 11:15:00							
SQU-US	2026-08-06 11:30:00							
SQU-US	2026-08-06 11:45:00							
SQU-US	2026-08-06 12:00:00							
SQU-US	2026-08-06 12:15:00							
SQU-US	2026-08-06 12:30:00							
SQU-US	2026-08-06 12:45:00							
SQU-US	2026-08-06 13:00:00							
SQU-US	2026-08-06 13:15:00							
SQU-US	2026-08-06 13:30:00							
SQU-US	2026-08-06 13:45:00							
SQU-US	2026-08-06 14:00:00							
SQU-US	2026-08-06 14:15:00							
SQU-US	2026-08-06 14:30:00							
SQU-US	2026-08-06 14:45:00							
SQU-US	2026-08-06 15:00:00							
SQU-US	2026-08-06 15:15:00							
SQU-US	2026-08-06 15:30:00							
SQU-US	2026-08-06 15:45:00							
SQU-US	2026-08-06 16:00:00							
SQU-US	2026-08-06 16:15:00							
SQU-US	2026-08-06 16:30:00							
SQU-US	2026-08-06 16:45:00							
SQU-US	2026-08-06 17:00:00							
SQU-US	2026-08-06 17:15:00							
SQU-US	2026-08-06 17:30:00							
SQU-US	2026-08-06 17:45:00							
SQU-US	2026-08-06 18:00:00							
SQU-US	2026-08-06 18:15:00							
SQU-US	2026-08-06 18:30:00							
SQU-US	2026-08-06 18:45:00							
SQU-US	2026-08-06 19:00:00							
SQU-US	2026-08-06 19:15:00							
SQU-US	2026-08-06 19:30:00							
SQU-US	2026-08-06 19:45:00							
SQU-US	2026-08-06 20:00:00							
SQU-US	2026-08-06 20:15:00							
SQU-US	2026-08-06 20:30:00							
SQU-US	2026-08-06 20:45:00							
SQU-US	2026-08-06 21:00:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-06 21:15:00							
SQU-US	2026-08-06 21:30:00							
SQU-US	2026-08-06 21:45:00							
SQU-US	2026-08-06 22:00:00							
SQU-US	2026-08-06 22:15:00							
SQU-US	2026-08-06 22:30:00							
SQU-US	2026-08-06 22:45:00							
SQU-US	2026-08-06 23:00:00							
SQU-US	2026-08-06 23:15:00							
SQU-US	2026-08-06 23:30:00							
SQU-US	2026-08-06 23:45:00							
SQU-US	2026-08-07 00:00:00							
SQU-US	2026-08-07 00:15:00							
SQU-US	2026-08-07 00:30:00							
SQU-US	2026-08-07 00:45:00							
SQU-US	2026-08-07 01:00:00							
SQU-US	2026-08-07 01:15:00							
SQU-US	2026-08-07 01:30:00							
SQU-US	2026-08-07 01:45:00							
SQU-US	2026-08-07 02:00:00							
SQU-US	2026-08-07 02:15:00							
SQU-US	2026-08-07 02:30:00							
SQU-US	2026-08-07 02:45:00							
SQU-US	2026-08-07 03:00:00							
SQU-US	2026-08-07 03:15:00							
SQU-US	2026-08-07 03:30:00							
SQU-US	2026-08-07 03:45:00							
SQU-US	2026-08-07 04:00:00							
SQU-US	2026-08-07 04:15:00							
SQU-US	2026-08-07 04:30:00							
SQU-US	2026-08-07 04:45:00							
SQU-US	2026-08-07 05:00:00							
SQU-US	2026-08-07 05:15:00							
SQU-US	2026-08-07 05:30:00							
SQU-US	2026-08-07 05:45:00							
SQU-US	2026-08-07 06:00:00							
SQU-US	2026-08-07 06:15:00							
SQU-US	2026-08-07 06:30:00							
SQU-US	2026-08-07 06:45:00							
SQU-US	2026-08-07 07:00:00							
SQU-US	2026-08-07 07:15:00							
SQU-US	2026-08-07 07:30:00							
SQU-US	2026-08-07 07:45:00							
SQU-US	2026-08-07 08:00:00							
SQU-US	2026-08-07 08:15:00							
SQU-US	2026-08-07 08:30:00							
SQU-US	2026-08-07 08:45:00							
SQU-US	2026-08-07 09:00:00							
SQU-US	2026-08-07 09:15:00							
SQU-US	2026-08-07 09:30:00							
SQU-US	2026-08-07 09:45:00							
SQU-US	2026-08-07 10:00:00							
SQU-US	2026-08-07 10:15:00							
SQU-US	2026-08-07 10:30:00							
SQU-US	2026-08-07 10:45:00							


Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-07 11:00:00							
SQU-US	2026-08-07 11:15:00							
SQU-US	2026-08-07 11:30:00							
SQU-US	2026-08-07 11:45:00							
SQU-US	2026-08-07 12:00:00							
SQU-US	2026-08-07 12:15:00							
SQU-US	2026-08-07 12:30:00							
SQU-US	2026-08-07 12:45:00							
SQU-US	2026-08-07 13:00:00							
SQU-US	2026-08-07 13:15:00							
SQU-US	2026-08-07 13:30:00							
SQU-US	2026-08-07 13:45:00							
SQU-US	2026-08-07 14:00:00							
SQU-US	2026-08-07 14:15:00							
SQU-US	2026-08-07 14:30:00							
SQU-US	2026-08-07 14:45:00							
SQU-US	2026-08-07 15:00:00							
SQU-US	2026-08-07 15:15:00							
SQU-US	2026-08-07 15:30:00							
SQU-US	2026-08-07 15:45:00							
SQU-US	2026-08-07 16:00:00							
SQU-US	2026-08-07 16:15:00							
SQU-US	2026-08-07 16:30:00							
SQU-US	2026-08-07 16:45:00							
SQU-US	2026-08-07 17:00:00							
SQU-US	2026-08-07 17:15:00							
SQU-US	2026-08-07 17:30:00							
SQU-US	2026-08-07 17:45:00							
SQU-US	2026-08-07 18:00:00							
SQU-US	2026-08-07 18:15:00							
SQU-US	2026-08-07 18:30:00							
SQU-US	2026-08-07 18:45:00							
SQU-US	2026-08-07 19:00:00							
SQU-US	2026-08-07 19:15:00							
SQU-US	2026-08-07 19:30:00							
SQU-US	2026-08-07 19:45:00							
SQU-US	2026-08-07 20:00:00							
SQU-US	2026-08-07 20:15:00							
SQU-US	2026-08-07 20:30:00							
SQU-US	2026-08-07 20:45:00							
SQU-US	2026-08-07 21:00:00							
SQU-US	2026-08-07 21:15:00							
SQU-US	2026-08-07 21:30:00							
SQU-US	2026-08-07 21:45:00							
SQU-US	2026-08-07 22:00:00							
SQU-US	2026-08-07 22:15:00							
SQU-US	2026-08-07 22:30:00							
SQU-US	2026-08-07 22:45:00							
SQU-US	2026-08-07 23:00:00							
SQU-US	2026-08-07 23:15:00							
SQU-US	2026-08-07 23:30:00							
SQU-US	2026-08-07 23:45:00							
SQU-US	2026-08-08 00:00:00							
SQU-US	2026-08-08 00:15:00							
SQU-US	2026-08-08 00:30:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-08 00:45:00							
SQU-US	2026-08-08 01:00:00							
SQU-US	2026-08-08 01:15:00							
SQU-US	2026-08-08 01:30:00							
SQU-US	2026-08-08 01:45:00							
SQU-US	2026-08-08 02:00:00							
SQU-US	2026-08-08 02:15:00							
SQU-US	2026-08-08 02:30:00							
SQU-US	2026-08-08 02:45:00							
SQU-US	2026-08-08 03:00:00							
SQU-US	2026-08-08 03:15:00							
SQU-US	2026-08-08 03:30:00							
SQU-US	2026-08-08 03:45:00							
SQU-US	2026-08-08 04:00:00							
SQU-US	2026-08-08 04:15:00							
SQU-US	2026-08-08 04:30:00							
SQU-US	2026-08-08 04:45:00							
SQU-US	2026-08-08 05:00:00							
SQU-US	2026-08-08 05:15:00							
SQU-US	2026-08-08 05:30:00							
SQU-US	2026-08-08 05:45:00							
SQU-US	2026-08-08 06:00:00							
SQU-US	2026-08-08 06:15:00							
SQU-US	2026-08-08 06:30:00							
SQU-US	2026-08-08 06:45:00							
SQU-US	2026-08-08 07:00:00							
SQU-US	2026-08-08 07:15:00							
SQU-US	2026-08-08 07:30:00							
SQU-US	2026-08-08 07:45:00							
SQU-US	2026-08-08 08:00:00							
SQU-US	2026-08-08 08:15:00							
SQU-US	2026-08-08 08:30:00							
SQU-US	2026-08-08 08:45:00							
SQU-US	2026-08-08 09:00:00							
SQU-US	2026-08-08 09:15:00							
SQU-US	2026-08-08 09:30:00							
SQU-US	2026-08-08 09:45:00							
SQU-US	2026-08-08 10:00:00							
SQU-US	2026-08-08 10:15:00							
SQU-US	2026-08-08 10:30:00							
SQU-US	2026-08-08 10:45:00							
SQU-US	2026-08-08 11:00:00							
SQU-US	2026-08-08 11:15:00							
SQU-US	2026-08-08 11:30:00							
SQU-US	2026-08-08 11:45:00							
SQU-US	2026-08-08 12:00:00							
SQU-US	2026-08-08 12:15:00							
SQU-US	2026-08-08 12:30:00							
SQU-US	2026-08-08 12:45:00							
SQU-US	2026-08-08 13:00:00							
SQU-US	2026-08-08 13:15:00							
SQU-US	2026-08-08 13:30:00							
SQU-US	2026-08-08 13:45:00							
SQU-US	2026-08-08 14:00:00							
SQU-US	2026-08-08 14:15:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-08 14:30:00							
SQU-US	2026-08-08 14:45:00							
SQU-US	2026-08-08 15:00:00							
SQU-US	2026-08-08 15:15:00							
SQU-US	2026-08-08 15:30:00							
SQU-US	2026-08-08 15:45:00							
SQU-US	2026-08-08 16:00:00							
SQU-US	2026-08-08 16:15:00							
SQU-US	2026-08-08 16:30:00							
SQU-US	2026-08-08 16:45:00							
SQU-US	2026-08-08 17:00:00							
SQU-US	2026-08-08 17:15:00							
SQU-US	2026-08-08 17:30:00							
SQU-US	2026-08-08 17:45:00							
SQU-US	2026-08-08 18:00:00							
SQU-US	2026-08-08 18:15:00							
SQU-US	2026-08-08 18:30:00							
SQU-US	2026-08-08 18:45:00							
SQU-US	2026-08-08 19:00:00							
SQU-US	2026-08-08 19:15:00							
SQU-US	2026-08-08 19:30:00							
SQU-US	2026-08-08 19:45:00							
SQU-US	2026-08-08 20:00:00							
SQU-US	2026-08-08 20:15:00							
SQU-US	2026-08-08 20:30:00							
SQU-US	2026-08-08 20:45:00							
SQU-US	2026-08-08 21:00:00							
SQU-US	2026-08-08 21:15:00							
SQU-US	2026-08-08 21:30:00							
SQU-US	2026-08-08 21:45:00							
SQU-US	2026-08-08 22:00:00							
SQU-US	2026-08-08 22:15:00							
SQU-US	2026-08-08 22:30:00							
SQU-US	2026-08-08 22:45:00							
SQU-US	2026-08-08 23:00:00							
SQU-US	2026-08-08 23:15:00							
SQU-US	2026-08-08 23:30:00							
SQU-US	2026-08-08 23:45:00							
SQU-US	2026-08-09 00:00:00							
SQU-US	2026-08-09 00:15:00							
SQU-US	2026-08-09 00:30:00							
SQU-US	2026-08-09 00:45:00							
SQU-US	2026-08-09 01:00:00							
SQU-US	2026-08-09 01:15:00							
SQU-US	2026-08-09 01:30:00							
SQU-US	2026-08-09 01:45:00							
SQU-US	2026-08-09 02:00:00							
SQU-US	2026-08-09 02:15:00							
SQU-US	2026-08-09 02:30:00							
SQU-US	2026-08-09 02:45:00							
SQU-US	2026-08-09 03:00:00							
SQU-US	2026-08-09 03:15:00							
SQU-US	2026-08-09 03:30:00							
SQU-US	2026-08-09 03:45:00							
SQU-US	2026-08-09 04:00:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-09 04:15:00							
SQU-US	2026-08-09 04:30:00							
SQU-US	2026-08-09 04:45:00							
SQU-US	2026-08-09 05:00:00							
SQU-US	2026-08-09 05:15:00							
SQU-US	2026-08-09 05:30:00							
SQU-US	2026-08-09 05:45:00							
SQU-US	2026-08-09 06:00:00							
SQU-US	2026-08-09 06:15:00							
SQU-US	2026-08-09 06:30:00							
SQU-US	2026-08-09 06:45:00							
SQU-US	2026-08-09 07:00:00							
SQU-US	2026-08-09 07:15:00							
SQU-US	2026-08-09 07:30:00							
SQU-US	2026-08-09 07:45:00							
SQU-US	2026-08-09 08:00:00							
SQU-US	2026-08-09 08:15:00							
SQU-US	2026-08-09 08:30:00							
SQU-US	2026-08-09 08:45:00							
SQU-US	2026-08-09 09:00:00							
SQU-US	2026-08-09 09:15:00							
SQU-US	2026-08-09 09:30:00							
SQU-US	2026-08-09 09:45:00							
SQU-US	2026-08-09 10:00:00							
SQU-US	2026-08-09 10:15:00							
SQU-US	2026-08-09 10:30:00							
SQU-US	2026-08-09 10:45:00							
SQU-US	2026-08-09 11:00:00							
SQU-US	2026-08-09 11:15:00							
SQU-US	2026-08-09 11:30:00							
SQU-US	2026-08-09 11:45:00							
SQU-US	2026-08-09 12:00:00							
SQU-US	2026-08-09 12:15:00							
SQU-US	2026-08-09 12:30:00							
SQU-US	2026-08-09 12:45:00							
SQU-US	2026-08-09 13:00:00							
SQU-US	2026-08-09 13:15:00							
SQU-US	2026-08-09 13:30:00							
SQU-US	2026-08-09 13:45:00							
SQU-US	2026-08-09 14:00:00							
SQU-US	2026-08-09 14:15:00							
SQU-US	2026-08-09 14:30:00							
SQU-US	2026-08-09 14:45:00							
SQU-US	2026-08-09 15:00:00							
SQU-US	2026-08-09 15:15:00							
SQU-US	2026-08-09 15:30:00							
SQU-US	2026-08-09 15:45:00							
SQU-US	2026-08-09 16:00:00							
SQU-US	2026-08-09 16:15:00							
SQU-US	2026-08-09 16:30:00							
SQU-US	2026-08-09 16:45:00							
SQU-US	2026-08-09 17:00:00							
SQU-US	2026-08-09 17:15:00							
SQU-US	2026-08-09 17:30:00							
SQU-US	2026-08-09 17:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-09 18:00:00							
SQU-US	2026-08-09 18:15:00							
SQU-US	2026-08-09 18:30:00							
SQU-US	2026-08-09 18:45:00							
SQU-US	2026-08-09 19:00:00							
SQU-US	2026-08-09 19:15:00							
SQU-US	2026-08-09 19:30:00							
SQU-US	2026-08-09 19:45:00							
SQU-US	2026-08-09 20:00:00							
SQU-US	2026-08-09 20:15:00							
SQU-US	2026-08-09 20:30:00							
SQU-US	2026-08-09 20:45:00							
SQU-US	2026-08-09 21:00:00							
SQU-US	2026-08-09 21:15:00							
SQU-US	2026-08-09 21:30:00							
SQU-US	2026-08-09 21:45:00							
SQU-US	2026-08-09 22:00:00							
SQU-US	2026-08-09 22:15:00							
SQU-US	2026-08-09 22:30:00							
SQU-US	2026-08-09 22:45:00							
SQU-US	2026-08-09 23:00:00							
SQU-US	2026-08-09 23:15:00							
SQU-US	2026-08-09 23:30:00							
SQU-US	2026-08-09 23:45:00							

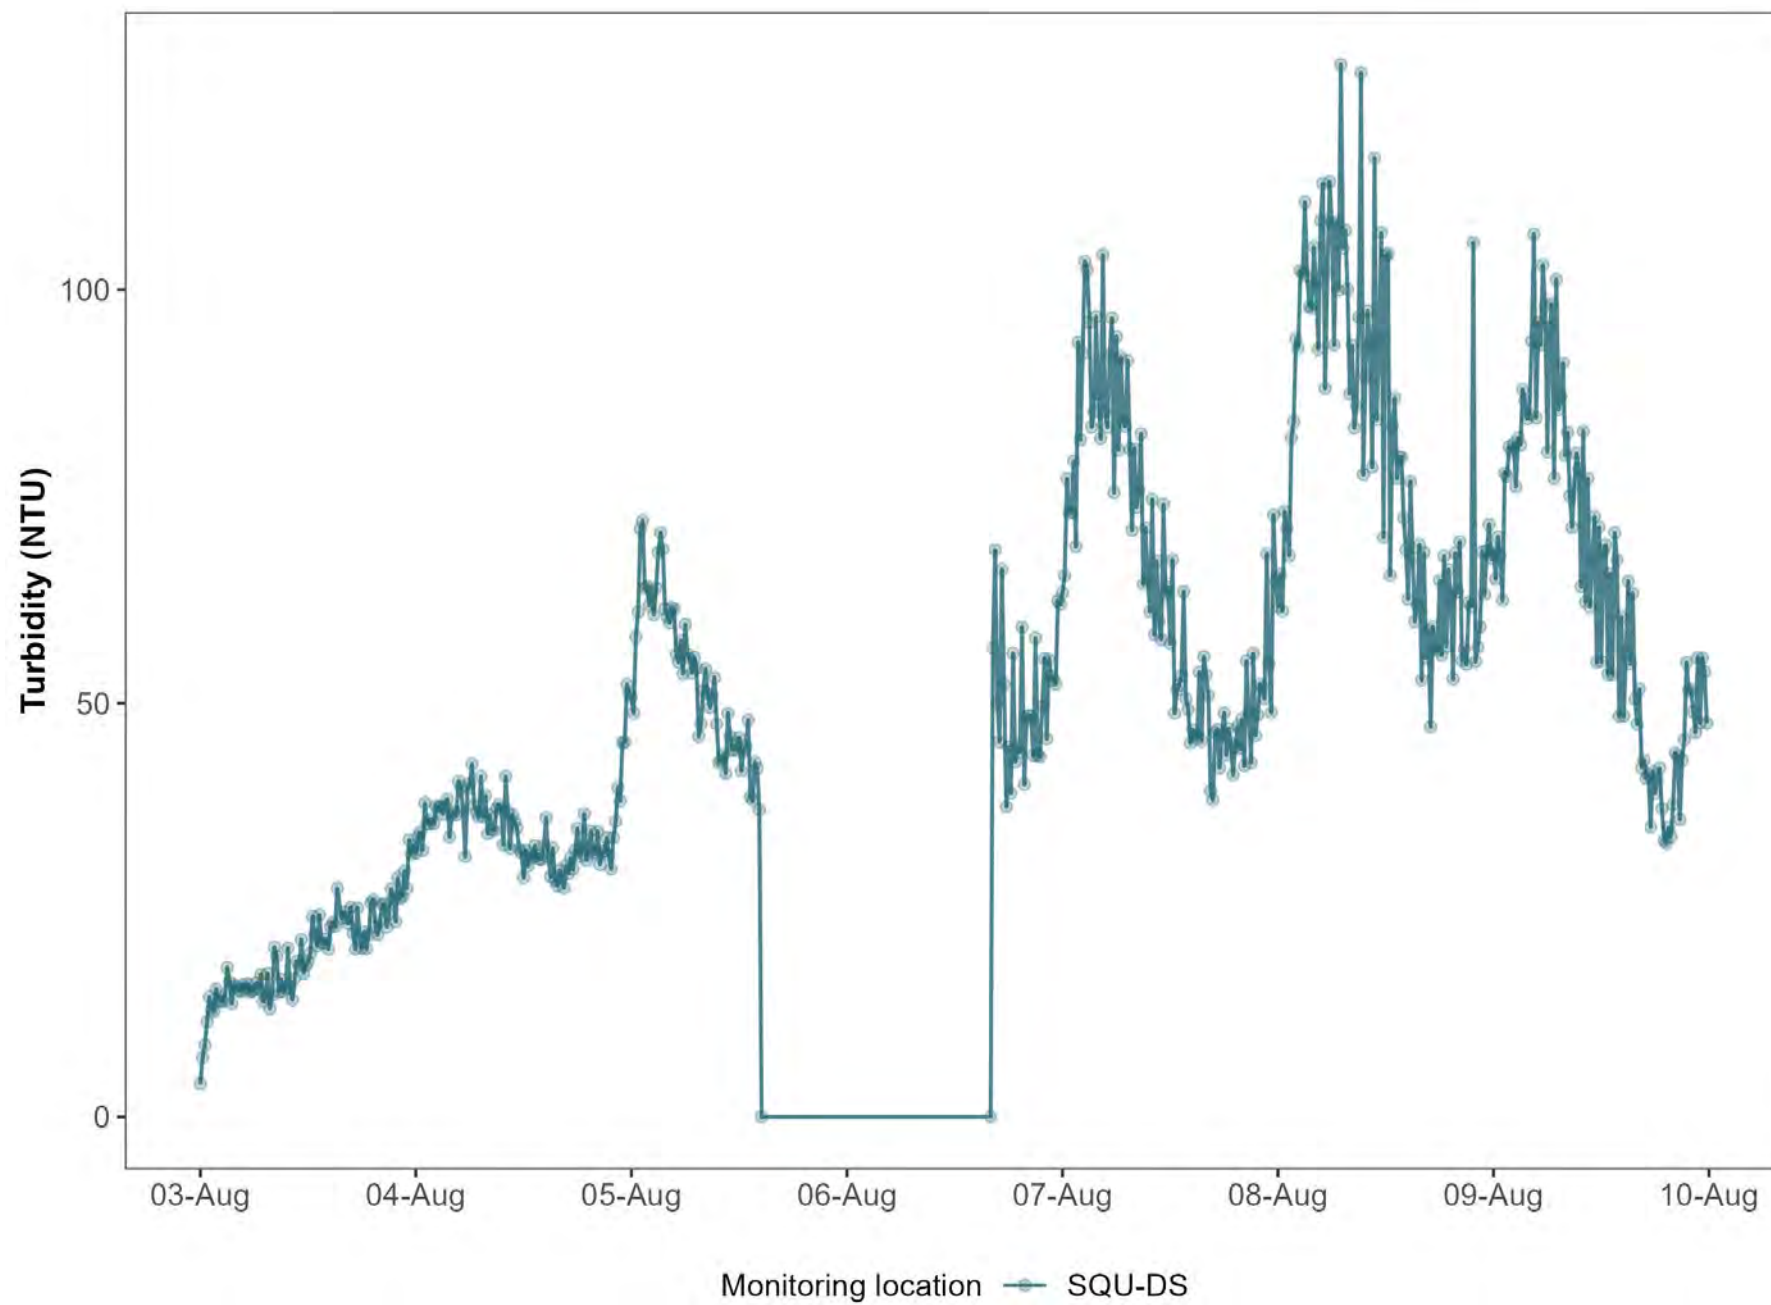

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix C	C-1

Appendix C: Woodfibre Site Point of Discharge from Water Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix C	C-2

Woodfibre Site Sample Analysis



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
In situ Parameters									
Field pH	pH Units			6.5 - 9			7 - 8.7		6.88
Field Temperature	°C		18	19					14.1
General Parameters									
pH	pH Units								7.28
Alkalinity (Total as CaCO ₃)	mg/L								47
Alkalinity (PP as CaCO ₃)	mg/L								<1
Hardness (CaCO ₃)-Total	mg/L								64.7
Hardness (CaCO ₃)-Dissolved	mg/L								61.2
Sulphide-Total	mg/L								<0.0018
Sulphide (as H ₂ S)	mg/L				0.002				<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L								<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L								<0.0018
Anions and Nutrients									
Ammonia (N)-Total	mg/L		1.77	21		20	131		<0.015
Bicarbonate (HCO ₃)	mg/L								57
Carbonate (CO ₃)	mg/L								<1
Hydroxide (OH)	mg/L								<1
Nitrate (N)	mg/L		3	32.8		3.7			<0.02
Nitrite (N)	mg/L		0.2	0.6					<0.005
Nitrate plus Nitrite (N)	mg/L								<0.02
Nitrogen (N)-Total	mg/L								0.197
Phosphorus (P)-Total (4500-P)	mg/L								0.0018
Bromide (Br)	mg/L								<0.01
Chloride (Cl)	mg/L		150	600					15
Fluoride (F)	mg/L			1.159054			1.5		0.28
Sulphate (SO ₄)-Dissolved	mg/L		218						14
Total Metals									
Aluminum (Al)-Total	mg/L		0.0434901						0.0725
Antimony (Sb)-Total	mg/L		0.074	0.25					0.000295
Arsenic (As)-Total	mg/L		0.005			0.0125			0.00108
Barium (Ba)-Total	mg/L				1				0.00357
Beryllium (Be)-Total	mg/L				0.00013			0.1	<0.00001
Bismuth (Bi)-Total	mg/L								<0.000005
Boron (B)-Total	mg/L		1.2			1.2			0.015
Cadmium (Cd)-Total	mg/L							0.00012	<0.000005
Calcium (Ca)-Total	mg/L								23.5
Cesium (Cs)-Total	mg/L								<0.00005
Chromium (Cr)-Total	mg/L								<0.0001

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
Total Metals (cont'd.)									
Chromium (Cr III)-Total	mg/L				0.0089			0.056	<0.00099
Chromium (Cr VI)-Total	mg/L				0.0025			0.0015	<0.00099
Cobalt (Co)-Total	mg/L								0.0000475
Copper (Cu)-Total	mg/L					0.002	0.003		0.000078
Iron (Fe)-Total	mg/L		0.045	1					0.013
Lead (Pb)-Total	mg/L					0.002	0.14		<0.000005
Lithium (Li)-Total	mg/L								0.00858
Magnesium (Mg)-Total	mg/L								1.42
Manganese (Mn)-Total	mg/L							0.1	0.0249
Mercury (Hg)-Total	mg/L		0.00002			0.0001			<0.0000019
Molybdenum (Mo)-Total	mg/L		7.6	46					0.0463
Nickel (Ni)-Total	mg/L							0.0083	0.000168
Phosphorus (P)-Total (ICPMS)	mg/L								0.0032
Potassium (K)-Total	mg/L								1.68
Rubidium (Rb)-Total	mg/L								0.00366
Selenium (Se)-Total	mg/L		0.002			0.002			<0.00004
Silicon (Si)-Total	mg/L								7.4
Silver (Ag)-Total	mg/L		0.00012			0.0005	0.0037	0.0005	<0.000005
Sodium (Na)-Total	mg/L								7.69
Strontium (Sr)-Total	mg/L								0.0498
Sulphur (S)-Total	mg/L								5.4
Tellurium (Te)-Total	mg/L								<0.00002
Thallium (Tl)-Total	mg/L				0.00003				0.0000077
Thorium (Th)-Total	mg/L								<0.00005
Tin (Sn)-Total	mg/L								<0.0002
Titanium (Ti)-Total	mg/L								<0.0005
Uranium (U)-Total	mg/L			0.0165	0.0075				0.000224
Vanadium (V)-Total	mg/L				0.06			0.005	<0.0002
Zinc (Zn)-Total	mg/L					0.01	0.055		0.00378
Zirconium (Zr)-Total	mg/L								<0.0001
Dissolved Metals									
Aluminum (Al)-Dissolved	mg/L								0.0274
Antimony (Sb)-Dissolved	mg/L								0.000306
Arsenic (As)-Dissolved	mg/L								0.00103
Barium (Ba)-Dissolved	mg/L								0.0033
Beryllium (Be)-Dissolved	mg/L								<0.00001
Bismuth (Bi)-Dissolved	mg/L								<0.000005
Boron (B)-Dissolved	mg/L								<0.01

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
Dissolved Metals (cont'd.)									
Cadmium (Cd)-Dissolved	mg/L		0.0001535	0.0003756					<0.000005
Calcium (Ca)-Dissolved	mg/L								22.4
Cesium (Cs)-Dissolved	mg/L								<0.00005
Chromium (Cr)-Dissolved	mg/L								<0.0001
Cobalt (Co)-Dissolved	mg/L		0.0004258						0.0000473
Copper (Cu)-Dissolved	mg/L	0.00366							0.00008
Iron (Fe)-Dissolved	mg/L								0.0018
Lead (Pb)-Dissolved	mg/L		0.0015932						<0.000005
Lithium (Li)-Dissolved	mg/L								0.0074
Manganese (Mn)-Dissolved	mg/L		0.245	2.270836					0.0244
Magnesium (Mg)-Dissolved	mg/L								1.29
Mercury (Hg)-Dissolved	mg/L								<0.0000019
Molybdenum (Mo)-Dissolved	mg/L								0.0466
Nickel (Ni)-Dissolved	mg/L		0.0012	0.022					0.000139
Phosphorus (P)-Dissolved	mg/L								0.0021
Potassium (K)-Dissolved	mg/L								1.61
Rubidium (Rb)-Dissolved	mg/L								0.00333
Selenium (Se)-Dissolved	mg/L								<0.00004
Silicon (Si)-Dissolved	mg/L								6.84
Silver (Ag)-Dissolved	mg/L								<0.000005
Sodium (Na)-Dissolved	mg/L								6.99
Strontium (Sr)-Dissolved	mg/L				1.25				0.0473
Sulphur (S)-Dissolved	mg/L								4.9
Tellurium (Te)-Dissolved	mg/L								<0.00002
Thallium (Tl)-Dissolved	mg/L								0.0000087
Thorium (Th)-Dissolved	mg/L								<0.000005
Tin (Sn)-Dissolved	mg/L								<0.0002
Titanium (Ti)-Dissolved	mg/L								<0.0005
Uranium (U)-Dissolved	mg/L								0.000176
Vanadium (V)-Dissolved	mg/L								<0.0002
Zinc (Zn)-Dissolved	mg/L		0.0085222	0.0252146					0.00356
Zirconium (Zr)-Dissolved	mg/L								<0.0001
Inorganics									
Organic Carbon (C)-Total	mg/L								0.95
Organic Carbon (C)-Dissolved	mg/L								0.72
Solids-Total Dissolved	mg/L								88
Solids-Total Suspended	mg/L		6.6	26.6					<1

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
Organics									
HEPH (C19-C32 less PAH)	mg/L								<0.2
LEPH (C10-C19 less PAH)	mg/L								<0.2
EPH (C10-C19)	mg/L								<0.2
EPH (C19-C32)	mg/L								<0.2
Ethylene Glycol	mg/L								<3
Diethylene Glycol	mg/L								<5
Triethylene Glycol	mg/L								<5
Propylene Glycol	mg/L								<5
Acenaphthene	mg/L		0.006			0.006			<0.00005
Acenaphthylene	mg/L								<0.00005
Acridine	mg/L		0.003						<0.00005
Anthracene	mg/L		0.004						<0.00001
Benzo(a)anthracene	mg/L		0.0001						<0.00001
Benzo(a)pyrene	mg/L		0.00001			0.00001			<0.000005
Benzo(b&j)fluoranthene	mg/L								<0.00003
Benzo(g,h,i)perylene	mg/L								<0.00005
Benzo(k)fluoranthene	mg/L								<0.00005
Chrysene	mg/L					0.0001			<0.00002
Dibenz(a,h)anthracene	mg/L								<0.000003
Fluoranthene	mg/L		0.004						<0.00002
Fluorene	mg/L		0.012			0.012			<0.00005
Indeno(1,2,3-cd)pyrene	mg/L								<0.00005
1-Methylnaphthalene	mg/L					0.001			<0.00005
2-Methylnaphthalene	mg/L					0.001			<0.0001
Naphthalene	mg/L		0.001	0.001		0.001			<0.0001
Phenanthrene	mg/L		0.0003						<0.00005
Pyrene	mg/L								<0.00002
Quinoline	mg/L								<0.00002
Low Molecular Weight PAH's	mg/L								<0.0001
High Molecular Weight PAH's	mg/L								<0.00005
Total PAH	mg/L								<0.0001
VH C6-C10	mg/L								<0.3
1,1,1,2-Tetrachloroethane	mg/L								<0.0005
1,1,1-Trichloroethane	mg/L								<0.0005
1,1,2,2-Tetrachloroethane	mg/L								<0.0005
1,1,2Trichloro-1,2,2Trifluoroethane	mg/L								<0.002
1,1,2-Trichloroethane	mg/L								<0.0005
1,1-Dichloroethane	mg/L								<0.0005

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
Organics (cont'd.)									
1,1-Dichloroethene	mg/L								<0.0005
1,2,3-trichlorobenzene	mg/L				0.008				<0.002
1,2,4-trichlorobenzene	mg/L				0.024			0.0054	<0.002
1,2-dibromoethane	mg/L								<0.0002
1,2-Dichlorobenzene	mg/L				0.0007			0.042	<0.0005
1,2-Dichloroethane	mg/L				0.1				<0.0005
1,2-Dichloropropane	mg/L								<0.0005
1,3,5-trimethylbenzene	mg/L								<0.002
1,3-Butadiene	mg/L								<0.0005
1,3-Dichlorobenzene	mg/L				0.15				<0.0005
1,3-dichloropropane	mg/L								<0.001
1,4-Dichlorobenzene	mg/L				0.026				<0.0005
Benzene	mg/L		0.04			0.11			<0.0004
Bromobenzene	mg/L								<0.002
Bromodichloromethane	mg/L								<0.001
Bromoform	mg/L								<0.001
Bromomethane	mg/L								<0.001
Carbon tetrachloride	mg/L								<0.0005
Chlorobenzene	mg/L				0.0013			0.025	<0.0005
Chloroethane	mg/L								<0.001
Chloroform	mg/L								<0.001
Chloromethane	mg/L								<0.001
cis-1,2-Dichloroethene	mg/L								<0.001
cis-1,3-Dichloropropene	mg/L								<0.001
Dibromochloromethane	mg/L								<0.001
Dichlorodifluoromethane	mg/L								<0.002
Dichloromethane	mg/L				0.0981				<0.002
Ethylbenzene	mg/L		0.2			0.25			<0.0004
Hexachlorobutadiene	mg/L								<0.0005
Isopropylbenzene	mg/L								<0.002
Methyl-tert-butylether (MTBE)	mg/L			3.4			0.44		<0.004
Styrene	mg/L				0.072				<0.0005
Tetrachloroethene	mg/L								<0.0005
Toluene	mg/L		0.0005						<0.0004
trans-1,2-dichloroethene	mg/L								<0.001
trans-1,3-dichloropropene	mg/L								<0.001
Trichloroethene	mg/L								<0.0005
Trichlorofluoromethane	mg/L								<0.004

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-05 09:14:00
Organics (cont'd.)									
Vinyl chloride	mg/L								<0.0005
VPH (VH6 to 10 - BTEX)	mg/L								<0.3
Xylenes (Total)	mg/L		0.03						<0.0004
m & p-Xylene	mg/L								<0.0004
o-Xylene	mg/L								<0.0004
Phenols	mg/L			0.05					<0.0015

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix C	C-3

Woodfibre Site WTP Discharge
Field Notes and Logs

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	WLNG EOP	Date:	August 5, 2026
Site Name:	East Creek	Time:	9:14
Site UTM:	Zone: 10U E: 482030	Crew:	AH
(NAD83)	N: 5501931	Weather:	Smoky/hazy, no clouds, no precip 24hrs+

In Situ Parameters

pH:	6.88	DO:	7.80 (mg/L)
Temp:	14.1 (°C)	Cond:	207.5 (us/cm)
Turbidity:	1.98 NTU	Salinity:	0.1 (ppt)
Visible Sheen:	No	ORP:	85.5 (mV)

Water Surface Condition: Clear

Photo Record



Observations

No notable observations. Sample point spigot running intermittently.

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Table of Contents:

1. Executive Summary and Field Notes
2. Daily Volume Summary
3. Portal Discharge Parameter Summary
4. CP2 Discharge Parameter Summary
5. In-situ Readings
6. WTP Calibration Log

Appendices:

- Appendix A- Portal WTP Data Log
- Appendix B- CP2 WTP Data Log
- Appendix C- Photos

1. Executive Summary and Field Notes:

Parameters, including temperature, NTU, pH, DO, salinity, conductivity, and oxidation-reduction potential (ORP), were monitored throughout the reporting period.

A NTU reading of 26.3 NTU was recorded on the Portal Water Treatment Plant (PWTP) data log on Aug 8th at 17:00 with the recirculation valve open at the time of the reading. The discharge valve which has a 10 second delay was in the process of closing. Discharge water was at 5.8 NTU at 17:15.

A reading of 23 NTU was recorded on the CP2 Water Treatment Plant (CP2 WTP) data log on Aug 5th at 21:45 while the NTU probe was being installed after calibration. Discharge water was ~0 NTU.

There were several conductivity readings of 0 uS/cm recorded on the CP2 WTP data logs when there was low flow, and water did not contact the conductivity probe. There were also misreadings of 13 uS/cm, 80 uS/cm and 110 uS/cm recorded. Typically, the conductivity is ~230 uS/cm.

No visible sheen was observed on the surface of the PWTP and CP2 WTP tanks or in the discharged water. All relevant parameters were measured using YSI instruments, Hanna NTU meters and WTP NTU, pH, conductivity and temperature probes.

The CP2 WTP received ~300 GPM (1.13 m³/min) and the PWTP received ~192 GPM (0.73 m³/min) from the tunnel.

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

The total discharge volume up to August 9th was 1,686,613m³.

2. Daily Volume Summary:

Table 1: Discharge Volumes Daily Summary

Date	Location	Volume (m3)	Comments
August 3	Woodfibre (WF)	2,814	None
August 4	WF	2,807	None
August 5	WF	2,583	None
August 6	WF	2,624	None
August 7	WF	2,637	None
August 8	WF	2,626	None
August 9	WF	2,675	None
Total		18,766	None

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

3. Discharge Parameter Summary:

Table 2: Portal Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	0:00:00	7.4	1.6050	1	1,426,843	15.3	324
8/3/2026	0:30:00	7.4	1.5823	0.9	1,426,863	15.2	324
8/3/2026	1:00:00	7.3	1.6315	2.4	1,426,878	15.5	323
8/3/2026	1:15:00	7.4	1.6050	2	1,426,903	15.1	321
8/3/2026	1:45:00	7.3	1.6164	1.8	1,426,922	15	318
8/3/2026	2:30:00	7.3	1.5634	2	1,426,959	14.7	309
8/3/2026	2:45:00	7.3	1.0031	1.7	1,426,981	14.7	308
8/3/2026	3:15:00	7.3	1.5520	0.3	1,426,998	14.7	308
8/3/2026	3:45:00	7.3	1.6050	0.4	1,427,016	15	308
8/3/2026	4:00:00	7.3	1.5407	0.1	1,427,039	14.6	303
8/3/2026	4:30:00	7.3	1.5823	0.2	1,427,058	14.5	303
8/3/2026	5:15:00	7.3	1.6202	0.7	1,427,090	14.4	301
8/3/2026	5:45:00	7.3	1.0258	1.3	1,427,117	14.4	301
8/3/2026	6:15:00	7.3	1.6088	1.1	1,427,138	14.4	300
8/3/2026	6:30:00	7.3	1.0713	0.8	1,427,162	14.3	301
8/3/2026	7:00:00	7.3	1.6012	0.3	1,427,187	14.3	304
8/3/2026	7:30:00	7.3	1.6126	0.3	1,427,204	14.5	304
8/3/2026	8:15:00	7.3	1.6050	0.3	1,427,242	14.3	301
8/3/2026	8:45:00	7.2	1.0675	0.3	1,427,258	14.8	299
8/3/2026	9:00:00	7.3	1.5823	0.4	1,427,278	14.3	298
8/3/2026	9:30:00	7.3	0.6511	0.6	1,427,304	14.3	296
8/3/2026	10:30:00	7.3	1.4082	0.7	1,427,328	14.6	293
8/3/2026	10:45:00	7.3	1.7489	0.5	1,427,336	14.8	296
8/3/2026	11:00:00	7.3	1.1394	4.4	1,427,361	14.9	294
8/3/2026	11:30:00	7.3	1.7526	4.1	1,427,389	15.1	298
8/3/2026	12:00:00	7.3	1.7640	3.8	1,427,407	15.5	298
8/3/2026	12:30:00	7.4	1.1924	0	1,427,429	15.9	296
8/3/2026	13:15:00	7.3	1.1962	0.2	1,427,456	16	296
8/3/2026	13:45:00	7.3	1.7564	0.1	1,427,481	15.9	294



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	14:15:00	7.3	1.7299	0.1	1,427,506	16.7	296
8/3/2026	14:30:00	7.3	1.6618	0.3	1,427,531	16	294
8/3/2026	14:45:00	7.2	1.2340	1.2	1,427,533	17.2	298
8/3/2026	15:00:00	7.3	1.7186	0.6	1,427,555	16.1	294
8/3/2026	15:30:00	7.3	1.1167	1.5	1,427,583	16.3	293
8/3/2026	16:00:00	7.3	1.6883	0.8	1,427,596	16.6	293
8/3/2026	16:30:00	7.3	1.6883	1.3	1,427,619	16.5	293
8/3/2026	17:00:00	7.2	1.1091	1.6	1,427,636	18.1	298
8/3/2026	17:15:00	7.3	1.6504	1.6	1,427,658	16.3	293
8/3/2026	17:30:00	7.2	1.7034	1.1	1,427,662	17.8	296
8/3/2026	17:45:00	7.2	1.0637	3.5	1,427,686	16.1	292
8/3/2026	18:15:00	7.3	1.6088	1.9	1,427,713	16.1	293
8/3/2026	19:00:00	7.2	1.5217	2.2	1,427,722	16.3	291
8/3/2026	19:15:00	7.2	0.9804	4.6	1,427,744	16	293
8/3/2026	19:30:00	7.2	1.6429	1.9	1,427,747	17.4	293
8/3/2026	19:45:00	7.3	1.5634	1.7	1,427,770	15.8	293
8/3/2026	20:00:00	7.3	0.9918	3.7	1,427,792	15.7	293
8/3/2026	20:15:00	7.2	1.6504	2.3	1,427,796	16.8	291
8/3/2026	20:30:00	7.3	1.5444	1.8	1,427,819	15.6	291
8/3/2026	21:00:00	7.3	1.5709	1.6	1,427,843	15.8	289
8/3/2026	21:15:00	7.3	1.4990	2	1,427,866	15.5	290
8/3/2026	21:45:00	7.3	0.5792	4.3	1,427,889	15.4	289
8/3/2026	22:15:00	7.3	1.4082	1.8	1,427,912	15.3	291
8/3/2026	23:00:00	7.3	1.5558	0.4	1,427,941	15.4	294
8/3/2026	23:15:00	7.3	1.0145	0.6	1,427,963	15.5	299
8/3/2026	23:30:00	7.3	1.5937	0.3	1,427,965	15.8	298
8/3/2026	23:45:00	7.3	1.5747	0.3	1,427,988	15.6	301
8/4/2026	0:15:00	7.3	1.5407	0.4	1,428,015	15.6	303
8/4/2026	0:45:00	7.3	1.0675	0.5	1,428,036	15.8	306
8/4/2026	1:00:00	7.3	1.5634	0.5	1,428,057	15.5	306
8/4/2026	1:30:00	7.3	1.0258	1.8	1,428,079	15.4	306
8/4/2026	2:00:00	7.3	1.5823	0.6	1,428,099	15.4	306



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	2:45:00	7.3	1.5823	0.7	1,428,120	15.7	306
8/4/2026	3:00:00	7.3	1.0031	2	1,428,142	15.2	306
8/4/2026	3:30:00	7.3	1.5142	0.7	1,428,164	15.1	306
8/4/2026	4:00:00	7.3	1.5634	0.9	1,428,186	15.3	303
8/4/2026	4:15:00	7.3	1.5369	0.9	1,428,209	14.9	302
8/4/2026	4:45:00	7.3	1.5407	0.5	1,428,233	14.9	304
8/4/2026	5:15:00	7.2	1.0599	2.5	1,428,243	15.2	303
8/4/2026	5:30:00	7.3	1.4952	0.7	1,428,263	14.9	303
8/4/2026	6:00:00	7.3	1.1243	2.4	1,428,287	14.9	303
8/4/2026	6:30:00	7.3	1.5444	1	1,428,313	14.7	304
8/4/2026	7:00:00	7.3	1.5937	0.9	1,428,331	14.8	305
8/4/2026	7:45:00	7.3	1.5482	1.1	1,428,366	14.7	303
8/4/2026	8:15:00	7.2	1.0599	3	1,428,379	14.7	303
8/4/2026	8:30:00	7.3	1.5634	1.2	1,428,400	14.5	299
8/4/2026	9:00:00	7.2	1.0296	1.9	1,428,422	14.5	298
8/4/2026	9:30:00	7.2	1.5747	1	1,428,443	14.6	296
8/4/2026	10:00:00	7.3	1.5672	1	1,428,466	14.8	293
8/4/2026	10:45:00	7.2	1.6088	1.1	1,428,493	15.2	299
8/4/2026	11:15:00	7.3	0.6852	1.5	1,428,523	15.3	302
8/4/2026	11:30:00	7.3	1.5899	1.2	1,428,542	15.4	302
8/4/2026	12:00:00	7.3	1.0599	2.6	1,428,561	15.7	299
8/4/2026	12:30:00	7.3	1.6353	1.4	1,428,584	15.8	298
8/4/2026	12:45:00	7.3	1.0713	3.7	1,428,607	15.8	298
8/4/2026	13:15:00	7.3	1.6353	2.3	1,428,632	16	299
8/4/2026	14:00:00	7.3	1.6277	2.8	1,428,675	16.3	306
8/4/2026	14:30:00	7.3	1.6050	2.3	1,428,694	16.9	306
8/4/2026	14:45:00	7.3	1.5747	2.5	1,428,718	16.4	306
8/4/2026	15:15:00	7.3	1.6239	1.5	1,428,740	16.6	309
8/4/2026	15:45:00	7.3	1.1016	2.8	1,428,755	17.2	311
8/4/2026	16:00:00	7.3	1.6202	0.5	1,428,777	16.5	309
8/4/2026	16:30:00	7.3	1.0978	1.1	1,428,801	16.7	309
8/4/2026	17:00:00	7.3	1.5785	1	1,428,824	16.6	308



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	17:30:00	7.3	1.6164	1.1	1,428,848	16.8	309
8/4/2026	18:00:00	7.3	1.1016	2.9	1,428,870	17.3	311
8/4/2026	18:15:00	7.3	1.6239	1.1	1,428,892	16.7	311
8/4/2026	18:45:00	7.3	1.0523	2.2	1,428,909	16.9	311
8/4/2026	19:15:00	7.3	1.6315	2	1,428,917	17.3	313
8/4/2026	19:45:00	7.2	1.6239	2.7	1,428,939	17.5	313
8/4/2026	20:00:00	7.2	1.6050	2.6	1,428,963	16.3	313
8/4/2026	20:30:00	7.2	1.6239	2.6	1,428,979	16.3	314
8/4/2026	21:30:00	7.2	1.4536	1.3	1,429,030	15.6	307
8/4/2026	21:45:00	7.2	1.4347	1.6	1,429,051	15.6	306
8/4/2026	22:15:00	7.2	1.4839	2.1	1,429,075	15.6	309
8/4/2026	22:30:00	7.2	1.4309	2	1,429,098	15.6	309
8/4/2026	23:15:00	7.2	1.4650	1.6	1,429,138	15.8	313
8/5/2026	0:00:00	7.2	1.4536	1.8	1,429,172	15.9	318
8/5/2026	0:30:00	7.2	1.4763	1.7	1,429,188	15.9	318
8/5/2026	0:45:00	7.3	1.4612	2.2	1,429,210	15.9	319
8/5/2026	1:15:00	7.3	1.4385	2.3	1,429,228	15.9	319
8/5/2026	1:30:00	7.3	1.4347	2.2	1,429,250	15.7	319
8/5/2026	2:00:00	7.2	1.4460	2.1	1,429,267	15.8	319
8/5/2026	2:45:00	7.3	0.9691	3.3	1,429,306	15.5	313
8/5/2026	3:30:00	7.3	1.5747	1.1	1,429,343	15.4	309
8/5/2026	4:00:00	7.3	1.5899	1.5	1,429,360	15.1	303
8/5/2026	4:15:00	7.3	1.0334	4.3	1,429,382	15.1	303
8/5/2026	4:45:00	7.2	0.9956	2	1,429,399	15.7	301
8/5/2026	5:15:00	7.2	1.0258	4.9	1,429,420	15.5	299
8/5/2026	5:30:00	7.3	1.5369	1.8	1,429,441	15.1	298
8/5/2026	6:15:00	7.3	1.0410	3.2	1,429,482	15	298
8/5/2026	6:45:00	7.2	1.0523	3	1,429,498	15.1	299
8/5/2026	7:00:00	7.3	1.5407	2.2	1,429,518	15	298
8/5/2026	7:30:00	7.3	1.5899	1.1	1,429,536	14.9	296
8/5/2026	8:15:00	7.2	0.6019	2.1	1,429,569	14.8	294
8/5/2026	8:45:00	7.2	1.1243	2.3	1,429,584	14.7	293



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	9:15:00	7.2	1.1432	2.2	1,429,603	14.8	291
8/5/2026	10:00:00	7.2	1.6921	1.2	1,429,634	14.8	290
8/5/2026	10:30:00	7.2	1.6769	1.6	1,429,660	15.1	288
8/5/2026	10:45:00	7.2	1.1243	1.8	1,429,684	15.2	288
8/5/2026	11:15:00	7.2	1.1394	3.5	1,429,706	15.5	290
8/5/2026	12:00:00	7.3	1.6164	4.3	1,429,751	15.7	290
8/5/2026	12:45:00	7.2	1.0902	5.6	1,429,781	16.1	289
8/5/2026	13:30:00	7.3	1.5634	4.3	1,429,817	16.2	292
8/5/2026	14:00:00	7.3	1.5747	2.8	1,429,839	16.7	293
8/5/2026	14:15:00	7.3	1.0145	3	1,429,861	16.4	291
8/5/2026	14:45:00	7.3	1.0372	3.8	1,429,881	17.1	293
8/5/2026	15:00:00	7.3	1.5179	5.3	1,429,902	16.6	291
8/5/2026	15:30:00	7.2	1.6164	5.4	1,429,922	17.4	293
8/5/2026	15:45:00	7.3	1.0713	6.3	1,429,944	16.9	289
8/5/2026	16:30:00	7.3	1.5066	6.6	1,429,972	16.9	292
8/5/2026	17:00:00	7.3	1.5596	6	1,429,993	17	290
8/5/2026	17:15:00	7.3	1.0448	7.1	1,430,014	16.9	289
8/5/2026	17:30:00	7.2	1.5217	6.2	1,430,017	17.4	292
8/5/2026	18:00:00	7.3	1.5899	10.5	1,430,033	16.8	288
8/5/2026	18:15:00	7.3	1.1053	5.9	1,430,054	17	289
8/5/2026	18:30:00	7.3	1.6088	6.3	1,430,076	17.6	290
8/5/2026	19:15:00	7.2	1.1394	4.1	1,430,099	18.5	292
8/5/2026	19:30:00	7.3	1.6391	2.8	1,430,122	16.8	291
8/5/2026	20:00:00	7.3	1.5937	1	1,430,146	16.4	292
8/5/2026	20:30:00	7.3	1.6467	0.3	1,430,172	16.3	292
8/5/2026	20:45:00	7.3	1.2000	0.4	1,430,195	16.2	290
8/5/2026	21:15:00	7.3	1.0486	0.5	1,430,217	16	288
8/5/2026	21:30:00	7.3	1.4650	0.5	1,430,237	15.9	288
8/5/2026	22:00:00	7.3	1.4725	0.8	1,430,264	15.9	292
8/5/2026	22:15:00	7.3	1.0372	1	1,430,285	15.8	290
8/5/2026	22:30:00	7.3	1.4460	1	1,430,305	15.8	290
8/5/2026	23:00:00	7.3	1.4422	1	1,430,328	15.9	292



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	23:15:00	7.3	1.0107	1.4	1,430,348	15.8	292
8/5/2026	23:45:00	7.3	0.9918	1.1	1,430,360	15.8	294
8/6/2026	0:00:00	7.3	1.4763	1.2	1,430,380	15.6	293
8/6/2026	0:15:00	7.3	0.9615	1.8	1,430,400	15.6	293
8/6/2026	0:45:00	7.3	0.9993	2	1,430,423	15.5	293
8/6/2026	1:00:00	7.3	1.4309	1.4	1,430,443	15.5	293
8/6/2026	1:15:00	7.3	0.9729	1.8	1,430,462	15.5	293
8/6/2026	1:30:00	7.3	1.4763	1.5	1,430,467	15.9	297
8/6/2026	1:45:00	7.3	0.9842	1.9	1,430,487	15.5	295
8/6/2026	2:00:00	7.3	1.4725	1.2	1,430,507	15.4	295
8/6/2026	2:15:00	7.3	0.9766	2.6	1,430,527	15.4	295
8/6/2026	2:45:00	7.3	0.9993	2.8	1,430,548	15.4	295
8/6/2026	3:00:00	7.3	1.4650	1.3	1,430,569	15.3	295
8/6/2026	3:30:00	7.2	1.4536	2.2	1,430,588	15.8	294
8/6/2026	3:45:00	7.2	0.9842	2.2	1,430,608	15.3	295
8/6/2026	4:00:00	7.3	1.4612	2.2	1,430,628	15.2	295
8/6/2026	4:30:00	7.3	1.4498	2	1,430,650	15.2	294
8/6/2026	4:45:00	7.3	0.7609	5.5	1,430,668	15.1	294
8/6/2026	5:30:00	7.3	1.0410	5.8	1,430,693	15	296
8/6/2026	5:45:00	7.3	1.4877	2.7	1,430,712	15	296
8/6/2026	6:15:00	7.3	1.5407	3.2	1,430,735	15.1	298
8/6/2026	7:15:00	7.3	1.6277	2.2	1,430,773	15.2	299
8/6/2026	7:30:00	7.3	1.6202	2.1	1,430,798	15.1	300
8/6/2026	8:00:00	7.2	0.2044	1.2	1,430,829	15.2	299
8/6/2026	8:15:00	7.2	1.0713	1.8	1,430,836	15.3	299
8/6/2026	8:30:00	7.3	1.5293	3.6	1,430,858	14.9	296
8/6/2026	9:00:00	7.2	1.5785	3.5	1,430,883	14.8	291
8/6/2026	9:15:00	7.2	1.0599	1.5	1,430,904	14.9	291
8/6/2026	9:45:00	7.2	1.0675	1.4	1,430,923	15.1	290
8/6/2026	10:30:00	7.2	1.4650	1.1	1,430,955	15.1	285
8/6/2026	10:45:00	7.2	1.0296	2.2	1,430,975	15.1	283
8/6/2026	11:30:00	7.2	1.4877	0.9	1,431,009	15.3	285



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	12:00:00	7.2	1.4612	1	1,431,030	15.6	288
8/6/2026	12:15:00	7.2	0.9766	1.1	1,431,049	15.5	285
8/6/2026	12:45:00	7.2	1.0637	1.1	1,431,069	15.9	287
8/6/2026	13:00:00	7.2	1.5331	0.6	1,431,090	15.6	285
8/6/2026	13:15:00	7.2	0.9956	1.6	1,431,111	15.8	285
8/6/2026	13:45:00	7.2	1.0448	0.8	1,431,135	16.1	285
8/6/2026	14:00:00	7.2	1.5255	0.5	1,431,156	16	287
8/6/2026	14:30:00	7.2	1.5331	0.6	1,431,181	16.4	290
8/6/2026	14:45:00	7.2	1.0523	1.2	1,431,202	16.5	290
8/6/2026	15:00:00	7.2	1.5142	0.4	1,431,223	16.4	291
8/6/2026	15:30:00	7.2	1.5217	3.1	1,431,250	16.5	291
8/6/2026	15:45:00	7.2	1.0410	0.8	1,431,270	16.8	294
8/6/2026	16:15:00	7.2	0.6662	1.5	1,431,289	16.7	294
8/6/2026	16:30:00	7.3	1.4915	0.7	1,431,309	16.7	294
8/6/2026	16:45:00	7.2	1.0258	1.2	1,431,329	16.8	294
8/6/2026	17:15:00	7.2	0.9691	1.1	1,431,352	16.8	296
8/6/2026	17:30:00	7.3	1.4915	0.6	1,431,373	16.6	294
8/6/2026	17:45:00	7.2	1.0069	0.7	1,431,393	16.7	294
8/6/2026	18:15:00	7.2	0.9804	0.7	1,431,416	16.8	293
8/6/2026	18:30:00	7.3	1.4725	0.6	1,431,436	16.6	293
8/6/2026	19:00:00	7.2	1.4952	0.3	1,431,453	16.7	293
8/6/2026	19:15:00	7.2	0.9729	0.2	1,431,473	16.7	295
8/6/2026	19:30:00	7.2	1.4612	0.1	1,431,493	16.5	294
8/6/2026	20:00:00	7.2	1.4763	0	1,431,520	16.4	293
8/6/2026	20:15:00	7.2	1.0069	0.1	1,431,540	16.5	293
8/6/2026	20:45:00	7.2	1.0258	0	1,431,563	16.3	293
8/6/2026	21:00:00	7.2	1.4801	0	1,431,584	15.9	290
8/6/2026	21:45:00	7.2	0.9653	0.1	1,431,613	15.9	290
8/6/2026	22:00:00	7.2	1.4422	0.1	1,431,634	15.6	288
8/6/2026	22:30:00	7.2	1.4460	0.6	1,431,657	15.9	288
8/6/2026	22:45:00	7.2	0.9880	0.6	1,431,676	15.7	290
8/6/2026	23:00:00	7.2	1.4612	0.6	1,431,696	15.7	290



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	23:30:00	7.2	1.4801	0.7	1,431,717	16.2	293
8/6/2026	23:45:00	7.2	0.9993	0.7	1,431,737	16	293
8/7/2026	0:00:00	7.2	1.4422	0.3	1,431,757	15.9	297
8/7/2026	0:30:00	7.2	1.4763	0.5	1,431,781	15.9	295
8/7/2026	0:45:00	7.2	1.0145	0.5	1,431,801	16	295
8/7/2026	1:00:00	7.2	1.4536	0.5	1,431,821	15.8	297
8/7/2026	1:30:00	7.2	1.4763	0.5	1,431,843	15.8	300
8/7/2026	1:45:00	7.2	0.9842	0.6	1,431,862	15.8	298
8/7/2026	2:00:00	7.2	1.4536	0.5	1,431,883	15.6	298
8/7/2026	2:30:00	7.2	1.4309	0.5	1,431,905	15.6	298
8/7/2026	2:45:00	7.2	0.9880	1.1	1,431,924	15.7	302
8/7/2026	3:15:00	7.2	0.6662	1.6	1,431,942	15.6	300
8/7/2026	3:30:00	7.2	1.4385	0.6	1,431,961	15.6	303
8/7/2026	3:45:00	7.2	0.9880	2.2	1,431,980	15.8	305
8/7/2026	4:15:00	7.2	1.0031	1.8	1,432,001	16	305
8/7/2026	5:00:00	7.2	1.5899	1.7	1,432,030	15.4	303
8/7/2026	5:15:00	7.2	1.0675	3.5	1,432,051	15.4	301
8/7/2026	5:30:00	7.2	1.5217	1.8	1,432,073	15.2	301
8/7/2026	6:00:00	7.2	1.5482	2	1,432,097	15.2	301
8/7/2026	6:15:00	7.2	1.0713	8.9	1,432,117	15.2	303
8/7/2026	6:45:00	7.2	1.0788	1.9	1,432,138	15.1	303
8/7/2026	7:00:00	7.2	1.5634	1.6	1,432,161	15	301
8/7/2026	7:30:00	7.2	1.5255	1.8	1,432,186	15	298
8/7/2026	8:00:00	7.2	1.5861	2.2	1,432,204	15.2	298
8/7/2026	8:15:00	7.2	1.0448	2.9	1,432,225	15	297
8/7/2026	9:00:00	7.2	1.5709	1.7	1,432,255	15	293
8/7/2026	9:30:00	7.2	1.5823	1.9	1,432,281	15	293
8/7/2026	10:00:00	7.2	1.5861	0.9	1,432,306	15.3	293
8/7/2026	10:15:00	7.2	1.1394	0.6	1,432,327	15.5	296
8/7/2026	10:30:00	7.2	1.5558	0.9	1,432,349	15.5	297
8/7/2026	11:00:00	7.2	1.5596	2.3	1,432,372	15.8	294
8/7/2026	11:15:00	7.1	1.1432	2.6	1,432,392	15.9	294



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	11:30:00	7.2	1.5369	2	1,432,406	16	293
8/7/2026	12:00:00	7.1	1.5974	2.5	1,432,432	16.2	293
8/7/2026	12:15:00	7.1	1.0978	3.6	1,432,452	16.2	293
8/7/2026	12:30:00	7.2	1.5293	2	1,432,475	16.2	293
8/7/2026	13:00:00	7.2	1.5937	1.2	1,432,500	16.4	293
8/7/2026	13:15:00	7.2	1.0675	0.8	1,432,521	16.4	293
8/7/2026	13:30:00	7.2	1.5255	0.8	1,432,543	16.4	292
8/7/2026	13:45:00	7.1	1.1053	1.8	1,432,547	16.9	292
8/7/2026	14:00:00	7.2	1.5785	1	1,432,570	16.6	290
8/7/2026	14:45:00	7.1	1.0523	1.8	1,432,605	16.9	290
8/7/2026	15:00:00	7.2	1.5444	2	1,432,628	16.7	288
8/7/2026	15:15:00	7.1	1.0713	2.4	1,432,648	16.8	287
8/7/2026	15:45:00	7.1	0.7382	3.9	1,432,673	16.9	287
8/7/2026	16:00:00	7.1	1.5520	2.1	1,432,695	16.8	287
8/7/2026	16:15:00	7.1	1.1016	2.1	1,432,715	16.9	287
8/7/2026	16:30:00	7.1	1.5672	2	1,432,721	17	288
8/7/2026	16:45:00	7.1	1.0486	2.2	1,432,741	16.9	287
8/7/2026	17:00:00	7.1	1.5407	1.6	1,432,763	16.8	287
8/7/2026	17:30:00	7.1	1.5596	1.2	1,432,792	16.9	288
8/7/2026	17:45:00	7.1	0.6624	3.1	1,432,807	16.8	288
8/7/2026	18:00:00	7.1	1.4044	0.1	1,432,828	16.9	288
8/7/2026	18:45:00	7.1	1.0599	1.5	1,432,851	17.2	292
8/7/2026	19:00:00	7.2	1.5709	1.8	1,432,874	16.9	290
8/7/2026	19:15:00	7.2	1.1281	1.9	1,432,894	17.2	293
8/7/2026	19:45:00	7.2	1.0788	0.5	1,432,919	16.9	293
8/7/2026	20:00:00	7.2	1.5558	0.1	1,432,942	16.5	293
8/7/2026	20:30:00	7.2	1.5028	0.3	1,432,966	16.4	297
8/7/2026	20:45:00	7.2	1.0031	0.4	1,432,985	16.2	295
8/7/2026	21:00:00	7.2	1.4877	0.3	1,433,007	16	293
8/7/2026	21:30:00	7.2	1.4650	0.4	1,433,028	15.8	292
8/7/2026	21:45:00	7.1	0.9993	0.7	1,433,047	15.8	292
8/7/2026	22:15:00	7.1	1.0410	0.1	1,433,068	16	295



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	22:30:00	7.2	1.4839	0.1	1,433,090	15.7	293
8/7/2026	23:00:00	7.2	1.4915	0.2	1,433,109	15.7	295
8/7/2026	23:15:00	7.2	1.0145	0.4	1,433,128	15.7	298
8/7/2026	23:45:00	7.2	1.0183	0.6	1,433,147	15.7	300
8/8/2026	0:00:00	7.2	1.4612	0.6	1,433,169	15.5	300
8/8/2026	0:30:00	7.2	1.5104	0.9	1,433,190	15.7	306
8/8/2026	0:45:00	7.2	0.9653	1.2	1,433,208	15.5	308
8/8/2026	1:00:00	7.2	1.4460	0.8	1,433,230	15.4	308
8/8/2026	1:30:00	7.2	1.5028	0.7	1,433,254	15.5	309
8/8/2026	1:45:00	7.2	0.9804	1.6	1,433,273	15.5	308
8/8/2026	2:00:00	7.2	1.4915	0.9	1,433,295	15.4	307
8/8/2026	2:30:00	7.2	1.4498	1	1,433,315	15.4	306
8/8/2026	2:45:00	7.2	0.9993	1.6	1,433,334	15.4	307
8/8/2026	3:15:00	7.2	1.0221	1.3	1,433,354	15.6	307
8/8/2026	3:30:00	7.2	1.4915	1	1,433,376	15.4	303
8/8/2026	4:00:00	7.1	1.4952	0.6	1,433,396	15.8	304
8/8/2026	4:15:00	7.1	1.0258	0.3	1,433,415	15.4	302
8/8/2026	4:30:00	7.1	1.4536	0.2	1,433,420	15.5	302
8/8/2026	4:45:00	7.2	0.9956	0.1	1,433,438	15.4	298
8/8/2026	5:00:00	7.2	1.4839	0.3	1,433,460	15.3	297
8/8/2026	5:15:00	7.2	1.0145	0.9	1,433,479	15.3	297
8/8/2026	5:45:00	7.1	0.9804	0.3	1,433,499	15.2	295
8/8/2026	6:00:00	7.2	1.4725	0.3	1,433,521	15.1	293
8/8/2026	6:15:00	7.2	1.0221	0.4	1,433,539	15.1	293
8/8/2026	6:45:00	7.2	1.0410	0.4	1,433,558	15.1	290
8/8/2026	7:00:00	7.2	1.5596	0.6	1,433,581	14.9	288
8/8/2026	7:30:00	7.2	1.5823	1.2	1,433,601	15.1	287
8/8/2026	7:45:00	7.1	1.0902	1.3	1,433,621	15.3	287
8/8/2026	8:15:00	7.1	0.7382	2.1	1,433,640	15.2	287
8/8/2026	9:00:00	7.1	1.5558	0.6	1,433,673	14.9	283
8/8/2026	9:15:00	7.1	1.0486	0.6	1,433,693	14.9	285
8/8/2026	9:30:00	7.2	1.4915	0.9	1,433,715	14.9	285



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	9:45:00	7.2	1.0296	0.7	1,433,723	15.1	283
8/8/2026	10:00:00	7.2	1.5444	1	1,433,746	15.1	285
8/8/2026	10:30:00	7.2	1.5104	1.2	1,433,774	15.3	285
8/8/2026	10:45:00	7.2	1.0599	1.4	1,433,794	15.6	287
8/8/2026	11:15:00	7.2	1.0751	1.4	1,433,812	16	288
8/8/2026	11:30:00	7.2	1.5482	1.3	1,433,835	15.8	290
8/8/2026	12:00:00	7.2	1.5558	1.4	1,433,862	16.1	292
8/8/2026	12:30:00	7.3	1.5331	3.6	1,433,893	16.1	292
8/8/2026	13:15:00	7.3	1.0864	3.8	1,433,929	16.5	297
8/8/2026	13:30:00	7.3	1.5104	3.9	1,433,952	16.4	295
8/8/2026	13:45:00	7.2	1.0751	7.3	1,433,955	16.8	295
8/8/2026	14:00:00	7.3	1.5596	3.2	1,433,979	16.5	295
8/8/2026	14:15:00	7.2	1.1016	2	1,433,998	16.6	298
8/8/2026	14:30:00	7.2	1.5709	2.5	1,434,000	17	300
8/8/2026	14:45:00	7.3	0.7344	2.9	1,434,019	16.7	300
8/8/2026	15:00:00	7.2	1.6202	3.8	1,434,044	16.7	303
8/8/2026	15:30:00	7.2	1.6012	4.2	1,434,061	16.9	303
8/8/2026	15:45:00	7.2	1.4422	4.4	1,434,081	17	303
8/8/2026	16:15:00	7.3	1.5899	2.5	1,434,103	17	303
8/8/2026	16:30:00	7.3	1.5899	5.4	1,434,127	16.9	303
8/8/2026	17:00:00	7.3	1.6883	26.3	1,434,145	17.1	302
8/8/2026	17:15:00	7.3	1.6202	5.8	1,434,164	17	302
8/8/2026	17:30:00	7.3	1.6391	2.8	1,434,166	17.5	304
8/8/2026	17:45:00	7.3	1.5937	4.8	1,434,187	17.1	304
8/8/2026	18:00:00	7.3	1.6164	0.5	1,434,211	17	304
8/8/2026	18:30:00	7.3	1.6277	0.5	1,434,231	17.3	307
8/8/2026	19:00:00	7.3	1.6126	2.2	1,434,260	17	305
8/8/2026	19:15:00	7.3	1.6050	2.6	1,434,280	17	303
8/8/2026	19:30:00	7.3	1.5558	0	1,434,302	16.7	303
8/8/2026	20:00:00	7.3	1.6164	0.3	1,434,328	16.6	303
8/8/2026	20:15:00	7.3	1.6050	1.1	1,434,348	16.5	303
8/8/2026	20:45:00	7.3	1.5255	0.8	1,434,368	16.2	298



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	21:00:00	7.3	1.4801	0.3	1,434,390	15.9	298
8/8/2026	21:30:00	7.2	1.5331	0.5	1,434,411	15.8	295
8/8/2026	21:45:00	7.2	1.5179	1.2	1,434,430	15.7	292
8/8/2026	22:15:00	7.2	1.5255	3.3	1,434,452	15.5	292
8/8/2026	22:30:00	7.2	1.5293	3	1,434,475	15.4	290
8/8/2026	22:45:00	7.2	1.4952	1.7	1,434,478	15.6	291
8/8/2026	23:15:00	7.3	1.5104	2.4	1,434,489	15.3	287
8/8/2026	23:30:00	7.3	1.5028	1.4	1,434,511	15.1	287
8/9/2026	0:00:00	7.3	1.5028	1	1,434,536	15	287
8/9/2026	0:15:00	7.3	1.4801	2.8	1,434,555	15	287
8/9/2026	0:30:00	7.3	1.5520	1.7	1,434,577	15	287
8/9/2026	1:00:00	7.3	1.6050	1.5	1,434,592	15.4	288
8/9/2026	1:15:00	7.4	1.4574	1.9	1,434,611	15.1	288
8/9/2026	1:30:00	7.4	1.6239	1.3	1,434,632	15.1	290
8/9/2026	1:45:00	7.4	1.6164	1.4	1,434,653	15.1	290
8/9/2026	2:15:00	7.4	1.6618	0.7	1,434,678	15.3	292
8/9/2026	2:30:00	7.4	1.6088	0.7	1,434,702	15.2	290
8/9/2026	3:00:00	7.3	1.6883	0.5	1,434,709	15.3	288
8/9/2026	3:15:00	7.3	1.6807	1.3	1,434,731	15.2	288
8/9/2026	3:45:00	7.3	1.6883	0.7	1,434,756	15.1	288
8/9/2026	4:00:00	7.4	1.6883	0.8	1,434,781	14.9	288
8/9/2026	4:45:00	7.4	1.6580	1.8	1,434,815	14.9	289
8/9/2026	5:30:00	7.4	1.5785	1.1	1,434,859	14.8	291
8/9/2026	5:45:00	7.4	1.5709	0.6	1,434,878	14.9	292
8/9/2026	6:00:00	7.4	1.5558	0.5	1,434,902	14.8	291
8/9/2026	6:15:00	7.4	1.5823	1.1	1,434,904	15.1	291
8/9/2026	6:30:00	7.4	1.5444	1	1,434,927	14.7	291
8/9/2026	7:00:00	7.4	1.6050	1.3	1,434,944	14.9	291
8/9/2026	7:15:00	7.4	1.6467	1.3	1,434,964	14.8	289
8/9/2026	7:45:00	7.3	1.6959	1.5	1,434,984	14.9	290
8/9/2026	8:15:00	7.3	1.6580	1.3	1,435,010	15	287
8/9/2026	8:30:00	7.3	1.6202	0.8	1,435,035	14.7	285



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	9:00:00	7.3	1.6694	3	1,435,049	14.9	285
8/9/2026	9:30:00	7.3	1.6580	1.1	1,435,074	15	283
8/9/2026	10:00:00	7.3	1.0410	1.5	1,435,094	15	285
8/9/2026	10:15:00	7.3	1.5520	1.5	1,435,110	15.2	285
8/9/2026	10:30:00	7.3	1.5672	2.3	1,435,134	15.3	287
8/9/2026	11:00:00	7.3	1.5823	2.4	1,435,160	15.5	288
8/9/2026	11:30:00	7.3	1.3627	2.4	1,435,179	15.6	288
8/9/2026	11:45:00	7.3	1.3590	2.4	1,435,195	15.8	290
8/9/2026	12:00:00	7.3	1.3514	0.5	1,435,216	15.9	290
8/9/2026	12:15:00	7.3	1.3249	0.7	1,435,232	16	290
8/9/2026	12:45:00	7.3	1.3552	0.6	1,435,244	16.3	288
8/9/2026	13:00:00	7.4	1.3325	0.5	1,435,264	16.2	287
8/9/2026	13:15:00	7.4	1.2908	0.4	1,435,279	16.2	287
8/9/2026	13:30:00	7.4	1.2643	0	1,435,298	16.3	287
8/9/2026	14:00:00	7.4	1.2984	0	1,435,323	16.4	287
8/9/2026	14:15:00	7.4	1.2984	0	1,435,339	16.5	287
8/9/2026	14:30:00	7.4	1.2946	0.1	1,435,358	16.4	287
8/9/2026	15:00:00	7.4	1.3060	0.1	1,435,379	16.6	285
8/9/2026	15:15:00	7.4	1.2946	0.2	1,435,395	16.6	285
8/9/2026	15:30:00	7.4	1.2605	0.4	1,435,414	16.5	285
8/9/2026	16:00:00	7.4	1.2833	0.4	1,435,433	16.6	287
8/9/2026	16:15:00	7.4	1.2454	0.8	1,435,449	16.6	287
8/9/2026	16:30:00	7.4	1.2265	0.5	1,435,467	16.5	287
8/9/2026	17:00:00	7.4	1.2643	1.1	1,435,487	16.6	290
8/9/2026	17:15:00	7.4	1.2454	1.5	1,435,502	16.6	292
8/9/2026	17:30:00	7.4	1.2189	0.9	1,435,521	16.4	292
8/9/2026	17:45:00	7.4	1.2303	1.3	1,435,536	16.4	292
8/9/2026	18:00:00	7.4	1.2227	0.7	1,435,554	16.3	290
8/9/2026	18:30:00	7.5	1.5823	1.6	1,435,559	16.4	290
8/9/2026	19:00:00	7.4	1.4574	0.2	1,435,580	16.4	288
8/9/2026	19:15:00	7.4	1.4498	0	1,435,598	16.4	288
8/9/2026	19:30:00	7.4	1.4460	0.2	1,435,620	16.2	288



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	20:00:00	7.4	1.4460	0.8	1,435,640	16.3	287
8/9/2026	20:15:00	7.4	1.4271	0.9	1,435,658	16.2	287
8/9/2026	20:45:00	7.4	1.4385	0.3	1,435,679	16.1	287
8/9/2026	21:15:00	7.4	1.4498	0.2	1,435,694	16.1	285
8/9/2026	21:30:00	7.4	1.4157	0.3	1,435,716	15.7	285
8/9/2026	21:45:00	7.4	1.3552	0.8	1,435,733	15.7	285
8/9/2026	22:00:00	7.4	1.4422	1.8	1,435,735	16.1	285
8/9/2026	22:15:00	7.4	1.7791	2.4	1,435,756	15.7	287
8/9/2026	22:45:00	7.4	1.7564	2.4	1,435,782	15.6	290
8/9/2026	23:15:00	7.4	1.0448	2.8	1,435,809	15.6	293
8/9/2026	23:30:00	7.4	1.6580	2.4	1,435,833	15.4	293

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

4. CP2 Discharge Parameter Summary:

Table 3: CP2 Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	0:00:00	6.97	1.5192	0	240062	13.7	234
8/3/2026	0:15:00	6.96	2.2284	0	240083	13.7	233
8/3/2026	0:30:00	6.96	1.9842	0	240119	13.6	232
8/3/2026	0:45:00	6.95	0.9262	0	240148	13.6	232
8/3/2026	1:00:00	6.96	0.3333	0	240154	13.6	233
8/3/2026	1:15:00	6.96	0.0039	0	240158	13.7	232
8/3/2026	1:30:00	6.94	2.4686	0	240173	13.5	231
8/3/2026	1:45:00	6.93	0.1318	0	240191	13.5	231
8/3/2026	2:00:00	6.94	0.0078	0	240191	13.7	231
8/3/2026	2:15:00	6.93	0.1783	0	240192	14.2	231
8/3/2026	2:30:00	6.93	2.4144	0	240204	13.5	230
8/3/2026	2:45:00	6.94	2.4454	0	240241	13.4	230
8/3/2026	3:00:00	6.93	2.3950	0	240273	13.4	230
8/3/2026	3:15:00	6.95	2.4028	0	240307	13.4	230
8/3/2026	3:30:00	6.95	1.1200	0	240337	13.4	229
8/3/2026	3:45:00	6.96	0.5271	0	240348	13.4	230
8/3/2026	4:00:00	6.96	2.3369	0	240362	13.3	229
8/3/2026	4:15:00	6.96	0.8293	0	240393	13.3	230
8/3/2026	4:30:00	6.98	0.0078	0	240402	13.4	0
8/3/2026	5:00:00	6.95	0.3798	0	240410	13.3	231
8/3/2026	5:15:00	6.96	0.6859	0	240415	13.3	232
8/3/2026	5:30:00	6.92	0.6937	0	240423	13.3	230
8/3/2026	5:45:00	6.91	2.1315	0	240453	13.3	231
8/3/2026	6:00:00	6.9	1.9532	0	240483	13.3	231
8/3/2026	6:15:00	6.9	1.7129	0	240510	13.3	230
8/3/2026	6:30:00	6.89	0.5232	0	240529	13.3	230
8/3/2026	6:45:00	6.9	0.0698	0	240529	13.5	230
8/3/2026	7:00:00	6.9	1.3370	0	240546	13.2	230



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	7:15:00	6.88	1.1665	0	240564	13.3	232
8/3/2026	7:30:00	6.88	0.9999	0	240580	13.3	232
8/3/2026	7:45:00	6.83	2.3911	0	240604	13.3	232
8/3/2026	8:00:00	6.82	2.4570	0	240639	13.3	230
8/3/2026	8:15:00	6.84	2.4376	0	240674	13.3	230
8/3/2026	8:30:00	6.89	0.4302	0	240687	13.4	230
8/3/2026	8:45:00	6.88	0.3992	0	240694	13.5	230
8/3/2026	9:00:00	6.87	0.7325	0	240698	13.6	231
8/3/2026	9:15:00	6.88	2.4454	0	240730	13.6	227
8/3/2026	9:30:00	6.88	1.1742	0	240759	13.6	227
8/3/2026	9:45:00	6.9	0.3410	0	240769	13.7	227
8/3/2026	10:00:00	6.9	0.3062	0	240773	14.1	227
8/3/2026	10:15:00	6.88	0.7983	0	240779	14.1	227
8/3/2026	10:30:00	6.89	0.8952	0	240790	14.1	226
8/3/2026	10:45:00	6.93	1.5734	0	240811	14.1	230
8/3/2026	11:00:00	6.97	1.8176	0	240833	14.2	231
8/3/2026	11:15:00	6.98	1.2246	0	240855	14.3	232
8/3/2026	11:30:00	6.98	1.4765	0	240871	14.4	233
8/3/2026	11:45:00	6.98	1.1975	0	240891	14.5	231
8/3/2026	12:00:00	6.97	0.9146	0	240905	14.7	231
8/3/2026	12:15:00	6.98	0.9456	0	240917	14.8	231
8/3/2026	12:30:00	6.98	1.5230	0	240936	14.9	232
8/3/2026	12:45:00	6.97	1.7284	0	240966	14.8	229
8/3/2026	13:00:00	6.97	1.0541	0	240997	14.8	229
8/3/2026	13:15:00	6.98	0.0078	0	241005	15	228
8/3/2026	13:30:00	6.95	0.4108	0	241010	15.6	229
8/3/2026	13:45:00	6.95	0.6821	0	241023	15.3	230
8/3/2026	14:00:00	6.95	0.7557	0	241039	15.1	227
8/3/2026	14:15:00	6.94	2.0113	0	241054	14.9	227
8/3/2026	14:30:00	6.96	2.4338	0	241085	14.8	226
8/3/2026	14:45:00	6.97	0.9689	0	241113	14.9	225
8/3/2026	15:00:00	6.98	0.4302	0	241117	15.1	227



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	15:15:00	6.96	0.4922	0	241124	15.2	227
8/3/2026	15:30:00	6.95	0.4340	0	241131	15.4	227
8/3/2026	15:45:00	6.99	1.9920	0	241151	15.3	226
8/3/2026	16:00:00	7	1.8331	0	241182	15.2	226
8/3/2026	16:15:00	6.99	1.0502	0	241209	15	226
8/3/2026	16:30:00	6.98	0.4495	0	241217	15.1	226
8/3/2026	16:45:00	6.97	0.2984	0	241223	15.3	226
8/3/2026	17:00:00	6.97	2.0307	0	241245	15.1	227
8/3/2026	17:15:00	6.97	0.5929	0	241270	15	225
8/3/2026	17:30:00	6.96	0.4922	0	241278	15	226
8/3/2026	17:45:00	6.95	0.4457	0	241285	15.1	226
8/3/2026	18:00:00	6.94	0.4263	0	241292	15.2	227
8/3/2026	18:15:00	6.96	2.3020	0	241314	15	226
8/3/2026	18:30:00	6.97	2.3136	0	241345	14.8	225
8/3/2026	18:45:00	6.97	0.6007	0	241366	14.8	226
8/3/2026	19:00:00	6.97	0.6976	0	241374	14.8	228
8/3/2026	19:15:00	6.99	2.2865	0	241405	14.7	227
8/3/2026	19:30:00	6.99	1.1626	0	241437	14.7	226
8/3/2026	19:45:00	6.99	0.6743	0	241453	14.7	227
8/3/2026	20:00:00	6.99	1.7827	0	241459	14.8	226
8/3/2026	20:15:00	6.98	0.1744	0	241476	14.7	225
8/3/2026	20:30:00	6.97	0.6666	0	241483	14.6	225
8/3/2026	20:45:00	6.99	1.7401	0	241503	14.4	226
8/3/2026	21:00:00	7.01	1.6626	0	241534	14.3	225
8/3/2026	21:15:00	7.01	2.0695	0	241563	14.3	224
8/3/2026	21:30:00	7.02	1.8912	0	241588	14.2	223
8/3/2026	21:45:00	7.01	0.7596	0	241611	14.1	223
8/3/2026	22:00:00	7.02	0.0039	0	241616	14.4	80
8/3/2026	22:30:00	6.98	1.5850	0	241622	14.3	226
8/3/2026	22:45:00	6.99	0.5891	0	241639	14.1	227
8/3/2026	23:00:00	7	0.9960	0	241645	14	227
8/3/2026	23:15:00	6.99	1.4765	0	241670	13.8	229



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	23:30:00	6.98	2.4725	0	241702	13.7	230
8/3/2026	23:45:00	6.99	0.4147	0	241718	13.7	231
8/4/2026	0:00:00	6.98	0.5154	0	241724	13.7	232
8/4/2026	0:15:00	7	2.4570	0	241754	13.6	229
8/4/2026	0:30:00	7	2.2284	0	241789	13.6	230
8/4/2026	0:45:00	6.99	0.2790	0	241813	13.6	230
8/4/2026	1:00:00	7	0.4030	0	241821	13.6	230
8/4/2026	1:15:00	6.99	0.4263	0	241825	14.1	230
8/4/2026	1:30:00	6.98	0.5154	0	241832	14.7	231
8/4/2026	1:45:00	7	0.5232	0	241843	13.7	231
8/4/2026	2:00:00	6.99	0.1201	0	241851	13.6	231
8/4/2026	2:15:00	7	2.1857	0	241857	13.6	232
8/4/2026	2:30:00	6.99	2.3136	0	241893	13.6	233
8/4/2026	2:45:00	6.99	1.0386	0	241921	13.6	233
8/4/2026	3:00:00	7	0.0039	0	241926	13.7	232
8/4/2026	3:15:00	6.99	0.4844	0	241932	13.6	233
8/4/2026	3:30:00	6.99	2.2361	0	241957	13.5	230
8/4/2026	3:45:00	6.98	2.2245	0	241986	13.5	230
8/4/2026	4:00:00	6.98	0.5116	0	242011	13.5	229
8/4/2026	4:15:00	6.99	0.4844	0	242019	13.5	229
8/4/2026	4:30:00	6.98	0.4340	0	242022	13.5	229
8/4/2026	4:45:00	6.97	0.3255	0	242026	13.5	230
8/4/2026	5:00:00	6.97	0.1163	0	242034	13.4	229
8/4/2026	5:15:00	6.97	0.3100	0	242038	13.5	230
8/4/2026	5:30:00	6.98	2.4299	0	242050	13.5	232
8/4/2026	5:45:00	6.97	0.6821	0	242079	13.5	231
8/4/2026	6:00:00	6.97	0.4883	0	242088	13.4	233
8/4/2026	6:15:00	6.97	2.4376	0	242104	13.4	232
8/4/2026	6:30:00	6.97	2.4531	0	242138	13.5	233
8/4/2026	6:45:00	6.97	2.4454	0	242175	13.5	233
8/4/2026	7:00:00	6.98	0.6472	0	242188	13.5	234
8/4/2026	7:15:00	6.97	0.0039	0	242195	13.5	233



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	7:30:00	6.97	2.1005	0	242203	13.5	233
8/4/2026	7:45:00	6.99	2.0811	0	242234	13.5	233
8/4/2026	8:00:00	6.99	0.8371	0	242254	13.6	235
8/4/2026	8:15:00	7	1.7362	0	242280	13.6	234
8/4/2026	8:30:00	7	0.5426	0	242290	13.7	233
8/4/2026	8:45:00	7.01	0.7363	0	242309	13.8	230
8/4/2026	9:00:00	7.01	2.4919	0	242323	13.8	230
8/4/2026	9:15:00	7.03	0.4069	0	242335	13.9	229
8/4/2026	9:45:00	7.02	2.2206	0	242365	14	230
8/4/2026	10:00:00	7.04	1.2401	0	242400	14.1	231
8/4/2026	10:15:00	7.02	0.2442	0	242408	14.3	230
8/4/2026	10:30:00	7	0.0039	0	242410	14.8	233
8/4/2026	10:45:00	7	0.0039	0	242410	14.7	233
8/4/2026	11:00:00	6.99	1.1859	0	242420	14.7	233
8/4/2026	11:15:00	7.02	1.7168	0	242442	14.8	232
8/4/2026	11:30:00	7.02	2.4415	0	242470	14.7	232
8/4/2026	11:45:00	7.02	2.4531	0	242508	14.7	231
8/4/2026	12:00:00	7.02	2.4299	0	242543	14.7	233
8/4/2026	12:15:00	7.02	2.4183	0	242577	14.7	233
8/4/2026	12:30:00	7.02	0.7441	0	242594	14.9	233
8/4/2026	12:45:00	7.04	1.8718	0	242610	15.1	237
8/4/2026	13:00:00	7.04	0.3720	0	242624	15.3	238
8/4/2026	13:15:00	7.03	0.3953	0	242628	15.5	241
8/4/2026	13:30:00	7.01	2.3795	0	242638	15.5	240
8/4/2026	13:45:00	7.04	1.2169	0	242660	15.5	244
8/4/2026	14:00:00	7.04	0.9689	0	242677	15.5	247
8/4/2026	14:30:00	7.04	1.8641	0	242704	15.4	251
8/4/2026	14:45:00	7.04	2.3834	0	242735	15.2	250
8/4/2026	15:00:00	7.04	0.5736	0	242760	15.3	251
8/4/2026	15:15:00	7.04	0.5116	0	242768	15.4	251
8/4/2026	15:30:00	7.06	1.8176	0	242793	15.3	252
8/4/2026	15:45:00	7.07	0.0039	0	242802	15.6	251



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	16:00:00	7.03	0.2519	0	242804	15.7	251
8/4/2026	16:15:00	7.04	0.6472	0	242815	16.2	253
8/4/2026	16:30:00	7.03	0.8332	0	242829	15.5	250
8/4/2026	16:45:00	7.02	0.9223	0	242842	15.4	249
8/4/2026	17:00:00	7.02	2.4028	0	242873	15.2	249
8/4/2026	17:15:00	7.03	2.3718	0	242907	15.1	250
8/4/2026	17:30:00	7.04	1.2634	0	242941	15.2	249
8/4/2026	17:45:00	7.04	0.5193	0	242952	15.3	250
8/4/2026	18:00:00	7.04	0.3217	0	242957	15.4	249
8/4/2026	18:15:00	7.02	0.3255	0	242961	15.5	251
8/4/2026	18:30:00	7.04	2.3640	0	242976	15.4	248
8/4/2026	18:45:00	7.05	2.3485	0	243011	15	248
8/4/2026	19:00:00	7.03	2.2904	0	243045	14.9	249
8/4/2026	19:15:00	6.99	0.5697	0	243059	14.9	253
8/4/2026	19:30:00	6.97	0.3062	0	243063	14.9	256
8/4/2026	19:45:00	6.95	0.3682	0	243068	15	256
8/4/2026	20:00:00	6.97	0.6084	0	243088	14.8	252
8/4/2026	20:45:00	6.93	1.7711	0	243095	15	251
8/4/2026	21:00:00	6.94	0.0078	0	243108	14.5	247
8/4/2026	21:15:00	6.93	2.3059	0	243121	14.4	243
8/4/2026	21:30:00	6.93	2.2787	0	243155	14.1	235
8/4/2026	21:45:00	6.93	2.0113	0	243188	14	233
8/4/2026	22:00:00	6.93	0.2945	0	243209	14.1	234
8/4/2026	22:15:00	6.9	0.0078	0	243209	15.2	0
8/4/2026	22:30:00	6.95	1.4068	0	243218	14.3	236
8/4/2026	22:45:00	6.98	2.1354	0	243249	14.2	238
8/4/2026	23:00:00	6.99	2.1509	0	243279	14.2	237
8/4/2026	23:15:00	6.99	1.7749	0	243309	14.1	236
8/4/2026	23:30:00	6.95	0.2442	0	243318	14.2	238
8/4/2026	23:45:00	6.92	0.0078	0	243321	14.5	241
8/5/2026	0:00:00	6.95	1.2440	0	243328	14.3	236
8/5/2026	0:15:00	6.94	0.4999	0	243340	14.2	235



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	0:30:00	6.9	0.1163	0	243346	14.2	241
8/5/2026	0:45:00	6.88	0.0969	0	243346	14.2	241
8/5/2026	1:00:00	6.92	0.6239	0	243355	14.1	234
8/5/2026	1:15:00	6.95	2.2555	0	243380	13.9	233
8/5/2026	1:30:00	6.96	2.2245	0	243414	13.9	234
8/5/2026	1:45:00	6.95	0.5464	0	243434	14	233
8/5/2026	2:00:00	6.95	1.5114	0	243441	14	233
8/5/2026	2:15:00	6.96	2.2090	0	243475	13.9	233
8/5/2026	2:30:00	6.96	2.1741	0	243506	13.9	232
8/5/2026	2:45:00	6.96	0.4457	0	243524	13.9	232
8/5/2026	3:00:00	6.96	0.2054	0	243527	13.9	234
8/5/2026	3:15:00	6.95	0.6317	0	243534	13.9	233
8/5/2026	3:45:00	6.95	1.3874	0	243541	13.9	234
8/5/2026	4:00:00	6.95	0.6394	0	243563	13.8	231
8/5/2026	4:15:00	6.96	0.8875	0	243568	13.8	233
8/5/2026	4:30:00	6.96	2.0966	0	243595	13.7	230
8/5/2026	4:45:00	6.96	0.8758	0	243617	13.7	229
8/5/2026	5:00:00	6.96	0.8255	0	243631	13.7	229
8/5/2026	5:15:00	6.96	1.9881	0	243651	13.7	228
8/5/2026	5:30:00	6.96	2.4686	0	243682	13.7	229
8/5/2026	5:45:00	6.96	2.4996	0	243718	13.7	232
8/5/2026	6:00:00	6.95	2.4725	0	243755	13.7	230
8/5/2026	6:15:00	6.94	1.1200	0	243789	13.7	230
8/5/2026	6:30:00	6.94	0.4185	0	243798	13.7	232
8/5/2026	6:45:00	6.93	0.4108	0	243805	13.7	233
8/5/2026	7:00:00	6.94	2.4299	0	243819	13.6	232
8/5/2026	7:15:00	6.94	2.4299	0	243853	13.6	231
8/5/2026	7:30:00	6.94	0.6201	0	243873	13.6	231
8/5/2026	7:45:00	6.94	0.3759	0	243880	13.7	232
8/5/2026	8:00:00	6.93	0.8797	0	243887	13.7	232
8/5/2026	8:15:00	6.96	0.7053	0	243902	13.7	230
8/5/2026	8:30:00	6.95	2.4493	0	243921	13.7	226



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	8:45:00	6.94	2.4531	0	243958	13.6	225
8/5/2026	9:00:00	6.95	0.5658	0	243973	13.7	226
8/5/2026	9:15:00	6.96	0.3875	0	243980	13.8	227
8/5/2026	9:30:00	6.94	1.0231	0	243987	13.9	229
8/5/2026	9:45:00	6.95	2.3640	0	244021	13.8	224
8/5/2026	10:00:00	6.95	0.9921	0	244051	13.9	224
8/5/2026	10:15:00	6.96	0.3604	0	244061	14	225
8/5/2026	10:30:00	6.94	0.8255	0	244068	14.1	226
8/5/2026	10:45:00	6.95	0.1976	0	244072	14.5	223
8/5/2026	11:00:00	6.94	0.6743	0	244083	14.4	223
8/5/2026	11:15:00	6.94	2.1974	0	244095	14.4	223
8/5/2026	11:30:00	6.95	0.5619	0	244107	14.3	222
8/5/2026	11:45:00	6.95	2.4493	0	244123	14.5	223
8/5/2026	12:00:00	6.96	2.4415	0	244160	14.4	222
8/5/2026	12:15:00	6.97	2.4570	0	244197	14.5	222
8/5/2026	12:30:00	6.99	2.4493	0	244235	14.6	225
8/5/2026	12:45:00	6.98	0.6472	0	244253	14.7	223
8/5/2026	13:00:00	6.98	0.3759	0	244261	14.9	225
8/5/2026	13:15:00	6.96	0.4108	0	244268	15.2	227
8/5/2026	13:30:00	6.97	1.0851	0	244279	15.3	226
8/5/2026	13:45:00	6.98	0.2442	0	244288	15.4	228
8/5/2026	14:00:00	6.97	1.0657	1	244303	15.2	230
8/5/2026	14:15:00	6.96	2.4686	0	244319	15	231
8/5/2026	14:30:00	6.97	0.5852	0	244338	15.1	230
8/5/2026	14:45:00	6.96	0.4418	0	244345	15.3	230
8/5/2026	15:00:00	6.97	2.4609	0	244365	15.3	229
8/5/2026	15:15:00	6.97	2.4648	0	244403	15	226
8/5/2026	15:30:00	6.98	1.1006	0	244437	15	226
8/5/2026	15:45:00	6.98	0.4302	0	244446	15.2	226
8/5/2026	16:00:00	6.97	0.3798	0	244453	15.3	227
8/5/2026	16:15:00	6.97	0.9340	0	244462	15.4	227
8/5/2026	16:30:00	6.96	2.2477	0	244472	15.5	225



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	16:45:00	6.98	2.4299	0	244508	15	223
8/5/2026	17:00:00	6.98	0.6433	0	244523	15	224
8/5/2026	17:15:00	6.99	0.4340	0	244530	15.4	226
8/5/2026	17:30:00	6.97	2.4609	0	244541	15.5	223
8/5/2026	17:45:00	6.98	2.4260	0	244575	14.8	222
8/5/2026	18:00:00	6.99	1.1626	0	244611	14.6	222
8/5/2026	18:15:00	6.99	0.4224	0	244622	14.8	223
8/5/2026	18:30:00	6.98	0.4379	0	244629	14.9	223
8/5/2026	18:45:00	6.98	2.4299	0	244645	14.8	223
8/5/2026	19:00:00	6.98	2.4570	0	244682	14.4	222
8/5/2026	19:15:00	6.98	0.9301	0	244711	14.3	222
8/5/2026	19:30:00	6.99	0.3643	0	244720	14.4	222
8/5/2026	19:45:00	6.98	0.4340	0	244726	14.5	224
8/5/2026	20:00:00	6.97	0.9107	0	244733	14.5	222
8/5/2026	20:15:00	6.99	1.1161	0	244763	14.2	221
8/5/2026	20:45:00	6.99	0.0271	0	244772	15.9	0
8/5/2026	21:00:00	6.97	0.0116	0	244772	17	0
8/5/2026	21:15:00	6.99	0.4961	0	244787	14.4	220
8/5/2026	21:30:00	6.99	0.1783	0	244794	14.3	220
8/5/2026	21:45:00	6.99	0.7402	23	244802	14.2	220
8/5/2026	22:00:00	7.01	0.9107	0	244817	14.1	218
8/5/2026	22:15:00	7.03	0.0155	0	244826	14.2	222
8/5/2026	22:30:00	7.04	1.9532	0	244837	14.2	222
8/5/2026	22:45:00	7.05	2.4725	0	244868	14.2	223
8/5/2026	23:00:00	7.05	2.4531	0	244906	14.1	225
8/5/2026	23:15:00	7.04	0.6317	0	244929	14.2	223
8/5/2026	23:30:00	7.04	0.3914	0	244937	14.2	222
8/5/2026	23:45:00	7.04	0.0194	0	244937	15.3	0
8/6/2026	0:00:00	7.01	0.0271	0	244937	16.3	0
8/6/2026	0:15:00	7.01	0.7596	0	244939	14.8	222
8/6/2026	0:30:00	7.02	0.7014	0	244955	14.1	222
8/6/2026	0:45:00	7.01	0.2442	0	244963	14.1	223



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	1:00:00	7.02	2.4493	0	244979	14	222
8/6/2026	1:15:00	7.04	2.4531	0	245016	13.9	224
8/6/2026	1:30:00	7.05	1.0309	0	245047	14	222
8/6/2026	1:45:00	7.06	0.4263	2	245057	14.1	222
8/6/2026	2:00:00	7.06	0.5852	0	245067	14	222
8/6/2026	2:15:00	7.06	0.4767	0	245072	14	222
8/6/2026	2:30:00	7.05	0.7170	0	245094	14	222
8/6/2026	2:45:00	7.04	0.3875	0	245101	14	222
8/6/2026	3:00:00	7.03	0.0194	0	245102	14.6	222
8/6/2026	3:15:00	7.06	0.5154	0	245118	14	223
8/6/2026	3:30:00	7.05	0.7441	0	245125	13.9	222
8/6/2026	3:45:00	7.05	0.7131	0	245145	13.9	223
8/6/2026	4:00:00	7.06	0.4185	0	245153	13.9	222
8/6/2026	4:15:00	7.06	2.4531	0	245168	13.9	222
8/6/2026	4:30:00	7.06	1.9455	0	245202	13.8	223
8/6/2026	4:45:00	7.06	2.3446	0	245229	13.8	224
8/6/2026	5:00:00	7.05	0.6821	0	245247	13.8	224
8/6/2026	5:15:00	7.06	0.4612	0	245255	13.9	226
8/6/2026	5:30:00	7.05	0.4263	0	245262	13.8	225
8/6/2026	5:45:00	7.04	0.7635	0	245269	13.8	226
8/6/2026	6:00:00	7.06	2.4299	0	245301	13.7	226
8/6/2026	6:15:00	7.05	0.9456	0	245330	13.7	226
8/6/2026	6:30:00	7.05	0.3914	0	245339	13.8	227
8/6/2026	6:45:00	7.04	0.3294	0	245344	13.8	229
8/6/2026	7:00:00	7.03	0.4302	0	245350	13.8	229
8/6/2026	7:15:00	7.03	0.4728	0	245356	13.8	229
8/6/2026	7:30:00	7.03	0.4534	0	245363	13.8	228
8/6/2026	7:45:00	7.03	2.3330	0	245373	13.8	228
8/6/2026	8:00:00	7.04	0.6472	0	245387	13.8	227
8/6/2026	8:15:00	7.04	0.5232	0	245396	13.9	226
8/6/2026	8:30:00	7.02	0.8952	0	245404	13.9	226
8/6/2026	8:45:00	7.02	0.8177	0	245421	14	224



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	9:00:00	7.01	0.9921	1	245433	14.1	222
8/6/2026	9:15:00	6.99	0.9727	0	245447	14	222
8/6/2026	9:30:00	7	2.4183	0	245479	14	221
8/6/2026	9:45:00	7.01	0.3992	0	245502	14.1	221
8/6/2026	10:00:00	7.02	0.3100	0	245509	14.2	220
8/6/2026	10:15:00	7.02	0.0271	0	245511	14.7	220
8/6/2026	10:30:00	7.01	1.9842	0	245524	14.6	221
8/6/2026	10:45:00	7.03	0.9727	0	245549	14.5	222
8/6/2026	11:00:00	7.04	0.3643	0	245558	14.6	222
8/6/2026	11:15:00	7.03	1.7672	0	245568	14.8	224
8/6/2026	11:30:00	7.02	0.6433	0	245580	14.9	222
8/6/2026	11:45:00	7.03	2.5539	0	245607	14.8	225
8/6/2026	12:00:00	7.04	2.5345	0	245644	14.8	224
8/6/2026	12:15:00	7.03	2.5423	0	245681	14.8	224
8/6/2026	12:30:00	7.03	0.9650	0	245709	14.9	226
8/6/2026	12:45:00	7.04	0.3875	0	245718	15.2	227
8/6/2026	13:00:00	7.02	0.4185	0	245725	15.5	228
8/6/2026	13:15:00	7	0.7596	0	245732	15.7	229
8/6/2026	13:30:00	7.01	2.5190	0	245765	15.3	226
8/6/2026	13:45:00	6.99	0.7014	0	245793	15.3	227
8/6/2026	14:00:00	7.01	0.3837	0	245801	15.5	229
8/6/2026	14:15:00	6.99	0.0465	0	245806	15.8	230
8/6/2026	14:30:00	6.98	0.7983	0	245815	15.8	227
8/6/2026	14:45:00	6.99	0.3333	0	245821	15.8	228
8/6/2026	15:00:00	6.98	0.5542	0	245831	15.7	230
8/6/2026	15:15:00	6.97	0.4612	0	245838	15.8	230
8/6/2026	15:30:00	6.96	0.8565	3	245849	15.8	227
8/6/2026	15:45:00	6.95	0.4224	0	245858	15.6	225
8/6/2026	16:00:00	6.96	2.0385	0	245881	15.3	227
8/6/2026	16:15:00	6.97	2.5461	0	245918	15.2	226
8/6/2026	16:30:00	6.98	0.7790	0	245934	15.3	226
8/6/2026	16:45:00	6.99	0.3720	0	245942	15.5	227



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	17:00:00	7	0.4612	0	245949	15.9	227
8/6/2026	17:15:00	6.99	2.5229	0	245971	15.7	227
8/6/2026	17:30:00	6.98	0.9030	0	245993	15.5	227
8/6/2026	17:45:00	6.98	0.6937	0	246002	15.6	229
8/6/2026	18:00:00	6.99	0.4185	0	246009	15.7	228
8/6/2026	18:15:00	6.97	0.8642	0	246016	15.8	228
8/6/2026	18:30:00	6.97	2.4996	0	246050	15.1	227
8/6/2026	18:45:00	6.98	0.5077	0	246062	15.1	229
8/6/2026	19:00:00	6.97	0.4302	0	246069	15.2	227
8/6/2026	19:15:00	6.96	2.1974	0	246077	15.2	229
8/6/2026	19:30:00	6.94	2.4338	0	246115	14.7	226
8/6/2026	20:00:00	6.96	0.0310	0	246125	16.6	0
8/6/2026	20:15:00	6.93	0.0349	0	246125	17.7	0
8/6/2026	20:30:00	6.92	0.0426	0	246125	18.6	0
8/6/2026	20:45:00	6.96	0.6666	0	246135	14.8	228
8/6/2026	21:00:00	6.96	0.0891	0	246140	14.7	224
8/6/2026	21:15:00	6.96	1.4300	0	246153	14.5	225
8/6/2026	21:30:00	6.96	1.4145	0	246173	14.3	226
8/6/2026	21:45:00	6.98	2.4686	0	246200	14.2	226
8/6/2026	22:00:00	7	1.9261	0	246233	14.2	225
8/6/2026	22:15:00	7.01	0.0349	0	246246	14.3	223
8/6/2026	22:30:00	7.01	2.4144	0	246257	14.3	228
8/6/2026	22:45:00	7.01	2.4105	0	246291	14.2	228
8/6/2026	23:00:00	7.01	1.3254	0	246325	14.2	229
8/6/2026	23:15:00	7.02	0.3914	0	246336	14.3	228
8/6/2026	23:30:00	7.01	0.0465	0	246337	15.4	227
8/6/2026	23:45:00	7.03	0.0271	0	246337	15	13
8/7/2026	0:00:00	6.99	1.8176	0	246342	14.6	227
8/7/2026	0:15:00	6.98	2.2090	0	246371	14.2	227
8/7/2026	0:30:00	6.99	0.5697	0	246386	14.2	227
8/7/2026	0:45:00	6.98	0.3217	0	246391	14.3	228
8/7/2026	1:00:00	6.97	1.7517	0	246397	14.3	227



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	1:45:00	6.96	0.2015	0	246406	14.4	226
8/7/2026	2:00:00	6.97	0.7363	0	246414	14.2	229
8/7/2026	2:15:00	6.96	0.7518	0	246425	14.1	228
8/7/2026	2:30:00	6.96	2.1896	0	246435	14.1	228
8/7/2026	2:45:00	6.97	1.7013	0	246467	14	230
8/7/2026	3:00:00	6.98	1.5773	0	246491	14.1	231
8/7/2026	3:15:00	7	2.5306	0	246519	14.1	232
8/7/2026	3:30:00	7.02	2.5074	0	246556	14.1	233
8/7/2026	3:45:00	7.02	0.6356	0	246578	14.2	232
8/7/2026	4:00:00	7.02	0.3643	0	246586	14.2	232
8/7/2026	4:15:00	7.01	0.3953	0	246592	14.2	232
8/7/2026	4:30:00	7.01	0.0310	0	246595	14.6	231
8/7/2026	4:45:00	7.03	0.5348	0	246606	14.3	233
8/7/2026	5:00:00	7.03	0.2674	0	246610	14.3	235
8/7/2026	5:15:00	7.01	0.1511	0	246614	14.3	234
8/7/2026	5:30:00	7	2.5461	0	246631	14.2	237
8/7/2026	5:45:00	7	2.5268	0	246668	14.1	235
8/7/2026	6:00:00	7.01	2.4686	0	246706	14.1	237
8/7/2026	6:15:00	7.01	0.5929	0	246723	14.2	236
8/7/2026	6:30:00	7.01	0.4728	0	246730	14.2	237
8/7/2026	6:45:00	7.03	1.0580	0	246755	14.1	235
8/7/2026	7:00:00	7.02	0.6317	0	246766	14.2	234
8/7/2026	7:15:00	7.01	0.5232	0	246775	14.2	237
8/7/2026	7:30:00	7.02	2.5500	0	246788	14.2	236
8/7/2026	7:45:00	7.03	2.5229	0	246825	14.1	236
8/7/2026	8:00:00	7.02	0.8720	0	246853	14.2	236
8/7/2026	8:15:00	7.01	0.1240	0	246856	14.4	237
8/7/2026	8:30:00	7.02	2.5423	0	246889	14.2	232
8/7/2026	8:45:00	7	0.3992	0	246913	14.3	233
8/7/2026	9:00:00	7	0.4457	0	246921	14.4	233
8/7/2026	9:15:00	7	0.8061	0	246928	14.5	233
8/7/2026	9:30:00	7.02	0.8797	0	246953	14.6	236



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	9:45:00	7.02	1.7633	0	246963	14.7	238
8/7/2026	10:00:00	7.03	0.0271	0	246975	14.9	238
8/7/2026	10:15:00	7.02	0.0233	0	246975	16	220
8/7/2026	10:30:00	7.02	0.0116	0	246975	15.9	236
8/7/2026	10:45:00	6.99	0.3875	0	246976	15.4	241
8/7/2026	11:00:00	6.99	0.6666	0	246984	15.4	239
8/7/2026	11:15:00	6.99	0.7441	0	246996	15.4	235
8/7/2026	11:30:00	6.99	1.1045	0	247030	15.2	234
8/7/2026	11:45:00	7	0.4224	0	247041	15.3	233
8/7/2026	12:00:00	6.99	0.3953	0	247048	15.6	234
8/7/2026	12:15:00	6.97	1.0347	0	247055	15.8	234
8/7/2026	12:30:00	7.01	2.5306	0	247090	15.8	237
8/7/2026	12:45:00	6.99	0.8875	0	247113	15.9	237
8/7/2026	13:00:00	7	1.1200	0	247135	15.7	237
8/7/2026	13:15:00	7.01	2.5423	0	247156	15.7	236
8/7/2026	13:30:00	7.02	2.5423	0	247193	15.5	233
8/7/2026	13:45:00	7.02	0.4457	0	247221	15.7	232
8/7/2026	14:00:00	7.02	0.4302	0	247228	15.9	233
8/7/2026	14:15:00	7.01	0.4147	0	247235	16.2	233
8/7/2026	14:30:00	6.99	0.4612	0	247242	16.3	234
8/7/2026	14:45:00	7.02	2.5461	0	247264	16.1	231
8/7/2026	15:00:00	6.98	1.9765	0	247301	15.8	231
8/7/2026	15:15:00	6.95	1.9726	0	247331	15.5	228
8/7/2026	15:30:00	6.94	0.5348	0	247354	15.4	230
8/7/2026	15:45:00	6.96	0.3759	0	247362	15.6	231
8/7/2026	16:00:00	6.94	0.3139	0	247367	15.8	232
8/7/2026	16:15:00	6.93	0.3643	0	247371	15.9	233
8/7/2026	16:30:00	6.93	0.4457	0	247378	16.1	233
8/7/2026	16:45:00	6.93	2.0268	0	247402	15.7	229
8/7/2026	17:00:00	6.92	0.6782	0	247428	15.2	227
8/7/2026	17:15:00	6.95	0.3139	0	247433	15.4	228
8/7/2026	17:30:00	6.93	0.3410	0	247437	15.5	230



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	17:45:00	6.92	0.4069	0	247443	15.7	230
8/7/2026	18:00:00	6.92	0.4418	0	247450	15.8	233
8/7/2026	18:15:00	6.93	0.4767	0	247458	15.8	229
8/7/2026	18:30:00	6.92	0.9185	3	247468	15.6	228
8/7/2026	18:45:00	6.91	2.5423	0	247486	15	228
8/7/2026	19:00:00	6.93	2.5655	0	247523	14.7	229
8/7/2026	19:15:00	6.95	0.9805	0	247553	14.8	230
8/7/2026	19:30:00	6.96	0.6046	0	247563	14.9	229
8/7/2026	19:45:00	6.99	2.5500	0	247588	14.9	233
8/7/2026	20:00:00	7.02	2.5616	0	247625	14.9	233
8/7/2026	20:15:00	7.01	0.6123	0	247651	14.9	232
8/7/2026	20:30:00	7.01	0.5271	0	247659	15	233
8/7/2026	20:45:00	6.99	0.8410	0	247667	14.9	233
8/7/2026	21:00:00	7.03	0.0233	0	247673	15.5	0
8/7/2026	21:15:00	7.01	0.0349	0	247673	15.3	232
8/7/2026	21:30:00	6.97	0.1938	0	247673	15	233
8/7/2026	21:45:00	7.02	2.0191	0	247700	14.5	230
8/7/2026	22:00:00	7.02	0.0194	0	247722	14.4	228
8/7/2026	22:15:00	7.02	0.5193	0	247730	14.4	230
8/7/2026	22:30:00	7.01	0.4573	0	247737	14.4	230
8/7/2026	22:45:00	7	1.1122	0	247747	14.4	228
8/7/2026	23:00:00	7	1.1704	0	247764	14.2	228
8/7/2026	23:15:00	7	0.9805	0	247783	14.2	230
8/7/2026	23:45:00	7.01	0.4418	0	247788	14.3	230
8/8/2026	0:00:00	6.99	1.9610	0	247797	14.2	231
8/8/2026	0:15:00	7.01	0.6976	0	247818	14.1	232
8/8/2026	0:30:00	7.01	0.0891	0	247822	14.2	233
8/8/2026	0:45:00	7.01	2.4183	0	247838	14.1	233
8/8/2026	1:00:00	7.02	2.4221	0	247873	14	237
8/8/2026	1:15:00	7.02	0.6704	0	247893	14	237
8/8/2026	1:30:00	7.02	0.4147	0	247900	14.1	237
8/8/2026	1:45:00	7	0.9301	0	247908	14.1	237



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	2:00:00	7.01	0.6123	0	247929	14	236
8/8/2026	2:15:00	7.01	0.7363	0	247934	14.1	237
8/8/2026	2:30:00	7.01	2.4183	0	247965	13.9	235
8/8/2026	2:45:00	7	0.7131	0	247989	13.9	234
8/8/2026	3:00:00	7.01	0.3720	0	247997	14	236
8/8/2026	3:15:00	7	0.4069	0	248004	14	235
8/8/2026	3:30:00	6.99	0.8991	0	248012	14	235
8/8/2026	3:45:00	6.99	0.9030	0	248025	13.9	233
8/8/2026	4:00:00	7.01	1.2285	0	248041	13.9	232
8/8/2026	4:15:00	7.01	0.6511	0	248052	13.9	233
8/8/2026	4:30:00	7.01	2.3989	0	248079	13.9	232
8/8/2026	4:45:00	7	2.4144	0	248113	13.9	233
8/8/2026	5:00:00	7.02	0.5774	0	248125	13.9	233
8/8/2026	5:15:00	7.01	0.1705	0	248130	13.9	231
8/8/2026	5:30:00	6.99	2.3950	0	248143	13.9	233
8/8/2026	5:45:00	6.99	2.3989	0	248177	13.7	230
8/8/2026	6:00:00	6.99	0.8797	0	248203	13.7	230
8/8/2026	6:15:00	7.01	0.4844	0	248212	13.8	231
8/8/2026	6:30:00	7	0.5154	0	248219	13.8	232
8/8/2026	6:45:00	7	2.3718	0	248248	13.7	228
8/8/2026	7:00:00	7	2.3679	0	248282	13.7	228
8/8/2026	7:15:00	7.01	0.6084	0	248297	13.7	228
8/8/2026	7:30:00	7.01	0.4185	0	248304	13.8	229
8/8/2026	7:45:00	7	0.3759	0	248311	13.8	229
8/8/2026	8:00:00	6.99	0.5852	0	248319	13.8	229
8/8/2026	8:15:00	6.99	2.2787	0	248329	13.9	229
8/8/2026	8:30:00	6.99	0.1976	0	248342	13.9	229
8/8/2026	8:45:00	6.97	0.0116	0	248345	14.3	110
8/8/2026	9:00:00	6.96	0.8875	0	248350	14.2	225
8/8/2026	9:15:00	6.96	1.8679	0	248365	13.9	225
8/8/2026	9:30:00	6.95	2.3911	0	248397	13.8	226
8/8/2026	9:45:00	6.96	2.3795	0	248431	13.9	225



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	10:00:00	6.97	0.5193	0	248449	14	227
8/8/2026	10:15:00	6.98	0.5038	0	248452	14.3	227
8/8/2026	10:30:00	6.99	2.3718	0	248477	14.3	227
8/8/2026	10:45:00	6.99	0.7208	0	248495	14.4	228
8/8/2026	11:00:00	6.99	0.3333	0	248502	14.6	229
8/8/2026	11:15:00	6.98	0.3449	0	248506	14.8	231
8/8/2026	11:30:00	6.96	0.4108	0	248513	15	231
8/8/2026	11:45:00	6.97	0.8022	0	248520	15.3	230
8/8/2026	12:00:00	7.01	0.0271	0	248524	15.8	0
8/8/2026	12:15:00	6.96	0.8216	7	248531	15.4	232
8/8/2026	12:30:00	6.95	2.3485	0	248561	15.1	233
8/8/2026	12:45:00	6.97	2.3214	0	248595	15.2	233
8/8/2026	13:00:00	6.98	0.6084	0	248621	15.3	233
8/8/2026	13:15:00	6.99	0.0155	0	248624	16.1	0
8/8/2026	13:30:00	6.99	2.2787	0	248635	15.8	233
8/8/2026	13:45:00	6.99	0.6317	0	248661	15.7	234
8/8/2026	14:00:00	6.99	0.3062	0	248669	15.9	234
8/8/2026	14:15:00	6.98	0.2364	0	248672	16.2	235
8/8/2026	14:30:00	6.96	0.2209	0	248676	16.4	236
8/8/2026	14:45:00	6.96	1.6897	0	248680	16.5	237
8/8/2026	15:00:00	6.98	0.0271	0	248684	16.5	237
8/8/2026	15:15:00	6.96	0.6666	2	248688	17.2	232
8/8/2026	15:30:00	6.96	2.1702	0	248704	15.9	239
8/8/2026	15:45:00	6.96	0.3449	0	248729	15.9	239
8/8/2026	16:00:00	6.98	2.1780	0	248753	15.9	240
8/8/2026	16:15:00	6.98	1.8990	0	248784	15.9	241
8/8/2026	16:30:00	6.97	2.0578	0	248813	15.9	240
8/8/2026	16:45:00	6.97	1.9958	0	248843	15.8	239
8/8/2026	17:00:00	6.97	0.6588	0	248864	15.8	241
8/8/2026	17:15:00	6.99	0.0310	0	248868	16.4	238
8/8/2026	17:30:00	6.96	0.1899	0	248874	16.3	241
8/8/2026	17:45:00	6.97	1.9183	0	248880	16.1	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	18:00:00	6.97	1.0502	0	248906	15.8	243
8/8/2026	18:15:00	6.98	0.4069	0	248916	15.8	241
8/8/2026	18:30:00	6.98	0.1279	0	248921	16	242
8/8/2026	18:45:00	6.97	0.1201	0	248925	16.1	244
8/8/2026	19:00:00	6.97	1.3021	0	248939	15.9	244
8/8/2026	19:15:00	6.97	1.5928	0	248962	15.5	241
8/8/2026	19:30:00	6.96	2.4221	0	248993	15.1	239
8/8/2026	19:45:00	6.96	2.4221	0	249026	14.8	236
8/8/2026	20:00:00	6.97	0.9068	0	249053	14.8	237
8/8/2026	20:15:00	6.98	0.3953	0	249061	14.8	237
8/8/2026	20:30:00	6.97	0.4147	0	249068	14.8	236
8/8/2026	20:45:00	6.96	0.4844	0	249075	14.8	237
8/8/2026	21:00:00	6.98	2.3718	0	249100	14.5	233
8/8/2026	21:15:00	6.98	0.6201	0	249121	14.4	232
8/8/2026	21:30:00	6.99	0.3914	0	249128	14.4	234
8/8/2026	21:45:00	6.97	0.4302	0	249135	14.5	233
8/8/2026	22:00:00	6.97	0.7983	0	249142	14.5	234
8/8/2026	22:15:00	6.97	2.3679	0	249173	14.1	226
8/8/2026	22:30:00	6.98	0.5038	0	249187	14.1	227
8/8/2026	22:45:00	6.98	0.3643	0	249194	14.1	228
8/8/2026	23:00:00	6.97	0.3992	0	249201	14.2	228
8/8/2026	23:15:00	6.97	0.1783	0	249207	14.2	228
8/8/2026	23:30:00	6.97	0.2752	0	249211	14.2	230
8/8/2026	23:45:00	6.97	0.8177	0	249218	14.2	228
8/9/2026	0:00:00	6.96	0.7983	0	249228	14	225
8/9/2026	0:15:00	6.99	0.7441	0	249244	13.9	224
8/9/2026	0:30:00	7	2.4066	0	249274	13.9	225
8/9/2026	0:45:00	6.99	2.4183	0	249308	13.8	226
8/9/2026	1:00:00	6.99	1.2518	0	249342	13.8	227
8/9/2026	1:15:00	7	0.5891	0	249354	13.9	227
8/9/2026	1:30:00	6.99	2.3950	0	249368	13.8	228
8/9/2026	1:45:00	6.96	2.3718	0	249402	13.7	228



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	2:00:00	6.96	0.0233	0	249419	13.7	228
8/9/2026	2:15:00	6.97	0.2829	0	249419	13.9	228
8/9/2026	2:30:00	6.95	2.1354	0	249446	13.6	228
8/9/2026	2:45:00	6.96	0.6511	0	249470	13.6	228
8/9/2026	3:00:00	6.98	0.0233	0	249474	13.6	229
8/9/2026	3:15:00	6.98	0.0194	0	249474	13.7	229
8/9/2026	3:30:00	6.97	0.3682	4	249480	13.7	229
8/9/2026	3:45:00	6.99	0.4108	0	249485	13.6	228
8/9/2026	4:00:00	7.01	0.0233	0	249493	13.6	225
8/9/2026	4:15:00	7.01	1.0735	0	249499	13.6	229
8/9/2026	4:30:00	7	2.3911	0	249532	13.5	230
8/9/2026	4:45:00	7	1.0502	0	249561	13.5	230
8/9/2026	5:00:00	7.03	0.0233	0	249566	13.9	228
8/9/2026	5:15:00	7	1.8718	0	249585	13.6	230
8/9/2026	5:30:00	7	0.5503	0	249611	13.5	230
8/9/2026	5:45:00	7.01	0.4030	0	249619	13.6	230
8/9/2026	6:00:00	7	0.4069	0	249626	13.6	232
8/9/2026	6:15:00	6.99	0.4806	0	249633	13.5	231
8/9/2026	6:30:00	7.01	2.4105	0	249655	13.5	231
8/9/2026	6:45:00	7.01	2.4183	0	249689	13.5	232
8/9/2026	7:00:00	7.01	0.8603	0	249703	13.6	230
8/9/2026	7:15:00	7	2.0423	0	249714	13.6	231
8/9/2026	7:30:00	7.01	0.6356	0	249733	13.6	232
8/9/2026	7:45:00	7	1.8679	0	249740	13.7	232
8/9/2026	8:00:00	7.07	0.1201	0	249743	14.4	226
8/9/2026	8:15:00	6.99	1.9300	0	249751	14	227
8/9/2026	8:30:00	7	1.9145	0	249778	13.8	227
8/9/2026	8:45:00	7.02	1.2750	0	249812	13.9	229
8/9/2026	9:00:00	7.02	0.6394	0	249824	13.9	228
8/9/2026	9:15:00	7.03	1.9028	0	249838	14.1	230
8/9/2026	9:30:00	7.02	0.4379	0	249859	14.1	226
8/9/2026	9:45:00	7.02	0.2790	0	249860	14.4	226



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	10:00:00	7.01	0.4922	0	249868	14.3	226
8/9/2026	10:15:00	7.01	0.5542	0	249875	14.7	227
8/9/2026	10:30:00	7	2.4454	0	249902	14.4	231
8/9/2026	10:45:00	7	2.4376	0	249939	14.4	232
8/9/2026	11:00:00	7	1.9028	0	249970	14.5	231
8/9/2026	11:15:00	7	0.6976	0	249994	14.6	232
8/9/2026	11:30:00	7.01	0.4999	0	250001	14.8	233
8/9/2026	11:45:00	6.99	0.8642	0	250015	14.9	234
8/9/2026	12:00:00	6.97	0.9030	0	250029	15	235
8/9/2026	12:15:00	6.96	2.4105	0	250057	14.8	233
8/9/2026	12:30:00	6.98	0.5077	0	250069	15	233
8/9/2026	12:45:00	6.99	0.0271	0	250073	15.5	234
8/9/2026	13:00:00	6.97	1.8912	0	250080	15.4	234
8/9/2026	13:15:00	6.99	0.6588	0	250092	15.3	232
8/9/2026	13:30:00	6.98	2.3718	0	250106	15.3	234
8/9/2026	13:45:00	6.97	2.4066	0	250140	15.1	232
8/9/2026	14:00:00	6.97	1.8873	0	250168	15	232
8/9/2026	14:15:00	6.98	0.4263	0	250187	15.2	232
8/9/2026	14:30:00	6.99	0.4612	0	250189	15.9	231
8/9/2026	14:45:00	6.97	2.3679	0	250213	15.2	228
8/9/2026	15:00:00	6.97	0.6201	0	250232	15	232
8/9/2026	15:15:00	6.98	0.0349	0	250234	15.7	229
8/9/2026	15:30:00	6.96	1.8873	0	250245	15.2	230
8/9/2026	15:45:00	6.96	2.3873	0	250275	14.8	231
8/9/2026	16:00:00	6.96	0.7053	0	250293	14.7	232
8/9/2026	16:15:00	6.97	0.6627	0	250302	14.8	232
8/9/2026	16:30:00	6.97	2.3756	0	250332	14.6	234
8/9/2026	16:45:00	6.99	1.8679	0	250363	14.6	238
8/9/2026	17:00:00	7	0.6084	0	250381	14.6	237
8/9/2026	17:15:00	7.01	0.4728	0	250388	14.7	238
8/9/2026	17:30:00	7	2.3640	0	250400	14.7	239
8/9/2026	17:45:00	7.02	0.8371	0	250428	14.6	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	18:00:00	7.02	0.2131	0	250436	14.7	240
8/9/2026	18:15:00	7.02	0.3604	0	250443	14.8	240
8/9/2026	18:30:00	7.01	0.4224	0	250450	14.9	241
8/9/2026	18:45:00	7.01	2.3873	0	250462	14.8	241
8/9/2026	19:00:00	7.02	2.3640	0	250496	14.6	236
8/9/2026	19:15:00	7.01	1.8602	0	250526	14.5	234
8/9/2026	19:30:00	7	1.1549	0	250553	14.4	234
8/9/2026	19:45:00	7.01	0.4457	0	250564	14.5	234
8/9/2026	20:00:00	7	0.3604	0	250570	14.5	234
8/9/2026	20:15:00	7.02	0.0233	0	250573	15.4	0
8/9/2026	20:30:00	6.99	0.0310	0	250573	16.6	0
8/9/2026	20:45:00	6.97	0.0388	0	250574	17.4	237
8/9/2026	21:00:00	6.96	0.1938	0	250577	17.8	236
8/9/2026	21:15:00	6.96	0.7828	4	250585	14.6	232
8/9/2026	21:30:00	6.93	0.2868	0	250592	14.2	231
8/9/2026	21:45:00	6.91	1.8602	0	250619	13.9	229
8/9/2026	22:00:00	6.91	2.3562	0	250649	13.9	230
8/9/2026	22:15:00	6.95	0.6162	0	250662	13.9	231
8/9/2026	22:30:00	6.95	2.3446	0	250676	14	232
8/9/2026	22:45:00	6.95	1.8098	0	250705	13.9	235
8/9/2026	23:00:00	6.95	1.7982	0	250733	14	234
8/9/2026	23:15:00	6.97	0.4844	0	250746	14	236
8/9/2026	23:30:00	6.96	0.4573	0	250753	14.1	237
8/9/2026	23:45:00	6.97	2.2904	0	250780	14	237

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

5. In-Situ Readings

Table 4. In-Situ Readings

Date	Temperature (C°)	DO mg/L	SAL-ppt	pH	ORP (mV)	NTU
08/03/2026	15.6	9.74	0.09	7.28	167.9	0.49
08/04/2026	13.9	9.74	0.09	7.08	181.0	0.30
08/05/2026	15.2	9.86	0.10	7.30	105.6	0.62
08/06/2026	15.1	9.42	0.09	7.10	215.4	0.33
08/07/2026	15.3	9.86	0.09	7.19	102.6	0.88
08/08/2026	15.0	9.54	0.09	7.07	182.0	0.24
08/09/2026	13.9	10.57	0.09	7.15	179.1	1.16

6. Calibration Log:

Table 5. Calibration Log

Date	Unit	pH	Conductivity/ Salinity	NTU
08/08/2026	YSI	✓	✓	✓
08/08/2026	Portal WTP	✓	N/A	✓
08/05/2026	CP2 WTP	✓	✓	✓

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

APPENDIX A: Portal WTP Data Log



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	0:00:00	7.4	1.6050	1	1,426,843	Open	15.3	324
8/3/2026	0:15:00	7.3	0.0000	1	1,426,846	Closed	15.6	322
8/3/2026	0:30:00	7.4	1.5823	0.9	1,426,863	Open	15.2	324
8/3/2026	0:45:00	7.3	0.0000	3.1	1,426,876	Closed	15.3	323
8/3/2026	1:00:00	7.3	1.6315	2.4	1,426,878	Open	15.5	323
8/3/2026	1:15:00	7.4	1.6050	2	1,426,903	Open	15.1	321
8/3/2026	1:30:00	7.3	0.0000	1.4	1,426,909	Closed	15.3	321
8/3/2026	1:45:00	7.3	1.6164	1.8	1,426,922	Open	15	318
8/3/2026	2:00:00	7.3	0.8517	1.7	1,426,943	Closed	14.8	313
8/3/2026	2:15:00	7.3	0.0000	2	1,426,949	Closed	14.8	309
8/3/2026	2:30:00	7.3	1.5634	2	1,426,959	Open	14.7	309
8/3/2026	2:45:00	7.3	1.0031	1.7	1,426,981	Open	14.7	308
8/3/2026	3:00:00	7.3	0.0000	0.5	1,426,982	Closed	15.1	308
8/3/2026	3:15:00	7.3	1.5520	0.3	1,426,998	Open	14.7	308
8/3/2026	3:30:00	7.3	0.0000	0.1	1,427,013	Closed	14.8	304
8/3/2026	3:45:00	7.3	1.6050	0.4	1,427,016	Open	15	308
8/3/2026	4:00:00	7.3	1.5407	0.1	1,427,039	Open	14.6	303
8/3/2026	4:15:00	7.3	0.0000	0.2	1,427,049	Closed	14.8	303
8/3/2026	4:30:00	7.3	1.5823	0.2	1,427,058	Open	14.5	303
8/3/2026	4:45:00	7.3	0.0000	0.2	1,427,073	Closed	14.6	301
8/3/2026	5:00:00	7.2	0.0000	0.1	1,427,073	Closed	15.1	303
8/3/2026	5:15:00	7.3	1.6202	0.7	1,427,090	Open	14.4	301
8/3/2026	5:30:00	7.3	0.0000	0.8	1,427,106	Closed	14.6	301
8/3/2026	5:45:00	7.3	1.0258	1.3	1,427,117	Open	14.4	301
8/3/2026	6:00:00	7.3	0.0000	1.5	1,427,134	Closed	14.4	300
8/3/2026	6:15:00	7.3	1.6088	1.1	1,427,138	Open	14.4	300
8/3/2026	6:30:00	7.3	1.0713	0.8	1,427,162	Open	14.3	301
8/3/2026	6:45:00	7.3	0.0000	0.5	1,427,164	Closed	14.7	304
8/3/2026	7:00:00	7.3	1.6012	0.3	1,427,187	Open	14.3	304
8/3/2026	7:15:00	7.3	0.0000	0.2	1,427,197	Closed	14.5	107
8/3/2026	7:30:00	7.3	1.6126	0.3	1,427,204	Open	14.5	304
8/3/2026	7:45:00	7.3	0.0000	0.3	1,427,226	Closed	14.3	303



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	8:00:00	7.2	0.0000	0.3	1,427,226	Closed	14.7	304
8/3/2026	8:15:00	7.3	1.6050	0.3	1,427,242	Open	14.3	301
8/3/2026	8:30:00	7.2	0.0000	0.3	1,427,257	Closed	14.4	107
8/3/2026	8:45:00	7.2	1.0675	0.3	1,427,258	Open	14.8	299
8/3/2026	9:00:00	7.3	1.5823	0.4	1,427,278	Open	14.3	298
8/3/2026	9:15:00	7.2	0.0000	0.4	1,427,288	Closed	14.5	298
8/3/2026	9:30:00	7.3	0.6511	0.6	1,427,304	Open	14.3	296
8/3/2026	9:45:00	7.3	0.0000	0.4	1,427,313	Closed	14.5	289
8/3/2026	10:00:00	7.2	0.0000	0.5	1,427,313	Closed	15	298
8/3/2026	10:15:00	7.3	0.9464	0.9	1,427,324	Closed	14.6	293
8/3/2026	10:30:00	7.3	1.4082	0.7	1,427,328	Open	14.6	293
8/3/2026	10:45:00	7.3	1.7489	0.5	1,427,336	Open	14.8	296
8/3/2026	11:00:00	7.3	1.1394	4.4	1,427,361	Open	14.9	294
8/3/2026	11:15:00	7.3	0.0000	7	1,427,375	Closed	15.2	294
8/3/2026	11:30:00	7.3	1.7526	4.1	1,427,389	Open	15.1	298
8/3/2026	11:45:00	7.3	0.0000	4.2	1,427,402	Closed	15.5	294
8/3/2026	12:00:00	7.3	1.7640	3.8	1,427,407	Open	15.5	298
8/3/2026	12:15:00	7.6	0.0000	0	1,427,426	Closed	15.6	293
8/3/2026	12:30:00	7.4	1.1924	0	1,427,429	Open	15.9	296
8/3/2026	12:45:00	7.3	0.0000	0	1,427,451	Open	15.5	294
8/3/2026	13:00:00	7.3	0.0000	0	1,427,451	Closed	16.6	296
8/3/2026	13:15:00	7.3	1.1962	0.2	1,427,456	Open	16	296
8/3/2026	13:30:00	7.3	0.0000	0	1,427,472	Closed	16.1	294
8/3/2026	13:45:00	7.3	1.7564	0.1	1,427,481	Open	15.9	294
8/3/2026	14:00:00	7.3	0.0000	0.1	1,427,504	Closed	16	293
8/3/2026	14:15:00	7.3	1.7299	0.1	1,427,506	Open	16.7	296
8/3/2026	14:30:00	7.3	1.6618	0.3	1,427,531	Open	16	294
8/3/2026	14:45:00	7.2	1.2340	1.2	1,427,533	Open	17.2	298
8/3/2026	15:00:00	7.3	1.7186	0.6	1,427,555	Open	16.1	294
8/3/2026	15:15:00	7.2	0.0000	0.1	1,427,562	Closed	18.2	299
8/3/2026	15:30:00	7.3	1.1167	1.5	1,427,583	Open	16.3	293
8/3/2026	15:45:00	7.2	0.0000	0.3	1,427,585	Closed	18.4	298



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	16:00:00	7.3	1.6883	0.8	1,427,596	Open	16.6	293
8/3/2026	16:15:00	7.2	0.0000	0.8	1,427,604	Closed	18.1	298
8/3/2026	16:30:00	7.3	1.6883	1.3	1,427,619	Open	16.5	293
8/3/2026	16:45:00	7.2	0.0000	0.7	1,427,635	Closed	17.1	294
8/3/2026	17:00:00	7.2	1.1091	1.6	1,427,636	Open	18.1	298
8/3/2026	17:15:00	7.3	1.6504	1.6	1,427,658	Open	16.3	293
8/3/2026	17:30:00	7.2	1.7034	1.1	1,427,662	Open	17.8	296
8/3/2026	17:45:00	7.2	1.0637	3.5	1,427,686	Open	16.1	292
8/3/2026	18:00:00	7.2	0.0000	1.1	1,427,692	Closed	17.5	294
8/3/2026	18:15:00	7.3	1.6088	1.9	1,427,713	Open	16.1	293
8/3/2026	18:30:00	7.2	0.0000	2.8	1,427,720	Closed	16.2	291
8/3/2026	18:45:00	7.2	0.0000	3	1,427,720	Closed	16.5	291
8/3/2026	19:00:00	7.2	1.5217	2.2	1,427,722	Open	16.3	291
8/3/2026	19:15:00	7.2	0.9804	4.6	1,427,744	Open	16	293
8/3/2026	19:30:00	7.2	1.6429	1.9	1,427,747	Open	17.4	293
8/3/2026	19:45:00	7.3	1.5634	1.7	1,427,770	Open	15.8	293
8/3/2026	20:00:00	7.3	0.9918	3.7	1,427,792	Open	15.7	293
8/3/2026	20:15:00	7.2	1.6504	2.3	1,427,796	Open	16.8	291
8/3/2026	20:30:00	7.3	1.5444	1.8	1,427,819	Open	15.6	291
8/3/2026	20:45:00	7.2	0.0000	4.2	1,427,837	Closed	15.9	289
8/3/2026	21:00:00	7.3	1.5709	1.6	1,427,843	Open	15.8	289
8/3/2026	21:15:00	7.3	1.4990	2	1,427,866	Open	15.5	290
8/3/2026	21:30:00	7.2	0.0000	1.5	1,427,874	Closed	16.3	292
8/3/2026	21:45:00	7.3	0.5792	4.3	1,427,889	Open	15.4	289
8/3/2026	22:00:00	7.2	0.0000	2.4	1,427,902	Closed	15.4	289
8/3/2026	22:15:00	7.3	1.4082	1.8	1,427,912	Open	15.3	291
8/3/2026	22:30:00	7.3	0.7874	6.9	1,427,918	Closed	15.3	293
8/3/2026	22:45:00	7.3	0.0000	4.1	1,427,925	Closed	15.6	293
8/3/2026	23:00:00	7.3	1.5558	0.4	1,427,941	Open	15.4	294
8/3/2026	23:15:00	7.3	1.0145	0.6	1,427,963	Open	15.5	299
8/3/2026	23:30:00	7.3	1.5937	0.3	1,427,965	Open	15.8	298
8/3/2026	23:45:00	7.3	1.5747	0.3	1,427,988	Open	15.6	301



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	0:00:00	7.3	0.0000	0.6	1,428,004	Closed	15.7	303
8/4/2026	0:15:00	7.3	1.5407	0.4	1,428,015	Open	15.6	303
8/4/2026	0:30:00	7.3	0.0000	0.7	1,428,035	Closed	15.5	304
8/4/2026	0:45:00	7.3	1.0675	0.5	1,428,036	Open	15.8	306
8/4/2026	1:00:00	7.3	1.5634	0.5	1,428,057	Open	15.5	306
8/4/2026	1:15:00	7.3	0.0000	0.4	1,428,069	Closed	15.7	306
8/4/2026	1:30:00	7.3	1.0258	1.8	1,428,079	Open	15.4	306
8/4/2026	1:45:00	7.3	0.0000	0.3	1,428,092	Closed	15.5	306
8/4/2026	2:00:00	7.3	1.5823	0.6	1,428,099	Open	15.4	306
8/4/2026	2:15:00	7.3	0.0000	0.4	1,428,119	Closed	15.3	309
8/4/2026	2:30:00	7.2	0.0000	0.4	1,428,119	Closed	15.9	308
8/4/2026	2:45:00	7.3	1.5823	0.7	1,428,120	Open	15.7	306
8/4/2026	3:00:00	7.3	1.0031	2	1,428,142	Open	15.2	306
8/4/2026	3:15:00	7.2	0.0000	0.8	1,428,147	Closed	15.5	306
8/4/2026	3:30:00	7.3	1.5142	0.7	1,428,164	Open	15.1	306
8/4/2026	3:45:00	7.3	0.2574	1.3	1,428,184	Closed	15	301
8/4/2026	4:00:00	7.3	1.5634	0.9	1,428,186	Open	15.3	303
8/4/2026	4:15:00	7.3	1.5369	0.9	1,428,209	Open	14.9	302
8/4/2026	4:30:00	7.3	0.0000	0.8	1,428,223	Closed	15.2	302
8/4/2026	4:45:00	7.3	1.5407	0.5	1,428,233	Open	14.9	304
8/4/2026	5:00:00	7.2	0.0000	0.7	1,428,241	Closed	15.2	303
8/4/2026	5:15:00	7.2	1.0599	2.5	1,428,243	Open	15.2	303
8/4/2026	5:30:00	7.3	1.4952	0.7	1,428,263	Open	14.9	303
8/4/2026	5:45:00	7.2	0.0000	0.7	1,428,270	Closed	15.2	303
8/4/2026	6:00:00	7.3	1.1243	2.4	1,428,287	Open	14.9	303
8/4/2026	6:15:00	7.2	0.0000	0.7	1,428,291	Closed	15.1	306
8/4/2026	6:30:00	7.3	1.5444	1	1,428,313	Open	14.7	304
8/4/2026	6:45:00	7.2	0.0000	0.6	1,428,318	Closed	15.1	303
8/4/2026	7:00:00	7.3	1.5937	0.9	1,428,331	Open	14.8	305
8/4/2026	7:15:00	7.2	0.0000	0.7	1,428,346	Closed	14.9	303
8/4/2026	7:30:00	7.2	0.0000	0.8	1,428,346	Closed	15.1	306
8/4/2026	7:45:00	7.3	1.5482	1.1	1,428,366	Open	14.7	303



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	8:00:00	7.2	0.0000	0.7	1,428,375	Closed	15	301
8/4/2026	8:15:00	7.2	1.0599	3	1,428,379	Open	14.7	303
8/4/2026	8:30:00	7.3	1.5634	1.2	1,428,400	Open	14.5	299
8/4/2026	8:45:00	7.2	0.0000	1.1	1,428,403	Closed	14.9	299
8/4/2026	9:00:00	7.2	1.0296	1.9	1,428,422	Open	14.5	298
8/4/2026	9:15:00	7.2	0.0000	0.8	1,428,429	Closed	14.9	298
8/4/2026	9:30:00	7.2	1.5747	1	1,428,443	Open	14.6	296
8/4/2026	9:45:00	7.2	0.0000	0.8	1,428,453	Closed	15	296
8/4/2026	10:00:00	7.3	1.5672	1	1,428,466	Open	14.8	293
8/4/2026	10:15:00	7.2	0.0000	0.8	1,428,482	Closed	15.1	293
8/4/2026	10:30:00	7.2	0.0000	0.7	1,428,482	Open	15.5	300
8/4/2026	10:45:00	7.2	1.6088	1.1	1,428,493	Open	15.2	299
8/4/2026	11:00:00	7.2	0.0000	0.9	1,428,511	Closed	15.3	301
8/4/2026	11:15:00	7.3	0.6852	1.5	1,428,523	Open	15.3	302
8/4/2026	11:30:00	7.3	1.5899	1.2	1,428,542	Open	15.4	302
8/4/2026	11:45:00	7.2	0.0000	0.8	1,428,544	Closed	16.3	302
8/4/2026	12:00:00	7.3	1.0599	2.6	1,428,561	Open	15.7	299
8/4/2026	12:15:00	7.2	0.0000	0.9	1,428,571	Closed	16.1	298
8/4/2026	12:30:00	7.3	1.6353	1.4	1,428,584	Open	15.8	298
8/4/2026	12:45:00	7.3	1.0713	3.7	1,428,607	Open	15.8	298
8/4/2026	13:00:00	7.2	1.5104	3.8	1,428,608	Closed	17.3	301
8/4/2026	13:15:00	7.3	1.6353	2.3	1,428,632	Open	16	299
8/4/2026	13:30:00	7.3	0.3066	6.3	1,428,654	Closed	16.1	303
8/4/2026	13:45:00	7.3	0.0000	2.3	1,428,654	Closed	17.2	303
8/4/2026	14:00:00	7.3	1.6277	2.8	1,428,675	Open	16.3	306
8/4/2026	14:15:00	7.3	0.0000	2.1	1,428,690	Closed	16.7	306
8/4/2026	14:30:00	7.3	1.6050	2.3	1,428,694	Open	16.9	306
8/4/2026	14:45:00	7.3	1.5747	2.5	1,428,718	Open	16.4	306
8/4/2026	15:00:00	7.3	0.0000	1.3	1,428,724	Closed	17.9	311
8/4/2026	15:15:00	7.3	1.6239	1.5	1,428,740	Open	16.6	309
8/4/2026	15:30:00	7.3	0.0000	3.7	1,428,752	Closed	16.9	308
8/4/2026	15:45:00	7.3	1.1016	2.8	1,428,755	Open	17.2	311



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	16:00:00	7.3	1.6202	0.5	1,428,777	Open	16.5	309
8/4/2026	16:15:00	7.3	0.0000	1.7	1,428,784	Closed	17.8	311
8/4/2026	16:30:00	7.3	1.0978	1.1	1,428,801	Open	16.7	309
8/4/2026	16:45:00	7.3	0.0000	1.5	1,428,805	Closed	17.7	309
8/4/2026	17:00:00	7.3	1.5785	1	1,428,824	Open	16.6	308
8/4/2026	17:15:00	7.3	0.0000	1	1,428,838	Closed	17.2	311
8/4/2026	17:30:00	7.3	1.6164	1.1	1,428,848	Open	16.8	309
8/4/2026	17:45:00	7.3	0.0000	0.9	1,428,866	Closed	17.1	311
8/4/2026	18:00:00	7.3	1.1016	2.9	1,428,870	Open	17.3	311
8/4/2026	18:15:00	7.3	1.6239	1.1	1,428,892	Open	16.7	311
8/4/2026	18:30:00	7.3	0.0000	0.8	1,428,901	Closed	17.9	314
8/4/2026	18:45:00	7.3	1.0523	2.2	1,428,909	Open	16.9	311
8/4/2026	19:00:00	7.3	0.0000	1.4	1,428,913	Closed	17.4	313
8/4/2026	19:15:00	7.3	1.6315	2	1,428,917	Open	17.3	313
8/4/2026	19:30:00	7.2	0.1779	2.6	1,428,937	Closed	16.6	313
8/4/2026	19:45:00	7.2	1.6239	2.7	1,428,939	Open	17.5	313
8/4/2026	20:00:00	7.2	1.6050	2.6	1,428,963	Open	16.3	313
8/4/2026	20:15:00	7.2	0.0000	2.1	1,428,967	Closed	17.2	314
8/4/2026	20:30:00	7.2	1.6239	2.6	1,428,979	Open	16.3	314
8/4/2026	20:45:00	7.2	0.3445	3.7	1,429,002	Closed	15.9	311
8/4/2026	21:00:00	7.2	0.0000	1.6	1,429,002	Closed	17.1	314
8/4/2026	21:15:00	7.2	0.5262	3.6	1,429,013	Closed	15.8	309
8/4/2026	21:30:00	7.2	1.4536	1.3	1,429,030	Open	15.6	307
8/4/2026	21:45:00	7.2	1.4347	1.6	1,429,051	Open	15.6	306
8/4/2026	22:00:00	7.2	0.0000	2	1,429,068	Closed	15.7	306
8/4/2026	22:15:00	7.2	1.4839	2.1	1,429,075	Open	15.6	309
8/4/2026	22:30:00	7.2	1.4309	2	1,429,098	Open	15.6	309
8/4/2026	22:45:00	7.2	0.0000	2.1	1,429,116	Closed	15.7	309
8/4/2026	23:00:00	7.2	1.4725	3.1	1,429,116	Closed	16.2	313
8/4/2026	23:15:00	7.2	1.4650	1.6	1,429,138	Open	15.8	313
8/4/2026	23:30:00	7.2	0.4391	3.8	1,429,156	Closed	15.9	316
8/4/2026	23:45:00	7.2	0.0000	1.7	1,429,156	Closed	16.4	316



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	0:00:00	7.2	1.4536	1.8	1,429,172	Open	15.9	318
8/5/2026	0:15:00	7.2	0.0000	1.4	1,429,176	Closed	16.5	318
8/5/2026	0:30:00	7.2	1.4763	1.7	1,429,188	Open	15.9	318
8/5/2026	0:45:00	7.3	1.4612	2.2	1,429,210	Open	15.9	319
8/5/2026	1:00:00	7.2	0.0000	1.1	1,429,218	Closed	16.4	323
8/5/2026	1:15:00	7.3	1.4385	2.3	1,429,228	Open	15.9	319
8/5/2026	1:30:00	7.3	1.4347	2.2	1,429,250	Open	15.7	319
8/5/2026	1:45:00	7.2	0.0000	1.4	1,429,263	Closed	15.9	319
8/5/2026	2:00:00	7.2	1.4460	2.1	1,429,267	Open	15.8	319
8/5/2026	2:15:00	7.3	0.5867	6.3	1,429,286	Closed	15.6	318
8/5/2026	2:30:00	7.3	1.4877	1.4	1,429,286	Closed	15.5	314
8/5/2026	2:45:00	7.3	0.9691	3.3	1,429,306	Open	15.5	313
8/5/2026	3:00:00	7.3	0.0000	1.5	1,429,324	Closed	15.5	313
8/5/2026	3:15:00	7.2	0.0000	1	1,429,324	Closed	16.1	313
8/5/2026	3:30:00	7.3	1.5747	1.1	1,429,343	Open	15.4	309
8/5/2026	3:45:00	7.3	0.6322	3.1	1,429,345	Closed	15.2	304
8/5/2026	4:00:00	7.3	1.5899	1.5	1,429,360	Open	15.1	303
8/5/2026	4:15:00	7.3	1.0334	4.3	1,429,382	Open	15.1	303
8/5/2026	4:30:00	7.3	0.0000	1.7	1,429,399	Closed	15.2	303
8/5/2026	4:45:00	7.2	0.9956	2	1,429,399	Open	15.7	301
8/5/2026	5:00:00	7.3	0.0000	1.4	1,429,419	Closed	15.1	300
8/5/2026	5:15:00	7.2	1.0258	4.9	1,429,420	Open	15.5	299
8/5/2026	5:30:00	7.3	1.5369	1.8	1,429,441	Open	15.1	298
8/5/2026	5:45:00	7.3	0.0000	5.1	1,429,462	Closed	15	298
8/5/2026	6:00:00	7.2	0.0000	1.5	1,429,462	Closed	15.5	298
8/5/2026	6:15:00	7.3	1.0410	3.2	1,429,482	Open	15	298
8/5/2026	6:30:00	7.2	0.0000	2.1	1,429,489	Closed	15.4	301
8/5/2026	6:45:00	7.2	1.0523	3	1,429,498	Open	15.1	299
8/5/2026	7:00:00	7.3	1.5407	2.2	1,429,518	Open	15	298
8/5/2026	7:15:00	7.2	0.0000	1	1,429,520	Closed	15.5	301
8/5/2026	7:30:00	7.3	1.5899	1.1	1,429,536	Open	14.9	296
8/5/2026	7:45:00	7.2	0.0000	0.9	1,429,551	Closed	15	296



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	8:00:00	7.2	0.0000	0.7	1,429,551	Closed	15.5	298
8/5/2026	8:15:00	7.2	0.6019	2.1	1,429,569	Open	14.8	294
8/5/2026	8:30:00	7.2	0.0000	1.9	1,429,571	Closed	15	293
8/5/2026	8:45:00	7.2	1.1243	2.3	1,429,584	Open	14.7	293
8/5/2026	9:00:00	7.2	0.0000	1.1	1,429,597	Closed	14.7	291
8/5/2026	9:15:00	7.2	1.1432	2.2	1,429,603	Open	14.8	291
8/5/2026	9:30:00	7.2	0.0000	1.9	1,429,613	Closed	14.8	289
8/5/2026	9:45:00	7.2	0.0000	1.7	1,429,613	Closed	15.2	289
8/5/2026	10:00:00	7.2	1.6921	1.2	1,429,634	Open	14.8	290
8/5/2026	10:15:00	7.2	0.0000	1.1	1,429,653	Closed	14.9	290
8/5/2026	10:30:00	7.2	1.6769	1.6	1,429,660	Open	15.1	288
8/5/2026	10:45:00	7.2	1.1243	1.8	1,429,684	Open	15.2	288
8/5/2026	11:00:00	7.2	0.0000	1.9	1,429,687	Closed	15.8	288
8/5/2026	11:15:00	7.2	1.1394	3.5	1,429,706	Open	15.5	290
8/5/2026	11:30:00	7.2	0.0000	3.7	1,429,725	Closed	15.6	289
8/5/2026	12:00:00	7.3	1.6164	4.3	1,429,751	Open	15.7	290
8/5/2026	12:15:00	7.2	0.0000	4.8	1,429,764	Closed	16	290
8/5/2026	12:30:00	7.3	0.0000	4.9	1,429,764	Open	15.9	288
8/5/2026	12:45:00	7.2	1.0902	5.6	1,429,781	Open	16.1	289
8/5/2026	13:00:00	7.3	0.0000	4.5	1,429,796	Closed	16.2	288
8/5/2026	13:15:00	7.3	1.0296	5.1	1,429,796	Closed	16.9	292
8/5/2026	13:30:00	7.3	1.5634	4.3	1,429,817	Open	16.2	292
8/5/2026	13:45:00	7.3	0.0000	3.2	1,429,837	Closed	16.3	292
8/5/2026	14:00:00	7.3	1.5747	2.8	1,429,839	Open	16.7	293
8/5/2026	14:15:00	7.3	1.0145	3	1,429,861	Open	16.4	291
8/5/2026	14:30:00	7.3	0.0000	3.6	1,429,881	Closed	16.5	291
8/5/2026	14:45:00	7.3	1.0372	3.8	1,429,881	Open	17.1	293
8/5/2026	15:00:00	7.3	1.5179	5.3	1,429,902	Open	16.6	291
8/5/2026	15:15:00	7.3	0.0000	5.3	1,429,922	Closed	16.7	289
8/5/2026	15:30:00	7.2	1.6164	5.4	1,429,922	Open	17.4	293
8/5/2026	15:45:00	7.3	1.0713	6.3	1,429,944	Open	16.9	289
8/5/2026	16:00:00	7.2	0.0000	7.7	1,429,954	Closed	17	290



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	16:15:00	7.2	0.0000	7.1	1,429,954	Closed	17.8	293
8/5/2026	16:30:00	7.3	1.5066	6.6	1,429,972	Open	16.9	292
8/5/2026	16:45:00	7.2	0.0000	5.6	1,429,984	Closed	17	290
8/5/2026	17:00:00	7.3	1.5596	6	1,429,993	Open	17	290
8/5/2026	17:15:00	7.3	1.0448	7.1	1,430,014	Open	16.9	289
8/5/2026	17:30:00	7.2	1.5217	6.2	1,430,017	Open	17.4	292
8/5/2026	17:45:00	7.3	0.0000	13.4	1,430,032	Open	16.8	290
8/5/2026	18:00:00	7.3	1.5899	10.5	1,430,033	Open	16.8	288
8/5/2026	18:15:00	7.3	1.1053	5.9	1,430,054	Open	17	289
8/5/2026	18:30:00	7.3	1.6088	6.3	1,430,076	Open	17.6	290
8/5/2026	18:45:00	7.2	0.0000	6.1	1,430,079	Closed	18.2	293
8/5/2026	19:00:00	7.2	0.0000	6.1	1,430,096	Closed	18.7	293
8/5/2026	19:15:00	7.2	1.1394	4.1	1,430,099	Open	18.5	292
8/5/2026	19:30:00	7.3	1.6391	2.8	1,430,122	Open	16.8	291
8/5/2026	19:45:00	7.3	0.0000	2.6	1,430,124	Closed	17.1	293
8/5/2026	20:00:00	7.3	1.5937	1	1,430,146	Open	16.4	292
8/5/2026	20:15:00	7.3	0.0000	0.6	1,430,163	Closed	16.3	292
8/5/2026	20:30:00	7.3	1.6467	0.3	1,430,172	Open	16.3	292
8/5/2026	20:45:00	7.3	1.2000	0.4	1,430,195	Open	16.2	290
8/5/2026	21:00:00	7.2	0.0000	0.2	1,430,198	Closed	16.7	292
8/5/2026	21:15:00	7.3	1.0486	0.5	1,430,217	Open	16	288
8/5/2026	21:30:00	7.3	1.4650	0.5	1,430,237	Open	15.9	288
8/5/2026	21:45:00	7.3	0.0000	0.8	1,430,253	Closed	16	290
8/5/2026	22:00:00	7.3	1.4725	0.8	1,430,264	Open	15.9	292
8/5/2026	22:15:00	7.3	1.0372	1	1,430,285	Open	15.8	290
8/5/2026	22:30:00	7.3	1.4460	1	1,430,305	Open	15.8	290
8/5/2026	22:45:00	7.3	0.0000	1	1,430,324	Closed	15.8	290
8/5/2026	23:00:00	7.3	1.4422	1	1,430,328	Open	15.9	292
8/5/2026	23:15:00	7.3	1.0107	1.4	1,430,348	Open	15.8	292
8/5/2026	23:30:00	7.3	0.0000	0.7	1,430,352	Closed	16.1	293
8/5/2026	23:45:00	7.3	0.9918	1.1	1,430,360	Open	15.8	294
8/6/2026	0:00:00	7.3	1.4763	1.2	1,430,380	Open	15.6	293



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	0:15:00	7.3	0.9615	1.8	1,430,400	Open	15.6	293
8/6/2026	0:30:00	7.3	1.4687	2.6	1,430,403	Closed	16	297
8/6/2026	0:45:00	7.3	0.9993	2	1,430,423	Open	15.5	293
8/6/2026	1:00:00	7.3	1.4309	1.4	1,430,443	Open	15.5	293
8/6/2026	1:15:00	7.3	0.9729	1.8	1,430,462	Open	15.5	293
8/6/2026	1:30:00	7.3	1.4763	1.5	1,430,467	Open	15.9	297
8/6/2026	1:45:00	7.3	0.9842	1.9	1,430,487	Open	15.5	295
8/6/2026	2:00:00	7.3	1.4725	1.2	1,430,507	Open	15.4	295
8/6/2026	2:15:00	7.3	0.9766	2.6	1,430,527	Open	15.4	295
8/6/2026	2:30:00	7.3	0.8631	1.5	1,430,529	Closed	15.8	298
8/6/2026	2:45:00	7.3	0.9993	2.8	1,430,548	Open	15.4	295
8/6/2026	3:00:00	7.3	1.4650	1.3	1,430,569	Open	15.3	295
8/6/2026	3:15:00	7.2	0.0000	3.2	1,430,587	Closed	15.4	295
8/6/2026	3:30:00	7.2	1.4536	2.2	1,430,588	Open	15.8	294
8/6/2026	3:45:00	7.2	0.9842	2.2	1,430,608	Open	15.3	295
8/6/2026	4:00:00	7.3	1.4612	2.2	1,430,628	Open	15.2	295
8/6/2026	4:15:00	7.2	0.0000	1.4	1,430,636	Closed	15.5	295
8/6/2026	4:30:00	7.3	1.4498	2	1,430,650	Open	15.2	294
8/6/2026	4:45:00	7.3	0.7609	5.5	1,430,668	Open	15.1	294
8/6/2026	5:00:00	7.3	0.0000	2.7	1,430,681	Closed	15.1	296
8/6/2026	5:15:00	7.3	0.0000	1	1,430,681	Closed	15.4	296
8/6/2026	5:30:00	7.3	1.0410	5.8	1,430,693	Open	15	296
8/6/2026	5:45:00	7.3	1.4877	2.7	1,430,712	Open	15	296
8/6/2026	6:00:00	7.3	0.0000	3.3	1,430,727	Closed	15.1	298
8/6/2026	6:15:00	7.3	1.5407	3.2	1,430,735	Open	15.1	298
8/6/2026	6:30:00	7.3	0.5830	9.1	1,430,756	Closed	15	298
8/6/2026	6:45:00	7.3	0.5489	154.9	1,430,760	Closed	15	301
8/6/2026	7:00:00	7.3	1.5444	1.2	1,430,760	Closed	15.1	301
8/6/2026	7:15:00	7.3	1.6277	2.2	1,430,773	Open	15.2	299
8/6/2026	7:30:00	7.3	1.6202	2.1	1,430,798	Open	15.1	300
8/6/2026	7:45:00	7.3	0.0000	3.9	1,430,819	Open	15.1	299
8/6/2026	8:00:00	7.2	0.2044	1.2	1,430,829	Open	15.2	299



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	8:15:00	7.2	1.0713	1.8	1,430,836	Open	15.3	299
8/6/2026	8:30:00	7.3	1.5293	3.6	1,430,858	Open	14.9	296
8/6/2026	8:45:00	7.2	0.0000	3.6	1,430,867	Closed	15	294
8/6/2026	9:00:00	7.2	1.5785	3.5	1,430,883	Open	14.8	291
8/6/2026	9:15:00	7.2	1.0599	1.5	1,430,904	Open	14.9	291
8/6/2026	9:30:00	7.2	0.0000	1	1,430,910	Closed	15	292
8/6/2026	9:45:00	7.2	1.0675	1.4	1,430,923	Open	15.1	290
8/6/2026	10:00:00	7.3	0.0000	2.1	1,430,933	Open	14.9	287
8/6/2026	10:15:00	7.2	0.0000	1.2	1,430,949	Closed	15.2	287
8/6/2026	10:30:00	7.2	1.4650	1.1	1,430,955	Open	15.1	285
8/6/2026	10:45:00	7.2	1.0296	2.2	1,430,975	Open	15.1	283
8/6/2026	11:00:00	7.2	0.0000	0.9	1,430,994	Closed	15.1	283
8/6/2026	11:15:00	7.2	0.0000	0.5	1,430,994	Closed	15.6	283
8/6/2026	11:30:00	7.2	1.4877	0.9	1,431,009	Open	15.3	285
8/6/2026	11:45:00	7.2	0.0000	2	1,431,027	Closed	15.2	285
8/6/2026	12:00:00	7.2	1.4612	1	1,431,030	Open	15.6	288
8/6/2026	12:15:00	7.2	0.9766	1.1	1,431,049	Open	15.5	285
8/6/2026	12:30:00	7.2	0.0000	0.5	1,431,065	Closed	15.5	285
8/6/2026	12:45:00	7.2	1.0637	1.1	1,431,069	Open	15.9	287
8/6/2026	13:00:00	7.2	1.5331	0.6	1,431,090	Open	15.6	285
8/6/2026	13:15:00	7.2	0.9956	1.6	1,431,111	Open	15.8	285
8/6/2026	13:30:00	7.2	0.0000	1.2	1,431,116	Closed	16.1	287
8/6/2026	13:45:00	7.2	1.0448	0.8	1,431,135	Open	16.1	285
8/6/2026	14:00:00	7.2	1.5255	0.5	1,431,156	Open	16	287
8/6/2026	14:15:00	7.2	0.0000	1	1,431,175	Closed	16.3	287
8/6/2026	14:30:00	7.2	1.5331	0.6	1,431,181	Open	16.4	290
8/6/2026	14:45:00	7.2	1.0523	1.2	1,431,202	Open	16.5	290
8/6/2026	15:00:00	7.2	1.5142	0.4	1,431,223	Open	16.4	291
8/6/2026	15:15:00	7.2	0.0000	0.2	1,431,231	Closed	16.7	293
8/6/2026	15:30:00	7.2	1.5217	3.1	1,431,250	Open	16.5	291
8/6/2026	15:45:00	7.2	1.0410	0.8	1,431,270	Open	16.8	294
8/6/2026	16:00:00	7.2	0.0000	0.4	1,431,281	Closed	16.8	294



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	16:15:00	7.2	0.6662	1.5	1,431,289	Open	16.7	294
8/6/2026	16:30:00	7.3	1.4915	0.7	1,431,309	Open	16.7	294
8/6/2026	16:45:00	7.2	1.0258	1.2	1,431,329	Open	16.8	294
8/6/2026	17:00:00	7.2	0.0000	0.7	1,431,342	Closed	16.8	294
8/6/2026	17:15:00	7.2	0.9691	1.1	1,431,352	Open	16.8	296
8/6/2026	17:30:00	7.3	1.4915	0.6	1,431,373	Open	16.6	294
8/6/2026	17:45:00	7.2	1.0069	0.7	1,431,393	Open	16.7	294
8/6/2026	18:00:00	7.2	0.0000	1.4	1,431,397	Closed	17.1	296
8/6/2026	18:15:00	7.2	0.9804	0.7	1,431,416	Open	16.8	293
8/6/2026	18:30:00	7.3	1.4725	0.6	1,431,436	Open	16.6	293
8/6/2026	18:45:00	7.2	0.0000	0.5	1,431,440	Closed	17	294
8/6/2026	19:00:00	7.2	1.4952	0.3	1,431,453	Open	16.7	293
8/6/2026	19:15:00	7.2	0.9729	0.2	1,431,473	Open	16.7	295
8/6/2026	19:30:00	7.2	1.4612	0.1	1,431,493	Open	16.5	294
8/6/2026	19:45:00	7.2	0.0000	0	1,431,504	Closed	16.7	295
8/6/2026	20:00:00	7.2	1.4763	0	1,431,520	Open	16.4	293
8/6/2026	20:15:00	7.2	1.0069	0.1	1,431,540	Open	16.5	293
8/6/2026	20:30:00	7.2	0.0000	0.2	1,431,548	Closed	16.5	293
8/6/2026	20:45:00	7.2	1.0258	0	1,431,563	Open	16.3	293
8/6/2026	21:00:00	7.2	1.4801	0	1,431,584	Open	15.9	290
8/6/2026	21:15:00	7.2	0.0000	0	1,431,602	Closed	15.9	290
8/6/2026	21:30:00	7.2	0.0000	0	1,431,602	Closed	16.4	291
8/6/2026	21:45:00	7.2	0.9653	0.1	1,431,613	Open	15.9	290
8/6/2026	22:00:00	7.2	1.4422	0.1	1,431,634	Open	15.6	288
8/6/2026	22:15:00	7.2	0.2877	0.3	1,431,653	Closed	15.8	288
8/6/2026	22:30:00	7.2	1.4460	0.6	1,431,657	Open	15.9	288
8/6/2026	22:45:00	7.2	0.9880	0.6	1,431,676	Open	15.7	290
8/6/2026	23:00:00	7.2	1.4612	0.6	1,431,696	Open	15.7	290
8/6/2026	23:15:00	7.2	0.0000	2.4	1,431,715	Closed	15.9	292
8/6/2026	23:30:00	7.2	1.4801	0.7	1,431,717	Open	16.2	293
8/6/2026	23:45:00	7.2	0.9993	0.7	1,431,737	Open	16	293
8/7/2026	0:00:00	7.2	1.4422	0.3	1,431,757	Open	15.9	297



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	0:15:00	7.2	0.0000	1.7	1,431,772	Closed	16	297
8/7/2026	0:30:00	7.2	1.4763	0.5	1,431,781	Open	15.9	295
8/7/2026	0:45:00	7.2	1.0145	0.5	1,431,801	Open	16	295
8/7/2026	1:00:00	7.2	1.4536	0.5	1,431,821	Open	15.8	297
8/7/2026	1:15:00	7.2	0.0000	0.4	1,431,834	Closed	15.9	296
8/7/2026	1:30:00	7.2	1.4763	0.5	1,431,843	Open	15.8	300
8/7/2026	1:45:00	7.2	0.9842	0.6	1,431,862	Open	15.8	298
8/7/2026	2:00:00	7.2	1.4536	0.5	1,431,883	Open	15.6	298
8/7/2026	2:15:00	7.2	0.0000	0.5	1,431,886	Closed	16	300
8/7/2026	2:30:00	7.2	1.4309	0.5	1,431,905	Open	15.6	298
8/7/2026	2:45:00	7.2	0.9880	1.1	1,431,924	Open	15.7	302
8/7/2026	3:00:00	7.2	0.0000	0.6	1,431,935	Closed	15.8	302
8/7/2026	3:15:00	7.2	0.6662	1.6	1,431,942	Open	15.6	300
8/7/2026	3:30:00	7.2	1.4385	0.6	1,431,961	Open	15.6	303
8/7/2026	3:45:00	7.2	0.9880	2.2	1,431,980	Open	15.8	305
8/7/2026	4:00:00	7.2	0.0000	0.8	1,431,997	Closed	15.7	303
8/7/2026	4:15:00	7.2	1.0031	1.8	1,432,001	Open	16	305
8/7/2026	4:30:00	7.2	1.4536	0.8	1,432,015	Closed	15.6	304
8/7/2026	4:45:00	7.2	0.0000	4.8	1,432,021	Closed	15.6	304
8/7/2026	5:00:00	7.2	1.5899	1.7	1,432,030	Open	15.4	303
8/7/2026	5:15:00	7.2	1.0675	3.5	1,432,051	Open	15.4	301
8/7/2026	5:30:00	7.2	1.5217	1.8	1,432,073	Open	15.2	301
8/7/2026	5:45:00	7.2	0.0000	1.6	1,432,087	Closed	15.3	301
8/7/2026	6:00:00	7.2	1.5482	2	1,432,097	Open	15.2	301
8/7/2026	6:15:00	7.2	1.0713	8.9	1,432,117	Open	15.2	303
8/7/2026	6:30:00	7.2	0.0000	1.6	1,432,127	Closed	15.3	304
8/7/2026	6:45:00	7.2	1.0788	1.9	1,432,138	Open	15.1	303
8/7/2026	7:00:00	7.2	1.5634	1.6	1,432,161	Open	15	301
8/7/2026	7:15:00	7.2	1.0221	1.9	1,432,163	Closed	15.3	302
8/7/2026	7:30:00	7.2	1.5255	1.8	1,432,186	Open	15	298
8/7/2026	7:45:00	7.2	0.0000	7.9	1,432,201	Closed	15.1	298
8/7/2026	8:00:00	7.2	1.5861	2.2	1,432,204	Open	15.2	298



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	8:15:00	7.2	1.0448	2.9	1,432,225	Open	15	297
8/7/2026	8:30:00	7.2	0.0000	1.7	1,432,239	Closed	15	293
8/7/2026	8:45:00	7.2	0.0000	1.7	1,432,239	Closed	15.4	297
8/7/2026	9:00:00	7.2	1.5709	1.7	1,432,255	Open	15	293
8/7/2026	9:15:00	7.1	0.0000	1.7	1,432,266	Closed	15.1	293
8/7/2026	9:30:00	7.2	1.5823	1.9	1,432,281	Open	15	293
8/7/2026	9:45:00	7.2	0.0000	1.7	1,432,298	Closed	15.2	293
8/7/2026	10:00:00	7.2	1.5861	0.9	1,432,306	Open	15.3	293
8/7/2026	10:15:00	7.2	1.1394	0.6	1,432,327	Open	15.5	296
8/7/2026	10:30:00	7.2	1.5558	0.9	1,432,349	Open	15.5	297
8/7/2026	10:45:00	7.1	0.0000	1.7	1,432,363	Closed	15.8	296
8/7/2026	11:00:00	7.2	1.5596	2.3	1,432,372	Open	15.8	294
8/7/2026	11:15:00	7.1	1.1432	2.6	1,432,392	Open	15.9	294
8/7/2026	11:30:00	7.2	1.5369	2	1,432,406	Open	16	293
8/7/2026	11:45:00	7.1	0.0000	4.2	1,432,422	Closed	16.2	295
8/7/2026	12:00:00	7.1	1.5974	2.5	1,432,432	Open	16.2	293
8/7/2026	12:15:00	7.1	1.0978	3.6	1,432,452	Open	16.2	293
8/7/2026	12:30:00	7.2	1.5293	2	1,432,475	Open	16.2	293
8/7/2026	12:45:00	7.1	0.0000	2.7	1,432,490	Closed	16.4	293
8/7/2026	13:00:00	7.2	1.5937	1.2	1,432,500	Open	16.4	293
8/7/2026	13:15:00	7.2	1.0675	0.8	1,432,521	Open	16.4	293
8/7/2026	13:30:00	7.2	1.5255	0.8	1,432,543	Open	16.4	292
8/7/2026	13:45:00	7.1	1.1053	1.8	1,432,547	Open	16.9	292
8/7/2026	14:00:00	7.2	1.5785	1	1,432,570	Open	16.6	290
8/7/2026	14:15:00	7.2	0.0000	3.4	1,432,588	Closed	16.8	290
8/7/2026	14:30:00	7.1	0.0000	2.1	1,432,588	Closed	17.2	290
8/7/2026	14:45:00	7.1	1.0523	1.8	1,432,605	Open	16.9	290
8/7/2026	15:00:00	7.2	1.5444	2	1,432,628	Open	16.7	288
8/7/2026	15:15:00	7.1	1.0713	2.4	1,432,648	Open	16.8	287
8/7/2026	15:30:00	7.1	0.0000	2.1	1,432,655	Closed	17	287
8/7/2026	15:45:00	7.1	0.7382	3.9	1,432,673	Open	16.9	287
8/7/2026	16:00:00	7.1	1.5520	2.1	1,432,695	Open	16.8	287



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	16:15:00	7.1	1.1016	2.1	1,432,715	Open	16.9	287
8/7/2026	16:30:00	7.1	1.5672	2	1,432,721	Open	17	288
8/7/2026	16:45:00	7.1	1.0486	2.2	1,432,741	Open	16.9	287
8/7/2026	17:00:00	7.1	1.5407	1.6	1,432,763	Open	16.8	287
8/7/2026	17:15:00	7.1	0.0000	1.3	1,432,777	Closed	17	287
8/7/2026	17:30:00	7.1	1.5596	1.2	1,432,792	Open	16.9	288
8/7/2026	17:45:00	7.1	0.6624	3.1	1,432,807	Open	16.8	288
8/7/2026	18:00:00	7.1	1.4044	0.1	1,432,828	Open	16.9	288
8/7/2026	18:15:00	7.2	0.0000	4.8	1,432,837	Closed	17.1	288
8/7/2026	18:30:00	7.2	0.0000	3.7	1,432,837	Closed	17.5	290
8/7/2026	18:45:00	7.1	1.0599	1.5	1,432,851	Open	17.2	292
8/7/2026	19:00:00	7.2	1.5709	1.8	1,432,874	Open	16.9	290
8/7/2026	19:15:00	7.2	1.1281	1.9	1,432,894	Open	17.2	293
8/7/2026	19:30:00	7.2	0.0000	2	1,432,900	Closed	17.2	293
8/7/2026	19:45:00	7.2	1.0788	0.5	1,432,919	Open	16.9	293
8/7/2026	20:00:00	7.2	1.5558	0.1	1,432,942	Open	16.5	293
8/7/2026	20:15:00	7.2	0.0000	0.6	1,432,956	Closed	16.6	295
8/7/2026	20:30:00	7.2	1.5028	0.3	1,432,966	Open	16.4	297
8/7/2026	20:45:00	7.2	1.0031	0.4	1,432,985	Open	16.2	295
8/7/2026	21:00:00	7.2	1.4877	0.3	1,433,007	Open	16	293
8/7/2026	21:15:00	7.2	0.0000	0.4	1,433,007	Closed	16.4	295
8/7/2026	21:30:00	7.2	1.4650	0.4	1,433,028	Open	15.8	292
8/7/2026	21:45:00	7.1	0.9993	0.7	1,433,047	Open	15.8	292
8/7/2026	22:00:00	7.1	0.0000	0.1	1,433,063	Closed	15.8	292
8/7/2026	22:15:00	7.1	1.0410	0.1	1,433,068	Open	16	295
8/7/2026	22:30:00	7.2	1.4839	0.1	1,433,090	Open	15.7	293
8/7/2026	22:45:00	7.1	0.0000	0.2	1,433,090	Closed	16.1	295
8/7/2026	23:00:00	7.2	1.4915	0.2	1,433,109	Open	15.7	295
8/7/2026	23:15:00	7.2	1.0145	0.4	1,433,128	Open	15.7	298
8/7/2026	23:30:00	7.2	0.0000	0.4	1,433,136	Closed	15.9	298
8/7/2026	23:45:00	7.2	1.0183	0.6	1,433,147	Open	15.7	300
8/8/2026	0:00:00	7.2	1.4612	0.6	1,433,169	Open	15.5	300



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	0:15:00	7.2	0.0000	2.1	1,433,185	Closed	15.6	305
8/8/2026	0:30:00	7.2	1.5104	0.9	1,433,190	Open	15.7	306
8/8/2026	0:45:00	7.2	0.9653	1.2	1,433,208	Open	15.5	308
8/8/2026	1:00:00	7.2	1.4460	0.8	1,433,230	Open	15.4	308
8/8/2026	1:15:00	7.2	0.0000	0.5	1,433,238	Closed	15.7	308
8/8/2026	1:30:00	7.2	1.5028	0.7	1,433,254	Open	15.5	309
8/8/2026	1:45:00	7.2	0.9804	1.6	1,433,273	Open	15.5	308
8/8/2026	2:00:00	7.2	1.4915	0.9	1,433,295	Open	15.4	307
8/8/2026	2:15:00	7.2	0.0000	1	1,433,297	Closed	15.7	306
8/8/2026	2:30:00	7.2	1.4498	1	1,433,315	Open	15.4	306
8/8/2026	2:45:00	7.2	0.9993	1.6	1,433,334	Open	15.4	307
8/8/2026	3:00:00	7.2	0.0000	1.4	1,433,350	Closed	15.4	307
8/8/2026	3:15:00	7.2	1.0221	1.3	1,433,354	Open	15.6	307
8/8/2026	3:30:00	7.2	1.4915	1	1,433,376	Open	15.4	303
8/8/2026	3:45:00	7.2	0.0000	2.2	1,433,394	Closed	15.4	303
8/8/2026	4:00:00	7.1	1.4952	0.6	1,433,396	Open	15.8	304
8/8/2026	4:15:00	7.1	1.0258	0.3	1,433,415	Open	15.4	302
8/8/2026	4:30:00	7.1	1.4536	0.2	1,433,420	Open	15.5	302
8/8/2026	4:45:00	7.2	0.9956	0.1	1,433,438	Open	15.4	298
8/8/2026	5:00:00	7.2	1.4839	0.3	1,433,460	Open	15.3	297
8/8/2026	5:15:00	7.2	1.0145	0.9	1,433,479	Open	15.3	297
8/8/2026	5:30:00	7.1	0.0000	0.3	1,433,484	Closed	15.6	294
8/8/2026	5:45:00	7.1	0.9804	0.3	1,433,499	Open	15.2	295
8/8/2026	6:00:00	7.2	1.4725	0.3	1,433,521	Open	15.1	293
8/8/2026	6:15:00	7.2	1.0221	0.4	1,433,539	Open	15.1	293
8/8/2026	6:30:00	7.2	1.4877	0.9	1,433,539	Closed	15.5	293
8/8/2026	6:45:00	7.2	1.0410	0.4	1,433,558	Open	15.1	290
8/8/2026	7:00:00	7.2	1.5596	0.6	1,433,581	Open	14.9	288
8/8/2026	7:15:00	7.2	0.0000	0.9	1,433,593	Closed	15.2	287
8/8/2026	7:30:00	7.2	1.5823	1.2	1,433,601	Open	15.1	287
8/8/2026	7:45:00	7.1	1.0902	1.3	1,433,621	Open	15.3	287
8/8/2026	8:00:00	7.1	0.0000	0.7	1,433,627	Closed	15.3	287



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	8:15:00	7.1	0.7382	2.1	1,433,640	Open	15.2	287
8/8/2026	8:30:00	7.1	0.0000	0.6	1,433,660	Closed	14.8	285
8/8/2026	8:45:00	7.1	0.0000	0.6	1,433,660	Closed	15.2	285
8/8/2026	9:00:00	7.1	1.5558	0.6	1,433,673	Open	14.9	283
8/8/2026	9:15:00	7.1	1.0486	0.6	1,433,693	Open	14.9	285
8/8/2026	9:30:00	7.2	1.4915	0.9	1,433,715	Open	14.9	285
8/8/2026	9:45:00	7.2	1.0296	0.7	1,433,723	Open	15.1	283
8/8/2026	10:00:00	7.2	1.5444	1	1,433,746	Open	15.1	285
8/8/2026	10:15:00	7.2	0.0000	1	1,433,758	Closed	15.4	287
8/8/2026	10:30:00	7.2	1.5104	1.2	1,433,774	Open	15.3	285
8/8/2026	10:45:00	7.2	1.0599	1.4	1,433,794	Open	15.6	287
8/8/2026	11:00:00	7.2	0.0000	1.3	1,433,801	Closed	15.8	288
8/8/2026	11:15:00	7.2	1.0751	1.4	1,433,812	Open	16	288
8/8/2026	11:30:00	7.2	1.5482	1.3	1,433,835	Open	15.8	290
8/8/2026	11:45:00	7.2	0.0000	1.3	1,433,846	Closed	16.1	290
8/8/2026	12:00:00	7.2	1.5558	1.4	1,433,862	Open	16.1	292
8/8/2026	12:15:00	7.3	0.0000	14	1,433,872	Open	16	292
8/8/2026	12:30:00	7.3	1.5331	3.6	1,433,893	Open	16.1	292
8/8/2026	12:45:00	7.3	0.0000	3.9	1,433,911	Closed	16.3	294
8/8/2026	13:00:00	7.2	0.0000	2.8	1,433,911	Closed	16.8	295
8/8/2026	13:15:00	7.3	1.0864	3.8	1,433,929	Open	16.5	297
8/8/2026	13:30:00	7.3	1.5104	3.9	1,433,952	Open	16.4	295
8/8/2026	13:45:00	7.2	1.0751	7.3	1,433,955	Open	16.8	295
8/8/2026	14:00:00	7.3	1.5596	3.2	1,433,979	Open	16.5	295
8/8/2026	14:15:00	7.2	1.1016	2	1,433,998	Open	16.6	298
8/8/2026	14:30:00	7.2	1.5709	2.5	1,434,000	Open	17	300
8/8/2026	14:45:00	7.3	0.7344	2.9	1,434,019	Open	16.7	300
8/8/2026	15:00:00	7.2	1.6202	3.8	1,434,044	Open	16.7	303
8/8/2026	15:15:00	7.2	0.0000	2.8	1,434,044	Closed	17.1	303
8/8/2026	15:30:00	7.2	1.6012	4.2	1,434,061	Open	16.9	303
8/8/2026	15:45:00	7.2	1.4422	4.4	1,434,081	Open	17	303
8/8/2026	16:00:00	7.2	1.6580	2.4	1,434,083	Closed	17.2	303



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	16:15:00	7.3	1.5899	2.5	1,434,103	Open	17	303
8/8/2026	16:30:00	7.3	1.5899	5.4	1,434,127	Open	16.9	303
8/8/2026	16:45:00	7.2	0.0000	3.7	1,434,129	Closed	17.2	305
8/8/2026	17:00:00	7.3	1.6883	26.3	1,434,145	Open	17.1	302
8/8/2026	17:15:00	7.3	1.6202	5.8	1,434,164	Open	17	302
8/8/2026	17:30:00	7.3	1.6391	2.8	1,434,166	Open	17.5	304
8/8/2026	17:45:00	7.3	1.5937	4.8	1,434,187	Open	17.1	304
8/8/2026	18:00:00	7.3	1.6164	0.5	1,434,211	Open	17	304
8/8/2026	18:15:00	7.3	0.0000	0.4	1,434,225	Closed	17.2	306
8/8/2026	18:30:00	7.3	1.6277	0.5	1,434,231	Open	17.3	307
8/8/2026	18:45:00	7.3	0.0000	0.6	1,434,251	Closed	17.1	304
8/8/2026	19:00:00	7.3	1.6126	2.2	1,434,260	Open	17	305
8/8/2026	19:15:00	7.3	1.6050	2.6	1,434,280	Open	17	303
8/8/2026	19:30:00	7.3	1.5558	0	1,434,302	Open	16.7	303
8/8/2026	19:45:00	7.3	0.0000	0	1,434,314	Closed	16.9	303
8/8/2026	20:00:00	7.3	1.6164	0.3	1,434,328	Open	16.6	303
8/8/2026	20:15:00	7.3	1.6050	1.1	1,434,348	Open	16.5	303
8/8/2026	20:30:00	7.3	0.0000	1.2	1,434,354	Closed	16.9	303
8/8/2026	20:45:00	7.3	1.5255	0.8	1,434,368	Open	16.2	298
8/8/2026	21:00:00	7.3	1.4801	0.3	1,434,390	Open	15.9	298
8/8/2026	21:15:00	7.2	0.0000	0.3	1,434,403	Closed	16	295
8/8/2026	21:30:00	7.2	1.5331	0.5	1,434,411	Open	15.8	295
8/8/2026	21:45:00	7.2	1.5179	1.2	1,434,430	Open	15.7	292
8/8/2026	22:00:00	7.2	0.0000	3.6	1,434,440	Closed	15.9	292
8/8/2026	22:15:00	7.2	1.5255	3.3	1,434,452	Open	15.5	292
8/8/2026	22:30:00	7.2	1.5293	3	1,434,475	Open	15.4	290
8/8/2026	22:45:00	7.2	1.4952	1.7	1,434,478	Open	15.6	291
8/8/2026	23:00:00	7.2	0.0000	1	1,434,481	Closed	15.6	287
8/8/2026	23:15:00	7.3	1.5104	2.4	1,434,489	Open	15.3	287
8/8/2026	23:30:00	7.3	1.5028	1.4	1,434,511	Open	15.1	287
8/8/2026	23:45:00	7.3	0.0000	1.8	1,434,523	Closed	15.2	287
8/9/2026	0:00:00	7.3	1.5028	1	1,434,536	Open	15	287



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	0:15:00	7.3	1.4801	2.8	1,434,555	Open	15	287
8/9/2026	0:30:00	7.3	1.5520	1.7	1,434,577	Open	15	287
8/9/2026	0:45:00	7.3	0.0000	1.3	1,434,591	Closed	15.2	287
8/9/2026	1:00:00	7.3	1.6050	1.5	1,434,592	Open	15.4	288
8/9/2026	1:15:00	7.4	1.4574	1.9	1,434,611	Open	15.1	288
8/9/2026	1:30:00	7.4	1.6239	1.3	1,434,632	Open	15.1	290
8/9/2026	1:45:00	7.4	1.6164	1.4	1,434,653	Open	15.1	290
8/9/2026	2:00:00	7.4	0.0000	0.8	1,434,671	Closed	15.2	292
8/9/2026	2:15:00	7.4	1.6618	0.7	1,434,678	Open	15.3	292
8/9/2026	2:30:00	7.4	1.6088	0.7	1,434,702	Open	15.2	290
8/9/2026	2:45:00	7.3	0.0000	3.7	1,434,704	Closed	15.5	292
8/9/2026	3:00:00	7.3	1.6883	0.5	1,434,709	Open	15.3	288
8/9/2026	3:15:00	7.3	1.6807	1.3	1,434,731	Open	15.2	288
8/9/2026	3:30:00	7.3	0.0000	0.6	1,434,745	Closed	15.2	290
8/9/2026	3:45:00	7.3	1.6883	0.7	1,434,756	Open	15.1	288
8/9/2026	4:00:00	7.4	1.6883	0.8	1,434,781	Open	14.9	288
8/9/2026	4:15:00	7.4	0.0000	1.2	1,434,800	Closed	15	287
8/9/2026	4:30:00	7.3	0.0000	1	1,434,800	Closed	15.4	289
8/9/2026	4:45:00	7.4	1.6580	1.8	1,434,815	Open	14.9	289
8/9/2026	5:00:00	7.4	0.0000	1.3	1,434,834	Closed	14.9	290
8/9/2026	5:15:00	7.4	0.0000	1	1,434,844	Closed	14.9	291
8/9/2026	5:30:00	7.4	1.5785	1.1	1,434,859	Open	14.8	291
8/9/2026	5:45:00	7.4	1.5709	0.6	1,434,878	Open	14.9	292
8/9/2026	6:00:00	7.4	1.5558	0.5	1,434,902	Open	14.8	291
8/9/2026	6:15:00	7.4	1.5823	1.1	1,434,904	Open	15.1	291
8/9/2026	6:30:00	7.4	1.5444	1	1,434,927	Open	14.7	291
8/9/2026	6:45:00	7.4	0.0000	1	1,434,936	Closed	14.9	291
8/9/2026	7:00:00	7.4	1.6050	1.3	1,434,944	Open	14.9	291
8/9/2026	7:15:00	7.4	1.6467	1.3	1,434,964	Open	14.8	289
8/9/2026	7:30:00	7.3	0.0000	1	1,434,970	Closed	15.2	290
8/9/2026	7:45:00	7.3	1.6959	1.5	1,434,984	Open	14.9	290
8/9/2026	8:00:00	7.3	0.0000	0.9	1,435,007	Closed	14.7	288



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	8:15:00	7.3	1.6580	1.3	1,435,010	Open	15	287
8/9/2026	8:30:00	7.3	1.6202	0.8	1,435,035	Open	14.7	285
8/9/2026	8:45:00	7.3	0.0000	2.2	1,435,044	Closed	14.9	283
8/9/2026	9:00:00	7.3	1.6694	3	1,435,049	Open	14.9	285
8/9/2026	9:15:00	7.3	0.0000	1.6	1,435,061	Closed	15.1	285
8/9/2026	9:30:00	7.3	1.6580	1.1	1,435,074	Open	15	283
8/9/2026	9:45:00	7.3	0.0000	1.2	1,435,088	Closed	15	283
8/9/2026	10:00:00	7.3	1.0410	1.5	1,435,094	Open	15	285
8/9/2026	10:15:00	7.3	1.5520	1.5	1,435,110	Open	15.2	285
8/9/2026	10:30:00	7.3	1.5672	2.3	1,435,134	Open	15.3	287
8/9/2026	10:45:00	7.3	0.0000	3.7	1,435,146	Closed	15.5	287
8/9/2026	11:00:00	7.3	1.5823	2.4	1,435,160	Open	15.5	288
8/9/2026	11:15:00	7.4	0.0000	3.5	1,435,163	Open	15.5	287
8/9/2026	11:30:00	7.3	1.3627	2.4	1,435,179	Open	15.6	288
8/9/2026	11:45:00	7.3	1.3590	2.4	1,435,195	Open	15.8	290
8/9/2026	12:00:00	7.3	1.3514	0.5	1,435,216	Open	15.9	290
8/9/2026	12:15:00	7.3	1.3249	0.7	1,435,232	Open	16	290
8/9/2026	12:30:00	7.3	0.0000	0.4	1,435,232	Closed	16.5	288
8/9/2026	12:45:00	7.3	1.3552	0.6	1,435,244	Open	16.3	288
8/9/2026	13:00:00	7.4	1.3325	0.5	1,435,264	Open	16.2	287
8/9/2026	13:15:00	7.4	1.2908	0.4	1,435,279	Open	16.2	287
8/9/2026	13:30:00	7.4	1.2643	0	1,435,298	Open	16.3	287
8/9/2026	13:45:00	7.4	0.0000	0	1,435,308	Closed	16.6	287
8/9/2026	14:00:00	7.4	1.2984	0	1,435,323	Open	16.4	287
8/9/2026	14:15:00	7.4	1.2984	0	1,435,339	Open	16.5	287
8/9/2026	14:30:00	7.4	1.2946	0.1	1,435,358	Open	16.4	287
8/9/2026	14:45:00	7.4	0.0000	0	1,435,370	Closed	16.6	287
8/9/2026	15:00:00	7.4	1.3060	0.1	1,435,379	Open	16.6	285
8/9/2026	15:15:00	7.4	1.2946	0.2	1,435,395	Open	16.6	285
8/9/2026	15:30:00	7.4	1.2605	0.4	1,435,414	Open	16.5	285
8/9/2026	15:45:00	7.3	0.0000	0.8	1,435,420	Closed	17	287
8/9/2026	16:00:00	7.4	1.2833	0.4	1,435,433	Open	16.6	287



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	16:15:00	7.4	1.2454	0.8	1,435,449	Open	16.6	287
8/9/2026	16:30:00	7.4	1.2265	0.5	1,435,467	Open	16.5	287
8/9/2026	16:45:00	7.4	0.0000	1	1,435,478	Closed	16.7	290
8/9/2026	17:00:00	7.4	1.2643	1.1	1,435,487	Open	16.6	290
8/9/2026	17:15:00	7.4	1.2454	1.5	1,435,502	Open	16.6	292
8/9/2026	17:30:00	7.4	1.2189	0.9	1,435,521	Open	16.4	292
8/9/2026	17:45:00	7.4	1.2303	1.3	1,435,536	Open	16.4	292
8/9/2026	18:00:00	7.4	1.2227	0.7	1,435,554	Open	16.3	290
8/9/2026	18:15:00	7.4	0.0000	0.5	1,435,556	Closed	16.9	290
8/9/2026	18:30:00	7.5	1.5823	1.6	1,435,559	Open	16.4	290
8/9/2026	18:45:00	7.4	0.0000	1.4	1,435,566	Closed	16.8	290
8/9/2026	19:00:00	7.4	1.4574	0.2	1,435,580	Open	16.4	288
8/9/2026	19:15:00	7.4	1.4498	0	1,435,598	Open	16.4	288
8/9/2026	19:30:00	7.4	1.4460	0.2	1,435,620	Open	16.2	288
8/9/2026	19:45:00	7.4	0.0000	0.3	1,435,632	Closed	16.5	288
8/9/2026	20:00:00	7.4	1.4460	0.8	1,435,640	Open	16.3	287
8/9/2026	20:15:00	7.4	1.4271	0.9	1,435,658	Open	16.2	287
8/9/2026	20:30:00	7.4	0.0000	0.6	1,435,670	Closed	16.2	287
8/9/2026	20:45:00	7.4	1.4385	0.3	1,435,679	Open	16.1	287
8/9/2026	21:00:00	7.4	0.0000	0.6	1,435,689	Closed	16.1	285
8/9/2026	21:15:00	7.4	1.4498	0.2	1,435,694	Open	16.1	285
8/9/2026	21:30:00	7.4	1.4157	0.3	1,435,716	Open	15.7	285
8/9/2026	21:45:00	7.4	1.3552	0.8	1,435,733	Open	15.7	285
8/9/2026	22:00:00	7.4	1.4422	1.8	1,435,735	Open	16.1	285
8/9/2026	22:15:00	7.4	1.7791	2.4	1,435,756	Open	15.7	287
8/9/2026	22:30:00	7.4	0.0000	1.2	1,435,769	Closed	15.9	290
8/9/2026	22:45:00	7.4	1.7564	2.4	1,435,782	Open	15.6	290
8/9/2026	23:00:00	7.4	0.0000	2.2	1,435,804	Closed	15.5	290
8/9/2026	23:15:00	7.4	1.0448	2.8	1,435,809	Open	15.6	293
8/9/2026	23:30:00	7.4	1.6580	2.4	1,435,833	Open	15.4	293
8/9/2026	23:45:00	7.4	0.0000	2.1	1,435,835	Closed	16	295

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

Appendix B: CP2 WTP Data Logs



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	0:00:00	6.97	1.5192	0	240062	ON	13.7	234
8/3/2026	0:15:00	6.96	2.2284	0	240083	ON	13.7	233
8/3/2026	0:30:00	6.96	1.9842	0	240119	ON	13.6	232
8/3/2026	0:45:00	6.95	0.9262	0	240148	ON	13.6	232
8/3/2026	1:00:00	6.96	0.3333	0	240154	ON	13.6	233
8/3/2026	1:15:00	6.96	0.0039	0	240158	ON	13.7	232
8/3/2026	1:30:00	6.94	2.4686	0	240173	ON	13.5	231
8/3/2026	1:45:00	6.93	0.1318	0	240191	ON	13.5	231
8/3/2026	2:00:00	6.94	0.0078	0	240191	ON	13.7	231
8/3/2026	2:15:00	6.93	0.1783	0	240192	ON	14.2	231
8/3/2026	2:30:00	6.93	2.4144	0	240204	ON	13.5	230
8/3/2026	2:45:00	6.94	2.4454	0	240241	ON	13.4	230
8/3/2026	3:00:00	6.93	2.3950	0	240273	ON	13.4	230
8/3/2026	3:15:00	6.95	2.4028	0	240307	ON	13.4	230
8/3/2026	3:30:00	6.95	1.1200	0	240337	ON	13.4	229
8/3/2026	3:45:00	6.96	0.5271	0	240348	ON	13.4	230
8/3/2026	4:00:00	6.96	2.3369	0	240362	ON	13.3	229
8/3/2026	4:15:00	6.96	0.8293	0	240393	ON	13.3	230
8/3/2026	4:30:00	6.98	0.0078	0	240402	ON	13.4	0
8/3/2026	4:45:00	6.97	0.0000	0	240402	ON	13.6	230
8/3/2026	5:00:00	6.95	0.3798	0	240410	ON	13.3	231
8/3/2026	5:15:00	6.96	0.6859	0	240415	ON	13.3	232
8/3/2026	5:30:00	6.92	0.6937	0	240423	ON	13.3	230
8/3/2026	5:45:00	6.91	2.1315	0	240453	ON	13.3	231
8/3/2026	6:00:00	6.9	1.9532	0	240483	ON	13.3	231
8/3/2026	6:15:00	6.9	1.7129	0	240510	ON	13.3	230
8/3/2026	6:30:00	6.89	0.5232	0	240529	ON	13.3	230
8/3/2026	6:45:00	6.9	0.0698	0	240529	ON	13.5	230
8/3/2026	7:00:00	6.9	1.3370	0	240546	ON	13.2	230
8/3/2026	7:15:00	6.88	1.1665	0	240564	ON	13.3	232
8/3/2026	7:30:00	6.88	0.9999	0	240580	ON	13.3	232
8/3/2026	7:45:00	6.83	2.3911	0	240604	ON	13.3	232



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	8:00:00	6.82	2.4570	0	240639	ON	13.3	230
8/3/2026	8:15:00	6.84	2.4376	0	240674	ON	13.3	230
8/3/2026	8:30:00	6.89	0.4302	0	240687	ON	13.4	230
8/3/2026	8:45:00	6.88	0.3992	0	240694	ON	13.5	230
8/3/2026	9:00:00	6.87	0.7325	0	240698	ON	13.6	231
8/3/2026	9:15:00	6.88	2.4454	0	240730	ON	13.6	227
8/3/2026	9:30:00	6.88	1.1742	0	240759	ON	13.6	227
8/3/2026	9:45:00	6.9	0.3410	0	240769	ON	13.7	227
8/3/2026	10:00:00	6.9	0.3062	0	240773	ON	14.1	227
8/3/2026	10:15:00	6.88	0.7983	0	240779	ON	14.1	227
8/3/2026	10:30:00	6.89	0.8952	0	240790	ON	14.1	226
8/3/2026	10:45:00	6.93	1.5734	0	240811	ON	14.1	230
8/3/2026	11:00:00	6.97	1.8176	0	240833	ON	14.2	231
8/3/2026	11:15:00	6.98	1.2246	0	240855	ON	14.3	232
8/3/2026	11:30:00	6.98	1.4765	0	240871	ON	14.4	233
8/3/2026	11:45:00	6.98	1.1975	0	240891	ON	14.5	231
8/3/2026	12:00:00	6.97	0.9146	0	240905	ON	14.7	231
8/3/2026	12:15:00	6.98	0.9456	0	240917	ON	14.8	231
8/3/2026	12:30:00	6.98	1.5230	0	240936	ON	14.9	232
8/3/2026	12:45:00	6.97	1.7284	0	240966	ON	14.8	229
8/3/2026	13:00:00	6.97	1.0541	0	240997	ON	14.8	229
8/3/2026	13:15:00	6.98	0.0078	0	241005	ON	15	228
8/3/2026	13:30:00	6.95	0.4108	0	241010	ON	15.6	229
8/3/2026	13:45:00	6.95	0.6821	0	241023	ON	15.3	230
8/3/2026	14:00:00	6.95	0.7557	0	241039	ON	15.1	227
8/3/2026	14:15:00	6.94	2.0113	0	241054	ON	14.9	227
8/3/2026	14:30:00	6.96	2.4338	0	241085	ON	14.8	226
8/3/2026	14:45:00	6.97	0.9689	0	241113	ON	14.9	225
8/3/2026	15:00:00	6.98	0.4302	0	241117	ON	15.1	227
8/3/2026	15:15:00	6.96	0.4922	0	241124	ON	15.2	227
8/3/2026	15:30:00	6.95	0.4340	0	241131	ON	15.4	227
8/3/2026	15:45:00	6.99	1.9920	0	241151	ON	15.3	226



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/3/2026	16:00:00	7	1.8331	0	241182	ON	15.2	226
8/3/2026	16:15:00	6.99	1.0502	0	241209	ON	15	226
8/3/2026	16:30:00	6.98	0.4495	0	241217	ON	15.1	226
8/3/2026	16:45:00	6.97	0.2984	0	241223	ON	15.3	226
8/3/2026	17:00:00	6.97	2.0307	0	241245	ON	15.1	227
8/3/2026	17:15:00	6.97	0.5929	0	241270	ON	15	225
8/3/2026	17:30:00	6.96	0.4922	0	241278	ON	15	226
8/3/2026	17:45:00	6.95	0.4457	0	241285	ON	15.1	226
8/3/2026	18:00:00	6.94	0.4263	0	241292	ON	15.2	227
8/3/2026	18:15:00	6.96	2.3020	0	241314	ON	15	226
8/3/2026	18:30:00	6.97	2.3136	0	241345	ON	14.8	225
8/3/2026	18:45:00	6.97	0.6007	0	241366	ON	14.8	226
8/3/2026	19:00:00	6.97	0.6976	0	241374	ON	14.8	228
8/3/2026	19:15:00	6.99	2.2865	0	241405	ON	14.7	227
8/3/2026	19:30:00	6.99	1.1626	0	241437	ON	14.7	226
8/3/2026	19:45:00	6.99	0.6743	0	241453	ON	14.7	227
8/3/2026	20:00:00	6.99	1.7827	0	241459	ON	14.8	226
8/3/2026	20:15:00	6.98	0.1744	0	241476	ON	14.7	225
8/3/2026	20:30:00	6.97	0.6666	0	241483	ON	14.6	225
8/3/2026	20:45:00	6.99	1.7401	0	241503	ON	14.4	226
8/3/2026	21:00:00	7.01	1.6626	0	241534	ON	14.3	225
8/3/2026	21:15:00	7.01	2.0695	0	241563	ON	14.3	224
8/3/2026	21:30:00	7.02	1.8912	0	241588	ON	14.2	223
8/3/2026	21:45:00	7.01	0.7596	0	241611	ON	14.1	223
8/3/2026	22:00:00	7.02	0.0039	0	241616	ON	14.4	80
8/3/2026	22:15:00	6.98	0.0000	0	241616	ON	15	205
8/3/2026	22:30:00	6.98	1.5850	0	241622	ON	14.3	226
8/3/2026	22:45:00	6.99	0.5891	0	241639	ON	14.1	227
8/3/2026	23:00:00	7	0.9960	0	241645	ON	14	227
8/3/2026	23:15:00	6.99	1.4765	0	241670	ON	13.8	229
8/3/2026	23:30:00	6.98	2.4725	0	241702	ON	13.7	230
8/3/2026	23:45:00	6.99	0.4147	0	241718	ON	13.7	231



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	0:00:00	6.98	0.5154	0	241724	ON	13.7	232
8/4/2026	0:15:00	7	2.4570	0	241754	ON	13.6	229
8/4/2026	0:30:00	7	2.2284	0	241789	ON	13.6	230
8/4/2026	0:45:00	6.99	0.2790	0	241813	ON	13.6	230
8/4/2026	1:00:00	7	0.4030	0	241821	ON	13.6	230
8/4/2026	1:15:00	6.99	0.4263	0	241825	ON	14.1	230
8/4/2026	1:30:00	6.98	0.5154	0	241832	ON	14.7	231
8/4/2026	1:45:00	7	0.5232	0	241843	ON	13.7	231
8/4/2026	2:00:00	6.99	0.1201	0	241851	ON	13.6	231
8/4/2026	2:15:00	7	2.1857	0	241857	ON	13.6	232
8/4/2026	2:30:00	6.99	2.3136	0	241893	ON	13.6	233
8/4/2026	2:45:00	6.99	1.0386	0	241921	ON	13.6	233
8/4/2026	3:00:00	7	0.0039	0	241926	ON	13.7	232
8/4/2026	3:15:00	6.99	0.4844	0	241932	ON	13.6	233
8/4/2026	3:30:00	6.99	2.2361	0	241957	ON	13.5	230
8/4/2026	3:45:00	6.98	2.2245	0	241986	ON	13.5	230
8/4/2026	4:00:00	6.98	0.5116	0	242011	ON	13.5	229
8/4/2026	4:15:00	6.99	0.4844	0	242019	ON	13.5	229
8/4/2026	4:30:00	6.98	0.4340	0	242022	ON	13.5	229
8/4/2026	4:45:00	6.97	0.3255	0	242026	ON	13.5	230
8/4/2026	5:00:00	6.97	0.1163	0	242034	ON	13.4	229
8/4/2026	5:15:00	6.97	0.3100	0	242038	ON	13.5	230
8/4/2026	5:30:00	6.98	2.4299	0	242050	ON	13.5	232
8/4/2026	5:45:00	6.97	0.6821	0	242079	ON	13.5	231
8/4/2026	6:00:00	6.97	0.4883	0	242088	ON	13.4	233
8/4/2026	6:15:00	6.97	2.4376	0	242104	ON	13.4	232
8/4/2026	6:30:00	6.97	2.4531	0	242138	ON	13.5	233
8/4/2026	6:45:00	6.97	2.4454	0	242175	ON	13.5	233
8/4/2026	7:00:00	6.98	0.6472	0	242188	ON	13.5	234
8/4/2026	7:15:00	6.97	0.0039	0	242195	ON	13.5	233
8/4/2026	7:30:00	6.97	2.1005	0	242203	ON	13.5	233
8/4/2026	7:45:00	6.99	2.0811	0	242234	ON	13.5	233



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	8:00:00	6.99	0.8371	0	242254	ON	13.6	235
8/4/2026	8:15:00	7	1.7362	0	242280	ON	13.6	234
8/4/2026	8:30:00	7	0.5426	0	242290	ON	13.7	233
8/4/2026	8:45:00	7.01	0.7363	0	242309	ON	13.8	230
8/4/2026	9:00:00	7.01	2.4919	0	242323	ON	13.8	230
8/4/2026	9:15:00	7.03	0.4069	0	242335	ON	13.9	229
8/4/2026	9:30:00	7.01	0.0000	0	242339	ON	14	230
8/4/2026	9:45:00	7.02	2.2206	0	242365	ON	14	230
8/4/2026	10:00:00	7.04	1.2401	0	242400	ON	14.1	231
8/4/2026	10:15:00	7.02	0.2442	0	242408	ON	14.3	230
8/4/2026	10:30:00	7	0.0039	0	242410	ON	14.8	233
8/4/2026	10:45:00	7	0.0039	0	242410	ON	14.7	233
8/4/2026	11:00:00	6.99	1.1859	0	242420	ON	14.7	233
8/4/2026	11:15:00	7.02	1.7168	0	242442	ON	14.8	232
8/4/2026	11:30:00	7.02	2.4415	0	242470	ON	14.7	232
8/4/2026	11:45:00	7.02	2.4531	0	242508	ON	14.7	231
8/4/2026	12:00:00	7.02	2.4299	0	242543	ON	14.7	233
8/4/2026	12:15:00	7.02	2.4183	0	242577	ON	14.7	233
8/4/2026	12:30:00	7.02	0.7441	0	242594	ON	14.9	233
8/4/2026	12:45:00	7.04	1.8718	0	242610	ON	15.1	237
8/4/2026	13:00:00	7.04	0.3720	0	242624	ON	15.3	238
8/4/2026	13:15:00	7.03	0.3953	0	242628	ON	15.5	241
8/4/2026	13:30:00	7.01	2.3795	0	242638	ON	15.5	240
8/4/2026	13:45:00	7.04	1.2169	0	242660	ON	15.5	244
8/4/2026	14:00:00	7.04	0.9689	0	242677	ON	15.5	247
8/4/2026	14:15:00	7.03	0.0000	0	242684	ON	15.6	248
8/4/2026	14:30:00	7.04	1.8641	0	242704	ON	15.4	251
8/4/2026	14:45:00	7.04	2.3834	0	242735	ON	15.2	250
8/4/2026	15:00:00	7.04	0.5736	0	242760	ON	15.3	251
8/4/2026	15:15:00	7.04	0.5116	0	242768	ON	15.4	251
8/4/2026	15:30:00	7.06	1.8176	0	242793	ON	15.3	252
8/4/2026	15:45:00	7.07	0.0039	0	242802	ON	15.6	251



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/4/2026	16:00:00	7.03	0.2519	0	242804	ON	15.7	251
8/4/2026	16:15:00	7.04	0.6472	0	242815	ON	16.2	253
8/4/2026	16:30:00	7.03	0.8332	0	242829	ON	15.5	250
8/4/2026	16:45:00	7.02	0.9223	0	242842	ON	15.4	249
8/4/2026	17:00:00	7.02	2.4028	0	242873	ON	15.2	249
8/4/2026	17:15:00	7.03	2.3718	0	242907	ON	15.1	250
8/4/2026	17:30:00	7.04	1.2634	0	242941	ON	15.2	249
8/4/2026	17:45:00	7.04	0.5193	0	242952	ON	15.3	250
8/4/2026	18:00:00	7.04	0.3217	0	242957	ON	15.4	249
8/4/2026	18:15:00	7.02	0.3255	0	242961	ON	15.5	251
8/4/2026	18:30:00	7.04	2.3640	0	242976	ON	15.4	248
8/4/2026	18:45:00	7.05	2.3485	0	243011	ON	15	248
8/4/2026	19:00:00	7.03	2.2904	0	243045	ON	14.9	249
8/4/2026	19:15:00	6.99	0.5697	0	243059	ON	14.9	253
8/4/2026	19:30:00	6.97	0.3062	0	243063	ON	14.9	256
8/4/2026	19:45:00	6.95	0.3682	0	243068	ON	15	256
8/4/2026	20:00:00	6.97	0.6084	0	243088	ON	14.8	252
8/4/2026	20:15:00	6.94	0.0000	0	243089	ON	15.8	253
8/4/2026	20:30:00	6.93	0.0000	0	243089	ON	16.2	248
8/4/2026	20:45:00	6.93	1.7711	0	243095	ON	15	251
8/4/2026	21:00:00	6.94	0.0078	0	243108	ON	14.5	247
8/4/2026	21:15:00	6.93	2.3059	0	243121	ON	14.4	243
8/4/2026	21:30:00	6.93	2.2787	0	243155	ON	14.1	235
8/4/2026	21:45:00	6.93	2.0113	0	243188	ON	14	233
8/4/2026	22:00:00	6.93	0.2945	0	243209	ON	14.1	234
8/4/2026	22:15:00	6.9	0.0078	0	243209	ON	15.2	0
8/4/2026	22:30:00	6.95	1.4068	0	243218	ON	14.3	236
8/4/2026	22:45:00	6.98	2.1354	0	243249	ON	14.2	238
8/4/2026	23:00:00	6.99	2.1509	0	243279	ON	14.2	237
8/4/2026	23:15:00	6.99	1.7749	0	243309	ON	14.1	236
8/4/2026	23:30:00	6.95	0.2442	0	243318	ON	14.2	238
8/4/2026	23:45:00	6.92	0.0078	0	243321	ON	14.5	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	0:00:00	6.95	1.2440	0	243328	ON	14.3	236
8/5/2026	0:15:00	6.94	0.4999	0	243340	ON	14.2	235
8/5/2026	0:30:00	6.9	0.1163	0	243346	ON	14.2	241
8/5/2026	0:45:00	6.88	0.0969	0	243346	ON	14.2	241
8/5/2026	1:00:00	6.92	0.6239	0	243355	ON	14.1	234
8/5/2026	1:15:00	6.95	2.2555	0	243380	ON	13.9	233
8/5/2026	1:30:00	6.96	2.2245	0	243414	ON	13.9	234
8/5/2026	1:45:00	6.95	0.5464	0	243434	ON	14	233
8/5/2026	2:00:00	6.95	1.5114	0	243441	ON	14	233
8/5/2026	2:15:00	6.96	2.2090	0	243475	ON	13.9	233
8/5/2026	2:30:00	6.96	2.1741	0	243506	ON	13.9	232
8/5/2026	2:45:00	6.96	0.4457	0	243524	ON	13.9	232
8/5/2026	3:00:00	6.96	0.2054	0	243527	ON	13.9	234
8/5/2026	3:15:00	6.95	0.6317	0	243534	ON	13.9	233
8/5/2026	3:30:00	6.96	0.0000	0	243537	ON	13.9	234
8/5/2026	3:45:00	6.95	1.3874	0	243541	ON	13.9	234
8/5/2026	4:00:00	6.95	0.6394	0	243563	ON	13.8	231
8/5/2026	4:15:00	6.96	0.8875	0	243568	ON	13.8	233
8/5/2026	4:30:00	6.96	2.0966	0	243595	ON	13.7	230
8/5/2026	4:45:00	6.96	0.8758	0	243617	ON	13.7	229
8/5/2026	5:00:00	6.96	0.8255	0	243631	ON	13.7	229
8/5/2026	5:15:00	6.96	1.9881	0	243651	ON	13.7	228
8/5/2026	5:30:00	6.96	2.4686	0	243682	ON	13.7	229
8/5/2026	5:45:00	6.96	2.4996	0	243718	ON	13.7	232
8/5/2026	6:00:00	6.95	2.4725	0	243755	ON	13.7	230
8/5/2026	6:15:00	6.94	1.1200	0	243789	ON	13.7	230
8/5/2026	6:30:00	6.94	0.4185	0	243798	ON	13.7	232
8/5/2026	6:45:00	6.93	0.4108	0	243805	ON	13.7	233
8/5/2026	7:00:00	6.94	2.4299	0	243819	ON	13.6	232
8/5/2026	7:15:00	6.94	2.4299	0	243853	ON	13.6	231
8/5/2026	7:30:00	6.94	0.6201	0	243873	ON	13.6	231
8/5/2026	7:45:00	6.94	0.3759	0	243880	ON	13.7	232



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	8:00:00	6.93	0.8797	0	243887	ON	13.7	232
8/5/2026	8:15:00	6.96	0.7053	0	243902	ON	13.7	230
8/5/2026	8:30:00	6.95	2.4493	0	243921	ON	13.7	226
8/5/2026	8:45:00	6.94	2.4531	0	243958	ON	13.6	225
8/5/2026	9:00:00	6.95	0.5658	0	243973	ON	13.7	226
8/5/2026	9:15:00	6.96	0.3875	0	243980	ON	13.8	227
8/5/2026	9:30:00	6.94	1.0231	0	243987	ON	13.9	229
8/5/2026	9:45:00	6.95	2.3640	0	244021	ON	13.8	224
8/5/2026	10:00:00	6.95	0.9921	0	244051	ON	13.9	224
8/5/2026	10:15:00	6.96	0.3604	0	244061	ON	14	225
8/5/2026	10:30:00	6.94	0.8255	0	244068	ON	14.1	226
8/5/2026	10:45:00	6.95	0.1976	0	244072	ON	14.5	223
8/5/2026	11:00:00	6.94	0.6743	0	244083	ON	14.4	223
8/5/2026	11:15:00	6.94	2.1974	0	244095	ON	14.4	223
8/5/2026	11:30:00	6.95	0.5619	0	244107	ON	14.3	222
8/5/2026	11:45:00	6.95	2.4493	0	244123	ON	14.5	223
8/5/2026	12:00:00	6.96	2.4415	0	244160	ON	14.4	222
8/5/2026	12:15:00	6.97	2.4570	0	244197	ON	14.5	222
8/5/2026	12:30:00	6.99	2.4493	0	244235	ON	14.6	225
8/5/2026	12:45:00	6.98	0.6472	0	244253	ON	14.7	223
8/5/2026	13:00:00	6.98	0.3759	0	244261	ON	14.9	225
8/5/2026	13:15:00	6.96	0.4108	0	244268	ON	15.2	227
8/5/2026	13:30:00	6.97	1.0851	0	244279	ON	15.3	226
8/5/2026	13:45:00	6.98	0.2442	0	244288	ON	15.4	228
8/5/2026	14:00:00	6.97	1.0657	1	244303	ON	15.2	230
8/5/2026	14:15:00	6.96	2.4686	0	244319	ON	15	231
8/5/2026	14:30:00	6.97	0.5852	0	244338	ON	15.1	230
8/5/2026	14:45:00	6.96	0.4418	0	244345	ON	15.3	230
8/5/2026	15:00:00	6.97	2.4609	0	244365	ON	15.3	229
8/5/2026	15:15:00	6.97	2.4648	0	244403	ON	15	226
8/5/2026	15:30:00	6.98	1.1006	0	244437	ON	15	226
8/5/2026	15:45:00	6.98	0.4302	0	244446	ON	15.2	226



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/5/2026	16:00:00	6.97	0.3798	0	244453	ON	15.3	227
8/5/2026	16:15:00	6.97	0.9340	0	244462	ON	15.4	227
8/5/2026	16:30:00	6.96	2.2477	0	244472	ON	15.5	225
8/5/2026	16:45:00	6.98	2.4299	0	244508	ON	15	223
8/5/2026	17:00:00	6.98	0.6433	0	244523	ON	15	224
8/5/2026	17:15:00	6.99	0.4340	0	244530	ON	15.4	226
8/5/2026	17:30:00	6.97	2.4609	0	244541	ON	15.5	223
8/5/2026	17:45:00	6.98	2.4260	0	244575	ON	14.8	222
8/5/2026	18:00:00	6.99	1.1626	0	244611	ON	14.6	222
8/5/2026	18:15:00	6.99	0.4224	0	244622	ON	14.8	223
8/5/2026	18:30:00	6.98	0.4379	0	244629	ON	14.9	223
8/5/2026	18:45:00	6.98	2.4299	0	244645	ON	14.8	223
8/5/2026	19:00:00	6.98	2.4570	0	244682	ON	14.4	222
8/5/2026	19:15:00	6.98	0.9301	0	244711	ON	14.3	222
8/5/2026	19:30:00	6.99	0.3643	0	244720	ON	14.4	222
8/5/2026	19:45:00	6.98	0.4340	0	244726	ON	14.5	224
8/5/2026	20:00:00	6.97	0.9107	0	244733	ON	14.5	222
8/5/2026	20:15:00	6.99	1.1161	0	244763	ON	14.2	221
8/5/2026	20:30:00	7.01	0.0000	0	244772	ON	14.3	222
8/5/2026	20:45:00	6.99	0.0271	0	244772	ON	15.9	0
8/5/2026	21:00:00	6.97	0.0116	0	244772	ON	17	0
8/5/2026	21:15:00	6.99	0.4961	0	244787	ON	14.4	220
8/5/2026	21:30:00	6.99	0.1783	0	244794	ON	14.3	220
8/5/2026	21:45:00	6.99	0.7402	23	244802	ON	14.2	220
8/5/2026	22:00:00	7.01	0.9107	0	244817	ON	14.1	218
8/5/2026	22:15:00	7.03	0.0155	0	244826	ON	14.2	222
8/5/2026	22:30:00	7.04	1.9532	0	244837	ON	14.2	222
8/5/2026	22:45:00	7.05	2.4725	0	244868	ON	14.2	223
8/5/2026	23:00:00	7.05	2.4531	0	244906	ON	14.1	225
8/5/2026	23:15:00	7.04	0.6317	0	244929	ON	14.2	223
8/5/2026	23:30:00	7.04	0.3914	0	244937	ON	14.2	222
8/5/2026	23:45:00	7.04	0.0194	0	244937	ON	15.3	0



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	0:00:00	7.01	0.0271	0	244937	ON	16.3	0
8/6/2026	0:15:00	7.01	0.7596	0	244939	ON	14.8	222
8/6/2026	0:30:00	7.02	0.7014	0	244955	ON	14.1	222
8/6/2026	0:45:00	7.01	0.2442	0	244963	ON	14.1	223
8/6/2026	1:00:00	7.02	2.4493	0	244979	ON	14	222
8/6/2026	1:15:00	7.04	2.4531	0	245016	ON	13.9	224
8/6/2026	1:30:00	7.05	1.0309	0	245047	ON	14	222
8/6/2026	1:45:00	7.06	0.4263	2	245057	ON	14.1	222
8/6/2026	2:00:00	7.06	0.5852	0	245067	ON	14	222
8/6/2026	2:15:00	7.06	0.4767	0	245072	ON	14	222
8/6/2026	2:30:00	7.05	0.7170	0	245094	ON	14	222
8/6/2026	2:45:00	7.04	0.3875	0	245101	ON	14	222
8/6/2026	3:00:00	7.03	0.0194	0	245102	ON	14.6	222
8/6/2026	3:15:00	7.06	0.5154	0	245118	ON	14	223
8/6/2026	3:30:00	7.05	0.7441	0	245125	ON	13.9	222
8/6/2026	3:45:00	7.05	0.7131	0	245145	ON	13.9	223
8/6/2026	4:00:00	7.06	0.4185	0	245153	ON	13.9	222
8/6/2026	4:15:00	7.06	2.4531	0	245168	ON	13.9	222
8/6/2026	4:30:00	7.06	1.9455	0	245202	ON	13.8	223
8/6/2026	4:45:00	7.06	2.3446	0	245229	ON	13.8	224
8/6/2026	5:00:00	7.05	0.6821	0	245247	ON	13.8	224
8/6/2026	5:15:00	7.06	0.4612	0	245255	ON	13.9	226
8/6/2026	5:30:00	7.05	0.4263	0	245262	ON	13.8	225
8/6/2026	5:45:00	7.04	0.7635	0	245269	ON	13.8	226
8/6/2026	6:00:00	7.06	2.4299	0	245301	ON	13.7	226
8/6/2026	6:15:00	7.05	0.9456	0	245330	ON	13.7	226
8/6/2026	6:30:00	7.05	0.3914	0	245339	ON	13.8	227
8/6/2026	6:45:00	7.04	0.3294	0	245344	ON	13.8	229
8/6/2026	7:00:00	7.03	0.4302	0	245350	ON	13.8	229
8/6/2026	7:15:00	7.03	0.4728	0	245356	ON	13.8	229
8/6/2026	7:30:00	7.03	0.4534	0	245363	ON	13.8	228
8/6/2026	7:45:00	7.03	2.3330	0	245373	ON	13.8	228



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	8:00:00	7.04	0.6472	0	245387	ON	13.8	227
8/6/2026	8:15:00	7.04	0.5232	0	245396	ON	13.9	226
8/6/2026	8:30:00	7.02	0.8952	0	245404	ON	13.9	226
8/6/2026	8:45:00	7.02	0.8177	0	245421	ON	14	224
8/6/2026	9:00:00	7.01	0.9921	1	245433	ON	14.1	222
8/6/2026	9:15:00	6.99	0.9727	0	245447	ON	14	222
8/6/2026	9:30:00	7	2.4183	0	245479	ON	14	221
8/6/2026	9:45:00	7.01	0.3992	0	245502	ON	14.1	221
8/6/2026	10:00:00	7.02	0.3100	0	245509	ON	14.2	220
8/6/2026	10:15:00	7.02	0.0271	0	245511	ON	14.7	220
8/6/2026	10:30:00	7.01	1.9842	0	245524	ON	14.6	221
8/6/2026	10:45:00	7.03	0.9727	0	245549	ON	14.5	222
8/6/2026	11:00:00	7.04	0.3643	0	245558	ON	14.6	222
8/6/2026	11:15:00	7.03	1.7672	0	245568	ON	14.8	224
8/6/2026	11:30:00	7.02	0.6433	0	245580	ON	14.9	222
8/6/2026	11:45:00	7.03	2.5539	0	245607	ON	14.8	225
8/6/2026	12:00:00	7.04	2.5345	0	245644	ON	14.8	224
8/6/2026	12:15:00	7.03	2.5423	0	245681	ON	14.8	224
8/6/2026	12:30:00	7.03	0.9650	0	245709	ON	14.9	226
8/6/2026	12:45:00	7.04	0.3875	0	245718	ON	15.2	227
8/6/2026	13:00:00	7.02	0.4185	0	245725	ON	15.5	228
8/6/2026	13:15:00	7	0.7596	0	245732	ON	15.7	229
8/6/2026	13:30:00	7.01	2.5190	0	245765	ON	15.3	226
8/6/2026	13:45:00	6.99	0.7014	0	245793	ON	15.3	227
8/6/2026	14:00:00	7.01	0.3837	0	245801	ON	15.5	229
8/6/2026	14:15:00	6.99	0.0465	0	245806	ON	15.8	230
8/6/2026	14:30:00	6.98	0.7983	0	245815	ON	15.8	227
8/6/2026	14:45:00	6.99	0.3333	0	245821	ON	15.8	228
8/6/2026	15:00:00	6.98	0.5542	0	245831	ON	15.7	230
8/6/2026	15:15:00	6.97	0.4612	0	245838	ON	15.8	230
8/6/2026	15:30:00	6.96	0.8565	3	245849	ON	15.8	227
8/6/2026	15:45:00	6.95	0.4224	0	245858	ON	15.6	225



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/6/2026	16:00:00	6.96	2.0385	0	245881	ON	15.3	227
8/6/2026	16:15:00	6.97	2.5461	0	245918	ON	15.2	226
8/6/2026	16:30:00	6.98	0.7790	0	245934	ON	15.3	226
8/6/2026	16:45:00	6.99	0.3720	0	245942	ON	15.5	227
8/6/2026	17:00:00	7	0.4612	0	245949	ON	15.9	227
8/6/2026	17:15:00	6.99	2.5229	0	245971	ON	15.7	227
8/6/2026	17:30:00	6.98	0.9030	0	245993	ON	15.5	227
8/6/2026	17:45:00	6.98	0.6937	0	246002	ON	15.6	229
8/6/2026	18:00:00	6.99	0.4185	0	246009	ON	15.7	228
8/6/2026	18:15:00	6.97	0.8642	0	246016	ON	15.8	228
8/6/2026	18:30:00	6.97	2.4996	0	246050	ON	15.1	227
8/6/2026	18:45:00	6.98	0.5077	0	246062	ON	15.1	229
8/6/2026	19:00:00	6.97	0.4302	0	246069	ON	15.2	227
8/6/2026	19:15:00	6.96	2.1974	0	246077	ON	15.2	229
8/6/2026	19:30:00	6.94	2.4338	0	246115	ON	14.7	226
8/6/2026	19:45:00	6.98	0.0000	0	246125	ON	15	96
8/6/2026	20:00:00	6.96	0.0310	0	246125	ON	16.6	0
8/6/2026	20:15:00	6.93	0.0349	0	246125	ON	17.7	0
8/6/2026	20:30:00	6.92	0.0426	0	246125	ON	18.6	0
8/6/2026	20:45:00	6.96	0.6666	0	246135	ON	14.8	228
8/6/2026	21:00:00	6.96	0.0891	0	246140	ON	14.7	224
8/6/2026	21:15:00	6.96	1.4300	0	246153	ON	14.5	225
8/6/2026	21:30:00	6.96	1.4145	0	246173	ON	14.3	226
8/6/2026	21:45:00	6.98	2.4686	0	246200	ON	14.2	226
8/6/2026	22:00:00	7	1.9261	0	246233	ON	14.2	225
8/6/2026	22:15:00	7.01	0.0349	0	246246	ON	14.3	223
8/6/2026	22:30:00	7.01	2.4144	0	246257	ON	14.3	228
8/6/2026	22:45:00	7.01	2.4105	0	246291	ON	14.2	228
8/6/2026	23:00:00	7.01	1.3254	0	246325	ON	14.2	229
8/6/2026	23:15:00	7.02	0.3914	0	246336	ON	14.3	228
8/6/2026	23:30:00	7.01	0.0465	0	246337	ON	15.4	227
8/6/2026	23:45:00	7.03	0.0271	0	246337	ON	15	13



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	0:00:00	6.99	1.8176	0	246342	ON	14.6	227
8/7/2026	0:15:00	6.98	2.2090	0	246371	ON	14.2	227
8/7/2026	0:30:00	6.99	0.5697	0	246386	ON	14.2	227
8/7/2026	0:45:00	6.98	0.3217	0	246391	ON	14.3	228
8/7/2026	1:00:00	6.97	1.7517	0	246397	ON	14.3	227
8/7/2026	1:15:00	7	0.0000	0	246402	ON	14.8	0
8/7/2026	1:30:00	6.97	0.0000	0	246402	ON	15.9	0
8/7/2026	1:45:00	6.96	0.2015	0	246406	ON	14.4	226
8/7/2026	2:00:00	6.97	0.7363	0	246414	ON	14.2	229
8/7/2026	2:15:00	6.96	0.7518	0	246425	ON	14.1	228
8/7/2026	2:30:00	6.96	2.1896	0	246435	ON	14.1	228
8/7/2026	2:45:00	6.97	1.7013	0	246467	ON	14	230
8/7/2026	3:00:00	6.98	1.5773	0	246491	ON	14.1	231
8/7/2026	3:15:00	7	2.5306	0	246519	ON	14.1	232
8/7/2026	3:30:00	7.02	2.5074	0	246556	ON	14.1	233
8/7/2026	3:45:00	7.02	0.6356	0	246578	ON	14.2	232
8/7/2026	4:00:00	7.02	0.3643	0	246586	ON	14.2	232
8/7/2026	4:15:00	7.01	0.3953	0	246592	ON	14.2	232
8/7/2026	4:30:00	7.01	0.0310	0	246595	ON	14.6	231
8/7/2026	4:45:00	7.03	0.5348	0	246606	ON	14.3	233
8/7/2026	5:00:00	7.03	0.2674	0	246610	ON	14.3	235
8/7/2026	5:15:00	7.01	0.1511	0	246614	ON	14.3	234
8/7/2026	5:30:00	7	2.5461	0	246631	ON	14.2	237
8/7/2026	5:45:00	7	2.5268	0	246668	ON	14.1	235
8/7/2026	6:00:00	7.01	2.4686	0	246706	ON	14.1	237
8/7/2026	6:15:00	7.01	0.5929	0	246723	ON	14.2	236
8/7/2026	6:30:00	7.01	0.4728	0	246730	ON	14.2	237
8/7/2026	6:45:00	7.03	1.0580	0	246755	ON	14.1	235
8/7/2026	7:00:00	7.02	0.6317	0	246766	ON	14.2	234
8/7/2026	7:15:00	7.01	0.5232	0	246775	ON	14.2	237
8/7/2026	7:30:00	7.02	2.5500	0	246788	ON	14.2	236
8/7/2026	7:45:00	7.03	2.5229	0	246825	ON	14.1	236



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	8:00:00	7.02	0.8720	0	246853	ON	14.2	236
8/7/2026	8:15:00	7.01	0.1240	0	246856	ON	14.4	237
8/7/2026	8:30:00	7.02	2.5423	0	246889	ON	14.2	232
8/7/2026	8:45:00	7	0.3992	0	246913	ON	14.3	233
8/7/2026	9:00:00	7	0.4457	0	246921	ON	14.4	233
8/7/2026	9:15:00	7	0.8061	0	246928	ON	14.5	233
8/7/2026	9:30:00	7.02	0.8797	0	246953	ON	14.6	236
8/7/2026	9:45:00	7.02	1.7633	0	246963	ON	14.7	238
8/7/2026	10:00:00	7.03	0.0271	0	246975	ON	14.9	238
8/7/2026	10:15:00	7.02	0.0233	0	246975	ON	16	220
8/7/2026	10:30:00	7.02	0.0116	0	246975	ON	15.9	236
8/7/2026	10:45:00	6.99	0.3875	0	246976	ON	15.4	241
8/7/2026	11:00:00	6.99	0.6666	0	246984	ON	15.4	239
8/7/2026	11:15:00	6.99	0.7441	0	246996	ON	15.4	235
8/7/2026	11:30:00	6.99	1.1045	0	247030	ON	15.2	234
8/7/2026	11:45:00	7	0.4224	0	247041	ON	15.3	233
8/7/2026	12:00:00	6.99	0.3953	0	247048	ON	15.6	234
8/7/2026	12:15:00	6.97	1.0347	0	247055	ON	15.8	234
8/7/2026	12:30:00	7.01	2.5306	0	247090	ON	15.8	237
8/7/2026	12:45:00	6.99	0.8875	0	247113	ON	15.9	237
8/7/2026	13:00:00	7	1.1200	0	247135	ON	15.7	237
8/7/2026	13:15:00	7.01	2.5423	0	247156	ON	15.7	236
8/7/2026	13:30:00	7.02	2.5423	0	247193	ON	15.5	233
8/7/2026	13:45:00	7.02	0.4457	0	247221	ON	15.7	232
8/7/2026	14:00:00	7.02	0.4302	0	247228	ON	15.9	233
8/7/2026	14:15:00	7.01	0.4147	0	247235	ON	16.2	233
8/7/2026	14:30:00	6.99	0.4612	0	247242	ON	16.3	234
8/7/2026	14:45:00	7.02	2.5461	0	247264	ON	16.1	231
8/7/2026	15:00:00	6.98	1.9765	0	247301	ON	15.8	231
8/7/2026	15:15:00	6.95	1.9726	0	247331	ON	15.5	228
8/7/2026	15:30:00	6.94	0.5348	0	247354	ON	15.4	230
8/7/2026	15:45:00	6.96	0.3759	0	247362	ON	15.6	231



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/7/2026	16:00:00	6.94	0.3139	0	247367	ON	15.8	232
8/7/2026	16:15:00	6.93	0.3643	0	247371	ON	15.9	233
8/7/2026	16:30:00	6.93	0.4457	0	247378	ON	16.1	233
8/7/2026	16:45:00	6.93	2.0268	0	247402	ON	15.7	229
8/7/2026	17:00:00	6.92	0.6782	0	247428	ON	15.2	227
8/7/2026	17:15:00	6.95	0.3139	0	247433	ON	15.4	228
8/7/2026	17:30:00	6.93	0.3410	0	247437	ON	15.5	230
8/7/2026	17:45:00	6.92	0.4069	0	247443	ON	15.7	230
8/7/2026	18:00:00	6.92	0.4418	0	247450	ON	15.8	233
8/7/2026	18:15:00	6.93	0.4767	0	247458	ON	15.8	229
8/7/2026	18:30:00	6.92	0.9185	3	247468	ON	15.6	228
8/7/2026	18:45:00	6.91	2.5423	0	247486	ON	15	228
8/7/2026	19:00:00	6.93	2.5655	0	247523	ON	14.7	229
8/7/2026	19:15:00	6.95	0.9805	0	247553	ON	14.8	230
8/7/2026	19:30:00	6.96	0.6046	0	247563	ON	14.9	229
8/7/2026	19:45:00	6.99	2.5500	0	247588	ON	14.9	233
8/7/2026	20:00:00	7.02	2.5616	0	247625	ON	14.9	233
8/7/2026	20:15:00	7.01	0.6123	0	247651	ON	14.9	232
8/7/2026	20:30:00	7.01	0.5271	0	247659	ON	15	233
8/7/2026	20:45:00	6.99	0.8410	0	247667	ON	14.9	233
8/7/2026	21:00:00	7.03	0.0233	0	247673	ON	15.5	0
8/7/2026	21:15:00	7.01	0.0349	0	247673	ON	15.3	232
8/7/2026	21:30:00	6.97	0.1938	0	247673	ON	15	233
8/7/2026	21:45:00	7.02	2.0191	0	247700	ON	14.5	230
8/7/2026	22:00:00	7.02	0.0194	0	247722	ON	14.4	228
8/7/2026	22:15:00	7.02	0.5193	0	247730	ON	14.4	230
8/7/2026	22:30:00	7.01	0.4573	0	247737	ON	14.4	230
8/7/2026	22:45:00	7	1.1122	0	247747	ON	14.4	228
8/7/2026	23:00:00	7	1.1704	0	247764	ON	14.2	228
8/7/2026	23:15:00	7	0.9805	0	247783	ON	14.2	230
8/7/2026	23:30:00	7.02	0.0000	0	247788	ON	14.2	229
8/7/2026	23:45:00	7.01	0.4418	0	247788	ON	14.3	230



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	0:00:00	6.99	1.9610	0	247797	ON	14.2	231
8/8/2026	0:15:00	7.01	0.6976	0	247818	ON	14.1	232
8/8/2026	0:30:00	7.01	0.0891	0	247822	ON	14.2	233
8/8/2026	0:45:00	7.01	2.4183	0	247838	ON	14.1	233
8/8/2026	1:00:00	7.02	2.4221	0	247873	ON	14	237
8/8/2026	1:15:00	7.02	0.6704	0	247893	ON	14	237
8/8/2026	1:30:00	7.02	0.4147	0	247900	ON	14.1	237
8/8/2026	1:45:00	7	0.9301	0	247908	ON	14.1	237
8/8/2026	2:00:00	7.01	0.6123	0	247929	ON	14	236
8/8/2026	2:15:00	7.01	0.7363	0	247934	ON	14.1	237
8/8/2026	2:30:00	7.01	2.4183	0	247965	ON	13.9	235
8/8/2026	2:45:00	7	0.7131	0	247989	ON	13.9	234
8/8/2026	3:00:00	7.01	0.3720	0	247997	ON	14	236
8/8/2026	3:15:00	7	0.4069	0	248004	ON	14	235
8/8/2026	3:30:00	6.99	0.8991	0	248012	ON	14	235
8/8/2026	3:45:00	6.99	0.9030	0	248025	ON	13.9	233
8/8/2026	4:00:00	7.01	1.2285	0	248041	ON	13.9	232
8/8/2026	4:15:00	7.01	0.6511	0	248052	ON	13.9	233
8/8/2026	4:30:00	7.01	2.3989	0	248079	ON	13.9	232
8/8/2026	4:45:00	7	2.4144	0	248113	ON	13.9	233
8/8/2026	5:00:00	7.02	0.5774	0	248125	ON	13.9	233
8/8/2026	5:15:00	7.01	0.1705	0	248130	ON	13.9	231
8/8/2026	5:30:00	6.99	2.3950	0	248143	ON	13.9	233
8/8/2026	5:45:00	6.99	2.3989	0	248177	ON	13.7	230
8/8/2026	6:00:00	6.99	0.8797	0	248203	ON	13.7	230
8/8/2026	6:15:00	7.01	0.4844	0	248212	ON	13.8	231
8/8/2026	6:30:00	7	0.5154	0	248219	ON	13.8	232
8/8/2026	6:45:00	7	2.3718	0	248248	ON	13.7	228
8/8/2026	7:00:00	7	2.3679	0	248282	ON	13.7	228
8/8/2026	7:15:00	7.01	0.6084	0	248297	ON	13.7	228
8/8/2026	7:30:00	7.01	0.4185	0	248304	ON	13.8	229
8/8/2026	7:45:00	7	0.3759	0	248311	ON	13.8	229



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	8:00:00	6.99	0.5852	0	248319	ON	13.8	229
8/8/2026	8:15:00	6.99	2.2787	0	248329	ON	13.9	229
8/8/2026	8:30:00	6.99	0.1976	0	248342	ON	13.9	229
8/8/2026	8:45:00	6.97	0.0116	0	248345	ON	14.3	110
8/8/2026	9:00:00	6.96	0.8875	0	248350	ON	14.2	225
8/8/2026	9:15:00	6.96	1.8679	0	248365	ON	13.9	225
8/8/2026	9:30:00	6.95	2.3911	0	248397	ON	13.8	226
8/8/2026	9:45:00	6.96	2.3795	0	248431	ON	13.9	225
8/8/2026	10:00:00	6.97	0.5193	0	248449	ON	14	227
8/8/2026	10:15:00	6.98	0.5038	0	248452	ON	14.3	227
8/8/2026	10:30:00	6.99	2.3718	0	248477	ON	14.3	227
8/8/2026	10:45:00	6.99	0.7208	0	248495	ON	14.4	228
8/8/2026	11:00:00	6.99	0.3333	0	248502	ON	14.6	229
8/8/2026	11:15:00	6.98	0.3449	0	248506	ON	14.8	231
8/8/2026	11:30:00	6.96	0.4108	0	248513	ON	15	231
8/8/2026	11:45:00	6.97	0.8022	0	248520	ON	15.3	230
8/8/2026	12:00:00	7.01	0.0271	0	248524	ON	15.8	0
8/8/2026	12:15:00	6.96	0.8216	7	248531	ON	15.4	232
8/8/2026	12:30:00	6.95	2.3485	0	248561	ON	15.1	233
8/8/2026	12:45:00	6.97	2.3214	0	248595	ON	15.2	233
8/8/2026	13:00:00	6.98	0.6084	0	248621	ON	15.3	233
8/8/2026	13:15:00	6.99	0.0155	0	248624	ON	16.1	0
8/8/2026	13:30:00	6.99	2.2787	0	248635	ON	15.8	233
8/8/2026	13:45:00	6.99	0.6317	0	248661	ON	15.7	234
8/8/2026	14:00:00	6.99	0.3062	0	248669	ON	15.9	234
8/8/2026	14:15:00	6.98	0.2364	0	248672	ON	16.2	235
8/8/2026	14:30:00	6.96	0.2209	0	248676	ON	16.4	236
8/8/2026	14:45:00	6.96	1.6897	0	248680	ON	16.5	237
8/8/2026	15:00:00	6.98	0.0271	0	248684	ON	16.5	237
8/8/2026	15:15:00	6.96	0.6666	2	248688	ON	17.2	232
8/8/2026	15:30:00	6.96	2.1702	0	248704	ON	15.9	239
8/8/2026	15:45:00	6.96	0.3449	0	248729	ON	15.9	239



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/8/2026	16:00:00	6.98	2.1780	0	248753	ON	15.9	240
8/8/2026	16:15:00	6.98	1.8990	0	248784	ON	15.9	241
8/8/2026	16:30:00	6.97	2.0578	0	248813	ON	15.9	240
8/8/2026	16:45:00	6.97	1.9958	0	248843	ON	15.8	239
8/8/2026	17:00:00	6.97	0.6588	0	248864	ON	15.8	241
8/8/2026	17:15:00	6.99	0.0310	0	248868	ON	16.4	238
8/8/2026	17:30:00	6.96	0.1899	0	248874	ON	16.3	241
8/8/2026	17:45:00	6.97	1.9183	0	248880	ON	16.1	241
8/8/2026	18:00:00	6.97	1.0502	0	248906	ON	15.8	243
8/8/2026	18:15:00	6.98	0.4069	0	248916	ON	15.8	241
8/8/2026	18:30:00	6.98	0.1279	0	248921	ON	16	242
8/8/2026	18:45:00	6.97	0.1201	0	248925	ON	16.1	244
8/8/2026	19:00:00	6.97	1.3021	0	248939	ON	15.9	244
8/8/2026	19:15:00	6.97	1.5928	0	248962	ON	15.5	241
8/8/2026	19:30:00	6.96	2.4221	0	248993	ON	15.1	239
8/8/2026	19:45:00	6.96	2.4221	0	249026	ON	14.8	236
8/8/2026	20:00:00	6.97	0.9068	0	249053	ON	14.8	237
8/8/2026	20:15:00	6.98	0.3953	0	249061	ON	14.8	237
8/8/2026	20:30:00	6.97	0.4147	0	249068	ON	14.8	236
8/8/2026	20:45:00	6.96	0.4844	0	249075	ON	14.8	237
8/8/2026	21:00:00	6.98	2.3718	0	249100	ON	14.5	233
8/8/2026	21:15:00	6.98	0.6201	0	249121	ON	14.4	232
8/8/2026	21:30:00	6.99	0.3914	0	249128	ON	14.4	234
8/8/2026	21:45:00	6.97	0.4302	0	249135	ON	14.5	233
8/8/2026	22:00:00	6.97	0.7983	0	249142	ON	14.5	234
8/8/2026	22:15:00	6.97	2.3679	0	249173	ON	14.1	226
8/8/2026	22:30:00	6.98	0.5038	0	249187	ON	14.1	227
8/8/2026	22:45:00	6.98	0.3643	0	249194	ON	14.1	228
8/8/2026	23:00:00	6.97	0.3992	0	249201	ON	14.2	228
8/8/2026	23:15:00	6.97	0.1783	0	249207	ON	14.2	228
8/8/2026	23:30:00	6.97	0.2752	0	249211	ON	14.2	230
8/8/2026	23:45:00	6.97	0.8177	0	249218	ON	14.2	228



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	0:00:00	6.96	0.7983	0	249228	ON	14	225
8/9/2026	0:15:00	6.99	0.7441	0	249244	ON	13.9	224
8/9/2026	0:30:00	7	2.4066	0	249274	ON	13.9	225
8/9/2026	0:45:00	6.99	2.4183	0	249308	ON	13.8	226
8/9/2026	1:00:00	6.99	1.2518	0	249342	ON	13.8	227
8/9/2026	1:15:00	7	0.5891	0	249354	ON	13.9	227
8/9/2026	1:30:00	6.99	2.3950	0	249368	ON	13.8	228
8/9/2026	1:45:00	6.96	2.3718	0	249402	ON	13.7	228
8/9/2026	2:00:00	6.96	0.0233	0	249419	ON	13.7	228
8/9/2026	2:15:00	6.97	0.2829	0	249419	ON	13.9	228
8/9/2026	2:30:00	6.95	2.1354	0	249446	ON	13.6	228
8/9/2026	2:45:00	6.96	0.6511	0	249470	ON	13.6	228
8/9/2026	3:00:00	6.98	0.0233	0	249474	ON	13.6	229
8/9/2026	3:15:00	6.98	0.0194	0	249474	ON	13.7	229
8/9/2026	3:30:00	6.97	0.3682	4	249480	ON	13.7	229
8/9/2026	3:45:00	6.99	0.4108	0	249485	ON	13.6	228
8/9/2026	4:00:00	7.01	0.0233	0	249493	ON	13.6	225
8/9/2026	4:15:00	7.01	1.0735	0	249499	ON	13.6	229
8/9/2026	4:30:00	7	2.3911	0	249532	ON	13.5	230
8/9/2026	4:45:00	7	1.0502	0	249561	ON	13.5	230
8/9/2026	5:00:00	7.03	0.0233	0	249566	ON	13.9	228
8/9/2026	5:15:00	7	1.8718	0	249585	ON	13.6	230
8/9/2026	5:30:00	7	0.5503	0	249611	ON	13.5	230
8/9/2026	5:45:00	7.01	0.4030	0	249619	ON	13.6	230
8/9/2026	6:00:00	7	0.4069	0	249626	ON	13.6	232
8/9/2026	6:15:00	6.99	0.4806	0	249633	ON	13.5	231
8/9/2026	6:30:00	7.01	2.4105	0	249655	ON	13.5	231
8/9/2026	6:45:00	7.01	2.4183	0	249689	ON	13.5	232
8/9/2026	7:00:00	7.01	0.8603	0	249703	ON	13.6	230
8/9/2026	7:15:00	7	2.0423	0	249714	ON	13.6	231
8/9/2026	7:30:00	7.01	0.6356	0	249733	ON	13.6	232
8/9/2026	7:45:00	7	1.8679	0	249740	ON	13.7	232



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	8:00:00	7.07	0.1201	0	249743	ON	14.4	226
8/9/2026	8:15:00	6.99	1.9300	0	249751	ON	14	227
8/9/2026	8:30:00	7	1.9145	0	249778	ON	13.8	227
8/9/2026	8:45:00	7.02	1.2750	0	249812	ON	13.9	229
8/9/2026	9:00:00	7.02	0.6394	0	249824	ON	13.9	228
8/9/2026	9:15:00	7.03	1.9028	0	249838	ON	14.1	230
8/9/2026	9:30:00	7.02	0.4379	0	249859	ON	14.1	226
8/9/2026	9:45:00	7.02	0.2790	0	249860	ON	14.4	226
8/9/2026	10:00:00	7.01	0.4922	0	249868	ON	14.3	226
8/9/2026	10:15:00	7.01	0.5542	0	249875	ON	14.7	227
8/9/2026	10:30:00	7	2.4454	0	249902	ON	14.4	231
8/9/2026	10:45:00	7	2.4376	0	249939	ON	14.4	232
8/9/2026	11:00:00	7	1.9028	0	249970	ON	14.5	231
8/9/2026	11:15:00	7	0.6976	0	249994	ON	14.6	232
8/9/2026	11:30:00	7.01	0.4999	0	250001	ON	14.8	233
8/9/2026	11:45:00	6.99	0.8642	0	250015	ON	14.9	234
8/9/2026	12:00:00	6.97	0.9030	0	250029	ON	15	235
8/9/2026	12:15:00	6.96	2.4105	0	250057	ON	14.8	233
8/9/2026	12:30:00	6.98	0.5077	0	250069	ON	15	233
8/9/2026	12:45:00	6.99	0.0271	0	250073	ON	15.5	234
8/9/2026	13:00:00	6.97	1.8912	0	250080	ON	15.4	234
8/9/2026	13:15:00	6.99	0.6588	0	250092	ON	15.3	232
8/9/2026	13:30:00	6.98	2.3718	0	250106	ON	15.3	234
8/9/2026	13:45:00	6.97	2.4066	0	250140	ON	15.1	232
8/9/2026	14:00:00	6.97	1.8873	0	250168	ON	15	232
8/9/2026	14:15:00	6.98	0.4263	0	250187	ON	15.2	232
8/9/2026	14:30:00	6.99	0.4612	0	250189	ON	15.9	231
8/9/2026	14:45:00	6.97	2.3679	0	250213	ON	15.2	228
8/9/2026	15:00:00	6.97	0.6201	0	250232	ON	15	232
8/9/2026	15:15:00	6.98	0.0349	0	250234	ON	15.7	229
8/9/2026	15:30:00	6.96	1.8873	0	250245	ON	15.2	230
8/9/2026	15:45:00	6.96	2.3873	0	250275	ON	14.8	231



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/9/2026	16:00:00	6.96	0.7053	0	250293	ON	14.7	232
8/9/2026	16:15:00	6.97	0.6627	0	250302	ON	14.8	232
8/9/2026	16:30:00	6.97	2.3756	0	250332	ON	14.6	234
8/9/2026	16:45:00	6.99	1.8679	0	250363	ON	14.6	238
8/9/2026	17:00:00	7	0.6084	0	250381	ON	14.6	237
8/9/2026	17:15:00	7.01	0.4728	0	250388	ON	14.7	238
8/9/2026	17:30:00	7	2.3640	0	250400	ON	14.7	239
8/9/2026	17:45:00	7.02	0.8371	0	250428	ON	14.6	241
8/9/2026	18:00:00	7.02	0.2131	0	250436	ON	14.7	240
8/9/2026	18:15:00	7.02	0.3604	0	250443	ON	14.8	240
8/9/2026	18:30:00	7.01	0.4224	0	250450	ON	14.9	241
8/9/2026	18:45:00	7.01	2.3873	0	250462	ON	14.8	241
8/9/2026	19:00:00	7.02	2.3640	0	250496	ON	14.6	236
8/9/2026	19:15:00	7.01	1.8602	0	250526	ON	14.5	234
8/9/2026	19:30:00	7	1.1549	0	250553	ON	14.4	234
8/9/2026	19:45:00	7.01	0.4457	0	250564	ON	14.5	234
8/9/2026	20:00:00	7	0.3604	0	250570	ON	14.5	234
8/9/2026	20:15:00	7.02	0.0233	0	250573	ON	15.4	0
8/9/2026	20:30:00	6.99	0.0310	0	250573	ON	16.6	0
8/9/2026	20:45:00	6.97	0.0388	0	250574	ON	17.4	237
8/9/2026	21:00:00	6.96	0.1938	0	250577	ON	17.8	236
8/9/2026	21:15:00	6.96	0.7828	4	250585	ON	14.6	232
8/9/2026	21:30:00	6.93	0.2868	0	250592	ON	14.2	231
8/9/2026	21:45:00	6.91	1.8602	0	250619	ON	13.9	229
8/9/2026	22:00:00	6.91	2.3562	0	250649	ON	13.9	230
8/9/2026	22:15:00	6.95	0.6162	0	250662	ON	13.9	231
8/9/2026	22:30:00	6.95	2.3446	0	250676	ON	14	232
8/9/2026	22:45:00	6.95	1.8098	0	250705	ON	13.9	235
8/9/2026	23:00:00	6.95	1.7982	0	250733	ON	14	234
8/9/2026	23:15:00	6.97	0.4844	0	250746	ON	14	236
8/9/2026	23:30:00	6.96	0.4573	0	250753	ON	14.1	237
8/9/2026	23:45:00	6.97	2.2904	0	250780	ON	14	237


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

Appendix C: Photos


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	



		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

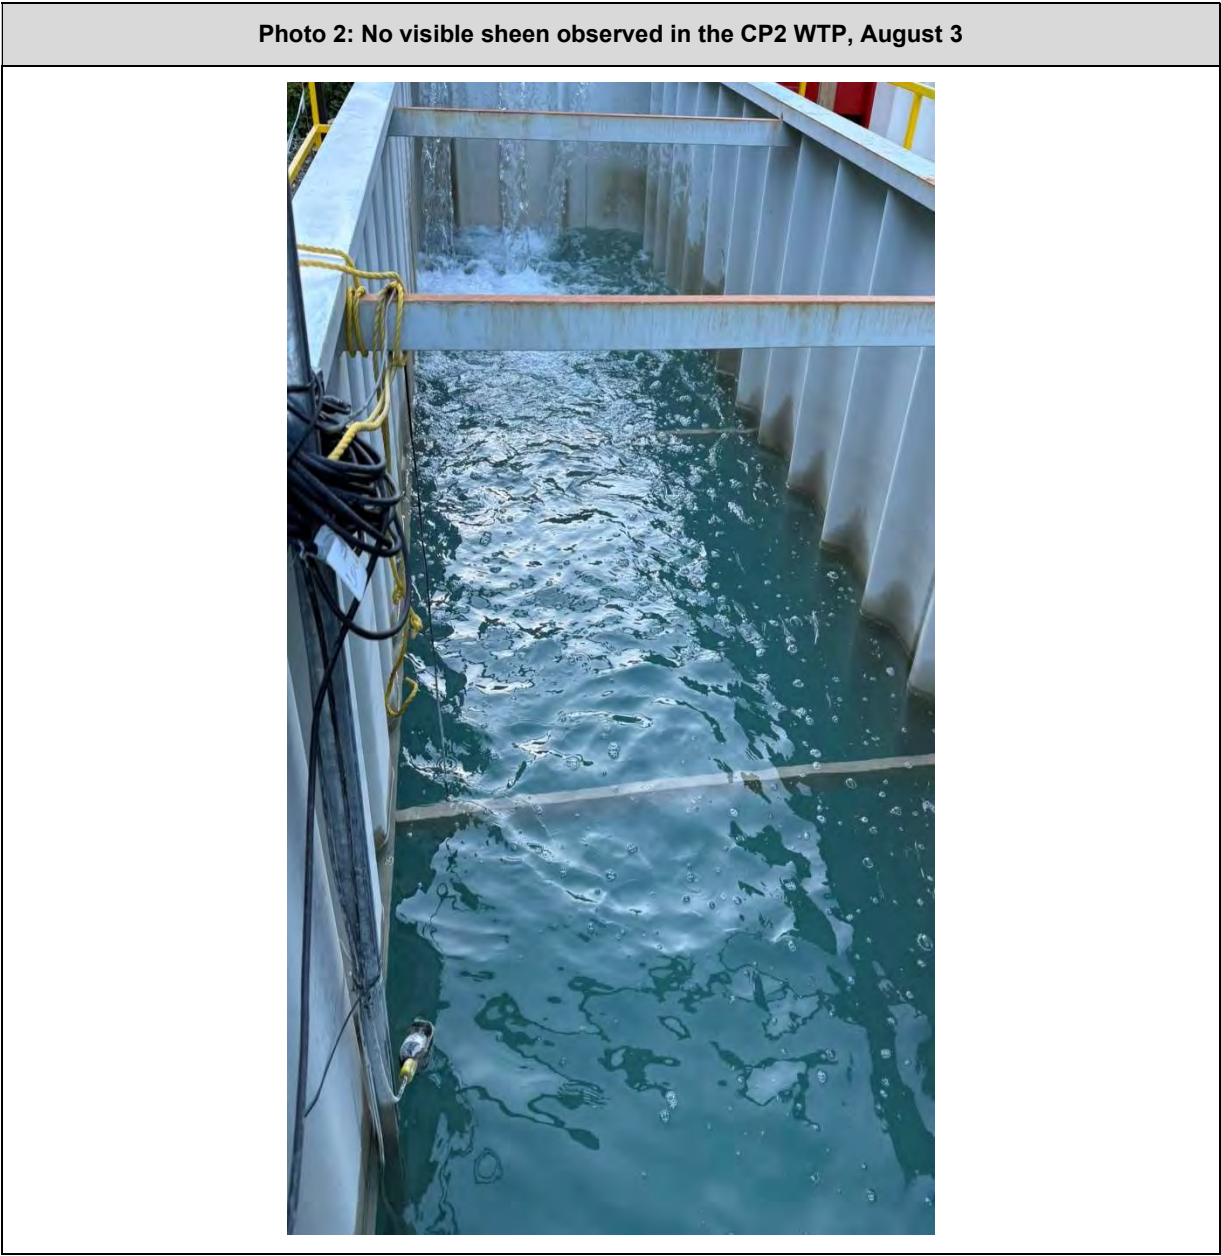

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

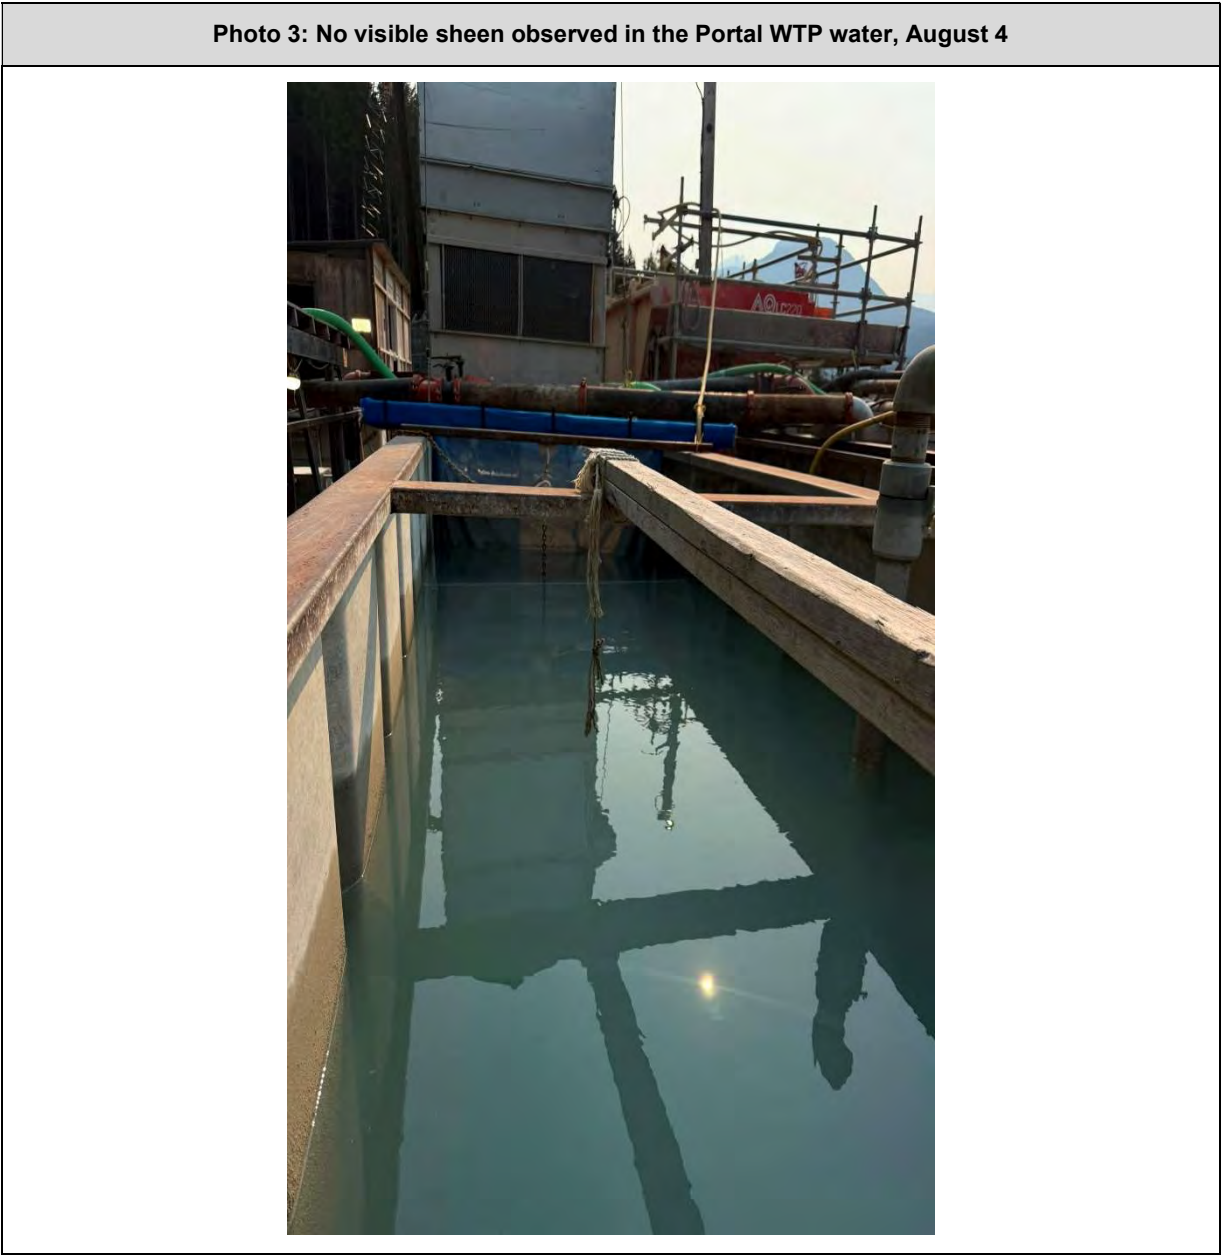





Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Photo 4: No visible sheen observed in the CP2 WTP water, August 4

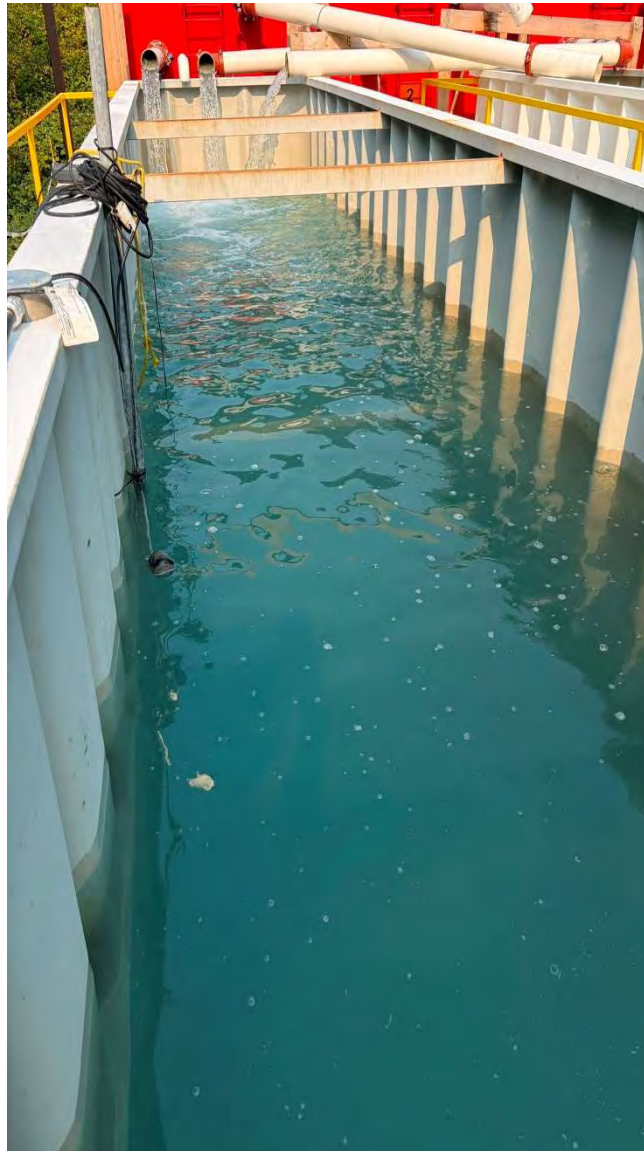

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

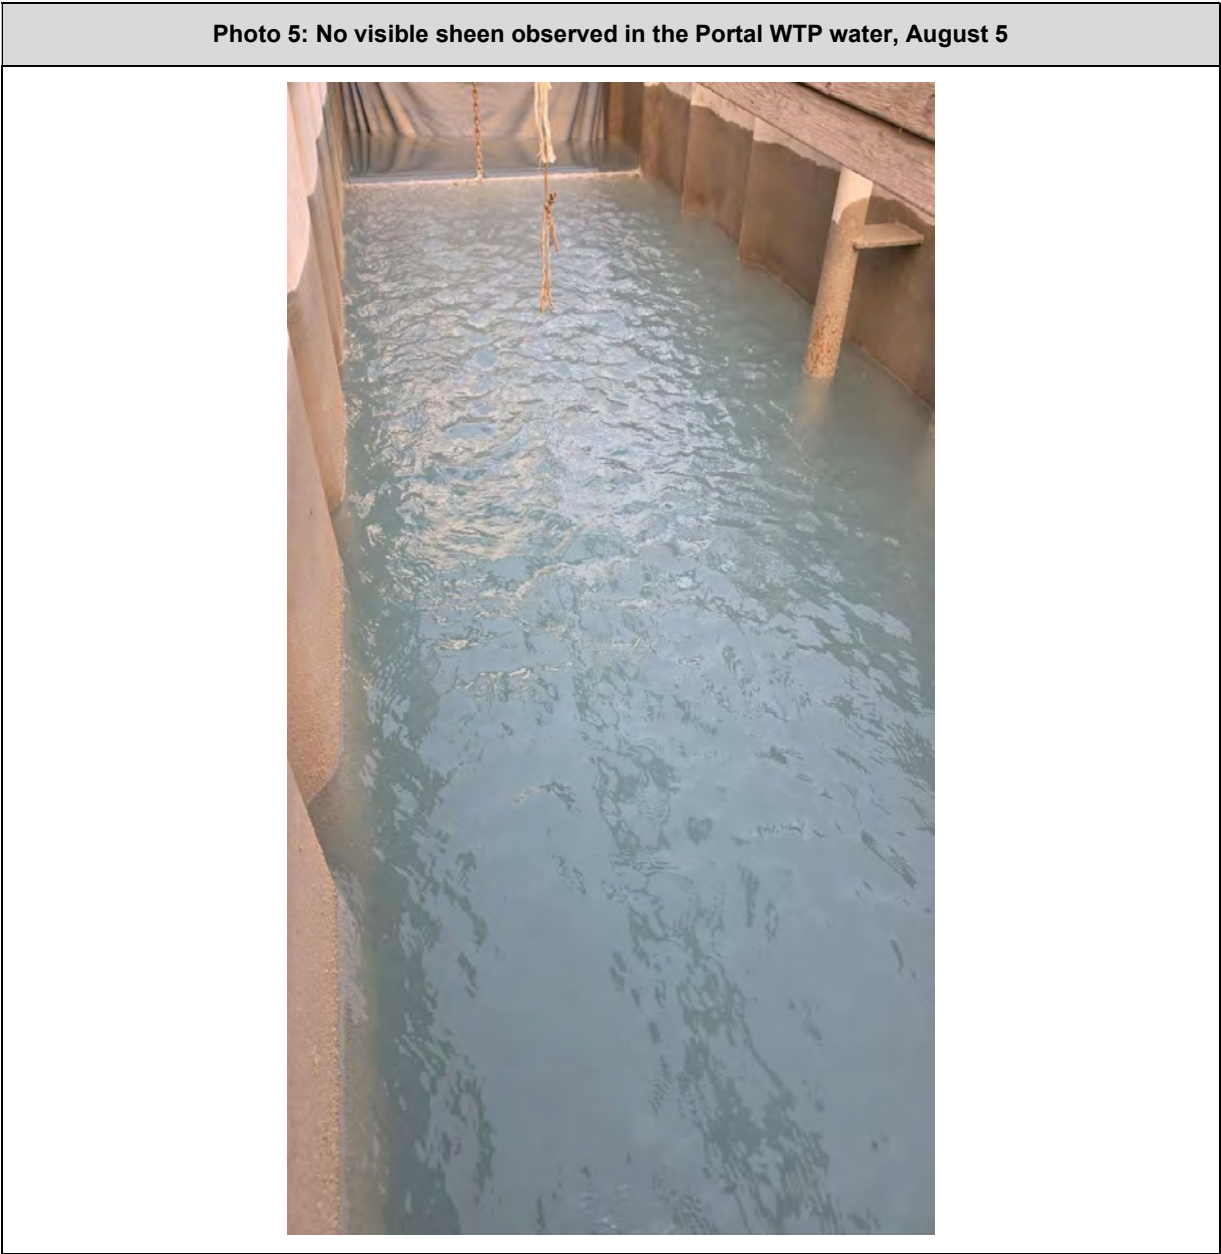





Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

Photo 6: No visible sheen observed in the CP2 WTP water, August 5

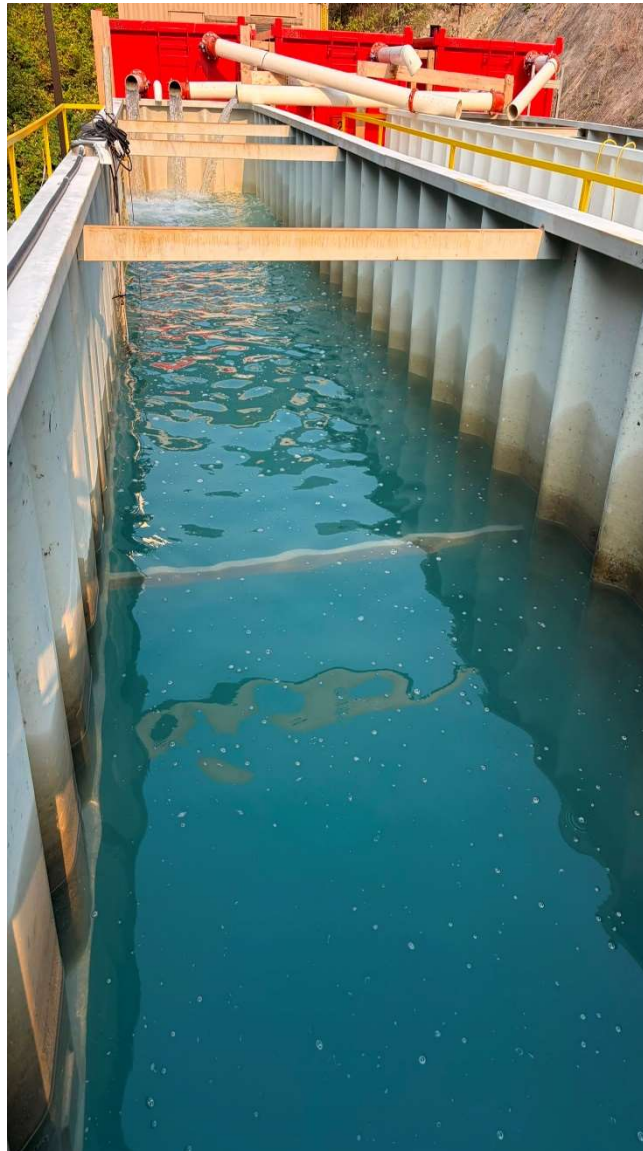

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

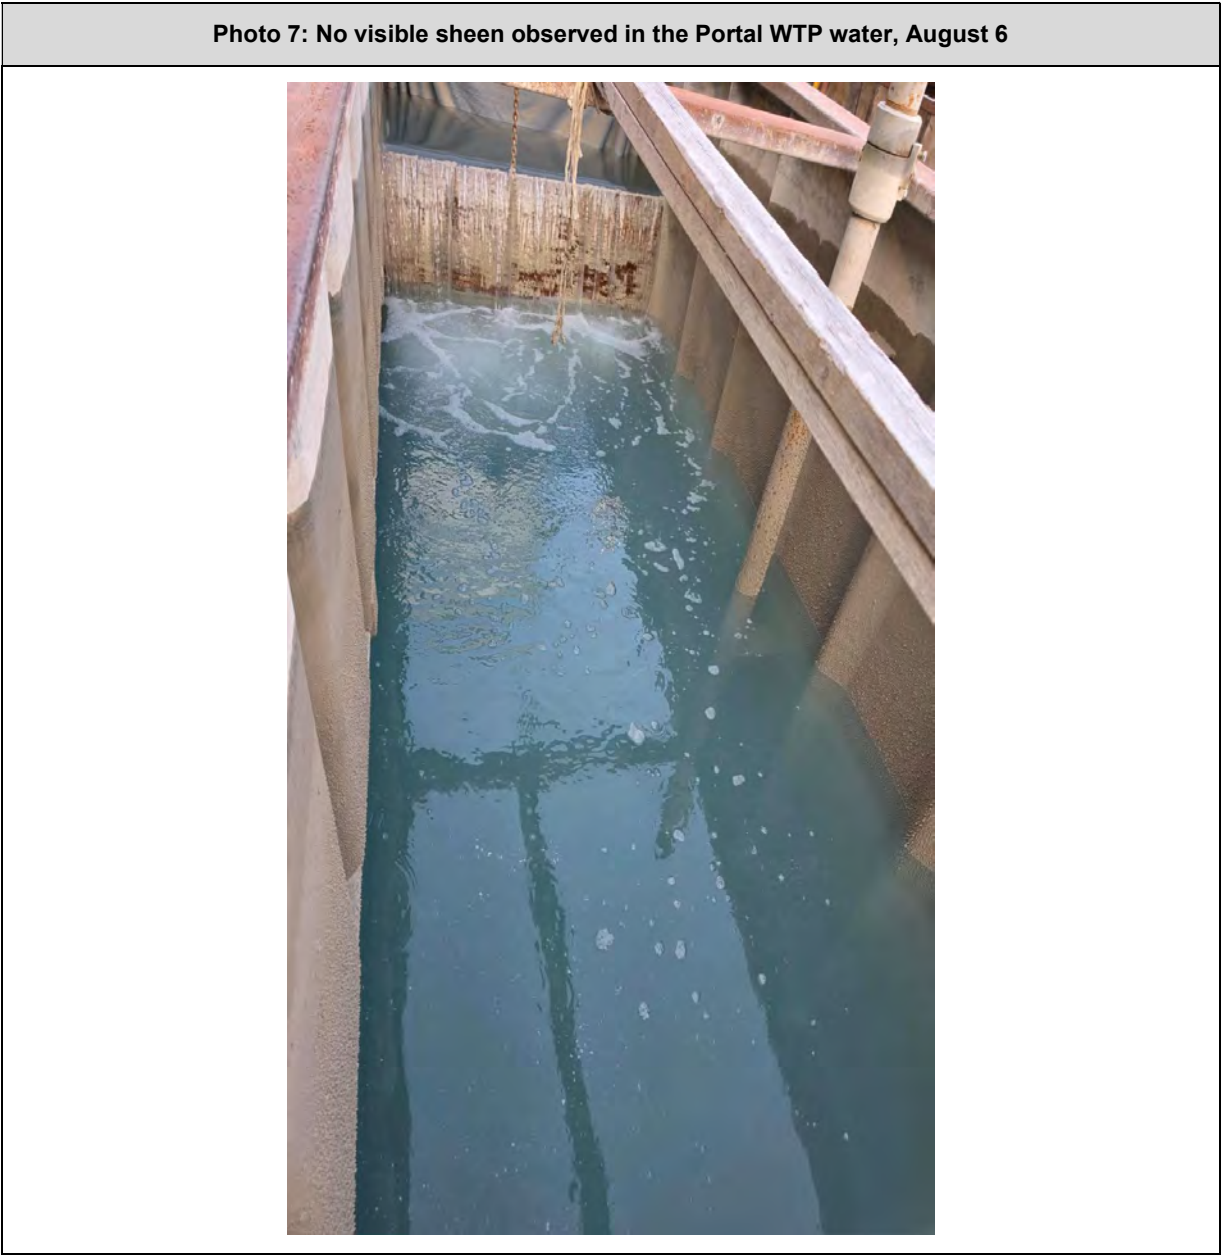




Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026


Photo 8: No visible sheen observed in the CP2 WTP water, August 6




		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: BC1 Approved by: BC2 Date: August 12, 2026	

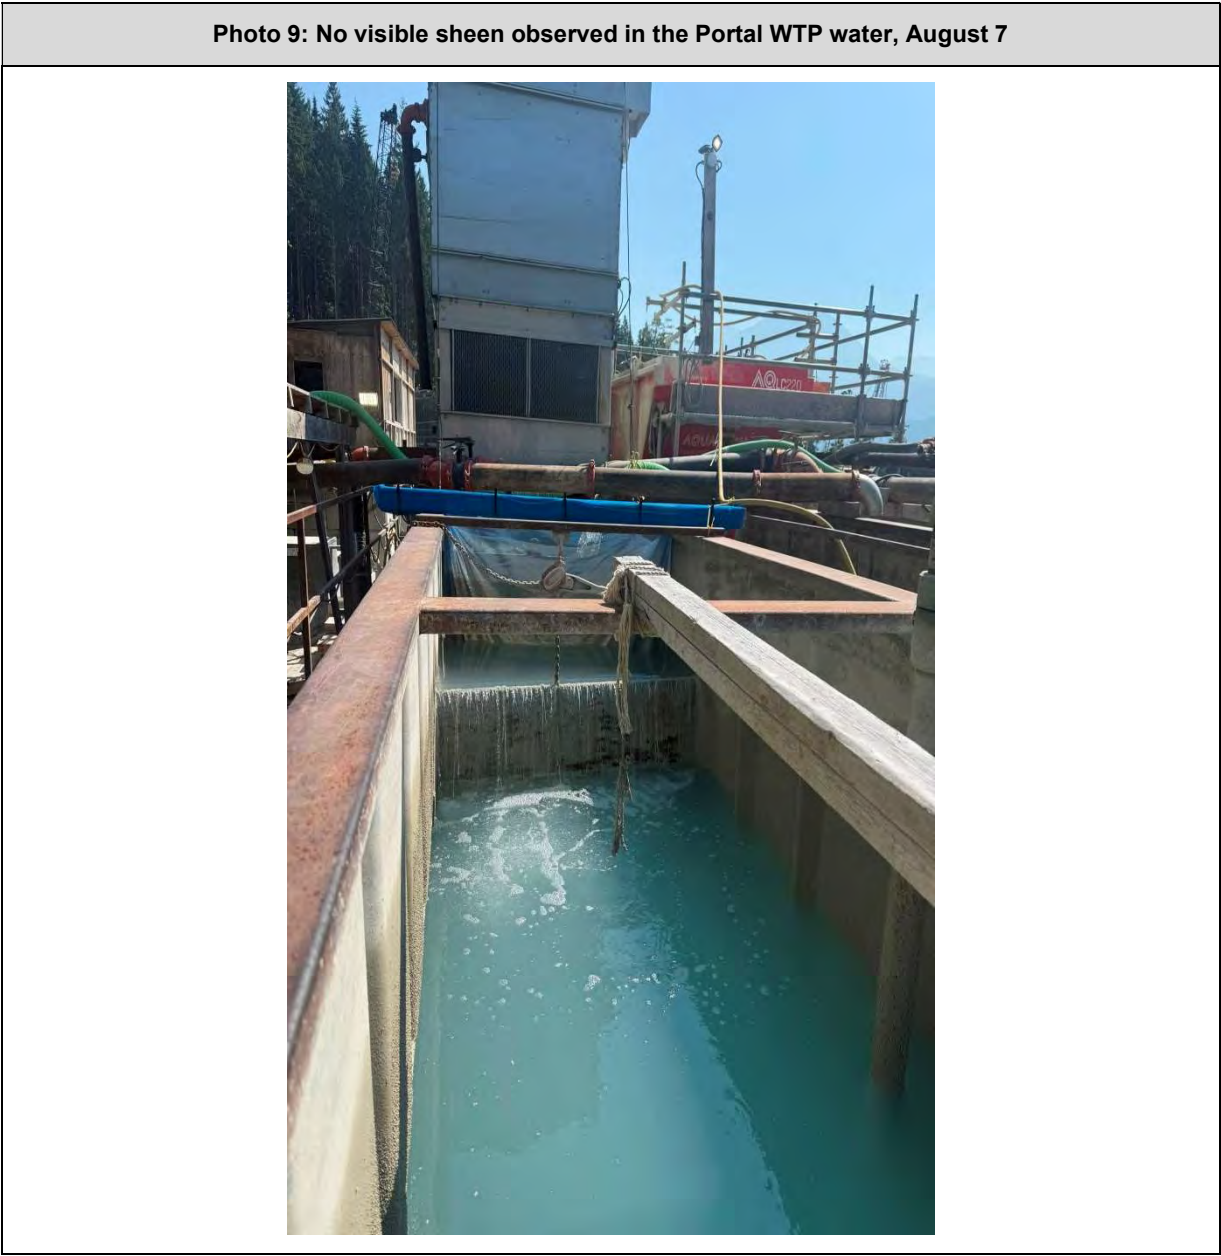

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

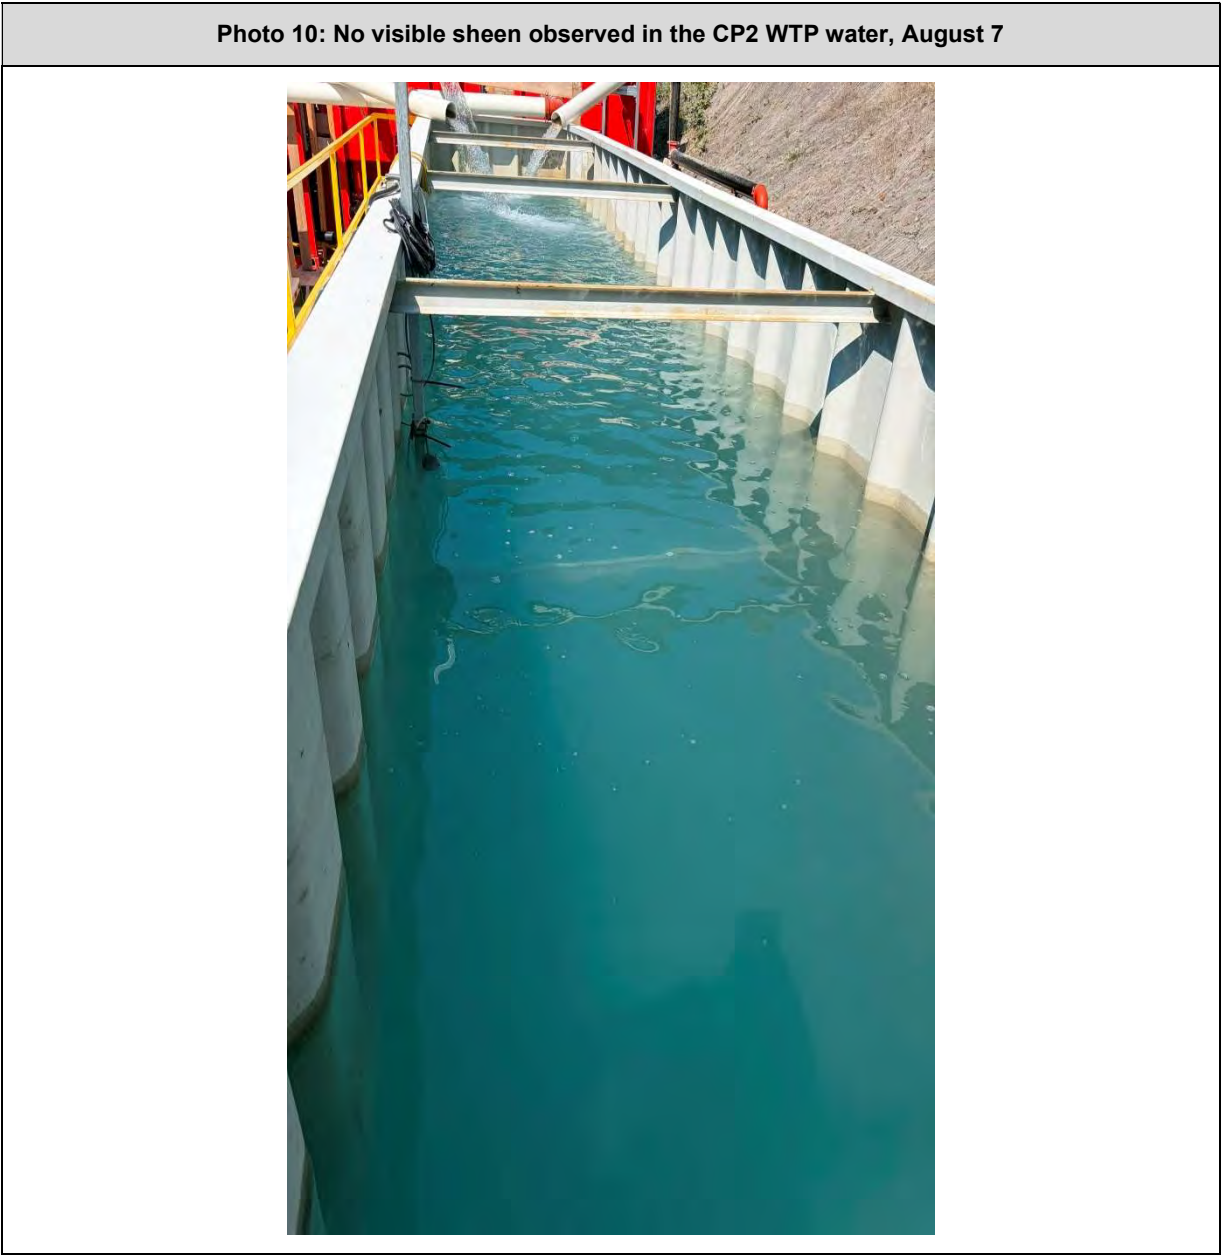

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

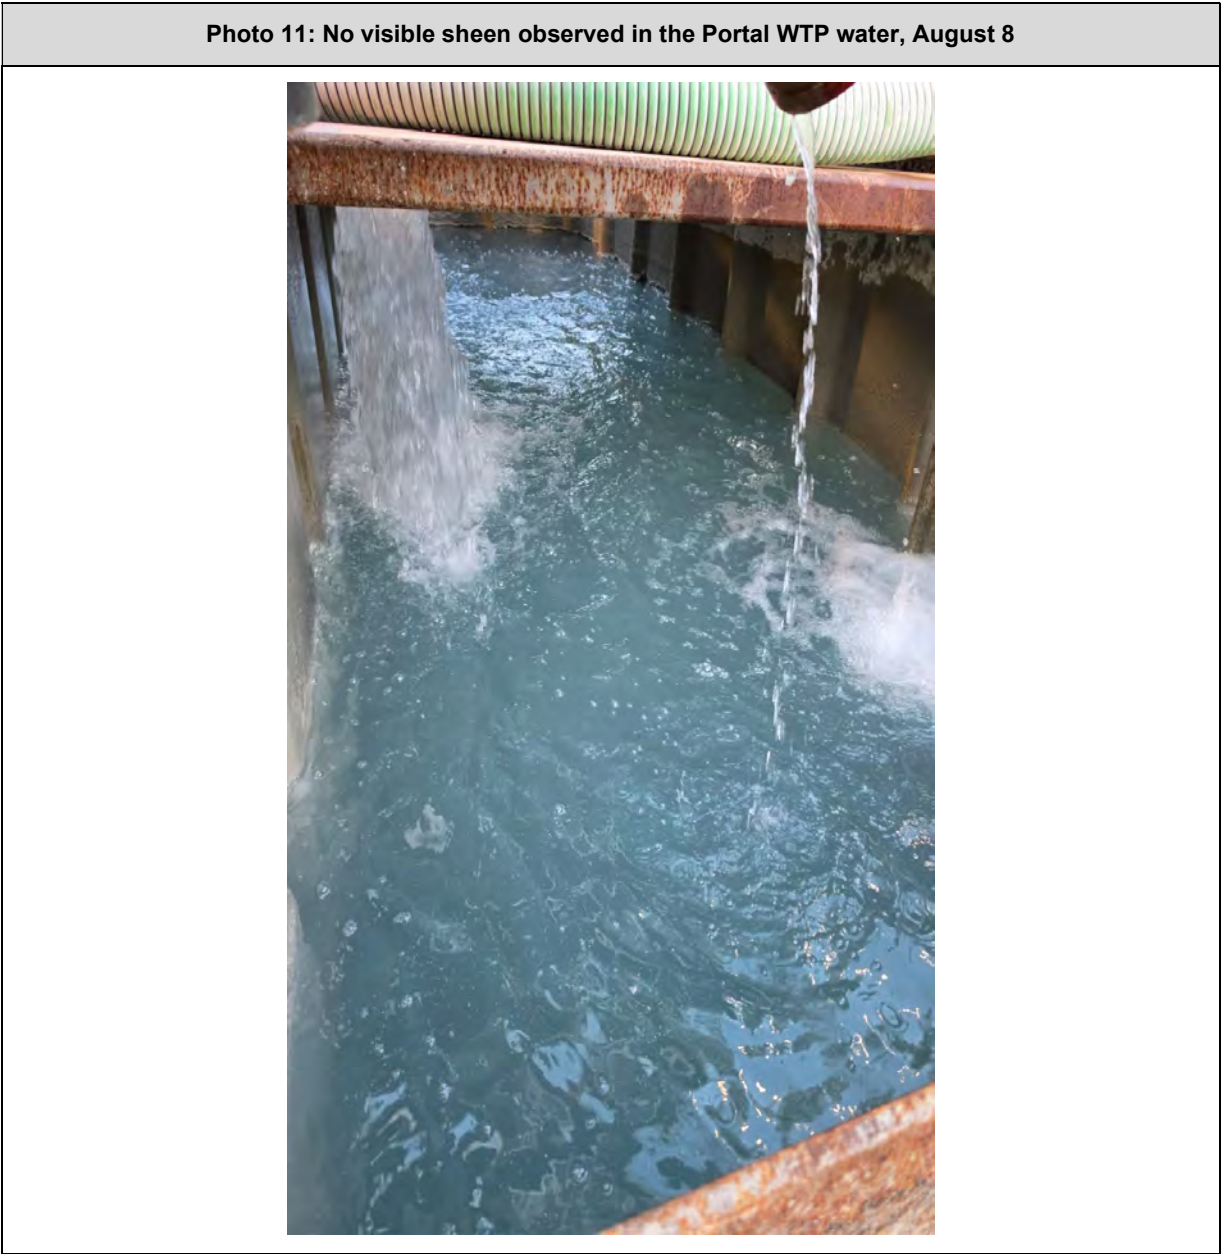




Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026


Photo 12: No visible sheen observed in the CP2 WTP water, August 8



		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

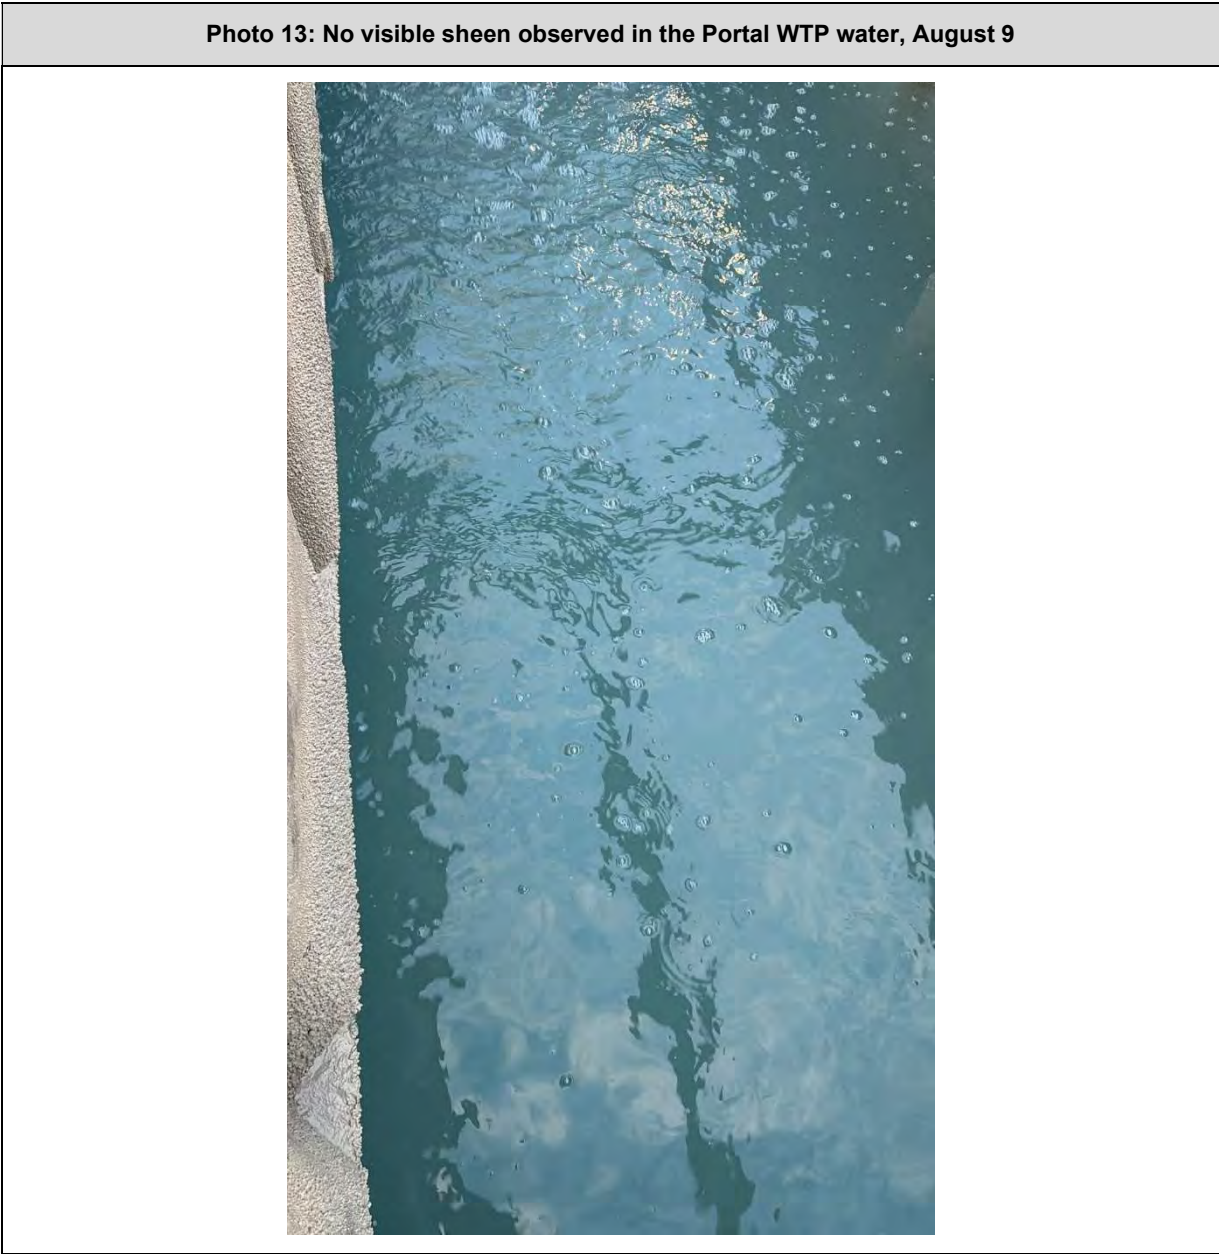

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 3, 2026 to August 9, 2026	Prepared by: Approved by: Date:	BC1 BC2 August 12, 2026

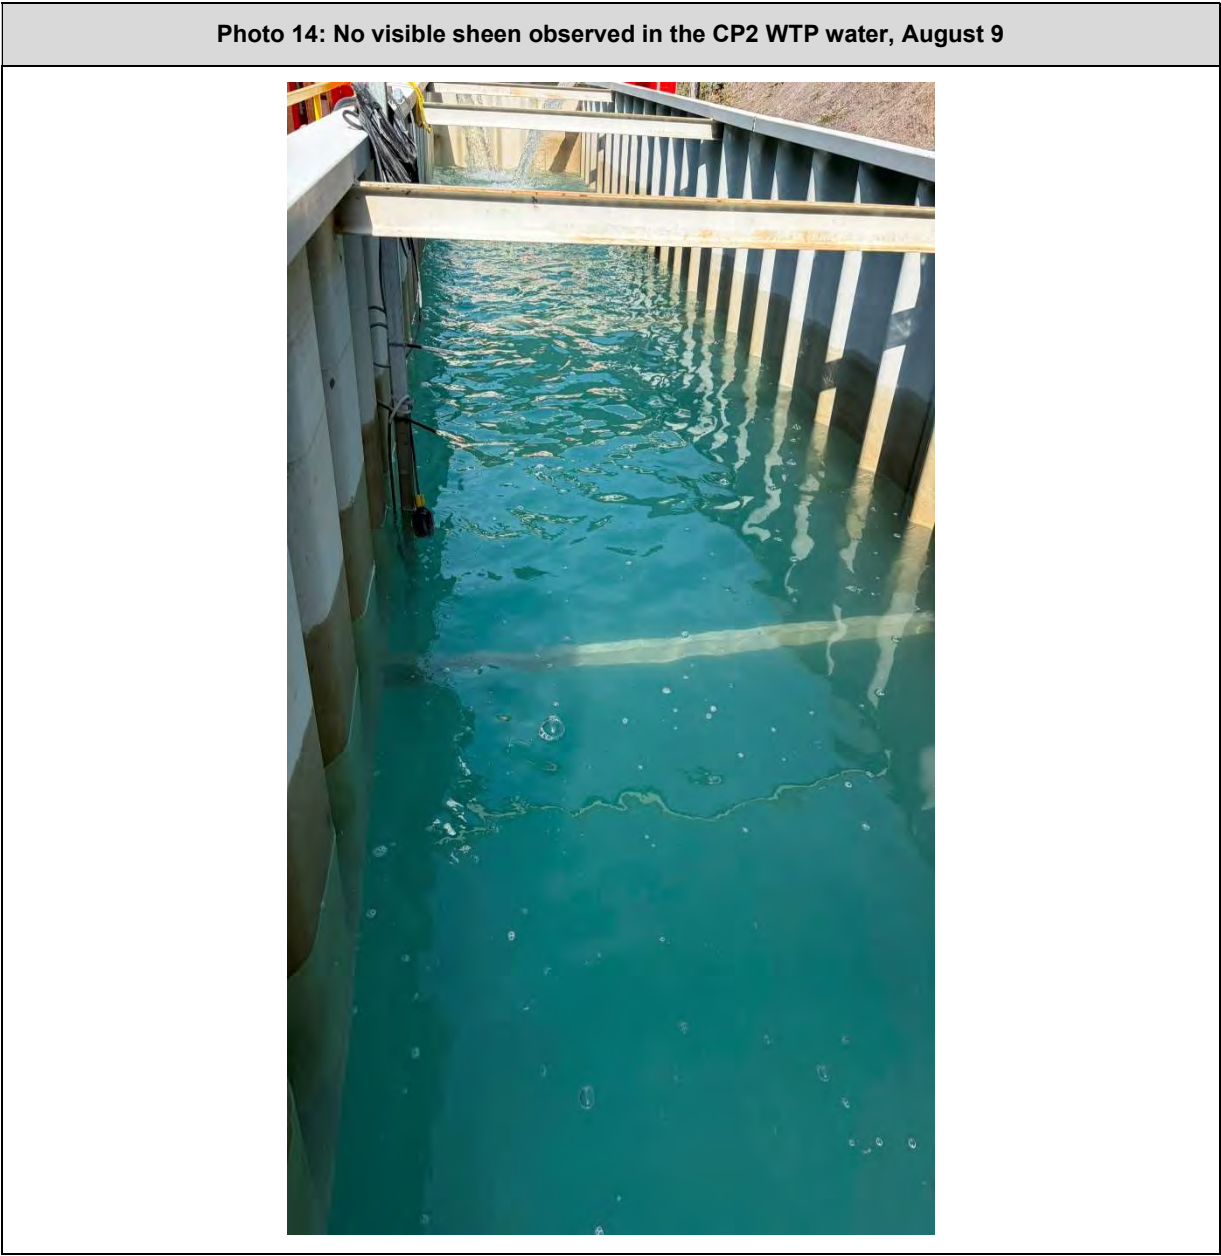

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix D	D-1

Appendix D:
Woodfibre Site Receiving Environment
Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix D	D-2

Woodfibre Site Receiving Environment
Sample Analysis



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-05 10:27:00	WLNG DS 2026-08-05 09:54:00
In situ Parameters									
Field pH	pH Units		6.5 - 9			7 - 8.7		6.92	7.48
Field Temperature	°C	18	19					14.9	13.5
General Parameters									
pH	pH Units							6.55	7.22
Alkalinity (Total as CaCO ₃)	mg/L							8.2	43
Alkalinity (PP as CaCO ₃)	mg/L							<1	<1
Hardness (CaCO ₃)-Total	mg/L							7.6	52.6
Hardness (CaCO ₃)-Dissolved	mg/L							8.83	60.7
Sulphide-Total	mg/L							<0.0018	<0.0018
Sulphide (as H ₂ S)	mg/L			0.002				<0.002	<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L							<0.0019	<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L							<0.0018	<0.0018
Anions and Nutrients									
Ammonia (N)-Total	mg/L	1.77	12.4		20	131		<0.015	<0.015
Bicarbonate (HCO ₃)	mg/L							9.9	53
Carbonate (CO ₃)	mg/L							<1	<1
Hydroxide (OH)	mg/L							<1	<1
Nitrate (N)	mg/L	3	32.8		3.7			0.039	0.021
Nitrite (N)	mg/L	0.02	0.06					<0.005	<0.005
Nitrate plus Nitrite (N)	mg/L							0.039	0.021
Nitrogen (N)-Total	mg/L							0.131	0.177
Phosphorus (P)-Total (4500-P)	mg/L							0.022	0.0025
Bromide (Br)	mg/L							<0.01	<0.01
Chloride (Cl)	mg/L	150	600					<1	18
Fluoride (F)	mg/L		0.4			1.5		<0.05	0.27
Sulphate (SO ₄)-Dissolved	mg/L	128						2	14
Total Metals									
Aluminum (Al)-Total	mg/L	0.0489054						0.0557	0.0757
Antimony (Sb)-Total	mg/L	0.074	0.25					0.000024	0.000339
Arsenic (As)-Total	mg/L	0.005			0.0125			0.000133	0.000895
Barium (Ba)-Total	mg/L			1				0.00396	0.0042
Beryllium (Be)-Total	mg/L			0.00013			0.1	<0.00001	<0.00001
Bismuth (Bi)-Total	mg/L							<0.00001	<0.00001
Boron (B)-Total	mg/L	1.2			1.2			<0.01	<0.01
Cadmium (Cd)-Total	mg/L						0.00012	0.0000062	0.0000059
Calcium (Ca)-Total	mg/L							2.57	19.2
Cesium (Cs)-Total	mg/L							<0.00005	<0.00005
Chromium (Cr)-Total	mg/L							0.00022	<0.0001

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-05 10:27:00	WLNG DS 2026-08-05 09:54:00
Total Metals (cont'd.)									
Chromium (Cr III)-Total	mg/L			0.0089			0.056	<0.00099	<0.00099
Chromium (Cr VI)-Total	mg/L			0.0025			0.0015	<0.00099	<0.00099
Cobalt (Co)-Total	mg/L							0.000032	0.000035
Copper (Cu)-Total	mg/L				0.002	0.003		0.00081	0.00011
Iron (Fe)-Total	mg/L	0.055	1					0.0613	0.0176
Lead (Pb)-Total	mg/L				0.002	0.14		0.000035	<0.00002
Lithium (Li)-Total	mg/L							<0.0005	0.00728
Magnesium (Mg)-Total	mg/L							0.29	1.12
Manganese (Mn)-Total	mg/L						0.1	0.00213	0.0174
Mercury (Hg)-Total	mg/L	0.00002			0.0001			<0.0000019	<0.0000019
Molybdenum (Mo)-Total	mg/L	7.6	46					0.000447	0.0405
Nickel (Ni)-Total	mg/L						0.0083	0.00034	0.00019
Phosphorus (P)-Total (ICPMS)	mg/L							0.0191	0.0051
Potassium (K)-Total	mg/L							<0.25	1.76
Rubidium (Rb)-Total	mg/L							0.000341	0.00369
Selenium (Se)-Total	mg/L	0.002			0.002			<0.00004	<0.00004
Silicon (Si)-Total	mg/L							4.1	5.96
Silver (Ag)-Total	mg/L	0.00012			0.0005	0.0037	0.0005	<0.00001	<0.00001
Sodium (Na)-Total	mg/L							1.48	6.74
Strontium (Sr)-Total	mg/L							0.0132	0.0443
Sulphur (S)-Total	mg/L							<3	4.3
Tellurium (Te)-Total	mg/L							<0.00002	<0.00002
Thallium (Tl)-Total	mg/L			0.00003				<0.000002	0.0000078
Thorium (Th)-Total	mg/L							<0.00005	<0.00005
Tin (Sn)-Total	mg/L							<0.0002	<0.0002
Titanium (Ti)-Total	mg/L							<0.002	<0.002
Uranium (U)-Total	mg/L		0.0165	0.0075				0.000054	0.000217
Vanadium (V)-Total	mg/L			0.06			0.005	<0.0002	<0.0002
Zinc (Zn)-Total	mg/L				0.01	0.055		0.0023	0.0026
Zirconium (Zr)-Total	mg/L							<0.0001	<0.0001
Dissolved Metals									
Aluminum (Al)-Dissolved	mg/L							0.0338	0.0401
Antimony (Sb)-Dissolved	mg/L							<0.00002	0.000349
Arsenic (As)-Dissolved	mg/L							0.000115	0.000896
Barium (Ba)-Dissolved	mg/L							0.00391	0.00429
Beryllium (Be)-Dissolved	mg/L							<0.00001	<0.00001
Bismuth (Bi)-Dissolved	mg/L							<0.000005	<0.000005
Boron (B)-Dissolved	mg/L							<0.01	<0.01

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-05 10:27:00	WLNG DS 2026-08-05 09:54:00
Dissolved Metals (cont'd.)									
Cadmium (Cd)-Dissolved	mg/L	0.0000317	0.0000414					0.0000057	<0.000005
Calcium (Ca)-Dissolved	mg/L							2.99	22.2
Cesium (Cs)-Dissolved	mg/L							<0.00005	<0.00005
Chromium (Cr)-Dissolved	mg/L							<0.0001	<0.0001
Cobalt (Co)-Dissolved	mg/L	0.0003889						0.0000211	0.0000334
Copper (Cu)-Dissolved	mg/L	0.0002	0.00108					0.000717	0.000087
Iron (Fe)-Dissolved	mg/L							0.0323	0.0028
Lead (Pb)-Dissolved	mg/L	0.0013996						0.0000149	<0.000005
Lithium (Li)-Dissolved	mg/L							<0.0005	0.00751
Manganese (Mn)-Dissolved	mg/L	0.115	0.4407697					0.0013	0.0175
Magnesium (Mg)-Dissolved	mg/L							0.333	1.25
Mercury (Hg)-Dissolved	mg/L							<0.0000019	<0.0000019
Molybdenum (Mo)-Dissolved	mg/L							0.00052	0.044
Nickel (Ni)-Dissolved	mg/L	0.0007	0.0117					0.000232	0.000119
Phosphorus (P)-Dissolved	mg/L							0.0162	0.0042
Potassium (K)-Dissolved	mg/L							0.188	1.82
Rubidium (Rb)-Dissolved	mg/L							0.000379	0.00375
Selenium (Se)-Dissolved	mg/L							<0.00004	<0.00004
Silicon (Si)-Dissolved	mg/L							4.55	6.67
Silver (Ag)-Dissolved	mg/L							<0.000005	<0.000005
Sodium (Na)-Dissolved	mg/L							1.76	7.28
Strontium (Sr)-Dissolved	mg/L			1.25				0.0148	0.0474
Sulphur (S)-Dissolved	mg/L							<3	4.9
Tellurium (Te)-Dissolved	mg/L							<0.00002	<0.00002
Thallium (Tl)-Dissolved	mg/L							0.0000024	0.0000079
Thorium (Th)-Dissolved	mg/L							0.000013	<0.000005
Tin (Sn)-Dissolved	mg/L							<0.0002	<0.0002
Titanium (Ti)-Dissolved	mg/L							<0.0005	<0.0005
Uranium (U)-Dissolved	mg/L							0.0000575	0.000211
Vanadium (V)-Dissolved	mg/L							0.00021	<0.0002
Zinc (Zn)-Dissolved	mg/L	0.0040213	0.0087868					0.0006	0.00206
Zirconium (Zr)-Dissolved	mg/L							<0.0001	<0.0001

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-05 10:27:00	WLNG DS 2026-08-05 09:54:00
Inorganics									
Organic Carbon (C)-Total	mg/L							2.4	0.99
Organic Carbon (C)-Dissolved	mg/L							1.9	0.61
Solids-Total Dissolved	mg/L							48	96
Solids-Total Suspended	mg/L	6.6	26.6					1.6	<1

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix D	D-3

Woodfibre Site Receiving Environment
Field Notes and Logs

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	WLNG (EAS) DS	Date:	August 5, 2026
Site Name:	East Creek	Time:	9:54
Site UTM:	Zone: 10U E: 482092	Crew:	AH
(NAD83)	N: 5501875	Weather:	Smoky/hazy, no clouds, no precip 24hrs+

In Situ Parameters

pH:	7.48	DO:	10.46 (mg/L)
Temp:	13.5 (°C)	Cond:	205.5 (us/cm)
Turbidity:	1.57 NTU	Salinity:	0.10 (ppt)
Visible Sheen:	No	ORP:	55.8 (mV)

Water Surface Condition: Clear

Photo Record



Observations

No notable observations

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	WLNG (EAS) US	Date:	August 5, 2026
Site Name:	East Creek	Time:	10:27
Site UTM:	Zone: 10U E: 481908	Crew:	AH
(NAD83)	N: 5501909	Weather:	Smoky/hazy, no clouds, no precip 24hrs+

In Situ Parameters

pH:	6.92	DO:	6.41 (mg/L)
Temp:	14.9 (°C)	Cond:	48.5 (us/cm)
Turbidity:	2.53 NTU	Salinity:	0.03 (ppt)
Visible Sheen:		ORP:	58.6 (mV)

Water Surface Condition:

Photo Record



Observations

No notable observations

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-03 00:00:00	14.02	252.15	0.23	7.82	9.67	0.00	0.14
EAS-DS	2026-08-03 00:15:00	13.86	235.45	0.23	7.73	9.44	0.00	0.13
EAS-DS	2026-08-03 00:30:00	13.78	242.61	0.24	7.80	9.76	0.00	0.13
EAS-DS	2026-08-03 00:45:00	13.79	243.65	0.01	7.73	9.74	0.00	0.13
EAS-DS	2026-08-03 01:00:00	13.63	227.90	0.22	7.70	9.41	0.00	0.12
EAS-DS	2026-08-03 01:15:00	14.00	256.57	0.23	7.77	9.60	0.00	0.14
EAS-DS	2026-08-03 01:30:00	13.99	251.54	0.23	7.69	9.26	0.00	0.14
EAS-DS	2026-08-03 01:45:00	13.49	228.63	0.02	7.68	9.50	0.00	0.12
EAS-DS	2026-08-03 02:00:00	13.89	253.01	0.22	7.78	9.57	0.00	0.14
EAS-DS	2026-08-03 02:15:00	13.86	250.77	0.24	7.74	9.45	0.00	0.13
EAS-DS	2026-08-03 02:30:00	13.80	238.23	0.24	7.75	9.47	0.00	0.13
EAS-DS	2026-08-03 02:45:00	13.46	234.80	0.00	7.72	9.86	0.00	0.13
EAS-DS	2026-08-03 03:00:00	13.30	223.11	0.22	7.72	9.82	0.00	0.12
EAS-DS	2026-08-03 03:15:00	13.38	232.80	0.24	7.76	9.91	0.47	0.13
EAS-DS	2026-08-03 03:30:00	13.42	234.59	0.24	7.77	9.86	0.00	0.13
EAS-DS	2026-08-03 03:45:00	13.32	223.15	0.02	7.65	9.63	0.00	0.12
EAS-DS	2026-08-03 04:00:00	13.47	239.66	0.23	7.80	9.85	0.00	0.13
EAS-DS	2026-08-03 04:15:00	13.29	228.24	0.24	7.76	9.86	0.00	0.12
EAS-DS	2026-08-03 04:30:00	13.22	220.74	0.25	7.71	9.66	0.00	0.12
EAS-DS	2026-08-03 04:45:00	13.44	242.08	0.01	7.68	9.76	0.00	0.13
EAS-DS	2026-08-03 05:00:00	13.37	225.86	0.22	7.72	9.59	0.00	0.12
EAS-DS	2026-08-03 05:15:00	13.28	231.17	0.24	7.70	9.62	0.00	0.12
EAS-DS	2026-08-03 05:30:00	13.38	242.45	0.23	7.75	9.82	0.00	0.13
EAS-DS	2026-08-03 05:45:00	13.13	228.99	0.01	7.74	9.97	0.00	0.12
EAS-DS	2026-08-03 06:00:00	13.22	233.59	0.23	7.79	9.94	0.00	0.13
EAS-DS	2026-08-03 06:15:00	13.09	221.80	0.25	7.74	9.87	0.00	0.12
EAS-DS	2026-08-03 06:30:00	13.25	237.02	0.25	7.78	9.89	0.03	0.13
EAS-DS	2026-08-03 06:45:00	13.34	242.39	0.02	7.66	9.52	0.00	0.13
EAS-DS	2026-08-03 07:00:00	13.26	239.61	0.22	7.77	9.88	0.00	0.13
EAS-DS	2026-08-03 07:15:00	13.27	239.55	0.24	7.71	9.83	0.00	0.13
EAS-DS	2026-08-03 07:30:00	13.11	222.96	0.24	7.65	9.53	0.00	0.12
EAS-DS	2026-08-03 07:45:00	13.22	234.98	0.02	7.74	9.90	0.00	0.13
EAS-DS	2026-08-03 08:00:00	13.08	223.44	0.23	7.74	9.88	0.00	0.12
EAS-DS	2026-08-03 08:15:00	13.18	232.88	0.24	7.76	9.93	0.00	0.13
EAS-DS	2026-08-03 08:30:00	13.30	237.87	0.25	7.72	9.76	0.00	0.13
EAS-DS	2026-08-03 08:45:00	13.27	223.91	0.02	7.64	9.48	0.00	0.12
EAS-DS	2026-08-03 09:00:00	13.36	235.17	0.23	7.71	9.58	38.93	0.13
EAS-DS	2026-08-03 09:15:00	13.40	223.66	0.24	7.72	9.81	0.00	0.12
EAS-DS	2026-08-03 09:30:00	13.41	228.07	0.24	7.75	9.88	0.00	0.12
EAS-DS	2026-08-03 09:45:00	13.47	230.57	0.04	7.73	9.77	0.00	0.12
EAS-DS	2026-08-03 10:00:00	13.50	221.45	0.23	7.75	9.69	0.00	0.12
EAS-DS	2026-08-03 10:15:00	13.64	229.63	0.24	7.74	9.76	0.00	0.12
EAS-DS	2026-08-03 10:30:00	13.70	222.43	0.25	7.69	9.52	0.00	0.12
EAS-DS	2026-08-03 10:45:00	13.85	218.05	0.02	7.68	9.75	0.00	0.12
EAS-DS	2026-08-03 11:00:00	13.96	233.02	0.23	7.77	9.77	0.00	0.12
EAS-DS	2026-08-03 11:15:00	14.03	233.15	0.24	7.80	9.79	0.00	0.12
EAS-DS	2026-08-03 11:30:00	14.16	229.56	0.24	7.76	9.63	0.00	0.12
EAS-DS	2026-08-03 11:45:00	14.25	233.41	0.03	7.74	9.65	0.00	0.13
EAS-DS	2026-08-03 12:00:00	14.29	221.46	0.23	7.70	9.37	0.00	0.12
EAS-DS	2026-08-03 12:15:00	14.55	234.49	0.24	7.84	9.65	0.00	0.13
EAS-DS	2026-08-03 12:30:00	14.68	220.96	0.25	7.76	9.50	0.00	0.12
EAS-DS	2026-08-03 12:45:00	14.66	229.74	0.02	7.75	9.65	0.58	0.12
EAS-DS	2026-08-03 13:00:00	14.61	222.13	0.22	7.74	9.58	0.00	0.12
EAS-DS	2026-08-03 13:15:00	14.64	219.76	0.24	7.67	9.36	0.00	0.12
EAS-DS	2026-08-03 13:30:00	14.93	234.66	0.24	7.76	9.45	0.00	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-03 13:45:00	15.04	222.09	0.03	7.69	9.33	0.00	0.12
EAS-DS	2026-08-03 14:00:00	15.05	232.26	0.22	7.79	9.53	0.00	0.12
EAS-DS	2026-08-03 14:15:00	15.03	223.64	0.24	7.73	9.18	0.00	0.12
EAS-DS	2026-08-03 14:30:00	14.94	228.85	0.24	7.81	9.56	0.00	0.12
EAS-DS	2026-08-03 14:45:00	14.82	220.47	0.02	7.70	9.50	0.00	0.12
EAS-DS	2026-08-03 15:00:00	15.10	233.80	0.22	7.74	9.40	0.00	0.12
EAS-DS	2026-08-03 15:15:00	15.13	233.21	0.23	7.68	9.14	0.00	0.12
EAS-DS	2026-08-03 15:30:00	15.31	234.45	0.24	7.74	9.37	0.00	0.13
EAS-DS	2026-08-03 15:45:00	15.28	222.36	0.03	7.74	9.39	0.00	0.12
EAS-DS	2026-08-03 16:00:00	15.22	223.48	0.23	7.80	9.48	0.00	0.12
EAS-DS	2026-08-03 16:15:00	15.11	221.64	0.24	7.79	9.44	0.00	0.12
EAS-DS	2026-08-03 16:30:00	15.15	221.71	0.24	7.74	9.35	0.00	0.12
EAS-DS	2026-08-03 16:45:00	15.28	234.71	0.02	7.71	9.38	0.00	0.13
EAS-DS	2026-08-03 17:00:00	15.24	219.96	0.22	7.75	9.39	0.00	0.12
EAS-DS	2026-08-03 17:15:00	15.08	228.91	0.24	7.76	9.48	0.00	0.12
EAS-DS	2026-08-03 17:30:00	15.08	226.81	0.24	7.68	9.13	0.00	0.12
EAS-DS	2026-08-03 17:45:00	15.12	232.44	0.02	7.74	9.41	0.00	0.12
EAS-DS	2026-08-03 18:00:00	15.06	231.09	0.23	7.70	9.22	0.00	0.12
EAS-DS	2026-08-03 18:15:00	15.07	227.94	0.23	7.78	9.50	0.00	0.12
EAS-DS	2026-08-03 18:30:00	14.83	221.50	0.24	7.77	9.49	0.00	0.12
EAS-DS	2026-08-03 18:45:00	14.69	219.18	0.01	7.66	9.44	0.00	0.12
EAS-DS	2026-08-03 19:00:00	14.75	216.95	0.23	7.66	9.16	0.00	0.12
EAS-DS	2026-08-03 19:15:00	14.80	227.77	0.23	7.78	9.56	0.00	0.12
EAS-DS	2026-08-03 19:30:00	14.60	219.83	0.24	7.76	9.54	0.00	0.12
EAS-DS	2026-08-03 19:45:00	14.74	230.70	0.02	7.77	9.59	0.00	0.12
EAS-DS	2026-08-03 20:00:00	14.77	234.31	0.23	7.75	9.44	0.00	0.13
EAS-DS	2026-08-03 20:15:00	14.61	221.92	0.24	7.70	9.26	0.00	0.12
EAS-DS	2026-08-03 20:30:00	14.70	232.78	0.24	7.78	9.54	0.00	0.12
EAS-DS	2026-08-03 20:45:00	14.51	227.88	0.01	7.75	9.63	0.00	0.12
EAS-DS	2026-08-03 21:00:00	14.27	217.97	0.22	7.76	9.62	0.00	0.12
EAS-DS	2026-08-03 21:15:00	14.33	225.54	0.23	7.78	9.69	0.00	0.12
EAS-DS	2026-08-03 21:30:00	14.29	223.27	0.24	7.76	9.60	0.00	0.12
EAS-DS	2026-08-03 21:45:00	14.19	226.83	0.01	7.77	9.71	0.00	0.12
EAS-DS	2026-08-03 22:00:00	14.26	226.95	0.22	7.75	9.55	0.00	0.12
EAS-DS	2026-08-03 22:15:00	14.39	231.31	0.24	7.75	9.52	0.00	0.12
EAS-DS	2026-08-03 22:30:00	14.44	235.50	0.24	7.73	9.37	0.00	0.13
EAS-DS	2026-08-03 22:45:00	14.19	229.58	0.00	7.66	9.58	0.00	0.12
EAS-DS	2026-08-03 23:00:00	14.20	227.61	0.22	7.74	9.62	0.00	0.12
EAS-DS	2026-08-03 23:15:00	14.10	233.62	0.23	7.78	9.73	0.00	0.13
EAS-DS	2026-08-03 23:30:00	13.75	222.62	0.23	7.74	9.75	0.00	0.12
EAS-DS	2026-08-03 23:45:00	14.09	241.03	0.01	7.74	9.68	0.00	0.13
EAS-DS	2026-08-04 00:00:00	14.26	246.24	0.22	7.80	9.61	0.00	0.13
EAS-DS	2026-08-04 00:15:00	13.77	231.87	0.23	7.79	9.82	0.00	0.12
EAS-DS	2026-08-04 00:30:00	13.88	236.73	0.24	7.83	9.78	0.00	0.13
EAS-DS	2026-08-04 00:45:00	13.65	223.66	0.01	7.66	9.65	0.18	0.12
EAS-DS	2026-08-04 01:00:00	13.98	244.21	0.22	7.76	9.71	0.00	0.13
EAS-DS	2026-08-04 01:15:00	14.19	251.21	0.23	7.75	9.59	0.00	0.13
EAS-DS	2026-08-04 01:30:00	13.90	225.52	0.24	7.70	9.38	0.00	0.12
EAS-DS	2026-08-04 01:45:00	13.91	242.56	0.03	7.74	9.71	0.00	0.13
EAS-DS	2026-08-04 02:00:00	13.81	228.68	0.22	7.71	9.37	0.00	0.12
EAS-DS	2026-08-04 02:15:00	14.08	252.94	0.23	7.78	9.59	0.78	0.14
EAS-DS	2026-08-04 02:30:00	13.53	224.93	0.23	7.80	9.83	0.00	0.12
EAS-DS	2026-08-04 02:45:00	13.49	222.66	0.01	7.72	9.80	0.00	0.12
EAS-DS	2026-08-04 03:00:00	13.85	246.54	0.22	7.77	9.69	0.00	0.13
EAS-DS	2026-08-04 03:15:00	13.89	242.26	0.23	7.70	9.43	0.00	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-04 03:30:00	13.66	234.38	0.23	7.78	9.80	0.00	0.13
EAS-DS	2026-08-04 03:45:00	13.64	234.84	0.02	7.76	9.82	0.00	0.13
EAS-DS	2026-08-04 04:00:00	13.46	223.19	0.22	7.76	9.80	0.00	0.12
EAS-DS	2026-08-04 04:15:00	13.69	239.73	0.24	7.81	9.77	0.00	0.13
EAS-DS	2026-08-04 04:30:00	13.81	245.90	0.24	7.80	9.70	0.00	0.13
EAS-DS	2026-08-04 04:45:00	13.63	224.58	0.01	7.69	9.57	0.00	0.12
EAS-DS	2026-08-04 05:00:00	13.73	240.78	0.22	7.69	9.51	0.00	0.13
EAS-DS	2026-08-04 05:15:00	13.59	226.81	0.23	7.73	9.66	0.00	0.12
EAS-DS	2026-08-04 05:30:00	13.69	242.30	0.24	7.76	9.69	0.00	0.13
EAS-DS	2026-08-04 05:45:00	13.45	227.07	0.03	7.72	9.77	0.00	0.12
EAS-DS	2026-08-04 06:00:00	13.55	241.29	0.23	7.77	9.79	0.00	0.13
EAS-DS	2026-08-04 06:15:00	13.61	237.19	0.24	7.72	9.46	0.00	0.13
EAS-DS	2026-08-04 06:30:00	13.47	236.16	0.24	7.80	9.87	0.00	0.13
EAS-DS	2026-08-04 06:45:00	13.36	225.63	0.01	7.73	9.88	0.00	0.12
EAS-DS	2026-08-04 07:00:00	13.39	226.45	0.22	7.71	9.60	0.00	0.12
EAS-DS	2026-08-04 07:15:00	13.62	246.11	0.23	7.76	9.76	0.00	0.13
EAS-DS	2026-08-04 07:30:00	13.60	236.94	0.24	7.77	9.61	0.00	0.13
EAS-DS	2026-08-04 07:45:00	13.49	236.78	0.02	7.76	9.86	0.00	0.13
EAS-DS	2026-08-04 08:00:00	13.51	236.15	0.22	7.75	9.69	0.00	0.13
EAS-DS	2026-08-04 08:15:00	13.43	223.90	0.24	7.80	9.84	0.00	0.12
EAS-DS	2026-08-04 08:30:00	13.56	239.76	0.24	7.78	9.79	0.00	0.13
EAS-DS	2026-08-04 08:45:00	13.54	224.70	0.01	7.72	9.77	0.00	0.12
EAS-DS	2026-08-04 09:00:00	13.62	235.84	0.22	7.75	9.79	0.00	0.13
EAS-DS	2026-08-04 09:15:00	13.60	231.29	0.23	7.73	9.64	0.00	0.12
EAS-DS	2026-08-04 09:30:00	13.67	220.58	0.24	7.71	9.50	0.00	0.12
EAS-DS	2026-08-04 09:45:00	13.79	227.00	0.01	7.73	9.76	0.00	0.12
EAS-DS	2026-08-04 10:00:00	13.84	229.33	0.23	7.80	9.82	0.00	0.12
EAS-DS	2026-08-04 10:15:00	13.94	237.21	0.24	7.79	9.72	0.00	0.13
EAS-DS	2026-08-04 10:30:00	13.98	229.19	0.18	7.76	9.49	1.80	0.12
EAS-DS	2026-08-04 10:45:00	13.82	228.92	0.02	7.41	8.73	0.00	0.12
EAS-DS	2026-08-04 11:00:00	14.36	241.31	0.22	7.82	9.77	2.58	0.13
EAS-DS	2026-08-04 11:15:00	14.48	236.67	0.23	7.79	9.74	0.00	0.13
EAS-DS	2026-08-04 11:30:00	14.52	233.58	0.23	7.82	9.73	0.26	0.12
EAS-DS	2026-08-04 11:45:00	14.52	224.35	0.02	7.78	9.70	0.54	0.12
EAS-DS	2026-08-04 12:00:00	14.56	232.68	0.22	7.83	9.72	0.00	0.12
EAS-DS	2026-08-04 12:15:00	14.58	230.80	0.24	7.82	9.68	0.00	0.12
EAS-DS	2026-08-04 12:30:00	14.70	228.01	0.24	7.82	9.66	0.00	0.12
EAS-DS	2026-08-04 12:45:00	14.83	238.06	0.02	7.80	9.66	0.34	0.13
EAS-DS	2026-08-04 13:00:00	14.93	228.41	0.22	7.81	9.54	0.00	0.12
EAS-DS	2026-08-04 13:15:00	15.08	244.13	0.23	7.84	9.56	0.00	0.13
EAS-DS	2026-08-04 13:30:00	15.13	247.95	0.23	7.84	9.54	0.00	0.13
EAS-DS	2026-08-04 13:45:00	15.33	232.37	0.02	7.81	9.46	0.00	0.12
EAS-DS	2026-08-04 14:00:00	15.34	247.56	0.23	7.86	9.54	1.63	0.13
EAS-DS	2026-08-04 14:15:00	15.33	253.81	0.24	7.86	9.49	0.00	0.14
EAS-DS	2026-08-04 14:30:00	15.46	237.71	0.24	7.87	9.47	0.00	0.13
EAS-DS	2026-08-04 14:45:00	15.32	250.41	0.02	7.84	9.53	0.67	0.13
EAS-DS	2026-08-04 15:00:00	15.22	241.38	0.22	7.84	9.48	0.24	0.13
EAS-DS	2026-08-04 15:15:00	15.47	251.42	0.24	7.85	9.42	0.20	0.13
EAS-DS	2026-08-04 15:30:00	15.36	247.63	0.24	7.83	9.47	0.00	0.13
EAS-DS	2026-08-04 15:45:00	15.29	240.09	0.03	7.77	9.31	0.00	0.13
EAS-DS	2026-08-04 16:00:00	15.52	257.40	0.22	7.86	9.36	0.00	0.14
EAS-DS	2026-08-04 16:15:00	15.48	248.60	0.23	7.87	9.40	0.05	0.13
EAS-DS	2026-08-04 16:30:00	15.50	250.83	0.23	7.86	9.43	0.00	0.13
EAS-DS	2026-08-04 16:45:00	15.41	247.41	0.02	7.80	9.39	0.00	0.13
EAS-DS	2026-08-04 17:00:00	15.28	248.62	0.22	7.86	9.51	1.01	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-04 17:15:00	15.18	249.66	0.23	7.83	9.52	0.00	0.13
EAS-DS	2026-08-04 17:30:00	15.04	239.31	0.24	7.83	9.53	0.00	0.13
EAS-DS	2026-08-04 17:45:00	15.32	258.10	0.03	7.84	9.42	0.00	0.14
EAS-DS	2026-08-04 18:00:00	15.29	245.99	0.22	7.79	9.23	0.00	0.13
EAS-DS	2026-08-04 18:15:00	15.43	260.80	0.22	7.88	9.42	0.00	0.14
EAS-DS	2026-08-04 18:30:00	15.38	253.24	0.23	7.88	9.33	0.00	0.14
EAS-DS	2026-08-04 18:45:00	15.08	240.55	0.02	7.82	9.50	0.00	0.13
EAS-DS	2026-08-04 19:00:00	14.92	240.27	0.22	7.82	9.51	0.00	0.13
EAS-DS	2026-08-04 19:15:00	14.87	238.45	0.24	7.77	9.38	0.00	0.13
EAS-DS	2026-08-04 19:30:00	15.20	261.93	0.24	7.84	9.33	0.00	0.14
EAS-DS	2026-08-04 19:45:00	15.15	254.75	0.02	7.73	8.88	0.00	0.14
EAS-DS	2026-08-04 20:00:00	14.98	253.99	0.22	7.83	9.30	0.00	0.14
EAS-DS	2026-08-04 20:15:00	15.06	263.79	0.23	7.76	8.72	0.00	0.14
EAS-DS	2026-08-04 20:30:00	15.07	263.56	0.24	7.43	7.41	0.00	0.14
EAS-DS	2026-08-04 20:45:00	15.00	265.63	0.01	7.75	8.78	52.08	0.14
EAS-DS	2026-08-04 21:00:00	14.69	246.79	0.23	7.70	8.85	0.00	0.13
EAS-DS	2026-08-04 21:15:00	14.69	253.54	0.24	7.75	9.12	0.00	0.14
EAS-DS	2026-08-04 21:30:00	14.30	242.03	0.24	7.76	9.29	0.00	0.13
EAS-DS	2026-08-04 21:45:00	14.22	241.19	0.03	7.75	9.28	0.00	0.13
EAS-DS	2026-08-04 22:00:00	14.26	244.61	0.22	7.76	9.21	0.00	0.13
EAS-DS	2026-08-04 22:15:00	14.45	248.88	0.24	7.62	8.70	0.00	0.13
EAS-DS	2026-08-04 22:30:00	14.57	257.84	0.24	7.77	9.15	0.28	0.14
EAS-DS	2026-08-04 22:45:00	14.28	244.84	0.01	7.72	9.20	0.00	0.13
EAS-DS	2026-08-04 23:00:00	14.07	230.35	0.23	7.75	9.35	0.00	0.12
EAS-DS	2026-08-04 23:15:00	14.25	245.32	0.24	7.76	9.38	27.60	0.13
EAS-DS	2026-08-04 23:30:00	14.47	258.75	0.24	7.76	9.31	0.00	0.14
EAS-DS	2026-08-04 23:45:00	14.52	257.13	0.01	7.68	8.82	0.00	0.14
EAS-DS	2026-08-05 00:00:00	14.60	259.68	0.23	7.76	8.77	2.24	0.14
EAS-DS	2026-08-05 00:15:00	14.44	248.64	0.23	7.75	8.97	0.00	0.13
EAS-DS	2026-08-05 00:30:00	14.26	230.48	0.25	7.71	8.66	1.21	0.12
EAS-DS	2026-08-05 00:45:00	14.72	274.06	0.02	7.76	9.09	0.00	0.15
EAS-DS	2026-08-05 01:00:00	14.62	265.44	0.22	7.74	9.19	0.00	0.14
EAS-DS	2026-08-05 01:15:00	14.06	234.18	0.24	7.74	9.50	0.00	0.13
EAS-DS	2026-08-05 01:30:00	14.18	246.95	0.24	7.76	9.53	0.00	0.13
EAS-DS	2026-08-05 01:45:00	14.28	255.72	0.02	7.77	9.53	0.00	0.14
EAS-DS	2026-08-05 02:00:00	14.19	236.81	0.23	7.75	9.23	0.00	0.13
EAS-DS	2026-08-05 02:15:00	14.09	244.46	0.24	7.79	9.60	0.00	0.13
EAS-DS	2026-08-05 02:30:00	13.80	224.78	0.24	7.76	9.64	0.19	0.12
EAS-DS	2026-08-05 02:45:00	14.08	248.84	0.01	7.74	9.60	0.00	0.13
EAS-DS	2026-08-05 03:00:00	14.24	257.84	0.23	7.78	9.60	0.00	0.14
EAS-DS	2026-08-05 03:15:00	14.20	241.62	0.24	7.74	9.42	0.00	0.13
EAS-DS	2026-08-05 03:30:00	14.15	251.74	0.24	7.79	9.65	0.00	0.14
EAS-DS	2026-08-05 03:45:00	14.23	253.38	0.03	7.71	9.41	0.00	0.14
EAS-DS	2026-08-05 04:00:00	13.87	238.93	0.22	7.78	9.70	0.50	0.13
EAS-DS	2026-08-05 04:15:00	14.07	249.05	0.24	7.80	9.60	0.00	0.13
EAS-DS	2026-08-05 04:30:00	13.86	236.47	0.24	7.79	9.74	0.00	0.13
EAS-DS	2026-08-05 04:45:00	13.65	222.32	0.03	7.72	9.71	0.44	0.12
EAS-DS	2026-08-05 05:00:00	13.87	239.13	0.23	7.76	9.73	0.00	0.13
EAS-DS	2026-08-05 05:15:00	13.71	222.97	0.24	7.77	9.76	27.85	0.12
EAS-DS	2026-08-05 05:30:00	13.74	233.97	0.25	7.77	9.79	0.19	0.13
EAS-DS	2026-08-05 05:45:00	13.71	233.18	0.04	7.79	9.84	2.64	0.13
EAS-DS	2026-08-05 06:00:00	13.53	222.94	0.23	7.76	9.74	0.00	0.12
EAS-DS	2026-08-05 06:15:00	13.66	232.95	0.24	7.81	9.81	0.00	0.13
EAS-DS	2026-08-05 06:30:00	13.77	238.41	0.24	7.79	9.65	0.00	0.13
EAS-DS	2026-08-05 06:45:00	13.69	223.35	0.03	7.69	9.54	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-05 07:00:00	13.82	241.60	0.22	7.79	9.78	0.00	0.13
EAS-DS	2026-08-05 07:15:00	13.50	223.67	0.24	7.73	9.83	0.42	0.12
EAS-DS	2026-08-05 07:30:00	13.65	236.77	0.25	7.78	9.82	0.04	0.13
EAS-DS	2026-08-05 07:45:00	13.80	240.20	0.05	7.79	9.78	4.45	0.13
EAS-DS	2026-08-05 08:00:00	13.74	227.74	0.24	7.75	9.56	0.04	0.12
EAS-DS	2026-08-05 08:15:00	13.74	235.05	0.24	7.78	9.70	0.00	0.13
EAS-DS	2026-08-05 08:30:00	13.70	223.39	0.24	7.79	9.57	0.00	0.12
EAS-DS	2026-08-05 08:45:00	13.59	227.02	0.02	7.75	9.88	0.00	0.12
EAS-DS	2026-08-05 09:00:00	13.67	230.64	0.23	7.77	9.86	0.00	0.12
EAS-DS	2026-08-05 09:15:00	13.67	218.92	0.25	7.73	9.63	0.00	0.12
EAS-DS	2026-08-05 09:30:00	13.75	228.79	0.25	7.77	9.83	0.00	0.12
EAS-DS	2026-08-05 09:45:00	13.73	217.95	0.00	7.67	9.69	2.44	0.12
EAS-DS	2026-08-05 10:00:00	13.73	222.83	0.22	7.74	9.79	0.00	0.12
EAS-DS	2026-08-05 10:15:00	13.85	227.48	0.23	7.73	9.69	0.00	0.12
EAS-DS	2026-08-05 10:30:00	13.91	220.44	0.24	7.75	9.60	0.00	0.12
EAS-DS	2026-08-05 10:45:00	14.12	229.95	0.01	7.67	9.63	0.00	0.12
EAS-DS	2026-08-05 11:00:00	14.23	226.00	0.22	7.70	9.52	0.00	0.12
EAS-DS	2026-08-05 11:15:00	14.37	226.74	0.23	7.73	9.57	0.00	0.12
EAS-DS	2026-08-05 11:30:00	14.42	228.49	0.23	7.74	9.54	0.00	0.12
EAS-DS	2026-08-05 11:45:00	14.45	219.55	0.01	7.66	9.34	0.00	0.12
EAS-DS	2026-08-05 12:00:00	14.47	224.15	0.23	7.76	9.63	0.00	0.12
EAS-DS	2026-08-05 12:15:00	14.50	223.91	0.23	7.78	9.62	0.00	0.12
EAS-DS	2026-08-05 12:30:00	14.41	216.47	0.24	7.75	9.53	0.00	0.12
EAS-DS	2026-08-05 12:45:00	14.67	225.56	0.01	7.68	9.49	0.00	0.12
EAS-DS	2026-08-05 13:00:00	14.90	228.75	0.22	7.70	9.39	0.00	0.12
EAS-DS	2026-08-05 13:15:00	14.95	223.13	0.22	7.71	9.22	0.00	0.12
EAS-DS	2026-08-05 13:30:00	15.22	229.86	0.22	7.73	9.36	0.00	0.12
EAS-DS	2026-08-05 13:45:00	15.23	232.40	0.01	7.70	9.29	0.00	0.12
EAS-DS	2026-08-05 14:00:00	15.30	223.41	0.22	7.77	9.29	0.00	0.12
EAS-DS	2026-08-05 14:15:00	15.42	234.14	0.23	7.79	9.34	0.00	0.12
EAS-DS	2026-08-05 14:30:00	15.21	231.94	0.23	7.78	9.34	0.00	0.12
EAS-DS	2026-08-05 14:45:00	15.31	229.49	0.00	7.65	9.11	0.00	0.12
EAS-DS	2026-08-05 15:00:00	15.49	230.64	0.21	7.80	9.36	0.00	0.12
EAS-DS	2026-08-05 15:15:00	15.27	227.93	0.22	7.77	9.41	0.00	0.12
EAS-DS	2026-08-05 15:30:00	14.99	220.89	0.22	7.75	9.32	0.00	0.12
EAS-DS	2026-08-05 15:45:00	15.43	231.95	0.01	7.70	9.29	0.06	0.12
EAS-DS	2026-08-05 16:00:00	15.57	233.17	0.22	7.75	9.20	0.27	0.12
EAS-DS	2026-08-05 16:15:00	15.51	223.15	0.23	7.74	9.04	0.00	0.12
EAS-DS	2026-08-05 16:30:00	15.63	228.86	0.23	7.74	9.23	0.00	0.12
EAS-DS	2026-08-05 16:45:00	15.37	225.30	-0.01	7.69	9.33	0.00	0.12
EAS-DS	2026-08-05 17:00:00	15.05	218.54	0.22	7.70	9.27	0.00	0.12
EAS-DS	2026-08-05 17:15:00	15.51	231.31	0.22	7.74	9.19	0.32	0.12
EAS-DS	2026-08-05 17:30:00	15.48	230.62	0.22	7.65	9.09	0.00	0.12
EAS-DS	2026-08-05 17:45:00	15.21	225.41	0.00	7.73	9.43	0.00	0.12
EAS-DS	2026-08-05 18:00:00	14.77	217.27	0.22	7.75	9.31	0.00	0.12
EAS-DS	2026-08-05 18:15:00	15.09	229.03	0.23	7.72	9.35	0.08	0.12
EAS-DS	2026-08-05 18:30:00	15.29	233.26	0.23	7.73	9.24	0.36	0.12
EAS-DS	2026-08-05 18:45:00	15.28	227.50	-0.01	7.67	9.15	0.00	0.12
EAS-DS	2026-08-05 19:00:00	14.87	225.75	0.21	7.77	9.45	0.00	0.12
EAS-DS	2026-08-05 19:15:00	14.45	217.63	0.22	7.70	9.36	0.00	0.12
EAS-DS	2026-08-05 19:30:00	14.92	229.17	0.22	7.72	9.40	0.00	0.12
EAS-DS	2026-08-05 19:45:00	15.13	232.16	0.00	7.66	9.16	0.00	0.12
EAS-DS	2026-08-05 20:00:00	15.03	231.24	0.22	7.71	9.12	0.00	0.12
EAS-DS	2026-08-05 20:15:00	14.64	225.76	0.22	7.77	9.53	0.00	0.12
EAS-DS	2026-08-05 20:30:00	14.47	218.47	0.23	7.76	9.36	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-05 20:45:00	14.82	233.75	-0.01	7.66	9.40	0.00	0.12
EAS-DS	2026-08-05 21:00:00	14.82	233.93	0.21	7.72	9.23	0.00	0.13
EAS-DS	2026-08-05 21:15:00	14.65	225.76	0.21	7.79	9.45	0.00	0.12
EAS-DS	2026-08-05 21:30:00	14.60	228.45	0.21	7.73	9.36	0.00	0.12
EAS-DS	2026-08-05 21:45:00	14.67	231.62	0.00	7.66	9.29	0.00	0.12
EAS-DS	2026-08-05 22:00:00	14.40	217.31	0.21	7.73	9.20	0.00	0.12
EAS-DS	2026-08-05 22:15:00	14.48	229.96	0.22	7.74	9.44	0.00	0.12
EAS-DS	2026-08-05 22:30:00	14.60	232.84	0.22	7.76	9.37	0.00	0.12
EAS-DS	2026-08-05 22:45:00	14.31	226.46	-0.02	7.71	9.60	0.00	0.12
EAS-DS	2026-08-05 23:00:00	14.10	218.12	0.21	7.74	9.47	0.00	0.12
EAS-DS	2026-08-05 23:15:00	14.27	227.94	0.22	7.73	9.57	0.00	0.12
EAS-DS	2026-08-05 23:30:00	14.36	230.33	0.22	7.70	9.41	0.00	0.12
EAS-DS	2026-08-05 23:45:00	14.31	219.74	-0.01	7.72	9.42	0.00	0.12
EAS-DS	2026-08-06 00:00:00	14.50	235.14	0.21	7.64	9.17	0.00	0.13
EAS-DS	2026-08-06 00:15:00	14.52	240.13	0.22	7.67	9.15	0.00	0.13
EAS-DS	2026-08-06 00:30:00	14.29	227.74	0.23	7.63	9.15	0.00	0.12
EAS-DS	2026-08-06 00:45:00	14.27	232.52	-0.02	7.60	9.29	0.00	0.12
EAS-DS	2026-08-06 01:00:00	14.26	232.01	0.20	7.74	9.53	0.00	0.12
EAS-DS	2026-08-06 01:15:00	14.02	227.06	0.21	7.73	9.64	0.00	0.12
EAS-DS	2026-08-06 01:30:00	13.93	222.24	0.21	7.69	9.43	0.00	0.12
EAS-DS	2026-08-06 01:45:00	14.09	232.69	-0.02	7.62	9.52	0.00	0.12
EAS-DS	2026-08-06 02:00:00	14.18	234.62	0.21	7.72	9.37	0.00	0.13
EAS-DS	2026-08-06 02:15:00	14.19	238.44	0.22	7.66	9.53	0.00	0.13
EAS-DS	2026-08-06 02:30:00	13.95	222.58	0.22	7.71	9.17	0.00	0.12
EAS-DS	2026-08-06 02:45:00	14.06	234.56	-0.02	7.62	9.57	0.00	0.13
EAS-DS	2026-08-06 03:00:00	14.16	236.14	0.21	7.54	8.70	0.00	0.13
EAS-DS	2026-08-06 03:15:00	14.04	230.98	0.22	7.74	9.63	0.00	0.12
EAS-DS	2026-08-06 03:30:00	14.05	230.82	0.22	7.69	9.38	0.00	0.12
EAS-DS	2026-08-06 03:45:00	13.97	230.12	-0.01	7.64	9.58	0.00	0.12
EAS-DS	2026-08-06 04:00:00	14.03	234.47	0.22	7.59	9.53	0.00	0.13
EAS-DS	2026-08-06 04:15:00	14.06	236.15	0.23	7.61	9.22	0.00	0.13
EAS-DS	2026-08-06 04:30:00	13.78	225.29	0.22	7.77	9.73	0.00	0.12
EAS-DS	2026-08-06 04:45:00	13.84	229.50	-0.02	7.70	9.73	0.00	0.12
EAS-DS	2026-08-06 05:00:00	13.78	223.40	0.21	7.61	9.64	0.00	0.12
EAS-DS	2026-08-06 05:15:00	13.87	232.22	0.22	7.71	9.54	0.00	0.12
EAS-DS	2026-08-06 05:30:00	13.81	218.85	0.21	7.58	9.41	0.00	0.12
EAS-DS	2026-08-06 05:45:00	13.92	237.37	-0.01	7.59	9.34	0.00	0.13
EAS-DS	2026-08-06 06:00:00	13.78	231.78	0.21	7.76	9.77	0.00	0.12
EAS-DS	2026-08-06 06:15:00	13.62	221.06	0.23	7.71	9.69	0.00	0.12
EAS-DS	2026-08-06 06:30:00	13.84	239.45	0.23	7.60	9.57	0.00	0.13
EAS-DS	2026-08-06 06:45:00	13.90	235.46	0.00	7.67	9.47	0.00	0.13
EAS-DS	2026-08-06 07:00:00	13.87	228.93	0.20	7.70	9.50	2.29	0.12
EAS-DS	2026-08-06 07:15:00	13.79	223.85	0.22	7.61	9.52	0.00	0.12
EAS-DS	2026-08-06 07:30:00	13.94	241.78	0.21	7.61	9.57	0.00	0.13
EAS-DS	2026-08-06 07:45:00	13.95	243.58	0.00	7.60	9.55	0.00	0.13
EAS-DS	2026-08-06 08:00:00	13.83	237.03	0.21	7.69	9.64	0.00	0.13
EAS-DS	2026-08-06 08:15:00	13.81	229.04	0.22	7.70	9.45	0.00	0.12
EAS-DS	2026-08-06 08:30:00	13.88	236.57	0.22	7.63	9.59	0.00	0.13
EAS-DS	2026-08-06 08:45:00	13.86	232.27	-0.02	7.58	9.51	0.00	0.12
EAS-DS	2026-08-06 09:00:00	13.87	227.77	0.21	7.69	9.59	0.00	0.12
EAS-DS	2026-08-06 09:15:00	13.88	231.04	0.22	7.70	9.47	0.00	0.12
EAS-DS	2026-08-06 09:30:00	13.84	220.23	0.22	7.72	9.64	0.00	0.12
EAS-DS	2026-08-06 09:45:00	13.86	223.14	-0.01	7.65	9.67	0.00	0.12
EAS-DS	2026-08-06 10:00:00	13.93	227.58	0.22	7.60	9.64	0.00	0.12
EAS-DS	2026-08-06 10:15:00	14.00	225.85	0.23	7.68	9.66	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-06 10:30:00	14.04	224.68	0.23	7.73	9.57	1.00	0.12
EAS-DS	2026-08-06 10:45:00	14.17	221.37	-0.01	7.69	9.66	0.00	0.12
EAS-DS	2026-08-06 11:00:00	14.19	222.80	0.22	7.63	9.61	0.00	0.12
EAS-DS	2026-08-06 11:15:00	14.23	223.95	0.22	7.65	9.47	0.00	0.12
EAS-DS	2026-08-06 11:30:00	14.53	218.98	0.23	7.64	9.52	0.00	0.12
EAS-DS	2026-08-06 11:45:00	14.55	222.88	0.00	7.73	9.60	0.00	0.12
EAS-DS	2026-08-06 12:00:00	14.59	217.74	0.23	7.75	9.47	0.00	0.12
EAS-DS	2026-08-06 12:15:00	14.60	222.35	0.23	7.79	9.62	0.00	0.12
EAS-DS	2026-08-06 12:30:00	14.62	221.92	0.24	7.75	9.56	0.00	0.12
EAS-DS	2026-08-06 12:45:00	14.73	220.13	-0.01	7.65	9.37	0.00	0.12
EAS-DS	2026-08-06 13:00:00	14.87	223.99	0.22	7.71	9.39	0.00	0.12
EAS-DS	2026-08-06 13:15:00	14.87	227.17	0.22	7.71	9.38	0.00	0.12
EAS-DS	2026-08-06 13:30:00	15.17	222.77	0.23	7.75	9.39	0.00	0.12
EAS-DS	2026-08-06 13:45:00	15.07	225.79	0.01	7.72	9.43	0.00	0.12
EAS-DS	2026-08-06 14:00:00	15.10	228.97	0.22	7.68	9.34	0.00	0.12
EAS-DS	2026-08-06 14:15:00	15.15	232.08	0.23	7.69	9.34	0.00	0.12
EAS-DS	2026-08-06 14:30:00	15.28	232.30	0.23	7.69	9.32	0.00	0.12
EAS-DS	2026-08-06 14:45:00	15.42	234.07	0.00	7.66	9.05	0.00	0.12
EAS-DS	2026-08-06 15:00:00	15.45	234.05	0.21	7.69	9.23	0.00	0.12
EAS-DS	2026-08-06 15:15:00	15.44	236.50	0.22	7.69	9.22	0.00	0.13
EAS-DS	2026-08-06 15:30:00	15.62	233.79	0.22	7.72	9.22	0.00	0.12
EAS-DS	2026-08-06 15:45:00	15.58	236.81	0.00	7.67	9.16	0.00	0.13
EAS-DS	2026-08-06 16:00:00	15.48	233.19	0.22	7.77	9.30	0.00	0.12
EAS-DS	2026-08-06 16:15:00	15.22	225.88	0.23	7.78	9.43	0.00	0.12
EAS-DS	2026-08-06 16:30:00	15.33	233.58	0.23	7.69	9.29	0.00	0.12
EAS-DS	2026-08-06 16:45:00	15.50	240.51	-0.01	7.62	9.09	0.00	0.13
EAS-DS	2026-08-06 17:00:00	15.55	240.29	0.21	7.69	9.20	0.00	0.13
EAS-DS	2026-08-06 17:15:00	15.62	231.65	0.22	7.75	9.30	0.00	0.12
EAS-DS	2026-08-06 17:30:00	15.45	234.19	0.22	7.75	9.27	0.00	0.12
EAS-DS	2026-08-06 17:45:00	15.42	236.79	-0.01	7.65	9.20	0.00	0.13
EAS-DS	2026-08-06 18:00:00	15.44	236.92	0.20	7.67	9.13	0.00	0.13
EAS-DS	2026-08-06 18:15:00	15.51	237.14	0.21	7.64	9.24	0.00	0.13
EAS-DS	2026-08-06 18:30:00	15.37	231.49	0.21	7.79	9.37	22.45	0.12
EAS-DS	2026-08-06 18:45:00	15.24	230.70	-0.02	7.67	9.20	0.00	0.12
EAS-DS	2026-08-06 19:00:00	15.22	224.37	0.21	7.66	9.14	0.00	0.12
EAS-DS	2026-08-06 19:15:00	15.32	237.80	0.21	7.60	9.16	0.00	0.13
EAS-DS	2026-08-06 19:30:00	15.02	231.34	0.22	7.77	9.44	0.00	0.12
EAS-DS	2026-08-06 19:45:00	15.03	236.38	-0.01	7.67	9.37	0.01	0.13
EAS-DS	2026-08-06 20:00:00	15.14	234.76	0.21	7.69	9.15	28.70	0.13
EAS-DS	2026-08-06 20:15:00	15.21	243.46	0.22	7.58	9.13	0.00	0.13
EAS-DS	2026-08-06 20:30:00	15.18	243.08	0.21	7.65	9.11	0.00	0.13
EAS-DS	2026-08-06 20:45:00	15.08	235.92	-0.02	7.63	9.09	0.00	0.13
EAS-DS	2026-08-06 21:00:00	14.91	236.25	0.21	7.54	9.35	0.00	0.13
EAS-DS	2026-08-06 21:15:00	14.79	234.73	0.21	7.77	9.43	0.00	0.13
EAS-DS	2026-08-06 21:30:00	14.51	224.55	0.22	7.59	9.25	0.00	0.12
EAS-DS	2026-08-06 21:45:00	14.38	227.28	0.00	7.69	9.58	0.00	0.12
EAS-DS	2026-08-06 22:00:00	14.30	226.68	0.18	7.76	9.64	0.00	0.12
EAS-DS	2026-08-06 22:15:00	14.33	228.44	0.22	7.71	9.56	1.00	0.12
EAS-DS	2026-08-06 22:30:00	14.46	229.69	0.22	7.68	9.40	0.00	0.12
EAS-DS	2026-08-06 22:45:00	14.27	227.41	-0.02	7.68	9.53	0.00	0.12
EAS-DS	2026-08-06 23:00:00	14.23	228.04	0.20	7.76	9.67	0.00	0.12
EAS-DS	2026-08-06 23:15:00	14.35	233.29	0.22	7.70	9.56	0.00	0.12
EAS-DS	2026-08-06 23:30:00	14.44	234.60	0.22	7.68	9.37	0.00	0.13
EAS-DS	2026-08-06 23:45:00	14.58	240.60	-0.01	7.63	9.43	1.01	0.13
EAS-DS	2026-08-07 00:00:00	14.64	244.08	0.20	7.62	9.32	0.00	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-07 00:15:00	14.39	233.90	0.21	7.79	9.61	3.07	0.13
EAS-DS	2026-08-07 00:30:00	14.20	222.71	0.22	7.65	9.49	0.00	0.12
EAS-DS	2026-08-07 00:45:00	14.44	240.97	-0.01	7.64	9.34	0.00	0.13
EAS-DS	2026-08-07 01:00:00	14.48	241.05	0.21	7.70	9.46	0.00	0.13
EAS-DS	2026-08-07 01:15:00	14.43	240.00	0.22	7.66	9.35	0.00	0.13
EAS-DS	2026-08-07 01:30:00	14.48	242.14	0.22	7.69	9.40	0.00	0.13
EAS-DS	2026-08-07 01:45:00	14.50	243.21	-0.01	7.62	9.45	0.00	0.13
EAS-DS	2026-08-07 02:00:00	14.40	242.74	0.21	7.67	9.41	30.56	0.13
EAS-DS	2026-08-07 02:15:00	14.31	236.87	0.21	7.56	9.25	0.00	0.13
EAS-DS	2026-08-07 02:30:00	14.23	238.30	0.21	7.57	9.50	0.00	0.13
EAS-DS	2026-08-07 02:45:00	14.09	235.54	-0.02	7.69	9.69	0.00	0.13
EAS-DS	2026-08-07 03:00:00	14.09	236.95	0.21	7.72	9.63	0.00	0.13
EAS-DS	2026-08-07 03:15:00	13.98	227.22	0.21	7.70	9.66	0.00	0.12
EAS-DS	2026-08-07 03:30:00	14.05	235.84	0.22	7.70	9.73	0.00	0.13
EAS-DS	2026-08-07 03:45:00	14.12	240.10	0.00	7.64	9.59	0.00	0.13
EAS-DS	2026-08-07 04:00:00	14.20	245.41	0.21	7.61	9.45	0.00	0.13
EAS-DS	2026-08-07 04:15:00	14.25	241.26	0.21	7.50	9.50	0.00	0.13
EAS-DS	2026-08-07 04:30:00	14.26	246.27	0.21	7.41	9.20	0.00	0.13
EAS-DS	2026-08-07 04:45:00	14.26	237.06	-0.02	7.65	9.36	0.00	0.13
EAS-DS	2026-08-07 05:00:00	14.24	238.52	0.20	7.61	9.49	0.00	0.13
EAS-DS	2026-08-07 05:15:00	14.31	247.15	0.21	7.59	9.47	0.00	0.13
EAS-DS	2026-08-07 05:30:00	14.28	245.32	0.21	7.75	9.55	0.00	0.13
EAS-DS	2026-08-07 05:45:00	14.12	239.37	-0.01	7.66	9.60	0.35	0.13
EAS-DS	2026-08-07 06:00:00	13.98	229.97	0.21	7.71	9.59	0.00	0.12
EAS-DS	2026-08-07 06:15:00	14.11	243.52	0.21	7.65	9.50	0.00	0.13
EAS-DS	2026-08-07 06:30:00	14.17	247.34	0.22	7.37	9.26	0.00	0.13
EAS-DS	2026-08-07 06:45:00	14.08	237.63	-0.03	7.68	9.61	30.80	0.13
EAS-DS	2026-08-07 07:00:00	14.14	244.73	0.21	7.69	9.50	0.00	0.13
EAS-DS	2026-08-07 07:15:00	14.14	241.63	0.21	7.63	9.43	0.00	0.13
EAS-DS	2026-08-07 07:30:00	14.13	244.51	0.22	7.69	9.28	0.00	0.13
EAS-DS	2026-08-07 07:45:00	14.03	237.06	-0.02	7.67	9.67	0.00	0.13
EAS-DS	2026-08-07 08:00:00	13.97	229.46	0.19	7.65	9.52	0.00	0.12
EAS-DS	2026-08-07 08:15:00	14.06	242.49	0.21	7.47	9.35	0.00	0.13
EAS-DS	2026-08-07 08:30:00	14.04	234.97	0.21	7.73	9.69	0.00	0.13
EAS-DS	2026-08-07 08:45:00	14.03	227.16	-0.02	7.62	9.42	0.00	0.12
EAS-DS	2026-08-07 09:00:00	14.10	229.36	0.21	7.45	9.46	0.00	0.12
EAS-DS	2026-08-07 09:15:00	14.10	237.17	0.21	7.66	9.54	0.00	0.13
EAS-DS	2026-08-07 09:30:00	14.25	232.90	0.22	7.66	9.59	0.00	0.12
EAS-DS	2026-08-07 09:45:00	14.27	239.21	-0.01	7.64	9.55	0.00	0.13
EAS-DS	2026-08-07 10:00:00	14.38	231.13	0.20	7.68	9.35	0.00	0.12
EAS-DS	2026-08-07 10:15:00	14.44	242.73	0.21	7.46	9.20	0.00	0.13
EAS-DS	2026-08-07 10:30:00	14.51	244.83	0.21	7.61	9.36	0.00	0.13
EAS-DS	2026-08-07 10:45:00	14.61	245.52	-0.02	7.49	9.28	0.00	0.13
EAS-DS	2026-08-07 11:00:00	14.70	242.12	0.20	7.56	9.20	0.00	0.13
EAS-DS	2026-08-07 11:15:00	14.97	240.31	0.21	7.73	9.37	0.00	0.13
EAS-DS	2026-08-07 11:30:00	15.03	227.47	-0.04	7.77	9.61	0.00	0.12
EAS-DS	2026-08-07 11:45:00	15.10	238.20	0.18	7.82	9.55	0.00	0.13
EAS-DS	2026-08-07 12:00:00	15.22	231.53	0.19	7.81	9.40	0.00	0.12
EAS-DS	2026-08-07 12:15:00	15.41	239.28	0.20	7.82	9.48	0.00	0.13
EAS-DS	2026-08-07 12:30:00	15.57	234.76	-0.03	7.78	9.46	0.00	0.13
EAS-DS	2026-08-07 12:45:00	15.53	237.41	0.18	7.83	9.45	0.00	0.13
EAS-DS	2026-08-07 13:00:00	15.66	227.91	0.18	7.83	9.40	0.00	0.12
EAS-DS	2026-08-07 13:15:00	15.69	236.50	0.17	7.85	9.48	1.56	0.13
EAS-DS	2026-08-07 13:30:00	15.55	232.74	-0.02	7.81	9.50	0.00	0.12
EAS-DS	2026-08-07 13:45:00	15.56	225.65	0.18	7.87	9.47	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-07 14:00:00	15.79	235.97	0.19	7.87	9.41	0.00	0.13
EAS-DS	2026-08-07 14:15:00	15.87	236.05	0.19	7.85	9.39	0.00	0.13
EAS-DS	2026-08-07 14:30:00	15.99	231.85	-0.03	7.78	9.30	0.00	0.12
EAS-DS	2026-08-07 14:45:00	16.17	230.96	0.18	7.86	9.42	0.72	0.12
EAS-DS	2026-08-07 15:00:00	15.85	229.38	0.19	7.83	9.42	0.00	0.12
EAS-DS	2026-08-07 15:15:00	15.72	228.95	0.18	7.86	9.49	0.00	0.12
EAS-DS	2026-08-07 15:30:00	15.58	224.36	-0.02	7.80	9.46	0.00	0.12
EAS-DS	2026-08-07 15:45:00	15.81	232.10	0.19	7.86	9.36	0.00	0.12
EAS-DS	2026-08-07 16:00:00	15.88	233.56	0.19	7.88	9.34	0.00	0.12
EAS-DS	2026-08-07 16:15:00	15.91	234.04	0.19	7.85	9.36	0.00	0.12
EAS-DS	2026-08-07 16:30:00	15.96	231.66	-0.01	7.77	9.26	0.00	0.12
EAS-DS	2026-08-07 16:45:00	15.92	228.56	0.18	7.85	9.45	0.00	0.12
EAS-DS	2026-08-07 17:00:00	15.52	228.28	0.18	7.83	9.52	1.96	0.12
EAS-DS	2026-08-07 17:15:00	15.68	232.98	0.19	7.81	9.40	0.00	0.12
EAS-DS	2026-08-07 17:30:00	15.80	226.76	0.00	7.80	9.28	0.00	0.12
EAS-DS	2026-08-07 17:45:00	15.78	234.13	0.19	7.84	9.35	0.00	0.12
EAS-DS	2026-08-07 18:00:00	15.79	234.12	0.19	7.86	9.35	0.00	0.12
EAS-DS	2026-08-07 18:15:00	15.78	233.46	0.20	7.86	9.36	0.00	0.12
EAS-DS	2026-08-07 18:30:00	15.80	224.11	-0.01	7.77	9.28	0.00	0.12
EAS-DS	2026-08-07 18:45:00	15.64	232.51	0.19	7.80	9.40	0.00	0.12
EAS-DS	2026-08-07 19:00:00	15.19	229.50	0.19	7.81	9.52	0.01	0.12
EAS-DS	2026-08-07 19:15:00	15.13	231.07	0.19	7.82	9.50	0.00	0.12
EAS-DS	2026-08-07 19:30:00	15.36	235.01	-0.01	7.80	9.44	0.00	0.13
EAS-DS	2026-08-07 19:45:00	15.13	232.15	0.19	7.84	9.52	0.00	0.12
EAS-DS	2026-08-07 20:00:00	15.03	234.95	0.20	7.86	9.56	0.00	0.13
EAS-DS	2026-08-07 20:15:00	15.02	237.70	0.20	7.84	9.52	0.00	0.13
EAS-DS	2026-08-07 20:30:00	14.97	226.40	-0.02	7.79	9.47	0.00	0.12
EAS-DS	2026-08-07 20:45:00	15.06	240.53	0.18	7.84	9.53	0.00	0.13
EAS-DS	2026-08-07 21:00:00	14.97	239.81	0.19	7.81	9.55	0.00	0.13
EAS-DS	2026-08-07 21:15:00	15.00	240.83	0.19	7.82	9.33	0.00	0.13
EAS-DS	2026-08-07 21:30:00	14.97	239.91	-0.01	7.74	9.49	0.00	0.13
EAS-DS	2026-08-07 21:45:00	14.65	231.71	0.19	7.85	9.67	0.00	0.12
EAS-DS	2026-08-07 22:00:00	14.50	233.02	0.19	7.85	9.66	0.00	0.12
EAS-DS	2026-08-07 22:15:00	14.51	224.56	0.19	7.86	9.60	0.00	0.12
EAS-DS	2026-08-07 22:30:00	14.57	237.58	-0.02	7.75	9.64	0.00	0.13
EAS-DS	2026-08-07 22:45:00	14.57	232.38	0.19	7.80	9.62	0.00	0.12
EAS-DS	2026-08-07 23:00:00	14.42	234.55	0.20	7.80	9.67	0.00	0.13
EAS-DS	2026-08-07 23:15:00	14.33	233.87	0.20	7.79	9.68	0.00	0.13
EAS-DS	2026-08-07 23:30:00	14.42	241.46	0.01	7.77	9.64	0.00	0.13
EAS-DS	2026-08-07 23:45:00	14.53	234.80	0.20	7.73	8.77	0.00	0.13
EAS-DS	2026-08-08 00:00:00	14.41	246.63	0.20	7.84	9.67	0.00	0.13
EAS-DS	2026-08-08 00:15:00	14.24	242.49	0.20	7.85	9.71	0.00	0.13
EAS-DS	2026-08-08 00:30:00	14.28	236.18	0.00	7.76	9.59	0.00	0.13
EAS-DS	2026-08-08 00:45:00	14.23	241.25	0.18	7.83	9.82	0.97	0.13
EAS-DS	2026-08-08 01:00:00	14.09	241.04	0.19	7.83	9.78	0.00	0.13
EAS-DS	2026-08-08 01:15:00	14.11	243.99	0.19	7.83	9.78	0.00	0.13
EAS-DS	2026-08-08 01:30:00	14.17	247.65	0.00	7.80	9.76	0.00	0.13
EAS-DS	2026-08-08 01:45:00	14.25	254.22	0.18	7.84	9.70	0.00	0.14
EAS-DS	2026-08-08 02:00:00	14.10	245.07	0.19	7.84	9.72	0.00	0.13
EAS-DS	2026-08-08 02:15:00	14.20	248.79	0.20	7.81	9.62	0.00	0.13
EAS-DS	2026-08-08 02:30:00	13.97	236.12	-0.01	7.80	9.90	1.15	0.13
EAS-DS	2026-08-08 02:45:00	14.01	241.43	0.18	7.82	9.77	0.00	0.13
EAS-DS	2026-08-08 03:00:00	14.13	249.29	0.20	7.82	9.74	0.00	0.13
EAS-DS	2026-08-08 03:15:00	14.15	239.71	0.19	7.80	9.59	0.00	0.13
EAS-DS	2026-08-08 03:30:00	14.15	248.76	0.00	7.79	9.72	0.00	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-08 03:45:00	14.07	243.79	0.19	7.83	9.71	0.00	0.13
EAS-DS	2026-08-08 04:00:00	13.92	228.10	0.20	7.81	9.70	0.00	0.12
EAS-DS	2026-08-08 04:15:00	14.03	243.46	0.20	7.81	9.74	0.00	0.13
EAS-DS	2026-08-08 04:30:00	13.78	226.63	0.00	7.76	9.81	0.00	0.12
EAS-DS	2026-08-08 04:45:00	13.83	232.35	0.19	7.81	9.90	0.00	0.12
EAS-DS	2026-08-08 05:00:00	13.99	239.81	0.20	7.79	9.76	0.00	0.13
EAS-DS	2026-08-08 05:15:00	14.06	241.59	0.20	7.80	9.72	0.00	0.13
EAS-DS	2026-08-08 05:30:00	14.10	239.44	0.00	7.75	9.65	0.11	0.13
EAS-DS	2026-08-08 05:45:00	13.78	229.86	0.19	7.83	9.91	0.00	0.12
EAS-DS	2026-08-08 06:00:00	13.77	231.62	0.20	7.82	9.84	0.00	0.12
EAS-DS	2026-08-08 06:15:00	13.87	235.11	0.21	7.81	9.79	0.00	0.13
EAS-DS	2026-08-08 06:30:00	13.85	229.64	0.00	7.74	9.71	0.00	0.12
EAS-DS	2026-08-08 06:45:00	13.69	226.77	0.19	7.78	9.92	0.14	0.12
EAS-DS	2026-08-08 07:00:00	13.65	226.84	0.20	7.78	9.89	0.00	0.12
EAS-DS	2026-08-08 07:15:00	13.72	228.69	0.20	7.77	9.83	0.00	0.12
EAS-DS	2026-08-08 07:30:00	13.71	220.43	0.00	7.75	9.78	0.00	0.12
EAS-DS	2026-08-08 07:45:00	13.79	228.83	0.20	7.79	9.80	0.00	0.12
EAS-DS	2026-08-08 08:00:00	13.79	227.40	0.20	7.82	9.79	0.00	0.12
EAS-DS	2026-08-08 08:15:00	13.80	224.70	0.21	7.82	9.81	0.00	0.12
EAS-DS	2026-08-08 08:30:00	13.75	224.85	0.00	7.74	9.84	0.00	0.12
EAS-DS	2026-08-08 08:45:00	13.79	224.72	0.19	7.76	9.62	0.00	0.12
EAS-DS	2026-08-08 09:00:00	13.88	218.94	0.20	7.68	9.17	0.00	0.12
EAS-DS	2026-08-08 09:15:00	13.77	222.43	0.20	7.79	9.85	0.00	0.12
EAS-DS	2026-08-08 09:30:00	13.72	221.47	0.01	7.78	9.89	0.00	0.12
EAS-DS	2026-08-08 09:45:00	13.70	220.12	0.20	7.84	9.97	1.70	0.12
EAS-DS	2026-08-08 10:00:00	13.87	223.03	0.21	7.85	9.83	0.00	0.12
EAS-DS	2026-08-08 10:15:00	14.06	225.82	0.21	7.82	9.76	0.00	0.12
EAS-DS	2026-08-08 10:30:00	14.18	224.38	0.01	7.78	9.85	0.00	0.12
EAS-DS	2026-08-08 10:45:00	14.26	226.61	0.20	7.82	9.73	0.00	0.12
EAS-DS	2026-08-08 11:00:00	14.38	229.68	0.20	7.82	9.70	0.00	0.12
EAS-DS	2026-08-08 11:15:00	14.48	219.52	0.21	7.78	9.43	0.00	0.12
EAS-DS	2026-08-08 11:30:00	14.69	233.62	0.20	7.82	9.56	0.00	0.12
EAS-DS	2026-08-08 11:45:00	14.77	235.99	0.20	7.82	9.49	0.00	0.13
EAS-DS	2026-08-08 12:00:00	15.07	229.57	0.21	7.80	9.42	0.00	0.12
EAS-DS	2026-08-08 12:15:00	15.08	237.08	0.19	7.79	9.43	0.00	0.13
EAS-DS	2026-08-08 12:30:00	15.12	231.84	0.20	7.80	9.49	0.00	0.12
EAS-DS	2026-08-08 12:45:00	15.12	231.52	0.21	7.83	9.58	0.00	0.12
EAS-DS	2026-08-08 13:00:00	15.13	225.45	0.22	7.78	9.47	0.00	0.12
EAS-DS	2026-08-08 13:15:00	15.40	236.99	0.19	7.83	9.38	0.00	0.13
EAS-DS	2026-08-08 13:30:00	15.67	241.29	0.22	7.88	9.48	1.58	0.13
EAS-DS	2026-08-08 13:45:00	15.55	227.38	0.22	7.84	9.35	0.00	0.12
EAS-DS	2026-08-08 14:00:00	15.66	238.88	0.22	7.83	9.31	0.00	0.13
EAS-DS	2026-08-08 14:15:00	15.71	243.64	0.20	7.81	9.25	0.00	0.13
EAS-DS	2026-08-08 14:30:00	15.70	241.91	0.21	7.72	8.87	0.00	0.13
EAS-DS	2026-08-08 14:45:00	15.94	246.79	0.21	7.79	9.17	0.00	0.13
EAS-DS	2026-08-08 15:00:00	15.99	249.16	0.21	7.80	9.19	0.00	0.13
EAS-DS	2026-08-08 15:15:00	15.79	248.41	0.19	7.64	8.78	0.00	0.13
EAS-DS	2026-08-08 15:30:00	16.21	245.86	0.21	7.91	9.37	0.00	0.13
EAS-DS	2026-08-08 15:45:00	15.85	242.43	0.21	7.91	9.45	0.00	0.13
EAS-DS	2026-08-08 16:00:00	15.85	234.22	0.21	7.87	9.36	0.00	0.12
EAS-DS	2026-08-08 16:15:00	15.86	240.33	0.19	7.86	9.41	0.36	0.13
EAS-DS	2026-08-08 16:30:00	15.83	242.81	0.21	7.85	9.38	0.00	0.13
EAS-DS	2026-08-08 16:45:00	15.77	233.70	0.21	7.79	9.27	0.00	0.12
EAS-DS	2026-08-08 17:00:00	15.83	244.01	0.21	7.88	9.48	0.00	0.13
EAS-DS	2026-08-08 17:15:00	15.89	249.58	0.19	7.81	9.19	0.00	0.13

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-08 17:30:00	15.91	247.25	0.21	7.76	8.92	0.00	0.13
EAS-DS	2026-08-08 17:45:00	16.03	253.84	0.21	7.83	9.17	0.00	0.14
EAS-DS	2026-08-08 18:00:00	15.81	247.40	0.21	7.87	9.37	0.00	0.13
EAS-DS	2026-08-08 18:15:00	15.84	253.81	0.19	7.80	9.22	0.00	0.14
EAS-DS	2026-08-08 18:30:00	15.79	240.93	0.20	7.72	8.84	0.00	0.13
EAS-DS	2026-08-08 18:45:00	15.93	256.61	0.20	7.79	9.17	0.00	0.14
EAS-DS	2026-08-08 19:00:00	15.88	240.24	0.20	7.80	9.06	0.64	0.13
EAS-DS	2026-08-08 19:15:00	15.63	245.09	0.18	7.90	9.51	0.00	0.13
EAS-DS	2026-08-08 19:30:00	15.37	242.12	0.20	7.84	9.43	0.00	0.13
EAS-DS	2026-08-08 19:45:00	15.09	237.75	0.21	7.88	9.61	0.00	0.13
EAS-DS	2026-08-08 20:00:00	14.86	237.58	0.21	7.88	9.71	0.22	0.13
EAS-DS	2026-08-08 20:15:00	15.20	245.80	0.19	7.80	9.37	0.00	0.13
EAS-DS	2026-08-08 20:30:00	15.24	245.46	0.20	7.71	9.25	0.00	0.13
EAS-DS	2026-08-08 20:45:00	15.12	241.93	0.20	7.78	9.40	0.00	0.13
EAS-DS	2026-08-08 21:00:00	14.82	235.72	0.20	7.80	9.54	0.00	0.13
EAS-DS	2026-08-08 21:15:00	14.65	234.75	0.19	7.80	9.59	0.00	0.13
EAS-DS	2026-08-08 21:30:00	14.76	229.69	0.22	7.67	9.15	0.00	0.12
EAS-DS	2026-08-08 21:45:00	14.68	237.04	0.21	7.78	9.49	0.00	0.13
EAS-DS	2026-08-08 22:00:00	14.63	236.67	0.22	7.76	9.49	0.00	0.13
EAS-DS	2026-08-08 22:15:00	14.29	227.43	0.18	7.83	9.74	1.01	0.12
EAS-DS	2026-08-08 22:30:00	14.34	231.43	0.20	7.77	9.66	0.00	0.12
EAS-DS	2026-08-08 22:45:00	14.44	230.36	0.21	7.70	9.29	0.00	0.12
EAS-DS	2026-08-08 23:00:00	14.43	228.95	0.20	7.70	9.34	0.00	0.12
EAS-DS	2026-08-08 23:15:00	14.38	220.38	0.19	7.72	9.26	0.00	0.12
EAS-DS	2026-08-08 23:30:00	14.33	230.77	0.20	7.82	9.58	0.00	0.12
EAS-DS	2026-08-08 23:45:00	14.24	231.07	0.21	7.81	9.60	0.00	0.12
EAS-DS	2026-08-09 00:00:00	14.12	222.60	0.22	7.81	9.69	0.00	0.12
EAS-DS	2026-08-09 00:15:00	14.03	227.59	0.18	7.81	9.74	0.39	0.12
EAS-DS	2026-08-09 00:30:00	13.93	225.78	0.21	7.79	9.76	0.00	0.12
EAS-DS	2026-08-09 00:45:00	13.85	224.49	0.21	7.83	9.85	0.13	0.12
EAS-DS	2026-08-09 01:00:00	13.67	218.69	0.22	7.83	9.97	0.00	0.12
EAS-DS	2026-08-09 01:15:00	13.97	229.75	0.20	7.83	9.70	0.00	0.12
EAS-DS	2026-08-09 01:30:00	14.08	233.35	0.22	7.88	9.79	0.00	0.13
EAS-DS	2026-08-09 01:45:00	13.84	227.01	0.22	7.84	9.77	0.00	0.12
EAS-DS	2026-08-09 02:00:00	13.94	232.27	0.21	7.88	9.87	0.00	0.12
EAS-DS	2026-08-09 02:15:00	14.06	229.37	0.19	7.56	9.02	0.00	0.12
EAS-DS	2026-08-09 02:30:00	13.83	228.36	0.21	7.83	9.83	3.56	0.12
EAS-DS	2026-08-09 02:45:00	13.63	221.24	0.21	7.77	9.78	0.00	0.12
EAS-DS	2026-08-09 03:00:00	13.69	220.11	0.21	7.71	9.47	0.00	0.12
EAS-DS	2026-08-09 03:15:00	13.98	231.82	0.19	7.80	9.64	0.00	0.12
EAS-DS	2026-08-09 03:30:00	13.95	231.65	0.21	7.84	9.82	0.00	0.12
EAS-DS	2026-08-09 03:45:00	13.85	222.32	0.21	7.77	9.44	0.00	0.12
EAS-DS	2026-08-09 04:00:00	13.78	229.62	0.21	7.82	9.81	0.00	0.12
EAS-DS	2026-08-09 04:15:00	13.83	232.11	0.18	7.81	9.68	0.00	0.12
EAS-DS	2026-08-09 04:30:00	13.41	220.43	0.20	7.84	10.01	0.03	0.12
EAS-DS	2026-08-09 04:45:00	13.50	226.59	0.21	7.85	9.99	1.55	0.12
EAS-DS	2026-08-09 05:00:00	13.74	234.91	0.21	7.85	9.73	0.00	0.13
EAS-DS	2026-08-09 05:15:00	13.60	228.82	0.18	7.90	9.97	0.43	0.12
EAS-DS	2026-08-09 05:30:00	13.56	230.71	0.21	7.88	10.00	0.79	0.12
EAS-DS	2026-08-09 05:45:00	13.73	233.93	0.22	7.81	9.72	0.00	0.13
EAS-DS	2026-08-09 06:00:00	13.79	236.31	0.22	7.80	9.69	0.00	0.13
EAS-DS	2026-08-09 06:15:00	13.79	232.45	0.19	7.71	9.31	0.00	0.12
EAS-DS	2026-08-09 06:30:00	13.62	229.97	0.21	7.81	9.80	0.00	0.12
EAS-DS	2026-08-09 06:45:00	13.45	223.42	0.21	7.83	10.00	0.48	0.12
EAS-DS	2026-08-09 07:00:00	13.47	222.83	0.21	7.75	9.73	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-09 07:15:00	13.68	231.76	0.18	7.82	9.77	0.00	0.12
EAS-DS	2026-08-09 07:30:00	13.60	228.00	0.21	7.79	9.77	0.00	0.12
EAS-DS	2026-08-09 07:45:00	13.59	222.58	0.22	7.75	9.57	0.00	0.12
EAS-DS	2026-08-09 08:00:00	13.68	229.52	0.21	7.81	9.75	0.00	0.12
EAS-DS	2026-08-09 08:15:00	13.70	228.15	0.18	7.69	9.45	0.00	0.12
EAS-DS	2026-08-09 08:30:00	13.63	224.04	0.20	7.82	9.83	0.00	0.12
EAS-DS	2026-08-09 08:45:00	13.62	220.61	0.20	7.85	9.97	0.00	0.12
EAS-DS	2026-08-09 09:00:00	13.66	212.08	0.22	7.76	9.60	0.00	0.11
EAS-DS	2026-08-09 09:15:00	13.78	222.96	0.15	7.84	9.76	0.00	0.12
EAS-DS	2026-08-09 09:30:00	13.85	218.92	0.17	7.88	9.88	0.00	0.12
EAS-DS	2026-08-09 09:45:00	13.94	225.19	0.17	7.85	9.68	0.00	0.12
EAS-DS	2026-08-09 10:00:00	13.98	223.27	0.18	7.79	9.34	0.00	0.12
EAS-DS	2026-08-09 10:15:00	14.16	224.60	0.15	7.84	9.61	0.00	0.12
EAS-DS	2026-08-09 10:30:00	14.23	225.11	0.16	7.88	9.68	0.00	0.12
EAS-DS	2026-08-09 10:45:00	14.25	225.34	0.17	7.90	9.81	0.00	0.12
EAS-DS	2026-08-09 11:00:00	14.31	225.91	0.17	7.87	9.76	0.00	0.12
EAS-DS	2026-08-09 11:15:00	14.38	223.38	0.18	7.80	9.62	0.30	0.12
EAS-DS	2026-08-09 11:30:00	14.63	226.88	0.09	7.73	9.65	9.59	0.12
EAS-DS	2026-08-09 11:45:00	14.74	229.90	0.18	7.89	9.68	0.55	0.12
EAS-DS	2026-08-09 12:00:00	14.84	230.98	0.19	7.84	9.60	4.83	0.12
EAS-DS	2026-08-09 12:15:00	14.81	227.43	0.16	7.86	9.69	0.00	0.12
EAS-DS	2026-08-09 12:30:00	14.84	224.61	0.18	7.83	9.58	0.00	0.12
EAS-DS	2026-08-09 12:45:00	15.06	225.06	0.19	7.82	9.51	0.00	0.12
EAS-DS	2026-08-09 13:00:00	15.15	229.57	0.19	7.83	9.50	1.24	0.12
EAS-DS	2026-08-09 13:15:00	15.15	228.12	0.17	7.86	9.44	0.00	0.12
EAS-DS	2026-08-09 13:30:00	15.28	230.32	0.18	7.88	9.55	0.00	0.12
EAS-DS	2026-08-09 13:45:00	15.12	227.89	0.19	7.88	9.58	0.00	0.12
EAS-DS	2026-08-09 14:00:00	15.09	228.47	0.18	7.89	9.61	0.19	0.12
EAS-DS	2026-08-09 14:15:00	15.10	226.85	0.17	7.83	9.53	0.00	0.12
EAS-DS	2026-08-09 14:30:00	15.32	229.65	0.19	7.82	9.45	0.00	0.12
EAS-DS	2026-08-09 14:45:00	15.23	226.48	0.19	7.86	9.59	0.00	0.12
EAS-DS	2026-08-09 15:00:00	14.99	221.99	0.19	7.80	9.49	0.00	0.12
EAS-DS	2026-08-09 15:15:00	15.31	228.00	0.17	7.89	9.49	0.00	0.12
EAS-DS	2026-08-09 15:30:00	15.42	228.59	0.18	7.88	9.59	0.00	0.12
EAS-DS	2026-08-09 15:45:00	14.96	223.83	0.18	7.83	9.57	3.84	0.12
EAS-DS	2026-08-09 16:00:00	14.91	227.60	0.19	7.83	9.55	0.00	0.12
EAS-DS	2026-08-09 16:15:00	15.14	229.55	0.16	7.81	9.39	0.00	0.12
EAS-DS	2026-08-09 16:30:00	14.89	230.75	0.18	7.86	9.64	0.00	0.12
EAS-DS	2026-08-09 16:45:00	14.78	231.64	0.19	7.87	9.68	1.33	0.12
EAS-DS	2026-08-09 17:00:00	14.62	227.94	0.19	7.80	9.57	0.00	0.12
EAS-DS	2026-08-09 17:15:00	15.04	235.02	0.17	7.86	9.41	0.00	0.13
EAS-DS	2026-08-09 17:30:00	15.06	236.62	0.18	7.88	9.51	0.00	0.13
EAS-DS	2026-08-09 17:45:00	14.68	233.60	0.18	7.86	9.60	1.42	0.12
EAS-DS	2026-08-09 18:00:00	14.91	235.57	0.18	7.87	9.50	5.27	0.13
EAS-DS	2026-08-09 18:15:00	14.97	233.58	0.17	7.85	9.47	0.00	0.12
EAS-DS	2026-08-09 18:30:00	14.93	228.94	0.18	7.83	9.50	0.00	0.12
EAS-DS	2026-08-09 18:45:00	15.04	233.30	0.18	7.83	9.46	0.00	0.12
EAS-DS	2026-08-09 19:00:00	14.73	233.00	0.18	7.87	9.68	2.93	0.12
EAS-DS	2026-08-09 19:15:00	14.66	231.11	0.16	7.91	9.74	3.46	0.12
EAS-DS	2026-08-09 19:30:00	14.65	230.39	0.18	7.88	9.73	0.67	0.12
EAS-DS	2026-08-09 19:45:00	14.74	229.42	0.18	7.84	9.53	1.47	0.12
EAS-DS	2026-08-09 20:00:00	14.71	226.21	0.18	7.82	9.47	0.00	0.12
EAS-DS	2026-08-09 20:15:00	14.82	229.42	0.17	7.80	9.43	0.00	0.12
EAS-DS	2026-08-09 20:30:00	14.87	229.46	0.18	7.78	9.42	0.00	0.12
EAS-DS	2026-08-09 20:45:00	14.83	228.45	0.18	7.57	8.77	0.00	0.12

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-09 21:00:00	14.79	227.19	0.18	7.81	9.49	0.00	0.12
EAS-DS	2026-08-09 21:15:00	14.77	221.58	0.17	7.82	9.38	0.00	0.12
EAS-DS	2026-08-09 21:30:00	14.52	225.54	0.18	7.81	9.58	0.00	0.12
EAS-DS	2026-08-09 21:45:00	14.15	223.89	0.18	7.86	9.78	0.36	0.12
EAS-DS	2026-08-09 22:00:00	13.94	221.85	0.18	7.81	9.80	0.00	0.12
EAS-DS	2026-08-09 22:15:00	14.22	227.82	0.17	7.82	9.70	0.00	0.12
EAS-DS	2026-08-09 22:30:00	14.32	232.42	0.19	7.80	9.62	0.00	0.12
EAS-DS	2026-08-09 22:45:00	13.99	230.97	0.17	7.87	9.91	2.59	0.12
EAS-DS	2026-08-09 23:00:00	14.09	233.56	0.18	7.86	9.82	0.00	0.13
EAS-DS	2026-08-09 23:15:00	13.99	225.66	0.17	7.81	9.71	0.00	0.12
EAS-DS	2026-08-09 23:30:00	14.23	237.33	0.18	7.85	9.71	13.05	0.13
EAS-DS	2026-08-09 23:45:00	13.95	228.23	0.19	7.82	9.77	2.59	0.12
EAS-US	2026-08-03 00:00:00	14.81	28.09	0.43	7.20	9.64	9.64	0.01
EAS-US	2026-08-03 00:15:00							
EAS-US	2026-08-03 00:30:00							
EAS-US	2026-08-03 00:45:00							
EAS-US	2026-08-03 01:00:00	14.64	28.00	0.43	7.20	9.69	9.73	0.01
EAS-US	2026-08-03 01:15:00							
EAS-US	2026-08-03 01:30:00							
EAS-US	2026-08-03 01:45:00							
EAS-US	2026-08-03 02:00:00	14.50	27.88	0.44	7.18	9.73	9.53	0.01
EAS-US	2026-08-03 02:15:00							
EAS-US	2026-08-03 02:30:00							
EAS-US	2026-08-03 02:45:00							
EAS-US	2026-08-03 03:00:00	14.33	27.78	0.44	7.19	9.77	9.49	0.01
EAS-US	2026-08-03 03:15:00							
EAS-US	2026-08-03 03:30:00							
EAS-US	2026-08-03 03:45:00							
EAS-US	2026-08-03 04:00:00	14.17	27.64	0.44	7.19	9.82	9.56	0.01
EAS-US	2026-08-03 04:15:00							
EAS-US	2026-08-03 04:30:00							
EAS-US	2026-08-03 04:45:00							
EAS-US	2026-08-03 05:00:00	14.01	27.57	0.44	7.19	9.86	9.50	0.01
EAS-US	2026-08-03 05:15:00							
EAS-US	2026-08-03 05:30:00							
EAS-US	2026-08-03 05:45:00							
EAS-US	2026-08-03 06:00:00	13.87	27.50	0.44	7.19	9.91	9.45	0.01
EAS-US	2026-08-03 06:15:00							
EAS-US	2026-08-03 06:30:00							
EAS-US	2026-08-03 06:45:00							
EAS-US	2026-08-03 07:00:00	13.73	27.38	0.44	7.19	9.97	9.48	0.01
EAS-US	2026-08-03 07:15:00							
EAS-US	2026-08-03 07:30:00							
EAS-US	2026-08-03 07:45:00							
EAS-US	2026-08-03 08:00:00	13.70	27.22	0.44	7.21	10.01	9.47	0.01
EAS-US	2026-08-03 08:15:00							
EAS-US	2026-08-03 08:30:00							
EAS-US	2026-08-03 08:45:00							
EAS-US	2026-08-03 09:00:00	13.79	27.11	0.44	7.21	10.04	9.39	0.01
EAS-US	2026-08-03 09:15:00							
EAS-US	2026-08-03 09:30:00							
EAS-US	2026-08-03 09:45:00							
EAS-US	2026-08-03 10:00:00	13.97	27.00	0.43	7.22	10.07	9.42	0.01
EAS-US	2026-08-03 10:15:00							
EAS-US	2026-08-03 10:30:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-03 10:45:00							
EAS-US	2026-08-03 11:00:00	14.73	26.70	0.42	7.28	10.12	9.45	0.01
EAS-US	2026-08-03 11:15:00							
EAS-US	2026-08-03 11:30:00							
EAS-US	2026-08-03 11:45:00							
EAS-US	2026-08-03 12:00:00	15.50	26.65	0.41	7.29	10.00	9.75	0.01
EAS-US	2026-08-03 12:15:00							
EAS-US	2026-08-03 12:30:00							
EAS-US	2026-08-03 12:45:00							
EAS-US	2026-08-03 13:00:00	15.72	26.79	0.41	7.28	9.77	9.86	0.01
EAS-US	2026-08-03 13:15:00							
EAS-US	2026-08-03 13:30:00							
EAS-US	2026-08-03 13:45:00							
EAS-US	2026-08-03 14:00:00	16.33	26.76	0.41	7.27	9.61	10.12	0.01
EAS-US	2026-08-03 14:15:00							
EAS-US	2026-08-03 14:30:00							
EAS-US	2026-08-03 14:45:00							
EAS-US	2026-08-03 15:00:00	16.85	26.88	0.41	7.26	9.43	10.20	0.01
EAS-US	2026-08-03 15:15:00							
EAS-US	2026-08-03 15:30:00							
EAS-US	2026-08-03 15:45:00							
EAS-US	2026-08-03 16:00:00	17.18	27.00	0.41	7.25	9.33	10.22	0.01
EAS-US	2026-08-03 16:15:00							
EAS-US	2026-08-03 16:30:00							
EAS-US	2026-08-03 16:45:00							
EAS-US	2026-08-03 17:00:00	17.06	27.30	0.42	7.23	9.28	10.14	0.01
EAS-US	2026-08-03 17:15:00							
EAS-US	2026-08-03 17:30:00							
EAS-US	2026-08-03 17:45:00							
EAS-US	2026-08-03 18:00:00	16.83	27.61	0.42	7.20	9.22	10.08	0.01
EAS-US	2026-08-03 18:15:00							
EAS-US	2026-08-03 18:30:00							
EAS-US	2026-08-03 18:45:00							
EAS-US	2026-08-03 19:00:00	16.42	28.12	0.43	7.18	9.25	10.03	0.01
EAS-US	2026-08-03 19:15:00							
EAS-US	2026-08-03 19:30:00							
EAS-US	2026-08-03 19:45:00							
EAS-US	2026-08-03 20:00:00	16.15	28.12	0.43	7.18	9.28	9.91	0.01
EAS-US	2026-08-03 20:15:00							
EAS-US	2026-08-03 20:30:00							
EAS-US	2026-08-03 20:45:00							
EAS-US	2026-08-03 21:00:00	15.94	28.18	0.44	7.18	9.24	9.79	0.01
EAS-US	2026-08-03 21:15:00							
EAS-US	2026-08-03 21:30:00							
EAS-US	2026-08-03 21:45:00							
EAS-US	2026-08-03 22:00:00	15.76	28.18	0.44	7.17	9.31	9.79	0.01
EAS-US	2026-08-03 22:15:00							
EAS-US	2026-08-03 22:30:00							
EAS-US	2026-08-03 22:45:00							
EAS-US	2026-08-03 23:00:00	15.60	28.15	0.45	7.16	9.31	9.70	0.01
EAS-US	2026-08-03 23:15:00							
EAS-US	2026-08-03 23:30:00							
EAS-US	2026-08-03 23:45:00							
EAS-US	2026-08-04 00:00:00	15.44	28.08	0.45	7.16	9.39	9.66	0.01
EAS-US	2026-08-04 00:15:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-04 00:30:00							
EAS-US	2026-08-04 00:45:00							
EAS-US	2026-08-04 01:00:00	15.28	28.02	0.45	7.16	9.42	9.62	0.01
EAS-US	2026-08-04 01:15:00							
EAS-US	2026-08-04 01:30:00							
EAS-US	2026-08-04 01:45:00							
EAS-US	2026-08-04 02:00:00	15.11	27.91	0.45	7.17	9.48	9.56	0.01
EAS-US	2026-08-04 02:15:00							
EAS-US	2026-08-04 02:30:00							
EAS-US	2026-08-04 02:45:00							
EAS-US	2026-08-04 03:00:00	14.98	27.83	0.45	7.17	9.51	9.54	0.01
EAS-US	2026-08-04 03:15:00							
EAS-US	2026-08-04 03:30:00							
EAS-US	2026-08-04 03:45:00							
EAS-US	2026-08-04 04:00:00	14.84	27.73	0.45	7.18	9.55	9.58	0.01
EAS-US	2026-08-04 04:15:00							
EAS-US	2026-08-04 04:30:00							
EAS-US	2026-08-04 04:45:00							
EAS-US	2026-08-04 05:00:00	14.73	27.69	0.45	7.17	9.57	9.46	0.01
EAS-US	2026-08-04 05:15:00							
EAS-US	2026-08-04 05:30:00							
EAS-US	2026-08-04 05:45:00							
EAS-US	2026-08-04 06:00:00	14.60	27.63	0.45	7.18	9.60	9.52	0.01
EAS-US	2026-08-04 06:15:00							
EAS-US	2026-08-04 06:30:00							
EAS-US	2026-08-04 06:45:00							
EAS-US	2026-08-04 07:00:00	14.52	27.53	0.45	7.18	9.67	9.40	0.01
EAS-US	2026-08-04 07:15:00							
EAS-US	2026-08-04 07:30:00							
EAS-US	2026-08-04 07:45:00							
EAS-US	2026-08-04 08:00:00	14.51	27.32	0.45	7.20	9.74	9.44	0.01
EAS-US	2026-08-04 08:15:00							
EAS-US	2026-08-04 08:30:00							
EAS-US	2026-08-04 08:45:00							
EAS-US	2026-08-04 09:00:00	14.61	27.16	0.45	7.21	9.81	9.48	0.01
EAS-US	2026-08-04 09:15:00							
EAS-US	2026-08-04 09:30:00							
EAS-US	2026-08-04 09:45:00							
EAS-US	2026-08-04 10:00:00	14.79	26.95	0.45	7.24	9.86	9.55	0.01
EAS-US	2026-08-04 10:15:00							
EAS-US	2026-08-04 10:30:00							
EAS-US	2026-08-04 10:45:00							
EAS-US	2026-08-04 11:00:00	15.38	26.81	0.45	7.26	9.92	9.56	0.01
EAS-US	2026-08-04 11:15:00							
EAS-US	2026-08-04 11:30:00							
EAS-US	2026-08-04 11:45:00							
EAS-US	2026-08-04 12:00:00	16.02	26.66	0.44	7.31	9.86	9.59	0.01
EAS-US	2026-08-04 12:15:00							
EAS-US	2026-08-04 12:30:00							
EAS-US	2026-08-04 12:45:00							
EAS-US	2026-08-04 13:00:00	16.20	26.74	0.43	7.31	9.75	14.51	0.01
EAS-US	2026-08-04 13:15:00							
EAS-US	2026-08-04 13:30:00							
EAS-US	2026-08-04 13:45:00							
EAS-US	2026-08-04 14:00:00	16.63	26.71	0.44	7.30	9.60	9.82	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-04 14:15:00							
EAS-US	2026-08-04 14:30:00							
EAS-US	2026-08-04 14:45:00							
EAS-US	2026-08-04 15:00:00	16.98	26.85	0.44	7.30	9.46	9.84	0.01
EAS-US	2026-08-04 15:15:00							
EAS-US	2026-08-04 15:30:00							
EAS-US	2026-08-04 15:45:00							
EAS-US	2026-08-04 16:00:00	17.30	27.06	0.43	7.28	9.36	9.83	0.01
EAS-US	2026-08-04 16:15:00							
EAS-US	2026-08-04 16:30:00							
EAS-US	2026-08-04 16:45:00							
EAS-US	2026-08-04 17:00:00	17.25	27.30	0.44	7.26	9.25	9.79	0.01
EAS-US	2026-08-04 17:15:00							
EAS-US	2026-08-04 17:30:00							
EAS-US	2026-08-04 17:45:00							
EAS-US	2026-08-04 18:00:00	17.08	27.67	0.44	7.22	9.18	9.70	0.01
EAS-US	2026-08-04 18:15:00							
EAS-US	2026-08-04 18:30:00							
EAS-US	2026-08-04 18:45:00							
EAS-US	2026-08-04 19:00:00	16.77	28.08	0.44	7.18	9.16	9.73	0.01
EAS-US	2026-08-04 19:15:00							
EAS-US	2026-08-04 19:30:00							
EAS-US	2026-08-04 19:45:00							
EAS-US	2026-08-04 20:00:00	16.51	28.36	0.45	7.17	9.14	9.66	0.01
EAS-US	2026-08-04 20:15:00							
EAS-US	2026-08-04 20:30:00							
EAS-US	2026-08-04 20:45:00							
EAS-US	2026-08-04 21:00:00	16.30	28.62	0.45	7.16	9.13	9.50	0.01
EAS-US	2026-08-04 21:15:00							
EAS-US	2026-08-04 21:30:00							
EAS-US	2026-08-04 21:45:00							
EAS-US	2026-08-04 22:00:00	16.11	28.62	0.45	7.16	9.16	9.57	0.01
EAS-US	2026-08-04 22:15:00							
EAS-US	2026-08-04 22:30:00							
EAS-US	2026-08-04 22:45:00							
EAS-US	2026-08-04 23:00:00	15.95	28.56	0.45	7.15	9.20	9.56	0.01
EAS-US	2026-08-04 23:15:00							
EAS-US	2026-08-04 23:30:00							
EAS-US	2026-08-04 23:45:00							
EAS-US	2026-08-05 00:00:00	15.78	28.35	0.45	7.16	9.25	9.41	0.01
EAS-US	2026-08-05 00:15:00							
EAS-US	2026-08-05 00:30:00							
EAS-US	2026-08-05 00:45:00							
EAS-US	2026-08-05 01:00:00	15.63	28.23	0.45	7.16	9.31	9.51	0.01
EAS-US	2026-08-05 01:15:00							
EAS-US	2026-08-05 01:30:00							
EAS-US	2026-08-05 01:45:00							
EAS-US	2026-08-05 02:00:00	15.47	28.07	0.45	7.16	9.33	9.33	0.01
EAS-US	2026-08-05 02:15:00							
EAS-US	2026-08-05 02:30:00							
EAS-US	2026-08-05 02:45:00							
EAS-US	2026-08-05 03:00:00	15.31	27.99	0.45	7.16	9.38	9.36	0.01
EAS-US	2026-08-05 03:15:00							
EAS-US	2026-08-05 03:30:00							
EAS-US	2026-08-05 03:45:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-05 04:00:00	15.17	27.88	0.45	7.17	9.41	9.39	0.01
EAS-US	2026-08-05 04:15:00							
EAS-US	2026-08-05 04:30:00							
EAS-US	2026-08-05 04:45:00							
EAS-US	2026-08-05 05:00:00	15.03	27.84	0.45	7.16	9.45	9.31	0.01
EAS-US	2026-08-05 05:15:00							
EAS-US	2026-08-05 05:30:00							
EAS-US	2026-08-05 05:45:00							
EAS-US	2026-08-05 06:00:00	14.88	27.74	0.45	7.17	9.47	9.36	0.01
EAS-US	2026-08-05 06:15:00							
EAS-US	2026-08-05 06:30:00							
EAS-US	2026-08-05 06:45:00							
EAS-US	2026-08-05 07:00:00	14.78	27.67	0.45	7.19	9.58	9.52	0.01
EAS-US	2026-08-05 07:15:00							
EAS-US	2026-08-05 07:30:00							
EAS-US	2026-08-05 07:45:00							
EAS-US	2026-08-05 08:00:00	14.77	27.34	0.45	7.21	9.67	9.45	0.01
EAS-US	2026-08-05 08:15:00							
EAS-US	2026-08-05 08:30:00							
EAS-US	2026-08-05 08:45:00							
EAS-US	2026-08-05 09:00:00	14.84	27.17	0.45	7.22	9.76	9.57	0.01
EAS-US	2026-08-05 09:15:00							
EAS-US	2026-08-05 09:30:00							
EAS-US	2026-08-05 09:45:00							
EAS-US	2026-08-05 10:00:00	15.03	27.09	0.45	7.23	9.79	9.58	0.01
EAS-US	2026-08-05 10:15:00							
EAS-US	2026-08-05 10:30:00							
EAS-US	2026-08-05 10:45:00							
EAS-US	2026-08-05 11:00:00	15.66	27.02	0.44	7.28	9.84	9.72	0.01
EAS-US	2026-08-05 11:15:00							
EAS-US	2026-08-05 11:30:00							
EAS-US	2026-08-05 11:45:00							
EAS-US	2026-08-05 12:00:00	16.22	26.88	0.43	7.32	9.77	9.84	0.01
EAS-US	2026-08-05 12:15:00							
EAS-US	2026-08-05 12:30:00							
EAS-US	2026-08-05 12:45:00							
EAS-US	2026-08-05 13:00:00	16.41	26.99	0.43	7.32	9.61	9.90	0.01
EAS-US	2026-08-05 13:15:00							
EAS-US	2026-08-05 13:30:00							
EAS-US	2026-08-05 13:45:00							
EAS-US	2026-08-05 14:00:00	16.97	26.99	0.43	7.31	9.47	9.95	0.01
EAS-US	2026-08-05 14:15:00							
EAS-US	2026-08-05 14:30:00							
EAS-US	2026-08-05 14:45:00							
EAS-US	2026-08-05 15:00:00	17.36	27.04	0.43	7.29	9.30	9.90	0.01
EAS-US	2026-08-05 15:15:00							
EAS-US	2026-08-05 15:30:00							
EAS-US	2026-08-05 15:45:00							
EAS-US	2026-08-05 16:00:00	17.68	27.15	0.43	7.28	9.21	10.05	0.01
EAS-US	2026-08-05 16:15:00							
EAS-US	2026-08-05 16:30:00							
EAS-US	2026-08-05 16:45:00							
EAS-US	2026-08-05 17:00:00	17.64	27.50	0.44	7.25	9.14	10.01	0.01
EAS-US	2026-08-05 17:15:00							
EAS-US	2026-08-05 17:30:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-05 17:45:00							
EAS-US	2026-08-05 18:00:00	17.44	27.83	0.44	7.21	9.05	9.92	0.01
EAS-US	2026-08-05 18:15:00							
EAS-US	2026-08-05 18:30:00							
EAS-US	2026-08-05 18:45:00							
EAS-US	2026-08-05 19:00:00	17.12	28.23	0.44	7.18	9.04	9.77	0.01
EAS-US	2026-08-05 19:15:00							
EAS-US	2026-08-05 19:30:00							
EAS-US	2026-08-05 19:45:00							
EAS-US	2026-08-05 20:00:00	16.85	28.51	0.45	7.17	9.03	9.71	0.01
EAS-US	2026-08-05 20:15:00							
EAS-US	2026-08-05 20:30:00							
EAS-US	2026-08-05 20:45:00							
EAS-US	2026-08-05 21:00:00	16.64	28.69	0.45	7.17	9.04	9.71	0.01
EAS-US	2026-08-05 21:15:00							
EAS-US	2026-08-05 21:30:00							
EAS-US	2026-08-05 21:45:00							
EAS-US	2026-08-05 22:00:00	16.48	28.73	0.45	7.17	9.07	9.65	0.01
EAS-US	2026-08-05 22:15:00							
EAS-US	2026-08-05 22:30:00							
EAS-US	2026-08-05 22:45:00							
EAS-US	2026-08-05 23:00:00	16.31	28.72	0.45	7.16	9.11	9.77	0.01
EAS-US	2026-08-05 23:15:00							
EAS-US	2026-08-05 23:30:00							
EAS-US	2026-08-05 23:45:00							
EAS-US	2026-08-06 00:00:00	16.14	28.47	0.45	7.16	9.16	9.52	0.01
EAS-US	2026-08-06 00:15:00							
EAS-US	2026-08-06 00:30:00							
EAS-US	2026-08-06 00:45:00							
EAS-US	2026-08-06 01:00:00	15.99	28.31	0.45	7.16	9.21	9.52	0.01
EAS-US	2026-08-06 01:15:00							
EAS-US	2026-08-06 01:30:00							
EAS-US	2026-08-06 01:45:00							
EAS-US	2026-08-06 02:00:00	15.86	28.14	0.45	7.17	9.24	9.50	0.01
EAS-US	2026-08-06 02:15:00							
EAS-US	2026-08-06 02:30:00							
EAS-US	2026-08-06 02:45:00							
EAS-US	2026-08-06 03:00:00	15.70	28.10	0.45	7.17	9.29	9.54	0.01
EAS-US	2026-08-06 03:15:00							
EAS-US	2026-08-06 03:30:00							
EAS-US	2026-08-06 03:45:00							
EAS-US	2026-08-06 04:00:00	15.56	27.94	0.45	7.17	9.32	9.55	0.01
EAS-US	2026-08-06 04:15:00							
EAS-US	2026-08-06 04:30:00							
EAS-US	2026-08-06 04:45:00							
EAS-US	2026-08-06 05:00:00	15.41	27.91	0.45	7.17	9.37	9.50	0.01
EAS-US	2026-08-06 05:15:00							
EAS-US	2026-08-06 05:30:00							
EAS-US	2026-08-06 05:45:00							
EAS-US	2026-08-06 06:00:00	15.29	27.80	0.45	7.18	9.40	9.46	0.01
EAS-US	2026-08-06 06:15:00							
EAS-US	2026-08-06 06:30:00							
EAS-US	2026-08-06 06:45:00							
EAS-US	2026-08-06 07:00:00	15.19	27.69	0.45	7.19	9.48	9.49	0.01
EAS-US	2026-08-06 07:15:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-06 07:30:00							
EAS-US	2026-08-06 07:45:00							
EAS-US	2026-08-06 08:00:00	15.13	27.47	0.45	7.20	9.55	9.57	0.01
EAS-US	2026-08-06 08:15:00							
EAS-US	2026-08-06 08:30:00							
EAS-US	2026-08-06 08:45:00							
EAS-US	2026-08-06 09:00:00	15.18	27.38	0.45	7.21	9.64	9.45	0.01
EAS-US	2026-08-06 09:15:00							
EAS-US	2026-08-06 09:30:00							
EAS-US	2026-08-06 09:45:00							
EAS-US	2026-08-06 10:00:00	15.36	27.36	0.45	7.22	9.68	9.42	0.01
EAS-US	2026-08-06 10:15:00							
EAS-US	2026-08-06 10:30:00							
EAS-US	2026-08-06 10:45:00							
EAS-US	2026-08-06 11:00:00	16.06	27.06	0.44	7.29	9.78	9.47	0.01
EAS-US	2026-08-06 11:15:00							
EAS-US	2026-08-06 11:30:00							
EAS-US	2026-08-06 11:45:00							
EAS-US	2026-08-06 12:00:00	16.79	26.97	0.42	7.32	9.70	9.60	0.01
EAS-US	2026-08-06 12:15:00							
EAS-US	2026-08-06 12:30:00							
EAS-US	2026-08-06 12:45:00							
EAS-US	2026-08-06 13:00:00	16.96	27.03	0.42	7.31	9.51	9.67	0.01
EAS-US	2026-08-06 13:15:00							
EAS-US	2026-08-06 13:30:00							
EAS-US	2026-08-06 13:45:00							
EAS-US	2026-08-06 14:00:00	17.52	26.91	0.43	7.30	9.35	9.79	0.01
EAS-US	2026-08-06 14:15:00							
EAS-US	2026-08-06 14:30:00							
EAS-US	2026-08-06 14:45:00							
EAS-US	2026-08-06 15:00:00	17.97	27.16	0.43	7.28	9.17	9.87	0.01
EAS-US	2026-08-06 15:15:00							
EAS-US	2026-08-06 15:30:00							
EAS-US	2026-08-06 15:45:00							
EAS-US	2026-08-06 16:00:00	18.29	27.32	0.43	7.27	9.08	9.86	0.01
EAS-US	2026-08-06 16:15:00							
EAS-US	2026-08-06 16:30:00							
EAS-US	2026-08-06 16:45:00							
EAS-US	2026-08-06 17:00:00	18.21	27.56	0.43	7.25	9.01	9.93	0.01
EAS-US	2026-08-06 17:15:00							
EAS-US	2026-08-06 17:30:00							
EAS-US	2026-08-06 17:45:00							
EAS-US	2026-08-06 18:00:00	17.97	27.94	0.44	7.20	8.93	9.81	0.01
EAS-US	2026-08-06 18:15:00							
EAS-US	2026-08-06 18:30:00							
EAS-US	2026-08-06 18:45:00							
EAS-US	2026-08-06 19:00:00	17.60	28.39	0.44	7.18	8.91	9.76	0.01
EAS-US	2026-08-06 19:15:00							
EAS-US	2026-08-06 19:30:00							
EAS-US	2026-08-06 19:45:00							
EAS-US	2026-08-06 20:00:00	17.28	28.58	0.44	7.16	8.93	9.66	0.01
EAS-US	2026-08-06 20:15:00							
EAS-US	2026-08-06 20:30:00							
EAS-US	2026-08-06 20:45:00							
EAS-US	2026-08-06 21:00:00	17.04	28.86	0.45	7.16	8.95	9.62	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-06 21:15:00							
EAS-US	2026-08-06 21:30:00							
EAS-US	2026-08-06 21:45:00							
EAS-US	2026-08-06 22:00:00	16.85	28.82	0.45	7.16	8.98	9.54	0.01
EAS-US	2026-08-06 22:15:00							
EAS-US	2026-08-06 22:30:00							
EAS-US	2026-08-06 22:45:00							
EAS-US	2026-08-06 23:00:00	16.68	28.85	0.45	7.16	9.04	9.50	0.01
EAS-US	2026-08-06 23:15:00							
EAS-US	2026-08-06 23:30:00							
EAS-US	2026-08-06 23:45:00							
EAS-US	2026-08-07 00:00:00	16.53	28.59	0.45	7.16	9.09	9.49	0.01
EAS-US	2026-08-07 00:15:00							
EAS-US	2026-08-07 00:30:00							
EAS-US	2026-08-07 00:45:00							
EAS-US	2026-08-07 01:00:00	16.38	28.46	0.45	7.16	9.13	9.54	0.01
EAS-US	2026-08-07 01:15:00							
EAS-US	2026-08-07 01:30:00							
EAS-US	2026-08-07 01:45:00							
EAS-US	2026-08-07 02:00:00	16.25	28.28	0.45	7.16	9.17	9.45	0.01
EAS-US	2026-08-07 02:15:00							
EAS-US	2026-08-07 02:30:00							
EAS-US	2026-08-07 02:45:00							
EAS-US	2026-08-07 03:00:00	16.12	28.42	0.45	7.16	9.19	9.41	0.01
EAS-US	2026-08-07 03:15:00							
EAS-US	2026-08-07 03:30:00							
EAS-US	2026-08-07 03:45:00							
EAS-US	2026-08-07 04:00:00	16.00	28.14	0.45	7.16	9.22	9.33	0.01
EAS-US	2026-08-07 04:15:00							
EAS-US	2026-08-07 04:30:00							
EAS-US	2026-08-07 04:45:00							
EAS-US	2026-08-07 05:00:00	15.89	28.10	0.45	7.17	9.26	9.36	0.01
EAS-US	2026-08-07 05:15:00							
EAS-US	2026-08-07 05:30:00							
EAS-US	2026-08-07 05:45:00							
EAS-US	2026-08-07 06:00:00	15.77	27.97	0.45	7.17	9.30	9.36	0.01
EAS-US	2026-08-07 06:15:00							
EAS-US	2026-08-07 06:30:00							
EAS-US	2026-08-07 06:45:00							
EAS-US	2026-08-07 07:00:00	15.67	27.90	0.45	7.18	9.37	9.38	0.01
EAS-US	2026-08-07 07:15:00							
EAS-US	2026-08-07 07:30:00							
EAS-US	2026-08-07 07:45:00							
EAS-US	2026-08-07 08:00:00	15.62	27.67	0.45	7.19	9.45	9.35	0.01
EAS-US	2026-08-07 08:15:00							
EAS-US	2026-08-07 08:30:00							
EAS-US	2026-08-07 08:45:00							
EAS-US	2026-08-07 09:00:00	15.67	27.71	0.45	7.20	9.51	9.35	0.01
EAS-US	2026-08-07 09:15:00							
EAS-US	2026-08-07 09:30:00							
EAS-US	2026-08-07 09:45:00							
EAS-US	2026-08-07 10:00:00	15.81	27.52	0.45	7.22	9.56	9.37	0.01
EAS-US	2026-08-07 10:15:00							
EAS-US	2026-08-07 10:30:00							
EAS-US	2026-08-07 10:45:00							


Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-07 11:00:00	16.57	27.30	0.44	7.29	9.68	9.33	0.01
EAS-US	2026-08-07 11:15:00							
EAS-US	2026-08-07 11:30:00							
EAS-US	2026-08-07 11:45:00							
EAS-US	2026-08-07 12:00:00	17.40	27.13	0.42	7.33	9.60	9.48	0.01
EAS-US	2026-08-07 12:15:00							
EAS-US	2026-08-07 12:30:00							
EAS-US	2026-08-07 12:45:00							
EAS-US	2026-08-07 13:00:00	17.60	27.15	0.42	7.31	9.39	9.58	0.01
EAS-US	2026-08-07 13:15:00							
EAS-US	2026-08-07 13:30:00							
EAS-US	2026-08-07 13:45:00							
EAS-US	2026-08-07 14:00:00	18.13	27.01	0.43	7.30	9.23	9.71	0.01
EAS-US	2026-08-07 14:15:00							
EAS-US	2026-08-07 14:30:00							
EAS-US	2026-08-07 14:45:00							
EAS-US	2026-08-07 15:00:00	18.55	27.13	0.43	7.29	9.06	9.64	0.01
EAS-US	2026-08-07 15:15:00							
EAS-US	2026-08-07 15:30:00							
EAS-US	2026-08-07 15:45:00							
EAS-US	2026-08-07 16:00:00	18.80	27.20	0.43	7.28	8.99	9.68	0.01
EAS-US	2026-08-07 16:15:00							
EAS-US	2026-08-07 16:30:00							
EAS-US	2026-08-07 16:45:00							
EAS-US	2026-08-07 17:00:00	18.69	27.49	0.43	7.26	8.93	9.68	0.01
EAS-US	2026-08-07 17:15:00							
EAS-US	2026-08-07 17:30:00							
EAS-US	2026-08-07 17:45:00							
EAS-US	2026-08-07 18:00:00	18.38	27.84	0.43	7.22	8.83	9.65	0.01
EAS-US	2026-08-07 18:15:00							
EAS-US	2026-08-07 18:30:00							
EAS-US	2026-08-07 18:45:00							
EAS-US	2026-08-07 19:00:00	17.99	28.29	0.44	7.18	8.82	9.43	0.01
EAS-US	2026-08-07 19:15:00							
EAS-US	2026-08-07 19:30:00							
EAS-US	2026-08-07 19:45:00							
EAS-US	2026-08-07 20:00:00	17.63	28.49	0.44	7.18	8.86	9.50	0.01
EAS-US	2026-08-07 20:15:00							
EAS-US	2026-08-07 20:30:00							
EAS-US	2026-08-07 20:45:00							
EAS-US	2026-08-07 21:00:00	17.34	28.68	0.45	7.17	8.91	9.33	0.01
EAS-US	2026-08-07 21:15:00							
EAS-US	2026-08-07 21:30:00							
EAS-US	2026-08-07 21:45:00							
EAS-US	2026-08-07 22:00:00	17.11	28.68	0.45	7.17	8.94	9.34	0.01
EAS-US	2026-08-07 22:15:00							
EAS-US	2026-08-07 22:30:00							
EAS-US	2026-08-07 22:45:00							
EAS-US	2026-08-07 23:00:00	16.92	28.63	0.45	7.16	9.00	9.21	0.01
EAS-US	2026-08-07 23:15:00							
EAS-US	2026-08-07 23:30:00							
EAS-US	2026-08-07 23:45:00							
EAS-US	2026-08-08 00:00:00	16.74	28.47	0.45	7.16	9.04	9.25	0.01
EAS-US	2026-08-08 00:15:00							
EAS-US	2026-08-08 00:30:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-08 00:45:00							
EAS-US	2026-08-08 01:00:00	16.57	28.39	0.45	7.17	9.11	9.21	0.01
EAS-US	2026-08-08 01:15:00							
EAS-US	2026-08-08 01:30:00							
EAS-US	2026-08-08 01:45:00							
EAS-US	2026-08-08 02:00:00	16.40	28.23	0.45	7.17	9.15	9.25	0.01
EAS-US	2026-08-08 02:15:00							
EAS-US	2026-08-08 02:30:00							
EAS-US	2026-08-08 02:45:00							
EAS-US	2026-08-08 03:00:00	16.25	28.15	0.45	7.17	9.19	9.19	0.01
EAS-US	2026-08-08 03:15:00							
EAS-US	2026-08-08 03:30:00							
EAS-US	2026-08-08 03:45:00							
EAS-US	2026-08-08 04:00:00	16.09	28.03	0.45	7.17	8.93	9.22	0.01
EAS-US	2026-08-08 04:15:00							
EAS-US	2026-08-08 04:30:00							
EAS-US	2026-08-08 04:45:00							
EAS-US	2026-08-08 05:00:00	15.94	28.00	0.45	7.18	9.27	9.16	0.01
EAS-US	2026-08-08 05:15:00							
EAS-US	2026-08-08 05:30:00							
EAS-US	2026-08-08 05:45:00							
EAS-US	2026-08-08 06:00:00	15.82	27.89	0.45	7.18	9.31	9.11	0.01
EAS-US	2026-08-08 06:15:00							
EAS-US	2026-08-08 06:30:00							
EAS-US	2026-08-08 06:45:00							
EAS-US	2026-08-08 07:00:00	15.73	27.74	0.45	7.19	9.38	9.13	0.01
EAS-US	2026-08-08 07:15:00							
EAS-US	2026-08-08 07:30:00							
EAS-US	2026-08-08 07:45:00							
EAS-US	2026-08-08 08:00:00	15.75	27.54	0.45	7.20	9.48	9.39	0.01
EAS-US	2026-08-08 08:15:00							
EAS-US	2026-08-08 08:30:00							
EAS-US	2026-08-08 08:45:00							
EAS-US	2026-08-08 09:00:00	15.85	27.67	0.45	7.20	9.53	8.41	0.01
EAS-US	2026-08-08 09:15:00							
EAS-US	2026-08-08 09:30:00							
EAS-US	2026-08-08 09:45:00							
EAS-US	2026-08-08 10:00:00	15.98	27.35	0.44	7.23	9.64	8.44	0.01
EAS-US	2026-08-08 10:15:00							
EAS-US	2026-08-08 10:30:00							
EAS-US	2026-08-08 10:45:00							
EAS-US	2026-08-08 11:00:00	16.54	27.07	0.41	7.27	9.87	8.32	0.01
EAS-US	2026-08-08 11:15:00							
EAS-US	2026-08-08 11:30:00							
EAS-US	2026-08-08 11:45:00							
EAS-US	2026-08-08 12:00:00	17.75	26.90	0.39	7.33	9.84	8.58	0.01
EAS-US	2026-08-08 12:15:00							
EAS-US	2026-08-08 12:30:00							
EAS-US	2026-08-08 12:45:00							
EAS-US	2026-08-08 13:00:00	18.22	27.17	0.41	7.36	9.58	8.79	0.01
EAS-US	2026-08-08 13:15:00							
EAS-US	2026-08-08 13:30:00							
EAS-US	2026-08-08 13:45:00							
EAS-US	2026-08-08 14:00:00	18.60	27.12	0.41	7.34	9.38	8.82	0.01
EAS-US	2026-08-08 14:15:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-08 14:30:00							
EAS-US	2026-08-08 14:45:00							
EAS-US	2026-08-08 15:00:00	18.97	27.22	0.42	7.31	9.23	8.85	0.01
EAS-US	2026-08-08 15:15:00							
EAS-US	2026-08-08 15:30:00							
EAS-US	2026-08-08 15:45:00							
EAS-US	2026-08-08 16:00:00	19.31	27.28	0.42	7.31	9.09	8.88	0.01
EAS-US	2026-08-08 16:15:00							
EAS-US	2026-08-08 16:30:00							
EAS-US	2026-08-08 16:45:00							
EAS-US	2026-08-08 17:00:00	19.12	27.70	0.42	7.28	8.97	8.72	0.01
EAS-US	2026-08-08 17:15:00							
EAS-US	2026-08-08 17:30:00							
EAS-US	2026-08-08 17:45:00							
EAS-US	2026-08-08 18:00:00	18.78	28.01	0.43	7.25	8.83	8.56	0.01
EAS-US	2026-08-08 18:15:00							
EAS-US	2026-08-08 18:30:00							
EAS-US	2026-08-08 18:45:00							
EAS-US	2026-08-08 19:00:00	18.31	28.50	0.44	7.20	8.72	8.57	0.01
EAS-US	2026-08-08 19:15:00							
EAS-US	2026-08-08 19:30:00							
EAS-US	2026-08-08 19:45:00							
EAS-US	2026-08-08 20:00:00	17.93	28.77	0.44	7.16	8.66	8.44	0.01
EAS-US	2026-08-08 20:15:00							
EAS-US	2026-08-08 20:30:00							
EAS-US	2026-08-08 20:45:00							
EAS-US	2026-08-08 21:00:00	17.61	28.94	0.44	7.14	8.68	8.37	0.01
EAS-US	2026-08-08 21:15:00							
EAS-US	2026-08-08 21:30:00							
EAS-US	2026-08-08 21:45:00							
EAS-US	2026-08-08 22:00:00	17.31	29.02	0.44	7.15	8.74	8.33	0.01
EAS-US	2026-08-08 22:15:00							
EAS-US	2026-08-08 22:30:00							
EAS-US	2026-08-08 22:45:00							
EAS-US	2026-08-08 23:00:00	17.05	28.90	0.45	7.14	8.81	8.37	0.01
EAS-US	2026-08-08 23:15:00							
EAS-US	2026-08-08 23:30:00							
EAS-US	2026-08-08 23:45:00							
EAS-US	2026-08-09 00:00:00	16.82	28.87	0.45	7.14	8.87	8.19	0.01
EAS-US	2026-08-09 00:15:00							
EAS-US	2026-08-09 00:30:00							
EAS-US	2026-08-09 00:45:00							
EAS-US	2026-08-09 01:00:00	16.60	28.53	0.45	7.14	8.93	8.18	0.01
EAS-US	2026-08-09 01:15:00							
EAS-US	2026-08-09 01:30:00							
EAS-US	2026-08-09 01:45:00							
EAS-US	2026-08-09 02:00:00	16.40	28.38	0.45	7.15	8.99	8.19	0.01
EAS-US	2026-08-09 02:15:00							
EAS-US	2026-08-09 02:30:00							
EAS-US	2026-08-09 02:45:00							
EAS-US	2026-08-09 03:00:00	16.19	28.27	0.45	7.14	9.08	8.17	0.01
EAS-US	2026-08-09 03:15:00							
EAS-US	2026-08-09 03:30:00							
EAS-US	2026-08-09 03:45:00							
EAS-US	2026-08-09 04:00:00	16.00	28.21	0.45	7.16	9.12	8.10	0.01

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-09 04:15:00							
EAS-US	2026-08-09 04:30:00							
EAS-US	2026-08-09 04:45:00							
EAS-US	2026-08-09 05:00:00	15.83	28.01	0.45	7.16	9.18	8.15	0.01
EAS-US	2026-08-09 05:15:00							
EAS-US	2026-08-09 05:30:00							
EAS-US	2026-08-09 05:45:00							
EAS-US	2026-08-09 06:00:00	15.66	27.93	0.45	7.16	9.20	8.17	0.01
EAS-US	2026-08-09 06:15:00							
EAS-US	2026-08-09 06:30:00							
EAS-US	2026-08-09 06:45:00							
EAS-US	2026-08-09 07:00:00	15.51	27.82	0.45	7.17	9.29	8.10	0.01
EAS-US	2026-08-09 07:15:00							
EAS-US	2026-08-09 07:30:00							
EAS-US	2026-08-09 07:45:00							
EAS-US	2026-08-09 08:00:00	15.44	27.62	0.45	7.18	9.39	8.11	0.01
EAS-US	2026-08-09 08:15:00							
EAS-US	2026-08-09 08:30:00							
EAS-US	2026-08-09 08:45:00							
EAS-US	2026-08-09 09:00:00	15.47	27.47	0.44	7.19	9.52	8.14	0.01
EAS-US	2026-08-09 09:15:00							
EAS-US	2026-08-09 09:30:00							
EAS-US	2026-08-09 09:45:00							
EAS-US	2026-08-09 10:00:00	15.63	27.12	0.44	7.23	9.69	8.17	0.01
EAS-US	2026-08-09 10:15:00							
EAS-US	2026-08-09 10:30:00							
EAS-US	2026-08-09 10:45:00							
EAS-US	2026-08-09 11:00:00	16.11	26.66	0.42	7.29	9.91	8.17	0.01
EAS-US	2026-08-09 11:15:00							
EAS-US	2026-08-09 11:30:00							
EAS-US	2026-08-09 11:45:00							
EAS-US	2026-08-09 12:00:00	17.07	26.67	0.41	7.32	9.65	9.49	0.01
EAS-US	2026-08-09 12:15:00							
EAS-US	2026-08-09 12:30:00							
EAS-US	2026-08-09 12:45:00							
EAS-US	2026-08-09 13:00:00	17.21	26.51	0.42	7.33	9.64	8.94	0.01
EAS-US	2026-08-09 13:15:00							
EAS-US	2026-08-09 13:30:00							
EAS-US	2026-08-09 13:45:00							
EAS-US	2026-08-09 14:00:00	17.51	26.56	0.42	7.35	9.55	8.91	0.01
EAS-US	2026-08-09 14:15:00							
EAS-US	2026-08-09 14:30:00							
EAS-US	2026-08-09 14:45:00							
EAS-US	2026-08-09 15:00:00	17.54	26.65	0.43	7.33	9.46	8.85	0.01
EAS-US	2026-08-09 15:15:00							
EAS-US	2026-08-09 15:30:00							
EAS-US	2026-08-09 15:45:00							
EAS-US	2026-08-09 16:00:00	17.54	26.77	0.43	7.32	9.32	8.90	0.01
EAS-US	2026-08-09 16:15:00							
EAS-US	2026-08-09 16:30:00							
EAS-US	2026-08-09 16:45:00							
EAS-US	2026-08-09 17:00:00	17.46	27.23	0.43	7.31	9.40	8.91	0.01
EAS-US	2026-08-09 17:15:00							
EAS-US	2026-08-09 17:30:00							
EAS-US	2026-08-09 17:45:00							

Woodfibre LNG (East Creek)								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-09 18:00:00	17.29	27.67	0.44	7.26	9.06	8.76	0.01
EAS-US	2026-08-09 18:15:00							
EAS-US	2026-08-09 18:30:00							
EAS-US	2026-08-09 18:45:00							
EAS-US	2026-08-09 19:00:00	17.17	27.93	0.45	7.25	9.14	8.71	0.01
EAS-US	2026-08-09 19:15:00							
EAS-US	2026-08-09 19:30:00							
EAS-US	2026-08-09 19:45:00							
EAS-US	2026-08-09 20:00:00	17.01	28.40	0.45	7.21	9.00	8.69	0.01
EAS-US	2026-08-09 20:15:00							
EAS-US	2026-08-09 20:30:00							
EAS-US	2026-08-09 20:45:00							
EAS-US	2026-08-09 21:00:00	16.82	29.04	0.46	7.18	8.71	8.62	0.01
EAS-US	2026-08-09 21:15:00							
EAS-US	2026-08-09 21:30:00							
EAS-US	2026-08-09 21:45:00							
EAS-US	2026-08-09 22:00:00	16.64	28.92	0.46	7.17	8.91	8.78	0.01
EAS-US	2026-08-09 22:15:00							
EAS-US	2026-08-09 22:30:00							
EAS-US	2026-08-09 22:45:00							
EAS-US	2026-08-09 23:00:00	16.49	28.78	0.46	7.17	8.98	8.68	0.01
EAS-US	2026-08-09 23:15:00							
EAS-US	2026-08-09 23:30:00							
EAS-US	2026-08-09 23:45:00							

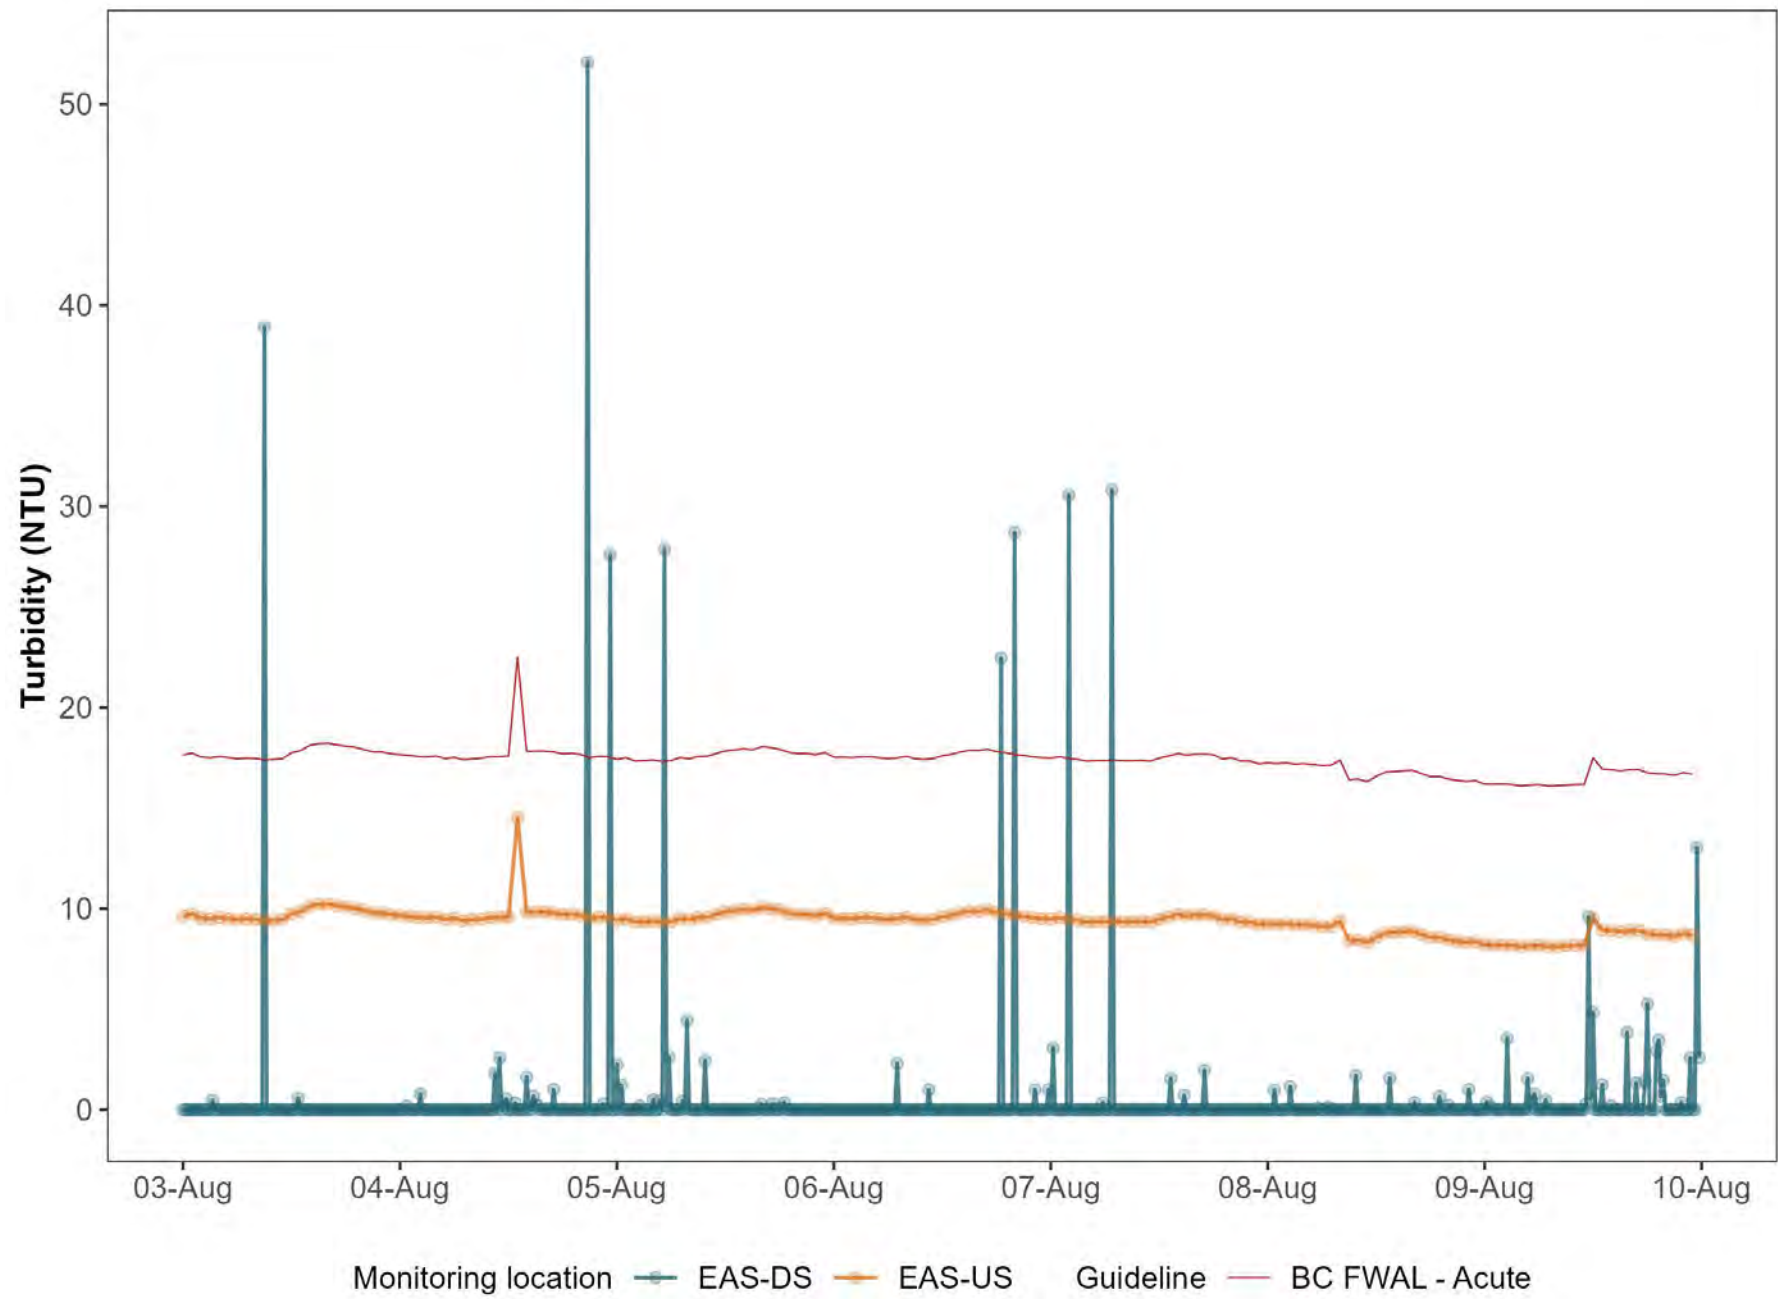

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 03 to August 09, 2026
	Report #	124
	Appendix E	E-1

Appendix E:
Lab Documentation



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 137689

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/08/13
 Report #: R3816379
 Version: 1 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C649494

Received: 2026/08/05, 16:42

Sample Matrix: Water
 # Samples Received: 5

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
Alkalinity @25C (pp, total), CO ₃ ,HCO ₃ ,OH	5	N/A	2026/08/07	BBY6SOP-00026	SM 24 2320 B m
Chloride/Sulphate by Auto Colourimetry	5	N/A	2026/08/06	BBY6SOP-00011 / BBY6SOP-00017	SM24-4500-Cl/SO ₄ -E m
Chromium III (Calc'd)	3	N/A	2026/08/11		
Chromium III (Calc'd)	2	N/A	2026/08/12		
Total Hexavalent Chromium	5	N/A	2026/08/11	BBY6SOP-00054	SM 24 3500-Cr B m
Carbon (DOC) -Lab Filtered (2)	5	N/A	2026/08/08	BBY6SOP-00053	SM 24 5310 B m
Fluoride	5	N/A	2026/08/06	BBY6SOP-00037	SM 24 4500-F C m
Glycols in Water by GC/FID (1)	1	N/A	2026/08/10	CAL SOP-00093	BCMOE Glycols 09/17
Sulphide (as H ₂ S) (1)	5	N/A	2026/08/11		Auto Calc
Un-ionized Hydrogen Sulphide as S Calc	3	N/A	2026/08/11	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	3	N/A	2026/08/11	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	2	N/A	2026/08/12	BBY WI-00033	Auto Calc
Hardness (calculated as CaCO ₃)	5	N/A	2026/08/10	BBY WI-00033	Auto Calc
Mercury (Dissolved) by CV-Lab Filtered	5	2026/08/12	2026/08/12	BBY7SOP-00032	BCMOE LMAug2023 C m
Mercury (Total) by CV	5	2026/08/07	2026/08/07	BBY7SOP-00032	BCMOE LMAug2023 C m
Bromide as Bromine (Br) by ICPMS	5	N/A	2026/08/12	BBY7SOP-00002	EPA 6020B R2 m
EPH in Water when PAH required	1	2026/08/07	2026/08/07	BBY8SOP-00029	BCMOE BCLM Sep2017 m
Na, K, Ca, Mg, S by CRC ICPMS (diss.)	5	N/A	2026/08/10	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (lab filter) (4)	5	N/A	2026/08/07	BBY7SOP-00002	EPA 6020b R2 m
Elements by ICPMS Digested LL (total)	2	2026/08/10	2026/08/11	BBY7SOP-00003 / BBY7SOP-00002	EPA 6020b R2 m
Na, K, Ca, Mg, S by CRC ICPMS (total)	3	N/A	2026/08/11	BBY WI-00033	Auto Calc
Na, K, Ca, Mg, S by CRC ICPMS (total)	2	N/A	2026/08/12	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (total)	3	N/A	2026/08/10	BBY7SOP-00002	EPA 6020b R2 m
Nitrogen (Total)	5	N/A	2026/08/10	BBY6SOP-00016	SM 24 4500-N C m
Ammonia-N (Total)	5	N/A	2026/08/06	AB SOP-00007	SM 24 4500-NH ₃ A G m
Nitrate + Nitrite (N)	5	N/A	2026/08/06	BBY6SOP-00010	SM 24 4500-NO ₃ - H m
Nitrite (N) Regular Level Water	5	N/A	2026/08/06	BBY6SOP-00010	SM 24 4500-NO ₂ - m
Nitrogen - Nitrate (as N)	5	N/A	2026/08/07	BBY WI-00033	Auto Calc
PAH in Water by GC/MS (SIM)	1	2026/08/07	2026/08/07	BBY8SOP-00021	BCMOE BCLM Jul2017m



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 137689

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/08/13
 Report #: R3816379
 Version: 1 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C649494

Received: 2026/08/05, 16:42

Sample Matrix: Water
 # Samples Received: 5

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
Total LMW, HMW, Total PAH Calc (5)	1	N/A	2026/08/10	BBY WI-00033	Auto Calc
pH @25°C (6)	5	N/A	2026/08/07	BBY6SOP-00026	SM 24 4500-H+ B m
Phenols (4-AAP) (1)	1	N/A	2026/08/10	AB SOP-00088	EPA 9066 R0 m
Total Sulphide (1)	5	2026/08/10	2026/08/11	AB SOP-00080	SM 24 4500 S2-A D Fm
Total Dissolved Solids (Filt. Residue)	3	2026/08/11	2026/08/12	BBY6SOP-00033	SM 24 2540 C m
Total Dissolved Solids (Filt. Residue)	2	2026/08/07	2026/08/08	BBY6SOP-00033	SM 24 2540 C m
EPH less PAH in Water by GC/FID (7)	1	N/A	2026/08/10	BBY WI-00033	Auto Calc
Carbon (Total Organic) (8)	5	N/A	2026/08/07	BBY6SOP-00053	SM 24 5310 B m
Total Phosphorus Low Level Total	5	2026/08/10	2026/08/12	BBY6SOP-00013	SM 24 4500-P E m
Total Suspended Solids (NFR)	3	2026/08/11	2026/08/12	BBY6SOP-00034	SM 24 2540 D m
Total Suspended Solids (NFR)	2	2026/08/06	2026/08/07	BBY6SOP-00034	SM 24 2540 D m
Field pH	3	N/A	2026/08/06	Field Test	Field Test
Field Temperature	3	N/A	2026/08/06	Field Test	Field Test
VOCs, VH, F1, LH in Water by HS GC/MS	1	N/A	2026/08/07	BBY8SOP-00009 / BBY8SOP-00011 / BBY8SOP-00012	BCMOE BCLM Jul2017 m
Volatile HC-BTEX (9)	1	N/A	2026/08/07	BBY WI-00033	Auto Calc

Remarks:

Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation. Unless otherwise noted, procedures used by Bureau Veritas are based upon recognized Provincial, Federal or US method compendia such as CCME, EPA, APHA or the Quebec Ministry of Environment.

All work recorded herein has been done in accordance with procedures and practices ordinarily exercised by professionals in Bureau Veritas' profession using accepted testing methodologies, quality assurance and quality control procedures (except where otherwise agreed by the client and Bureau Veritas in writing). All data is in statistical control and has met quality control and method performance criteria unless otherwise noted. All method blanks are reported; unless indicated otherwise, associated sample data are not blank corrected. Where applicable, unless otherwise noted, Measurement Uncertainty has not been accounted for when stating conformity to the referenced standard.

Bureau Veritas liability is limited to the actual cost of the requested analyses, unless otherwise agreed in writing. There is no other warranty expressed or implied. Bureau Veritas has been retained to provide analysis of samples provided by the Client using the testing methodology referenced in this report. Interpretation and use of test results are the sole responsibility of the Client and are not within the scope of services provided by Bureau Veritas, unless otherwise agreed in writing. Bureau Veritas is not responsible for the accuracy or any data impacts, that result from the information provided by the customer or their agent.



Your P.O. #: 4800010213
Your Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your C.O.C. #: 137689

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
N. VANCOUVER
200-850 Harbourside Dr
North Vancouver, BC
Canada V7P 0A3

Report Date: 2026/08/13
Report #: R3816379
Version: 1 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C649494

Received: 2026/08/05, 16:42

Solid sample results, except biota, are based on dry weight unless otherwise indicated. Organic analyses are not recovery corrected except for isotope dilution methods.

Results relate to samples tested. When sampling is not conducted by Bureau Veritas, results relate to the supplied samples tested.

This Certificate shall not be reproduced except in full, without the written approval of the laboratory.

Reference Method suffix "m" indicates test methods incorporate validated modifications from specific reference methods to improve performance.

* RPDs calculated using raw data. The rounding of final results may result in the apparent difference.

(1) This test was performed by Bureau Veritas Calgary, 4000 - 19 St. , Calgary, AB, T2E 6P8

(2) DOC present in the sample should be considered as non-purgeable DOC. Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(3) "Total Hardness" was calculated from Total Ca and Mg concentrations and may be biased high (Hardness, or Dissolved Hardness, calculated from Dissolved Ca and Mg, should be used for compliance if available).

(4) Samples were filtered and preserved at the lab. Values may not reflect concentrations at the time of sampling.

For Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(5) Total PAHs in Water include: Quinoline, Naphthalene, 1-Methylnaphthalene, 2-Methylnaphthalene, Acenaphthylene, Acenaphthene, Fluorene, Phenanthrene, Anthracene, Acridine, Fluoranthene, Pyrene, Benzo(a)anthracene, Chrysene, Benzo(b&j)fluoranthene, Benzo(k)fluoranthene, Benzo(a)pyrene, Indeno(1,2,3-cd)pyrene, Dibenzo(a,h)anthracene, and Benzo(g,h,i)perylene.

(6) The CCME method requires pH to be analysed within 15 minutes of sampling and therefore field analysis is required for compliance. All Laboratory pH analyses in this report are reported past the CCME holding time. Bureau Veritas endeavours to analyze samples as soon as possible after receipt.

(7) LEPH = EPH (C10 to C19) - (Acenaphthene + Acridine + Anthracene + Fluorene + Naphthalene + Phenanthrene)

HEPH = EPH (C19 to C32) - (Benzo(a)anthracene + Benzo(a)pyrene + Fluoranthene + Pyrene)

(8) TOC present in the sample should be considered as non-purgeable TOC.

(9) VPH = VH - (Benzene + Toluene + Ethylbenzene + m & p-Xylene + o-Xylene + Styrene)

Encryption Key

Please direct all questions regarding this Certificate of Analysis to:

Levi Manchak, Senior Project Manager

Email: Levi.MANCHAK@bureauveritas.com

Phone# (780)862-5634

=====

This report has been generated and distributed using a secure automated process.

Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports.

For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C370011				ND	0.0050	C370011
Calculated Parameters										
Total Chromium III	mg/L	ND	0.00099	C369330				ND	0.00099	C369330
Dissolved Hardness (CaCO ₃)	mg/L	60.7	0.50	C367501				61.2	0.50	C367501
Total Hardness (CaCO ₃)	mg/L	52.6	0.50	C368374				64.7	0.50	C368374
Nitrate (N)	mg/L	0.021	0.020	C367885				ND	0.020	C367885
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C368818				ND	0.0020	C368818
Field Parameters										
Field pH	pH	7.48	N/A	ONSITE				6.88	N/A	ONSITE
Field Temperature	°C	13.5	N/A	ONSITE				14.1	N/A	ONSITE
Misc. Inorganics										
pH	pH	7.22	N/A	C370266				7.28	N/A	C370266
Total Organic Carbon (C)	mg/L	0.99	0.50	C370940				0.95	0.50	C370940
Total Dissolved Solids	mg/L	96	10	C371183	100	10	C371183	88	10	C371183
Total Suspended Solids	mg/L	ND	1.0	C373876				ND	1.0	C373876
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L	0.61	0.50	C371380				0.72	0.50	C371380
Anions										
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Alkalinity (Total as CaCO ₃)	mg/L	43	1.0	C370269				47	1.0	C370269
Bicarbonate (HCO ₃)	mg/L	53	1.0	C370269				57	1.0	C370269
Carbonate (CO ₃)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Fluoride (F)	mg/L	0.27	0.050	C369761				0.28	0.050	C369761
Hydroxide (OH)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Total Sulphide	mg/L	ND	0.0018	C372985				ND	0.0018	C372985
Chloride (Cl)	mg/L	18	1.0	C369979				15	1.0	C369979
Sulphate (SO ₄)	mg/L	14	1.0	C369979				14	1.0	C369979
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.00099	C374026				ND	0.00099	C374026
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C369986				ND	0.015	C369986
Total Phosphorus (P)	mg/L	0.0025	0.0010	C373394				0.0018	0.0010	C373394
Nitrate plus Nitrite (N)	mg/L	0.021	0.020	C369991				ND	0.020	C369991
Total Nitrogen (N)	mg/L	0.177	0.020	C371141				0.197	0.020	C371141
Misc. Organics										
Phenols	mg/L							ND	0.0015	C372904
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE255			EKE255			EKE256		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-US	RDL	QC Batch	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C370011				ND	0.0050	C370011
Calculated Parameters										
Total Chromium III	mg/L	ND	0.00099	C369330				ND	0.00099	C369330
Dissolved Hardness (CaCO ₃)	mg/L	8.83	0.50	C367501				ND	0.50	C367501
Total Hardness (CaCO ₃)	mg/L	7.60	0.50	C368374				ND	0.50	C368374
Nitrate (N)	mg/L	0.039	0.020	C367885				ND	0.020	C367885
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C368818				ND	0.0020	C368818
Field Parameters										
Field pH	pH	6.92	N/A	ONSITE						
Field Temperature	°C	14.9	N/A	ONSITE						
Misc. Inorganics										
pH	pH	6.55	N/A	C370266				6.00	N/A	C370266
Total Organic Carbon (C)	mg/L	2.4	0.50	C370940				ND	0.50	C370940
Total Dissolved Solids	mg/L	48	10	C374012				ND	10	C374012
Total Suspended Solids	mg/L	1.6	1.0	C370012	1.6	1.0	C370012	ND	1.0	C370012
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L	1.9	0.50	C371380				ND	0.50	C371380
Anions										
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Alkalinity (Total as CaCO ₃)	mg/L	8.2	1.0	C370269				ND	1.0	C370269
Bicarbonate (HCO ₃)	mg/L	9.9	1.0	C370269				ND	1.0	C370269
Carbonate (CO ₃)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Fluoride (F)	mg/L	ND	0.050	C370219				ND	0.050	C369761
Hydroxide (OH)	mg/L	ND	1.0	C370269				ND	1.0	C370269
Total Sulphide	mg/L	ND	0.0018	C372985				ND	0.0018	C373023
Chloride (Cl)	mg/L	ND	1.0	C369979				ND	1.0	C369979
Sulphate (SO ₄)	mg/L	2.0	1.0	C369979				ND	1.0	C369979
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE255			EKE255			EKE256		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-US	RDL	QC Batch	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.00099	C374026				ND	0.00099	C374026
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C369986				ND	0.015	C369986
Total Phosphorus (P)	mg/L	0.022	0.0010	C373394				0.0026	0.0010	C373394
Nitrate plus Nitrite (N)	mg/L	0.039	0.020	C369991				ND	0.020	C369991
Total Nitrogen (N)	mg/L	0.131	0.020	C371141				ND	0.020	C371141
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE256			EKE257			EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C370011	ND	0.0050	C370011			
Calculated Parameters										
Total Chromium III	mg/L				ND	0.00099	C369330			
Dissolved Hardness (CaCO ₃)	mg/L				ND	0.50	C367501			
Total Hardness (CaCO ₃)	mg/L				ND	0.50	C368374			
Nitrate (N)	mg/L				ND	0.020	C367885			
Sulphide (as H ₂ S)	mg/L				ND	0.0020	C368818			
Misc. Inorganics										
pH	pH				5.81	N/A	C370266			
Total Organic Carbon (C)	mg/L				ND	0.50	C370940			
Total Dissolved Solids	mg/L	ND	10	C374012	ND	10	C374012			
Total Suspended Solids	mg/L				ND	1.0	C373874			
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L				ND	0.50	C371380			
Anions										
Alkalinity (PP as CaCO ₃)	mg/L				ND	1.0	C370269			
Alkalinity (Total as CaCO ₃)	mg/L				ND	1.0	C370269			
Bicarbonate (HCO ₃)	mg/L				ND	1.0	C370269			
Carbonate (CO ₃)	mg/L				ND	1.0	C370269			
Fluoride (F)	mg/L				ND	0.050	C369761			
Hydroxide (OH)	mg/L				ND	1.0	C370269			
Total Sulphide	mg/L	ND	0.0018	C373023	ND	0.0018	C373023			
Chloride (Cl)	mg/L				ND	1.0	C369979	ND	1.0	C369979
Sulphate (SO ₄)	mg/L				ND	1.0	C369979	ND	1.0	C369979
Metals										
Total Hex. Chromium (Cr 6+)	mg/L				0.00099	0.00099	C374026	ND	0.00099	C374026
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		EKE256			EKE257			EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch
Nutrients										
Total Ammonia (N)	mg/L				ND	0.015	C369986			
Total Phosphorus (P)	mg/L	ND	0.0010	C373394	ND	0.0010	C373394			
Nitrate plus Nitrite (N)	mg/L	ND	0.020	C369991	ND	0.020	C369991			
Total Nitrogen (N)	mg/L				ND	0.020	C371141			
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

GLYCOLS BY GC-FID (WATER)

Bureau Veritas ID		EKE254		
Sampling Date		2026/08/05 08:30		
COC Number		137689		
	UNITS	WLNG -EOP	RDL	QC Batch
Glycols				
Ethylene Glycol	mg/L	ND	3.0	C372871
Diethylene Glycol	mg/L	ND	5.0	C372871
Triethylene Glycol	mg/L	ND	5.0	C372871
Propylene Glycol	mg/L	ND	5.0	C372871
Surrogate Recovery (%)				
Methyl Sulfone (sur.)	%	92		C372871
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



MERCURY BY COLD VAPOR (WATER)

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch

Elements										
Total Mercury (Hg)	ug/L	ND	0.0019	C371159				ND	0.0019	C371166
Lab Filtered Elements										
Dissolved Mercury (Hg)	ug/L	ND	0.0019	C375500	ND	0.0019	C375500	ND	0.0019	C375500
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										

Bureau Veritas ID		EKE254			EKE255		EKE256		EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30		2026/08/05 08:30		2026/08/05 08:30		
COC Number		137689			137689		137689		137689		
	UNITS	WLNG -EOP Lab-Dup	RDL	QC Batch	WLNG-US	QC Batch	Field Blank	QC Batch	Trip Blank	RDL	QC Batch

Elements											
Total Mercury (Hg)	ug/L	ND	0.0019	C371166	ND	C371166	ND	C371159	ND	0.0019	C371166
Lab Filtered Elements											
Dissolved Mercury (Hg)	ug/L				ND	C375500	ND	C375500	ND	0.0019	C375500
RDL = Reportable Detection Limit											
Lab-Dup = Laboratory Initiated Duplicate											
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.											



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
ANIONS										
Bromide (Br)	mg/L	ND	0.010	C374700				ND	0.010	C374700
Dissolved Metals by ICPMS										
Dissolved Calcium (Ca)	mg/L	22.2	0.050	C367761				22.4	0.050	C367761
Dissolved Magnesium (Mg)	mg/L	1.25	0.050	C367761				1.29	0.050	C367761
Dissolved Potassium (K)	mg/L	1.82	0.050	C367761				1.61	0.050	C367761
Dissolved Sodium (Na)	mg/L	7.28	0.050	C367761				6.99	0.050	C367761
Dissolved Sulphur (S)	mg/L	4.9	3.0	C367761				4.9	3.0	C367761
Lab Filtered Metals										
Dissolved Aluminum (Al)	ug/L	40.1	0.50	C370805				27.4	0.50	C370805
Dissolved Antimony (Sb)	ug/L	0.349	0.020	C370805				0.306	0.020	C370805
Dissolved Arsenic (As)	ug/L	0.896	0.020	C370805				1.03	0.020	C370805
Dissolved Barium (Ba)	ug/L	4.29	0.020	C370805				3.30	0.020	C370805
Dissolved Beryllium (Be)	ug/L	ND	0.010	C370805				ND	0.010	C370805
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C370805				ND	0.0050	C370805
Dissolved Boron (B)	ug/L	ND	10	C370805				ND	10	C370805
Dissolved Cadmium (Cd)	ug/L	ND	0.0050	C370805				ND	0.0050	C370805
Dissolved Cesium (Cs)	ug/L	ND	0.050	C370805				ND	0.050	C370805
Dissolved Chromium (Cr)	ug/L	ND	0.10	C370805				ND	0.10	C370805
Dissolved Cobalt (Co)	ug/L	0.0334	0.0050	C370805				0.0473	0.0050	C370805
Dissolved Copper (Cu)	ug/L	0.087	0.050	C370805				0.080	0.050	C370805
Dissolved Iron (Fe)	ug/L	2.8	1.0	C370805				1.8	1.0	C370805
Dissolved Lead (Pb)	ug/L	ND	0.0050	C370805				ND	0.0050	C370805
Dissolved Lithium (Li)	ug/L	7.51	0.50	C370805				7.40	0.50	C370805
Dissolved Manganese (Mn)	ug/L	17.5	0.050	C370805				24.4	0.050	C370805
Dissolved Molybdenum (Mo)	ug/L	44.0	0.050	C370805				46.6	0.050	C370805
Dissolved Nickel (Ni)	ug/L	0.119	0.020	C370805				0.139	0.020	C370805
Dissolved Phosphorus (P)	ug/L	4.2	2.0	C370805				2.1	2.0	C370805
Dissolved Rubidium (Rb)	ug/L	3.75	0.050	C370805				3.33	0.050	C370805
Dissolved Selenium (Se)	ug/L	ND	0.040	C370805				ND	0.040	C370805
Dissolved Silicon (Si)	ug/L	6670	50	C370805				6840	50	C370805
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Dissolved Silver (Ag)	ug/L	ND	0.0050	C370805				ND	0.0050	C370805
Dissolved Strontium (Sr)	ug/L	47.4	0.050	C370805				47.3	0.050	C370805
Dissolved Tellurium (Te)	ug/L	ND	0.020	C370805				ND	0.020	C370805
Dissolved Thallium (Tl)	ug/L	0.0079	0.0020	C370805				0.0087	0.0020	C370805
Dissolved Thorium (Th)	ug/L	ND	0.0050	C370805				ND	0.0050	C370805
Dissolved Tin (Sn)	ug/L	ND	0.20	C370805				ND	0.20	C370805
Dissolved Titanium (Ti)	ug/L	ND	0.50	C370805				ND	0.50	C370805
Dissolved Uranium (U)	ug/L	0.211	0.0020	C370805				0.176	0.0020	C370805
Dissolved Vanadium (V)	ug/L	ND	0.20	C370805				ND	0.20	C370805
Dissolved Zinc (Zn)	ug/L	2.06	0.10	C370805				3.56	0.10	C370805
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C370805				ND	0.10	C370805
Total Metals by ICPMS										
Total Aluminum (Al)	ug/L	75.7	3.0	C372971	77.6	3.0	C372971	72.5	0.50	C372109
Total Antimony (Sb)	ug/L	0.339	0.020	C372971	0.318	0.020	C372971	0.295	0.020	C372109
Total Arsenic (As)	ug/L	0.895	0.020	C372971	0.914	0.020	C372971	1.08	0.020	C372109
Total Barium (Ba)	ug/L	4.20	0.050	C372971	4.17	0.050	C372971	3.57	0.020	C372109
Total Beryllium (Be)	ug/L	ND	0.010	C372971	ND	0.010	C372971	ND	0.010	C372109
Total Bismuth (Bi)	ug/L	ND	0.010	C372971	ND	0.010	C372971	ND	0.0050	C372109
Total Boron (B)	ug/L	10	10	C372971	10	10	C372971	15	10	C372109
Total Cadmium (Cd)	ug/L	0.0059	0.0050	C372971	ND	0.0050	C372971	ND	0.0050	C372109
Total Cesium (Cs)	ug/L	ND	0.050	C372971	ND	0.050	C372971	ND	0.050	C372109
Total Chromium (Cr)	ug/L	ND	0.10	C372971	ND	0.10	C372971	ND	0.10	C372109
Total Cobalt (Co)	ug/L	0.035	0.010	C372971	0.041	0.010	C372971	0.0475	0.0050	C372109
Total Copper (Cu)	ug/L	0.11	0.10	C372971	0.11	0.10	C372971	0.078	0.050	C372109
Total Iron (Fe)	ug/L	17.6	5.0	C372971	17.6	5.0	C372971	13.0	1.0	C372109
Total Lead (Pb)	ug/L	ND	0.020	C372971	ND	0.020	C372971	ND	0.0050	C372109
Total Lithium (Li)	ug/L	7.28	0.50	C372971	7.31	0.50	C372971	8.58	0.50	C372109
Total Manganese (Mn)	ug/L	17.4	0.10	C372971	17.1	0.10	C372971	24.9	0.050	C372109
Total Molybdenum (Mo)	ug/L	40.5	0.050	C372971	39.7	0.050	C372971	46.3	0.050	C372109
Total Nickel (Ni)	ug/L	0.19	0.10	C372971	0.15	0.10	C372971	0.168	0.020	C372109
Total Phosphorus (P)	ug/L	5.1	5.0	C372971	ND	5.0	C372971	3.2	2.0	C372109
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EKE253			EKE253			EKE254		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30			2026/08/05 08:30		
COC Number		137689			137689			137689		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch
Total Rubidium (Rb)	ug/L	3.69	0.050	C372971	3.58	0.050	C372971	3.66	0.050	C372109
Total Selenium (Se)	ug/L	ND	0.040	C372971	ND	0.040	C372971	ND	0.040	C372109
Total Silicon (Si)	ug/L	5960	50	C372971	5730	50	C372971	7400	50	C372109
Total Silver (Ag)	ug/L	ND	0.010	C372971	ND	0.010	C372971	ND	0.0050	C372109
Total Strontium (Sr)	ug/L	44.3	0.050	C372971	43.0	0.050	C372971	49.8	0.050	C372109
Total Tellurium (Te)	ug/L	ND	0.020	C372971	ND	0.020	C372971	ND	0.020	C372109
Total Thallium (Tl)	ug/L	0.0078	0.0020	C372971	0.0077	0.0020	C372971	0.0077	0.0020	C372109
Total Thorium (Th)	ug/L	ND	0.050	C372971	ND	0.050	C372971	ND	0.050	C372109
Total Tin (Sn)	ug/L	ND	0.20	C372971	ND	0.20	C372971	ND	0.20	C372109
Total Titanium (Ti)	ug/L	ND	2.0	C372971	ND	2.0	C372971	ND	0.50	C372109
Total Uranium (U)	ug/L	0.217	0.0050	C372971	0.218	0.0050	C372971	0.224	0.0020	C372109
Total Vanadium (V)	ug/L	ND	0.20	C372971	ND	0.20	C372971	ND	0.20	C372109
Total Zinc (Zn)	ug/L	2.6	1.0	C372971	2.6	1.0	C372971	3.78	0.10	C372109
Total Zirconium (Zr)	ug/L	ND	0.10	C372971	ND	0.10	C372971	ND	0.10	C372109
Total Calcium (Ca)	mg/L	19.2	0.25	C367762				23.5	0.050	C367762
Total Magnesium (Mg)	mg/L	1.12	0.25	C367762				1.42	0.050	C367762
Total Potassium (K)	mg/L	1.76	0.25	C367762				1.68	0.050	C367762
Total Sodium (Na)	mg/L	6.74	0.25	C367762				7.69	0.050	C367762
Total Sulphur (S)	mg/L	4.3	3.0	C367762				5.4	3.0	C367762
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EKE255			EKE256	EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30	2026/08/05 08:30		
COC Number		137689			137689	137689		
	UNITS	WLNG-US	RDL	QC Batch	Field Blank	Trip Blank	RDL	QC Batch
ANIONS								
Bromide (Br)	mg/L	ND	0.010	C374700	ND	ND	0.010	C374700
Dissolved Metals by ICPMS								
Dissolved Calcium (Ca)	mg/L	2.99	0.050	C367761	ND	ND	0.050	C367761
Dissolved Magnesium (Mg)	mg/L	0.333	0.050	C367761	ND	ND	0.050	C367761
Dissolved Potassium (K)	mg/L	0.188	0.050	C367761	ND	ND	0.050	C367761
Dissolved Sodium (Na)	mg/L	1.76	0.050	C367761	ND	ND	0.050	C367761
Dissolved Sulphur (S)	mg/L	ND	3.0	C367761	ND	ND	3.0	C367761
Lab Filtered Metals								
Dissolved Aluminum (Al)	ug/L	33.8	0.50	C370805	ND	ND	0.50	C370805
Dissolved Antimony (Sb)	ug/L	0.020	0.020	C370805	ND	ND	0.020	C370805
Dissolved Arsenic (As)	ug/L	0.115	0.020	C370805	ND	ND	0.020	C370805
Dissolved Barium (Ba)	ug/L	3.91	0.020	C370805	ND	ND	0.020	C370805
Dissolved Beryllium (Be)	ug/L	ND	0.010	C370805	ND	ND	0.010	C370805
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C370805	ND	ND	0.0050	C370805
Dissolved Boron (B)	ug/L	ND	10	C370805	ND	ND	10	C370805
Dissolved Cadmium (Cd)	ug/L	0.0057	0.0050	C370805	ND	ND	0.0050	C370805
Dissolved Cesium (Cs)	ug/L	ND	0.050	C370805	ND	ND	0.050	C370805
Dissolved Chromium (Cr)	ug/L	ND	0.10	C370805	ND	ND	0.10	C370805
Dissolved Cobalt (Co)	ug/L	0.0211	0.0050	C370805	ND	ND	0.0050	C370805
Dissolved Copper (Cu)	ug/L	0.717	0.050	C370805	ND	ND	0.050	C370805
Dissolved Iron (Fe)	ug/L	32.3	1.0	C370805	ND	ND	1.0	C370805
Dissolved Lead (Pb)	ug/L	0.0149	0.0050	C370805	ND	ND	0.0050	C370805
Dissolved Lithium (Li)	ug/L	ND	0.50	C370805	ND	ND	0.50	C370805
Dissolved Manganese (Mn)	ug/L	1.30	0.050	C370805	ND	ND	0.050	C370805
Dissolved Molybdenum (Mo)	ug/L	0.520	0.050	C370805	ND	ND	0.050	C370805
Dissolved Nickel (Ni)	ug/L	0.232	0.020	C370805	ND	ND	0.020	C370805
Dissolved Phosphorus (P)	ug/L	16.2	2.0	C370805	3.1	ND	2.0	C370805
Dissolved Rubidium (Rb)	ug/L	0.379	0.050	C370805	ND	ND	0.050	C370805
Dissolved Selenium (Se)	ug/L	ND	0.040	C370805	ND	ND	0.040	C370805
Dissolved Silicon (Si)	ug/L	4550	50	C370805	ND	ND	50	C370805
Dissolved Silver (Ag)	ug/L	ND	0.0050	C370805	ND	ND	0.0050	C370805
RDL = Reportable Detection Limit								
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.								

**ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)**

Bureau Veritas ID		EKE255			EKE256	EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30	2026/08/05 08:30		
COC Number		137689			137689	137689		
	UNITS	WLNG-US	RDL	QC Batch	Field Blank	Trip Blank	RDL	QC Batch
Dissolved Strontium (Sr)	ug/L	14.8	0.050	C370805	ND	ND	0.050	C370805
Dissolved Tellurium (Te)	ug/L	ND	0.020	C370805	ND	ND	0.020	C370805
Dissolved Thallium (Tl)	ug/L	0.0024	0.0020	C370805	ND	ND	0.0020	C370805
Dissolved Thorium (Th)	ug/L	0.0130	0.0050	C370805	ND	ND	0.0050	C370805
Dissolved Tin (Sn)	ug/L	ND	0.20	C370805	ND	ND	0.20	C370805
Dissolved Titanium (Ti)	ug/L	ND	0.50	C370805	ND	ND	0.50	C370805
Dissolved Uranium (U)	ug/L	0.0575	0.0020	C370805	ND	ND	0.0020	C370805
Dissolved Vanadium (V)	ug/L	0.21	0.20	C370805	ND	ND	0.20	C370805
Dissolved Zinc (Zn)	ug/L	0.60	0.10	C370805	ND	ND	0.10	C370805
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C370805	ND	ND	0.10	C370805
Total Metals by ICPMS								
Total Aluminum (Al)	ug/L	55.7	3.0	C372971	ND	ND	0.50	C372109
Total Antimony (Sb)	ug/L	0.024	0.020	C372971	ND	ND	0.020	C372109
Total Arsenic (As)	ug/L	0.133	0.020	C372971	ND	ND	0.020	C372109
Total Barium (Ba)	ug/L	3.96	0.050	C372971	ND	ND	0.020	C372109
Total Beryllium (Be)	ug/L	ND	0.010	C372971	ND	ND	0.010	C372109
Total Bismuth (Bi)	ug/L	ND	0.010	C372971	ND	ND	0.0050	C372109
Total Boron (B)	ug/L	ND	10	C372971	ND	ND	10	C372109
Total Cadmium (Cd)	ug/L	0.0062	0.0050	C372971	ND	ND	0.0050	C372109
Total Cesium (Cs)	ug/L	ND	0.050	C372971	ND	ND	0.050	C372109
Total Chromium (Cr)	ug/L	0.22	0.10	C372971	ND	ND	0.10	C372109
Total Cobalt (Co)	ug/L	0.032	0.010	C372971	ND	ND	0.0050	C372109
Total Copper (Cu)	ug/L	0.81	0.10	C372971	ND	ND	0.050	C372109
Total Iron (Fe)	ug/L	61.3	5.0	C372971	ND	ND	1.0	C372109
Total Lead (Pb)	ug/L	0.035	0.020	C372971	ND	ND	0.0050	C372109
Total Lithium (Li)	ug/L	ND	0.50	C372971	ND	ND	0.50	C372109
Total Manganese (Mn)	ug/L	2.13	0.10	C372971	ND	ND	0.050	C372109
Total Molybdenum (Mo)	ug/L	0.447	0.050	C372971	ND	ND	0.050	C372109
Total Nickel (Ni)	ug/L	0.34	0.10	C372971	ND	ND	0.020	C372109
Total Phosphorus (P)	ug/L	19.1	5.0	C372971	ND	ND	2.0	C372109
Total Rubidium (Rb)	ug/L	0.341	0.050	C372971	ND	ND	0.050	C372109
Total Selenium (Se)	ug/L	ND	0.040	C372971	ND	ND	0.040	C372109
RDL = Reportable Detection Limit								
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.								



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		EKE255			EKE256	EKE257		
Sampling Date		2026/08/05 08:30			2026/08/05 08:30	2026/08/05 08:30		
COC Number		137689			137689	137689		
	UNITS	WLNG-US	RDL	QC Batch	Field Blank	Trip Blank	RDL	QC Batch
Total Silicon (Si)	ug/L	4100	50	C372971	ND	ND	50	C372109
Total Silver (Ag)	ug/L	ND	0.010	C372971	ND	ND	0.0050	C372109
Total Strontium (Sr)	ug/L	13.2	0.050	C372971	ND	ND	0.050	C372109
Total Tellurium (Te)	ug/L	ND	0.020	C372971	ND	ND	0.020	C372109
Total Thallium (Tl)	ug/L	ND	0.0020	C372971	ND	ND	0.0020	C372109
Total Thorium (Th)	ug/L	ND	0.050	C372971	ND	ND	0.050	C372109
Total Tin (Sn)	ug/L	ND	0.20	C372971	ND	ND	0.20	C372109
Total Titanium (Ti)	ug/L	ND	2.0	C372971	ND	ND	0.50	C372109
Total Uranium (U)	ug/L	0.0540	0.0050	C372971	ND	ND	0.0020	C372109
Total Vanadium (V)	ug/L	ND	0.20	C372971	ND	ND	0.20	C372109
Total Zinc (Zn)	ug/L	2.3	1.0	C372971	ND	ND	0.10	C372109
Total Zirconium (Zr)	ug/L	ND	0.10	C372971	ND	ND	0.10	C372109
Total Calcium (Ca)	mg/L	2.57	0.25	C367762	ND	ND	0.050	C367762
Total Magnesium (Mg)	mg/L	0.29	0.25	C367762	ND	ND	0.050	C367762
Total Potassium (K)	mg/L	ND	0.25	C367762	ND	ND	0.050	C367762
Total Sodium (Na)	mg/L	1.48	0.25	C367762	ND	ND	0.050	C367762
Total Sulphur (S)	mg/L	ND	3.0	C367762	ND	ND	3.0	C367762
RDL = Reportable Detection Limit								
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.								



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

MISCELLANEOUS (WATER)

Bureau Veritas ID		EKE253	EKE254	EKE255		
Sampling Date		2026/08/05 08:30	2026/08/05 08:30	2026/08/05 08:30		
COC Number		137689	137689	137689		
	UNITS	WLNG-DS	WLNG -EOP	WLNG-US	RDL	QC Batch
Calculated Parameters						
Total Un-ionized Hydrogen Sulfide as S	mg/L	ND	ND	ND	0.0018	C369334
Total Un-ionized Hydrogen Sulfide as H2S	mg/L	ND	ND	ND	0.0019	C369334
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.						



LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)

Bureau Veritas ID		EKE254		
Sampling Date		2026/08/05 08:30		
COC Number		137689		
	UNITS	WLNG -EOP	RDL	QC Batch
Calculated Parameters				
Low Molecular Weight PAH's	ug/L	ND	0.10	C367887
High Molecular Weight PAH's	ug/L	ND	0.050	C367887
Total PAH	ug/L	ND	0.10	C367887
Polycyclic Aromatics				
Quinoline	ug/L	ND	0.020	C370948
Naphthalene	ug/L	ND	0.10	C370948
1-Methylnaphthalene	ug/L	ND	0.050	C370948
2-Methylnaphthalene	ug/L	ND	0.10	C370948
Acenaphthylene	ug/L	ND	0.050	C370948
Acenaphthene	ug/L	ND	0.050	C370948
Fluorene	ug/L	ND	0.050	C370948
Phenanthrene	ug/L	ND	0.050	C370948
Anthracene	ug/L	ND	0.010	C370948
Acridine	ug/L	ND	0.050	C370948
Fluoranthene	ug/L	ND	0.020	C370948
Pyrene	ug/L	ND	0.020	C370948
Benzo(a)anthracene	ug/L	ND	0.010	C370948
Chrysene	ug/L	ND	0.020	C370948
Benzo(b&j)fluoranthene	ug/L	ND	0.030	C370948
Benzo(k)fluoranthene	ug/L	ND	0.050	C370948
Benzo(a)pyrene	ug/L	ND	0.0050	C370948
Indeno(1,2,3-cd)pyrene	ug/L	ND	0.050	C370948
Dibenz(a,h)anthracene	ug/L	ND	0.0030	C370948
Benzo(g,h,i)perylene	ug/L	ND	0.050	C370948
Calculated Parameters				
LEPH (C10-C19 less PAH)	mg/L	ND	0.20	C368438
HEPH (C19-C32 less PAH)	mg/L	ND	0.20	C368438
Ext. Pet. Hydrocarbon				
EPH (C10-C19)	mg/L	ND	0.20	C370952
EPH (C19-C32)	mg/L	ND	0.20	C370952
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)

Bureau Veritas ID		EKE254		
Sampling Date		2026/08/05 08:30		
COC Number		137689		
	UNITS	WLNG -EOP	RDL	QC Batch
Surrogate Recovery (%)				
O-TERPHENYL (sur.)	%	99		C370952
D10-ANTHRACENE (sur.)	%	100		C370948
D8-ACENAPHTHYLENE (sur.)	%	94		C370948
D8-NAPHTHALENE (sur.)	%	75		C370948
TERPHENYL-D14 (sur.)	%	87		C370948
RDL = Reportable Detection Limit				



CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		EKE254		
Sampling Date		2026/08/05 08:30		
COC Number		137689		
	UNITS	WLNG -EOP	RDL	QC Batch
Calculated Parameters				
VPH (VH6 to 10 - BTEX)	ug/L	ND	300	C367892
Volatiles				
VH C6-C10	ug/L	ND	300	C369959
1,1,1,2-tetrachloroethane	ug/L	ND	0.50	C369959
1,1,1-trichloroethane	ug/L	ND	0.50	C369959
1,1,2,2-tetrachloroethane	ug/L	ND	0.50	C369959
1,1,2Trichloro-1,2,2Trifluoroethane	ug/L	ND	2.0	C369959
1,1,2-trichloroethane	ug/L	ND	0.50	C369959
1,1-dichloroethane	ug/L	ND	0.50	C369959
1,1-dichloroethene	ug/L	ND	0.50	C369959
1,2,3-trichlorobenzene	ug/L	ND	2.0	C369959
1,2,4-trichlorobenzene	ug/L	ND	2.0	C369959
1,2-dibromoethane	ug/L	ND	0.20	C369959
1,2-dichlorobenzene	ug/L	ND	0.50	C369959
1,2-dichloroethane	ug/L	ND	0.50	C369959
1,2-dichloropropane	ug/L	ND	0.50	C369959
1,3,5-trimethylbenzene	ug/L	ND	2.0	C369959
1,3-Butadiene	ug/L	ND	0.50	C369959
1,3-dichlorobenzene	ug/L	ND	0.50	C369959
1,3-dichloropropane	ug/L	ND	1.0	C369959
1,4-dichlorobenzene	ug/L	ND	0.50	C369959
Benzene	ug/L	ND	0.40	C369959
Bromobenzene	ug/L	ND	2.0	C369959
Bromodichloromethane	ug/L	ND	1.0	C369959
Bromoform	ug/L	ND	1.0	C369959
Bromomethane	ug/L	ND	1.0	C369959
Carbon tetrachloride	ug/L	ND	0.50	C369959
Chlorobenzene	ug/L	ND	0.50	C369959
Dibromochloromethane	ug/L	ND	1.0	C369959
Chloroethane	ug/L	ND	1.0	C369959
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		EKE254		
Sampling Date		2026/08/05 08:30		
COC Number		137689		
	UNITS	WLNG -EOP	RDL	QC Batch
Chloroform	ug/L	ND	1.0	C369959
Chloromethane	ug/L	ND	1.0	C369959
cis-1,2-dichloroethene	ug/L	ND	1.0	C369959
cis-1,3-dichloropropene	ug/L	ND	1.0	C369959
Dichlorodifluoromethane	ug/L	ND	2.0	C369959
Dichloromethane	ug/L	ND	2.0	C369959
Ethylbenzene	ug/L	ND	0.40	C369959
Hexachlorobutadiene	ug/L	ND	0.50	C369959
Isopropylbenzene	ug/L	ND	2.0	C369959
Methyl-tert-butylether (MTBE)	ug/L	ND	4.0	C369959
Styrene	ug/L	ND	0.50	C369959
Tetrachloroethene	ug/L	ND	0.50	C369959
Toluene	ug/L	ND	0.40	C369959
trans-1,2-dichloroethene	ug/L	ND	1.0	C369959
trans-1,3-dichloropropene	ug/L	ND	1.0	C369959
Trichloroethene	ug/L	ND	0.50	C369959
Trichlorofluoromethane	ug/L	ND	4.0	C369959
Vinyl chloride	ug/L	ND	0.50	C369959
m & p-Xylene	ug/L	ND	0.40	C369959
o-Xylene	ug/L	ND	0.40	C369959
Xylenes (Total)	ug/L	ND	0.40	C369959
Surrogate Recovery (%)				
1,4-Difluorobenzene (sur.)	%	100		C369959
4-Bromofluorobenzene (sur.)	%	82		C369959
D4-1,2-Dichloroethane (sur.)	%	102		C369959
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

GENERAL COMMENTS

Sample EKE257 [Trip Blank] : Total Chromium < Total Hexavalent Chromium. High Hexavalent result is likely due to matrix interference.

Results relate only to the items tested.



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C369761	BB3	Matrix Spike	Dissolved Fluoride (F)	2026/08/06		NC	%	80 - 120
C369761	BB3	Spiked Blank	Dissolved Fluoride (F)	2026/08/06		98	%	80 - 120
C369761	BB3	Method Blank	Dissolved Fluoride (F)	2026/08/06	ND, RDL=0.050		mg/L	
C369761	BB3	RPD	Fluoride (F)	2026/08/06	0.91		%	20
C369959	DWL	Matrix Spike	1,4-Difluorobenzene (sur.)	2026/08/07		97	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/07		105	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/07		103	%	50 - 140
			1,1,1,2-tetrachloroethane	2026/08/07		91	%	50 - 140
			1,1,1-trichloroethane	2026/08/07		97	%	50 - 140
			1,1,2,2-tetrachloroethane	2026/08/07		96	%	50 - 140
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/07		92	%	50 - 140
			1,1,2-trichloroethane	2026/08/07		96	%	50 - 140
			1,1-dichloroethane	2026/08/07		97	%	50 - 140
			1,1-dichloroethene	2026/08/07		91	%	50 - 140
			1,2,3-trichlorobenzene	2026/08/07		95	%	50 - 140
			1,2,4-trichlorobenzene	2026/08/07		94	%	50 - 140
			1,2-dibromoethane	2026/08/07		95	%	50 - 140
			1,2-dichlorobenzene	2026/08/07		104	%	50 - 140
			1,2-dichloroethane	2026/08/07		95	%	50 - 140
			1,2-dichloropropane	2026/08/07		97	%	50 - 140
			1,3,5-trimethylbenzene	2026/08/07		100	%	50 - 140
			1,3-Butadiene	2026/08/07		58	%	50 - 140
			1,3-dichlorobenzene	2026/08/07		112	%	50 - 140
			1,3-dichloropropane	2026/08/07		93	%	50 - 140
			1,4-dichlorobenzene	2026/08/07		118	%	50 - 140
			Benzene	2026/08/07		94	%	50 - 140
			Bromobenzene	2026/08/07		100	%	50 - 140
			Bromodichloromethane	2026/08/07		96	%	50 - 140
			Bromoform	2026/08/07		95	%	50 - 140
			Bromomethane	2026/08/07		72	%	50 - 140
			Carbon tetrachloride	2026/08/07		95	%	50 - 140
			Chlorobenzene	2026/08/07		93	%	50 - 140
			Dibromochloromethane	2026/08/07		96	%	50 - 140
			Chloroethane	2026/08/07		85	%	50 - 140
			Chloroform	2026/08/07		94	%	50 - 140
			Chloromethane	2026/08/07		79	%	50 - 140
			cis-1,2-dichloroethene	2026/08/07		88	%	50 - 140
			cis-1,3-dichloropropene	2026/08/07		85	%	50 - 140
			Dichlorodifluoromethane	2026/08/07		62	%	50 - 140
			Dichloromethane	2026/08/07		92	%	50 - 140
			Ethylbenzene	2026/08/07		82	%	50 - 140
			Hexachlorobutadiene	2026/08/07		97	%	50 - 140
			Isopropylbenzene	2026/08/07		80	%	50 - 140
			Methyl-tert-butylether (MTBE)	2026/08/07		80	%	50 - 140
			Styrene	2026/08/07		90	%	50 - 140
			Tetrachloroethene	2026/08/07		96	%	50 - 140
			Toluene	2026/08/07		92	%	50 - 140
			trans-1,2-dichloroethene	2026/08/07		94	%	50 - 140
			trans-1,3-dichloropropene	2026/08/07		82	%	50 - 140
			Trichloroethene	2026/08/07		93	%	50 - 140
			Trichlorofluoromethane	2026/08/07		91	%	50 - 140
			Vinyl chloride	2026/08/07		87	%	50 - 140



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C369959	DWL	Spiked Blank	m & p-Xylene	2026/08/07		100	%	50 - 140
			o-Xylene	2026/08/07		86	%	50 - 140
			1,4-Difluorobenzene (sur.)	2026/08/07		99	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/07		104	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/07		98	%	50 - 140
			VH C6-C10	2026/08/07		94	%	70 - 130
			1,1,1,2-tetrachloroethane	2026/08/07		94	%	60 - 130
			1,1,1-trichloroethane	2026/08/07		95	%	60 - 130
			1,1,2,2-tetrachloroethane	2026/08/07		92	%	60 - 130
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/07		90	%	60 - 130
			1,1,2-trichloroethane	2026/08/07		91	%	60 - 130
			1,1-dichloroethane	2026/08/07		94	%	60 - 130
			1,1-dichloroethene	2026/08/07		90	%	60 - 130
			1,2,3-trichlorobenzene	2026/08/07		96	%	60 - 130
			1,2,4-trichlorobenzene	2026/08/07		95	%	60 - 130
			1,2-dibromoethane	2026/08/07		91	%	60 - 130
			1,2-dichlorobenzene	2026/08/07		102	%	60 - 130
			1,2-dichloroethane	2026/08/07		91	%	60 - 130
			1,2-dichloropropane	2026/08/07		94	%	60 - 130
			1,3,5-trimethylbenzene	2026/08/07		100	%	60 - 130
			1,3-Butadiene	2026/08/07		58	%	50 - 140
			1,3-dichlorobenzene	2026/08/07		110	%	60 - 130
			1,3-dichloropropane	2026/08/07		90	%	60 - 130
			1,4-dichlorobenzene	2026/08/07		115	%	60 - 130
			Benzene	2026/08/07		94	%	60 - 130
			Bromobenzene	2026/08/07		99	%	60 - 130
			Bromodichloromethane	2026/08/07		92	%	60 - 130
			Bromoform	2026/08/07		91	%	60 - 130
			Bromomethane	2026/08/07		70	%	50 - 140
			Carbon tetrachloride	2026/08/07		92	%	60 - 130
			Chlorobenzene	2026/08/07		90	%	60 - 130
			Dibromochloromethane	2026/08/07		91	%	60 - 130
			Chloroethane	2026/08/07		86	%	50 - 140
			Chloroform	2026/08/07		91	%	60 - 130
			Chloromethane	2026/08/07		77	%	50 - 140
			cis-1,2-dichloroethene	2026/08/07		87	%	60 - 130
			cis-1,3-dichloropropene	2026/08/07		83	%	50 - 140
			Dichlorodifluoromethane	2026/08/07		61	%	50 - 140
			Dichloromethane	2026/08/07		89	%	60 - 130
			Ethylbenzene	2026/08/07		83	%	60 - 130
			Hexachlorobutadiene	2026/08/07		97	%	60 - 130
			Isopropylbenzene	2026/08/07		81	%	60 - 130
			Methyl-tert-butylether (MTBE)	2026/08/07		79	%	60 - 130
			Styrene	2026/08/07		89	%	60 - 130
			Tetrachloroethene	2026/08/07		94	%	60 - 130
			Toluene	2026/08/07		93	%	60 - 130
			trans-1,2-dichloroethene	2026/08/07		93	%	60 - 130
			trans-1,3-dichloropropene	2026/08/07		76	%	50 - 140
			Trichloroethene	2026/08/07		92	%	60 - 130
			Trichlorofluoromethane	2026/08/07		89	%	60 - 130
			Vinyl chloride	2026/08/07		86	%	50 - 140
			m & p-Xylene	2026/08/07		101	%	60 - 130
			o-Xylene	2026/08/07		86	%	60 - 130



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C369959	DWL	Method Blank	1,4-Difluorobenzene (sur.)	2026/08/07		102	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/07		86	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/07		107	%	50 - 140
			VH C6-C10	2026/08/07	ND, RDL=300		ug/L	
			1,1,1,2-tetrachloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,1,1-trichloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,1,2,2-tetrachloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/07	ND, RDL=2.0		ug/L	
			1,1,2-trichloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,1-dichloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,1-dichloroethene	2026/08/07	ND, RDL=0.50		ug/L	
			1,2,3-trichlorobenzene	2026/08/07	ND, RDL=2.0		ug/L	
			1,2,4-trichlorobenzene	2026/08/07	ND, RDL=2.0		ug/L	
			1,2-dibromoethane	2026/08/07	ND, RDL=0.20		ug/L	
			1,2-dichlorobenzene	2026/08/07	ND, RDL=0.50		ug/L	
			1,2-dichloroethane	2026/08/07	ND, RDL=0.50		ug/L	
			1,2-dichloropropane	2026/08/07	ND, RDL=0.50		ug/L	
			1,3,5-trimethylbenzene	2026/08/07	ND, RDL=2.0		ug/L	
			1,3-Butadiene	2026/08/07	ND, RDL=0.50		ug/L	
			1,3-dichlorobenzene	2026/08/07	ND, RDL=0.50		ug/L	
			1,3-dichloropropane	2026/08/07	ND, RDL=1.0		ug/L	
			1,4-dichlorobenzene	2026/08/07	ND, RDL=0.50		ug/L	
			Benzene	2026/08/07	ND, RDL=0.40		ug/L	
			Bromobenzene	2026/08/07	ND, RDL=2.0		ug/L	
			Bromodichloromethane	2026/08/07	ND, RDL=1.0		ug/L	
			Bromoform	2026/08/07	ND, RDL=1.0		ug/L	
			Bromomethane	2026/08/07	ND, RDL=1.0		ug/L	
			Carbon tetrachloride	2026/08/07	ND, RDL=0.50		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C369959	DWL	RPD	Chlorobenzene	2026/08/07	ND, RDL=0.50		ug/L	
			Dibromochloromethane	2026/08/07	ND, RDL=1.0		ug/L	
			Chloroethane	2026/08/07	ND, RDL=1.0		ug/L	
			Chloroform	2026/08/07	ND, RDL=1.0		ug/L	
			Chloromethane	2026/08/07	ND, RDL=1.0		ug/L	
			cis-1,2-dichloroethene	2026/08/07	ND, RDL=1.0		ug/L	
			cis-1,3-dichloropropene	2026/08/07	ND, RDL=1.0		ug/L	
			Dichlorodifluoromethane	2026/08/07	ND, RDL=2.0		ug/L	
			Dichloromethane	2026/08/07	ND, RDL=2.0		ug/L	
			Ethylbenzene	2026/08/07	ND, RDL=0.40		ug/L	
			Hexachlorobutadiene	2026/08/07	ND, RDL=0.50		ug/L	
			Isopropylbenzene	2026/08/07	ND, RDL=2.0		ug/L	
			Methyl-tert-butylether (MTBE)	2026/08/07	ND, RDL=4.0		ug/L	
			Styrene	2026/08/07	ND, RDL=0.50		ug/L	
			Tetrachloroethene	2026/08/07	ND, RDL=0.50		ug/L	
			Toluene	2026/08/07	ND, RDL=0.40		ug/L	
			trans-1,2-dichloroethene	2026/08/07	ND, RDL=1.0		ug/L	
			trans-1,3-dichloropropene	2026/08/07	ND, RDL=1.0		ug/L	
			Trichloroethene	2026/08/07	ND, RDL=0.50		ug/L	
			Trichlorofluoromethane	2026/08/07	ND, RDL=4.0		ug/L	
			Vinyl chloride	2026/08/07	ND, RDL=0.50		ug/L	
			m & p-Xylene	2026/08/07	ND, RDL=0.40		ug/L	
			o-Xylene	2026/08/07	ND, RDL=0.40		ug/L	
			Xylenes (Total)	2026/08/07	ND, RDL=0.40		ug/L	
			VH C6-C10	2026/08/07	NC		%	30
			1,1,1,2-tetrachloroethane	2026/08/07	NC		%	30
			1,1,1-trichloroethane	2026/08/07	NC		%	30
			1,1,2,2-tetrachloroethane	2026/08/07	NC		%	30
			1,1,2-trichloroethane	2026/08/07	NC		%	30
			1,1-dichloroethane	2026/08/07	NC		%	30



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			1,1-dichloroethene	2026/08/07	NC		%	30
			1,2,4-trichlorobenzene	2026/08/07	NC		%	30
			1,2-dibromoethane	2026/08/07	NC		%	30
			1,2-dichlorobenzene	2026/08/07	NC		%	30
			1,2-dichloroethane	2026/08/07	NC		%	30
			1,2-dichloropropane	2026/08/07	NC		%	30
			1,3,5-trimethylbenzene	2026/08/07	NC		%	30
			1,3-Butadiene	2026/08/07	NC		%	30
			Benzene	2026/08/07	NC		%	30
			Bromobenzene	2026/08/07	NC		%	30
			Bromodichloromethane	2026/08/07	NC		%	30
			Carbon tetrachloride	2026/08/07	NC		%	30
			Chlorobenzene	2026/08/07	NC		%	30
			Chloroethane	2026/08/07	NC		%	30
			cis-1,2-dichloroethene	2026/08/07	NC		%	30
			Dichlorodifluoromethane	2026/08/07	NC		%	30
			Dichloromethane	2026/08/07	NC		%	30
			Ethylbenzene	2026/08/07	NC		%	30
			Isopropylbenzene	2026/08/07	NC		%	30
			Methyl-tert-butylether (MTBE)	2026/08/07	NC		%	30
			Styrene	2026/08/07	NC		%	30
			Tetrachloroethene	2026/08/07	NC		%	30
			Toluene	2026/08/07	NC		%	30
			trans-1,2-dichloroethene	2026/08/07	NC		%	30
			Trichloroethene	2026/08/07	NC		%	30
			Vinyl chloride	2026/08/07	NC		%	30
			m & p-Xylene	2026/08/07	NC		%	30
			o-Xylene	2026/08/07	NC		%	30
			Xylenes (Total)	2026/08/07	NC		%	30
C369979	JAV	Matrix Spike [EKE257-12]	Chloride (Cl)	2026/08/06		103	%	80 - 120
			Sulphate (SO4)	2026/08/06		96	%	80 - 120
C369979	JAV	Spiked Blank	Chloride (Cl)	2026/08/06		99	%	80 - 120
			Sulphate (SO4)	2026/08/06		96	%	80 - 120
C369979	JAV	Method Blank	Chloride (Cl)	2026/08/06	ND, RDL=1.0		mg/L	
			Sulphate (SO4)	2026/08/06	ND, RDL=1.0		mg/L	
C369979	JAV	RPD [EKE257-12]	Chloride (Cl)	2026/08/06	NC		%	20
			Sulphate (SO4)	2026/08/06	NC		%	20
C369986	TSO	Matrix Spike	Total Ammonia (N)	2026/08/06		98	%	80 - 120
C369986	TSO	Spiked Blank	Total Ammonia (N)	2026/08/06		103	%	80 - 120
C369986	TSO	Method Blank	Total Ammonia (N)	2026/08/06	ND, RDL=0.015		mg/L	
C369986	TSO	RPD	Total Ammonia (N)	2026/08/06	NC		%	20
C369991	JGL	Matrix Spike [EKE256-12]	Nitrate plus Nitrite (N)	2026/08/06		117	%	80 - 120
C369991	JGL	Spiked Blank	Nitrate plus Nitrite (N)	2026/08/06		108	%	80 - 120
C369991	JGL	Method Blank	Nitrate plus Nitrite (N)	2026/08/06	ND, RDL=0.020		mg/L	
C369991	JGL	RPD [EKE256-12]	Nitrate plus Nitrite (N)	2026/08/06	NC		%	20
C370011	JGL	Matrix Spike [EKE256-12]	Nitrite (N)	2026/08/06		107	%	80 - 120
C370011	JGL	Spiked Blank	Nitrite (N)	2026/08/06		104	%	80 - 120
C370011	JGL	Method Blank	Nitrite (N)	2026/08/06	ND, RDL=0.0050		mg/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C370011	JGL	RPD [EKE256-12]	Nitrite (N)	2026/08/06	NC		%	20
C370012	SPP	Matrix Spike [EKE256-02]	Total Suspended Solids	2026/08/07		105	%	80 - 120
C370012	SPP	Spiked Blank	Total Suspended Solids	2026/08/07		96	%	80 - 120
C370012	SPP	Method Blank	Total Suspended Solids	2026/08/07	ND, RDL=1.0		mg/L	
C370012	SPP	RPD [EKE255-02]	Total Suspended Solids	2026/08/07	0		%	20
C370219	BB3	Matrix Spike	Dissolved Fluoride (F)	2026/08/06		97	%	80 - 120
C370219	BB3	Spiked Blank	Dissolved Fluoride (F)	2026/08/06		96	%	80 - 120
C370219	BB3	Method Blank	Dissolved Fluoride (F)	2026/08/06	ND, RDL=0.050		mg/L	
C370219	BB3	RPD	Fluoride (F)	2026/08/06	1.5		%	20
C370266	BB3	Spiked Blank	pH	2026/08/07		100	%	97 - 103
C370266	BB3	RPD	pH	2026/08/07	0.99		%	N/A
C370269	BB3	Spiked Blank	Alkalinity (Total as CaCO3)	2026/08/07		95	%	80 - 120
C370269	BB3	Method Blank	Alkalinity (PP as CaCO3)	2026/08/07	ND, RDL=1.0		mg/L	
			Alkalinity (Total as CaCO3)	2026/08/07	ND, RDL=1.0		mg/L	
			Bicarbonate (HCO3)	2026/08/07	ND, RDL=1.0		mg/L	
			Carbonate (CO3)	2026/08/07	ND, RDL=1.0		mg/L	
			Hydroxide (OH)	2026/08/07	ND, RDL=1.0		mg/L	
C370269	BB3	RPD	Alkalinity (PP as CaCO3)	2026/08/07	NC		%	20
			Alkalinity (Total as CaCO3)	2026/08/07	0.052		%	20
			Bicarbonate (HCO3)	2026/08/07	0.052		%	20
			Carbonate (CO3)	2026/08/07	NC		%	20
			Hydroxide (OH)	2026/08/07	NC		%	20
C370805	AA1	Matrix Spike	Dissolved Aluminum (Al)	2026/08/07		101	%	80 - 120
			Dissolved Antimony (Sb)	2026/08/07		107	%	80 - 120
			Dissolved Arsenic (As)	2026/08/07		106	%	80 - 120
			Dissolved Barium (Ba)	2026/08/07		102	%	80 - 120
			Dissolved Beryllium (Be)	2026/08/07		92	%	80 - 120
			Dissolved Bismuth (Bi)	2026/08/07		105	%	80 - 120
			Dissolved Boron (B)	2026/08/07		94	%	80 - 120
			Dissolved Cadmium (Cd)	2026/08/07		105	%	80 - 120
			Dissolved Cesium (Cs)	2026/08/07		102	%	80 - 120
			Dissolved Chromium (Cr)	2026/08/07		104	%	80 - 120
			Dissolved Cobalt (Co)	2026/08/07		98	%	80 - 120
			Dissolved Copper (Cu)	2026/08/07		101	%	80 - 120
			Dissolved Iron (Fe)	2026/08/07		102	%	80 - 120
			Dissolved Lead (Pb)	2026/08/07		103	%	80 - 120
			Dissolved Lithium (Li)	2026/08/07		90	%	80 - 120
			Dissolved Manganese (Mn)	2026/08/07		104	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/08/07		112	%	80 - 120
			Dissolved Nickel (Ni)	2026/08/07		102	%	80 - 120
			Dissolved Phosphorus (P)	2026/08/07		103	%	80 - 120
			Dissolved Rubidium (Rb)	2026/08/07		101	%	80 - 120
			Dissolved Selenium (Se)	2026/08/07		104	%	80 - 120
			Dissolved Silicon (Si)	2026/08/07		102	%	80 - 120
			Dissolved Silver (Ag)	2026/08/07		105	%	80 - 120
			Dissolved Strontium (Sr)	2026/08/07		104	%	80 - 120



Bureau Veritas Job #: C649494

Report Date: 2026/08/13

HATFIELD CONSULTANTS

Client Project #: FORTIS11234/PE110163

Site Location: WOODFIBRE PIPELINE PROJECT

Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C370805	AA1	Spiked Blank	Dissolved Tellurium (Te)	2026/08/07		112	%	80 - 120
			Dissolved Thallium (Tl)	2026/08/07		104	%	80 - 120
			Dissolved Thorium (Th)	2026/08/07		103	%	80 - 120
			Dissolved Tin (Sn)	2026/08/07		105	%	80 - 120
			Dissolved Titanium (Ti)	2026/08/07		107	%	80 - 120
			Dissolved Uranium (U)	2026/08/07		102	%	80 - 120
			Dissolved Vanadium (V)	2026/08/07		104	%	80 - 120
			Dissolved Zinc (Zn)	2026/08/07		104	%	80 - 120
			Dissolved Zirconium (Zr)	2026/08/07		106	%	80 - 120
			Dissolved Aluminum (Al)	2026/08/07		103	%	80 - 120
			Dissolved Antimony (Sb)	2026/08/07		105	%	80 - 120
			Dissolved Arsenic (As)	2026/08/07		105	%	80 - 120
			Dissolved Barium (Ba)	2026/08/07		103	%	80 - 120
			Dissolved Beryllium (Be)	2026/08/07		98	%	80 - 120
			Dissolved Bismuth (Bi)	2026/08/07		107	%	80 - 120
			Dissolved Boron (B)	2026/08/07		98	%	80 - 120
			Dissolved Cadmium (Cd)	2026/08/07		104	%	80 - 120
			Dissolved Cesium (Cs)	2026/08/07		102	%	80 - 120
			Dissolved Chromium (Cr)	2026/08/07		104	%	80 - 120
			Dissolved Cobalt (Co)	2026/08/07		98	%	80 - 120
			Dissolved Copper (Cu)	2026/08/07		102	%	80 - 120
			Dissolved Iron (Fe)	2026/08/07		103	%	80 - 120
			Dissolved Lead (Pb)	2026/08/07		104	%	80 - 120
			Dissolved Lithium (Li)	2026/08/07		97	%	80 - 120
			Dissolved Manganese (Mn)	2026/08/07		103	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/08/07		109	%	80 - 120
			Dissolved Nickel (Ni)	2026/08/07		102	%	80 - 120
			Dissolved Phosphorus (P)	2026/08/07		105	%	80 - 120
			Dissolved Rubidium (Rb)	2026/08/07		101	%	80 - 120
			Dissolved Selenium (Se)	2026/08/07		105	%	80 - 120
			Dissolved Silicon (Si)	2026/08/07		107	%	80 - 120
			Dissolved Silver (Ag)	2026/08/07		104	%	80 - 120
			Dissolved Strontium (Sr)	2026/08/07		103	%	80 - 120
			Dissolved Tellurium (Te)	2026/08/07		108	%	80 - 120
			Dissolved Thallium (Tl)	2026/08/07		106	%	80 - 120
			Dissolved Thorium (Th)	2026/08/07		104	%	80 - 120
			Dissolved Tin (Sn)	2026/08/07		106	%	80 - 120
			Dissolved Titanium (Ti)	2026/08/07		106	%	80 - 120
			Dissolved Uranium (U)	2026/08/07		104	%	80 - 120
			Dissolved Vanadium (V)	2026/08/07		104	%	80 - 120
			Dissolved Zinc (Zn)	2026/08/07		103	%	80 - 120
			Dissolved Zirconium (Zr)	2026/08/07		103	%	80 - 120
C370805	AA1	Method Blank	Dissolved Aluminum (Al)	2026/08/07	ND, RDL=0.50		ug/L	
			Dissolved Antimony (Sb)	2026/08/07	ND, RDL=0.020		ug/L	
			Dissolved Arsenic (As)	2026/08/07	ND, RDL=0.020		ug/L	
			Dissolved Barium (Ba)	2026/08/07	ND, RDL=0.020		ug/L	
			Dissolved Beryllium (Be)	2026/08/07	ND, RDL=0.010		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Dissolved Bismuth (Bi)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Boron (B)	2026/08/07	ND, RDL=10		ug/L	
			Dissolved Cadmium (Cd)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Cesium (Cs)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Chromium (Cr)	2026/08/07	ND, RDL=0.10		ug/L	
			Dissolved Cobalt (Co)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Copper (Cu)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Iron (Fe)	2026/08/07	ND, RDL=1.0		ug/L	
			Dissolved Lead (Pb)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Lithium (Li)	2026/08/07	ND, RDL=0.50		ug/L	
			Dissolved Manganese (Mn)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Molybdenum (Mo)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Nickel (Ni)	2026/08/07	ND, RDL=0.020		ug/L	
			Dissolved Phosphorus (P)	2026/08/07	ND, RDL=2.0		ug/L	
			Dissolved Rubidium (Rb)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Selenium (Se)	2026/08/07	ND, RDL=0.040		ug/L	
			Dissolved Silicon (Si)	2026/08/07	ND, RDL=50		ug/L	
			Dissolved Silver (Ag)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Strontium (Sr)	2026/08/07	ND, RDL=0.050		ug/L	
			Dissolved Tellurium (Te)	2026/08/07	ND, RDL=0.020		ug/L	
			Dissolved Thallium (Tl)	2026/08/07	ND, RDL=0.0020		ug/L	
			Dissolved Thorium (Th)	2026/08/07	ND, RDL=0.0050		ug/L	
			Dissolved Tin (Sn)	2026/08/07	ND, RDL=0.20		ug/L	
			Dissolved Titanium (Ti)	2026/08/07	ND, RDL=0.50		ug/L	
			Dissolved Uranium (U)	2026/08/07	ND, RDL=0.0020		ug/L	
			Dissolved Vanadium (V)	2026/08/07	ND, RDL=0.20		ug/L	
			Dissolved Zinc (Zn)	2026/08/07	ND, RDL=0.10		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Dissolved Zirconium (Zr)	2026/08/07	ND, RDL=0.10		ug/L	
C370805	AA1	RPD	Dissolved Aluminum (Al)	2026/08/07	1.5		%	20
			Dissolved Antimony (Sb)	2026/08/07	NC		%	20
			Dissolved Arsenic (As)	2026/08/07	0.70		%	20
			Dissolved Barium (Ba)	2026/08/07	2.8		%	20
			Dissolved Beryllium (Be)	2026/08/07	NC		%	20
			Dissolved Bismuth (Bi)	2026/08/07	NC		%	20
			Dissolved Boron (B)	2026/08/07	NC		%	20
			Dissolved Cadmium (Cd)	2026/08/07	5.6		%	20
			Dissolved Chromium (Cr)	2026/08/07	NC		%	20
			Dissolved Cobalt (Co)	2026/08/07	4.1		%	20
			Dissolved Copper (Cu)	2026/08/07	2.0		%	20
			Dissolved Iron (Fe)	2026/08/07	1.7		%	20
			Dissolved Lead (Pb)	2026/08/07	2.0		%	20
			Dissolved Lithium (Li)	2026/08/07	NC		%	20
			Dissolved Manganese (Mn)	2026/08/07	1.6		%	20
			Dissolved Molybdenum (Mo)	2026/08/07	3.6		%	20
			Dissolved Nickel (Ni)	2026/08/07	NC		%	20
			Dissolved Phosphorus (P)	2026/08/07	NC		%	20
			Dissolved Selenium (Se)	2026/08/07	NC		%	20
			Dissolved Silicon (Si)	2026/08/07	0.66		%	20
			Dissolved Silver (Ag)	2026/08/07	NC		%	20
			Dissolved Strontium (Sr)	2026/08/07	1.4		%	20
			Dissolved Thallium (Tl)	2026/08/07	NC		%	20
			Dissolved Tin (Sn)	2026/08/07	NC		%	20
			Dissolved Titanium (Ti)	2026/08/07	NC		%	20
			Dissolved Uranium (U)	2026/08/07	5.1		%	20
			Dissolved Vanadium (V)	2026/08/07	9.1		%	20
			Dissolved Zinc (Zn)	2026/08/07	0.22		%	20
			Dissolved Zirconium (Zr)	2026/08/07	NC		%	20
C370940	CJY	Matrix Spike	Total Organic Carbon (C)	2026/08/07		123 (1)	%	80 - 120
C370940	CJY	Spiked Blank	Total Organic Carbon (C)	2026/08/07		117	%	80 - 120
C370940	CJY	Method Blank	Total Organic Carbon (C)	2026/08/07	ND, RDL=0.50		mg/L	
C370940	CJY	RPD	Total Organic Carbon (C)	2026/08/07	5.6		%	20
C370948	JST	Spiked Blank	D10-ANTHRACENE (sur.)	2026/08/07		101	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/08/07		96	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/08/07		84	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/08/07		91	%	50 - 140
			Quinoline	2026/08/07		101	%	50 - 140
			Naphthalene	2026/08/07		82	%	50 - 140
			1-Methylnaphthalene	2026/08/07		88	%	50 - 140
			2-Methylnaphthalene	2026/08/07		85	%	50 - 140
			Acenaphthylene	2026/08/07		91	%	50 - 140
			Acenaphthene	2026/08/07		91	%	50 - 140
			Fluorene	2026/08/07		89	%	50 - 140
			Phenanthrene	2026/08/07		91	%	50 - 140
			Anthracene	2026/08/07		91	%	50 - 140
			Acridine	2026/08/07		91	%	50 - 140
			Fluoranthene	2026/08/07		91	%	50 - 140
			Pyrene	2026/08/07		86	%	50 - 140
			Benzo(a)anthracene	2026/08/07		95	%	50 - 140



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C370948	JST	Method Blank	Chrysene	2026/08/07		99	%	50 - 140
			Benzo(b&j)fluoranthene	2026/08/07		103	%	50 - 140
			Benzo(k)fluoranthene	2026/08/07		105	%	50 - 140
			Benzo(a)pyrene	2026/08/07		96	%	50 - 140
			Indeno(1,2,3-cd)pyrene	2026/08/07		98	%	50 - 140
			Dibenz(a,h)anthracene	2026/08/07		95	%	50 - 140
			Benzo(g,h,i)perylene	2026/08/07		97	%	50 - 140
			D10-ANTHRACENE (sur.)	2026/08/07		105	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/08/07		99	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/08/07		85	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/08/07		96	%	50 - 140
			Quinoline	2026/08/07	ND, RDL=0.020		ug/L	
			Naphthalene	2026/08/07	ND, RDL=0.10		ug/L	
			1-Methylnaphthalene	2026/08/07	ND, RDL=0.050		ug/L	
			2-Methylnaphthalene	2026/08/07	ND, RDL=0.10		ug/L	
			Acenaphthylene	2026/08/07	ND, RDL=0.050		ug/L	
			Acenaphthene	2026/08/07	ND, RDL=0.050		ug/L	
			Fluorene	2026/08/07	ND, RDL=0.050		ug/L	
			Phenanthrene	2026/08/07	ND, RDL=0.050		ug/L	
			Anthracene	2026/08/07	ND, RDL=0.010		ug/L	
			Acridine	2026/08/07	ND, RDL=0.050		ug/L	
			Fluoranthene	2026/08/07	ND, RDL=0.020		ug/L	
			Pyrene	2026/08/07	ND, RDL=0.020		ug/L	
			Benzo(a)anthracene	2026/08/07	ND, RDL=0.010		ug/L	
			Chrysene	2026/08/07	ND, RDL=0.020		ug/L	
			Benzo(b&j)fluoranthene	2026/08/07	ND, RDL=0.030		ug/L	
			Benzo(k)fluoranthene	2026/08/07	ND, RDL=0.050		ug/L	
			Benzo(a)pyrene	2026/08/07	ND, RDL=0.0050		ug/L	
			Indeno(1,2,3-cd)pyrene	2026/08/07	ND, RDL=0.050		ug/L	
			Dibenz(a,h)anthracene	2026/08/07	ND, RDL=0.0030		ug/L	
			Benzo(g,h,i)perylene	2026/08/07	ND, RDL=0.050		ug/L	
C370952	RYA	Spiked Blank	O-TERPHENYL (sur.)	2026/08/07		103	%	60 - 140
			EPH (C10-C19)	2026/08/07		96	%	70 - 130
			EPH (C19-C32)	2026/08/07		105	%	70 - 130



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C370952	RYA	Method Blank	O-TERPHENYL (sur.)	2026/08/07		102	%	60 - 140
			EPH (C10-C19)	2026/08/07	ND, RDL=0.20		mg/L	
			EPH (C19-C32)	2026/08/07	ND, RDL=0.20		mg/L	
C371141	TSO	Matrix Spike	Total Nitrogen (N)	2026/08/10		NC	%	80 - 120
C371141	TSO	Spiked Blank	Total Nitrogen (N)	2026/08/10		104	%	80 - 120
C371141	TSO	Method Blank	Total Nitrogen (N)	2026/08/10	ND, RDL=0.020		mg/L	
C371141	TSO	RPD	Total Nitrogen (N)	2026/08/10	0.65		%	20
C371159	MEM	Matrix Spike	Total Mercury (Hg)	2026/08/07		99	%	80 - 120
C371159	MEM	Spiked Blank	Total Mercury (Hg)	2026/08/07		108	%	80 - 120
C371159	MEM	Method Blank	Total Mercury (Hg)	2026/08/07	ND, RDL=0.0019		ug/L	
C371159	MEM	RPD	Total Mercury (Hg)	2026/08/07	9.2		%	20
C371166	MEM	Matrix Spike [EKE254-06]	Total Mercury (Hg)	2026/08/07		104	%	80 - 120
C371166	MEM	Spiked Blank	Total Mercury (Hg)	2026/08/07		106	%	80 - 120
C371166	MEM	Method Blank	Total Mercury (Hg)	2026/08/07	ND, RDL=0.0019		ug/L	
C371166	MEM	RPD [EKE254-06]	Total Mercury (Hg)	2026/08/07	NC		%	20
C371183	SPP	Matrix Spike [EKE254-03]	Total Dissolved Solids	2026/08/08		99	%	80 - 120
C371183	SPP	Spiked Blank	Total Dissolved Solids	2026/08/08		96	%	80 - 120
C371183	SPP	Method Blank	Total Dissolved Solids	2026/08/08	ND, RDL=10		mg/L	
C371183	SPP	RPD [EKE253-03]	Total Dissolved Solids	2026/08/08	8.0		%	20
C371380	CJY	Matrix Spike	Dissolved Organic Carbon (C)	2026/08/08		119	%	80 - 120
C371380	CJY	Spiked Blank	Dissolved Organic Carbon (C)	2026/08/07		114	%	80 - 120
C371380	CJY	Method Blank	Dissolved Organic Carbon (C)	2026/08/07	ND, RDL=0.50		mg/L	
C371380	CJY	RPD	Dissolved Organic Carbon (C)	2026/08/08	6.8		%	20
C372109	AA1	Matrix Spike	Total Aluminum (Al)	2026/08/10		101	%	80 - 120
			Total Antimony (Sb)	2026/08/10		101	%	80 - 120
			Total Arsenic (As)	2026/08/10		103	%	80 - 120
			Total Barium (Ba)	2026/08/10		100	%	80 - 120
			Total Beryllium (Be)	2026/08/10		101	%	80 - 120
			Total Bismuth (Bi)	2026/08/10		98	%	80 - 120
			Total Boron (B)	2026/08/10		98	%	80 - 120
			Total Cadmium (Cd)	2026/08/10		101	%	80 - 120
			Total Cesium (Cs)	2026/08/10		100	%	80 - 120
			Total Chromium (Cr)	2026/08/10		97	%	80 - 120
			Total Cobalt (Co)	2026/08/10		93	%	80 - 120
			Total Copper (Cu)	2026/08/10		94	%	80 - 120
			Total Iron (Fe)	2026/08/10		100	%	80 - 120
			Total Lead (Pb)	2026/08/10		96	%	80 - 120
			Total Lithium (Li)	2026/08/10		96	%	80 - 120
			Total Manganese (Mn)	2026/08/10		98	%	80 - 120
			Total Molybdenum (Mo)	2026/08/10		105	%	80 - 120
			Total Nickel (Ni)	2026/08/10		95	%	80 - 120
			Total Phosphorus (P)	2026/08/10		101	%	80 - 120
			Total Rubidium (Rb)	2026/08/10		98	%	80 - 120
			Total Selenium (Se)	2026/08/10		102	%	80 - 120
			Total Silicon (Si)	2026/08/10		105	%	80 - 120
			Total Silver (Ag)	2026/08/10		99	%	80 - 120



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C372109	AA1	Spiked Blank	Total Strontium (Sr)	2026/08/10		104	%	80 - 120
			Total Tellurium (Te)	2026/08/10		103	%	80 - 120
			Total Thallium (Tl)	2026/08/10		100	%	80 - 120
			Total Thorium (Th)	2026/08/10		101	%	80 - 120
			Total Tin (Sn)	2026/08/10		102	%	80 - 120
			Total Titanium (Ti)	2026/08/10		100	%	80 - 120
			Total Uranium (U)	2026/08/10		103	%	80 - 120
			Total Vanadium (V)	2026/08/10		100	%	80 - 120
			Total Zinc (Zn)	2026/08/10		98	%	80 - 120
			Total Zirconium (Zr)	2026/08/10		105	%	80 - 120
			Total Aluminum (Al)	2026/08/10		109	%	80 - 120
			Total Antimony (Sb)	2026/08/10		107	%	80 - 120
			Total Arsenic (As)	2026/08/10		106	%	80 - 120
			Total Barium (Ba)	2026/08/10		104	%	80 - 120
			Total Beryllium (Be)	2026/08/10		107	%	80 - 120
			Total Bismuth (Bi)	2026/08/10		104	%	80 - 120
			Total Boron (B)	2026/08/10		107	%	80 - 120
			Total Cadmium (Cd)	2026/08/10		105	%	80 - 120
			Total Cesium (Cs)	2026/08/10		105	%	80 - 120
			Total Chromium (Cr)	2026/08/10		105	%	80 - 120
			Total Cobalt (Co)	2026/08/10		99	%	80 - 120
			Total Copper (Cu)	2026/08/10		102	%	80 - 120
			Total Iron (Fe)	2026/08/10		105	%	80 - 120
			Total Lead (Pb)	2026/08/10		102	%	80 - 120
			Total Lithium (Li)	2026/08/10		103	%	80 - 120
			Total Manganese (Mn)	2026/08/10		104	%	80 - 120
			Total Molybdenum (Mo)	2026/08/10		107	%	80 - 120
			Total Nickel (Ni)	2026/08/10		103	%	80 - 120
			Total Phosphorus (P)	2026/08/10		109	%	80 - 120
			Total Rubidium (Rb)	2026/08/10		106	%	80 - 120
			Total Selenium (Se)	2026/08/10		105	%	80 - 120
			Total Silicon (Si)	2026/08/10		110	%	80 - 120
			Total Silver (Ag)	2026/08/10		103	%	80 - 120
			Total Strontium (Sr)	2026/08/10		106	%	80 - 120
			Total Tellurium (Te)	2026/08/10		109	%	80 - 120
			Total Thallium (Tl)	2026/08/10		104	%	80 - 120
			Total Thorium (Th)	2026/08/10		108	%	80 - 120
			Total Tin (Sn)	2026/08/10		107	%	80 - 120
			Total Titanium (Ti)	2026/08/10		105	%	80 - 120
			Total Uranium (U)	2026/08/10		107	%	80 - 120
			Total Vanadium (V)	2026/08/10		106	%	80 - 120
			Total Zinc (Zn)	2026/08/10		105	%	80 - 120
			Total Zirconium (Zr)	2026/08/10		108	%	80 - 120
C372109	AA1	Method Blank	Total Aluminum (Al)	2026/08/10	ND, RDL=0.50		ug/L	
			Total Antimony (Sb)	2026/08/10	ND, RDL=0.020		ug/L	
			Total Arsenic (As)	2026/08/10	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/08/10	ND, RDL=0.020		ug/L	
			Total Beryllium (Be)	2026/08/10	ND, RDL=0.010		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Bismuth (Bi)	2026/08/10	ND, RDL=0.0050		ug/L	
			Total Boron (B)	2026/08/10	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/08/10	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/08/10	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/08/10	ND, RDL=0.0050		ug/L	
			Total Copper (Cu)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Iron (Fe)	2026/08/10	ND, RDL=1.0		ug/L	
			Total Lead (Pb)	2026/08/10	ND, RDL=0.0050		ug/L	
			Total Lithium (Li)	2026/08/10	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Molybdenum (Mo)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/08/10	ND, RDL=0.020		ug/L	
			Total Phosphorus (P)	2026/08/10	ND, RDL=2.0		ug/L	
			Total Rubidium (Rb)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/08/10	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/08/10	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/08/10	ND, RDL=0.0050		ug/L	
			Total Strontium (Sr)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/08/10	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/08/10	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/08/10	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/08/10	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/08/10	ND, RDL=0.50		ug/L	
			Total Uranium (U)	2026/08/10	ND, RDL=0.0020		ug/L	
			Total Vanadium (V)	2026/08/10	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/08/10	ND, RDL=0.10		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C372109	AA1	RPD	Total Zirconium (Zr)	2026/08/10	ND, RDL=0.10		ug/L	
			Total Aluminum (Al)	2026/08/10	10		%	20
			Total Arsenic (As)	2026/08/10	0.52		%	20
			Total Cadmium (Cd)	2026/08/10	NC		%	20
			Total Cobalt (Co)	2026/08/10	3.9		%	20
			Total Copper (Cu)	2026/08/10	2.0		%	20
			Total Lead (Pb)	2026/08/10	0.18		%	20
			Total Molybdenum (Mo)	2026/08/10	3.2		%	20
			Total Phosphorus (P)	2026/08/10	11		%	20
			Total Selenium (Se)	2026/08/10	NC		%	20
			Total Thallium (Tl)	2026/08/10	NC		%	20
			Total Uranium (U)	2026/08/10	1.2		%	20
			Total Vanadium (V)	2026/08/10	NC		%	20
			Total Zinc (Zn)	2026/08/10	4.4		%	20
			Total Aluminum (Al)	2026/08/10	NC		%	20
			Total Antimony (Sb)	2026/08/10	NC		%	20
			Total Arsenic (As)	2026/08/10	NC		%	20
			Total Barium (Ba)	2026/08/10	NC		%	20
			Total Beryllium (Be)	2026/08/10	NC		%	20
			Total Bismuth (Bi)	2026/08/10	NC		%	20
			Total Boron (B)	2026/08/10	NC		%	20
			Total Cadmium (Cd)	2026/08/10	NC		%	20
			Total Chromium (Cr)	2026/08/10	NC		%	20
			Total Cobalt (Co)	2026/08/10	NC		%	20
			Total Copper (Cu)	2026/08/10	NC		%	20
			Total Iron (Fe)	2026/08/10	NC		%	20
			Total Lead (Pb)	2026/08/10	7.4		%	20
			Total Lithium (Li)	2026/08/10	NC		%	20
			Total Manganese (Mn)	2026/08/10	NC		%	20
			Total Molybdenum (Mo)	2026/08/10	NC		%	20
			Total Nickel (Ni)	2026/08/10	NC		%	20
			Total Selenium (Se)	2026/08/10	NC		%	20
			Total Silicon (Si)	2026/08/10	NC		%	20
			Total Silver (Ag)	2026/08/10	NC		%	20
			Total Strontium (Sr)	2026/08/10	NC		%	20
			Total Thallium (Tl)	2026/08/10	NC		%	20
			Total Tin (Sn)	2026/08/10	NC		%	20
			Total Titanium (Ti)	2026/08/10	NC		%	20
			Total Uranium (U)	2026/08/10	NC		%	20
			Total Vanadium (V)	2026/08/10	NC		%	20
			Total Zinc (Zn)	2026/08/10	3.7		%	20
			Total Zirconium (Zr)	2026/08/10	NC		%	20
C372871	AAX	Matrix Spike [EKE254-14]	Methyl Sulfone (sur.)	2026/08/10		93	%	50 - 140
			Ethylene Glycol	2026/08/10		85	%	60 - 140
			Diethylene Glycol	2026/08/10		103	%	60 - 140
			Triethylene Glycol	2026/08/10		88	%	60 - 140
			Propylene Glycol	2026/08/10		87	%	60 - 140
C372871	AAX	Spiked Blank	Methyl Sulfone (sur.)	2026/08/10		100	%	50 - 140
			Ethylene Glycol	2026/08/10		92	%	70 - 130
			Diethylene Glycol	2026/08/10		108	%	70 - 130
			Triethylene Glycol	2026/08/10		94	%	70 - 130
			Propylene Glycol	2026/08/10		89	%	70 - 130



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C372871	AAX	Method Blank	Methyl Sulfone (sur.)	2026/08/10		96	%	50 - 140
			Ethylene Glycol	2026/08/10	ND, RDL=3.0		mg/L	
			Diethylene Glycol	2026/08/10	ND, RDL=5.0		mg/L	
			Triethylene Glycol	2026/08/10	ND, RDL=5.0		mg/L	
			Propylene Glycol	2026/08/10	ND, RDL=5.0		mg/L	
C372871	AAX	RPD	Ethylene Glycol	2026/08/10	NC		%	30
			Diethylene Glycol	2026/08/10	NC		%	30
			Triethylene Glycol	2026/08/10	NC		%	30
			Propylene Glycol	2026/08/10	NC		%	30
C372904	JLD	Matrix Spike	Phenols	2026/08/10		4.0 (1)	%	80 - 120
C372904	JLD	Spiked Blank	Phenols	2026/08/10		99	%	80 - 120
C372904	JLD	Method Blank	Phenols	2026/08/10	ND, RDL=0.0015		mg/L	
C372904	JLD	RPD	Phenols	2026/08/10	3.8		%	20
C372971	AA1	Matrix Spike [EKE255-10]	Total Aluminum (Al)	2026/08/11		94	%	80 - 120
			Total Antimony (Sb)	2026/08/11		105	%	80 - 120
			Total Arsenic (As)	2026/08/11		104	%	80 - 120
			Total Barium (Ba)	2026/08/11		103	%	80 - 120
			Total Beryllium (Be)	2026/08/11		100	%	80 - 120
			Total Bismuth (Bi)	2026/08/11		99	%	80 - 120
			Total Boron (B)	2026/08/11		102	%	80 - 120
			Total Cadmium (Cd)	2026/08/11		103	%	80 - 120
			Total Cesium (Cs)	2026/08/11		101	%	80 - 120
			Total Chromium (Cr)	2026/08/11		103	%	80 - 120
			Total Cobalt (Co)	2026/08/11		101	%	80 - 120
			Total Copper (Cu)	2026/08/11		100	%	80 - 120
			Total Iron (Fe)	2026/08/11		98	%	80 - 120
			Total Lead (Pb)	2026/08/11		99	%	80 - 120
			Total Lithium (Li)	2026/08/11		97	%	80 - 120
			Total Manganese (Mn)	2026/08/11		101	%	80 - 120
			Total Molybdenum (Mo)	2026/08/11		108	%	80 - 120
			Total Nickel (Ni)	2026/08/11		101	%	80 - 120
			Total Phosphorus (P)	2026/08/11		98	%	80 - 120
			Total Rubidium (Rb)	2026/08/11		104	%	80 - 120
			Total Selenium (Se)	2026/08/11		104	%	80 - 120
			Total Silicon (Si)	2026/08/11		94	%	80 - 120
			Total Silver (Ag)	2026/08/11		101	%	80 - 120
			Total Strontium (Sr)	2026/08/11		104	%	80 - 120
			Total Tellurium (Te)	2026/08/11		112	%	80 - 120
			Total Thallium (Tl)	2026/08/11		101	%	80 - 120
			Total Thorium (Th)	2026/08/11		106	%	80 - 120
			Total Tin (Sn)	2026/08/11		103	%	80 - 120
			Total Titanium (Ti)	2026/08/11		103	%	80 - 120
			Total Uranium (U)	2026/08/11		108	%	80 - 120
			Total Vanadium (V)	2026/08/11		103	%	80 - 120
			Total Zinc (Zn)	2026/08/11		103	%	80 - 120
			Total Zirconium (Zr)	2026/08/11		102	%	80 - 120
C372971	AA1	Spiked Blank	Total Aluminum (Al)	2026/08/11		92	%	80 - 120
			Total Antimony (Sb)	2026/08/11		102	%	80 - 120



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C372971	AA1	Method Blank	Total Arsenic (As)	2026/08/11		102	%	80 - 120
			Total Barium (Ba)	2026/08/11		100	%	80 - 120
			Total Beryllium (Be)	2026/08/11		96	%	80 - 120
			Total Bismuth (Bi)	2026/08/11		99	%	80 - 120
			Total Boron (B)	2026/08/11		100	%	80 - 120
			Total Cadmium (Cd)	2026/08/11		102	%	80 - 120
			Total Cesium (Cs)	2026/08/11		101	%	80 - 120
			Total Chromium (Cr)	2026/08/11		103	%	80 - 120
			Total Cobalt (Co)	2026/08/11		101	%	80 - 120
			Total Copper (Cu)	2026/08/11		99	%	80 - 120
			Total Iron (Fe)	2026/08/11		97	%	80 - 120
			Total Lead (Pb)	2026/08/11		98	%	80 - 120
			Total Lithium (Li)	2026/08/11		95	%	80 - 120
			Total Manganese (Mn)	2026/08/11		99	%	80 - 120
			Total Molybdenum (Mo)	2026/08/11		106	%	80 - 120
			Total Nickel (Ni)	2026/08/11		100	%	80 - 120
			Total Phosphorus (P)	2026/08/11		97	%	80 - 120
			Total Rubidium (Rb)	2026/08/11		104	%	80 - 120
			Total Selenium (Se)	2026/08/11		101	%	80 - 120
			Total Silicon (Si)	2026/08/11		99	%	80 - 120
			Total Silver (Ag)	2026/08/11		99	%	80 - 120
			Total Strontium (Sr)	2026/08/11		100	%	80 - 120
			Total Tellurium (Te)	2026/08/11		104	%	80 - 120
			Total Thallium (Tl)	2026/08/11		99	%	80 - 120
			Total Thorium (Th)	2026/08/11		102	%	80 - 120
			Total Tin (Sn)	2026/08/11		103	%	80 - 120
			Total Titanium (Ti)	2026/08/11		102	%	80 - 120
			Total Uranium (U)	2026/08/11		100	%	80 - 120
			Total Vanadium (V)	2026/08/11		102	%	80 - 120
			Total Zinc (Zn)	2026/08/11		102	%	80 - 120
			Total Zirconium (Zr)	2026/08/11		99	%	80 - 120
			Total Aluminum (Al)	2026/08/11	ND, RDL=3.0		ug/L	
			Total Antimony (Sb)	2026/08/11	ND, RDL=0.020		ug/L	
			Total Arsenic (As)	2026/08/11	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Beryllium (Be)	2026/08/11	ND, RDL=0.010		ug/L	
			Total Bismuth (Bi)	2026/08/11	ND, RDL=0.010		ug/L	
			Total Boron (B)	2026/08/11	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/08/11	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/08/11	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/08/11	ND, RDL=0.010		ug/L	



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Copper (Cu)	2026/08/11	ND, RDL=0.10		ug/L	
			Total Iron (Fe)	2026/08/11	ND, RDL=5.0		ug/L	
			Total Lead (Pb)	2026/08/11	ND, RDL=0.020		ug/L	
			Total Lithium (Li)	2026/08/11	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/08/11	ND, RDL=0.10		ug/L	
			Total Molybdenum (Mo)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/08/11	ND, RDL=0.10		ug/L	
			Total Phosphorus (P)	2026/08/11	ND, RDL=5.0		ug/L	
			Total Rubidium (Rb)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/08/11	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/08/11	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/08/11	ND, RDL=0.010		ug/L	
			Total Strontium (Sr)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/08/11	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/08/11	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/08/11	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/08/11	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/08/11	ND, RDL=2.0		ug/L	
			Total Uranium (U)	2026/08/11	ND, RDL=0.0050		ug/L	
			Total Vanadium (V)	2026/08/11	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/08/11	ND, RDL=1.0		ug/L	
			Total Zirconium (Zr)	2026/08/11	ND, RDL=0.10		ug/L	
			Total Aluminum (Al)	2026/08/11	2.5		%	20
			Total Antimony (Sb)	2026/08/11	6.3		%	20
			Total Arsenic (As)	2026/08/11	2.0		%	20
			Total Barium (Ba)	2026/08/11	0.67		%	20
			Total Beryllium (Be)	2026/08/11	NC		%	20
			Total Bismuth (Bi)	2026/08/11	NC		%	20
			Total Boron (B)	2026/08/11	0.037		%	20
			Total Cadmium (Cd)	2026/08/11	17		%	20
			Total Cesium (Cs)	2026/08/11	NC		%	20
			Total Chromium (Cr)	2026/08/11	NC		%	20



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Cobalt (Co)	2026/08/11	16		%	20
			Total Copper (Cu)	2026/08/11	0.28		%	20
			Total Iron (Fe)	2026/08/11	0.16		%	20
			Total Lead (Pb)	2026/08/11	NC		%	20
			Total Lithium (Li)	2026/08/11	0.41		%	20
			Total Manganese (Mn)	2026/08/11	1.5		%	20
			Total Molybdenum (Mo)	2026/08/11	2.0		%	20
			Total Nickel (Ni)	2026/08/11	19		%	20
			Total Phosphorus (P)	2026/08/11	2.4		%	20
			Total Rubidium (Rb)	2026/08/11	3.0		%	20
			Total Selenium (Se)	2026/08/11	NC		%	20
			Total Silicon (Si)	2026/08/11	3.9		%	20
			Total Silver (Ag)	2026/08/11	NC		%	20
			Total Strontium (Sr)	2026/08/11	3.0		%	20
			Total Tellurium (Te)	2026/08/11	NC		%	20
			Total Thallium (Tl)	2026/08/11	1.3		%	20
			Total Thorium (Th)	2026/08/11	NC		%	20
			Total Tin (Sn)	2026/08/11	NC		%	20
			Total Titanium (Ti)	2026/08/11	NC		%	20
			Total Uranium (U)	2026/08/11	0.60		%	20
			Total Vanadium (V)	2026/08/11	NC		%	20
			Total Zinc (Zn)	2026/08/11	2.1		%	20
			Total Zirconium (Zr)	2026/08/11	NC		%	20
C372985	NJD	Matrix Spike	Total Sulphide	2026/08/11		97	%	80 - 120
C372985	NJD	Spiked Blank	Total Sulphide	2026/08/11		95	%	80 - 120
C372985	NJD	Method Blank	Total Sulphide	2026/08/11	ND, RDL=0.0018		mg/L	
C372985	NJD	RPD	Total Sulphide	2026/08/11	NC		%	20
C373023	NJD	Matrix Spike [EKE257-08]	Total Sulphide	2026/08/11		118	%	80 - 120
C373023	NJD	Spiked Blank	Total Sulphide	2026/08/11		87	%	80 - 120
C373023	NJD	Method Blank	Total Sulphide	2026/08/11	ND, RDL=0.0018		mg/L	
C373023	NJD	RPD [EKE256-08]	Total Sulphide	2026/08/11	NC		%	20
C373394	KA5	Matrix Spike [EKE256-04]	Total Phosphorus (P)	2026/08/12		132	%	N/A
C373394	KA5	Spiked Blank	Total Phosphorus (P)	2026/08/12		105	%	80 - 120
C373394	KA5	Method Blank	Total Phosphorus (P)	2026/08/12	ND, RDL=0.0010		mg/L	
C373394	KA5	RPD [EKE256-04]	Total Phosphorus (P)	2026/08/12	NC		%	20
C373874	SPP	Matrix Spike [EKE257-02]	Total Suspended Solids	2026/08/12		103	%	80 - 120
C373874	SPP	Spiked Blank	Total Suspended Solids	2026/08/12		108	%	80 - 120
C373874	SPP	Method Blank	Total Suspended Solids	2026/08/12	ND, RDL=1.0		mg/L	
C373874	SPP	RPD	Total Suspended Solids	2026/08/12	0		%	20
C373876	SPP	Matrix Spike	Total Suspended Solids	2026/08/12		101	%	80 - 120
C373876	SPP	Spiked Blank	Total Suspended Solids	2026/08/12		93	%	80 - 120
C373876	SPP	Method Blank	Total Suspended Solids	2026/08/12	ND, RDL=1.0		mg/L	
C373876	SPP	RPD	Total Suspended Solids	2026/08/12	NC		%	20
C374012	SPP	Matrix Spike [EKE257-03]	Total Dissolved Solids	2026/08/12		98	%	80 - 120
C374012	SPP	Spiked Blank	Total Dissolved Solids	2026/08/12		106	%	80 - 120
C374012	SPP	Method Blank	Total Dissolved Solids	2026/08/12	ND, RDL=10		mg/L	
C374012	SPP	RPD [EKE256-03]	Total Dissolved Solids	2026/08/12	NC		%	20



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C374026	JGL	Matrix Spike [EKE257-09]	Total Hex. Chromium (Cr 6+)	2026/08/11		91	%	80 - 120
C374026	JGL	Spiked Blank	Total Hex. Chromium (Cr 6+)	2026/08/11		105	%	80 - 120
C374026	JGL	Method Blank	Total Hex. Chromium (Cr 6+)	2026/08/11	ND, RDL=0.00099		mg/L	
C374026	JGL	RPD [EKE257-09]	Total Hex. Chromium (Cr 6+)	2026/08/11	0		%	20
C374700	MEM	Matrix Spike	Bromide (Br)	2026/08/12		83	%	78 - 120
C374700	MEM	Spiked Blank	Bromide (Br)	2026/08/12		88	%	80 - 120
C374700	MEM	Method Blank	Bromide (Br)	2026/08/12	ND, RDL=0.010		mg/L	
C374700	MEM	RPD	Bromide (Br)	2026/08/12	NC		%	20
C375500	C2L	Matrix Spike [EKE253-07]	Dissolved Mercury (Hg)	2026/08/12		102	%	80 - 120
C375500	C2L	Spiked Blank	Dissolved Mercury (Hg)	2026/08/12		114	%	80 - 120
C375500	C2L	Method Blank	Dissolved Mercury (Hg)	2026/08/12	ND, RDL=0.0019		ug/L	
C375500	C2L	RPD [EKE253-07]	Dissolved Mercury (Hg)	2026/08/12	NC		%	20

N/A = Not Applicable

Duplicate: Paired analysis of a separate portion of the same sample. Used to evaluate the variance in the measurement.

Matrix Spike: A sample to which a known amount of the analyte of interest has been added. Used to evaluate sample matrix interference.

Spiked Blank: A blank matrix sample to which a known amount of the analyte, usually from a second source, has been added. Used to evaluate method accuracy.

Method Blank: A blank matrix containing all reagents used in the analytical procedure. Used to identify laboratory contamination.

Surrogate: A pure or isotopically labeled compound whose behavior mirrors the analytes of interest. Used to evaluate extraction efficiency.

NC (Matrix Spike): The recovery in the matrix spike was not calculated. The relative difference between the concentration in the parent sample and the spike amount was too small to permit a reliable recovery calculation (matrix spike concentration was less than the native sample concentration)

NC (Duplicate RPD): The duplicate RPD was not calculated. The concentration in the sample and/or duplicate was too low to permit a reliable RPD calculation (absolute difference <= 2x RDL).

(1) Recovery or RPD for this parameter is outside control limits. The overall quality control for this analysis meets acceptability criteria.



Bureau Veritas Job #: C649494
Report Date: 2026/08/13

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

VALIDATION SIGNATURE PAGE

The analytical data and all QC contained in this report were reviewed and validated by:

David Huang, M.Sc., P.Chem., QP, Scientific Services Manager



Luba Shymushovska, B.Sc., QP, Senior Analyst, Organics

Mariel Saavedra Marquez, Project Solutions Representative

Suwan (Sze Yeung) Fock, B.Sc., Scientific Specialist

Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports. For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.

EPH in Water when PAH required Chromatogram

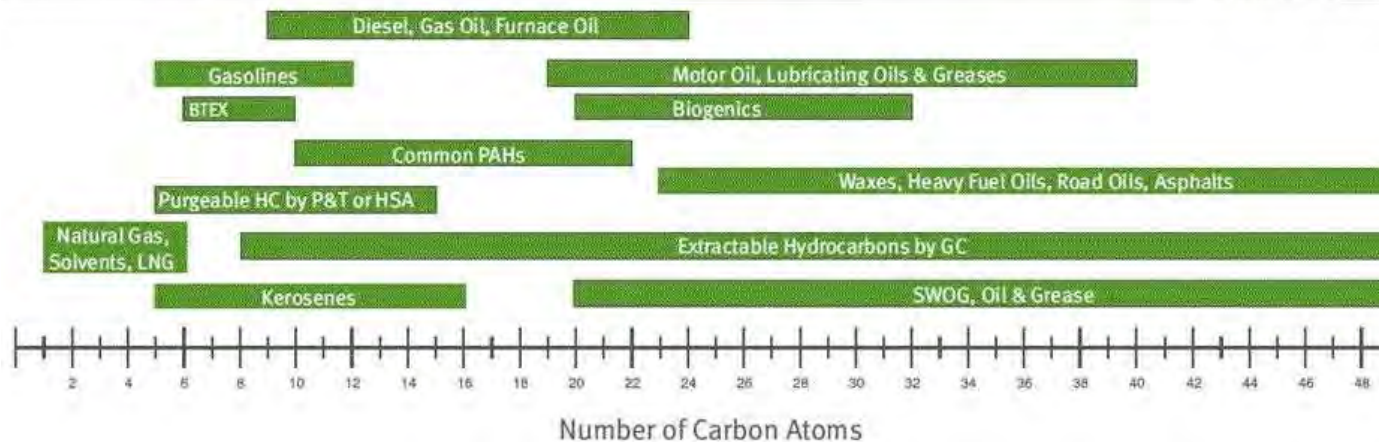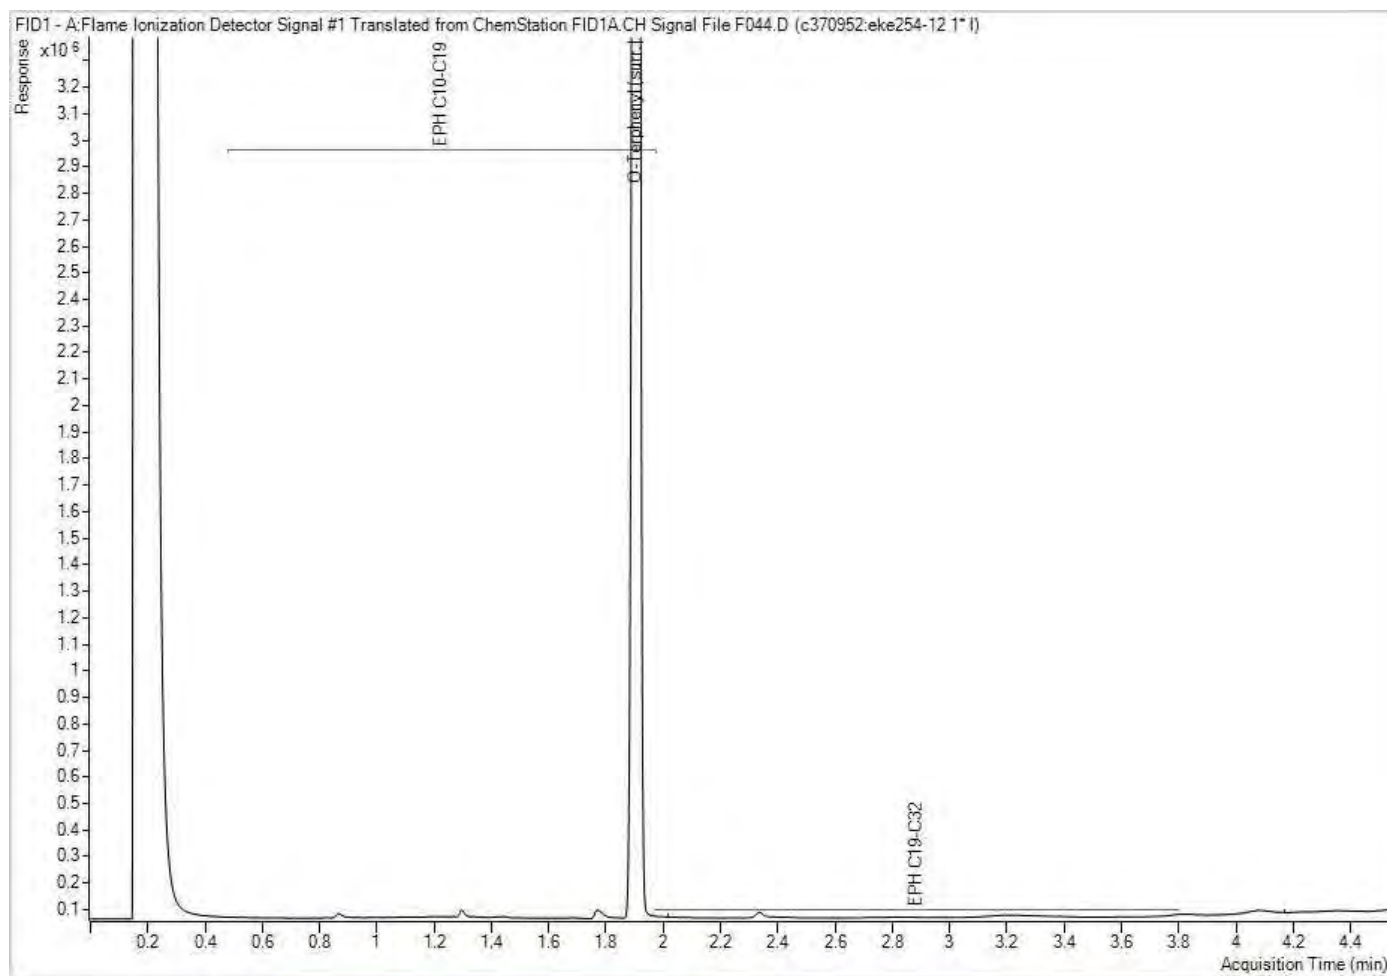

Note: This information is provided for reference purposes only. Should detailed chemist interpretation or fingerprinting be required, please contact the laboratory.



eCOC: W137689



Project Information: C649494
Job Received: 2026/08/05 16:42
Expected TAT: Standard TAT
Expected Arrival: 2026/08/05 15:30
Submitted By: Jackson Macpherson
Submitted To: Burnaby ENV: 4606
Canada Way

Invoice Information

Attn: Accounts Payable
Fortis BC Energy Inc
16705 Fraser Hwy
Surrey , BC , V4N 0E8
Email to:
einvoices@fortisbc.com

Report Information

Attn: Brett Lucas
HATFIELD CONSULTANTS
200-850 Harbourside Dr
North Vancouver , BC , V7P 0A3
Email to:
blucas@hatfieldgroup.com
danielle.samels@fortisbc.com
smangwani@hatfieldgroup.com
jmacpherson@hatfieldgroup.com
swolf@hatfieldgroup.com

Project Information

Quote #: C50083
PO/AFE#: 4800010213
Project #: Fortis11234/PE-110163
Site Location: Woodfibre Pipeline Project

Analytical Summary

A: Standard TAT

Client Sample ID	Cint Ref	Sampling Date/Time	Matrix	#Cont	Woodfibre	Woodfibre Additional	Woodfibre Blank	Set Number
WLNG-DS	1	2026/08/05 08:30	WATER	14	A			1
WLNG -EOP	2	2026/08/05 08:30	WATER	18	A	A		2
WLNG-US	3	2026/08/05 08:30	WATER	14	A			1
Field Blank	4	2026/08/05 08:30	WATER	14			A	3
Trip Blank	5	2026/08/05 08:30	WATER	14			A	3

Deadlines are estimates only and are subject to change. Please refer to your Job Confirmation report for final due dates.

Submission Information

of Samples: 5

Sample Set Listing

Set 1 (2 samples)	Set 2 (1 sample)	Set 3 (2 samples)
WLNG-DS WLNG-US	WLNG -EOP	Field Blank Trip Blank
