

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Page	1 of 12

Eagle Mountain – Woodfibre Gas Pipeline Project

BCER Waste Discharge Permit Weekly Report

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Page	2 of 12

Contents

Preamble 3

Introduction 3

Sampling Methodology 3

Summary-BC Rail Site 5

Site Activities 5

Discharge from Water Treatment Plant..... 5

Receiving Environment Monitoring-Squamish River 5

Summary-Woodfibre Site 6

Site Activities 6

Exceedances..... 6

Discharge from Water Treatment Plant..... 6

Receiving Environment Monitoring-East Creek..... 6

August 2026 BC Chronic Guideline Comparison 7

Total Aluminum (T-Al) and Dissolved Aluminum (D-Al) 7

Appendix A: BC Rail Point of Discharge from Water Treatment System Documentation

Appendix B: BC Rail Receiving Environment Documentation

Appendix C: Woodfibre Point of Discharge from Water Treatment System Documentation

Appendix D: Woodfibre Receiving Environment Documentation

Appendix E: Lab Documentation

M0012-REG-REP-2001

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Page	3 of 12

Preamble

This weekly report for the British Columbia Energy Regulator (BCER) Waste Discharge Permit (BCER number PE-110163) for the FortisBC Eagle Mountain – Woodfibre Gas Pipeline (EGP) Project includes the results of water quality monitoring and sampling of the receiving environments (upstream and downstream) and points of discharge during the reporting period.

FortisBC has retained Hatfield Consultants as the Qualified Professional to implement and oversee the monitoring and sampling programs. The data represented below, including laboratory reported exceedances, represent conditions measured from final discharge points and the associated receiving environments, as required under the Waste Discharge Permit.

Introduction

The results provided in this document have been submitted to BCER by FortisBC as per the requirements listed in Section 4.2 of the Waste Discharge Permit PE-110163:

The Permittee shall summarize the results of the discharge and receiving environment compliance sampling and monitoring program in a report that shall be submitted weekly over the term of this permit. The sampling and monitoring results shall be suitably tabulated and include comparison to the respective British Columbia Approved and Working Water Quality Guidelines for Freshwater & Marine Aquatic Life, as published by the Ministry of Environment & Climate Change Strategy. Any exceedance of regulatory guidelines shall be clearly highlighted, and any missed sampling events/missing data shall be identified with an explanation provided. Reporting frequency may be reduced upon a history of compliance and by written confirmation from the BCER. These reports shall be submitted to Waste.Management@bc-er.ca. A copy of the reports shall be provided to each First Nation consulted with regarding the subject permit, and also made publicly available on the FortisBC Eagle Mountain-Woodfibre Gas Pipeline Project | Talking Energy webpage.

Sampling Methodology

The monitoring and sampling has been carried out in accordance with the procedures described in the most recent edition of the “British Columbia Field Sampling Manual” using field equipment and laboratory samples to meet daily and real-time requirements for the Waste Discharge Permit.

In the receiving environments, real-time and daily readings were monitored at the same time with one piece of equipment, allowing real-time daily readings. Visible sheen was monitored through visual inspections during times of discharge or sampling.

At the point of discharges, parameters are monitored using field equipment and water quality sondes, as well as discrete weekly water quality sampling events for laboratory analyses. Table 1 and Table 2 below describe this monitoring.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

August 24 to
August 30, 2026

Report #

127

Page

4 of 12

Table 1. Monitor Details for the Point of Discharge from the Water Treatment System-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily (or per batch)	DO	Monitoring using YSI ProDSS
	ORP	Monitoring using YSI ProDSS
	Salinity	Monitoring using YSI ProDSS
Real-time (or per batch)	pH	Monitoring using GF Dryloc pH Series NPT
	Temperature	Monitoring using LevelPro PT100 Temperature and Signet 2350 Temp sensor
	NTU	Monitoring using Observer NEP9504GPI
	Electrical Conductivity	Monitoring using ProCon C450
Weekly (or per batch) Lab Samples	List prescribed in permit	Lab samples*

*Indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.

Table 2. Monitor Details for the Receiving Environment (upstream and downstream)-BC Rail and Woodfibre

Permit Frequency	Parameters	Details
During discharges	Visible Sheen	In field inspection
Daily	DO	Monitoring using Sonde- AquaTROLL 600 datalogger
	ORP	Monitoring using Sonde- AquaTROLL 600 datalogger
	Salinity	Monitoring using Sonde- AquaTROLL 600 datalogger
Real-time	pH	Monitoring using Sonde- AquaTROLL 600 datalogger
	Temperature	Monitoring using Sonde- AquaTROLL 600 datalogger
	NTU	Monitoring using Sonde- AquaTROLL 600 datalogger
	Electrical Conductivity	Monitoring using Sonde- AquaTROLL 600 datalogger
Weekly Lab Samples	List prescribed in permit	Lab samples*

*Indicates that weekly lab samples are currently only collected at the Woodfibre site, as approved by BCER, given that there is currently no discharge from the BC Rail site.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

August 24 to
August 30, 2026

Report #

127

Page

5 of 12

Summary-BC Rail Site

Site Activities

- The soft ground tunnel has been completed and FortisBC is in the process of demobilizing equipment and preparations for pipe stringing.

Discharge from Water Treatment Plant

- There was no discharge this week from the BC Rail Site.

Receiving Environment Monitoring-Squamish River

Tables 3 and 4 below provide information on water quality monitoring. Lab sampling has been put on hold with permission from BCER as there are currently no discharges. Appendix B includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit and confirmed by BCER, with additional oversight by the QP.

Table 3. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Upstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

Table 4. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
Squamish River Downstream	N/A	Yes *	Full set of real time monitoring results are provided in Appendix B. **

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

** Data gaps in available in-situ continuous monitoring data, included:

- SQU US
 - 2026/08/24 at 00:00 to 2026/08/27 at 12:00: Due to sonde maintenance, no data available.
- SQU DS
 - No data gaps observed.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

August 24 to
August 30, 2026

Report #

127

Page

6 of 12

Summary-Woodfibre Site

Site Activities

- Weekly upstream, downstream, and end of pipe water quality sampling performed by the QP.
- On-going tunnelling at WLNG and grouting works to mitigate water ingress.

Exceedances

There were no reportable exceedance identified during the August 24 to August 30, 2026 reporting period.

Discharge from Water Treatment Plant

Appendix C includes volume information and real-time/field samples from the discharge.

Receiving Environment Monitoring-East Creek

Tables 5 and 6 below provide information on water quality monitoring. Appendix D includes a full set of results with real-time data. The receiving environment is being monitored as outlined in the permit with additional oversight by the QP.

Table 5. Upstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Upstream	2026-08-25	Yes *	Full set of results are provided in Appendix D.**

Table 6. Downstream Monitoring Information

Location	Date of Lab Sample	Real-time Monitored	Results
East Creek Downstream	2026-08-25	Yes *	Full set of results are provided in Appendix D.**

* Sondes set up to log temperature, specific conductivity, salinity (in PSU), pH, ORP, DO (mg/L), and turbidity (NTU) at 15-minute intervals.

**Data gaps in available in-situ continuous monitoring data, included:

- EAS US
 - 2026/08/24 at 00:15 to 2026/08/30 at 23:45: and 08:45: Sonde sensor set to 60-minute recording interval rather than 15-minute recording interval, therefore creating three data gaps an hour.
- EAS DS
 - No data gaps observed.

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Page	7 of 12

August 2026 BC Chronic Guideline Comparison

Consistent with recommendations outlined in Hatfield (2024)¹, the applicable guideline at the WLNG EOP is the short-term freshwater guideline for protection of aquatic life. Additionally, as outlined in Hatfield (2024), an assessment is provided below in figures detailing trends in concentrations of constituents determined to exceed monthly average BC chronic water quality guidelines for the protection of aquatic life during at least one weekly sampling event in August at the WLNG DS station. Given that chronic BC WQGPAL are designed to be applied over a monthly period and include conservative assumptions in their derivation (e.g., safety factors), the below interpretation is provided to put these identified exceedance events into context from an ecological risk perspective. A summary of the August monthly chronic guideline comparisons are provided in Table 7.

Total Aluminum (T-Al) and Dissolved Aluminum (D-Al)

- The mean monthly T-Al concentration at the downstream WLNG DS (0.0593 mg/L) station was below the mean sample-specific calculated BC long-term (LT) WQGPAL (freshwater) of 0.0666 mg/L (See Figure 1) and the T-Al Federal WQG of 0.200 mg/L, suggesting limited risk to aquatic life. The Federal WQG was developed using a robust species sensitivity distribution involving IC10 (inhibitory concentration eliciting a 10% effect) values from sensitive aquatic species (reproduced in Figure 3). The BC WQGPAL was derived by applying a 3-fold safety factor to the Federal WQG based on conservative BC WQG development policies; however, as outlined in Section 4.4.6 of BC ENV (2023)² Protocol 1 *Detailed Risk Assessment* guidance, risk to aquatic life should be evaluated based on EC20 values. Given that the federal WQG was derived using the 5th percentile from a species sensitivity distribution approach that involved the use of IC10 values, the lack of exceedances of both the Provincial and Federal WQGs at WLNG DS suggests limited risk to aquatic life in East Creek during the month of August.
- It should also be acknowledged that most of the aluminum from WLNG DS was particulate aluminum, which would be expected to be less bioavailable to aquatic life. The mean dissolved aluminum concentration measured at WLNG DS was 0.0375 mg/L, which remained less than both the conservative BC WQGPAL and the federal WQG (See Figure 2). Therefore, these results suggest low risk to downstream aquatic life from the WLNG DS T-Al and D-AL mean concentrations determined for the month of August 2026.

¹ Hatfield Consultants LLP. 2024. EGP Effluent Discharge Permit Condition Review, FORTIS11234. Dated December 18, 2024.

² [BC ENV] British Columbia Ministry of Environment and Climate Strategy. 2023. Protocol 1 for Contaminated Sites. Detailed Risk Assessment. Version 4.0. Date: March 20, 2023.



**Eagle Mountain – Woodfibre Gas Pipeline Project
Waste Discharge Permit PE-110163 Report**

Reporting Week

August 24 to
August 30, 2026

Report #

127

Page

8 of 12

Table 7. August 2026 Monthly Chronic Guidelines Comparison in East Creek.

Analyte	Date	Measured Concentration at WLNG DS (mg/L)	Monthly Mean Value at WLNG DS (mg/L)	Monthly Mean BC WQG Chronic at WLNG DS (mg/L)	Monthly Mean Federal WQGPAL Chronic at WLNG DS (mg/L)
T-Al	2026/08/05	0.0757	0.0593	0.0666	0.200
T-Al	2026/08/11	0.05			
T-Al	2026/08/18	0.0573			
T-Al	2026/08/25	0.0542			
D-Al	2026/08/05	0.0401	0.0375	0.0666	0.200
D-Al	2026/08/11	0.0305			
D-Al	2026/08/18	0.0386			
D-Al	2026/08/25	0.0406			
TSS	2026/08/05	1	1.1	7.2	7.2
TSS	2026/08/11	1.2			
TSS	2026/08/18	1			
TSS	2026/08/25	1.2			

Figure 1: Total Aluminium (T-Al)

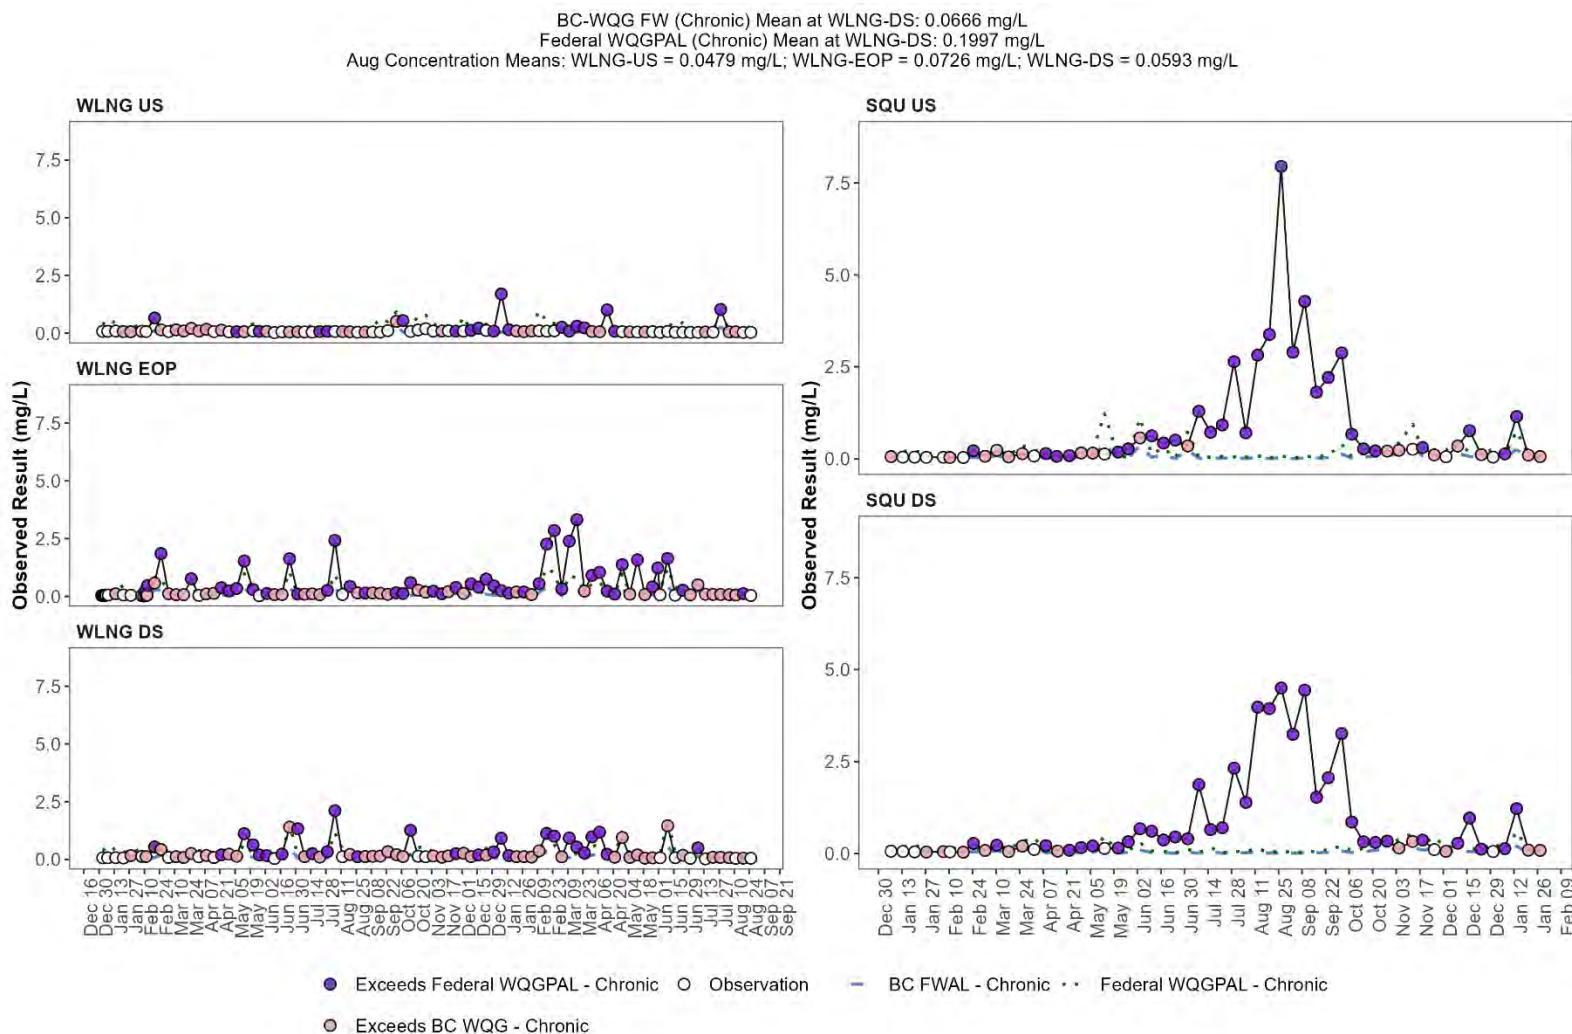


Figure 2: Dissolved Aluminum


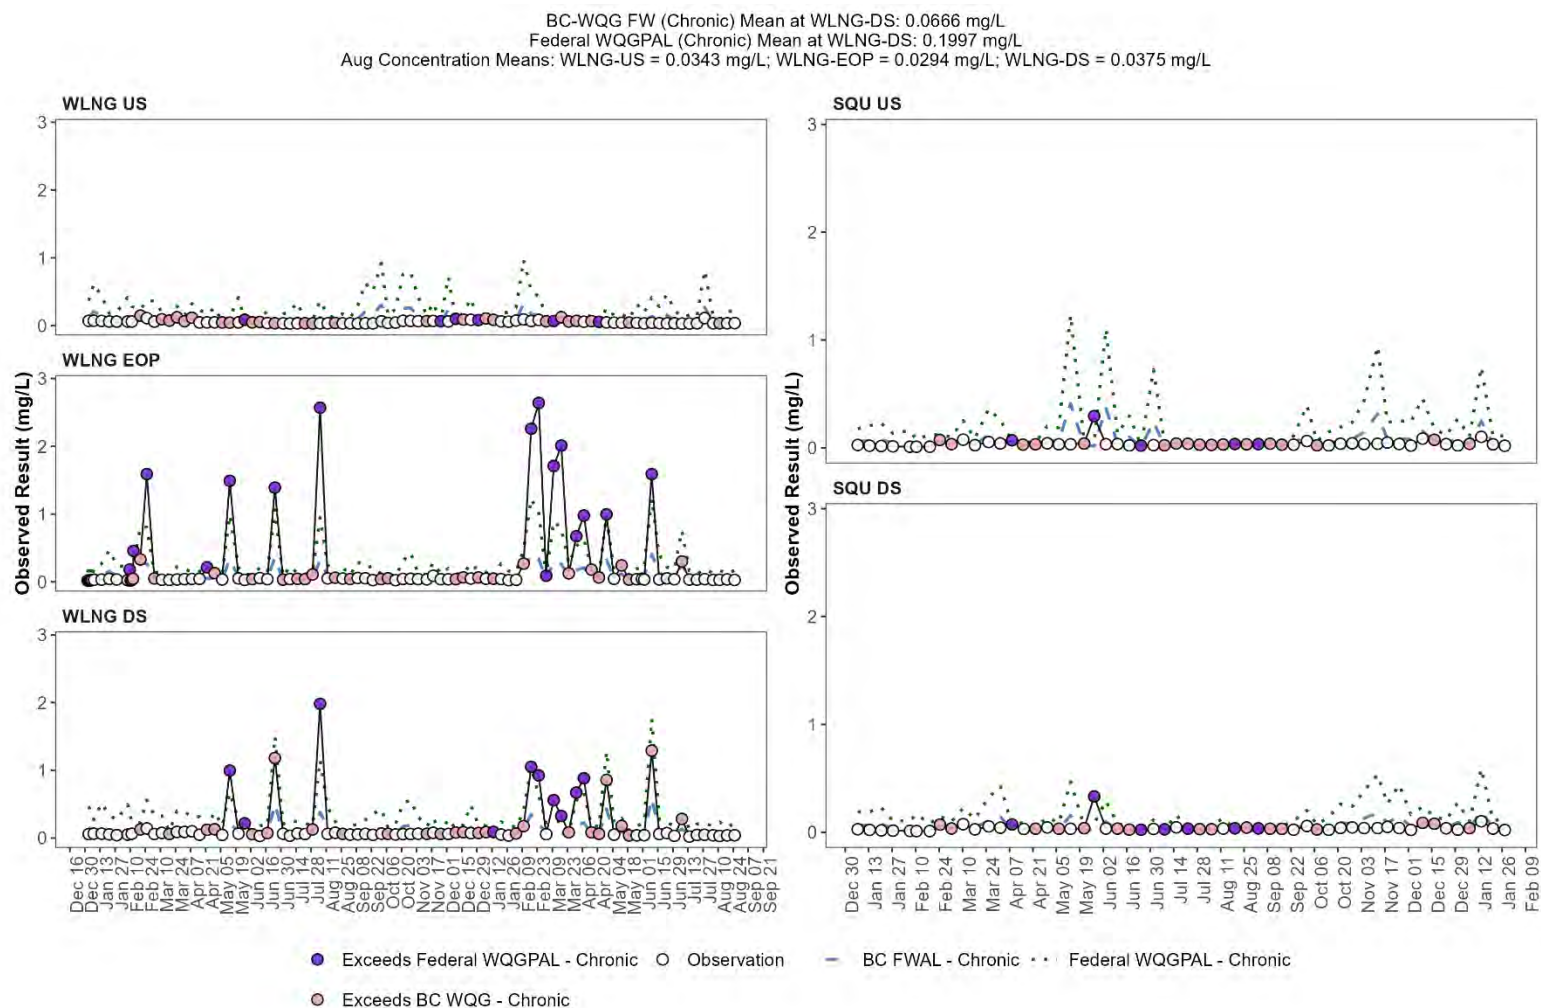


Figure 3: Species sensitivity distribution used to derive the federal water quality guideline for aluminum (reproduce from ECCC 2022³)

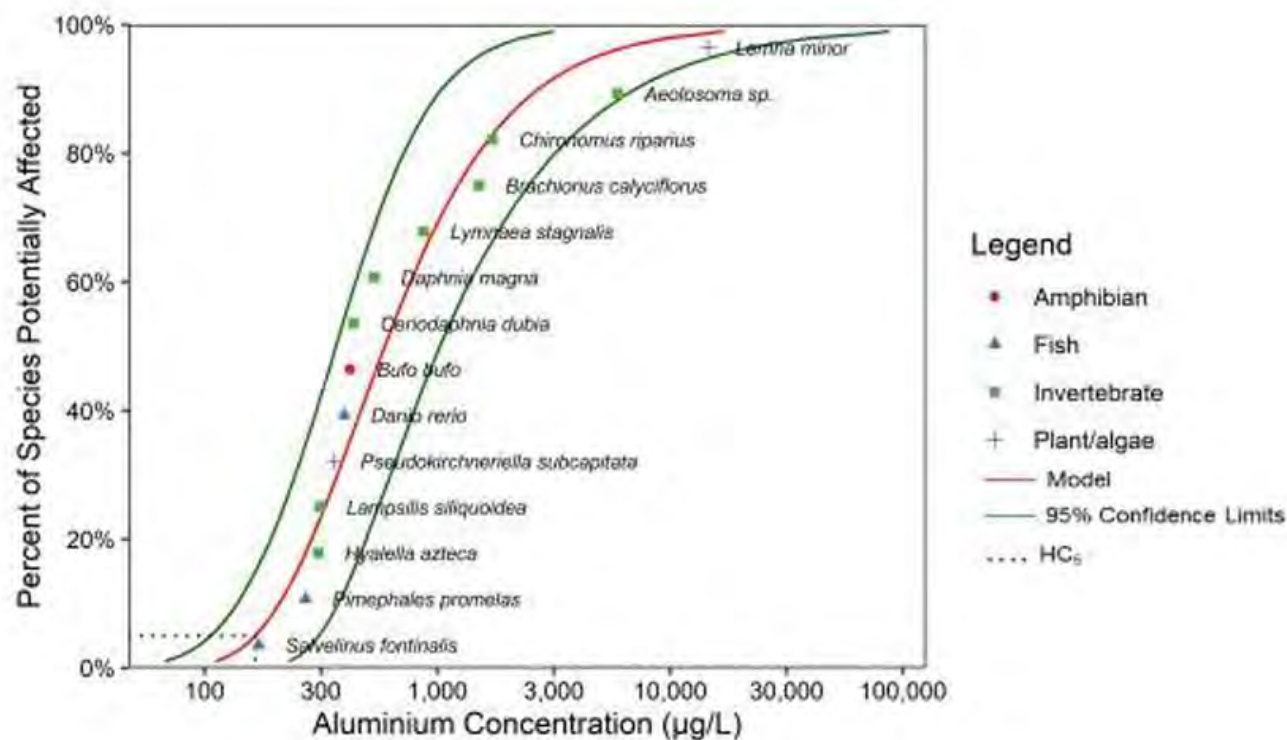

FWQG model averaged species sensitivity distribution (SSD) for aluminium in freshwater for an example site (pH7.5, DOC 0.5 mg/L, hardness 50 mg/L). The 5th percentile is 170 µg A1/L.

³ [ECCC] Environment and Climate Change Canada. 2022. Federal Environmental Quality Guidelines: Aluminum. Government of Canada. August 2022.

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix A	A-1

Appendix A:
BCR Site Point of Discharge from Water
Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix A	A-2

BCR Site Batch Sample Analysis
No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix A	A-3

BCR Site WTP Discharge Field Notes and Logs
No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix B	B-1

Appendix B: BCR Site Receiving Environment Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix B	B-2

BCR Site Receiving Environment Sample Analysis
No Discharge

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix B	B-3

BCR Site Receiving Environment
Field Notes and Logs

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-24 00:00:00	12.01	24.90	0.26	7.45	10.77	218.51	0.01
SQU-DS	2026-08-24 00:15:00	11.98	24.51	0.29	7.48	10.80	235.77	0.01
SQU-DS	2026-08-24 00:30:00	11.95	24.50	0.30	7.43	10.79	236.96	0.01
SQU-DS	2026-08-24 00:45:00	11.92	24.76	0.31	7.40	10.80	247.70	0.01
SQU-DS	2026-08-24 01:00:00	11.89	24.56	0.27	7.41	10.80	246.46	0.01
SQU-DS	2026-08-24 01:15:00	11.86	24.59	0.29	7.47	10.80	156.58	0.01
SQU-DS	2026-08-24 01:30:00	11.84	24.63	0.30	7.51	10.80	158.26	0.01
SQU-DS	2026-08-24 01:45:00	11.81	24.48	0.31	7.43	10.80	168.71	0.01
SQU-DS	2026-08-24 02:00:00	11.79	24.54	0.26	7.48	10.79	262.77	0.01
SQU-DS	2026-08-24 02:15:00	11.77	24.42	0.30	7.42	10.80	210.89	0.01
SQU-DS	2026-08-24 02:30:00	11.74	24.23	0.31	7.47	10.82	238.06	0.01
SQU-DS	2026-08-24 02:45:00	11.73	24.53	0.32	7.41	10.81	182.19	0.01
SQU-DS	2026-08-24 03:00:00	11.70	24.56	0.28	7.40	10.81	205.60	0.01
SQU-DS	2026-08-24 03:15:00	11.68	24.48	0.31	7.38	10.81	160.53	0.01
SQU-DS	2026-08-24 03:30:00	11.66	24.47	0.32	7.35	10.80	152.07	0.01
SQU-DS	2026-08-24 03:45:00	11.64	24.42	0.32	7.33	10.82	150.22	0.01
SQU-DS	2026-08-24 04:00:00	11.62	24.75	0.27	7.33	10.81	190.92	0.01
SQU-DS	2026-08-24 04:15:00	11.60	24.40	0.30	7.33	10.83	155.37	0.01
SQU-DS	2026-08-24 04:30:00	11.58	24.68	0.32	7.33	10.82	165.68	0.01
SQU-DS	2026-08-24 04:45:00	11.56	24.50	0.32	7.32	10.82	149.24	0.01
SQU-DS	2026-08-24 05:00:00	11.54	24.43	0.27	7.30	10.82	168.72	0.01
SQU-DS	2026-08-24 05:15:00	11.52	24.57	0.30	7.30	10.83	124.11	0.01
SQU-DS	2026-08-24 05:30:00	11.50	24.37	0.32	7.31	10.83	151.11	0.01
SQU-DS	2026-08-24 05:45:00	11.47	24.36	0.32	7.31	10.83	175.57	0.01
SQU-DS	2026-08-24 06:00:00	11.45	24.50	0.27	7.28	10.83	227.48	0.01
SQU-DS	2026-08-24 06:15:00	11.42	24.36	0.30	7.29	10.83	143.37	0.01
SQU-DS	2026-08-24 06:30:00	11.40	24.61	0.31	7.29	10.83	106.45	0.01
SQU-DS	2026-08-24 06:45:00	11.37	24.50	0.32	7.29	10.85	147.83	0.01
SQU-DS	2026-08-24 07:00:00	11.35	24.60	0.27	7.26	10.83	148.05	0.01
SQU-DS	2026-08-24 07:15:00	11.34	24.49	0.30	7.29	10.85	148.62	0.01
SQU-DS	2026-08-24 07:30:00	11.34	24.78	0.31	7.29	10.84	107.54	0.01
SQU-DS	2026-08-24 07:45:00	11.33	24.81	0.32	7.29	10.86	133.89	0.01
SQU-DS	2026-08-24 08:00:00	11.34	24.81	0.27	7.25	10.84	138.31	0.01
SQU-DS	2026-08-24 08:15:00	11.35	24.74	0.30	7.28	10.85	107.55	0.01
SQU-DS	2026-08-24 08:30:00	11.36	24.70	0.31	7.28	10.86	113.41	0.01
SQU-DS	2026-08-24 08:45:00	11.38	24.66	0.32	7.28	10.87	136.64	0.01
SQU-DS	2026-08-24 09:00:00	11.40	24.76	0.27	7.25	10.86	139.69	0.01
SQU-DS	2026-08-24 09:15:00	11.43	24.88	0.30	7.28	10.86	80.09	0.01
SQU-DS	2026-08-24 09:30:00	11.45	24.90	0.32	7.28	10.88	96.23	0.01
SQU-DS	2026-08-24 09:45:00	11.49	25.19	0.32	7.25	10.87	123.54	0.01
SQU-DS	2026-08-24 10:00:00	11.53	25.53	0.28	7.26	10.84	105.85	0.01
SQU-DS	2026-08-24 10:15:00	11.58	25.38	0.30	7.27	10.87	86.22	0.01
SQU-DS	2026-08-24 10:30:00	11.63	25.33	0.32	7.28	10.87	97.56	0.01
SQU-DS	2026-08-24 10:45:00	11.69	25.59	0.32	7.29	10.88	90.07	0.01
SQU-DS	2026-08-24 11:00:00	11.74	25.41	0.25	7.26	10.87	108.78	0.01
SQU-DS	2026-08-24 11:15:00	11.81	25.57	0.29	7.28	10.88	93.31	0.01
SQU-DS	2026-08-24 11:30:00	11.86	25.74	0.31	7.28	10.87	113.06	0.01
SQU-DS	2026-08-24 11:45:00	11.93	25.88	0.32	7.28	10.84	87.38	0.01
SQU-DS	2026-08-24 12:00:00	12.00	25.81	0.28	7.27	10.84	107.96	0.01
SQU-DS	2026-08-24 12:15:00	12.06	26.04	0.30	7.28	10.83	92.28	0.01
SQU-DS	2026-08-24 12:30:00	12.14	26.06	0.32	7.27	10.85	80.27	0.01
SQU-DS	2026-08-24 12:45:00	12.21	25.93	0.32	7.30	10.85	96.89	0.01
SQU-DS	2026-08-24 13:00:00	12.30	26.17	0.28	7.28	10.83	74.29	0.01
SQU-DS	2026-08-24 13:15:00	12.37	25.98	0.31	7.29	10.84	82.24	0.01
SQU-DS	2026-08-24 13:30:00	12.45	26.42	0.32	7.30	10.81	110.89	0.01
SQU-DS	2026-08-24 13:45:00	12.52	26.74	0.33	7.26	10.79	90.86	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-24 14:00:00	12.59	26.71	0.29	7.27	10.79	119.15	0.01
SQU-DS	2026-08-24 14:15:00	12.66	26.98	0.31	7.26	10.77	95.50	0.01
SQU-DS	2026-08-24 14:30:00	12.74	26.87	0.32	7.28	10.78	82.71	0.01
SQU-DS	2026-08-24 14:45:00	12.80	27.30	0.33	7.28	10.76	82.59	0.01
SQU-DS	2026-08-24 15:00:00	12.87	27.40	0.28	7.28	10.75	105.61	0.01
SQU-DS	2026-08-24 15:15:00	12.93	27.16	0.31	7.30	10.76	90.85	0.01
SQU-DS	2026-08-24 15:30:00	12.99	27.11	0.32	7.31	10.75	68.42	0.01
SQU-DS	2026-08-24 15:45:00	13.05	27.34	0.33	7.32	10.76	79.07	0.01
SQU-DS	2026-08-24 16:00:00	13.11	27.28	0.29	7.33	10.75	93.65	0.01
SQU-DS	2026-08-24 16:15:00	13.15	27.14	0.31	7.36	10.75	61.28	0.01
SQU-DS	2026-08-24 16:30:00	13.20	27.54	0.33	7.36	10.74	70.47	0.01
SQU-DS	2026-08-24 16:45:00	13.23	27.48	0.33	7.36	10.74	95.82	0.01
SQU-DS	2026-08-24 17:00:00	13.27	27.91	0.29	7.39	10.73	72.38	0.01
SQU-DS	2026-08-24 17:15:00	13.30	27.88	0.32	7.39	10.71	73.52	0.01
SQU-DS	2026-08-24 17:30:00	13.32	28.36	0.32	7.47	10.71	73.61	0.01
SQU-DS	2026-08-24 17:45:00	13.30	28.49	0.33	7.50	10.69	70.43	0.01
SQU-DS	2026-08-24 18:00:00	13.28	28.91	0.27	7.51	10.66	75.96	0.01
SQU-DS	2026-08-24 18:15:00	13.28	29.25	0.30	7.47	10.67	59.61	0.01
SQU-DS	2026-08-24 18:30:00	13.27	29.81	0.31	7.43	10.65	45.02	0.01
SQU-DS	2026-08-24 18:45:00	13.25	30.29	0.32	7.40	10.62	62.14	0.01
SQU-DS	2026-08-24 19:00:00	13.22	30.48	0.28	7.41	10.58	86.30	0.01
SQU-DS	2026-08-24 19:15:00	13.20	30.66	0.30	7.38	10.57	75.22	0.01
SQU-DS	2026-08-24 19:30:00	13.18	30.96	0.31	7.42	10.56	45.22	0.01
SQU-DS	2026-08-24 19:45:00	13.17	31.03	0.31	7.38	10.53	69.82	0.01
SQU-DS	2026-08-24 20:00:00	13.17	31.11	0.27	7.36	10.51	92.50	0.01
SQU-DS	2026-08-24 20:15:00	13.17	31.11	0.29	7.39	10.49	59.90	0.01
SQU-DS	2026-08-24 20:30:00	13.18	31.14	0.31	7.32	10.47	53.96	0.01
SQU-DS	2026-08-24 20:45:00	13.18	31.15	0.31	7.32	10.45	67.19	0.01
SQU-DS	2026-08-24 21:00:00	13.18	31.53	0.27	7.31	10.43	73.44	0.01
SQU-DS	2026-08-24 21:15:00	13.19	31.14	0.30	7.33	10.44	72.98	0.01
SQU-DS	2026-08-24 21:30:00	13.20	30.91	0.31	7.31	10.41	83.80	0.01
SQU-DS	2026-08-24 21:45:00	13.20	31.05	0.31	7.32	10.42	47.26	0.01
SQU-DS	2026-08-24 22:00:00	13.20	30.77	0.27	7.32	10.40	89.33	0.01
SQU-DS	2026-08-24 22:15:00	13.20	30.62	0.29	7.33	10.42	66.02	0.01
SQU-DS	2026-08-24 22:30:00	13.19	30.88	0.31	7.31	10.40	65.25	0.01
SQU-DS	2026-08-24 22:45:00	13.19	30.54	0.31	7.31	10.40	86.08	0.01
SQU-DS	2026-08-24 23:00:00	13.17	30.53	0.26	7.31	10.39	104.81	0.01
SQU-DS	2026-08-24 23:15:00	13.15	30.09	0.29	7.32	10.41	67.00	0.01
SQU-DS	2026-08-24 23:30:00	13.13	30.08	0.31	7.29	10.37	68.79	0.01
SQU-DS	2026-08-24 23:45:00	13.11	29.84	0.31	7.31	10.39	87.67	0.01
SQU-DS	2026-08-25 00:00:00	13.08	29.74	0.27	7.30	10.39	86.51	0.01
SQU-DS	2026-08-25 00:15:00	13.04	29.43	0.29	7.32	10.40	75.08	0.01
SQU-DS	2026-08-25 00:30:00	13.01	29.28	0.30	7.33	10.41	88.64	0.01
SQU-DS	2026-08-25 00:45:00	12.96	29.14	0.31	7.32	10.40	89.79	0.01
SQU-DS	2026-08-25 01:00:00	12.91	28.88	0.28	7.30	10.40	120.39	0.01
SQU-DS	2026-08-25 01:15:00	12.86	28.65	0.30	7.32	10.43	97.37	0.01
SQU-DS	2026-08-25 01:30:00	12.81	28.74	0.31	7.32	10.43	142.76	0.01
SQU-DS	2026-08-25 01:45:00	12.76	28.58	0.32	7.32	10.44	95.52	0.01
SQU-DS	2026-08-25 02:00:00	12.70	28.03	0.26	7.31	10.44	104.02	0.01
SQU-DS	2026-08-25 02:15:00	12.65	28.16	0.29	7.32	10.46	96.67	0.01
SQU-DS	2026-08-25 02:30:00	12.59	28.05	0.31	7.35	10.48	104.18	0.01
SQU-DS	2026-08-25 02:45:00	12.53	27.80	0.32	7.34	10.49	103.80	0.01
SQU-DS	2026-08-25 03:00:00	12.47	27.80	0.29	7.32	10.50	170.85	0.01
SQU-DS	2026-08-25 03:15:00	12.40	27.53	0.31	7.33	10.51	123.02	0.01
SQU-DS	2026-08-25 03:30:00	12.34	27.63	0.32	7.36	10.53	120.64	0.01
SQU-DS	2026-08-25 03:45:00	12.28	27.42	0.33	7.32	10.54	113.34	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-25 04:00:00	12.21	27.39	0.26	7.32	10.54	249.78	0.01
SQU-DS	2026-08-25 04:15:00	12.16	27.40	0.29	7.30	10.54	109.30	0.01
SQU-DS	2026-08-25 04:30:00	12.10	27.38	0.31	7.32	10.56	128.38	0.01
SQU-DS	2026-08-25 04:45:00	12.05	27.24	0.32	7.31	10.58	122.26	0.01
SQU-DS	2026-08-25 05:00:00	11.99	27.29	0.25	7.28	10.58	227.81	0.01
SQU-DS	2026-08-25 05:15:00	11.94	27.05	0.29	7.28	10.60	143.15	0.01
SQU-DS	2026-08-25 05:30:00	11.89	27.06	0.31	7.28	10.61	133.43	0.01
SQU-DS	2026-08-25 05:45:00	11.84	26.73	0.32	7.26	10.62	107.98	0.01
SQU-DS	2026-08-25 06:00:00	11.79	26.83	0.27	7.26	10.63	122.29	0.01
SQU-DS	2026-08-25 06:15:00	11.75	26.63	0.30	7.26	10.65	132.33	0.01
SQU-DS	2026-08-25 06:30:00	11.71	26.49	0.31	7.25	10.64	116.95	0.01
SQU-DS	2026-08-25 06:45:00	11.68	26.45	0.32	7.26	10.68	107.00	0.01
SQU-DS	2026-08-25 07:00:00	11.64	26.21	0.27	7.23	10.67	171.93	0.01
SQU-DS	2026-08-25 07:15:00	11.62	26.24	0.30	7.25	10.68	88.77	0.01
SQU-DS	2026-08-25 07:30:00	11.60	26.09	0.31	7.25	10.71	133.43	0.01
SQU-DS	2026-08-25 07:45:00	11.59	26.23	0.32	7.24	10.70	109.08	0.01
SQU-DS	2026-08-25 08:00:00	11.58	25.97	0.27	7.24	10.71	133.60	0.01
SQU-DS	2026-08-25 08:15:00	11.58	26.22	0.30	7.24	10.72	83.08	0.01
SQU-DS	2026-08-25 08:30:00	11.59	26.15	0.32	7.27	10.72	72.89	0.01
SQU-DS	2026-08-25 08:45:00	11.60	26.10	0.32	7.26	10.73	89.83	0.01
SQU-DS	2026-08-25 09:00:00	11.63	26.15	0.28	7.24	10.72	95.20	0.01
SQU-DS	2026-08-25 09:15:00	11.65	26.49	0.31	7.24	10.73	85.41	0.01
SQU-DS	2026-08-25 09:30:00	11.69	26.29	0.32	7.26	10.74	75.67	0.01
SQU-DS	2026-08-25 09:45:00	11.73	26.56	0.32	7.25	10.74	101.91	0.01
SQU-DS	2026-08-25 10:00:00	11.77	26.49	0.26	7.24	10.73	108.93	0.01
SQU-DS	2026-08-25 10:15:00	11.82	26.46	0.29	7.26	10.73	75.29	0.01
SQU-DS	2026-08-25 10:30:00	11.88	26.60	0.31	7.25	10.74	74.56	0.01
SQU-DS	2026-08-25 10:45:00	11.94	26.93	0.32	7.25	10.73	96.66	0.01
SQU-DS	2026-08-25 11:00:00	12.00	27.01	0.28	7.23	10.71	87.10	0.01
SQU-DS	2026-08-25 11:15:00	12.06	26.98	0.31	7.25	10.72	93.17	0.01
SQU-DS	2026-08-25 11:30:00	12.13	27.17	0.32	7.26	10.73	73.47	0.01
SQU-DS	2026-08-25 11:45:00	12.20	26.90	0.32	7.29	10.72	79.46	0.01
SQU-DS	2026-08-25 12:00:00	12.27	27.04	0.28	7.26	10.72	89.55	0.01
SQU-DS	2026-08-25 12:15:00	12.34	27.24	0.30	7.28	10.72	81.51	0.01
SQU-DS	2026-08-25 12:30:00	12.41	27.23	0.31	7.28	10.73	81.04	0.01
SQU-DS	2026-08-25 12:45:00	12.48	27.38	0.32	7.24	10.70	100.27	0.01
SQU-DS	2026-08-25 13:00:00	12.56	27.47	0.29	7.27	10.70	133.23	0.01
SQU-DS	2026-08-25 13:15:00	12.62	27.45	0.31	7.28	10.70	93.14	0.01
SQU-DS	2026-08-25 13:30:00	12.70	27.70	0.32	7.26	10.69	55.24	0.01
SQU-DS	2026-08-25 13:45:00	12.78	28.13	0.33	7.28	10.67	69.64	0.01
SQU-DS	2026-08-25 14:00:00	12.87	28.05	0.28	7.29	10.66	82.69	0.01
SQU-DS	2026-08-25 14:15:00	12.94	28.39	0.31	7.27	10.66	64.49	0.01
SQU-DS	2026-08-25 14:30:00	13.00	28.44	0.32	7.29	10.66	60.21	0.01
SQU-DS	2026-08-25 14:45:00	13.04	28.73	0.33	7.29	10.63	55.00	0.01
SQU-DS	2026-08-25 15:00:00	13.07	28.66	0.28	7.28	10.63	80.50	0.01
SQU-DS	2026-08-25 15:15:00	13.12	28.68	0.31	7.27	10.64	80.36	0.01
SQU-DS	2026-08-25 15:30:00	13.17	28.53	0.32	7.33	10.65	48.24	0.01
SQU-DS	2026-08-25 15:45:00	13.22	28.69	0.33	7.33	10.65	51.19	0.01
SQU-DS	2026-08-25 16:00:00	13.26	28.57	0.28	7.32	10.63	109.42	0.01
SQU-DS	2026-08-25 16:15:00	13.28	28.74	0.30	7.34	10.64	54.72	0.01
SQU-DS	2026-08-25 16:30:00	13.30	28.85	0.31	7.35	10.64	48.00	0.01
SQU-DS	2026-08-25 16:45:00	13.31	28.97	0.33	7.37	10.64	46.60	0.01
SQU-DS	2026-08-25 17:00:00	13.32	29.19	0.28	7.36	10.62	86.22	0.01
SQU-DS	2026-08-25 17:15:00	13.32	29.17	0.31	7.36	10.64	59.25	0.01
SQU-DS	2026-08-25 17:30:00	13.33	29.35	0.32	7.40	10.62	50.54	0.01
SQU-DS	2026-08-25 17:45:00	13.32	29.61	0.33	7.39	10.60	59.00	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-25 18:00:00	13.31	29.80	0.28	7.40	10.59	65.73	0.01
SQU-DS	2026-08-25 18:15:00	13.32	30.26	0.30	7.40	10.59	91.57	0.01
SQU-DS	2026-08-25 18:30:00	13.32	30.83	0.31	7.40	10.57	57.87	0.01
SQU-DS	2026-08-25 18:45:00	13.32	31.22	0.32	7.38	10.56	89.39	0.01
SQU-DS	2026-08-25 19:00:00	13.31	31.57	0.25	7.46	10.53	97.41	0.01
SQU-DS	2026-08-25 19:15:00	13.29	31.77	0.29	7.41	10.52	49.52	0.01
SQU-DS	2026-08-25 19:30:00	13.29	32.25	0.30	7.39	10.51	51.62	0.01
SQU-DS	2026-08-25 19:45:00	13.29	32.01	0.31	7.38	10.49	46.95	0.01
SQU-DS	2026-08-25 20:00:00	13.29	32.39	0.27	7.40	10.46	161.25	0.01
SQU-DS	2026-08-25 20:15:00	13.30	31.98	0.30	7.38	10.44	41.17	0.01
SQU-DS	2026-08-25 20:30:00	13.30	32.35	0.31	7.36	10.43	50.36	0.01
SQU-DS	2026-08-25 20:45:00	13.30	32.23	0.32	7.33	10.41	48.22	0.01
SQU-DS	2026-08-25 21:00:00	13.30	32.59	0.26	7.36	10.39	83.84	0.01
SQU-DS	2026-08-25 21:15:00	13.31	32.03	0.29	7.32	10.38	73.13	0.01
SQU-DS	2026-08-25 21:30:00	13.31	31.77	0.31	7.33	10.38	60.99	0.01
SQU-DS	2026-08-25 21:45:00	13.32	31.73	0.31	7.34	10.38	74.71	0.01
SQU-DS	2026-08-25 22:00:00	13.32	31.16	0.25	7.32	10.36	114.40	0.01
SQU-DS	2026-08-25 22:15:00	13.32	31.06	0.28	7.32	10.38	74.77	0.01
SQU-DS	2026-08-25 22:30:00	13.31	30.73	0.30	7.34	10.37	81.58	0.01
SQU-DS	2026-08-25 22:45:00	13.30	30.18	0.31	7.33	10.37	81.64	0.01
SQU-DS	2026-08-25 23:00:00	13.28	30.31	0.26	7.30	10.35	66.41	0.01
SQU-DS	2026-08-25 23:15:00	13.26	29.95	0.29	7.32	10.35	74.10	0.01
SQU-DS	2026-08-25 23:30:00	13.23	29.77	0.31	7.29	10.34	66.61	0.01
SQU-DS	2026-08-25 23:45:00	13.20	29.47	0.32	7.30	10.38	89.81	0.01
SQU-DS	2026-08-26 00:00:00	13.16	29.41	0.26	7.28	10.34	95.01	0.01
SQU-DS	2026-08-26 00:15:00	13.12	29.06	0.29	7.29	10.38	94.63	0.01
SQU-DS	2026-08-26 00:30:00	13.08	28.57	0.31	7.32	10.39	91.73	0.01
SQU-DS	2026-08-26 00:45:00	13.04	28.59	0.32	7.30	10.39	97.24	0.01
SQU-DS	2026-08-26 01:00:00	13.00	28.69	0.27	7.31	10.40	116.82	0.01
SQU-DS	2026-08-26 01:15:00	12.95	28.19	0.30	7.31	10.43	125.00	0.01
SQU-DS	2026-08-26 01:30:00	12.91	28.08	0.31	7.33	10.44	94.72	0.01
SQU-DS	2026-08-26 01:45:00	12.86	27.94	0.32	7.33	10.43	129.73	0.01
SQU-DS	2026-08-26 02:00:00	12.80	27.65	0.26	7.32	10.44	105.28	0.01
SQU-DS	2026-08-26 02:15:00	12.74	27.36	0.29	7.34	10.46	84.95	0.01
SQU-DS	2026-08-26 02:30:00	12.68	27.16	0.31	7.34	10.48	111.24	0.01
SQU-DS	2026-08-26 02:45:00	12.61	26.84	0.32	7.33	10.49	107.27	0.01
SQU-DS	2026-08-26 03:00:00	12.55	26.85	0.27	7.31	10.49	149.10	0.01
SQU-DS	2026-08-26 03:15:00	12.48	26.42	0.30	7.32	10.52	130.22	0.01
SQU-DS	2026-08-26 03:30:00	12.42	26.29	0.31	7.32	10.54	102.85	0.01
SQU-DS	2026-08-26 03:45:00	12.35	26.05	0.32	7.32	10.55	117.71	0.01
SQU-DS	2026-08-26 04:00:00	12.29	25.95	0.26	7.34	10.55	115.91	0.01
SQU-DS	2026-08-26 04:15:00	12.23	25.83	0.29	7.33	10.57	114.01	0.01
SQU-DS	2026-08-26 04:30:00	12.17	25.96	0.31	7.35	10.58	162.99	0.01
SQU-DS	2026-08-26 04:45:00	12.11	25.63	0.32	7.35	10.60	118.94	0.01
SQU-DS	2026-08-26 05:00:00	12.06	25.87	0.26	7.32	10.60	184.20	0.01
SQU-DS	2026-08-26 05:15:00	12.00	25.85	0.29	7.34	10.61	114.51	0.01
SQU-DS	2026-08-26 05:30:00	11.95	25.64	0.31	7.32	10.64	116.00	0.01
SQU-DS	2026-08-26 05:45:00	11.89	25.53	0.32	7.27	10.65	142.84	0.01
SQU-DS	2026-08-26 06:00:00	11.84	25.54	0.26	7.30	10.64	160.23	0.01
SQU-DS	2026-08-26 06:15:00	11.80	25.49	0.29	7.32	10.66	150.40	0.01
SQU-DS	2026-08-26 06:30:00	11.75	25.21	0.31	7.28	10.68	101.27	0.01
SQU-DS	2026-08-26 06:45:00	11.72	25.26	0.32	7.26	10.68	151.72	0.01
SQU-DS	2026-08-26 07:00:00	11.69	25.15	0.27	7.25	10.69	140.28	0.01
SQU-DS	2026-08-26 07:15:00	11.65	24.94	0.30	7.24	10.71	95.01	0.01
SQU-DS	2026-08-26 07:30:00	11.63	24.81	0.32	7.25	10.71	93.16	0.01
SQU-DS	2026-08-26 07:45:00	11.62	24.63	0.33	7.25	10.72	109.34	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-26 08:00:00	11.62	24.80	0.28	7.25	10.71	107.92	0.01
SQU-DS	2026-08-26 08:15:00	11.62	24.78	0.30	7.25	10.72	100.02	0.01
SQU-DS	2026-08-26 08:30:00	11.63	24.81	0.32	7.23	10.75	106.47	0.01
SQU-DS	2026-08-26 08:45:00	11.65	24.73	0.33	7.23	10.73	82.95	0.01
SQU-DS	2026-08-26 09:00:00	11.67	24.68	0.29	7.23	10.74	90.24	0.01
SQU-DS	2026-08-26 09:15:00	11.70	24.70	0.31	7.26	10.75	92.67	0.01
SQU-DS	2026-08-26 09:30:00	11.74	24.78	0.33	7.25	10.76	79.17	0.01
SQU-DS	2026-08-26 09:45:00	11.79	24.81	0.33	7.22	10.76	108.81	0.01
SQU-DS	2026-08-26 10:00:00	11.84	24.90	0.29	7.24	10.73	157.80	0.01
SQU-DS	2026-08-26 10:15:00	11.91	24.87	0.31	7.24	10.75	83.14	0.01
SQU-DS	2026-08-26 10:30:00	11.98	24.87	0.32	7.24	10.75	81.60	0.01
SQU-DS	2026-08-26 10:45:00	12.06	25.04	0.33	7.22	10.74	63.83	0.01
SQU-DS	2026-08-26 11:00:00	12.13	25.19	0.27	7.23	10.72	110.26	0.01
SQU-DS	2026-08-26 11:15:00	12.21	24.96	0.30	7.26	10.74	80.04	0.01
SQU-DS	2026-08-26 11:30:00	12.29	24.86	0.32	7.27	10.73	73.37	0.01
SQU-DS	2026-08-26 11:45:00	12.36	25.10	0.33	7.26	10.72	103.42	0.01
SQU-DS	2026-08-26 12:00:00	12.43	24.87	0.28	7.25	10.72	144.76	0.01
SQU-DS	2026-08-26 12:15:00	12.51	24.96	0.30	7.26	10.72	86.02	0.01
SQU-DS	2026-08-26 12:30:00	12.59	25.30	0.32	7.25	10.70	70.89	0.01
SQU-DS	2026-08-26 12:45:00	12.66	25.17	0.33	7.25	10.71	85.22	0.01
SQU-DS	2026-08-26 13:00:00	12.73	25.23	0.26	7.26	10.69	139.56	0.01
SQU-DS	2026-08-26 13:15:00	12.81	25.02	0.30	7.26	10.72	65.00	0.01
SQU-DS	2026-08-26 13:30:00	12.88	25.25	0.31	7.27	10.70	61.44	0.01
SQU-DS	2026-08-26 13:45:00	12.95	25.40	0.32	7.28	10.69	73.48	0.01
SQU-DS	2026-08-26 14:00:00	13.03	25.58	0.29	7.26	10.69	94.56	0.01
SQU-DS	2026-08-26 14:15:00	13.09	25.73	0.31	7.26	10.67	78.50	0.01
SQU-DS	2026-08-26 14:30:00	13.16	25.62	0.32	7.28	10.67	82.60	0.01
SQU-DS	2026-08-26 14:45:00	13.23	25.55	0.33	7.28	10.67	100.54	0.01
SQU-DS	2026-08-26 15:00:00	13.28	26.05	0.27	7.25	10.64	63.51	0.01
SQU-DS	2026-08-26 15:15:00	13.31	25.95	0.30	7.25	10.65	65.24	0.01
SQU-DS	2026-08-26 15:30:00	13.33	26.06	0.31	7.27	10.65	81.62	0.01
SQU-DS	2026-08-26 15:45:00	13.37	26.33	0.32	7.31	10.63	80.35	0.01
SQU-DS	2026-08-26 16:00:00	13.39	25.91	0.28	7.28	10.65	116.32	0.01
SQU-DS	2026-08-26 16:15:00	13.45	25.99	0.30	7.32	10.65	55.63	0.01
SQU-DS	2026-08-26 16:30:00	13.51	26.07	0.32	7.33	10.65	54.94	0.01
SQU-DS	2026-08-26 16:45:00	13.54	26.11	0.33	7.36	10.65	79.93	0.01
SQU-DS	2026-08-26 17:00:00	13.57	26.14	0.28	7.32	10.63	96.26	0.01
SQU-DS	2026-08-26 17:15:00	13.59	26.14	0.31	7.37	10.64	70.66	0.01
SQU-DS	2026-08-26 17:30:00	13.60	26.27	0.32	7.39	10.62	63.87	0.01
SQU-DS	2026-08-26 17:45:00	13.60	26.70	0.33	7.42	10.62	60.09	0.01
SQU-DS	2026-08-26 18:00:00	13.59	27.11	0.28	7.47	10.60	83.71	0.01
SQU-DS	2026-08-26 18:15:00	13.58	27.15	0.30	7.48	10.58	32.23	0.01
SQU-DS	2026-08-26 18:30:00	13.59	28.05	0.32	7.49	10.57	38.73	0.01
SQU-DS	2026-08-26 18:45:00	13.60	28.69	0.33	7.46	10.56	42.31	0.01
SQU-DS	2026-08-26 19:00:00	13.60	28.57	0.27	7.60	10.53	133.23	0.01
SQU-DS	2026-08-26 19:15:00	13.58	28.83	0.30	7.46	10.52	42.72	0.01
SQU-DS	2026-08-26 19:30:00	13.58	29.57	0.31	7.42	10.49	60.72	0.01
SQU-DS	2026-08-26 19:45:00	13.58	29.87	0.32	7.43	10.47	50.41	0.01
SQU-DS	2026-08-26 20:00:00	13.58	29.39	0.28	7.43	10.46	135.64	0.01
SQU-DS	2026-08-26 20:15:00	13.58	29.94	0.30	7.43	10.44	52.79	0.01
SQU-DS	2026-08-26 20:30:00	13.59	29.76	0.31	7.39	10.42	61.80	0.01
SQU-DS	2026-08-26 20:45:00	13.61	30.19	0.32	7.38	10.40	51.78	0.01
SQU-DS	2026-08-26 21:00:00	13.62	30.15	0.27	7.37	10.38	112.66	0.01
SQU-DS	2026-08-26 21:15:00	13.63	30.08	0.29	7.38	10.36	56.29	0.01
SQU-DS	2026-08-26 21:30:00	13.63	29.84	0.30	7.39	10.35	54.30	0.01
SQU-DS	2026-08-26 21:45:00	13.63	29.71	0.31	7.36	10.34	78.29	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-26 22:00:00	13.62	29.48	0.27	7.34	10.33	117.27	0.01
SQU-DS	2026-08-26 22:15:00	13.61	29.35	0.29	7.33	10.32	74.04	0.01
SQU-DS	2026-08-26 22:30:00	13.59	28.97	0.31	7.32	10.33	53.32	0.01
SQU-DS	2026-08-26 22:45:00	13.57	28.36	0.31	7.32	10.35	96.90	0.01
SQU-DS	2026-08-26 23:00:00	13.55	28.24	0.28	7.31	10.33	67.97	0.01
SQU-DS	2026-08-26 23:15:00	13.53	28.08	0.30	7.34	10.33	75.75	0.01
SQU-DS	2026-08-26 23:30:00	13.50	27.86	0.31	7.32	10.32	95.94	0.01
SQU-DS	2026-08-26 23:45:00	13.47	27.57	0.32	7.34	10.33	81.96	0.01
SQU-DS	2026-08-27 00:00:00	13.44	27.25	0.28	7.30	10.33	66.28	0.01
SQU-DS	2026-08-27 00:15:00	13.40	27.18	0.30	7.31	10.33	73.70	0.01
SQU-DS	2026-08-27 00:30:00	13.37	27.01	0.31	7.33	10.35	80.31	0.01
SQU-DS	2026-08-27 00:45:00	13.32	27.02	0.32	7.31	10.34	72.84	0.01
SQU-DS	2026-08-27 01:00:00	13.26	26.62	0.28	7.32	10.36	100.32	0.01
SQU-DS	2026-08-27 01:15:00	13.20	26.55	0.31	7.31	10.36	75.12	0.01
SQU-DS	2026-08-27 01:30:00	13.14	26.71	0.32	7.33	10.37	75.84	0.01
SQU-DS	2026-08-27 01:45:00	13.07	26.20	0.33	7.32	10.40	86.66	0.01
SQU-DS	2026-08-27 02:00:00	13.00	26.27	0.28	7.31	10.39	147.66	0.01
SQU-DS	2026-08-27 02:15:00	12.94	26.03	0.30	7.34	10.42	71.94	0.01
SQU-DS	2026-08-27 02:30:00	12.87	25.98	0.31	7.33	10.43	104.11	0.01
SQU-DS	2026-08-27 02:45:00	12.80	25.67	0.32	7.34	10.45	87.02	0.01
SQU-DS	2026-08-27 03:00:00	12.74	25.76	0.27	7.30	10.45	94.60	0.01
SQU-DS	2026-08-27 03:15:00	12.68	25.48	0.30	7.36	10.48	84.07	0.01
SQU-DS	2026-08-27 03:30:00	12.61	25.54	0.32	7.33	10.49	80.87	0.01
SQU-DS	2026-08-27 03:45:00	12.55	25.22	0.32	7.36	10.51	100.57	0.01
SQU-DS	2026-08-27 04:00:00	12.49	25.25	0.27	7.36	10.52	161.40	0.01
SQU-DS	2026-08-27 04:15:00	12.44	25.08	0.29	7.39	10.54	124.65	0.01
SQU-DS	2026-08-27 04:30:00	12.38	24.99	0.31	7.37	10.55	81.76	0.01
SQU-DS	2026-08-27 04:45:00	12.33	24.95	0.32	7.40	10.57	85.94	0.01
SQU-DS	2026-08-27 05:00:00	12.27	24.76	0.27	7.35	10.58	127.25	0.01
SQU-DS	2026-08-27 05:15:00	12.22	24.70	0.30	7.37	10.59	74.50	0.01
SQU-DS	2026-08-27 05:30:00	12.17	24.75	0.31	7.40	10.60	77.92	0.01
SQU-DS	2026-08-27 05:45:00	12.11	24.59	0.32	7.38	10.61	82.06	0.01
SQU-DS	2026-08-27 06:00:00	12.07	24.63	0.28	7.34	10.62	126.80	0.01
SQU-DS	2026-08-27 06:15:00	12.02	24.62	0.30	7.34	10.64	108.58	0.01
SQU-DS	2026-08-27 06:30:00	11.98	24.70	0.32	7.33	10.63	87.24	0.01
SQU-DS	2026-08-27 06:45:00	11.93	24.52	0.32	7.33	10.64	105.14	0.01
SQU-DS	2026-08-27 07:00:00	11.89	24.46	0.27	7.29	10.65	127.05	0.01
SQU-DS	2026-08-27 07:15:00	11.87	24.54	0.30	7.32	10.65	116.43	0.01
SQU-DS	2026-08-27 07:30:00	11.85	24.55	0.32	7.28	10.65	106.29	0.01
SQU-DS	2026-08-27 07:45:00	11.82	24.23	0.32	7.26	10.67	118.60	0.01
SQU-DS	2026-08-27 08:00:00	11.81	24.29	0.26	7.25	10.66	73.63	0.01
SQU-DS	2026-08-27 08:15:00	11.80	24.62	0.30	7.26	10.65	77.24	0.01
SQU-DS	2026-08-27 08:30:00	11.79	24.45	0.31	7.24	10.67	97.75	0.01
SQU-DS	2026-08-27 08:45:00	11.79	24.71	0.32	7.24	10.65	97.13	0.01
SQU-DS	2026-08-27 09:00:00	11.80	25.01	0.27	7.22	10.65	107.13	0.01
SQU-DS	2026-08-27 09:15:00	11.80	24.58	0.30	7.25	10.67	83.52	0.01
SQU-DS	2026-08-27 09:30:00	11.81	24.91	0.31	7.24	10.67	73.20	0.01
SQU-DS	2026-08-27 09:45:00	11.82	24.91	0.32	7.23	10.67	107.63	0.01
SQU-DS	2026-08-27 10:00:00	11.85	24.96	0.28	7.23	10.66	105.48	0.01
SQU-DS	2026-08-27 10:15:00	11.85	25.24	0.30	7.22	10.66	62.82	0.01
SQU-DS	2026-08-27 10:30:00	11.85	25.31	0.32	7.20	10.64	92.93	0.01
SQU-DS	2026-08-27 10:45:00	11.85	25.46	0.32	7.19	10.65	169.46	0.01
SQU-DS	2026-08-27 11:00:00	11.85	25.46	0.27	7.23	10.66	123.44	0.01
SQU-DS	2026-08-27 11:15:00	11.83	25.26	0.30	7.23	10.69	109.16	0.01
SQU-DS	2026-08-27 11:30:00	11.80	25.38	0.32	7.24	10.69	75.89	0.01
SQU-DS	2026-08-27 11:45:00	11.77	25.39	0.32	7.23	10.69	93.02	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-27 12:00:00	11.74	25.48	0.29	7.20	10.68	71.94	0.01
SQU-DS	2026-08-27 12:15:00	11.72	25.18	0.31	7.22	10.70	69.44	0.01
SQU-DS	2026-08-27 12:30:00	11.71	24.99	0.32	7.24	10.73	70.27	0.01
SQU-DS	2026-08-27 12:45:00	11.69	25.21	0.32	7.23	10.72	66.89	0.01
SQU-DS	2026-08-27 13:00:00	11.69	25.67	0.28	7.21	10.71	146.62	0.01
SQU-DS	2026-08-27 13:15:00	11.69	25.72	0.30	7.20	10.72	69.84	0.01
SQU-DS	2026-08-27 13:30:00	11.74	25.73	0.32	7.21	10.72	59.62	0.01
SQU-DS	2026-08-27 13:45:00	11.76	25.73	0.32	7.22	10.74	92.87	0.01
SQU-DS	2026-08-27 14:00:00	11.80	25.48	0.29	7.22	10.75	89.87	0.01
SQU-DS	2026-08-27 14:15:00	11.82	25.35	0.30	7.25	10.76	62.70	0.01
SQU-DS	2026-08-27 14:30:00	11.82	25.73	0.32	7.23	10.76	64.99	0.01
SQU-DS	2026-08-27 14:45:00	11.85	25.66	0.32	7.23	10.78	81.34	0.01
SQU-DS	2026-08-27 15:00:00	11.85	25.90	0.29	7.22	10.76	134.30	0.01
SQU-DS	2026-08-27 15:15:00	11.86	26.02	0.31	7.21	10.77	68.23	0.01
SQU-DS	2026-08-27 15:30:00	11.86	25.92	0.32	7.21	10.75	58.23	0.01
SQU-DS	2026-08-27 15:45:00	11.87	26.27	0.33	7.22	10.74	56.63	0.01
SQU-DS	2026-08-27 16:00:00	11.88	26.25	0.28	7.22	10.75	94.73	0.01
SQU-DS	2026-08-27 16:15:00	11.88	26.02	0.30	7.24	10.78	67.51	0.01
SQU-DS	2026-08-27 16:30:00	11.89	26.05	0.31	7.26	10.79	76.91	0.01
SQU-DS	2026-08-27 16:45:00	11.91	26.25	0.32	7.28	10.80	73.33	0.01
SQU-DS	2026-08-27 17:00:00	11.91	26.35	0.28	7.29	10.78	62.94	0.01
SQU-DS	2026-08-27 17:15:00	11.90	26.60	0.31	7.32	10.80	82.91	0.01
SQU-DS	2026-08-27 17:30:00	11.89	26.97	0.32	7.33	10.79	72.68	0.01
SQU-DS	2026-08-27 17:45:00	11.88	27.01	0.33	7.32	10.79	55.72	0.01
SQU-DS	2026-08-27 18:00:00	11.87	27.37	0.29	7.33	10.78	93.39	0.01
SQU-DS	2026-08-27 18:15:00	11.86	27.57	0.31	7.35	10.80	62.98	0.01
SQU-DS	2026-08-27 18:30:00	11.85	28.04	0.32	7.36	10.80	92.65	0.01
SQU-DS	2026-08-27 18:45:00	11.84	28.73	0.32	7.41	10.79	100.11	0.01
SQU-DS	2026-08-27 19:00:00	11.83	29.34	0.28	7.45	10.77	58.76	0.01
SQU-DS	2026-08-27 19:15:00	11.82	29.54	0.31	7.42	10.77	55.50	0.01
SQU-DS	2026-08-27 19:30:00	11.80	29.84	0.32	7.41	10.76	61.05	0.01
SQU-DS	2026-08-27 19:45:00	11.79	30.21	0.32	7.43	10.75	47.58	0.01
SQU-DS	2026-08-27 20:00:00	11.78	30.64	0.27	7.44	10.73	89.97	0.01
SQU-DS	2026-08-27 20:15:00	11.76	30.48	0.29	7.38	10.74	58.74	0.01
SQU-DS	2026-08-27 20:30:00	11.73	30.03	0.31	7.37	10.74	59.37	0.01
SQU-DS	2026-08-27 20:45:00	11.71	29.75	0.32	7.38	10.74	69.71	0.01
SQU-DS	2026-08-27 21:00:00	11.69	29.12	0.27	7.37	10.73	114.71	0.01
SQU-DS	2026-08-27 21:15:00	11.67	28.87	0.30	7.34	10.74	78.84	0.01
SQU-DS	2026-08-27 21:30:00	11.65	28.37	0.31	7.33	10.75	88.12	0.01
SQU-DS	2026-08-27 21:45:00	11.61	27.75	0.32	7.35	10.76	88.66	0.01
SQU-DS	2026-08-27 22:00:00	11.58	27.14	0.27	7.31	10.76	113.81	0.01
SQU-DS	2026-08-27 22:15:00	11.54	26.44	0.30	7.31	10.78	79.36	0.01
SQU-DS	2026-08-27 22:30:00	11.51	25.78	0.31	7.32	10.79	72.57	0.01
SQU-DS	2026-08-27 22:45:00	11.47	25.15	0.32	7.31	10.81	92.20	0.01
SQU-DS	2026-08-27 23:00:00	11.42	24.59	0.29	7.33	10.82	152.10	0.01
SQU-DS	2026-08-27 23:15:00	11.37	24.25	0.31	7.33	10.85	110.39	0.01
SQU-DS	2026-08-27 23:30:00	11.31	24.10	0.32	7.33	10.88	181.01	0.01
SQU-DS	2026-08-27 23:45:00	11.24	24.61	0.33	7.36	10.89	196.31	0.01
SQU-DS	2026-08-28 00:00:00	11.19	25.74	0.28	7.39	10.89	296.64	0.01
SQU-DS	2026-08-28 00:15:00	11.13	26.94	0.30	7.44	10.92	336.75	0.01
SQU-DS	2026-08-28 00:30:00	11.08	28.32	0.31	7.51	10.94	373.06	0.01
SQU-DS	2026-08-28 00:45:00	11.04	29.31	0.31	7.54	10.94	401.17	0.01
SQU-DS	2026-08-28 01:00:00	10.99	29.74	0.26	7.57	10.95	469.49	0.01
SQU-DS	2026-08-28 01:15:00	10.96	30.04	0.28	7.64	10.95	432.36	0.01
SQU-DS	2026-08-28 01:30:00	10.95	29.72	0.30	7.59	10.97	397.31	0.01
SQU-DS	2026-08-28 01:45:00	10.96	29.40	0.31	7.55	10.96	356.49	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-28 02:00:00	10.97	28.97	0.26	7.56	10.94	418.40	0.01
SQU-DS	2026-08-28 02:15:00	10.97	28.32	0.29	7.56	10.97	372.84	0.01
SQU-DS	2026-08-28 02:30:00	10.98	27.93	0.30	7.50	10.98	324.26	0.01
SQU-DS	2026-08-28 02:45:00	10.97	27.45	0.32	7.48	10.98	311.53	0.01
SQU-DS	2026-08-28 03:00:00	10.97	27.27	0.25	7.50	10.98	290.43	0.01
SQU-DS	2026-08-28 03:15:00	10.96	26.79	0.28	7.58	11.00	227.24	0.01
SQU-DS	2026-08-28 03:30:00	10.95	26.39	0.30	7.53	11.01	325.62	0.01
SQU-DS	2026-08-28 03:45:00	10.93	25.88	0.31	7.50	11.00	258.74	0.01
SQU-DS	2026-08-28 04:00:00	10.92	25.98	0.27	7.49	11.00	202.61	0.01
SQU-DS	2026-08-28 04:15:00	10.90	25.83	0.29	7.55	11.00	195.61	0.01
SQU-DS	2026-08-28 04:30:00	10.88	25.01	0.31	7.53	11.02	188.83	0.01
SQU-DS	2026-08-28 04:45:00	10.87	24.98	0.32	7.52	11.02	316.51	0.01
SQU-DS	2026-08-28 05:00:00	10.85	24.77	0.27	7.57	11.02	173.16	0.01
SQU-DS	2026-08-28 05:15:00	10.84	24.74	0.29	7.56	11.03	129.63	0.01
SQU-DS	2026-08-28 05:30:00	10.82	24.46	0.34	7.54	11.03	88.61	0.01
SQU-DS	2026-08-28 05:45:00	10.80	24.47	0.37	7.52	11.04	156.00	0.01
SQU-DS	2026-08-28 06:00:00	10.78	23.92	0.37	7.48	11.06	143.11	0.01
SQU-DS	2026-08-28 06:15:00	10.75	23.96	0.38	7.46	11.07	123.75	0.01
SQU-DS	2026-08-28 06:30:00	10.72	24.46	0.27	7.55	11.06	152.62	0.01
SQU-DS	2026-08-28 06:45:00	10.69	23.68	0.30	7.54	11.08	151.04	0.01
SQU-DS	2026-08-28 07:00:00	10.67	23.61	0.31	7.51	11.08	169.14	0.01
SQU-DS	2026-08-28 07:15:00	10.64	23.36	0.32	7.46	11.08	131.41	0.01
SQU-DS	2026-08-28 07:30:00	10.62	23.48	0.27	7.47	11.09	154.38	0.01
SQU-DS	2026-08-28 07:45:00	10.60	23.22	0.30	7.50	11.10	179.06	0.01
SQU-DS	2026-08-28 08:00:00	10.59	23.30	0.32	7.45	11.10	175.18	0.01
SQU-DS	2026-08-28 08:15:00	10.57	23.15	0.33	7.41	11.11	220.22	0.01
SQU-DS	2026-08-28 08:30:00	10.57	23.32	0.29	7.41	11.10	206.92	0.01
SQU-DS	2026-08-28 08:45:00	10.57	23.21	0.31	7.47	11.11	199.97	0.01
SQU-DS	2026-08-28 09:00:00	10.57	23.11	0.32	7.44	11.11	211.38	0.01
SQU-DS	2026-08-28 09:15:00	10.59	23.09	0.33	7.44	11.11	173.40	0.01
SQU-DS	2026-08-28 09:30:00	10.64	23.10	0.30	7.36	11.11	228.60	0.01
SQU-DS	2026-08-28 09:45:00	10.68	23.37	0.32	7.32	11.11	194.22	0.01
SQU-DS	2026-08-28 10:00:00	10.71	23.43	0.33	7.34	11.13	180.58	0.01
SQU-DS	2026-08-28 10:15:00	10.74	23.42	0.34	7.35	11.11	175.65	0.01
SQU-DS	2026-08-28 10:30:00	10.78	23.49	0.30	7.35	11.10	181.15	0.01
SQU-DS	2026-08-28 10:45:00	10.80	23.40	0.32	7.34	11.11	203.82	0.01
SQU-DS	2026-08-28 11:00:00	10.81	23.30	0.34	7.32	11.12	202.61	0.01
SQU-DS	2026-08-28 11:15:00	10.83	23.33	0.34	7.32	11.11	124.36	0.01
SQU-DS	2026-08-28 11:30:00	10.84	23.26	0.29	7.35	11.11	189.08	0.01
SQU-DS	2026-08-28 11:45:00	10.84	23.37	0.32	7.34	11.12	143.12	0.01
SQU-DS	2026-08-28 12:00:00	10.84	23.34	0.33	7.32	11.11	140.36	0.01
SQU-DS	2026-08-28 12:15:00	10.84	23.30	0.34	7.34	11.11	115.66	0.01
SQU-DS	2026-08-28 12:30:00	10.83	23.21	0.29	7.31	11.11	238.58	0.01
SQU-DS	2026-08-28 12:45:00	10.84	23.22	0.31	7.34	11.10	107.88	0.01
SQU-DS	2026-08-28 13:00:00	10.85	23.46	0.33	7.35	11.10	128.47	0.01
SQU-DS	2026-08-28 13:15:00	10.86	23.35	0.34	7.35	11.10	159.76	0.01
SQU-DS	2026-08-28 13:30:00	10.89	23.40	0.29	7.32	11.09	160.47	0.01
SQU-DS	2026-08-28 13:45:00	10.91	23.38	0.31	7.33	11.11	144.72	0.01
SQU-DS	2026-08-28 14:00:00	10.91	23.12	0.33	7.32	11.10	132.04	0.01
SQU-DS	2026-08-28 14:15:00	10.93	23.30	0.34	7.34	11.10	150.06	0.01
SQU-DS	2026-08-28 14:30:00	10.95	23.57	0.29	7.30	11.10	177.85	0.01
SQU-DS	2026-08-28 14:45:00	10.96	23.53	0.32	7.34	11.10	132.66	0.01
SQU-DS	2026-08-28 15:00:00	10.99	23.46	0.33	7.34	11.10	124.68	0.01
SQU-DS	2026-08-28 15:15:00	11.03	23.57	0.34	7.36	11.10	144.14	0.01
SQU-DS	2026-08-28 15:30:00	11.07	23.76	0.28	7.33	11.08	221.66	0.01
SQU-DS	2026-08-28 15:45:00	11.12	24.00	0.31	7.35	11.07	141.96	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-28 16:00:00	11.16	24.18	0.32	7.33	11.07	113.34	0.01
SQU-DS	2026-08-28 16:15:00	11.19	24.41	0.34	7.30	11.07	143.38	0.01
SQU-DS	2026-08-28 16:30:00	11.21	24.11	0.27	7.30	11.04	138.82	0.01
SQU-DS	2026-08-28 16:45:00	11.23	24.39	0.31	7.35	11.06	102.15	0.01
SQU-DS	2026-08-28 17:00:00	11.24	24.29	0.32	7.37	11.05	106.28	0.01
SQU-DS	2026-08-28 17:15:00	11.25	24.58	0.32	7.50	11.04	90.02	0.01
SQU-DS	2026-08-28 17:30:00	11.26	24.81	0.25	7.42	11.02	144.39	0.01
SQU-DS	2026-08-28 17:45:00	11.26	24.71	0.29	7.54	11.04	104.49	0.01
SQU-DS	2026-08-28 18:00:00	11.26	24.62	0.31	7.52	11.03	91.21	0.01
SQU-DS	2026-08-28 18:15:00	11.26	25.21	0.27	7.52	11.02	106.14	0.01
SQU-DS	2026-08-28 18:30:00	11.26	25.40	0.31	7.45	11.02	90.79	0.01
SQU-DS	2026-08-28 18:45:00	11.27	25.62	0.32	7.49	11.01	76.14	0.01
SQU-DS	2026-08-28 19:00:00	11.27	25.85	0.33	7.52	10.99	92.38	0.01
SQU-DS	2026-08-28 19:15:00	11.29	25.88	0.26	7.55	10.97	2.20	0.01
SQU-DS	2026-08-28 19:30:00	11.30	26.31	0.29	7.51	10.95	0.00	0.01
SQU-DS	2026-08-28 19:45:00	11.32	26.32	0.32	7.46	10.93	0.00	0.01
SQU-DS	2026-08-28 20:00:00	11.34	27.05	0.33	7.45	10.92	0.00	0.01
SQU-DS	2026-08-28 20:15:00	11.35	28.23	0.27	7.48	10.88	5.67	0.01
SQU-DS	2026-08-28 20:30:00	11.36	27.46	0.30	7.55	10.87	90.25	0.01
SQU-DS	2026-08-28 20:45:00	11.38	28.08	0.32	7.54	10.91	55.23	0.01
SQU-DS	2026-08-28 21:00:00	11.40	27.55	0.32	7.53	10.90	73.36	0.01
SQU-DS	2026-08-28 21:15:00	11.41	27.33	0.27	7.50	10.88	83.83	0.01
SQU-DS	2026-08-28 21:30:00	11.41	27.76	0.30	7.47	10.88	76.69	0.01
SQU-DS	2026-08-28 21:45:00	11.41	27.45	0.32	7.43	10.87	85.06	0.01
SQU-DS	2026-08-28 22:00:00	11.40	27.09	0.33	7.38	10.88	82.18	0.01
SQU-DS	2026-08-28 22:15:00	11.39	27.15	0.28	7.40	10.86	91.86	0.01
SQU-DS	2026-08-28 22:30:00	11.39	27.19	0.30	7.37	10.85	82.97	0.01
SQU-DS	2026-08-28 22:45:00	11.38	26.80	0.32	7.36	10.85	72.67	0.01
SQU-DS	2026-08-28 23:00:00	11.38	27.00	0.32	7.37	10.85	86.08	0.01
SQU-DS	2026-08-28 23:15:00	11.39	26.74	0.27	7.36	10.83	123.64	0.01
SQU-DS	2026-08-28 23:30:00	11.38	26.43	0.30	7.35	10.85	78.20	0.01
SQU-DS	2026-08-28 23:45:00	11.38	26.71	0.32	7.35	10.84	92.09	0.01
SQU-DS	2026-08-29 00:00:00	11.38	26.76	0.32	7.36	10.84	102.08	0.01
SQU-DS	2026-08-29 00:15:00	11.36	26.76	0.29	7.36	10.82	87.94	0.01
SQU-DS	2026-08-29 00:30:00	11.35	26.81	0.31	7.36	10.84	61.55	0.01
SQU-DS	2026-08-29 00:45:00	11.33	27.08	0.32	7.35	10.83	113.91	0.01
SQU-DS	2026-08-29 01:00:00	11.30	27.30	0.33	7.39	10.84	62.11	0.01
SQU-DS	2026-08-29 01:15:00	11.27	27.19	0.27	7.38	10.85	105.78	0.01
SQU-DS	2026-08-29 01:30:00	11.23	27.19	0.30	7.38	10.86	119.92	0.01
SQU-DS	2026-08-29 01:45:00	11.20	27.12	0.32	7.40	10.85	92.51	0.01
SQU-DS	2026-08-29 02:00:00	11.16	26.86	0.33	7.35	10.88	150.96	0.01
SQU-DS	2026-08-29 02:15:00	11.12	26.88	0.30	7.37	10.88	134.15	0.01
SQU-DS	2026-08-29 02:30:00	11.06	26.83	0.32	7.40	10.89	110.17	0.01
SQU-DS	2026-08-29 02:45:00	10.99	26.29	0.33	7.39	10.92	72.26	0.01
SQU-DS	2026-08-29 03:00:00	10.92	26.22	0.34	7.40	10.93	86.28	0.01
SQU-DS	2026-08-29 03:15:00	10.83	25.63	0.27	7.37	10.95	111.81	0.01
SQU-DS	2026-08-29 03:30:00	10.76	25.75	0.30	7.40	10.97	101.19	0.01
SQU-DS	2026-08-29 03:45:00	10.70	25.48	0.32	7.39	11.00	79.82	0.01
SQU-DS	2026-08-29 04:00:00	10.65	25.31	0.33	7.41	11.01	119.93	0.01
SQU-DS	2026-08-29 04:15:00	10.60	25.55	0.30	7.39	11.01	113.15	0.01
SQU-DS	2026-08-29 04:30:00	10.56	25.42	0.32	7.41	11.04	108.63	0.01
SQU-DS	2026-08-29 04:45:00	10.53	25.84	0.33	7.43	11.05	122.33	0.01
SQU-DS	2026-08-29 05:00:00	10.48	25.75	0.34	7.42	11.06	121.31	0.01
SQU-DS	2026-08-29 05:15:00	10.45	25.99	0.28	7.46	11.07	167.86	0.01
SQU-DS	2026-08-29 05:30:00	10.41	26.72	0.30	7.51	11.09	160.98	0.01
SQU-DS	2026-08-29 05:45:00	10.37	27.35	0.31	7.58	11.09	211.53	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-29 06:00:00	10.33	28.03	0.31	7.73	11.12	280.55	0.01
SQU-DS	2026-08-29 06:15:00	10.29	29.58	0.28	7.74	11.10	415.27	0.01
SQU-DS	2026-08-29 06:30:00	10.25	30.28	0.29	7.78	11.12	353.68	0.01
SQU-DS	2026-08-29 06:45:00	10.21	30.25	0.31	7.78	11.13	523.79	0.01
SQU-DS	2026-08-29 07:00:00	10.18	31.06	0.31	7.76	11.14	472.05	0.01
SQU-DS	2026-08-29 07:15:00	10.13	30.70	0.26	7.74	11.14	320.26	0.01
SQU-DS	2026-08-29 07:30:00	10.09	30.52	0.28	7.78	11.16	556.85	0.01
SQU-DS	2026-08-29 07:45:00	10.04	29.61	0.30	7.73	11.17	587.10	0.01
SQU-DS	2026-08-29 08:00:00	10.01	28.84	0.31	7.68	11.18	337.12	0.01
SQU-DS	2026-08-29 08:15:00	9.99	28.41	0.27	7.74	11.17	355.59	0.01
SQU-DS	2026-08-29 08:30:00	9.97	27.57	0.29	7.71	11.20	367.37	0.01
SQU-DS	2026-08-29 08:45:00	9.98	27.12	0.31	7.63	11.19	277.06	0.01
SQU-DS	2026-08-29 09:00:00	9.99	26.63	0.32	7.53	11.19	318.78	0.01
SQU-DS	2026-08-29 09:15:00	10.01	26.24	0.27	7.61	11.19	330.04	0.01
SQU-DS	2026-08-29 09:30:00	10.03	25.96	0.30	7.48	11.20	238.21	0.01
SQU-DS	2026-08-29 09:45:00	10.05	25.47	0.32	7.47	11.20	289.12	0.01
SQU-DS	2026-08-29 10:00:00	10.08	25.27	0.33	7.47	11.22	232.68	0.01
SQU-DS	2026-08-29 10:15:00	10.11	25.15	0.29	7.43	11.19	282.61	0.01
SQU-DS	2026-08-29 10:30:00	10.14	24.96	0.31	7.47	11.20	182.73	0.01
SQU-DS	2026-08-29 10:45:00	10.18	24.97	0.33	7.37	11.21	150.60	0.01
SQU-DS	2026-08-29 11:00:00	10.22	24.87	0.33	7.40	11.20	189.44	0.01
SQU-DS	2026-08-29 11:15:00	10.28	24.97	0.27	7.35	11.18	184.13	0.01
SQU-DS	2026-08-29 11:30:00	10.32	24.87	0.30	7.36	11.20	191.42	0.01
SQU-DS	2026-08-29 11:45:00	10.37	25.06	0.32	7.34	11.18	172.14	0.01
SQU-DS	2026-08-29 12:00:00	10.43	24.62	0.33	7.36	11.18	195.93	0.01
SQU-DS	2026-08-29 12:15:00	10.49	24.87	0.29	7.31	11.17	201.60	0.01
SQU-DS	2026-08-29 12:30:00	10.55	24.74	0.32	7.32	11.19	142.65	0.01
SQU-DS	2026-08-29 12:45:00	10.62	24.98	0.33	7.32	11.17	160.87	0.01
SQU-DS	2026-08-29 13:00:00	10.68	24.88	0.34	7.33	11.17	151.22	0.01
SQU-DS	2026-08-29 13:15:00	10.74	25.15	0.29	7.29	11.15	234.10	0.01
SQU-DS	2026-08-29 13:30:00	10.82	25.15	0.32	7.32	11.17	132.03	0.01
SQU-DS	2026-08-29 13:45:00	10.89	25.08	0.33	7.30	11.14	144.93	0.01
SQU-DS	2026-08-29 14:00:00	10.96	25.31	0.34	7.31	11.15	150.88	0.01
SQU-DS	2026-08-29 14:15:00	11.02	25.38	0.30	7.30	11.15	163.96	0.01
SQU-DS	2026-08-29 14:30:00	11.09	25.91	0.32	7.32	11.14	187.53	0.01
SQU-DS	2026-08-29 14:45:00	11.11	25.87	0.34	7.30	11.14	126.16	0.01
SQU-DS	2026-08-29 15:00:00	11.15	26.05	0.34	7.31	11.12	117.93	0.01
SQU-DS	2026-08-29 15:15:00	11.14	26.20	0.29	7.29	11.10	221.54	0.01
SQU-DS	2026-08-29 15:30:00	11.15	26.10	0.32	7.31	11.12	188.90	0.01
SQU-DS	2026-08-29 15:45:00	11.22	26.34	0.33	7.32	11.10	120.10	0.01
SQU-DS	2026-08-29 16:00:00	11.24	26.52	0.34	7.29	11.08	139.78	0.01
SQU-DS	2026-08-29 16:15:00	11.24	26.88	0.30	7.28	11.07	320.20	0.01
SQU-DS	2026-08-29 16:30:00	11.26	26.91	0.32	7.30	11.05	126.34	0.01
SQU-DS	2026-08-29 16:45:00	11.31	27.17	0.33	7.30	11.07	100.18	0.01
SQU-DS	2026-08-29 17:00:00	11.34	27.46	0.34	7.31	11.06	95.26	0.01
SQU-DS	2026-08-29 17:15:00	11.33	27.37	0.29	7.31	11.04	162.38	0.01
SQU-DS	2026-08-29 17:30:00	11.34	27.19	0.32	7.33	11.06	122.98	0.01
SQU-DS	2026-08-29 17:45:00	11.35	27.34	0.33	7.33	11.05	98.98	0.01
SQU-DS	2026-08-29 18:00:00	11.37	27.42	0.34	7.37	11.04	95.94	0.01
SQU-DS	2026-08-29 18:15:00	11.39	27.63	0.29	7.33	11.01	114.04	0.01
SQU-DS	2026-08-29 18:30:00	11.40	27.91	0.32	7.40	11.01	94.61	0.01
SQU-DS	2026-08-29 18:45:00	11.41	28.25	0.33	7.43	11.01	98.25	0.01
SQU-DS	2026-08-29 19:00:00	11.43	28.49	0.33	7.47	10.99	86.19	0.01
SQU-DS	2026-08-29 19:15:00	11.45	28.76	0.28	7.49	10.97	83.13	0.01
SQU-DS	2026-08-29 19:30:00	11.46	28.83	0.31	7.47	10.97	96.67	0.01
SQU-DS	2026-08-29 19:45:00	11.47	29.04	0.32	7.45	10.94	80.89	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-29 20:00:00	11.48	30.06	0.33	7.43	10.93	80.12	0.01
SQU-DS	2026-08-29 20:15:00	11.46	30.65	0.27	7.55	10.90	129.92	0.01
SQU-DS	2026-08-29 20:30:00	11.43	30.99	0.30	7.48	10.88	93.98	0.01
SQU-DS	2026-08-29 20:45:00	11.43	32.26	0.32	7.41	10.86	112.29	0.01
SQU-DS	2026-08-29 21:00:00	11.42	32.46	0.32	7.38	10.81	80.38	0.01
SQU-DS	2026-08-29 21:15:00	11.43	32.95	0.25	7.35	10.80	122.05	0.01
SQU-DS	2026-08-29 21:30:00	11.43	32.73	0.29	7.37	10.79	101.06	0.01
SQU-DS	2026-08-29 21:45:00	11.44	32.96	0.30	7.37	10.76	90.91	0.01
SQU-DS	2026-08-29 22:00:00	11.44	32.72	0.31	7.34	10.76	121.74	0.01
SQU-DS	2026-08-29 22:15:00	11.44	32.41	0.28	7.31	10.74	83.66	0.01
SQU-DS	2026-08-29 22:30:00	11.43	32.37	0.30	7.33	10.74	90.42	0.01
SQU-DS	2026-08-29 22:45:00	11.42	32.12	0.32	7.32	10.75	67.52	0.01
SQU-DS	2026-08-29 23:00:00	11.42	32.02	0.32	7.30	10.72	97.43	0.01
SQU-DS	2026-08-29 23:15:00	11.40	31.82	0.28	7.29	10.74	127.89	0.01
SQU-DS	2026-08-29 23:30:00	11.38	31.81	0.30	7.27	10.71	64.17	0.01
SQU-DS	2026-08-29 23:45:00	11.36	31.47	0.32	7.27	10.71	96.54	0.01
SQU-DS	2026-08-30 00:00:00	11.34	31.24	0.32	7.27	10.73	80.52	0.01
SQU-DS	2026-08-30 00:15:00	11.33	30.91	0.29	7.29	10.73	84.22	0.01
SQU-DS	2026-08-30 00:30:00	11.32	30.94	0.31	7.28	10.73	55.10	0.01
SQU-DS	2026-08-30 00:45:00	11.31	30.95	0.32	7.31	10.75	76.83	0.01
SQU-DS	2026-08-30 01:00:00	11.30	31.50	0.33	7.30	10.72	96.44	0.01
SQU-DS	2026-08-30 01:15:00	11.28	30.93	0.29	7.28	10.74	85.70	0.01
SQU-DS	2026-08-30 01:30:00	11.26	30.85	0.31	7.27	10.72	93.51	0.01
SQU-DS	2026-08-30 01:45:00	11.24	30.70	0.32	7.29	10.75	58.90	0.01
SQU-DS	2026-08-30 02:00:00	11.21	31.13	0.33	7.30	10.73	69.74	0.01
SQU-DS	2026-08-30 02:15:00	11.18	30.85	0.29	7.29	10.76	76.30	0.01
SQU-DS	2026-08-30 02:30:00	11.15	31.05	0.31	7.29	10.75	74.92	0.01
SQU-DS	2026-08-30 02:45:00	11.11	30.90	0.32	7.28	10.76	61.74	0.01
SQU-DS	2026-08-30 03:00:00	11.07	30.88	0.33	7.30	10.77	63.87	0.01
SQU-DS	2026-08-30 03:15:00	11.04	30.74	0.29	7.30	10.79	63.96	0.01
SQU-DS	2026-08-30 03:30:00	11.00	30.69	0.30	7.31	10.80	60.20	0.01
SQU-DS	2026-08-30 03:45:00	10.97	30.80	0.32	7.30	10.80	76.50	0.01
SQU-DS	2026-08-30 04:00:00	10.94	30.93	0.33	7.30	10.82	67.94	0.01
SQU-DS	2026-08-30 04:15:00	10.91	30.90	0.28	7.29	10.81	58.52	0.01
SQU-DS	2026-08-30 04:30:00	10.89	30.72	0.31	7.31	10.83	61.33	0.01
SQU-DS	2026-08-30 04:45:00	10.87	30.90	0.32	7.30	10.83	68.70	0.01
SQU-DS	2026-08-30 05:00:00	10.85	30.40	0.33	7.32	10.85	48.62	0.01
SQU-DS	2026-08-30 05:15:00	10.83	30.77	0.28	7.28	10.83	58.76	0.01
SQU-DS	2026-08-30 05:30:00	10.81	30.56	0.30	7.31	10.85	68.42	0.01
SQU-DS	2026-08-30 05:45:00	10.79	30.24	0.32	7.31	10.86	62.17	0.01
SQU-DS	2026-08-30 06:00:00	10.77	30.20	0.33	7.31	10.86	57.61	0.01
SQU-DS	2026-08-30 06:15:00	10.75	30.48	0.29	7.30	10.86	62.66	0.01
SQU-DS	2026-08-30 06:30:00	10.73	30.06	0.31	7.33	10.88	71.67	0.01
SQU-DS	2026-08-30 06:45:00	10.72	30.29	0.32	7.33	10.89	49.19	0.01
SQU-DS	2026-08-30 07:00:00	10.70	30.26	0.33	7.34	10.89	85.37	0.01
SQU-DS	2026-08-30 07:15:00	10.68	30.48	0.28	7.32	10.90	96.24	0.01
SQU-DS	2026-08-30 07:30:00	10.66	30.68	0.31	7.34	10.90	69.27	0.01
SQU-DS	2026-08-30 07:45:00	10.65	30.64	0.32	7.34	10.90	74.62	0.01
SQU-DS	2026-08-30 08:00:00	10.63	30.80	0.33	7.35	10.91	52.53	0.01
SQU-DS	2026-08-30 08:15:00	10.62	31.14	0.30	7.30	10.91	63.92	0.01
SQU-DS	2026-08-30 08:30:00	10.61	31.48	0.31	7.34	10.90	60.02	0.01
SQU-DS	2026-08-30 08:45:00	10.60	31.48	0.32	7.30	10.90	60.62	0.01
SQU-DS	2026-08-30 09:00:00	10.60	31.11	0.33	7.30	10.90	70.52	0.01
SQU-DS	2026-08-30 09:15:00	10.60	31.21	0.29	7.29	10.91	56.00	0.01
SQU-DS	2026-08-30 09:30:00	10.61	31.15	0.31	7.28	10.91	64.86	0.01
SQU-DS	2026-08-30 09:45:00	10.62	31.55	0.32	7.26	10.89	43.39	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-DS	2026-08-30 10:00:00	10.63	31.19	0.32	7.28	10.92	59.40	0.01
SQU-DS	2026-08-30 10:15:00	10.65	31.31	0.30	7.26	10.92	64.19	0.01
SQU-DS	2026-08-30 10:30:00	10.68	31.35	0.31	7.26	10.93	80.10	0.01
SQU-DS	2026-08-30 10:45:00	10.70	31.72	0.32	7.23	10.91	62.64	0.01
SQU-DS	2026-08-30 11:00:00	10.72	31.35	0.32	7.28	10.93	53.80	0.01
SQU-DS	2026-08-30 11:15:00	10.75	31.53	0.29	7.25	10.91	46.13	0.01
SQU-DS	2026-08-30 11:30:00	10.78	31.57	0.31	7.27	10.94	41.24	0.01
SQU-DS	2026-08-30 11:45:00	10.81	31.69	0.31	7.27	10.93	52.38	0.01
SQU-DS	2026-08-30 12:00:00	10.84	31.74	0.32	7.28	10.94	47.75	0.01
SQU-DS	2026-08-30 12:15:00	10.88	32.14	0.30	7.22	10.90	69.64	0.01
SQU-DS	2026-08-30 12:30:00	10.91	31.57	0.31	7.27	10.93	50.14	0.01
SQU-DS	2026-08-30 12:45:00	10.93	32.09	0.32	7.27	10.91	72.43	0.01
SQU-DS	2026-08-30 13:00:00	10.95	31.86	0.33	7.28	10.93	43.48	0.01
SQU-DS	2026-08-30 13:15:00	10.98	31.90	0.29	7.27	10.91	46.93	0.01
SQU-DS	2026-08-30 13:30:00	11.01	32.15	0.30	7.30	10.92	58.26	0.01
SQU-DS	2026-08-30 13:45:00	11.04	32.28	0.31	7.29	10.91	40.58	0.01
SQU-DS	2026-08-30 14:00:00	11.06	32.57	0.32	7.27	10.90	52.74	0.01
SQU-DS	2026-08-30 14:15:00	11.08	32.56	0.30	7.28	10.89	42.55	0.01
SQU-DS	2026-08-30 14:30:00	11.11	32.58	0.31	7.29	10.90	46.42	0.01
SQU-DS	2026-08-30 14:45:00	11.14	32.40	0.32	7.30	10.90	55.36	0.01
SQU-DS	2026-08-30 15:00:00	11.16	32.68	0.32	7.30	10.89	37.20	0.01
SQU-DS	2026-08-30 15:15:00	11.20	32.57	0.30	7.30	10.89	48.41	0.01
SQU-DS	2026-08-30 15:30:00	11.24	33.02	0.31	7.31	10.87	62.59	0.01
SQU-DS	2026-08-30 15:45:00	11.27	32.81	0.32	7.32	10.89	56.14	0.01
SQU-DS	2026-08-30 16:00:00	11.30	33.03	0.32	7.30	10.87	45.18	0.01
SQU-DS	2026-08-30 16:15:00	11.32	33.21	0.31	7.29	10.87	52.87	0.01
SQU-DS	2026-08-30 16:30:00	11.34	33.08	0.32	7.30	10.87	45.04	0.01
SQU-DS	2026-08-30 16:45:00	11.36	33.46	0.32	7.31	10.85	43.81	0.01
SQU-DS	2026-08-30 17:00:00	11.38	33.52	0.32	7.31	10.86	51.61	0.01
SQU-DS	2026-08-30 17:15:00	11.39	33.28	0.30	7.30	10.86	42.64	0.01
SQU-DS	2026-08-30 17:30:00	11.40	33.43	0.31	7.33	10.85	53.00	0.01
SQU-DS	2026-08-30 17:45:00	11.41	33.48	0.32	7.32	10.85	52.20	0.01
SQU-DS	2026-08-30 18:00:00	11.41	33.29	0.32	7.35	10.87	29.15	0.01
SQU-DS	2026-08-30 18:15:00	11.41	33.08	0.30	7.34	10.87	67.14	0.01
SQU-DS	2026-08-30 18:30:00	11.41	33.19	0.32	7.37	10.87	45.91	0.01
SQU-DS	2026-08-30 18:45:00	11.41	33.10	0.33	7.38	10.87	40.28	0.01
SQU-DS	2026-08-30 19:00:00	11.39	33.41	0.34	7.38	10.86	44.93	0.01
SQU-DS	2026-08-30 19:15:00	11.38	33.47	0.30	7.38	10.85	67.93	0.01
SQU-DS	2026-08-30 19:30:00	11.37	33.69	0.31	7.40	10.85	53.78	0.01
SQU-DS	2026-08-30 19:45:00	11.36	33.91	0.33	7.39	10.84	29.42	0.01
SQU-DS	2026-08-30 20:00:00	11.36	34.31	0.33	7.41	10.83	39.80	0.01
SQU-DS	2026-08-30 20:15:00	11.35	34.99	0.30	7.42	10.82	92.76	0.02
SQU-DS	2026-08-30 20:30:00	11.35	35.48	0.31	7.41	10.81	44.76	0.02
SQU-DS	2026-08-30 20:45:00	11.36	35.94	0.32	7.48	10.79	26.92	0.02
SQU-DS	2026-08-30 21:00:00	11.37	36.89	0.32	7.45	10.76	41.73	0.02
SQU-DS	2026-08-30 21:15:00	11.37	37.38	0.28	7.39	10.74	101.24	0.02
SQU-DS	2026-08-30 21:30:00	11.38	37.60	0.30	7.37	10.72	39.57	0.02
SQU-DS	2026-08-30 21:45:00	11.39	37.86	0.31	7.36	10.71	48.35	0.02
SQU-DS	2026-08-30 22:00:00	11.39	37.50	0.32	7.35	10.70	56.00	0.02
SQU-DS	2026-08-30 22:15:00	11.40	37.37	0.29	7.33	10.69	52.58	0.02
SQU-DS	2026-08-30 22:30:00	11.41	36.81	0.31	7.34	10.69	35.55	0.02
SQU-DS	2026-08-30 22:45:00	11.40	36.68	0.31	7.33	10.71	40.55	0.02
SQU-DS	2026-08-30 23:00:00	11.41	36.46	0.32	7.33	10.68	37.79	0.02
SQU-DS	2026-08-30 23:15:00	11.40	36.12	0.29	7.29	10.67	31.11	0.02
SQU-DS	2026-08-30 23:30:00	11.39	35.96	0.30	7.30	10.68	44.26	0.02
SQU-DS	2026-08-30 23:45:00	11.38	35.73	0.31	7.30	10.68	48.33	0.02

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-24 00:00:00							
SQU-US	2026-08-24 00:15:00							
SQU-US	2026-08-24 00:30:00							
SQU-US	2026-08-24 00:45:00							
SQU-US	2026-08-24 01:00:00							
SQU-US	2026-08-24 01:15:00							
SQU-US	2026-08-24 01:30:00							
SQU-US	2026-08-24 01:45:00							
SQU-US	2026-08-24 02:00:00							
SQU-US	2026-08-24 02:15:00							
SQU-US	2026-08-24 02:30:00							
SQU-US	2026-08-24 02:45:00							
SQU-US	2026-08-24 03:00:00							
SQU-US	2026-08-24 03:15:00							
SQU-US	2026-08-24 03:30:00							
SQU-US	2026-08-24 03:45:00							
SQU-US	2026-08-24 04:00:00							
SQU-US	2026-08-24 04:15:00							
SQU-US	2026-08-24 04:30:00							
SQU-US	2026-08-24 04:45:00							
SQU-US	2026-08-24 05:00:00							
SQU-US	2026-08-24 05:15:00							
SQU-US	2026-08-24 05:30:00							
SQU-US	2026-08-24 05:45:00							
SQU-US	2026-08-24 06:00:00							
SQU-US	2026-08-24 06:15:00							
SQU-US	2026-08-24 06:30:00							
SQU-US	2026-08-24 06:45:00							
SQU-US	2026-08-24 07:00:00							
SQU-US	2026-08-24 07:15:00							
SQU-US	2026-08-24 07:30:00							
SQU-US	2026-08-24 07:45:00							
SQU-US	2026-08-24 08:00:00							
SQU-US	2026-08-24 08:15:00							
SQU-US	2026-08-24 08:30:00							
SQU-US	2026-08-24 08:45:00							
SQU-US	2026-08-24 09:00:00							
SQU-US	2026-08-24 09:15:00							
SQU-US	2026-08-24 09:30:00							
SQU-US	2026-08-24 09:45:00							
SQU-US	2026-08-24 10:00:00							
SQU-US	2026-08-24 10:15:00							
SQU-US	2026-08-24 10:30:00							
SQU-US	2026-08-24 10:45:00							
SQU-US	2026-08-24 11:00:00							
SQU-US	2026-08-24 11:15:00							
SQU-US	2026-08-24 11:30:00							
SQU-US	2026-08-24 11:45:00							
SQU-US	2026-08-24 12:00:00							
SQU-US	2026-08-24 12:15:00							
SQU-US	2026-08-24 12:30:00							
SQU-US	2026-08-24 12:45:00							
SQU-US	2026-08-24 13:00:00							
SQU-US	2026-08-24 13:15:00							
SQU-US	2026-08-24 13:30:00							
SQU-US	2026-08-24 13:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-24 14:00:00							
SQU-US	2026-08-24 14:15:00							
SQU-US	2026-08-24 14:30:00							
SQU-US	2026-08-24 14:45:00							
SQU-US	2026-08-24 15:00:00							
SQU-US	2026-08-24 15:15:00							
SQU-US	2026-08-24 15:30:00							
SQU-US	2026-08-24 15:45:00							
SQU-US	2026-08-24 16:00:00							
SQU-US	2026-08-24 16:15:00							
SQU-US	2026-08-24 16:30:00							
SQU-US	2026-08-24 16:45:00							
SQU-US	2026-08-24 17:00:00							
SQU-US	2026-08-24 17:15:00							
SQU-US	2026-08-24 17:30:00							
SQU-US	2026-08-24 17:45:00							
SQU-US	2026-08-24 18:00:00							
SQU-US	2026-08-24 18:15:00							
SQU-US	2026-08-24 18:30:00							
SQU-US	2026-08-24 18:45:00							
SQU-US	2026-08-24 19:00:00							
SQU-US	2026-08-24 19:15:00							
SQU-US	2026-08-24 19:30:00							
SQU-US	2026-08-24 19:45:00							
SQU-US	2026-08-24 20:00:00							
SQU-US	2026-08-24 20:15:00							
SQU-US	2026-08-24 20:30:00							
SQU-US	2026-08-24 20:45:00							
SQU-US	2026-08-24 21:00:00							
SQU-US	2026-08-24 21:15:00							
SQU-US	2026-08-24 21:30:00							
SQU-US	2026-08-24 21:45:00							
SQU-US	2026-08-24 22:00:00							
SQU-US	2026-08-24 22:15:00							
SQU-US	2026-08-24 22:30:00							
SQU-US	2026-08-24 22:45:00							
SQU-US	2026-08-24 23:00:00							
SQU-US	2026-08-24 23:15:00							
SQU-US	2026-08-24 23:30:00							
SQU-US	2026-08-24 23:45:00							
SQU-US	2026-08-25 00:00:00							
SQU-US	2026-08-25 00:15:00							
SQU-US	2026-08-25 00:30:00							
SQU-US	2026-08-25 00:45:00							
SQU-US	2026-08-25 01:00:00							
SQU-US	2026-08-25 01:15:00							
SQU-US	2026-08-25 01:30:00							
SQU-US	2026-08-25 01:45:00							
SQU-US	2026-08-25 02:00:00							
SQU-US	2026-08-25 02:15:00							
SQU-US	2026-08-25 02:30:00							
SQU-US	2026-08-25 02:45:00							
SQU-US	2026-08-25 03:00:00							
SQU-US	2026-08-25 03:15:00							
SQU-US	2026-08-25 03:30:00							
SQU-US	2026-08-25 03:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-25 04:00:00							
SQU-US	2026-08-25 04:15:00							
SQU-US	2026-08-25 04:30:00							
SQU-US	2026-08-25 04:45:00							
SQU-US	2026-08-25 05:00:00							
SQU-US	2026-08-25 05:15:00							
SQU-US	2026-08-25 05:30:00							
SQU-US	2026-08-25 05:45:00							
SQU-US	2026-08-25 06:00:00							
SQU-US	2026-08-25 06:15:00							
SQU-US	2026-08-25 06:30:00							
SQU-US	2026-08-25 06:45:00							
SQU-US	2026-08-25 07:00:00							
SQU-US	2026-08-25 07:15:00							
SQU-US	2026-08-25 07:30:00							
SQU-US	2026-08-25 07:45:00							
SQU-US	2026-08-25 08:00:00							
SQU-US	2026-08-25 08:15:00							
SQU-US	2026-08-25 08:30:00							
SQU-US	2026-08-25 08:45:00							
SQU-US	2026-08-25 09:00:00							
SQU-US	2026-08-25 09:15:00							
SQU-US	2026-08-25 09:30:00							
SQU-US	2026-08-25 09:45:00							
SQU-US	2026-08-25 10:00:00							
SQU-US	2026-08-25 10:15:00							
SQU-US	2026-08-25 10:30:00							
SQU-US	2026-08-25 10:45:00							
SQU-US	2026-08-25 11:00:00							
SQU-US	2026-08-25 11:15:00							
SQU-US	2026-08-25 11:30:00							
SQU-US	2026-08-25 11:45:00							
SQU-US	2026-08-25 12:00:00							
SQU-US	2026-08-25 12:15:00							
SQU-US	2026-08-25 12:30:00							
SQU-US	2026-08-25 12:45:00							
SQU-US	2026-08-25 13:00:00							
SQU-US	2026-08-25 13:15:00							
SQU-US	2026-08-25 13:30:00							
SQU-US	2026-08-25 13:45:00							
SQU-US	2026-08-25 14:00:00							
SQU-US	2026-08-25 14:15:00							
SQU-US	2026-08-25 14:30:00							
SQU-US	2026-08-25 14:45:00							
SQU-US	2026-08-25 15:00:00							
SQU-US	2026-08-25 15:15:00							
SQU-US	2026-08-25 15:30:00							
SQU-US	2026-08-25 15:45:00							
SQU-US	2026-08-25 16:00:00							
SQU-US	2026-08-25 16:15:00							
SQU-US	2026-08-25 16:30:00							
SQU-US	2026-08-25 16:45:00							
SQU-US	2026-08-25 17:00:00							
SQU-US	2026-08-25 17:15:00							
SQU-US	2026-08-25 17:30:00							
SQU-US	2026-08-25 17:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-25 18:00:00							
SQU-US	2026-08-25 18:15:00							
SQU-US	2026-08-25 18:30:00							
SQU-US	2026-08-25 18:45:00							
SQU-US	2026-08-25 19:00:00							
SQU-US	2026-08-25 19:15:00							
SQU-US	2026-08-25 19:30:00							
SQU-US	2026-08-25 19:45:00							
SQU-US	2026-08-25 20:00:00							
SQU-US	2026-08-25 20:15:00							
SQU-US	2026-08-25 20:30:00							
SQU-US	2026-08-25 20:45:00							
SQU-US	2026-08-25 21:00:00							
SQU-US	2026-08-25 21:15:00							
SQU-US	2026-08-25 21:30:00							
SQU-US	2026-08-25 21:45:00							
SQU-US	2026-08-25 22:00:00							
SQU-US	2026-08-25 22:15:00							
SQU-US	2026-08-25 22:30:00							
SQU-US	2026-08-25 22:45:00							
SQU-US	2026-08-25 23:00:00							
SQU-US	2026-08-25 23:15:00							
SQU-US	2026-08-25 23:30:00							
SQU-US	2026-08-25 23:45:00							
SQU-US	2026-08-26 00:00:00							
SQU-US	2026-08-26 00:15:00							
SQU-US	2026-08-26 00:30:00							
SQU-US	2026-08-26 00:45:00							
SQU-US	2026-08-26 01:00:00							
SQU-US	2026-08-26 01:15:00							
SQU-US	2026-08-26 01:30:00							
SQU-US	2026-08-26 01:45:00							
SQU-US	2026-08-26 02:00:00							
SQU-US	2026-08-26 02:15:00							
SQU-US	2026-08-26 02:30:00							
SQU-US	2026-08-26 02:45:00							
SQU-US	2026-08-26 03:00:00							
SQU-US	2026-08-26 03:15:00							
SQU-US	2026-08-26 03:30:00							
SQU-US	2026-08-26 03:45:00							
SQU-US	2026-08-26 04:00:00							
SQU-US	2026-08-26 04:15:00							
SQU-US	2026-08-26 04:30:00							
SQU-US	2026-08-26 04:45:00							
SQU-US	2026-08-26 05:00:00							
SQU-US	2026-08-26 05:15:00							
SQU-US	2026-08-26 05:30:00							
SQU-US	2026-08-26 05:45:00							
SQU-US	2026-08-26 06:00:00							
SQU-US	2026-08-26 06:15:00							
SQU-US	2026-08-26 06:30:00							
SQU-US	2026-08-26 06:45:00							
SQU-US	2026-08-26 07:00:00							
SQU-US	2026-08-26 07:15:00							
SQU-US	2026-08-26 07:30:00							
SQU-US	2026-08-26 07:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-26 08:00:00							
SQU-US	2026-08-26 08:15:00							
SQU-US	2026-08-26 08:30:00							
SQU-US	2026-08-26 08:45:00							
SQU-US	2026-08-26 09:00:00							
SQU-US	2026-08-26 09:15:00							
SQU-US	2026-08-26 09:30:00							
SQU-US	2026-08-26 09:45:00							
SQU-US	2026-08-26 10:00:00							
SQU-US	2026-08-26 10:15:00							
SQU-US	2026-08-26 10:30:00							
SQU-US	2026-08-26 10:45:00							
SQU-US	2026-08-26 11:00:00							
SQU-US	2026-08-26 11:15:00							
SQU-US	2026-08-26 11:30:00							
SQU-US	2026-08-26 11:45:00							
SQU-US	2026-08-26 12:00:00							
SQU-US	2026-08-26 12:15:00							
SQU-US	2026-08-26 12:30:00							
SQU-US	2026-08-26 12:45:00							
SQU-US	2026-08-26 13:00:00							
SQU-US	2026-08-26 13:15:00							
SQU-US	2026-08-26 13:30:00							
SQU-US	2026-08-26 13:45:00							
SQU-US	2026-08-26 14:00:00							
SQU-US	2026-08-26 14:15:00							
SQU-US	2026-08-26 14:30:00							
SQU-US	2026-08-26 14:45:00							
SQU-US	2026-08-26 15:00:00							
SQU-US	2026-08-26 15:15:00							
SQU-US	2026-08-26 15:30:00							
SQU-US	2026-08-26 15:45:00							
SQU-US	2026-08-26 16:00:00							
SQU-US	2026-08-26 16:15:00							
SQU-US	2026-08-26 16:30:00							
SQU-US	2026-08-26 16:45:00							
SQU-US	2026-08-26 17:00:00							
SQU-US	2026-08-26 17:15:00							
SQU-US	2026-08-26 17:30:00							
SQU-US	2026-08-26 17:45:00							
SQU-US	2026-08-26 18:00:00							
SQU-US	2026-08-26 18:15:00							
SQU-US	2026-08-26 18:30:00							
SQU-US	2026-08-26 18:45:00							
SQU-US	2026-08-26 19:00:00							
SQU-US	2026-08-26 19:15:00							
SQU-US	2026-08-26 19:30:00							
SQU-US	2026-08-26 19:45:00							
SQU-US	2026-08-26 20:00:00							
SQU-US	2026-08-26 20:15:00							
SQU-US	2026-08-26 20:30:00							
SQU-US	2026-08-26 20:45:00							
SQU-US	2026-08-26 21:00:00							
SQU-US	2026-08-26 21:15:00							
SQU-US	2026-08-26 21:30:00							
SQU-US	2026-08-26 21:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-26 22:00:00							
SQU-US	2026-08-26 22:15:00							
SQU-US	2026-08-26 22:30:00							
SQU-US	2026-08-26 22:45:00							
SQU-US	2026-08-26 23:00:00							
SQU-US	2026-08-26 23:15:00							
SQU-US	2026-08-26 23:30:00							
SQU-US	2026-08-26 23:45:00							
SQU-US	2026-08-27 00:00:00							
SQU-US	2026-08-27 00:15:00							
SQU-US	2026-08-27 00:30:00							
SQU-US	2026-08-27 00:45:00							
SQU-US	2026-08-27 01:00:00							
SQU-US	2026-08-27 01:15:00							
SQU-US	2026-08-27 01:30:00							
SQU-US	2026-08-27 01:45:00							
SQU-US	2026-08-27 02:00:00							
SQU-US	2026-08-27 02:15:00							
SQU-US	2026-08-27 02:30:00							
SQU-US	2026-08-27 02:45:00							
SQU-US	2026-08-27 03:00:00							
SQU-US	2026-08-27 03:15:00							
SQU-US	2026-08-27 03:30:00							
SQU-US	2026-08-27 03:45:00							
SQU-US	2026-08-27 04:00:00							
SQU-US	2026-08-27 04:15:00							
SQU-US	2026-08-27 04:30:00							
SQU-US	2026-08-27 04:45:00							
SQU-US	2026-08-27 05:00:00							
SQU-US	2026-08-27 05:15:00							
SQU-US	2026-08-27 05:30:00							
SQU-US	2026-08-27 05:45:00							
SQU-US	2026-08-27 06:00:00							
SQU-US	2026-08-27 06:15:00							
SQU-US	2026-08-27 06:30:00							
SQU-US	2026-08-27 06:45:00							
SQU-US	2026-08-27 07:00:00							
SQU-US	2026-08-27 07:15:00							
SQU-US	2026-08-27 07:30:00							
SQU-US	2026-08-27 07:45:00							
SQU-US	2026-08-27 08:00:00							
SQU-US	2026-08-27 08:15:00							
SQU-US	2026-08-27 08:30:00							
SQU-US	2026-08-27 08:45:00							
SQU-US	2026-08-27 09:00:00							
SQU-US	2026-08-27 09:15:00							
SQU-US	2026-08-27 09:30:00							
SQU-US	2026-08-27 09:45:00							
SQU-US	2026-08-27 10:00:00							
SQU-US	2026-08-27 10:15:00							
SQU-US	2026-08-27 10:30:00							
SQU-US	2026-08-27 10:45:00							
SQU-US	2026-08-27 11:00:00							
SQU-US	2026-08-27 11:15:00							
SQU-US	2026-08-27 11:30:00							
SQU-US	2026-08-27 11:45:00							

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-27 12:00:00							
SQU-US	2026-08-27 12:15:00	21.89	92.87	0.32	6.61	7.19	2.16	0.04
SQU-US	2026-08-27 12:30:00	11.61	26.82	0.32	6.49	10.10	71.83	0.01
SQU-US	2026-08-27 12:45:00	11.68	27.00	0.33	6.42	10.07	59.88	0.01
SQU-US	2026-08-27 13:00:00	11.68	26.90	0.33	6.41	10.07	59.42	0.01
SQU-US	2026-08-27 13:15:00	11.72	27.50	0.32	6.43	10.07	69.54	0.01
SQU-US	2026-08-27 13:30:00	11.78	27.06	0.32	6.47	10.07	62.83	0.01
SQU-US	2026-08-27 13:45:00	11.81	27.34	0.32	6.51	10.09	62.38	0.01
SQU-US	2026-08-27 14:00:00	11.86	27.39	0.32	6.52	10.08	60.40	0.01
SQU-US	2026-08-27 14:15:00	11.88	27.51	0.32	6.52	10.10	60.61	0.01
SQU-US	2026-08-27 14:30:00	11.88	27.19	0.32	6.54	10.10	63.35	0.01
SQU-US	2026-08-27 14:45:00	11.92	27.61	0.32	6.51	10.09	62.95	0.01
SQU-US	2026-08-27 15:00:00	11.92	28.08	0.32	6.50	10.09	60.22	0.01
SQU-US	2026-08-27 15:15:00	11.93	27.80	0.31	6.52	10.09	67.75	0.01
SQU-US	2026-08-27 15:30:00	11.94	28.07	0.31	6.51	10.08	61.40	0.01
SQU-US	2026-08-27 15:45:00	11.95	28.39	0.31	6.47	10.09	57.60	0.01
SQU-US	2026-08-27 16:00:00	11.96	28.28	0.32	6.47	10.09	57.92	0.01
SQU-US	2026-08-27 16:15:00	11.97	28.43	0.31	6.52	10.10	62.31	0.01
SQU-US	2026-08-27 16:30:00	11.97	28.55	0.32	6.53	10.10	58.51	0.01
SQU-US	2026-08-27 16:45:00	11.98	28.38	0.31	6.55	10.10	55.60	0.01
SQU-US	2026-08-27 17:00:00	11.97	28.58	0.31	6.62	10.12	55.38	0.01
SQU-US	2026-08-27 17:15:00	11.94	28.58	0.32	6.56	10.13	54.04	0.01
SQU-US	2026-08-27 17:30:00	11.92	28.62	0.32	6.59	10.12	60.73	0.01
SQU-US	2026-08-27 17:45:00	11.90	28.70	0.33	6.57	10.13	55.48	0.01
SQU-US	2026-08-27 18:00:00	11.88	28.95	0.33	6.61	10.12	53.23	0.01
SQU-US	2026-08-27 18:15:00	11.87	29.21	0.33	6.62	10.13	56.90	0.01
SQU-US	2026-08-27 18:30:00	11.86	29.83	0.33	6.63	10.11	60.28	0.01
SQU-US	2026-08-27 18:45:00	11.84	30.00	0.34	6.61	10.10	59.31	0.01
SQU-US	2026-08-27 19:00:00	11.83	30.89	0.34	6.53	10.10	56.29	0.01
SQU-US	2026-08-27 19:15:00	11.81	31.40	0.34	6.63	10.10	61.15	0.01
SQU-US	2026-08-27 19:30:00	11.80	32.46	0.34	6.61	10.08	52.76	0.01
SQU-US	2026-08-27 19:45:00	11.79	32.54	0.34	6.65	10.06	54.61	0.01
SQU-US	2026-08-27 20:00:00	11.78	32.75	0.34	6.60	10.04	58.39	0.01
SQU-US	2026-08-27 20:15:00	11.76	32.50	0.34	6.59	10.04	54.69	0.01
SQU-US	2026-08-27 20:30:00	11.74	32.44	0.34	6.59	10.04	64.93	0.01
SQU-US	2026-08-27 20:45:00	11.72	32.31	0.34	6.58	10.02	60.88	0.01
SQU-US	2026-08-27 21:00:00	11.70	31.44	0.33	6.56	10.04	66.58	0.01
SQU-US	2026-08-27 21:15:00	11.68	30.93	0.33	6.54	10.02	67.44	0.01
SQU-US	2026-08-27 21:30:00	11.65	30.49	0.33	6.57	10.03	64.79	0.01
SQU-US	2026-08-27 21:45:00	11.63	29.81	0.33	6.50	10.04	76.88	0.01
SQU-US	2026-08-27 22:00:00	11.59	28.76	0.33	6.49	10.07	75.42	0.01
SQU-US	2026-08-27 22:15:00	11.56	28.12	0.32	6.48	10.07	77.92	0.01
SQU-US	2026-08-27 22:30:00	11.52	27.03	0.32	6.49	10.09	76.42	0.01
SQU-US	2026-08-27 22:45:00	11.49	26.31	0.32	6.56	10.12	80.32	0.01
SQU-US	2026-08-27 23:00:00	11.45	25.52	0.33	6.47	10.13	77.74	0.01
SQU-US	2026-08-27 23:15:00	11.40	25.30	0.33	6.51	10.14	102.98	0.01
SQU-US	2026-08-27 23:30:00	11.34	25.23	0.34	6.52	10.17	110.06	0.01
SQU-US	2026-08-27 23:45:00	11.27	25.45	0.34	6.52	10.19	144.12	0.01
SQU-US	2026-08-28 00:00:00	11.22	26.72	0.34	6.62	10.20	182.84	0.01
SQU-US	2026-08-28 00:15:00	11.17	28.08	0.35	6.59	10.21	307.22	0.01
SQU-US	2026-08-28 00:30:00	11.13	29.31	0.34	6.69	10.22	315.81	0.01
SQU-US	2026-08-28 00:45:00	11.07	30.16	0.34	6.83	10.22	327.06	0.01
SQU-US	2026-08-28 01:00:00	11.02	30.02	0.34	6.80	10.26	451.12	0.01
SQU-US	2026-08-28 01:15:00	11.01	30.58	0.34	6.82	10.24	342.69	0.01
SQU-US	2026-08-28 01:30:00	11.00	30.11	0.34	6.82	10.25	342.70	0.01
SQU-US	2026-08-28 01:45:00	10.99	29.39	0.34	6.85	10.25	294.80	0.01


Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-28 02:00:00	11.00	29.19	0.34	6.79	10.26	220.53	0.01
SQU-US	2026-08-28 02:15:00	11.00	28.53	0.35	6.78	10.26	274.05	0.01
SQU-US	2026-08-28 02:30:00	11.02	28.81	0.35	6.76	10.26	200.17	0.01
SQU-US	2026-08-28 02:45:00	11.01	28.41	0.35	6.68	10.27	191.36	0.01
SQU-US	2026-08-28 03:00:00	11.01	28.27	0.35	6.77	10.28	230.52	0.01
SQU-US	2026-08-28 03:15:00	10.98	27.06	0.35	6.77	10.28	231.21	0.01
SQU-US	2026-08-28 03:30:00	10.98	27.56	0.35	6.79	10.29	161.81	0.01
SQU-US	2026-08-28 03:45:00	10.96	27.11	0.36	6.72	10.29	164.66	0.01
SQU-US	2026-08-28 04:00:00	10.95	27.32	0.35	6.74	10.29	157.19	0.01
SQU-US	2026-08-28 04:15:00	10.92	25.98	0.35	6.81	10.30	143.98	0.01
SQU-US	2026-08-28 04:30:00	10.91	25.90	0.35	6.81	10.30	123.05	0.01
SQU-US	2026-08-28 04:45:00	10.90	25.44	0.36	6.76	10.31	140.37	0.01
SQU-US	2026-08-28 05:00:00	10.88	25.22	0.36	6.80	10.31	128.83	0.01
SQU-US	2026-08-28 05:15:00	10.87	25.23	0.36	6.84	10.31	126.11	0.01
SQU-US	2026-08-28 05:30:00	10.85	24.89	0.36	6.80	10.32	160.93	0.01
SQU-US	2026-08-28 05:45:00	10.84	24.92	0.36	6.77	10.31	136.31	0.01
SQU-US	2026-08-28 06:00:00	10.81	24.56	0.36	6.81	10.32	171.06	0.01
SQU-US	2026-08-28 06:15:00	10.77	24.08	0.36	6.81	10.34	137.91	0.01
SQU-US	2026-08-28 06:30:00	10.74	24.04	0.36	6.82	10.34	158.48	0.01
SQU-US	2026-08-28 06:45:00	10.72	23.74	0.36	6.80	10.35	105.99	0.01
SQU-US	2026-08-28 07:00:00	10.70	24.13	0.37	6.77	10.35	125.74	0.01
SQU-US	2026-08-28 07:15:00	10.67	24.17	0.37	6.77	10.34	108.59	0.01
SQU-US	2026-08-28 07:30:00	10.64	23.85	0.37	6.74	10.36	137.42	0.01
SQU-US	2026-08-28 07:45:00	10.63	25.22	0.37	6.79	10.36	126.52	0.01
SQU-US	2026-08-28 08:00:00	10.61	24.98	0.37	6.73	10.36	146.90	0.01
SQU-US	2026-08-28 08:15:00	10.60	24.90	0.37	6.70	10.37	132.35	0.01
SQU-US	2026-08-28 08:30:00	10.60	24.55	0.37	6.74	10.37	163.56	0.01
SQU-US	2026-08-28 08:45:00	10.60	25.33	0.37	6.71	10.38	149.39	0.01
SQU-US	2026-08-28 09:00:00	10.61	24.86	0.37	6.74	10.37	148.14	0.01
SQU-US	2026-08-28 09:15:00	10.64	25.51	0.37	6.70	10.37	119.61	0.01
SQU-US	2026-08-28 09:30:00	10.69	24.70	0.37	6.70	10.37	134.80	0.01
SQU-US	2026-08-28 09:45:00	10.75	25.48	0.37	6.72	10.37	123.18	0.01
SQU-US	2026-08-28 10:00:00	10.78	25.17	0.37	6.68	10.38	155.89	0.01
SQU-US	2026-08-28 10:15:00	10.82	24.87	0.37	6.69	10.36	152.29	0.01
SQU-US	2026-08-28 10:30:00	10.85	25.00	0.37	6.68	10.37	121.44	0.01
SQU-US	2026-08-28 10:45:00	10.88	24.41	0.37	6.73	10.38	164.76	0.01
SQU-US	2026-08-28 11:00:00	10.88	23.61	0.37	6.63	10.37	142.73	0.01
SQU-US	2026-08-28 11:15:00	10.92	24.07	0.36	6.74	10.37	129.28	0.01
SQU-US	2026-08-28 11:30:00	10.92	23.96	0.36	6.72	10.38	140.44	0.01
SQU-US	2026-08-28 11:45:00	10.91	23.25	0.37	6.64	10.37	117.79	0.01
SQU-US	2026-08-28 12:00:00	10.93	23.83	0.36	6.67	10.36	116.66	0.01
SQU-US	2026-08-28 12:15:00	10.93	23.79	0.36	6.68	10.37	107.05	0.01
SQU-US	2026-08-28 12:30:00	10.93	23.84	0.37	6.61	10.36	121.62	0.01
SQU-US	2026-08-28 12:45:00	10.93	24.15	0.36	6.71	10.37	142.94	0.01
SQU-US	2026-08-28 13:00:00	10.94	24.01	0.36	6.71	10.36	131.76	0.01
SQU-US	2026-08-28 13:15:00	10.94	23.29	0.36	6.71	10.38	123.92	0.01
SQU-US	2026-08-28 13:30:00	10.98	24.14	0.36	6.71	10.36	124.27	0.01
SQU-US	2026-08-28 13:45:00	10.99	24.06	0.36	6.72	10.36	131.30	0.01
SQU-US	2026-08-28 14:00:00	11.00	24.06	0.36	6.67	10.37	123.71	0.01
SQU-US	2026-08-28 14:15:00	11.00	24.19	0.36	6.68	10.38	125.65	0.01
SQU-US	2026-08-28 14:30:00	11.02	24.22	0.36	6.68	10.36	137.38	0.01
SQU-US	2026-08-28 14:45:00	11.04	24.50	0.36	6.70	10.37	145.37	0.01
SQU-US	2026-08-28 15:00:00	11.08	24.66	0.35	6.84	10.36	107.34	0.01
SQU-US	2026-08-28 15:15:00	11.11	24.55	0.35	6.79	10.36	112.89	0.01
SQU-US	2026-08-28 15:30:00	11.15	24.59	0.35	6.76	10.35	89.74	0.01
SQU-US	2026-08-28 15:45:00	11.19	24.83	0.36	6.73	10.34	94.64	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-28 16:00:00	11.22	24.98	0.36	6.72	10.34	74.74	0.01
SQU-US	2026-08-28 16:15:00	11.24	25.07	0.36	6.70	10.33	89.44	0.01
SQU-US	2026-08-28 16:30:00	11.26	25.34	0.36	6.71	10.32	88.83	0.01
SQU-US	2026-08-28 16:45:00	11.27	25.57	0.36	6.71	10.32	84.59	0.01
SQU-US	2026-08-28 17:00:00	11.27	25.40	0.36	6.71	10.32	87.43	0.01
SQU-US	2026-08-28 17:15:00	11.27	25.30	0.36	6.71	10.31	86.14	0.01
SQU-US	2026-08-28 17:30:00	11.28	25.69	0.36	6.71	10.29	92.94	0.01
SQU-US	2026-08-28 17:45:00	11.27	25.45	0.36	6.68	10.31	82.07	0.01
SQU-US	2026-08-28 18:00:00	11.28	25.70	0.36	6.68	10.29	91.01	0.01
SQU-US	2026-08-28 18:15:00	11.27	25.50	0.36	6.68	10.29	73.93	0.01
SQU-US	2026-08-28 18:30:00	11.28	26.09	0.36	6.68	10.28	79.52	0.01
SQU-US	2026-08-28 18:45:00	11.28	26.00	0.36	6.68	10.28	68.45	0.01
SQU-US	2026-08-28 19:00:00	11.28	26.41	0.36	6.68	10.27	74.29	0.01
SQU-US	2026-08-28 19:15:00	11.29	26.39	0.36	6.67	10.26	70.75	0.01
SQU-US	2026-08-28 19:30:00	11.31	26.64	0.37	6.67	10.25	92.43	0.01
SQU-US	2026-08-28 19:45:00	11.32	26.87	0.37	6.67	10.24	66.94	0.01
SQU-US	2026-08-28 20:00:00	11.35	28.08	0.37	6.67	10.21	63.83	0.01
SQU-US	2026-08-28 20:15:00	11.36	28.34	0.37	6.66	10.20	68.79	0.01
SQU-US	2026-08-28 20:30:00	11.37	27.97	0.37	6.65	10.19	75.98	0.01
SQU-US	2026-08-28 20:45:00	11.38	28.33	0.36	6.65	10.17	69.70	0.01
SQU-US	2026-08-28 21:00:00	11.39	28.42	0.36	6.64	10.16	70.93	0.01
SQU-US	2026-08-28 21:15:00	11.39	28.24	0.36	6.64	10.16	85.03	0.01
SQU-US	2026-08-28 21:30:00	11.41	28.50	0.36	6.63	10.14	71.82	0.01
SQU-US	2026-08-28 21:45:00	11.41	28.38	0.36	6.63	10.12	61.34	0.01
SQU-US	2026-08-28 22:00:00	11.40	27.92	0.36	6.62	10.12	83.19	0.01
SQU-US	2026-08-28 22:15:00	11.40	28.21	0.36	6.62	10.09	63.46	0.01
SQU-US	2026-08-28 22:30:00	11.40	28.36	0.36	6.61	10.08	75.04	0.01
SQU-US	2026-08-28 22:45:00	11.39	27.71	0.36	6.61	10.07	75.68	0.01
SQU-US	2026-08-28 23:00:00	11.38	26.95	0.36	6.60	10.08	66.88	0.01
SQU-US	2026-08-28 23:15:00	11.39	27.10	0.36	6.61	10.07	79.44	0.01
SQU-US	2026-08-28 23:30:00	11.38	26.16	0.36	6.61	10.10	81.87	0.01
SQU-US	2026-08-28 23:45:00	11.38	25.96	0.36	6.60	10.09	71.27	0.01
SQU-US	2026-08-29 00:00:00	11.37	26.14	0.36	6.60	10.08	66.20	0.01
SQU-US	2026-08-29 00:15:00	11.35	26.22	0.36	6.59	10.08	79.82	0.01
SQU-US	2026-08-29 00:30:00	11.34	26.15	0.36	6.59	10.08	85.42	0.01
SQU-US	2026-08-29 00:45:00	11.32	26.22	0.36	6.58	10.07	62.70	0.01
SQU-US	2026-08-29 01:00:00	11.29	26.19	0.36	6.57	10.07	75.26	0.01
SQU-US	2026-08-29 01:15:00	11.25	26.05	0.36	6.57	10.03	84.70	0.01
SQU-US	2026-08-29 01:30:00	11.22	26.00	0.37	6.57	9.96	87.81	0.01
SQU-US	2026-08-29 01:45:00	11.18	25.78	0.37	6.56	9.92	85.53	0.01
SQU-US	2026-08-29 02:00:00	11.15	25.57	0.37	6.55	9.85	96.03	0.01
SQU-US	2026-08-29 02:15:00	11.10	25.53	0.37	6.55	9.78	93.11	0.01
SQU-US	2026-08-29 02:30:00	11.05	25.22	0.37	6.55	9.68	80.07	0.01
SQU-US	2026-08-29 02:45:00	10.98	24.90	0.37	6.55	9.60	68.04	0.01
SQU-US	2026-08-29 03:00:00	10.90	24.50	0.37	6.54	9.52	78.68	0.01
SQU-US	2026-08-29 03:15:00	10.81	24.22	0.37	6.54	9.45	73.82	0.01
SQU-US	2026-08-29 03:30:00	10.76	24.70	0.37	6.54	9.34	65.15	0.01
SQU-US	2026-08-29 03:45:00	10.70	24.18	0.37	6.54	9.23	74.65	0.01
SQU-US	2026-08-29 04:00:00	10.65	23.96	0.37	6.55	9.07	114.19	0.01
SQU-US	2026-08-29 04:15:00	10.62	24.17	0.37	6.54	8.88	89.61	0.01
SQU-US	2026-08-29 04:30:00	10.58	24.19	0.37	6.54	8.65	80.84	0.01
SQU-US	2026-08-29 04:45:00	10.55	24.52	0.37	6.53	8.42	109.05	0.01
SQU-US	2026-08-29 05:00:00	10.51	24.23	0.37	6.53	8.21	187.72	0.01
SQU-US	2026-08-29 05:15:00	10.47	24.24	0.37	6.53	7.96	108.54	0.01
SQU-US	2026-08-29 05:30:00	10.44	24.79	0.37	6.53	7.67	121.92	0.01
SQU-US	2026-08-29 05:45:00	10.41	25.28	0.37	6.52	7.35	176.62	0.01

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-29 06:00:00	10.37	25.59	0.38	6.52	7.03	228.11	0.01
SQU-US	2026-08-29 06:15:00	10.34	26.40	0.38	6.52	6.73	269.60	0.01
SQU-US	2026-08-29 06:30:00	10.30	26.82	0.38	6.51	6.41	283.25	0.01
SQU-US	2026-08-29 06:45:00	10.25	27.20	0.38	6.51	6.10	296.96	0.01
SQU-US	2026-08-29 07:00:00	10.22	27.73	0.38	6.51	5.78	289.40	0.01
SQU-US	2026-08-29 07:15:00	10.18	27.70	0.38	6.50	5.46	301.11	0.01
SQU-US	2026-08-29 07:30:00	10.13	27.54	0.38	6.50	5.15	386.92	0.01
SQU-US	2026-08-29 07:45:00	10.09	27.42	0.38	6.49	4.85	358.18	0.01
SQU-US	2026-08-29 08:00:00	10.05	27.04	0.38	6.49	4.56	268.21	0.01
SQU-US	2026-08-29 08:15:00	10.02	26.78	0.38	6.49	4.28	289.21	0.01
SQU-US	2026-08-29 08:30:00	10.03	26.98	0.38	6.48	4.02	266.15	0.01
SQU-US	2026-08-29 08:45:00	10.04	27.02	0.38	6.48	3.76	217.64	0.01
SQU-US	2026-08-29 09:00:00	10.05	26.73	0.38	6.48	3.52	213.88	0.01
SQU-US	2026-08-29 09:15:00	10.07	26.69	0.38	6.47	3.29	183.89	0.01
SQU-US	2026-08-29 09:30:00	10.11	26.92	0.38	6.47	3.08	195.79	0.01
SQU-US	2026-08-29 09:45:00	10.13	26.77	0.38	6.47	2.89	163.08	0.01
SQU-US	2026-08-29 10:00:00	10.16	26.59	0.38	6.46	2.70	187.79	0.01
SQU-US	2026-08-29 10:15:00	10.20	26.77	0.38	6.46	2.55	121.90	0.01
SQU-US	2026-08-29 10:30:00	10.23	26.64	0.38	6.46	2.41	153.55	0.01
SQU-US	2026-08-29 10:45:00	10.28	26.95	0.38	6.46	2.29	131.88	0.01
SQU-US	2026-08-29 11:00:00	10.32	26.88	0.38	6.45	2.18	140.66	0.01
SQU-US	2026-08-29 11:15:00	10.37	26.71	0.38	6.45	2.09	130.78	0.01
SQU-US	2026-08-29 11:30:00	10.44	27.19	0.38	6.45	2.00	139.49	0.01
SQU-US	2026-08-29 11:45:00	10.50	27.56	0.38	6.45	1.94	141.74	0.01
SQU-US	2026-08-29 12:00:00	10.56	27.38	0.38	6.44	1.89	128.05	0.01
SQU-US	2026-08-29 12:15:00	10.62	27.63	0.39	6.44	1.86	134.71	0.01
SQU-US	2026-08-29 12:30:00	10.70	28.03	0.39	6.44	1.85	159.16	0.01
SQU-US	2026-08-29 12:45:00	10.76	28.38	0.39	6.44	1.86	140.12	0.01
SQU-US	2026-08-29 13:00:00	10.84	28.89	0.39	6.43	1.90	145.83	0.01
SQU-US	2026-08-29 13:15:00	10.90	29.13	0.39	6.43	1.97	140.09	0.01
SQU-US	2026-08-29 13:30:00	10.99	29.72	0.39	6.43	2.05	134.46	0.01
SQU-US	2026-08-29 13:45:00	11.07	30.10	0.39	6.43	2.15	122.95	0.01
SQU-US	2026-08-29 14:00:00	11.12	30.41	0.39	6.42	2.26	117.97	0.01
SQU-US	2026-08-29 14:15:00	11.20	30.99	0.39	6.42	2.38	136.91	0.01
SQU-US	2026-08-29 14:30:00	11.26	31.16	0.39	6.42	2.49	120.95	0.01
SQU-US	2026-08-29 14:45:00	11.27	31.29	0.39	6.41	2.59	102.81	0.01
SQU-US	2026-08-29 15:00:00	11.30	31.67	0.38	6.41	2.59	113.31	0.01
SQU-US	2026-08-29 15:15:00	11.28	31.97	0.38	6.41	2.46	121.35	0.01
SQU-US	2026-08-29 15:30:00	11.31	32.05	0.38	6.40	2.21	107.28	0.01
SQU-US	2026-08-29 15:45:00	11.35	32.06	0.38	6.40	1.89	124.04	0.01
SQU-US	2026-08-29 16:00:00	11.38	32.39	0.38	6.40	1.57	111.39	0.01
SQU-US	2026-08-29 16:15:00	11.38	32.52	0.38	6.40	1.31	106.48	0.01
SQU-US	2026-08-29 16:30:00	11.40	32.59	0.38	6.39	1.10	87.60	0.01
SQU-US	2026-08-29 16:45:00	11.45	32.88	0.38	6.39	0.97	102.23	0.01
SQU-US	2026-08-29 17:00:00	11.47	32.82	0.38	6.39	0.90	96.67	0.01
SQU-US	2026-08-29 17:15:00	11.45	32.82	0.38	6.39	0.89	99.38	0.01
SQU-US	2026-08-29 17:30:00	11.46	33.03	0.38	6.38	0.91	97.03	0.01
SQU-US	2026-08-29 17:45:00	11.44	32.91	0.38	6.38	0.93	102.73	0.01
SQU-US	2026-08-29 18:00:00	11.46	33.01	0.38	6.38	0.94	77.09	0.01
SQU-US	2026-08-29 18:15:00	11.46	33.33	0.38	6.38	0.92	90.42	0.01
SQU-US	2026-08-29 18:30:00	11.46	33.49	0.38	6.38	0.86	68.43	0.01
SQU-US	2026-08-29 18:45:00	11.45	33.61	0.38	6.38	0.79	81.46	0.01
SQU-US	2026-08-29 19:00:00	11.47	34.04	0.38	6.38	0.71	81.53	0.01
SQU-US	2026-08-29 19:15:00	11.49	34.47	0.38	6.37	0.62	74.31	0.02
SQU-US	2026-08-29 19:30:00	11.49	34.63	0.38	6.37	0.54	76.17	0.02
SQU-US	2026-08-29 19:45:00	11.50	35.02	0.38	6.37	0.45	68.31	0.02

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-29 20:00:00	11.49	35.29	0.38	6.37	0.38	64.48	0.02
SQU-US	2026-08-29 20:15:00	11.47	35.94	0.38	6.37	0.32	67.01	0.02
SQU-US	2026-08-29 20:30:00	11.46	36.72	0.38	6.37	0.27	69.23	0.02
SQU-US	2026-08-29 20:45:00	11.46	37.56	0.38	6.37	0.22	75.76	0.02
SQU-US	2026-08-29 21:00:00	11.46	38.29	0.38	6.36	0.19	64.54	0.02
SQU-US	2026-08-29 21:15:00	11.45	38.57	0.38	6.36	0.15	68.00	0.02
SQU-US	2026-08-29 21:30:00	11.46	39.05	0.38	6.36	0.12	58.84	0.02
SQU-US	2026-08-29 21:45:00	11.45	39.17	0.38	6.36	0.09	69.76	0.02
SQU-US	2026-08-29 22:00:00	11.45	39.30	0.38	6.36	0.07	79.52	0.02
SQU-US	2026-08-29 22:15:00	11.43	39.05	0.38	6.36	0.05	74.80	0.02
SQU-US	2026-08-29 22:30:00	11.43	39.21	0.38	6.36	0.04	71.62	0.02
SQU-US	2026-08-29 22:45:00	11.42	39.05	0.38	6.36	0.05	57.09	0.02
SQU-US	2026-08-29 23:00:00	11.41	38.95	0.38	6.35	0.07	65.71	0.02
SQU-US	2026-08-29 23:15:00	11.39	38.87	0.38	6.35	0.08	58.56	0.02
SQU-US	2026-08-29 23:30:00	11.38	38.73	0.38	6.35	0.09	76.84	0.02
SQU-US	2026-08-29 23:45:00	11.36	38.52	0.38	6.35	0.10	56.28	0.02
SQU-US	2026-08-30 00:00:00	11.34	38.10	0.38	6.35	0.11	56.39	0.02
SQU-US	2026-08-30 00:15:00	11.32	37.71	0.38	6.35	0.11	68.29	0.02
SQU-US	2026-08-30 00:30:00	11.32	37.79	0.38	6.34	0.11	64.53	0.02
SQU-US	2026-08-30 00:45:00	11.31	37.53	0.38	6.34	0.10	71.39	0.02
SQU-US	2026-08-30 01:00:00	11.30	37.33	0.38	6.34	0.09	70.25	0.02
SQU-US	2026-08-30 01:15:00	11.28	37.27	0.38	6.34	0.06	59.76	0.02
SQU-US	2026-08-30 01:30:00	11.26	37.26	0.38	6.34	0.04	71.20	0.02
SQU-US	2026-08-30 01:45:00	11.24	37.25	0.38	6.35	0.02	84.13	0.02
SQU-US	2026-08-30 02:00:00	11.21	37.21	0.38	6.35	0.00	70.03	0.02
SQU-US	2026-08-30 02:15:00	11.19	37.34	0.38	6.35	0.00	81.03	0.02
SQU-US	2026-08-30 02:30:00	11.15	37.46	0.38	6.35	0.00	79.85	0.02
SQU-US	2026-08-30 02:45:00	11.12	37.66	0.38	6.35	0.00	65.25	0.02
SQU-US	2026-08-30 03:00:00	11.09	37.83	0.38	6.35	0.00	67.96	0.02
SQU-US	2026-08-30 03:15:00	11.05	37.88	0.38	6.35	0.00	64.34	0.02
SQU-US	2026-08-30 03:30:00	11.02	37.97	0.38	6.35	0.00	63.06	0.02
SQU-US	2026-08-30 03:45:00	10.98	37.94	0.38	6.35	0.00	63.74	0.02
SQU-US	2026-08-30 04:00:00	10.95	37.86	0.38	6.35	0.00	69.37	0.02
SQU-US	2026-08-30 04:15:00	10.93	37.92	0.38	6.35	0.00	69.86	0.02
SQU-US	2026-08-30 04:30:00	10.91	37.86	0.38	6.35	0.00	68.96	0.02
SQU-US	2026-08-30 04:45:00	10.89	37.76	0.38	6.35	0.00	77.28	0.02
SQU-US	2026-08-30 05:00:00	10.87	37.71	0.38	6.36	0.00	63.47	0.02
SQU-US	2026-08-30 05:15:00	10.85	37.76	0.38	6.36	0.00	66.94	0.02
SQU-US	2026-08-30 05:30:00	10.83	37.58	0.38	6.36	0.00	60.95	0.02
SQU-US	2026-08-30 05:45:00	10.80	37.52	0.38	6.36	0.00	46.70	0.02
SQU-US	2026-08-30 06:00:00	10.79	37.52	0.38	6.36	0.00	36.99	0.02
SQU-US	2026-08-30 06:15:00	10.77	37.57	0.38	6.36	0.00	2.18	0.02
SQU-US	2026-08-30 06:30:00	10.75	37.39	0.38	6.36	0.00	0.00	0.02
SQU-US	2026-08-30 06:45:00	10.73	37.18	0.38	6.36	0.00	0.00	0.02
SQU-US	2026-08-30 07:00:00	10.71	37.17	0.38	6.35	0.00	0.00	0.02
SQU-US	2026-08-30 07:15:00	10.69	37.12	0.38	6.35	0.00	0.00	0.02
SQU-US	2026-08-30 07:30:00	10.68	37.15	0.38	6.35	0.00	0.00	0.02
SQU-US	2026-08-30 07:45:00	10.66	37.13	0.38	6.35	0.00	0.00	0.02
SQU-US	2026-08-30 08:00:00	10.65	37.22	0.38	6.35	0.00	0.00	0.02
SQU-US	2026-08-30 08:15:00	10.63	37.26	0.38	6.34	0.00	0.00	0.02
SQU-US	2026-08-30 08:30:00	10.62	37.34	0.38	6.34	0.00	0.00	0.02
SQU-US	2026-08-30 08:45:00	10.62	37.17	0.38	6.33	0.00	0.00	0.02
SQU-US	2026-08-30 09:00:00	10.62	37.08	0.38	6.33	0.00	0.00	0.02
SQU-US	2026-08-30 09:15:00	10.62	37.02	0.38	6.33	0.00	0.00	0.02
SQU-US	2026-08-30 09:30:00	10.62	36.83	0.38	6.32	0.00	0.00	0.02
SQU-US	2026-08-30 09:45:00	10.63	36.68	0.38	6.30	0.04	0.00	0.02

Squamish River								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
SQU-US	2026-08-30 10:00:00	10.65	36.59	0.38	6.27	0.17	0.00	0.02
SQU-US	2026-08-30 10:15:00	10.67	36.41	0.38	6.25	0.34	0.00	0.02
SQU-US	2026-08-30 10:30:00	10.70	36.44	0.38	6.24	0.57	0.00	0.02
SQU-US	2026-08-30 10:45:00	10.72	36.37	0.38	6.24	0.65	0.00	0.02
SQU-US	2026-08-30 11:00:00	10.74	36.29	0.38	6.25	0.77	0.00	0.02
SQU-US	2026-08-30 11:15:00	10.77	36.27	0.38	6.26	0.83	0.00	0.02
SQU-US	2026-08-30 11:30:00	10.80	36.27	0.38	6.29	0.81	0.00	0.02
SQU-US	2026-08-30 11:45:00	10.83	36.23	0.38	6.33	0.83	0.00	0.02
SQU-US	2026-08-30 12:00:00	10.87	36.19	0.38	6.35	0.94	0.00	0.02
SQU-US	2026-08-30 12:15:00	10.91	36.26	0.38	6.38	1.07	0.00	0.02
SQU-US	2026-08-30 12:30:00	10.93	36.23	0.38	6.40	1.20	0.00	0.02
SQU-US	2026-08-30 12:45:00	10.95	36.17	0.38	6.41	1.30	0.00	0.02
SQU-US	2026-08-30 13:00:00	10.98	36.28	0.38	6.42	1.37	0.00	0.02
SQU-US	2026-08-30 13:15:00	11.01	36.33	0.38	6.42	1.44	0.00	0.02
SQU-US	2026-08-30 13:30:00	11.03	36.37	0.38	6.43	1.53	0.00	0.02
SQU-US	2026-08-30 13:45:00	11.06	36.47	0.38	6.43	1.63	0.00	0.02
SQU-US	2026-08-30 14:00:00	11.08	36.60	0.38	6.43	1.73	0.00	0.02
SQU-US	2026-08-30 14:15:00	11.10	36.66	0.39	6.44	1.83	0.00	0.02
SQU-US	2026-08-30 14:30:00	11.12	36.82	0.38	6.45	1.89	0.00	0.02
SQU-US	2026-08-30 14:45:00	11.15	36.87	0.39	6.48	1.88	0.00	0.02
SQU-US	2026-08-30 15:00:00	11.17	36.90	0.39	6.50	1.87	0.00	0.02
SQU-US	2026-08-30 15:15:00	11.21	36.95	0.39	6.51	1.89	0.00	0.02
SQU-US	2026-08-30 15:30:00	11.25	37.15	0.39	6.51	1.95	0.00	0.02
SQU-US	2026-08-30 15:45:00	11.28	37.23	0.39	6.52	2.02	0.00	0.02
SQU-US	2026-08-30 16:00:00	11.31	37.28	0.39	6.52	2.11	0.00	0.02
SQU-US	2026-08-30 16:15:00	11.33	37.45	0.39	6.55	2.10	0.00	0.02
SQU-US	2026-08-30 16:30:00	11.35	37.42	0.39	6.56	2.09	0.00	0.02
SQU-US	2026-08-30 16:45:00	11.36	37.52	0.39	6.56	2.03	0.00	0.02
SQU-US	2026-08-30 17:00:00	11.38	37.59	0.39	6.57	1.99	0.00	0.02
SQU-US	2026-08-30 17:15:00	11.39	37.66	0.39	6.57	2.00	0.00	0.02
SQU-US	2026-08-30 17:30:00	11.40	37.69	0.39	6.58	2.03	0.00	0.02
SQU-US	2026-08-30 17:45:00	11.40	37.73	0.39	6.58	2.07	0.00	0.02
SQU-US	2026-08-30 18:00:00	11.40	37.80	0.39	6.58	2.12	0.00	0.02
SQU-US	2026-08-30 18:15:00	11.39	37.84	0.39	6.58	2.16	0.00	0.02
SQU-US	2026-08-30 18:30:00	11.38	37.88	0.39	6.58	2.20	0.00	0.02
SQU-US	2026-08-30 18:45:00	11.37	37.93	0.39	6.59	2.22	0.00	0.02
SQU-US	2026-08-30 19:00:00	11.36	37.94	0.39	6.59	2.24	0.00	0.02
SQU-US	2026-08-30 19:15:00	11.34	37.97	0.39	6.60	2.29	0.00	0.02
SQU-US	2026-08-30 19:30:00	11.32	38.05	0.39	6.59	2.33	0.00	0.02
SQU-US	2026-08-30 19:45:00	11.31	38.08	0.39	6.59	2.37	0.00	0.02
SQU-US	2026-08-30 20:00:00	11.30	38.13	0.39	6.59	2.41	0.00	0.02
SQU-US	2026-08-30 20:15:00	11.29	38.30	0.39	6.59	2.44	0.00	0.02
SQU-US	2026-08-30 20:30:00	11.28	38.51	0.39	6.59	2.47	0.00	0.02
SQU-US	2026-08-30 20:45:00	11.28	38.70	0.39	6.59	2.51	0.00	0.02
SQU-US	2026-08-30 21:00:00	11.29	39.03	0.39	6.59	2.57	0.00	0.02
SQU-US	2026-08-30 21:15:00	11.29	39.31	0.39	6.59	2.63	0.00	0.02
SQU-US	2026-08-30 21:30:00	11.30	39.66	0.39	6.61	2.63	0.00	0.02
SQU-US	2026-08-30 21:45:00	11.30	39.79	0.40	6.59	2.59	0.00	0.02
SQU-US	2026-08-30 22:00:00	11.30	39.90	0.40	6.59	2.48	0.00	0.02
SQU-US	2026-08-30 22:15:00	11.30	39.93	0.39	6.63	2.43	0.00	0.02
SQU-US	2026-08-30 22:30:00	11.30	39.88	0.39	6.60	2.35	0.00	0.02
SQU-US	2026-08-30 22:45:00	11.30	39.94	0.39	6.60	2.32	0.00	0.02
SQU-US	2026-08-30 23:00:00	11.29	40.16	0.39	6.65	2.24	0.00	0.02
SQU-US	2026-08-30 23:15:00	11.29	39.99	0.39	6.62	2.09	0.00	0.02
SQU-US	2026-08-30 23:30:00	11.28	39.69	0.39	6.60	1.94	0.00	0.02
SQU-US	2026-08-30 23:45:00	11.27	39.42	0.39	6.58	1.83	0.00	0.02

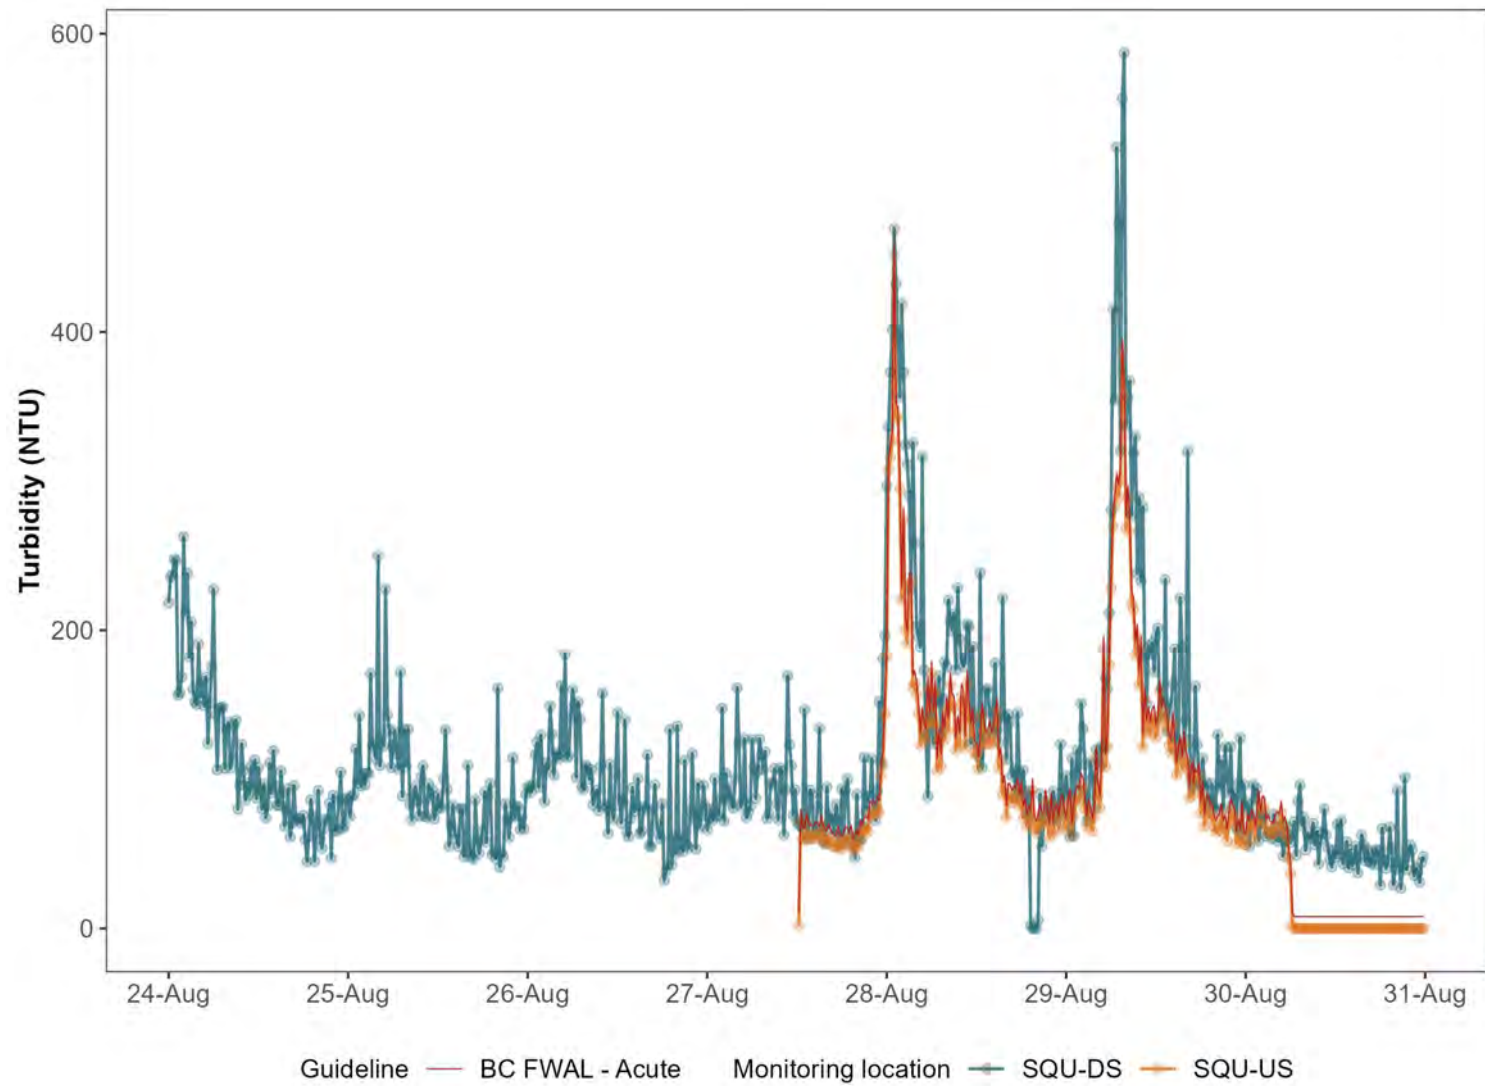

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix C	C-1

Appendix C:
Woodfibre Site Point of Discharge from Water
Treatment Plant Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix C	C-2

Woodfibre Site Sample Analysis



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
In situ Parameters									
Field pH	pH Units			6.5 - 9			7 - 8.7		7.22
Field Temperature	°C		18	19					14.6
General Parameters									
pH	pH Units								7.42
Alkalinity (Total as CaCO ₃)	mg/L								56
Alkalinity (PP as CaCO ₃)	mg/L								<1
Hardness (CaCO ₃)-Total	mg/L								68.7
Hardness (CaCO ₃)-Dissolved	mg/L								69.9
Sulphide-Total	mg/L								<0.0018
Sulphide (as H ₂ S)	mg/L				0.002				<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L								<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L								<0.0018
Anions and Nutrients									
Ammonia (N)-Total	mg/L		1.78	15.4		12	83		<0.015
Bicarbonate (HCO ₃)	mg/L								68
Carbonate (CO ₃)	mg/L								<1
Hydroxide (OH)	mg/L								<1
Nitrate (N)	mg/L		3	32.8		3.7			<0.02
Nitrite (N)	mg/L		0.2	0.6					<0.005
Nitrate plus Nitrite (N)	mg/L								<0.02
Nitrogen (N)-Total	mg/L								0.185
Phosphorus (P)-Total (4500-P)	mg/L								0.0019
Bromide (Br)	mg/L								<0.01
Chloride (Cl)	mg/L		150	600					17
Fluoride (F)	mg/L			1.183171			1.5		0.35
Sulphate (SO ₄)-Dissolved	mg/L		218						15
Total Metals									
Aluminum (Al)-Total	mg/L		0.0564311						0.0381
Antimony (Sb)-Total	mg/L		0.074	0.25					0.000735
Arsenic (As)-Total	mg/L		0.005			0.0125			0.000997
Barium (Ba)-Total	mg/L				1				0.00414
Beryllium (Be)-Total	mg/L				0.00013			0.1	<0.00001
Bismuth (Bi)-Total	mg/L								<0.000005
Boron (B)-Total	mg/L		1.2			1.2			0.011
Cadmium (Cd)-Total	mg/L							0.00012	<0.000005
Calcium (Ca)-Total	mg/L								25.3
Cesium (Cs)-Total	mg/L								<0.00005
Chromium (Cr)-Total	mg/L								<0.0001
Chromium (Cr III)-Total	mg/L				0.0089			0.056	<0.00099

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
Total Metals (Cont'd.)									
Chromium (Cr VI)-Total	mg/L				0.0025			0.0015	<0.00099
Cobalt (Co)-Total	mg/L								0.000029
Copper (Cu)-Total	mg/L					0.002	0.003		<0.00005
Iron (Fe)-Total	mg/L		0.05	1					0.0098
Lead (Pb)-Total	mg/L					0.002	0.14		0.0000051
Lithium (Li)-Total	mg/L								0.00729
Magnesium (Mg)-Total	mg/L								1.37
Manganese (Mn)-Total	mg/L							0.1	0.0253
Mercury (Hg)-Total	mg/L		0.00002			0.0001			<0.0000019
Molybdenum (Mo)-Total	mg/L		7.6	46					0.0485
Nickel (Ni)-Total	mg/L							0.0083	0.000155
Phosphorus (P)-Total (ICPMS)	mg/L								<0.002
Potassium (K)-Total	mg/L								1.75
Rubidium (Rb)-Total	mg/L								0.00381
Selenium (Se)-Total	mg/L		0.002			0.002			0.000046
Silicon (Si)-Total	mg/L								6.65
Silver (Ag)-Total	mg/L		0.00012			0.0005	0.0037	0.0005	<0.000005
Sodium (Na)-Total	mg/L								8.8
Strontium (Sr)-Total	mg/L								0.0516
Sulphur (S)-Total	mg/L								4.9
Tellurium (Te)-Total	mg/L								<0.00002
Thallium (Tl)-Total	mg/L				0.00003				0.0000077
Thorium (Th)-Total	mg/L								<0.00005
Tin (Sn)-Total	mg/L								<0.0002
Titanium (Ti)-Total	mg/L								<0.0005
Uranium (U)-Total	mg/L			0.0165	0.0075				0.000281
Vanadium (V)-Total	mg/L				0.06			0.005	<0.0002
Zinc (Zn)-Total	mg/L					0.01	0.055		0.00283
Zirconium (Zr)-Total	mg/L								<0.0001
Dissolved Metals									
Aluminum (Al)-Dissolved	mg/L								0.0267
Antimony (Sb)-Dissolved	mg/L								0.00072
Arsenic (As)-Dissolved	mg/L								0.00101
Barium (Ba)-Dissolved	mg/L								0.00421
Beryllium (Be)-Dissolved	mg/L								<0.00001
Bismuth (Bi)-Dissolved	mg/L								<0.000005
Boron (B)-Dissolved	mg/L								0.014
Cadmium (Cd)-Dissolved	mg/L		0.0001604	0.0003996					<0.000005
Calcium (Ca)-Dissolved	mg/L								25.6

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
Dissolved Metals (Cont'd.)									
Cesium (Cs)-Dissolved	mg/L								<0.00005
Chromium (Cr)-Dissolved	mg/L								<0.0001
Cobalt (Co)-Dissolved	mg/L		0.0004365						0.000027
Copper (Cu)-Dissolved	mg/L	0.00366							0.000058
Iron (Fe)-Dissolved	mg/L								<0.001
Lead (Pb)-Dissolved	mg/L		0.0015788						<0.000005
Lithium (Li)-Dissolved	mg/L								0.00826
Manganese (Mn)-Dissolved	mg/L		0.245	2.393645					0.0245
Magnesium (Mg)-Dissolved	mg/L								1.44
Mercury (Hg)-Dissolved	mg/L								<0.0000019
Molybdenum (Mo)-Dissolved	mg/L								0.0482
Nickel (Ni)-Dissolved	mg/L		0.0012	0.0217					0.000173
Phosphorus (P)-Dissolved	mg/L								0.0032
Potassium (K)-Dissolved	mg/L								1.7
Rubidium (Rb)-Dissolved	mg/L								0.00389
Selenium (Se)-Dissolved	mg/L								<0.00004
Silicon (Si)-Dissolved	mg/L								6.8
Silver (Ag)-Dissolved	mg/L								<0.000005
Sodium (Na)-Dissolved	mg/L								9.27
Strontium (Sr)-Dissolved	mg/L				1.25				0.0537
Sulphur (S)-Dissolved	mg/L								5.2
Tellurium (Te)-Dissolved	mg/L								<0.00002
Thallium (Tl)-Dissolved	mg/L								0.0000085
Thorium (Th)-Dissolved	mg/L								<0.000005
Tin (Sn)-Dissolved	mg/L								<0.0002
Titanium (Ti)-Dissolved	mg/L								<0.0005
Uranium (U)-Dissolved	mg/L								0.000254
Vanadium (V)-Dissolved	mg/L								<0.0002
Zinc (Zn)-Dissolved	mg/L		0.0067224	0.0262372					0.00277
Zirconium (Zr)-Dissolved	mg/L								<0.0001
Inorganics									
Organic Carbon (C)-Total	mg/L								0.66
Organic Carbon (C)-Dissolved	mg/L								0.69
Solids-Total Dissolved	mg/L								64
Solids-Total Suspended	mg/L		6	26					1.6
Organics									
HEPH (C19-C32 less PAH)	mg/L								<0.2
LEPH (C10-C19 less PAH)	mg/L								<0.2
EPH (C10-C19)	mg/L								<0.2

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
Organics (Cont'd.)									
EPH (C19-C32)	mg/L								<0.2
Ethylene Glycol	mg/L								<3
Diethylene Glycol	mg/L								<5
Triethylene Glycol	mg/L								<5
Propylene Glycol	mg/L								<5
Acenaphthene	mg/L		0.006			0.006			<0.00005
Acenaphthylene	mg/L								<0.00005
Acridine	mg/L		0.003						<0.00005
Anthracene	mg/L		0.004						<0.00001
Benzo(a)anthracene	mg/L		0.0001						<0.00001
Benzo(a)pyrene	mg/L		0.00001			0.00001			<0.000005
Benzo(b&j)fluoranthene	mg/L								<0.00003
Benzo(g,h,i)perylene	mg/L								<0.00005
Benzo(k)fluoranthene	mg/L								<0.00005
Chrysene	mg/L					0.0001			<0.00002
Dibenz(a,h)anthracene	mg/L								<0.000003
Fluoranthene	mg/L		0.004						<0.00002
Fluorene	mg/L		0.012			0.012			<0.00005
Indeno(1,2,3-cd)pyrene	mg/L								<0.00005
1-Methylnaphthalene	mg/L					0.001			<0.00005
2-Methylnaphthalene	mg/L					0.001			<0.0001
Naphthalene	mg/L		0.001	0.001		0.001			<0.0001
Phenanthrene	mg/L		0.0003						<0.00005
Pyrene	mg/L								<0.00002
Quinoline	mg/L								<0.00002
Low Molecular Weight PAH's	mg/L								<0.0001
High Molecular Weight PAH's	mg/L								<0.00005
Total PAH	mg/L								<0.0001
VH C6-C10	mg/L								<0.3
1,1,1,2-Tetrachloroethane	mg/L								<0.0005
1,1,1-Trichloroethane	mg/L								<0.0005
1,1,2,2-Tetrachloroethane	mg/L								<0.0005
1,1,2Trichloro-1,2,2Trifluoroethane	mg/L								<0.002
1,1,2-Trichloroethane	mg/L								<0.0005
1,1-Dichloroethane	mg/L								<0.0005
1,1-Dichloroethene	mg/L								<0.0005
1,2,3-trichlorobenzene	mg/L				0.008				<0.002
1,2,4-trichlorobenzene	mg/L				0.024			0.0054	<0.002
1,2-dibromoethane	mg/L								<0.0002

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
Organics (Cont'd.)									
1,2-Dichlorobenzene	mg/L				0.0007			0.042	<0.0005
1,2-Dichloroethane	mg/L				0.1				<0.0005
1,2-Dichloropropane	mg/L								<0.0005
1,3,5-trimethylbenzene	mg/L								<0.002
1,3-Butadiene	mg/L								<0.0005
1,3-Dichlorobenzene	mg/L				0.15				<0.0005
1,3-dichloropropane	mg/L								<0.001
1,4-Dichlorobenzene	mg/L				0.026				<0.0005
Benzene	mg/L		0.04			0.11			<0.0004
Bromobenzene	mg/L								<0.002
Bromodichloromethane	mg/L								<0.001
Bromoform	mg/L								<0.001
Bromomethane	mg/L								<0.001
Carbon tetrachloride	mg/L								<0.0005
Chlorobenzene	mg/L				0.0013			0.025	<0.0005
Chloroethane	mg/L								<0.001
Chloroform	mg/L								<0.001
Chloromethane	mg/L								<0.001
cis-1,2-Dichloroethene	mg/L								<0.001
cis-1,3-Dichloropropene	mg/L								<0.001
Dibromochloromethane	mg/L								<0.001
Dichlorodifluoromethane	mg/L								<0.002
Dichloromethane	mg/L				0.0981				<0.002
Ethylbenzene	mg/L		0.2			0.25			<0.0004
Hexachlorobutadiene	mg/L								<0.0005
Isopropylbenzene	mg/L								<0.002
Methyl-tert-butylether (MTBE)	mg/L			3.4			0.44		<0.004
Styrene	mg/L				0.072				<0.0005
Tetrachloroethene	mg/L								<0.0005
Toluene	mg/L		0.0005						<0.0004
trans-1,2-dichloroethene	mg/L								<0.001
trans-1,3-dichloropropene	mg/L								<0.001
Trichloroethene	mg/L								<0.0005
Trichlorofluoromethane	mg/L								<0.004
Vinyl chloride	mg/L								<0.0005
VPH (VH6 to 10 - BTEX)	mg/L								<0.3
Xylenes (Total)	mg/L		0.03						<0.0004
m & p-Xylene	mg/L								<0.0004
o-Xylene	mg/L								<0.0004
Phenols	mg/L			0.05					<0.0015

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

Analyte	Unit	Permit PE-110163 Discharge Limit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG EOP 2026-08-25 08:25:00
Acute Toxicity									
Rainbow Trout LC50	% vol/vol								>100%
Daphnia Magna LC50	% vol/vol								>100%

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix C	C-3

Woodfibre Site WTP Discharge Field Notes and Logs

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	<u>WLNG EOP</u>		Date:	<u>August 25, 2026</u>	
Site Name:	<u>East Creek</u>		Time:	<u>8:25</u>	
Site UTM:	Zone: 10U	E: <u>482030</u>	Crew:	<u>BG</u>	
(NAD83)		N: <u>5501931</u>	Weather:	<u>20°C, Clear skies</u>	

In Situ Parameters

pH:	<u>7.22</u>	DO:	<u>8.67</u>	(mg/L)
Temp:	<u>14.6</u>	Cond:	<u>268.6</u>	(us/cm)
Turbidity:	<u>3.16</u>	Salinity:	<u>0.1</u>	(ppt)
Visible Sheen:	<u>No</u>	ORP:	<u>61.1</u>	(mV)
Water Surface Condition:	<u>Clear</u>			

Photo Record



Observations

No notable observations.

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Table of Contents:

1. Executive Summary and Field Notes
2. Daily Volume Summary
3. Portal Discharge Parameter Summary
4. CP2 Discharge Parameter Summary
5. In-situ Readings
6. WTP Calibration Log

Appendices:

- Appendix A- Portal WTP Data Log
- Appendix B- CP2 WTP Data Log
- Appendix C- Photos

1. Executive Summary and Field Notes:

Parameters, including temperature, NTU, pH, DO, salinity, conductivity, and oxidation-reduction potential (ORP), were monitored throughout the reporting period.

On Aug 24th at 17:15 a temperature of 19.2°C was recorded on the Check Point 2 Water Treatment Plant (CP2 WTP) data log. The reading was recorded when there was low discharge flow rate which meant the discharge pump was off at the time, minimal water was syphoning past the flow meter and no water was flowing past the temperature sensor. When the pump turned on and the discharge water contacted the temperature sensor the actual water temperature was 15.4°C.

On Aug 27th at 21:45 a reading of 779 NTU was recorded on the CP2 WTP data log when there was low flow and water was not contacting the NTU probe. The discharged water was between 0-1 NTU.

There were a few elevated NTU values recorded on the Portal Water Treatment Plant (PWTP) data logs. The values were recorded when the discharge pump turned on and the NTU meter was stabilizing due to air and water passing the probe. Once a steady flow of water passed the probe and the readings stabilized the NTU values were generally <10 NTU. A reading of 401 NTU was recorded on Aug 30th at 19:45 while the probe was being calibrated.

Between Aug 24th and 30th there were 30 conductivity readings of 0 uS/cm and some misreadings recorded on the CP2 WTP data logs. These readings were recorded during low

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

flows and water was not contacting the conductivity probe. Discharge conductivity was ~230 uS/cm.

No visible sheen was observed on the surface of the PWTP and CP2 WTP tanks or in the discharged water. All relevant parameters were measured using YSI instruments, Hanna NTU meters and WTP NTU, pH, conductivity and temperature probes.

CP2 WTP received ~291 GPM (1.10 m³/min) and the PWTP received ~188 GPM (0.71 m³/min) from the tunnel.

The total discharge volume up to August 30th was 1,743,427 m³.

2. Daily Volume Summary:

Table 1: Discharge Volumes Daily Summary

Date	Location	Volume (m3)	Comments
August 24	Woodfibre (WF)	2,595	None
August 25	WF	2,626	None
August 26	WF	2,661	None
August 27	WF	2,600	None
August 28	WF	2,601	None
August 29	WF	2,590	None
August 30	WF	2,604	None
Total		18,277	None

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

3. Discharge Parameter Summary:

Table 2: Portal Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	0:00:00	7.4	1.1924	5.7	1,455,950	15.7	279
8/24/2026	0:30:00	7.4	1.2189	36.3	1,455,958	17.5	283
8/24/2026	0:45:00	7.4	1.7602	2.3	1,455,982	16.1	281
8/24/2026	1:00:00	7.4	1.2151	7.2	1,456,007	16.2	281
8/24/2026	1:30:00	7.4	1.2227	4	1,456,021	16.2	279
8/24/2026	1:45:00	7.4	1.7261	3.9	1,456,044	16	282
8/24/2026	2:15:00	7.4	1.6732	3.1	1,456,060	16.7	286
8/24/2026	2:30:00	7.4	1.1508	8.1	1,456,083	15.9	283
8/24/2026	2:45:00	7.4	1.6277	3.9	1,456,106	15.8	285
8/24/2026	3:15:00	7.4	1.6694	3.9	1,456,116	15.9	285
8/24/2026	3:30:00	7.4	1.1394	7.2	1,456,139	15.7	287
8/24/2026	4:15:00	7.4	1.6467	4.8	1,456,173	15.5	287
8/24/2026	5:00:00	7.4	1.1356	6	1,456,201	15.9	288
8/24/2026	5:15:00	7.5	1.6391	4.3	1,456,223	16	286
8/24/2026	6:00:00	7.5	1.1167	7.8	1,456,262	15.9	285
8/24/2026	6:15:00	7.5	1.6391	4.3	1,456,285	15.9	286
8/24/2026	6:45:00	7.5	1.6618	4.6	1,456,301	16.6	283
8/24/2026	7:00:00	7.5	1.1129	7.2	1,456,323	16.5	284
8/24/2026	7:15:00	7.5	1.6126	5.1	1,456,346	16.5	281
8/24/2026	7:45:00	7.5	1.6391	6.3	1,456,364	16.3	286
8/24/2026	8:00:00	7.5	1.6769	5.9	1,456,384	15.9	288
8/24/2026	8:15:00	7.5	1.6618	4.3	1,456,409	15.8	288
8/24/2026	8:45:00	7.5	1.6732	4.1	1,456,421	16.1	288
8/24/2026	9:00:00	7.5	1.6732	4.9	1,456,440	15.9	288
8/24/2026	9:15:00	7.5	1.5785	4.8	1,456,465	15.9	288
8/24/2026	10:30:00	7.5	1.5482	2.8	1,456,502	16.2	290
8/24/2026	10:45:00	7.5	1.5482	2.2	1,456,525	16.4	290
8/24/2026	11:30:00	7.4	1.5709	1.3	1,456,551	16.9	292



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	11:45:00	7.4	1.5596	1.5	1,456,575	17	295
8/24/2026	12:00:00	7.4	1.5407	1.5	1,456,592	17.2	299
8/24/2026	12:15:00	7.4	1.5142	1.8	1,456,615	17.3	299
8/24/2026	12:30:00	7.5	1.4839	1.8	1,456,633	17.4	298
8/24/2026	12:45:00	7.5	1.4687	2.4	1,456,655	17.3	296
8/24/2026	13:15:00	7.5	1.5066	3.3	1,456,670	17.4	293
8/24/2026	13:30:00	7.5	1.4650	3.6	1,456,688	17.4	294
8/24/2026	13:45:00	7.5	1.4347	3.2	1,456,709	17.4	292
8/24/2026	14:15:00	7.5	1.4347	2	1,456,729	17.4	293
8/24/2026	14:30:00	7.5	1.4233	6.4	1,456,746	17.3	294
8/24/2026	14:45:00	7.5	1.4120	1.9	1,456,767	17.3	293
8/24/2026	15:00:00	7.5	1.3930	3.7	1,456,785	17.4	293
8/24/2026	15:15:00	7.5	1.4915	2.8	1,456,807	17.5	293
8/24/2026	15:45:00	7.5	1.4801	2.1	1,456,819	18.1	294
8/24/2026	16:00:00	7.5	1.4877	2.3	1,456,837	17.8	293
8/24/2026	16:15:00	7.5	1.4801	3.2	1,456,860	17.7	293
8/24/2026	17:00:00	7.5	1.4801	2.4	1,456,886	18	293
8/24/2026	17:15:00	7.5	1.2870	1.6	1,456,908	17.8	295
8/24/2026	17:30:00	7.5	1.4498	2.3	1,456,926	17.9	293
8/24/2026	17:45:00	7.5	1.0183	2.9	1,456,948	17.7	293
8/24/2026	18:00:00	7.5	1.5634	4.3	1,456,966	17.6	293
8/24/2026	18:45:00	7.5	1.0826	17	1,457,005	17.5	292
8/24/2026	19:15:00	7.5	0.9918	5	1,457,028	17.5	291
8/24/2026	19:45:00	7.5	1.1886	3.8	1,457,042	17.2	290
8/24/2026	20:15:00	7.4	1.2038	3.2	1,457,062	16.8	290
8/24/2026	20:45:00	7.4	1.2946	2.4	1,457,084	16.7	290
8/24/2026	21:00:00	7.4	1.6542	2.6	1,457,105	16.5	288
8/24/2026	21:30:00	7.4	1.6883	2.9	1,457,122	16.4	289
8/24/2026	21:45:00	7.5	1.6542	3	1,457,147	16.3	290
8/24/2026	22:30:00	7.5	1.6656	5.4	1,457,177	16.4	290
8/24/2026	22:45:00	7.5	1.6315	2.2	1,457,202	16.2	290
8/24/2026	23:15:00	7.5	1.6504	2.8	1,457,216	16.5	291



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	23:30:00	7.5	1.6429	2.6	1,457,240	15.9	288
8/25/2026	0:15:00	7.5	1.6618	3.2	1,457,275	15.8	286
8/25/2026	0:30:00	7.5	1.6429	2.7	1,457,300	15.7	286
8/25/2026	1:15:00	7.5	1.1924	1.7	1,457,337	15.7	286
8/25/2026	2:00:00	7.5	1.6694	1.5	1,457,374	15.9	288
8/25/2026	2:15:00	7.5	1.6353	1.8	1,457,399	15.9	288
8/25/2026	3:30:00	7.5	1.6050	1	1,457,434	15.7	289
8/25/2026	3:45:00	7.5	1.5861	0.4	1,457,458	15.6	290
8/25/2026	4:15:00	7.5	1.6050	0.3	1,457,470	15.8	292
8/25/2026	4:30:00	7.5	1.5974	0.5	1,457,490	15.7	293
8/25/2026	4:45:00	7.5	1.5407	0.8	1,457,514	15.7	293
8/25/2026	5:00:00	7.5	1.4801	0.8	1,457,537	15.7	295
8/25/2026	5:30:00	7.5	1.4990	0.5	1,457,550	16	294
8/25/2026	5:45:00	7.5	1.4536	0.1	1,457,572	15.9	294
8/25/2026	6:30:00	7.5	1.0183	0.6	1,457,602	15.8	293
8/25/2026	6:45:00	7.5	1.4612	0.6	1,457,623	15.7	291
8/25/2026	7:00:00	7.5	1.0031	1.7	1,457,643	15.8	291
8/25/2026	7:30:00	7.5	1.0069	1.3	1,457,651	16	293
8/25/2026	7:45:00	7.5	1.4763	1.1	1,457,671	15.8	293
8/25/2026	8:00:00	7.5	0.7230	1.6	1,457,692	15.7	294
8/25/2026	8:15:00	7.5	1.3514	1.5	1,457,708	15.6	294
8/25/2026	8:30:00	7.5	0.9577	1.7	1,457,728	15.6	298
8/25/2026	9:00:00	7.5	0.9539	1.8	1,457,740	15.7	299
8/25/2026	9:15:00	7.5	1.4612	2.5	1,457,758	15.6	299
8/25/2026	9:30:00	7.5	1.4498	2.9	1,457,780	15.7	300
8/25/2026	10:15:00	7.4	1.4460	1.6	1,457,804	15.9	303
8/25/2026	10:30:00	7.4	1.4650	1.9	1,457,826	15.9	303
8/25/2026	10:45:00	7.4	1.4574	2.2	1,457,844	16.1	304
8/25/2026	11:00:00	7.5	1.4498	3.4	1,457,865	16.1	304
8/25/2026	11:15:00	7.5	0.3028	15.1	1,457,880	16.2	304
8/25/2026	11:45:00	7.5	1.5407	5.1	1,457,895	16.6	306
8/25/2026	12:00:00	7.5	1.6012	6.4	1,457,919	16.4	304



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	12:15:00	7.5	1.5861	7.9	1,457,939	16.5	308
8/25/2026	12:30:00	7.5	1.5255	3.7	1,457,955	16.6	306
8/25/2026	13:00:00	7.5	1.5672	4.3	1,457,971	16.9	303
8/25/2026	13:15:00	7.5	1.5407	2.1	1,457,994	16.9	304
8/25/2026	14:30:00	7.5	1.5331	1.8	1,458,041	17.5	309
8/25/2026	14:45:00	7.5	1.5142	1.1	1,458,064	17.4	309
8/25/2026	15:00:00	7.5	1.0107	1.1	1,458,082	17.5	310
8/25/2026	15:30:00	7.5	1.0069	1.3	1,458,099	17.7	313
8/25/2026	15:45:00	7.5	1.5142	1.3	1,458,110	17.6	311
8/25/2026	16:00:00	7.5	0.9880	5.1	1,458,125	17.9	312
8/25/2026	16:15:00	7.5	1.4915	1.2	1,458,147	17.6	311
8/25/2026	16:30:00	7.4	0.9388	1.9	1,458,166	17.6	317
8/25/2026	16:45:00	7.4	1.4460	0.9	1,458,186	17.5	317
8/25/2026	17:30:00	7.4	0.9085	0.9	1,458,208	17.8	320
8/25/2026	18:00:00	7.3	0.9766	2.7	1,458,232	17.3	324
8/25/2026	18:15:00	7.3	1.4233	1	1,458,251	17.2	325
8/25/2026	20:00:00	7.2	1.7678	3.3	1,458,293	16.8	324
8/25/2026	20:15:00	7.3	1.6315	2	1,458,316	16.8	324
8/25/2026	21:00:00	7.2	1.6656	2.2	1,458,325	17.2	323
8/25/2026	21:15:00	7.3	1.6315	1.2	1,458,349	16.7	323
8/25/2026	22:00:00	7.3	1.6239	0.3	1,458,370	16.8	323
8/25/2026	23:00:00	7.2	1.6618	0.3	1,458,392	18	319
8/25/2026	23:15:00	7.3	1.6126	0.6	1,458,417	17.1	319
8/26/2026	0:45:00	7.3	1.6239	0	1,458,430	18	315
8/26/2026	1:00:00	7.3	1.5066	1.1	1,458,453	17.4	317
8/26/2026	2:00:00	7.2	1.5407	3	1,458,466	17.1	318
8/26/2026	3:00:00	7.1	1.5217	1.4	1,458,505	16.4	322
8/26/2026	4:00:00	7.1	1.5520	1.3	1,458,524	17.5	327
8/26/2026	4:15:00	7.1	1.4687	2.4	1,458,546	16.2	322
8/26/2026	5:00:00	7.1	1.0334	8.7	1,458,565	16.3	327
8/26/2026	5:15:00	7.1	1.4801	4.5	1,458,586	15.9	327
8/26/2026	6:15:00	7	1.4498	1.8	1,458,616	15.6	324



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	6:30:00	7	0.9842	3.8	1,458,637	15.5	324
8/26/2026	7:15:00	7	1.4385	5	1,458,656	15.4	324
8/26/2026	7:30:00	7	1.4347	6.1	1,458,677	15.2	324
8/26/2026	8:00:00	7	1.4687	4.5	1,458,686	15.5	324
8/26/2026	8:15:00	7	1.4460	3.4	1,458,704	15.2	324
8/26/2026	8:30:00	7	1.4309	4.4	1,458,725	15.2	324
8/26/2026	9:00:00	7	0.7798	5.2	1,458,735	15.5	324
8/26/2026	9:15:00	7	1.4536	6.1	1,458,752	15.3	324
8/26/2026	9:30:00	7.1	0.9691	12.5	1,458,774	15.4	324
8/26/2026	10:00:00	7.1	1.4536	5.9	1,458,789	15.8	325
8/26/2026	10:15:00	7.1	1.4460	10.3	1,458,807	15.8	325
8/26/2026	10:30:00	7.1	1.4309	3.9	1,458,829	15.9	326
8/26/2026	10:45:00	7.1	1.5104	5.1	1,458,847	16	325
8/26/2026	11:30:00	7.2	1.5331	14.2	1,458,883	16.3	323
8/26/2026	11:45:00	7.2	1.4877	3	1,458,902	16.3	323
8/26/2026	12:00:00	7.2	1.4763	0.9	1,458,925	16.4	323
8/26/2026	12:30:00	7.2	1.5104	1.3	1,458,936	16.8	320
8/26/2026	12:45:00	7.2	1.4877	1.8	1,458,954	16.7	321
8/26/2026	13:30:00	7.2	1.4725	1.5	1,458,974	17.1	321
8/26/2026	13:45:00	7.2	0.9842	3	1,458,992	17.2	321
8/26/2026	14:00:00	7.2	1.4271	1.3	1,459,013	17	319
8/26/2026	14:15:00	7.2	0.9426	1.7	1,459,032	17	318
8/26/2026	14:30:00	7.2	1.3703	3.6	1,459,052	16.9	319
8/26/2026	15:00:00	7.2	1.4006	3.9	1,459,064	17.6	319
8/26/2026	15:15:00	7.2	0.8858	10.8	1,459,079	17.2	319
8/26/2026	15:30:00	7.2	1.5142	4.2	1,459,098	17.3	316
8/26/2026	15:45:00	7.2	0.9956	3.4	1,459,119	17.4	316
8/26/2026	16:30:00	7.2	1.4801	5.2	1,459,139	17.5	313
8/26/2026	16:45:00	7.2	1.0107	5.9	1,459,158	17.5	313
8/26/2026	17:00:00	7.2	1.4536	4.7	1,459,177	17.4	313
8/26/2026	17:15:00	7.2	0.9691	4.8	1,459,199	17.3	313
8/26/2026	17:45:00	7.2	1.4347	5.6	1,459,216	17.4	311



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	18:00:00	7.2	1.4157	5.2	1,459,233	17.2	311
8/26/2026	18:15:00	7.2	1.3779	4.7	1,459,254	17.1	308
8/26/2026	18:30:00	7.2	1.3817	5.3	1,459,271	17.1	308
8/26/2026	18:45:00	7.2	1.3627	6.1	1,459,292	17	305
8/26/2026	20:15:00	7.2	1.3287	20.5	1,459,300	16.8	301
8/26/2026	20:30:00	7.2	1.5709	4.7	1,459,321	16.3	303
8/26/2026	20:45:00	7.2	1.5672	1.8	1,459,344	16.2	301
8/26/2026	21:45:00	7.2	1.5558	0.6	1,459,369	15.7	289
8/26/2026	22:30:00	7.2	1.5823	0.5	1,459,397	15.6	288
8/26/2026	22:45:00	7.2	1.5596	0.7	1,459,418	15.6	291
8/26/2026	23:00:00	7.2	1.5596	0.5	1,459,441	15.5	291
8/26/2026	23:30:00	7.2	1.2038	0.6	1,459,447	15.8	294
8/26/2026	23:45:00	7.2	1.5407	0.9	1,459,470	15.5	291
8/27/2026	0:15:00	7.2	1.5596	0.9	1,459,482	15.5	288
8/27/2026	0:30:00	7.2	1.5482	1.2	1,459,505	15.4	286
8/27/2026	1:30:00	7.2	1.5785	1	1,459,526	15.4	286
8/27/2026	1:45:00	7.2	1.5596	1.1	1,459,550	15.2	286
8/27/2026	2:45:00	7.2	1.7754	6.3	1,459,562	15.6	283
8/27/2026	3:00:00	7.2	1.7602	1.5	1,459,588	15	294
8/27/2026	3:45:00	7.2	1.7602	1.5	1,459,614	15.3	298
8/27/2026	4:30:00	7.2	1.6883	4.7	1,459,644	15.1	286
8/27/2026	4:45:00	7.2	1.6277	4.7	1,459,669	15.1	289
8/27/2026	5:15:00	7.2	1.6126	3	1,459,700	15	288
8/27/2026	5:30:00	7.1	1.6504	3.4	1,459,709	15	289
8/27/2026	5:45:00	7.1	1.6050	3.8	1,459,733	14.8	289
8/27/2026	6:00:00	7.1	1.5293	5.7	1,459,757	14.8	296
8/27/2026	6:45:00	7.1	1.6126	5.9	1,459,777	14.8	293
8/27/2026	7:30:00	7.1	1.6353	6.1	1,459,804	14.8	298
8/27/2026	7:45:00	7.1	1.1394	10.8	1,459,826	14.7	299
8/27/2026	8:15:00	7.1	1.6845	6.5	1,459,841	14.7	299
8/27/2026	8:30:00	7.1	1.1470	14.4	1,459,864	14.6	301
8/27/2026	9:00:00	7.1	1.6959	8.4	1,459,886	14.8	299



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	9:15:00	7.1	1.1129	18.8	1,459,909	14.9	313
8/27/2026	9:30:00	7.1	1.6580	7.6	1,459,931	14.9	298
8/27/2026	9:45:00	7.1	1.6202	8.9	1,459,955	14.9	304
8/27/2026	10:15:00	7.2	1.7489	20.8	1,459,975	15.4	306
8/27/2026	10:30:00	7.2	1.4877	8	1,459,996	15.1	313
8/27/2026	10:45:00	7.2	0.7003	11.2	1,460,015	15.1	313
8/27/2026	11:15:00	7.2	1.4877	11.4	1,460,040	15.2	313
8/27/2026	11:30:00	7.2	0.9653	8.1	1,460,060	15.2	313
8/27/2026	11:45:00	7.2	1.4650	5.6	1,460,081	15.2	311
8/27/2026	12:30:00	7.2	1.4763	2.2	1,460,119	15.3	313
8/27/2026	12:45:00	7.2	1.4498	3.7	1,460,141	15.2	313
8/27/2026	13:15:00	7.2	1.4763	5.3	1,460,157	15.4	316
8/27/2026	13:30:00	7.2	1.4612	2.2	1,460,179	15.4	316
8/27/2026	14:00:00	7.2	1.4687	5.1	1,460,203	15.5	318
8/27/2026	14:15:00	7.2	1.4460	3.5	1,460,224	15.5	318
8/27/2026	15:00:00	7.2	1.4612	4.2	1,460,260	15.6	321
8/27/2026	15:30:00	7.2	1.4801	6.9	1,460,281	15.7	323
8/27/2026	16:15:00	7.2	1.4915	5.6	1,460,314	15.7	324
8/27/2026	16:30:00	7.2	1.4763	5.1	1,460,336	15.7	321
8/27/2026	16:45:00	7.2	0.9577	7.8	1,460,355	15.7	319
8/27/2026	17:00:00	7.2	1.4650	5	1,460,360	15.8	318
8/27/2026	17:15:00	7.2	1.4877	9	1,460,382	15.7	316
8/27/2026	17:30:00	7.2	0.6170	17.6	1,460,401	15.6	314
8/27/2026	17:45:00	7.2	1.5444	12.2	1,460,421	15.6	314
8/27/2026	18:00:00	7.2	1.4915	17	1,460,443	15.5	314
8/27/2026	18:15:00	7.2	0.8517	9	1,460,462	15.5	314
8/27/2026	18:30:00	7.2	1.3287	14.9	1,460,464	15.8	313
8/27/2026	18:45:00	7.2	1.2984	6.4	1,460,483	15.4	313
8/27/2026	19:00:00	7.2	0.8744	8.1	1,460,501	15.3	313
8/27/2026	20:00:00	7.2	1.7413	2.7	1,460,516	15.3	313
8/27/2026	20:30:00	7.2	1.6769	1.9	1,460,567	15	313
8/27/2026	21:00:00	7.2	1.7375	1.1	1,460,588	15.3	312



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	21:15:00	7.2	1.5672	0.6	1,460,612	15.4	309
8/27/2026	21:30:00	7.2	1.6164	3.6	1,460,619	15.7	309
8/27/2026	21:45:00	7.2	1.1886	1.5	1,460,638	15.4	310
8/27/2026	22:00:00	7.2	1.6088	4.5	1,460,661	15.3	313
8/27/2026	22:30:00	7.1	1.6088	3.7	1,460,684	15.6	316
8/27/2026	22:45:00	7.1	1.5974	3.1	1,460,708	15.4	313
8/27/2026	23:15:00	7.2	1.3098	4.8	1,460,724	15.4	312
8/27/2026	23:30:00	7.2	1.3287	35.9	1,460,733	15.6	313
8/27/2026	23:45:00	7.2	1.4271	0.8	1,460,754	15.3	309
8/28/2026	0:00:00	7.2	1.3855	0.5	1,460,775	15.2	309
8/28/2026	0:30:00	7.1	1.0864	0.7	1,460,793	15.3	311
8/28/2026	0:45:00	7.1	1.4309	0.8	1,460,796	15.3	313
8/28/2026	1:00:00	7.2	1.4195	1	1,460,817	15	313
8/28/2026	1:15:00	7.2	1.4044	0.9	1,460,838	15	313
8/28/2026	1:45:00	7.2	1.6542	0.4	1,460,859	14.8	309
8/28/2026	2:00:00	7.2	1.6164	0.1	1,460,883	14.9	310
8/28/2026	2:30:00	7.2	1.7072	0	1,460,897	15.2	312
8/28/2026	3:00:00	7.2	1.6921	0	1,460,927	15.1	310
8/28/2026	3:30:00	7.1	1.6921	0.3	1,460,943	15.5	304
8/28/2026	3:45:00	7.1	1.6807	0.9	1,460,968	15	310
8/28/2026	4:45:00	7.1	0.9615	0.7	1,460,987	14.9	314
8/28/2026	5:00:00	7.1	1.5407	0.7	1,461,006	14.7	312
8/28/2026	5:15:00	7.1	1.5142	0.7	1,461,029	14.6	312
8/28/2026	5:45:00	7.1	1.1205	41.3	1,461,047	14.7	310
8/28/2026	6:00:00	7.1	1.6012	2.7	1,461,069	14.6	299
8/28/2026	6:30:00	7.1	1.5634	2.8	1,461,095	14.6	298
8/28/2026	7:15:00	7.1	1.5709	1.4	1,461,134	14.5	296
8/28/2026	8:00:00	7.1	1.6429	1.2	1,461,156	14.8	297
8/28/2026	8:15:00	7.1	1.5861	1.6	1,461,180	14.5	296
8/28/2026	8:45:00	7.1	1.1167	5.4	1,461,205	14.5	296
8/28/2026	9:15:00	7.1	1.4687	1.1	1,461,231	14.6	294
8/28/2026	9:30:00	7.2	1.4536	1.5	1,461,253	14.7	307



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	9:45:00	7.2	0.9577	5.8	1,461,274	14.8	309
8/28/2026	10:15:00	7.1	0.9880	4.8	1,461,295	15	307
8/28/2026	10:30:00	7.2	1.4309	4.2	1,461,313	15	306
8/28/2026	10:45:00	7.2	0.9918	10.3	1,461,317	15.2	306
8/28/2026	11:00:00	7.2	1.2795	7	1,461,334	15.1	309
8/28/2026	11:15:00	7.2	0.8517	12.2	1,461,352	15.1	309
8/28/2026	11:30:00	7.2	1.4385	3.9	1,461,369	15.1	306
8/28/2026	12:00:00	7.2	1.4385	4.5	1,461,392	15.4	306
8/28/2026	12:15:00	7.2	0.6246	10.8	1,461,413	15.2	308
8/28/2026	12:30:00	7.2	1.3627	5.8	1,461,426	15.2	308
8/28/2026	12:45:00	7.2	0.9161	5.5	1,461,446	15.2	308
8/28/2026	13:15:00	7.2	0.9388	6.6	1,461,458	15.3	306
8/28/2026	13:30:00	7.2	1.3779	3.4	1,461,475	15.3	306
8/28/2026	13:45:00	7.2	0.9199	6.6	1,461,495	15.3	306
8/28/2026	14:00:00	7.2	1.3287	5.3	1,461,512	15.3	306
8/28/2026	14:15:00	7.2	0.9009	8.2	1,461,532	15.4	306
8/28/2026	14:45:00	7.2	0.9161	6.4	1,461,553	15.4	304
8/28/2026	15:00:00	7.2	1.3325	13.6	1,461,570	15.4	304
8/28/2026	15:15:00	7.2	0.8934	15.1	1,461,589	15.4	304
8/28/2026	15:30:00	7.2	1.3060	10.9	1,461,605	15.4	304
8/28/2026	16:15:00	7.1	0.8820	4.5	1,461,629	15.7	301
8/28/2026	16:30:00	7.2	1.2908	7.9	1,461,646	15.5	303
8/28/2026	16:45:00	7.2	0.8858	5.3	1,461,664	15.4	304
8/28/2026	17:00:00	7.2	1.2946	6.7	1,461,680	15.4	304
8/28/2026	17:15:00	7.2	0.8706	5	1,461,699	15.3	309
8/28/2026	17:45:00	7.2	0.3899	17	1,461,715	15.8	311
8/28/2026	18:00:00	7.2	1.5104	2.7	1,461,728	15.2	313
8/28/2026	18:15:00	7.2	1.0334	1.9	1,461,750	15.2	313
8/28/2026	18:45:00	7.2	1.0675	1	1,461,768	15.3	311
8/28/2026	19:00:00	7.2	1.5709	1.3	1,461,788	15.1	311
8/28/2026	19:30:00	7.2	1.5709	1.1	1,461,803	16	306
8/28/2026	19:45:00	7.2	1.0599	11.8	1,461,826	15.1	309



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	20:15:00	7.2	0.6473	2	1,461,846	15.2	305
8/28/2026	21:00:00	7.2	1.3627	3	1,461,857	14.9	309
8/28/2026	21:30:00	7.2	1.4650	7.7	1,461,883	14.9	306
8/28/2026	21:45:00	7.2	0.4883	0	1,461,901	15.4	112
8/28/2026	22:00:00	7.2	1.3892	0.7	1,461,919	15.2	307
8/28/2026	23:00:00	7.2	1.6239	76.6	1,461,945	15.1	311
8/28/2026	23:15:00	7.2	1.5520	1.2	1,461,968	15.3	313
8/28/2026	23:45:00	7.2	1.4422	1.2	1,461,993	15.1	313
8/29/2026	0:00:00	7.2	1.3968	1.4	1,462,014	15	314
8/29/2026	0:15:00	7.2	1.4120	1.4	1,462,036	15	314
8/29/2026	0:30:00	7.2	1.4195	1.9	1,462,052	15.1	314
8/29/2026	0:45:00	7.2	1.4082	1.9	1,462,073	15.1	316
8/29/2026	1:15:00	7.3	1.3968	1.8	1,462,099	15.1	318
8/29/2026	1:30:00	7.3	0.9766	1.1	1,462,116	15.2	323
8/29/2026	2:45:00	7.3	1.6050	5.3	1,462,156	15	319
8/29/2026	3:00:00	7.3	1.6277	6.2	1,462,180	14.9	317
8/29/2026	3:15:00	7.3	1.5217	5.7	1,462,201	14.8	315
8/29/2026	4:00:00	7.3	1.5747	5.6	1,462,218	14.7	317
8/29/2026	4:15:00	7.2	1.5331	4.8	1,462,240	14.7	320
8/29/2026	4:30:00	7.3	1.5217	4.3	1,462,262	14.7	320
8/29/2026	5:00:00	7.3	1.5293	5.3	1,462,293	15	322
8/29/2026	5:15:00	7.3	1.4347	6.4	1,462,314	15.1	324
8/29/2026	5:45:00	7.3	1.4271	5.1	1,462,336	15.2	320
8/29/2026	6:15:00	7.2	1.4725	11.9	1,462,352	16.4	319
8/29/2026	6:30:00	7.3	1.4120	6.2	1,462,374	15.4	324
8/29/2026	7:00:00	7.2	1.0978	6	1,462,388	15.3	322
8/29/2026	7:15:00	7.2	1.4195	5.6	1,462,408	15.3	324
8/29/2026	7:45:00	7.3	1.4271	4.7	1,462,425	15.6	318
8/29/2026	8:00:00	7.2	1.1129	5.4	1,462,446	15.4	319
8/29/2026	8:45:00	7.2	1.5293	5	1,462,457	14.8	317
8/29/2026	9:00:00	7.2	1.1394	2.5	1,462,479	14.8	317
8/29/2026	9:30:00	7.2	1.2189	1.9	1,462,505	14.9	317



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	9:45:00	7.2	1.5444	6.3	1,462,525	15	321
8/29/2026	10:00:00	7.2	1.1546	4.7	1,462,547	15	319
8/29/2026	10:30:00	7.2	1.2303	4.8	1,462,564	15.2	319
8/29/2026	11:00:00	7.2	1.1053	2.1	1,462,590	15.2	318
8/29/2026	11:15:00	7.2	1.4725	4.5	1,462,609	15.2	318
8/29/2026	11:30:00	7.2	1.1205	5.4	1,462,631	15.2	318
8/29/2026	12:00:00	7.2	1.1243	7.4	1,462,653	15.4	316
8/29/2026	12:15:00	7.2	1.4801	6	1,462,673	15.5	316
8/29/2026	12:30:00	7.2	1.0713	7.3	1,462,694	15.5	316
8/29/2026	12:45:00	7.2	1.4650	7.5	1,462,713	15.6	316
8/29/2026	13:00:00	7.2	1.0826	12.8	1,462,734	15.6	313
8/29/2026	13:30:00	7.2	1.0221	8.2	1,462,756	15.7	311
8/29/2026	13:45:00	7.2	1.3665	2.3	1,462,774	15.7	311
8/29/2026	14:00:00	7.3	1.0221	4.9	1,462,794	15.8	311
8/29/2026	14:30:00	7.2	1.0334	6.8	1,462,812	15.9	309
8/29/2026	14:45:00	7.3	1.4044	5.6	1,462,831	15.9	309
8/29/2026	15:30:00	7.4	0.9918	7.7	1,462,872	15.9	313
8/29/2026	15:45:00	7.4	1.4460	3.8	1,462,891	15.8	313
8/29/2026	16:00:00	7.4	0.9880	4.1	1,462,912	15.8	313
8/29/2026	16:15:00	7.4	1.4120	4.1	1,462,929	15.8	313
8/29/2026	16:30:00	7.4	0.9312	11.8	1,462,949	15.8	313
8/29/2026	17:00:00	7.4	0.9350	13.5	1,462,966	16.3	311
8/29/2026	17:15:00	7.4	1.4385	3.5	1,462,983	16	313
8/29/2026	17:30:00	7.3	0.9501	10.3	1,463,003	15.9	314
8/29/2026	17:45:00	7.3	1.3703	6.2	1,463,021	15.9	314
8/29/2026	18:00:00	7.3	0.9539	8.6	1,463,041	15.9	313
8/29/2026	18:15:00	7.3	1.3362	3.9	1,463,058	16	313
8/29/2026	18:30:00	7.4	0.8934	9.3	1,463,078	15.9	316
8/29/2026	18:45:00	7.3	1.3665	3.8	1,463,081	16	311
8/29/2026	19:00:00	7.3	0.9539	9.6	1,463,101	15.8	313
8/29/2026	19:45:00	7.3	1.5293	8.5	1,463,118	15.3	309
8/29/2026	20:00:00	7.3	1.5293	6.9	1,463,141	15.1	306



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	20:15:00	7.3	1.5217	8.5	1,463,164	15.2	308
8/29/2026	20:30:00	7.4	1.5293	9.6	1,463,181	15.4	304
8/29/2026	20:45:00	7.4	1.4725	6.1	1,463,204	15.5	304
8/29/2026	21:00:00	7.3	0.8139	3.3	1,463,224	15.7	304
8/29/2026	21:15:00	7.3	1.1924	4.6	1,463,231	15.9	302
8/29/2026	21:30:00	7.3	1.1659	0.8	1,463,248	15.8	300
8/29/2026	22:00:00	7.3	0.7949	18.1	1,463,271	15.6	304
8/29/2026	22:15:00	7.3	1.3135	2.4	1,463,289	15.5	304
8/29/2026	22:30:00	7.3	1.2605	2.7	1,463,308	15.4	304
8/29/2026	22:45:00	7.3	0.8669	1.9	1,463,325	15.4	304
8/29/2026	23:00:00	7.3	0.9804	0.9	1,463,343	15.3	304
8/29/2026	23:15:00	7.3	1.3325	1.4	1,463,362	15.2	304
8/29/2026	23:45:00	7.4	1.4195	1.9	1,463,380	15.9	300
8/30/2026	0:00:00	7.4	1.0637	0.5	1,463,400	15.8	300
8/30/2026	0:15:00	7.3	1.4309	0.3	1,463,405	16.3	302
8/30/2026	0:30:00	7.4	1.4195	2.2	1,463,426	15.8	302
8/30/2026	0:45:00	7.4	1.4006	2.3	1,463,447	15.8	300
8/30/2026	1:15:00	7.4	1.4044	2.2	1,463,472	15.8	300
8/30/2026	1:45:00	7.4	1.4157	0	1,463,492	15.9	297
8/30/2026	2:00:00	7.4	1.0864	0	1,463,512	16	300
8/30/2026	2:15:00	7.4	0.9804	0	1,463,516	16.2	299
8/30/2026	2:30:00	7.5	1.4195	0	1,463,535	16.1	302
8/30/2026	2:45:00	7.5	1.4195	0	1,463,556	16.2	302
8/30/2026	3:15:00	7.4	1.4347	0	1,463,577	17	297
8/30/2026	3:30:00	7.5	1.4157	0	1,463,598	16.3	302
8/30/2026	4:00:00	7.5	1.1016	0	1,463,623	16.2	300
8/30/2026	4:15:00	7.5	1.4233	0	1,463,644	16	300
8/30/2026	4:30:00	7.5	1.4195	0	1,463,665	16.1	304
8/30/2026	5:00:00	7.5	1.4952	4.4	1,463,681	16	305
8/30/2026	5:15:00	7.5	1.4763	5	1,463,703	16	309
8/30/2026	5:30:00	7.5	1.4612	5.5	1,463,725	16	308
8/30/2026	6:00:00	7.5	1.4612	7.2	1,463,748	15.5	312



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	6:15:00	7.5	1.4347	8.6	1,463,770	15.2	309
8/30/2026	6:45:00	7.4	1.4460	10.4	1,463,790	15	305
8/30/2026	7:00:00	7.4	1.4612	10.4	1,463,811	14.9	305
8/30/2026	7:30:00	7.4	0.6700	7.5	1,463,829	14.8	304
8/30/2026	8:00:00	7.4	1.2757	1.6	1,463,854	14.7	306
8/30/2026	8:15:00	7.4	1.2454	2.1	1,463,873	14.7	304
8/30/2026	8:30:00	7.4	0.8820	2.7	1,463,890	14.7	301
8/30/2026	8:45:00	7.4	1.3249	2.4	1,463,909	14.7	301
8/30/2026	9:00:00	7.4	1.3098	4.1	1,463,929	14.7	300
8/30/2026	9:15:00	7.4	0.7798	3.5	1,463,948	14.8	303
8/30/2026	9:30:00	7.5	0.8744	4	1,463,957	14.8	306
8/30/2026	9:45:00	7.5	0.9350	2.2	1,463,979	14.9	304
8/30/2026	10:00:00	7.4	1.4801	1.4	1,463,985	15	309
8/30/2026	10:15:00	7.4	0.9842	1.8	1,464,007	15	304
8/30/2026	10:30:00	7.4	1.4725	1.1	1,464,025	15	306
8/30/2026	10:45:00	7.4	0.9426	3.6	1,464,047	15	303
8/30/2026	11:30:00	7.4	1.4347	3	1,464,079	15	301
8/30/2026	11:45:00	7.4	0.9123	6.7	1,464,100	14.9	301
8/30/2026	12:00:00	7.4	1.3892	2.3	1,464,117	15	301
8/30/2026	12:15:00	7.4	0.8820	7.3	1,464,137	15	301
8/30/2026	12:30:00	7.4	1.3930	2.6	1,464,141	15.1	299
8/30/2026	12:45:00	7.4	0.8896	5.6	1,464,161	15	299
8/30/2026	13:00:00	7.4	1.3438	1.7	1,464,178	15	303
8/30/2026	13:15:00	7.4	0.9312	6.1	1,464,198	15.1	303
8/30/2026	13:30:00	7.4	1.4044	3.2	1,464,216	15.1	303
8/30/2026	13:45:00	7.4	0.9161	7	1,464,221	15.1	304
8/30/2026	14:00:00	7.4	1.4347	5.8	1,464,227	15.2	306
8/30/2026	14:15:00	7.4	0.9274	9.5	1,464,248	15.1	306
8/30/2026	14:30:00	7.4	1.4120	7	1,464,266	15.2	308
8/30/2026	14:45:00	7.4	0.9161	21.5	1,464,286	15.2	311
8/30/2026	15:00:00	7.4	1.3930	8.8	1,464,304	15.2	309
8/30/2026	15:30:00	7.4	1.4271	6.7	1,464,319	15.3	309



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	15:45:00	7.4	0.4505	9.8	1,464,334	15.2	311
8/30/2026	16:00:00	7.4	1.4195	5.4	1,464,349	15.2	309
8/30/2026	16:15:00	7.4	0.9426	10.4	1,464,368	15.2	309
8/30/2026	16:30:00	7.4	1.4233	11.3	1,464,388	15.2	309
8/30/2026	16:45:00	7.4	0.9501	13.6	1,464,406	15.3	309
8/30/2026	17:00:00	7.4	1.3968	7.7	1,464,426	15.2	309
8/30/2026	17:45:00	7.4	0.9577	7.9	1,464,455	15.3	308
8/30/2026	18:00:00	7.4	1.4271	8.6	1,464,476	15.3	306
8/30/2026	18:15:00	7.4	0.7117	9.2	1,464,492	15.2	306
8/30/2026	18:30:00	7.4	1.3968	7.4	1,464,512	15.2	306
8/30/2026	19:00:00	7.3	1.3362	9	1,464,536	15.3	303
8/30/2026	19:15:00	7.3	0.9009	14.2	1,464,553	15.3	303
8/30/2026	19:30:00	7.3	1.3892	8.6	1,464,574	15.2	303
8/30/2026	19:45:00	7.7	0.1325	401	1,464,583	16.5	108
8/30/2026	20:00:00	7.4	1.4044	10	1,464,594	15.2	297
8/30/2026	20:30:00	7.3	0.6965	1.5	1,464,620	15	298
8/30/2026	20:45:00	7.3	1.2303	9.2	1,464,627	15.2	293
8/30/2026	21:00:00	7.3	1.4044	7.9	1,464,636	15.2	296
8/30/2026	21:15:00	7.3	1.3968	2.7	1,464,657	14.8	294
8/30/2026	21:30:00	7.3	0.9577	2.6	1,464,675	14.9	296
8/30/2026	22:00:00	7.3	1.4233	1.4	1,464,704	14.8	298
8/30/2026	22:15:00	7.3	1.4952	1	1,464,726	14.8	298
8/30/2026	22:30:00	7.3	1.4650	1	1,464,748	14.8	298
8/30/2026	23:00:00	7.3	1.5255	1.6	1,464,763	15.7	294
8/30/2026	23:15:00	7.3	1.4990	1.4	1,464,786	14.8	296
8/30/2026	23:45:00	7.3	1.5179	0.6	1,464,810	15	294

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

4. CP2 Discharge Parameter Summary:

Table 3: CP2 Discharge Parameter Summary

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	0:00:00	6.93	1.5407	0	269180	14.2	229
8/24/2026	0:15:00	6.93	1.5444	0	269204	14.2	228
8/24/2026	0:30:00	6.93	1.8397	0	269229	14.1	229
8/24/2026	0:45:00	6.95	0.5678	0	269246	14.3	231
8/24/2026	1:00:00	6.94	0.3710	0	269250	15.2	229
8/24/2026	1:15:00	6.94	0.9426	0	269261	14.3	231
8/24/2026	1:30:00	6.94	1.7943	0	269283	14	233
8/24/2026	1:45:00	6.95	0.9539	0	269305	14.2	233
8/24/2026	2:00:00	6.95	0.9993	0	269321	14.2	235
8/24/2026	2:30:00	6.92	0.0227	0	269326	16	221
8/24/2026	2:45:00	6.93	1.3098	0	269327	16.3	235
8/24/2026	3:00:00	6.96	0.0303	0	269335	14.9	238
8/24/2026	3:15:00	6.94	1.2870	0	269343	14.3	234
8/24/2026	3:30:00	6.95	0.0189	0	269349	15	237
8/24/2026	3:45:00	6.94	1.2605	0	269356	14.3	233
8/24/2026	4:00:00	6.95	0.4050	0	269372	14.5	234
8/24/2026	4:15:00	6.93	0.2120	0	269373	15.5	236
8/24/2026	4:30:00	6.95	0.6095	0	269389	14.2	236
8/24/2026	4:45:00	6.95	1.2492	0	269402	14.2	232
8/24/2026	5:00:00	6.96	1.2643	0	269423	14.2	236
8/24/2026	5:15:00	6.96	0.7874	0	269435	14.3	236
8/24/2026	5:30:00	6.95	1.5444	0	269452	14.3	236
8/24/2026	5:45:00	6.96	0.6927	0	269469	14.4	237
8/24/2026	6:00:00	6.95	0.8441	0	269481	14.3	239
8/24/2026	6:15:00	6.96	0.0265	0	269494	14.5	240
8/24/2026	6:30:00	6.93	0.0265	0	269494	15.4	240
8/24/2026	6:45:00	6.94	0.7798	0	269499	14.6	239
8/24/2026	7:00:00	6.94	0.5905	0	269509	15.1	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	7:15:00	6.93	1.5974	0	269527	14.2	241
8/24/2026	7:30:00	6.92	1.6996	0	269550	14.2	241
8/24/2026	7:45:00	6.93	1.6542	0	269574	14.2	242
8/24/2026	8:00:00	6.95	0.6057	0	269588	14.6	242
8/24/2026	8:15:00	6.93	0.0265	0	269589	15.7	69
8/24/2026	8:30:00	6.94	1.7299	0	269606	14.5	241
8/24/2026	8:45:00	6.95	1.6618	0	269630	14.4	240
8/24/2026	9:00:00	6.96	1.6618	1	269653	14.4	237
8/24/2026	9:15:00	6.97	0.3748	0	269671	14.8	237
8/24/2026	9:45:00	6.94	1.8927	1	269678	15	233
8/24/2026	10:00:00	6.96	0.2612	0	269686	15.9	236
8/24/2026	10:15:00	6.94	0.2650	0	269690	16.4	237
8/24/2026	10:30:00	6.97	0.1514	1	269694	16.1	232
8/24/2026	10:45:00	6.96	1.8889	0	269703	15.2	230
8/24/2026	11:00:00	6.97	0.0189	0	269712	16.2	0
8/24/2026	11:30:00	7	0.5186	0	269728	15.7	233
8/24/2026	11:45:00	6.98	0.0303	1	269729	16.9	234
8/24/2026	12:00:00	6.95	0.1476	1	269729	17.6	234
8/24/2026	12:15:00	7.01	1.6202	1	269749	15.8	233
8/24/2026	12:30:00	7	1.9381	1	269774	15.7	232
8/24/2026	12:45:00	6.98	1.6164	1	269800	15.5	228
8/24/2026	13:00:00	6.98	0.5754	0	269823	15.6	233
8/24/2026	13:15:00	6.99	0.0379	1	269825	16.8	171
8/24/2026	13:30:00	6.97	0.0303	1	269826	17.7	0
8/24/2026	13:45:00	6.93	1.2833	1	269826	18.3	235
8/24/2026	14:00:00	6.97	1.6467	1	269850	15.5	255
8/24/2026	14:15:00	6.98	1.9041	0	269874	15.3	257
8/24/2026	14:30:00	6.99	1.6239	0	269902	15.2	257
8/24/2026	14:45:00	7	1.7716	0	269930	15.1	256
8/24/2026	15:00:00	7.01	1.9306	0	269954	15.2	252
8/24/2026	15:15:00	7.02	0.5867	0	269977	15.6	253
8/24/2026	15:30:00	6.99	0.0265	1	269979	17	252



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	15:45:00	7	1.8889	0	269994	15.5	246
8/24/2026	16:00:00	7.03	0.6889	0	270018	15.8	248
8/24/2026	16:15:00	6.99	0.0189	0	270021	17.5	251
8/24/2026	16:30:00	7.02	0.2763	0	270028	16.5	246
8/24/2026	16:45:00	7.02	0.0227	1	270028	18.1	0
8/24/2026	17:00:00	6.99	0.2309	1	270030	18.8	248
8/24/2026	17:15:00	6.96	0.2385	1	270034	19.2	248
8/24/2026	17:30:00	7.02	0.6700	1	270043	16.8	244
8/24/2026	17:45:00	7.01	1.9571	0	270068	15.4	244
8/24/2026	18:00:00	7	1.6239	0	270092	15.3	244
8/24/2026	18:15:00	6.99	1.6315	0	270118	15.3	244
8/24/2026	18:30:00	7	0.7987	0	270136	15.5	243
8/24/2026	18:45:00	7.02	0.0265	0	270140	16.8	0
8/24/2026	19:00:00	6.99	1.4801	1	270145	15.8	242
8/24/2026	19:15:00	7.01	1.6429	0	270173	15.1	244
8/24/2026	19:30:00	7.01	1.8473	0	270195	15	246
8/24/2026	19:45:00	7.03	1.6088	0	270222	14.9	246
8/24/2026	20:00:00	7.03	1.6050	0	270244	15	246
8/24/2026	20:15:00	7.04	0.0681	0	270254	16.1	248
8/24/2026	20:30:00	7.04	1.2265	0	270263	15.2	244
8/24/2026	20:45:00	7.04	1.1470	0	270285	14.9	245
8/24/2026	21:00:00	7.04	0.0303	0	270291	16.2	155
8/24/2026	21:15:00	7.02	0.0227	0	270291	17.2	245
8/24/2026	21:30:00	7	0.0151	1	270292	17.9	241
8/24/2026	21:45:00	7.01	1.4271	0	270297	15.6	240
8/24/2026	22:00:00	7.01	1.5937	0	270320	14.8	242
8/24/2026	22:15:00	6.99	1.5596	0	270342	14.7	241
8/24/2026	22:30:00	7.01	0.1855	0	270363	15	243
8/24/2026	22:45:00	6.98	1.4385	0	270369	14.8	241
8/24/2026	23:00:00	6.99	1.5937	0	270394	14.4	242
8/24/2026	23:15:00	6.99	1.8927	0	270418	14.4	241
8/24/2026	23:30:00	7	0.5035	0	270438	14.6	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	23:45:00	7.02	0.0379	1	270440	15.2	242
8/25/2026	0:00:00	6.99	1.6012	0	270460	14.3	243
8/25/2026	0:15:00	7.01	0.5905	0	270481	14.6	245
8/25/2026	0:30:00	6.99	0.0303	0	270483	15.9	246
8/25/2026	0:45:00	6.99	1.5482	0	270501	14.4	245
8/25/2026	1:00:00	7.01	0.5640	0	270517	14.6	244
8/25/2026	1:15:00	7.02	0.0189	0	270520	14.9	244
8/25/2026	1:30:00	7.01	1.4460	0	270532	14.3	247
8/25/2026	1:45:00	7.02	1.6050	0	270556	14.3	248
8/25/2026	2:00:00	7.03	0.2385	0	270563	15	249
8/25/2026	2:15:00	7.04	1.6012	1	270582	14.2	251
8/25/2026	2:30:00	7.04	1.6088	0	270606	14.2	250
8/25/2026	2:45:00	7.04	1.9192	0	270633	14.1	251
8/25/2026	3:00:00	7.05	0.8555	0	270656	14.2	249
8/25/2026	3:15:00	7.06	0.0151	0	270660	15	251
8/25/2026	3:30:00	7.03	0.0265	0	270660	15.4	250
8/25/2026	4:30:00	7.01	0.0114	0	270663	17.4	0
8/25/2026	4:45:00	7.02	1.8284	0	270670	14.7	242
8/25/2026	5:00:00	7.04	0.3407	0	270690	14.6	246
8/25/2026	5:30:00	7.03	0.1893	0	270697	14.9	244
8/25/2026	5:45:00	6.97	1.9192	0	270715	14.1	243
8/25/2026	6:00:00	6.97	1.9192	0	270742	13.9	245
8/25/2026	6:15:00	6.99	0.1779	0	270759	14.2	249
8/25/2026	6:30:00	7	0.4505	0	270765	14.3	248
8/25/2026	6:45:00	6.98	0.9426	0	270773	14.2	250
8/25/2026	7:00:00	6.96	1.9268	0	270798	13.9	251
8/25/2026	7:15:00	6.96	1.7148	0	270826	13.9	252
8/25/2026	7:30:00	6.97	0.6927	0	270847	14.1	253
8/25/2026	7:45:00	6.98	0.0492	0	270849	15.1	0
8/25/2026	8:00:00	6.98	1.4385	0	270856	14.3	255
8/25/2026	8:15:00	7.01	1.5747	0	270879	14.1	258
8/25/2026	8:30:00	7.03	1.5672	0	270903	14.1	260



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	8:45:00	7.06	1.5785	0	270927	14.2	259
8/25/2026	9:00:00	7.07	1.5520	0	270951	14.3	259
8/25/2026	9:15:00	7.08	0.7495	0	270975	14.3	260
8/25/2026	9:30:00	7.08	0.0189	0	270978	15.3	0
8/25/2026	9:45:00	7.06	0.0265	0	270978	16.3	0
8/25/2026	10:00:00	7.07	1.4498	0	270988	14.8	255
8/25/2026	10:15:00	7.08	1.8473	0	271012	14.6	253
8/25/2026	10:30:00	7.08	0.0265	0	271027	15	255
8/25/2026	10:45:00	7.06	0.0341	0	271027	16.3	85
8/25/2026	11:00:00	7.05	0.0189	1	271027	17.2	255
8/25/2026	11:15:00	7.03	0.1703	0	271030	17.6	255
8/25/2026	11:30:00	7.01	0.1703	0	271033	18.1	257
8/25/2026	11:45:00	7.02	1.5369	0	271047	15.5	254
8/25/2026	12:00:00	7.01	1.5444	0	271071	15.4	257
8/25/2026	12:15:00	7	1.5331	0	271095	15.5	256
8/25/2026	12:30:00	6.99	1.5028	0	271118	15.6	256
8/25/2026	12:45:00	6.99	1.5672	0	271143	15.5	255
8/25/2026	13:00:00	7	0.7230	0	271161	16.1	256
8/25/2026	13:15:00	6.99	0.0265	0	271166	18.2	260
8/25/2026	13:30:00	6.98	1.3287	1	271168	18.4	251
8/25/2026	13:45:00	7.03	1.4385	0	271189	16.1	255
8/25/2026	14:00:00	7.02	1.3855	0	271209	16.1	255
8/25/2026	14:15:00	7.04	1.3362	0	271232	16	259
8/25/2026	14:30:00	7.06	1.2757	0	271252	16.2	259
8/25/2026	14:45:00	7.07	1.1886	0	271274	16.2	258
8/25/2026	15:00:00	7.08	1.1281	1	271291	16.5	258
8/25/2026	15:15:00	7.09	0.3180	0	271304	17.2	261
8/25/2026	15:30:00	7.08	0.0076	1	271306	18.3	117
8/25/2026	15:45:00	7.06	0.5224	0	271311	17.6	256
8/25/2026	16:00:00	7.05	0.4656	0	271318	17.8	260
8/25/2026	16:15:00	7.05	0.0871	0	271326	17.6	261
8/25/2026	16:30:00	7.07	1.9608	1	271346	15.9	264



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	16:45:00	7.08	1.4650	1	271359	16.1	263
8/25/2026	17:00:00	7.06	0.9766	1	271370	16.7	265
8/25/2026	17:15:00	7.04	0.9729	1	271384	17.7	265
8/25/2026	17:30:00	7.04	1.9873	1	271401	16	262
8/25/2026	17:45:00	7.06	1.9836	1	271432	15.5	268
8/25/2026	18:00:00	7.06	1.6921	1	271460	15.6	265
8/25/2026	18:15:00	7.07	1.9684	1	271490	15.5	265
8/25/2026	18:30:00	7.08	1.6845	1	271520	15.5	266
8/25/2026	18:45:00	7.08	1.9722	1	271547	15.4	263
8/25/2026	19:00:00	7.09	0.8025	1	271569	15.7	266
8/25/2026	19:15:00	7.1	0.6322	2	271577	16.2	265
8/25/2026	19:30:00	7.09	1.9684	1	271604	15.3	264
8/25/2026	19:45:00	7.08	1.6921	1	271632	15.3	263
8/25/2026	20:00:00	7.08	0.5943	1	271646	16.1	266
8/25/2026	20:15:00	7.08	1.5520	0	271657	15.5	260
8/25/2026	20:30:00	7.05	1.9608	0	271684	15.2	264
8/25/2026	20:45:00	7.05	1.6542	0	271711	15.1	257
8/25/2026	21:00:00	7.04	0.8479	0	271732	15.3	255
8/25/2026	21:30:00	7.01	0.0227	0	271737	18.1	0
8/25/2026	21:45:00	7.02	1.8284	1	271746	15.5	250
8/25/2026	22:00:00	7.01	1.8927	0	271773	14.8	245
8/25/2026	22:15:00	7	1.6315	0	271800	14.7	244
8/25/2026	22:30:00	7	0.5186	0	271818	15.1	244
8/25/2026	22:45:00	7	1.2416	0	271827	14.9	240
8/25/2026	23:00:00	6.97	1.6126	0	271849	14.8	242
8/25/2026	23:15:00	6.99	0.0265	0	271855	16.2	0
8/25/2026	23:30:00	6.96	1.7602	0	271869	14.8	241
8/25/2026	23:45:00	6.96	1.7564	0	271899	14.5	239
8/26/2026	0:00:00	6.95	2.1690	0	271929	14.5	240
8/26/2026	0:15:00	6.95	1.8208	0	271958	14.5	241
8/26/2026	0:30:00	6.95	1.8208	0	271989	14.5	238
8/26/2026	0:45:00	6.98	0.0265	0	271996	15.3	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	1:00:00	6.96	1.6807	0	272007	14.7	239
8/26/2026	1:15:00	6.95	2.1501	0	272036	14.4	240
8/26/2026	1:30:00	6.95	2.1463	0	272063	14.4	241
8/26/2026	1:45:00	6.96	1.8056	0	272092	14.4	239
8/26/2026	2:00:00	6.96	2.1350	0	272121	14.3	240
8/26/2026	2:15:00	6.98	1.7791	0	272150	14.4	240
8/26/2026	2:30:00	6.99	1.7943	0	272178	14.4	239
8/26/2026	2:45:00	6.99	2.1236	0	272206	14.3	241
8/26/2026	3:00:00	7	0.8404	0	272232	14.5	245
8/26/2026	3:15:00	7.02	0.0265	0	272239	15.5	0
8/26/2026	3:30:00	7	1.8473	0	272252	14.5	238
8/26/2026	3:45:00	7.02	0.1855	0	272267	14.8	238
8/26/2026	4:00:00	7.02	0.0265	0	272267	15.2	237
8/26/2026	4:15:00	7.01	2.0706	0	272289	14.3	238
8/26/2026	4:30:00	7.03	1.8056	0	272316	14.3	241
8/26/2026	4:45:00	7.04	0.3104	0	272335	14.7	243
8/26/2026	5:00:00	7.04	1.7451	0	272348	14.4	244
8/26/2026	5:15:00	7.06	0.0341	0	272361	15.1	0
8/26/2026	5:30:00	7.05	1.7905	0	272371	14.5	246
8/26/2026	5:45:00	7.06	1.8132	0	272398	14.3	247
8/26/2026	6:00:00	7.08	0.0189	0	272412	14.8	247
8/26/2026	6:15:00	7.08	0.0416	1	272412	15.3	247
8/26/2026	6:30:00	7.07	1.8094	0	272436	14.4	247
8/26/2026	6:45:00	7.08	1.8208	0	272467	14.3	248
8/26/2026	7:00:00	7.07	2.1615	1	272497	14.3	247
8/26/2026	7:15:00	7.07	2.1350	1	272526	14.3	247
8/26/2026	7:30:00	7.07	0.7457	0	272551	14.4	247
8/26/2026	8:00:00	7.06	0.0227	0	272554	16.1	0
8/26/2026	8:15:00	7.06	0.2271	0	272555	16.5	249
8/26/2026	8:30:00	7.04	0.0341	0	272556	17	247
8/26/2026	8:45:00	7.04	0.5186	1	272557	17.4	247
8/26/2026	9:00:00	7.03	0.5905	0	272566	16.4	248



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	9:15:00	7.02	0.5678	0	272576	16.5	252
8/26/2026	9:30:00	7.03	0.6359	0	272586	16.2	247
8/26/2026	9:45:00	7.04	1.7791	0	272606	14.9	198
8/26/2026	10:00:00	7.05	2.1085	0	272634	14.8	244
8/26/2026	10:15:00	7.06	0.3483	0	272653	15.3	241
8/26/2026	10:30:00	7.07	0.0265	1	272654	16.3	243
8/26/2026	10:45:00	7.04	2.0101	1	272662	15.5	241
8/26/2026	11:00:00	7.05	2.0971	0	272691	15.2	239
8/26/2026	11:15:00	7.07	0.3520	0	272709	15.6	240
8/26/2026	11:30:00	7.06	0.0227	0	272711	16.8	0
8/26/2026	11:45:00	7.04	1.7224	0	272730	15.6	241
8/26/2026	12:00:00	7.05	1.7413	1	272759	15.5	243
8/26/2026	12:15:00	7.05	2.0895	1	272788	15.5	245
8/26/2026	12:30:00	7.06	1.0372	1	272814	15.8	245
8/26/2026	12:45:00	7.06	0.0265	1	272820	16.7	245
8/26/2026	13:00:00	7.04	2.0933	1	272832	16	245
8/26/2026	13:15:00	7.05	0.1022	0	272848	16.4	247
8/26/2026	13:30:00	7.04	0.1666	1	272852	17	250
8/26/2026	13:45:00	7.04	0.0189	1	272852	17.8	94
8/26/2026	14:00:00	7.01	0.0265	1	272852	18.5	170
8/26/2026	14:15:00	7.02	1.6429	0	272868	16.4	246
8/26/2026	14:30:00	7.04	1.6391	1	272892	16.1	247
8/26/2026	14:45:00	7.05	1.6467	1	272916	16.1	248
8/26/2026	15:00:00	7.05	0.6435	1	272941	16.3	246
8/26/2026	15:15:00	7.06	0.4542	1	272944	17.5	246
8/26/2026	15:30:00	7.04	0.2574	1	272951	17.3	246
8/26/2026	15:45:00	7.02	0.7041	0	272956	17.1	245
8/26/2026	16:00:00	7	0.2461	0	272963	17.6	246
8/26/2026	16:15:00	7	1.9646	0	272978	16.1	241
8/26/2026	16:30:00	7.01	1.8738	0	273003	16.1	242
8/26/2026	16:45:00	7.03	0.0681	0	273020	16.6	242
8/26/2026	17:00:00	7.03	0.9842	2	273023	17.4	239



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	17:15:00	7.03	0.0416	1	273030	18.1	242
8/26/2026	17:30:00	7.01	1.4801	0	273035	16.7	238
8/26/2026	17:45:00	6.98	1.8965	0	273060	15.8	238
8/26/2026	18:00:00	6.97	1.0902	0	273085	15.9	238
8/26/2026	18:15:00	6.96	1.5520	0	273108	15.8	237
8/26/2026	18:30:00	6.96	1.7981	0	273133	15.4	237
8/26/2026	18:45:00	6.97	1.0031	0	273150	15.6	237
8/26/2026	19:00:00	6.98	0.0189	0	273155	16.6	52
8/26/2026	19:15:00	6.99	0.7533	0	273167	15.6	235
8/26/2026	19:30:00	6.98	1.4157	0	273186	15.2	235
8/26/2026	19:45:00	7	1.2340	0	273208	15.2	234
8/26/2026	20:00:00	7	1.2340	0	273224	15.2	233
8/26/2026	20:15:00	7	1.6126	0	273244	15.1	234
8/26/2026	20:30:00	7.02	0.6397	0	273258	15.7	233
8/26/2026	20:45:00	7.02	0.1628	0	273269	15.3	233
8/26/2026	21:00:00	7.01	1.5104	0	273272	15.6	230
8/26/2026	21:15:00	7.02	2.0214	0	273299	14.7	231
8/26/2026	21:30:00	7.02	0.3028	1	273306	15.4	232
8/26/2026	21:45:00	7	2.0933	0	273320	14.6	230
8/26/2026	22:00:00	7	1.5444	0	273350	14.5	229
8/26/2026	22:15:00	6.98	2.0971	0	273377	14.4	229
8/26/2026	22:30:00	6.97	2.0176	0	273405	14.3	228
8/26/2026	22:45:00	6.98	1.7375	0	273432	14.3	228
8/26/2026	23:00:00	7	1.1318	0	273460	14.3	227
8/26/2026	23:15:00	7	0.0303	0	273465	15.5	141
8/26/2026	23:30:00	7	0.1628	1	273469	16.1	228
8/26/2026	23:45:00	6.98	0.7306	1	273472	16.6	228
8/27/2026	0:00:00	7	1.5255	0	273500	14.3	227
8/27/2026	0:15:00	6.99	2.0858	0	273527	14.2	227
8/27/2026	0:30:00	6.99	2.0744	0	273555	14.1	225
8/27/2026	0:45:00	6.99	1.7564	0	273581	14.1	226
8/27/2026	1:00:00	7	2.0328	0	273611	14.1	227



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	1:15:00	7.01	1.7110	0	273640	14.1	227
8/27/2026	1:30:00	7.02	1.0145	0	273667	14.1	228
8/27/2026	2:00:00	7.01	0.0265	0	273672	15.7	170
8/27/2026	2:15:00	7.02	0.0795	0	273675	16	226
8/27/2026	2:30:00	7	0.4391	0	273678	16.3	228
8/27/2026	2:45:00	7.02	2.0138	0	273696	14.2	228
8/27/2026	3:00:00	7.03	1.4801	0	273723	14.1	228
8/27/2026	3:15:00	7.04	0.5224	0	273735	14.4	227
8/27/2026	3:30:00	7.04	0.0227	0	273737	15.3	0
8/27/2026	3:45:00	7.03	0.3369	1	273738	15.6	228
8/27/2026	4:00:00	7.01	1.9987	1	273761	14	227
8/27/2026	4:15:00	7	2.0366	0	273788	13.9	227
8/27/2026	4:30:00	7.02	0.8479	0	273810	14	227
8/27/2026	4:45:00	7.03	0.6435	1	273817	14.2	226
8/27/2026	5:00:00	7.02	0.0303	0	273822	14.9	226
8/27/2026	5:15:00	7.01	0.8176	1	273829	15.2	226
8/27/2026	5:30:00	7.02	0.8101	2	273844	14.1	224
8/27/2026	5:45:00	7.03	1.6050	1	273860	14	227
8/27/2026	6:00:00	7.05	2.0214	1	273887	13.9	228
8/27/2026	6:15:00	7.07	2.0593	1	273917	13.8	230
8/27/2026	6:30:00	7.08	0.7912	1	273938	14	230
8/27/2026	6:45:00	7.09	0.4883	1	273945	14.5	232
8/27/2026	7:00:00	7.09	0.5413	2	273952	14.5	230
8/27/2026	7:15:00	7.11	2.0517	2	273979	13.9	236
8/27/2026	7:30:00	7.12	1.6959	1	274007	13.9	238
8/27/2026	7:45:00	7.14	0.0151	2	274023	14.2	237
8/27/2026	8:00:00	7.11	0.0303	1	274023	14.9	39
8/27/2026	8:15:00	7.1	0.0265	2	274023	15.4	184
8/27/2026	8:30:00	7.1	0.1022	2	274023	15.9	238
8/27/2026	8:45:00	7.11	0.0833	1	274026	15.6	237
8/27/2026	9:00:00	7.08	0.1136	1	274028	15.8	238
8/27/2026	9:15:00	7.1	0.5905	1	274032	15.6	233



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	9:30:00	7.14	1.6769	1	274054	14.2	234
8/27/2026	9:45:00	7.14	1.9987	1	274083	14.1	235
8/27/2026	10:00:00	7.15	0.0946	1	274098	14.4	234
8/27/2026	10:15:00	7.15	0.4807	1	274104	14.6	234
8/27/2026	10:30:00	7.11	1.8927	1	274110	14.4	232
8/27/2026	10:45:00	7.1	1.6732	1	274137	14.2	233
8/27/2026	11:00:00	7.09	0.9993	0	274162	14.3	233
8/27/2026	11:15:00	7.1	0.3710	1	274166	14.9	234
8/27/2026	11:30:00	7.11	0.0189	1	274173	15.4	0
8/27/2026	11:45:00	7.09	0.0189	1	274173	15.9	45
8/27/2026	12:00:00	7.07	0.0227	1	274173	16.2	233
8/27/2026	12:15:00	7.05	1.5974	1	274176	15.2	232
8/27/2026	12:30:00	7.04	1.6769	1	274200	14.4	233
8/27/2026	12:45:00	7.05	1.9684	0	274224	14.3	235
8/27/2026	13:00:00	7.06	1.6921	0	274254	14.3	236
8/27/2026	13:15:00	7.09	1.0902	1	274280	14.5	238
8/27/2026	13:30:00	7.08	0.4315	1	274286	15	235
8/27/2026	13:45:00	7.07	0.5035	1	274293	15.6	237
8/27/2026	14:00:00	7.06	0.0908	1	274295	16.1	238
8/27/2026	14:15:00	7.09	1.6391	1	274315	14.7	238
8/27/2026	14:30:00	7.11	0.4883	1	274336	14.9	239
8/27/2026	15:45:00	7.05	0.0151	1	274340	17.6	241
8/27/2026	16:00:00	7.05	0.0341	1	274340	17.8	241
8/27/2026	16:15:00	7.04	0.0114	1	274340	18	241
8/27/2026	16:30:00	7.04	0.2574	1	274343	16.8	242
8/27/2026	16:45:00	7.04	2.0820	1	274365	14.9	239
8/27/2026	17:00:00	7.04	2.2069	0	274395	14.7	244
8/27/2026	17:15:00	7.07	0.5981	0	274414	14.9	245
8/27/2026	17:30:00	7.05	0.0341	1	274417	16	246
8/27/2026	17:45:00	7.02	2.0441	0	274444	14.5	253
8/27/2026	18:00:00	7.03	2.0441	0	274472	14.4	254
8/27/2026	18:15:00	7.04	1.7224	0	274501	14.4	253



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	18:30:00	7.05	2.0403	0	274531	14.4	255
8/27/2026	18:45:00	7.07	2.0214	0	274558	14.4	255
8/27/2026	19:00:00	7.1	0.6852	0	274582	14.6	255
8/27/2026	19:15:00	7.1	0.0227	1	274590	15	252
8/27/2026	19:30:00	7.08	2.0290	0	274611	14.4	255
8/27/2026	19:45:00	7.09	1.9873	0	274638	14.4	256
8/27/2026	20:00:00	7.09	1.6580	0	274667	14.3	255
8/27/2026	20:15:00	7.1	0.6624	0	274685	14.5	255
8/27/2026	20:30:00	7.09	0.0265	0	274686	15.4	252
8/27/2026	20:45:00	7.08	0.0114	0	274686	16.1	0
8/27/2026	21:00:00	7.08	0.0341	0	274686	16.4	252
8/27/2026	21:15:00	7.07	1.5066	0	274693	14.9	250
8/27/2026	21:30:00	7.08	0.3861	0	274705	14.8	252
8/27/2026	21:45:00	7.18	0.0189	779	274709	15.3	0
8/27/2026	22:00:00	7.05	0.7230	0	274716	14.8	248
8/27/2026	22:15:00	7.03	1.9646	0	274730	14.4	247
8/27/2026	22:30:00	7.03	1.6580	0	274757	14.3	246
8/27/2026	22:45:00	7.03	1.6126	0	274784	14.3	245
8/27/2026	23:00:00	7.02	2.0479	1	274812	14.2	244
8/27/2026	23:15:00	7.02	1.8549	0	274839	14.3	241
8/27/2026	23:30:00	7.04	0.2006	0	274858	14.4	242
8/27/2026	23:45:00	7.03	0.0265	0	274858	15.1	242
8/28/2026	0:00:00	7.01	0.1855	0	274858	15.6	243
8/28/2026	0:15:00	7.05	0.5678	0	274871	14.6	241
8/28/2026	0:30:00	7.04	0.1211	0	274872	15.3	243
8/28/2026	0:45:00	7.03	1.6202	0	274895	14.2	243
8/28/2026	1:00:00	7.02	1.5747	0	274921	14.1	241
8/28/2026	1:15:00	7.02	1.8321	0	274947	14.1	241
8/28/2026	1:30:00	7.02	1.7299	0	274970	14.2	242
8/28/2026	1:45:00	7.04	1.4082	0	274996	14.2	243
8/28/2026	2:15:00	7.04	0.0189	1	275001	15.3	164
8/28/2026	2:30:00	7.05	0.3634	0	275005	15.2	243



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	2:45:00	7.04	0.0303	0	275007	15.7	246
8/28/2026	3:00:00	7.01	1.1470	0	275015	14.5	243
8/28/2026	3:15:00	6.99	1.8132	1	275032	14.2	243
8/28/2026	3:30:00	6.97	2.2031	0	275063	13.9	243
8/28/2026	3:45:00	7	0.9085	0	275087	14	244
8/28/2026	4:00:00	7.01	0.4240	0	275095	14.5	244
8/28/2026	4:15:00	7	2.2485	1	275120	13.9	242
8/28/2026	4:30:00	7.04	0.0151	1	275129	14.3	242
8/28/2026	4:45:00	7.02	1.8208	0	275141	14	241
8/28/2026	5:00:00	7.02	1.1356	1	275167	14	242
8/28/2026	5:15:00	7.03	0.5489	0	275179	14.3	242
8/28/2026	5:30:00	6.99	2.0025	1	275200	13.9	244
8/28/2026	5:45:00	7.02	0.6776	0	275217	14.1	242
8/28/2026	6:00:00	7.02	0.0227	1	275221	14.4	242
8/28/2026	6:15:00	6.99	2.2410	0	275247	13.9	243
8/28/2026	6:30:00	6.99	2.2258	0	275278	13.8	244
8/28/2026	6:45:00	6.99	2.2296	0	275309	13.9	243
8/28/2026	7:00:00	7.02	0.4050	0	275330	14.1	244
8/28/2026	7:15:00	7.02	0.7192	1	275335	14.2	243
8/28/2026	7:45:00	7.01	0.0227	0	275347	14.9	244
8/28/2026	8:00:00	7.01	0.0189	1	275348	15.6	244
8/28/2026	8:15:00	7	0.0227	1	275348	15.9	244
8/28/2026	8:30:00	7	0.2120	1	275349	16.1	245
8/28/2026	8:45:00	6.98	0.2536	1	275353	16.3	246
8/28/2026	9:00:00	7.02	0.3483	2	275361	14.8	243
8/28/2026	9:15:00	7.01	1.5899	1	275372	14.3	243
8/28/2026	9:30:00	7.02	1.6921	1	275400	14.2	244
8/28/2026	9:45:00	7.01	2.0101	1	275425	14.2	244
8/28/2026	10:00:00	7.02	1.6883	0	275452	14.3	242
8/28/2026	10:15:00	7.04	0.1060	1	275465	14.8	242
8/28/2026	10:30:00	7.01	1.9192	1	275472	14.5	241
8/28/2026	10:45:00	7	1.6845	0	275500	14.3	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	11:00:00	6.99	1.7526	0	275528	14.2	242
8/28/2026	11:15:00	6.98	1.7375	1	275555	14.2	239
8/28/2026	11:30:00	7.01	0.4126	0	275575	14.5	241
8/28/2026	11:45:00	6.99	0.0227	1	275576	15.4	240
8/28/2026	12:00:00	6.98	0.0265	1	275576	15.8	241
8/28/2026	12:15:00	6.97	0.0227	1	275576	16.3	241
8/28/2026	12:30:00	6.98	1.7678	1	275601	14.3	240
8/28/2026	12:45:00	6.99	1.7451	1	275628	14.2	242
8/28/2026	13:00:00	6.99	1.7564	0	275655	14.2	243
8/28/2026	13:15:00	7	2.0668	0	275684	14.2	242
8/28/2026	13:30:00	7.04	0.1741	1	275697	14.7	242
8/28/2026	13:45:00	7.02	0.0189	1	275697	15.5	242
8/28/2026	14:00:00	7.02	1.6202	1	275706	14.6	241
8/28/2026	14:15:00	7.03	0.6662	0	275725	14.6	244
8/28/2026	14:30:00	7.03	0.2725	1	275730	15.1	242
8/28/2026	14:45:00	7.01	0.7230	1	275736	14.7	239
8/28/2026	15:00:00	7.02	0.9161	1	275745	14.6	241
8/28/2026	15:15:00	7.02	0.0227	1	275748	15.5	202
8/28/2026	15:30:00	7	0.0416	1	275748	16.1	240
8/28/2026	15:45:00	7	1.6239	1	275757	14.8	240
8/28/2026	16:00:00	6.99	1.7186	1	275784	14.3	241
8/28/2026	16:15:00	6.99	1.6921	1	275810	14.3	243
8/28/2026	16:30:00	7	1.6883	1	275834	14.2	242
8/28/2026	16:45:00	7.02	0.3975	1	275851	14.6	242
8/28/2026	17:00:00	7.02	0.0189	1	275852	15.7	245
8/28/2026	17:15:00	7.02	0.6473	1	275861	14.7	241
8/28/2026	17:30:00	7.04	0.0341	1	275869	15.5	0
8/28/2026	17:45:00	7.02	0.1855	1	275870	15.9	243
8/28/2026	18:00:00	7.03	2.0138	1	275886	14.4	246
8/28/2026	18:15:00	7.04	1.6845	1	275914	14.2	250
8/28/2026	18:30:00	7.04	1.6996	1	275943	14.1	250
8/28/2026	18:45:00	7.03	1.9911	1	275969	14.1	247



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	19:00:00	7.05	0.0871	1	275982	14.6	248
8/28/2026	19:15:00	7.04	1.9533	1	275990	14.4	246
8/28/2026	19:30:00	7.04	1.6883	1	276017	14.2	245
8/28/2026	19:45:00	7.03	1.9987	1	276042	14.1	246
8/28/2026	20:00:00	7.04	1.6845	1	276067	14.1	243
8/28/2026	20:15:00	7.05	1.9873	1	276093	14.1	245
8/28/2026	20:30:00	7.08	0.0946	1	276106	14.4	246
8/28/2026	20:45:00	7.07	0.0151	1	276108	14.9	246
8/28/2026	21:00:00	7.06	0.1363	1	276108	15.3	246
8/28/2026	21:15:00	7.05	0.1666	1	276111	15.6	247
8/28/2026	21:30:00	7.04	0.0227	1	276113	15.9	246
8/28/2026	21:45:00	7.04	0.3445	1	276113	16.1	248
8/28/2026	22:00:00	7.07	0.3710	1	276121	14.9	248
8/28/2026	22:15:00	7.03	1.9381	1	276127	15.2	250
8/28/2026	22:30:00	7.05	1.7034	1	276154	13.9	243
8/28/2026	22:45:00	7.04	1.6996	1	276180	13.9	242
8/28/2026	23:00:00	7.04	1.6694	1	276207	13.9	241
8/28/2026	23:15:00	7.03	1.6618	0	276231	13.9	241
8/28/2026	23:30:00	7.05	0.1287	0	276247	14.2	239
8/28/2026	23:45:00	7.06	0.6587	1	276249	14.3	239
8/29/2026	0:00:00	7.06	0.0303	1	276255	14.9	242
8/29/2026	0:15:00	7.04	1.5407	1	276262	14.3	244
8/29/2026	0:30:00	7.06	0.6776	1	276283	14	250
8/29/2026	0:45:00	7.07	0.0341	1	276286	15.2	252
8/29/2026	1:00:00	7.06	0.4013	1	276287	15.7	251
8/29/2026	1:15:00	7.06	1.6088	1	276302	14	253
8/29/2026	1:30:00	7.09	1.6656	1	276326	13.9	259
8/29/2026	1:45:00	7.08	1.6732	1	276353	13.8	257
8/29/2026	2:00:00	7.08	1.6467	1	276377	13.9	256
8/29/2026	2:15:00	7.09	0.7912	1	276402	13.9	256
8/29/2026	2:30:00	7.1	0.2915	1	276407	14.2	254
8/29/2026	3:00:00	7.08	0.0189	2	276407	15.8	233



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	3:15:00	7.07	0.0227	1	276407	16.3	0
8/29/2026	3:30:00	7.08	0.0416	1	276407	16	255
8/29/2026	3:45:00	7.07	0.2082	1	276409	16.2	255
8/29/2026	4:00:00	7.06	0.7117	1	276417	14.3	252
8/29/2026	4:15:00	7.07	1.6959	1	276443	13.8	254
8/29/2026	4:30:00	7.06	1.9684	1	276468	13.8	256
8/29/2026	4:45:00	7.06	1.6467	1	276494	13.8	254
8/29/2026	5:00:00	7.05	1.6126	1	276521	13.7	254
8/29/2026	5:15:00	7.07	0.0341	1	276529	14.2	252
8/29/2026	5:30:00	7.07	0.7382	2	276531	14.3	252
8/29/2026	5:45:00	7.05	1.8624	1	276556	13.8	253
8/29/2026	6:00:00	7.06	1.5899	1	276581	13.8	254
8/29/2026	6:15:00	7.08	0.0946	1	276596	13.9	254
8/29/2026	6:30:00	7.07	1.4157	1	276604	13.8	255
8/29/2026	6:45:00	7.07	1.5596	1	276629	13.7	256
8/29/2026	7:00:00	7.06	1.8284	1	276653	13.7	260
8/29/2026	7:15:00	7.07	1.5066	1	276679	13.7	260
8/29/2026	7:30:00	7.07	1.4877	1	276704	13.7	259
8/29/2026	7:45:00	7.07	1.7413	1	276727	13.8	261
8/29/2026	8:00:00	7.08	1.3855	1	276752	13.8	262
8/29/2026	8:15:00	7.1	0.2082	1	276762	13.8	261
8/29/2026	8:30:00	7.1	0.0341	1	276764	14.1	261
8/29/2026	8:45:00	7.09	0.0416	1	276764	14.2	261
8/29/2026	9:00:00	7.08	0.0227	1	276764	14.3	262
8/29/2026	9:15:00	7.07	0.0379	1	276764	14.5	262
8/29/2026	9:30:00	7.07	1.3968	1	276772	14.1	259
8/29/2026	9:45:00	7.08	1.7564	1	276795	14	255
8/29/2026	10:00:00	7.07	1.7640	1	276824	14	253
8/29/2026	10:15:00	7.07	0.3785	1	276844	14.2	252
8/29/2026	10:30:00	7.05	0.8971	1	276854	14.3	250
8/29/2026	10:45:00	7.05	0.3785	1	276866	14.5	248
8/29/2026	11:00:00	7.03	0.4202	1	276873	14.6	248



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	11:15:00	7.02	1.6996	1	276886	14.4	246
8/29/2026	11:30:00	7.03	1.7489	1	276913	14.4	247
8/29/2026	13:45:00	7.03	1.7564	2	276945	15.3	251
8/29/2026	14:00:00	7.02	1.7489	2	276974	15.1	253
8/29/2026	14:15:00	7.01	1.7905	1	277004	15.1	254
8/29/2026	14:30:00	7.02	1.1659	1	277031	15.2	255
8/29/2026	14:45:00	7.04	0.0265	1	277037	16.2	257
8/29/2026	15:00:00	7.01	0.0341	1	277037	16.9	0
8/29/2026	15:15:00	7.01	0.4807	1	277040	17.3	257
8/29/2026	15:30:00	6.99	0.4467	1	277047	17.6	256
8/29/2026	15:45:00	6.98	0.2044	1	277052	17.9	256
8/29/2026	16:00:00	6.99	0.0303	1	277054	18.5	0
8/29/2026	16:15:00	6.99	0.1211	1	277055	18.5	258
8/29/2026	16:30:00	7.01	0.0341	2	277055	17.8	262
8/29/2026	16:45:00	6.98	2.1577	2	277055	18.1	262
8/29/2026	17:00:00	7.08	1.7754	2	277082	15.2	262
8/29/2026	17:15:00	7.08	0.8669	2	277103	15.4	262
8/29/2026	17:30:00	7.07	0.0189	2	277106	16.5	262
8/29/2026	17:45:00	7.08	1.7451	2	277124	15.3	261
8/29/2026	18:00:00	7.09	0.0946	2	277139	15.6	261
8/29/2026	18:15:00	7.08	2.1009	2	277148	15.3	260
8/29/2026	18:30:00	7.07	2.0858	1	277177	15	260
8/29/2026	18:45:00	7.06	1.7829	2	277206	15	259
8/29/2026	19:00:00	7.06	0.6624	1	277232	14.9	259
8/29/2026	19:15:00	7.08	0.4618	2	277238	15.2	259
8/29/2026	19:45:00	7.05	0.0114	2	277240	16.9	0
8/29/2026	20:00:00	7.04	0.0341	2	277240	17	257
8/29/2026	20:15:00	7.06	0.7533	1	277257	14.8	255
8/29/2026	20:30:00	7.07	0.3937	1	277264	15	253
8/29/2026	20:45:00	7.04	2.0138	2	277277	14.5	252
8/29/2026	21:00:00	7.05	1.7526	1	277306	14.2	253
8/29/2026	21:15:00	7.06	0.8063	1	277326	14.3	249



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	21:30:00	7.08	0.0151	1	277328	15.2	0
8/29/2026	21:45:00	7.06	0.0227	1	277328	15.8	0
8/29/2026	22:00:00	7.05	0.0341	1	277328	16.3	0
8/29/2026	22:15:00	7.05	1.6504	1	277335	14.5	246
8/29/2026	22:30:00	7.04	2.0858	1	277364	14	247
8/29/2026	22:45:00	7.04	1.1583	1	277394	14	244
8/29/2026	23:00:00	7.06	0.4353	1	277403	14.2	243
8/29/2026	23:15:00	7.06	0.2763	1	277408	14.4	243
8/29/2026	23:30:00	7.05	0.2801	1	277411	14.9	242
8/29/2026	23:45:00	7.03	0.0265	1	277418	14.6	243
8/30/2026	0:00:00	7	1.7526	2	277422	14.5	241
8/30/2026	0:15:00	7.09	0.4770	1	277442	14.2	245
8/30/2026	0:30:00	7.09	0.0265	2	277443	15.1	0
8/30/2026	0:45:00	7.07	0.0151	1	277443	15.7	0
8/30/2026	1:00:00	7.08	0.3710	2	277443	16	245
8/30/2026	1:15:00	7.1	1.7640	2	277470	14	250
8/30/2026	1:30:00	7.1	2.0971	1	277497	14	251
8/30/2026	1:45:00	7.11	0.9312	2	277525	14	254
8/30/2026	2:00:00	7.1	0.2763	1	277532	14.4	253
8/30/2026	2:15:00	7.09	0.2233	1	277536	14.9	253
8/30/2026	2:30:00	7.09	0.0341	2	277536	15.7	0
8/30/2026	2:45:00	7.08	0.0303	1	277536	16.1	0
8/30/2026	3:00:00	7.08	0.2650	1	277536	15.8	251
8/30/2026	3:15:00	7.09	0.3520	1	277561	14.1	255
8/30/2026	3:30:00	7.08	0.3748	1	277568	14.3	256
8/30/2026	3:45:00	7.08	0.3899	1	277574	14.3	255
8/30/2026	4:00:00	7.08	1.7716	2	277597	14	257
8/30/2026	4:15:00	7.09	1.7564	1	277625	13.9	259
8/30/2026	4:30:00	7.11	0.0151	2	277632	14.4	259
8/30/2026	4:45:00	7.1	1.6807	1	277643	14	257
8/30/2026	5:00:00	7.11	0.5640	2	277664	14.1	260
8/30/2026	5:30:00	7.1	0.0303	2	277665	15.4	260



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	5:45:00	7.09	0.0151	2	277665	15.9	260
8/30/2026	6:00:00	7.07	0.1401	2	277667	16.3	260
8/30/2026	6:15:00	7.11	1.7602	2	277688	14	263
8/30/2026	6:30:00	7.11	1.7905	2	277717	13.9	266
8/30/2026	6:45:00	7.11	2.1009	1	277746	13.9	263
8/30/2026	7:00:00	7.13	0.6246	2	277770	14	263
8/30/2026	7:15:00	7.11	0.1628	1	277776	14.5	265
8/30/2026	7:30:00	7.11	2.0858	1	277798	14	262
8/30/2026	7:45:00	7.12	0.0341	1	277814	14.2	262
8/30/2026	8:00:00	7.11	0.2877	1	277815	14.7	262
8/30/2026	8:15:00	7.11	0.1476	1	277816	15.2	261
8/30/2026	8:30:00	7.1	2.0782	1	277844	14	261
8/30/2026	8:45:00	7.12	0.1552	5	277850	14.3	259
8/30/2026	9:00:00	7.11	0.6019	1	277857	14.3	255
8/30/2026	9:15:00	7.11	0.4467	2	277862	14.4	256
8/30/2026	9:30:00	7.14	0.4921	1	277869	14.5	255
8/30/2026	9:45:00	7.11	0.0341	1	277873	14.8	255
8/30/2026	10:00:00	7.1	1.7829	1	277891	14.2	254
8/30/2026	10:15:00	7.1	1.6429	1	277917	14.2	252
8/30/2026	10:30:00	7.11	0.0227	1	277922	14.6	251
8/30/2026	10:45:00	7.08	1.8056	1	277936	14.3	250
8/30/2026	11:00:00	7.06	1.6353	1	277961	14.1	247
8/30/2026	11:15:00	7.07	1.3476	2	277984	14.2	247
8/30/2026	11:30:00	7.08	0.4694	1	277999	14.4	245
8/30/2026	11:45:00	7.08	0.1628	2	278003	14.6	244
8/30/2026	12:00:00	7.08	0.0379	2	278004	15.2	242
8/30/2026	12:15:00	7.06	0.0379	2	278004	15.4	243
8/30/2026	12:30:00	7.08	0.0303	1	278014	15	245
8/30/2026	12:45:00	7.08	1.5558	1	278019	14.6	241
8/30/2026	13:00:00	7.09	1.6996	1	278045	14.3	241
8/30/2026	13:15:00	7.08	2.0138	1	278070	14.3	242
8/30/2026	13:30:00	7.08	1.9949	1	278101	14.2	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	13:45:00	7.09	0.3823	1	278112	14.6	242
8/30/2026	14:00:00	7.09	0.0189	1	278117	15.3	2
8/30/2026	14:15:00	7.1	0.2006	1	278119	15.8	242
8/30/2026	14:30:00	7.08	0.2309	2	278122	16.2	244
8/30/2026	14:45:00	7.06	0.2271	1	278126	16.8	245
8/30/2026	15:00:00	7.09	0.8176	1	278132	15.2	243
8/30/2026	15:15:00	7.07	0.0795	1	278135	16.3	231
8/30/2026	15:30:00	7.07	0.0341	1	278135	16.5	249
8/30/2026	15:45:00	7.07	1.5407	1	278139	15.4	242
8/30/2026	16:00:00	7.08	1.6353	1	278163	14.5	246
8/30/2026	16:15:00	7.08	1.6315	1	278189	14.4	244
8/30/2026	16:30:00	7.08	1.8246	1	278213	14.4	245
8/30/2026	16:45:00	7.1	0.0265	1	278223	15	244
8/30/2026	17:00:00	7.09	0.7192	1	278224	15.7	245
8/30/2026	17:15:00	7.1	0.0227	2	278237	15	243
8/30/2026	17:30:00	7.09	0.1211	1	278237	15.6	244
8/30/2026	17:45:00	7.09	2.0328	2	278260	14.5	243
8/30/2026	18:00:00	7.1	1.7564	1	278289	14.4	244
8/30/2026	18:15:00	7.11	0.2650	2	278307	14.7	245
8/30/2026	18:30:00	7.09	2.0025	2	278314	14.6	242
8/30/2026	18:45:00	7.1	1.7489	2	278342	14.5	243
8/30/2026	19:00:00	7.1	1.7602	1	278372	14.4	244
8/30/2026	19:15:00	7.1	1.0599	1	278398	14.5	244
8/30/2026	19:30:00	7.1	0.0189	1	278403	15.3	245
8/30/2026	19:45:00	7.1	1.8246	2	278422	14.5	244
8/30/2026	20:15:00	7.09	0.7949	2	278438	15.9	245
8/30/2026	20:30:00	7.11	0.0908	1	278449	15.2	244
8/30/2026	20:45:00	7.09	0.4013	1	278449	15.6	246
8/30/2026	21:15:00	7.09	0.0227	2	278453	17	0
8/30/2026	21:30:00	7.08	0.1022	2	278456	16.8	244
8/30/2026	21:45:00	7.11	2.0858	2	278473	14.4	243
8/30/2026	22:00:00	7.11	1.7299	2	278502	14.1	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	22:15:00	7.11	1.7413	1	278531	14.1	241
8/30/2026	22:30:00	7.11	1.3590	1	278560	14	238
8/30/2026	22:45:00	7.12	0.0151	1	278567	14.6	238
8/30/2026	23:00:00	7.11	0.2763	1	278571	14.6	234
8/30/2026	23:30:00	7.08	2.0517	1	278594	14	231
8/30/2026	23:45:00	7.11	0.5489	1	278617	14.2	232

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

5. In-Situ Readings

Table 4. In-Situ Readings

Date	Temperature (C°)	DO mg/L	SAL-ppt	pH	ORP (mV)	NTU
08/24/2026	14.7	10.09	0.09	7.15	111.0	0.03
08/25/2026	13.7	10.28	0.09	7.14	88.8	0.04
08/26/2026	14.3	10.11	0.09	7.15	198.4	0.25
08/27/2026	14.8	9.86	0.09	7.24	191.5	0.23
08/28/2026	13.9	9.98	0.09	7.24	180.6	0.18
08/29/2026	15.2	10.05	0.10	7.17	182.8	0.35
08/30/2026	13.9	10.50	0.10	7.24	182.9	0.33

6. Calibration Log:

Table 5. Calibration Log

Date	Unit	pH	Conductivity/ Salinity	NTU
08/29/2026	YSI	✓	✓	✓
08/30/2026	Portal WTP	✓	N/A	✓
08/30/2026	CP2 WTP	✓	✓	✓

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

APPENDIX A: Portal WTP Data Log



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	0:00:00	7.4	1.1924	5.7	1,455,950	Open	15.7	279
8/24/2026	0:15:00	7.4	0.0000	1	1,455,957	Closed	16.2	281
8/24/2026	0:30:00	7.4	1.2189	36.3	1,455,958	Open	17.5	283
8/24/2026	0:45:00	7.4	1.7602	2.3	1,455,982	Open	16.1	281
8/24/2026	1:00:00	7.4	1.2151	7.2	1,456,007	Open	16.2	281
8/24/2026	1:15:00	7.4	0.0000	1.9	1,456,008	Closed	16.9	283
8/24/2026	1:30:00	7.4	1.2227	4	1,456,021	Open	16.2	279
8/24/2026	1:45:00	7.4	1.7261	3.9	1,456,044	Open	16	282
8/24/2026	2:00:00	7.4	0.0000	1.8	1,456,059	Closed	16.1	284
8/24/2026	2:15:00	7.4	1.6732	3.1	1,456,060	Open	16.7	286
8/24/2026	2:30:00	7.4	1.1508	8.1	1,456,083	Open	15.9	283
8/24/2026	2:45:00	7.4	1.6277	3.9	1,456,106	Open	15.8	285
8/24/2026	3:00:00	7.4	0.0000	2.1	1,456,109	Closed	16.2	288
8/24/2026	3:15:00	7.4	1.6694	3.9	1,456,116	Open	15.9	285
8/24/2026	3:30:00	7.4	1.1394	7.2	1,456,139	Open	15.7	287
8/24/2026	3:45:00	7.4	0.0000	3.7	1,456,153	Closed	15.7	286
8/24/2026	4:00:00	7.4	0.0000	2	1,456,153	Closed	16.2	288
8/24/2026	4:15:00	7.4	1.6467	4.8	1,456,173	Open	15.5	287
8/24/2026	4:30:00	7.4	0.0000	3.9	1,456,191	Closed	15.6	287
8/24/2026	4:45:00	7.4	0.0000	3.3	1,456,191	Closed	16.1	290
8/24/2026	5:00:00	7.4	1.1356	6	1,456,201	Open	15.9	288
8/24/2026	5:15:00	7.5	1.6391	4.3	1,456,223	Open	16	286
8/24/2026	5:30:00	7.5	0.0000	2.3	1,456,242	Closed	16.2	288
8/24/2026	5:45:00	7.4	0.0000	2.3	1,456,242	Closed	17	289
8/24/2026	6:00:00	7.5	1.1167	7.8	1,456,262	Open	15.9	285
8/24/2026	6:15:00	7.5	1.6391	4.3	1,456,285	Open	15.9	286
8/24/2026	6:30:00	7.4	0.0000	3.4	1,456,296	Closed	16.2	288
8/24/2026	6:45:00	7.5	1.6618	4.6	1,456,301	Open	16.6	283
8/24/2026	7:00:00	7.5	1.1129	7.2	1,456,323	Open	16.5	284
8/24/2026	7:15:00	7.5	1.6126	5.1	1,456,346	Open	16.5	281
8/24/2026	7:30:00	7.6	0.0000	401.8	1,456,359	Closed	16.7	274
8/24/2026	7:45:00	7.5	1.6391	6.3	1,456,364	Open	16.3	286



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	8:00:00	7.5	1.6769	5.9	1,456,384	Open	15.9	288
8/24/2026	8:15:00	7.5	1.6618	4.3	1,456,409	Open	15.8	288
8/24/2026	8:30:00	7.5	0.0000	4	1,456,411	Closed	16.4	292
8/24/2026	8:45:00	7.5	1.6732	4.1	1,456,421	Open	16.1	288
8/24/2026	9:00:00	7.5	1.6732	4.9	1,456,440	Open	15.9	288
8/24/2026	9:15:00	7.5	1.5785	4.8	1,456,465	Open	15.9	288
8/24/2026	9:30:00	7.5	0.0000	5.9	1,456,468	Closed	16.3	292
8/24/2026	9:45:00	7.5	0.3748	11.4	1,456,477	Closed	15.9	290
8/24/2026	10:00:00	7.5	0.0000	3.9	1,456,487	Closed	16.1	290
8/24/2026	10:15:00	7.4	0.0000	3.9	1,456,487	Closed	16.7	292
8/24/2026	10:30:00	7.5	1.5482	2.8	1,456,502	Open	16.2	290
8/24/2026	10:45:00	7.5	1.5482	2.2	1,456,525	Open	16.4	290
8/24/2026	11:00:00	7.5	0.0000	1.8	1,456,536	Closed	16.8	291
8/24/2026	11:15:00	7.4	0.0000	1.5	1,456,536	Closed	17.7	295
8/24/2026	11:30:00	7.4	1.5709	1.3	1,456,551	Open	16.9	292
8/24/2026	11:45:00	7.4	1.5596	1.5	1,456,575	Open	17	295
8/24/2026	12:00:00	7.4	1.5407	1.5	1,456,592	Open	17.2	299
8/24/2026	12:15:00	7.4	1.5142	1.8	1,456,615	Open	17.3	299
8/24/2026	12:30:00	7.5	1.4839	1.8	1,456,633	Open	17.4	298
8/24/2026	12:45:00	7.5	1.4687	2.4	1,456,655	Open	17.3	296
8/24/2026	13:00:00	7.5	0.0000	2.8	1,456,658	Closed	17.7	298
8/24/2026	13:15:00	7.5	1.5066	3.3	1,456,670	Open	17.4	293
8/24/2026	13:30:00	7.5	1.4650	3.6	1,456,688	Open	17.4	294
8/24/2026	13:45:00	7.5	1.4347	3.2	1,456,709	Open	17.4	292
8/24/2026	14:00:00	7.5	0.0000	2.9	1,456,711	Closed	17.9	295
8/24/2026	14:15:00	7.5	1.4347	2	1,456,729	Open	17.4	293
8/24/2026	14:30:00	7.5	1.4233	6.4	1,456,746	Open	17.3	294
8/24/2026	14:45:00	7.5	1.4120	1.9	1,456,767	Open	17.3	293
8/24/2026	15:00:00	7.5	1.3930	3.7	1,456,785	Open	17.4	293
8/24/2026	15:15:00	7.5	1.4915	2.8	1,456,807	Open	17.5	293
8/24/2026	15:30:00	7.5	0.0000	2.8	1,456,814	Closed	18.5	296
8/24/2026	15:45:00	7.5	1.4801	2.1	1,456,819	Open	18.1	294



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	16:00:00	7.5	1.4877	2.3	1,456,837	Open	17.8	293
8/24/2026	16:15:00	7.5	1.4801	3.2	1,456,860	Open	17.7	293
8/24/2026	16:30:00	7.5	0.0000	2.3	1,456,868	Closed	18.7	296
8/24/2026	16:45:00	7.5	0.0000	2.4	1,456,868	Closed	19.5	298
8/24/2026	17:00:00	7.5	1.4801	2.4	1,456,886	Open	18	293
8/24/2026	17:15:00	7.5	1.2870	1.6	1,456,908	Open	17.8	295
8/24/2026	17:30:00	7.5	1.4498	2.3	1,456,926	Open	17.9	293
8/24/2026	17:45:00	7.5	1.0183	2.9	1,456,948	Open	17.7	293
8/24/2026	18:00:00	7.5	1.5634	4.3	1,456,966	Open	17.6	293
8/24/2026	18:15:00	7.5	0.0000	4.1	1,456,981	Closed	17.7	291
8/24/2026	18:30:00	7.5	1.6239	4.4	1,456,981	Closed	18.4	293
8/24/2026	18:45:00	7.5	1.0826	17	1,457,005	Open	17.5	292
8/24/2026	19:00:00	7.5	0.0000	3.4	1,457,024	Closed	17.4	290
8/24/2026	19:15:00	7.5	0.9918	5	1,457,028	Open	17.5	291
8/24/2026	19:30:00	7.5	0.0000	6.2	1,457,033	Closed	17.3	290
8/24/2026	19:45:00	7.5	1.1886	3.8	1,457,042	Open	17.2	290
8/24/2026	20:00:00	7.5	0.0000	12.2	1,457,044	Open	16.9	290
8/24/2026	20:15:00	7.4	1.2038	3.2	1,457,062	Open	16.8	290
8/24/2026	20:30:00	7.4	0.0000	1.4	1,457,069	Closed	17.1	293
8/24/2026	20:45:00	7.4	1.2946	2.4	1,457,084	Open	16.7	290
8/24/2026	21:00:00	7.4	1.6542	2.6	1,457,105	Open	16.5	288
8/24/2026	21:15:00	7.4	0.0000	2.5	1,457,105	Closed	16.9	291
8/24/2026	21:30:00	7.4	1.6883	2.9	1,457,122	Open	16.4	289
8/24/2026	21:45:00	7.5	1.6542	3	1,457,147	Open	16.3	290
8/24/2026	22:00:00	7.5	0.0000	2.6	1,457,164	Closed	16.4	290
8/24/2026	22:15:00	7.4	0.0000	2.3	1,457,164	Closed	17	292
8/24/2026	22:30:00	7.5	1.6656	5.4	1,457,177	Open	16.4	290
8/24/2026	22:45:00	7.5	1.6315	2.2	1,457,202	Open	16.2	290
8/24/2026	23:00:00	7.5	0.0000	2.3	1,457,214	Closed	16.3	288
8/24/2026	23:15:00	7.5	1.6504	2.8	1,457,216	Open	16.5	291
8/24/2026	23:30:00	7.5	1.6429	2.6	1,457,240	Open	15.9	288
8/24/2026	23:45:00	7.5	0.0000	2.2	1,457,258	Closed	15.9	289



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	0:00:00	7.5	0.0000	2.1	1,457,258	Closed	16.3	289
8/25/2026	0:15:00	7.5	1.6618	3.2	1,457,275	Open	15.8	286
8/25/2026	0:30:00	7.5	1.6429	2.7	1,457,300	Open	15.7	286
8/25/2026	0:45:00	7.5	0.0000	2.6	1,457,313	Closed	15.8	287
8/25/2026	1:00:00	7.5	1.6542	2.8	1,457,313	Closed	16.2	290
8/25/2026	1:15:00	7.5	1.1924	1.7	1,457,337	Open	15.7	286
8/25/2026	1:30:00	7.5	0.0000	1	1,457,354	Closed	15.9	288
8/25/2026	1:45:00	7.5	0.0000	0.8	1,457,354	Closed	16.5	289
8/25/2026	2:00:00	7.5	1.6694	1.5	1,457,374	Open	15.9	288
8/25/2026	2:15:00	7.5	1.6353	1.8	1,457,399	Open	15.9	288
8/25/2026	2:30:00	7.5	0.0000	1.5	1,457,414	Closed	16.1	288
8/25/2026	2:45:00	7.4	0.0000	1.5	1,457,414	Closed	16.6	289
8/25/2026	3:00:00	7.4	1.6694	2.1	1,457,414	Closed	17.2	291
8/25/2026	3:15:00	7.5	0.0000	6	1,457,426	Open	15.8	288
8/25/2026	3:30:00	7.5	1.6050	1	1,457,434	Open	15.7	289
8/25/2026	3:45:00	7.5	1.5861	0.4	1,457,458	Open	15.6	290
8/25/2026	4:00:00	7.5	0.0000	0.3	1,457,463	Closed	16	292
8/25/2026	4:15:00	7.5	1.6050	0.3	1,457,470	Open	15.8	292
8/25/2026	4:30:00	7.5	1.5974	0.5	1,457,490	Open	15.7	293
8/25/2026	4:45:00	7.5	1.5407	0.8	1,457,514	Open	15.7	293
8/25/2026	5:00:00	7.5	1.4801	0.8	1,457,537	Open	15.7	295
8/25/2026	5:15:00	7.5	0.0000	0.3	1,457,544	Closed	16	296
8/25/2026	5:30:00	7.5	1.4990	0.5	1,457,550	Open	16	294
8/25/2026	5:45:00	7.5	1.4536	0.1	1,457,572	Open	15.9	294
8/25/2026	6:00:00	7.5	0.0000	0.4	1,457,591	Closed	16	293
8/25/2026	6:15:00	7.5	0.0000	0	1,457,591	Closed	16.6	293
8/25/2026	6:30:00	7.5	1.0183	0.6	1,457,602	Open	15.8	293
8/25/2026	6:45:00	7.5	1.4612	0.6	1,457,623	Open	15.7	291
8/25/2026	7:00:00	7.5	1.0031	1.7	1,457,643	Open	15.8	291
8/25/2026	7:15:00	7.5	0.0000	0.6	1,457,643	Closed	16.4	293
8/25/2026	7:30:00	7.5	1.0069	1.3	1,457,651	Open	16	293
8/25/2026	7:45:00	7.5	1.4763	1.1	1,457,671	Open	15.8	293



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	8:00:00	7.5	0.7230	1.6	1,457,692	Open	15.7	294
8/25/2026	8:15:00	7.5	1.3514	1.5	1,457,708	Open	15.6	294
8/25/2026	8:30:00	7.5	0.9577	1.7	1,457,728	Open	15.6	298
8/25/2026	8:45:00	7.4	0.0000	2.2	1,457,731	Closed	16.2	301
8/25/2026	9:00:00	7.5	0.9539	1.8	1,457,740	Open	15.7	299
8/25/2026	9:15:00	7.5	1.4612	2.5	1,457,758	Open	15.6	299
8/25/2026	9:30:00	7.5	1.4498	2.9	1,457,780	Open	15.7	300
8/25/2026	9:45:00	7.4	0.0000	1.3	1,457,788	Closed	16.2	303
8/25/2026	10:00:00	7.4	0.0000	1.6	1,457,788	Closed	16.7	303
8/25/2026	10:15:00	7.4	1.4460	1.6	1,457,804	Open	15.9	303
8/25/2026	10:30:00	7.4	1.4650	1.9	1,457,826	Open	15.9	303
8/25/2026	10:45:00	7.4	1.4574	2.2	1,457,844	Open	16.1	304
8/25/2026	11:00:00	7.5	1.4498	3.4	1,457,865	Open	16.1	304
8/25/2026	11:15:00	7.5	0.3028	15.1	1,457,880	Open	16.2	304
8/25/2026	11:30:00	7.5	0.0000	4.1	1,457,892	Closed	16.3	306
8/25/2026	11:45:00	7.5	1.5407	5.1	1,457,895	Open	16.6	306
8/25/2026	12:00:00	7.5	1.6012	6.4	1,457,919	Open	16.4	304
8/25/2026	12:15:00	7.5	1.5861	7.9	1,457,939	Open	16.5	308
8/25/2026	12:30:00	7.5	1.5255	3.7	1,457,955	Open	16.6	306
8/25/2026	12:45:00	7.5	0.0000	2.7	1,457,964	Closed	16.9	304
8/25/2026	13:00:00	7.5	1.5672	4.3	1,457,971	Open	16.9	303
8/25/2026	13:15:00	7.5	1.5407	2.1	1,457,994	Open	16.9	304
8/25/2026	13:30:00	7.5	0.0000	1.2	1,458,008	Closed	17.1	306
8/25/2026	13:45:00	7.5	0.0000	1	1,458,008	Closed	17.6	308
8/25/2026	14:00:00	7.5	0.0000	1	1,458,008	Closed	18.5	311
8/25/2026	14:15:00	0	0.0000	0	0	Closed	0	0
8/25/2026	14:30:00	7.5	1.5331	1.8	1,458,041	Open	17.5	309
8/25/2026	14:45:00	7.5	1.5142	1.1	1,458,064	Open	17.4	309
8/25/2026	15:00:00	7.5	1.0107	1.1	1,458,082	Open	17.5	310
8/25/2026	15:15:00	7.5	0.0000	0.5	1,458,083	Closed	18	313
8/25/2026	15:30:00	7.5	1.0069	1.3	1,458,099	Open	17.7	313
8/25/2026	15:45:00	7.5	1.5142	1.3	1,458,110	Open	17.6	311



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	16:00:00	7.5	0.9880	5.1	1,458,125	Open	17.9	312
8/25/2026	16:15:00	7.5	1.4915	1.2	1,458,147	Open	17.6	311
8/25/2026	16:30:00	7.4	0.9388	1.9	1,458,166	Open	17.6	317
8/25/2026	16:45:00	7.4	1.4460	0.9	1,458,186	Open	17.5	317
8/25/2026	17:00:00	7.4	0.0000	1.8	1,458,204	Closed	17.5	319
8/25/2026	17:15:00	7.4	0.0000	1.3	1,458,204	Closed	18.1	323
8/25/2026	17:30:00	7.4	0.9085	0.9	1,458,208	Open	17.8	320
8/25/2026	17:45:00	7.4	1.3325	1.1	1,458,225	Closed	17.4	321
8/25/2026	18:00:00	7.3	0.9766	2.7	1,458,232	Open	17.3	324
8/25/2026	18:15:00	7.3	1.4233	1	1,458,251	Open	17.2	325
8/25/2026	18:30:00	7.3	0.2461	0.9	1,458,270	Closed	17	325
8/25/2026	18:45:00	7.3	0.0000	0.8	1,458,270	Closed	17.5	329
8/25/2026	19:00:00	7.3	0.8631	1.1	1,458,274	Closed	17.5	324
8/25/2026	19:15:00	7.3	0.5830	4.8	1,458,274	Closed	17.2	323
8/25/2026	19:30:00	7.3	1.5899	13.1	1,458,274	Closed	16.8	323
8/25/2026	19:45:00	7.2	0.1779	1.3	1,458,275	Closed	16.8	324
8/25/2026	20:00:00	7.2	1.7678	3.3	1,458,293	Open	16.8	324
8/25/2026	20:15:00	7.3	1.6315	2	1,458,316	Open	16.8	324
8/25/2026	20:30:00	7.2	0.0000	0.7	1,458,319	Closed	17.1	326
8/25/2026	20:45:00	7.2	0.0000	1	1,458,319	Closed	17.8	328
8/25/2026	21:00:00	7.2	1.6656	2.2	1,458,325	Open	17.2	323
8/25/2026	21:15:00	7.3	1.6315	1.2	1,458,349	Open	16.7	323
8/25/2026	21:30:00	7.2	0.0000	0.6	1,458,356	Closed	17.1	325
8/25/2026	21:45:00	7.2	0.0000	0.6	1,458,356	Closed	17.8	327
8/25/2026	22:00:00	7.3	1.6239	0.3	1,458,370	Open	16.8	323
8/25/2026	22:15:00	7.3	0.0000	0.5	1,458,391	Closed	16.8	323
8/25/2026	22:30:00	7.2	0.0000	0.2	1,458,391	Closed	17.4	324
8/25/2026	22:45:00	7.2	0.0000	0.2	1,458,391	Closed	17.9	324
8/25/2026	23:00:00	7.2	1.6618	0.3	1,458,392	Open	18	319
8/25/2026	23:15:00	7.3	1.6126	0.6	1,458,417	Open	17.1	319
8/25/2026	23:30:00	7.3	0.0000	0	1,458,420	Closed	17.7	321
8/25/2026	23:45:00	7.2	0.0000	0.1	1,458,420	Closed	18.4	324



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	0:00:00	7.2	0.0000	0	1,458,420	Closed	19.1	324
8/26/2026	0:15:00	7.2	0.0000	0	1,458,420	Closed	19.5	324
8/26/2026	0:30:00	7.2	0.0000	0	1,458,420	Closed	20.1	325
8/26/2026	0:45:00	7.3	1.6239	0	1,458,430	Open	18	315
8/26/2026	1:00:00	7.3	1.5066	1.1	1,458,453	Open	17.4	317
8/26/2026	1:15:00	7.2	0.0000	0.6	1,458,455	Closed	17.7	322
8/26/2026	1:30:00	7.2	0.0000	0.7	1,458,455	Closed	18.5	324
8/26/2026	1:45:00	7.2	0.0000	0.4	1,458,455	Closed	19	322
8/26/2026	2:00:00	7.2	1.5407	3	1,458,466	Open	17.1	318
8/26/2026	2:15:00	7.2	0.0000	1.5	1,458,486	Closed	16.6	321
8/26/2026	2:30:00	7.1	0.0000	3.7	1,458,486	Closed	17.1	322
8/26/2026	2:45:00	7.1	0.0000	2.4	1,458,486	Closed	17.7	324
8/26/2026	3:00:00	7.1	1.5217	1.4	1,458,505	Open	16.4	322
8/26/2026	3:15:00	7.1	0.3142	1.2	1,458,523	Closed	16.2	321
8/26/2026	3:30:00	7.1	0.0000	1.2	1,458,523	Closed	16.5	324
8/26/2026	3:45:00	7.1	0.0000	1.3	1,458,523	Closed	17.1	328
8/26/2026	4:00:00	7.1	1.5520	1.3	1,458,524	Open	17.5	327
8/26/2026	4:15:00	7.1	1.4687	2.4	1,458,546	Open	16.2	322
8/26/2026	4:30:00	7.1	0.0000	3.4	1,458,557	Closed	16.2	327
8/26/2026	4:45:00	7	0.0000	2.6	1,458,557	Closed	16.7	327
8/26/2026	5:00:00	7.1	1.0334	8.7	1,458,565	Open	16.3	327
8/26/2026	5:15:00	7.1	1.4801	4.5	1,458,586	Open	15.9	327
8/26/2026	5:30:00	7	0.0000	2.6	1,458,599	Closed	15.8	325
8/26/2026	5:45:00	7	0.0000	2.4	1,458,599	Closed	16.3	327
8/26/2026	6:00:00	7	0.0000	1.9	1,458,599	Closed	16.8	327
8/26/2026	6:15:00	7	1.4498	1.8	1,458,616	Open	15.6	324
8/26/2026	6:30:00	7	0.9842	3.8	1,458,637	Open	15.5	324
8/26/2026	6:45:00	7	0.0000	2.5	1,458,638	Closed	15.8	325
8/26/2026	7:00:00	7	0.5337	2.6	1,458,638	Closed	16.4	327
8/26/2026	7:15:00	7	1.4385	5	1,458,656	Open	15.4	324
8/26/2026	7:30:00	7	1.4347	6.1	1,458,677	Open	15.2	324
8/26/2026	7:45:00	7	0.0000	5.3	1,458,681	Closed	15.5	325



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	8:00:00	7	1.4687	4.5	1,458,686	Open	15.5	324
8/26/2026	8:15:00	7	1.4460	3.4	1,458,704	Open	15.2	324
8/26/2026	8:30:00	7	1.4309	4.4	1,458,725	Open	15.2	324
8/26/2026	8:45:00	7	0.0000	3.8	1,458,731	Closed	15.5	325
8/26/2026	9:00:00	7	0.7798	5.2	1,458,735	Open	15.5	324
8/26/2026	9:15:00	7	1.4536	6.1	1,458,752	Open	15.3	324
8/26/2026	9:30:00	7.1	0.9691	12.5	1,458,774	Open	15.4	324
8/26/2026	9:45:00	7.1	0.0000	8.7	1,458,786	Closed	15.6	326
8/26/2026	10:00:00	7.1	1.4536	5.9	1,458,789	Open	15.8	325
8/26/2026	10:15:00	7.1	1.4460	10.3	1,458,807	Open	15.8	325
8/26/2026	10:30:00	7.1	1.4309	3.9	1,458,829	Open	15.9	326
8/26/2026	10:45:00	7.1	1.5104	5.1	1,458,847	Open	16	325
8/26/2026	11:00:00	7.1	0.0000	5.1	1,458,861	Closed	16.2	326
8/26/2026	11:15:00	7.1	1.5444	5.9	1,458,861	Closed	16.7	327
8/26/2026	11:30:00	7.2	1.5331	14.2	1,458,883	Open	16.3	323
8/26/2026	11:45:00	7.2	1.4877	3	1,458,902	Open	16.3	323
8/26/2026	12:00:00	7.2	1.4763	0.9	1,458,925	Open	16.4	323
8/26/2026	12:15:00	7.2	0.0000	1.2	1,458,931	Closed	16.7	321
8/26/2026	12:30:00	7.2	1.5104	1.3	1,458,936	Open	16.8	320
8/26/2026	12:45:00	7.2	1.4877	1.8	1,458,954	Open	16.7	321
8/26/2026	13:00:00	7.2	0.0000	1.2	1,458,966	Closed	16.9	321
8/26/2026	13:15:00	7.1	0.0000	1.3	1,458,966	Closed	17.4	324
8/26/2026	13:30:00	7.2	1.4725	1.5	1,458,974	Open	17.1	321
8/26/2026	13:45:00	7.2	0.9842	3	1,458,992	Open	17.2	321
8/26/2026	14:00:00	7.2	1.4271	1.3	1,459,013	Open	17	319
8/26/2026	14:15:00	7.2	0.9426	1.7	1,459,032	Open	17	318
8/26/2026	14:30:00	7.2	1.3703	3.6	1,459,052	Open	16.9	319
8/26/2026	14:45:00	7.2	0.0000	3.8	1,459,061	Closed	17.2	318
8/26/2026	15:00:00	7.2	1.4006	3.9	1,459,064	Open	17.6	319
8/26/2026	15:15:00	7.2	0.8858	10.8	1,459,079	Open	17.2	319
8/26/2026	15:30:00	7.2	1.5142	4.2	1,459,098	Open	17.3	316
8/26/2026	15:45:00	7.2	0.9956	3.4	1,459,119	Open	17.4	316



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	16:00:00	7.2	0.0000	2.8	1,459,120	Closed	17.9	316
8/26/2026	16:15:00	7.2	0.0000	3.1	1,459,120	Closed	18.5	318
8/26/2026	16:30:00	7.2	1.4801	5.2	1,459,139	Open	17.5	313
8/26/2026	16:45:00	7.2	1.0107	5.9	1,459,158	Open	17.5	313
8/26/2026	17:00:00	7.2	1.4536	4.7	1,459,177	Open	17.4	313
8/26/2026	17:15:00	7.2	0.9691	4.8	1,459,199	Open	17.3	313
8/26/2026	17:30:00	7.2	0.0000	3.3	1,459,205	Closed	17.8	313
8/26/2026	17:45:00	7.2	1.4347	5.6	1,459,216	Open	17.4	311
8/26/2026	18:00:00	7.2	1.4157	5.2	1,459,233	Open	17.2	311
8/26/2026	18:15:00	7.2	1.3779	4.7	1,459,254	Open	17.1	308
8/26/2026	18:30:00	7.2	1.3817	5.3	1,459,271	Open	17.1	308
8/26/2026	18:45:00	7.2	1.3627	6.1	1,459,292	Open	17	305
8/26/2026	19:00:00	7.1	0.0000	5.5	1,459,299	Closed	17.4	307
8/26/2026	19:15:00	7.1	0.0000	4.6	1,459,299	Closed	17.8	306
8/26/2026	19:30:00	7.1	0.0000	22.4	1,459,299	Closed	17.9	301
8/26/2026	19:45:00	7.1	0.0000	11	1,459,299	Closed	17.9	108
8/26/2026	20:00:00	7.2	0.0000	33.1	1,459,299	Closed	17	299
8/26/2026	20:15:00	7.2	1.3287	20.5	1,459,300	Open	16.8	301
8/26/2026	20:30:00	7.2	1.5709	4.7	1,459,321	Open	16.3	303
8/26/2026	20:45:00	7.2	1.5672	1.8	1,459,344	Open	16.2	301
8/26/2026	21:00:00	7.2	0.0000	2.2	1,459,353	Closed	16.5	303
8/26/2026	21:15:00	7.1	0.0000	0.8	1,459,353	Closed	16.8	304
8/26/2026	21:30:00	7.1	0.0000	3	1,459,353	Closed	17.2	304
8/26/2026	21:45:00	7.2	1.5558	0.6	1,459,369	Open	15.7	289
8/26/2026	22:00:00	7.2	0.0000	0.5	1,459,387	Closed	15.7	291
8/26/2026	22:15:00	7.2	0.0000	0.4	1,459,387	Closed	16.3	293
8/26/2026	22:30:00	7.2	1.5823	0.5	1,459,397	Open	15.6	288
8/26/2026	22:45:00	7.2	1.5596	0.7	1,459,418	Open	15.6	291
8/26/2026	23:00:00	7.2	1.5596	0.5	1,459,441	Open	15.5	291
8/26/2026	23:15:00	7.2	0.0000	0.4	1,459,444	Closed	16	293
8/26/2026	23:30:00	7.2	1.2038	0.6	1,459,447	Open	15.8	294
8/26/2026	23:45:00	7.2	1.5407	0.9	1,459,470	Open	15.5	291



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	0:00:00	7.2	0.0000	0.9	1,459,471	Closed	15.9	293
8/27/2026	0:15:00	7.2	1.5596	0.9	1,459,482	Open	15.5	288
8/27/2026	0:30:00	7.2	1.5482	1.2	1,459,505	Open	15.4	286
8/27/2026	0:45:00	7.2	0.0000	1	1,459,513	Closed	15.6	293
8/27/2026	1:00:00	7.2	0.0000	1	1,459,513	Closed	16.1	294
8/27/2026	1:15:00	7.2	0.0000	0.7	1,459,513	Closed	16.6	289
8/27/2026	1:30:00	7.2	1.5785	1	1,459,526	Open	15.4	286
8/27/2026	1:45:00	7.2	1.5596	1.1	1,459,550	Open	15.2	286
8/27/2026	2:00:00	7.2	0.0000	3.8	1,459,561	Closed	15.1	294
8/27/2026	2:15:00	7.2	0.0000	1.3	1,459,561	Closed	15.3	107
8/27/2026	2:30:00	7.2	0.0000	1.6	1,459,561	Closed	15.9	107
8/27/2026	2:45:00	7.2	1.7754	6.3	1,459,562	Open	15.6	283
8/27/2026	3:00:00	7.2	1.7602	1.5	1,459,588	Open	15	294
8/27/2026	3:15:00	7.2	0.0000	0.8	1,459,608	Closed	15.2	298
8/27/2026	3:30:00	7.2	0.0000	0.4	1,459,608	Closed	15.9	301
8/27/2026	3:45:00	7.2	1.7602	1.5	1,459,614	Open	15.3	298
8/27/2026	4:00:00	7.2	0.0000	0.8	1,459,623	Closed	15.6	304
8/27/2026	4:15:00	7.1	0.0000	1.8	1,459,623	Closed	15.9	304
8/27/2026	4:30:00	7.2	1.6883	4.7	1,459,644	Open	15.1	286
8/27/2026	4:45:00	7.2	1.6277	4.7	1,459,669	Open	15.1	289
8/27/2026	5:00:00	7.1	0.0000	6.6	1,459,686	Closed	15.2	299
8/27/2026	5:15:00	7.2	1.6126	3	1,459,700	Open	15	288
8/27/2026	5:30:00	7.1	1.6504	3.4	1,459,709	Open	15	289
8/27/2026	5:45:00	7.1	1.6050	3.8	1,459,733	Open	14.8	289
8/27/2026	6:00:00	7.1	1.5293	5.7	1,459,757	Open	14.8	296
8/27/2026	6:15:00	7.1	0.0000	1.5	1,459,757	Closed	15.2	107
8/27/2026	6:30:00	7.1	0.0000	1.9	1,459,757	Closed	15.8	293
8/27/2026	6:45:00	7.1	1.6126	5.9	1,459,777	Open	14.8	293
8/27/2026	7:00:00	7.1	0.0000	5.2	1,459,794	Closed	14.9	309
8/27/2026	7:15:00	7.1	0.0000	1.8	1,459,794	Closed	15.4	298
8/27/2026	7:30:00	7.1	1.6353	6.1	1,459,804	Open	14.8	298
8/27/2026	7:45:00	7.1	1.1394	10.8	1,459,826	Open	14.7	299



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	8:00:00	7.1	0.0000	4	1,459,826	Closed	15.2	299
8/27/2026	8:15:00	7.1	1.6845	6.5	1,459,841	Open	14.7	299
8/27/2026	8:30:00	7.1	1.1470	14.4	1,459,864	Open	14.6	301
8/27/2026	8:45:00	7.1	0.0000	7.8	1,459,883	Closed	14.7	311
8/27/2026	9:00:00	7.1	1.6959	8.4	1,459,886	Open	14.8	299
8/27/2026	9:15:00	7.1	1.1129	18.8	1,459,909	Open	14.9	313
8/27/2026	9:30:00	7.1	1.6580	7.6	1,459,931	Open	14.9	298
8/27/2026	9:45:00	7.1	1.6202	8.9	1,459,955	Open	14.9	304
8/27/2026	10:00:00	7.1	0.3180	80.8	1,459,973	Closed	15	309
8/27/2026	10:15:00	7.2	1.7489	20.8	1,459,975	Open	15.4	306
8/27/2026	10:30:00	7.2	1.4877	8	1,459,996	Open	15.1	313
8/27/2026	10:45:00	7.2	0.7003	11.2	1,460,015	Open	15.1	313
8/27/2026	11:00:00	7.2	0.0000	10	1,460,020	Closed	15.5	314
8/27/2026	11:15:00	7.2	1.4877	11.4	1,460,040	Open	15.2	313
8/27/2026	11:30:00	7.2	0.9653	8.1	1,460,060	Open	15.2	313
8/27/2026	11:45:00	7.2	1.4650	5.6	1,460,081	Open	15.2	311
8/27/2026	12:00:00	7.2	0.0000	3.1	1,460,099	Closed	15.2	314
8/27/2026	12:15:00	7.2	0.0000	3	1,460,099	Closed	15.9	316
8/27/2026	12:30:00	7.2	1.4763	2.2	1,460,119	Open	15.3	313
8/27/2026	12:45:00	7.2	1.4498	3.7	1,460,141	Open	15.2	313
8/27/2026	13:00:00	7.2	0.0000	3.4	1,460,152	Closed	15.6	318
8/27/2026	13:15:00	7.2	1.4763	5.3	1,460,157	Open	15.4	316
8/27/2026	13:30:00	7.2	1.4612	2.2	1,460,179	Open	15.4	316
8/27/2026	13:45:00	7.2	0.0000	12.9	1,460,196	Closed	15.5	319
8/27/2026	14:00:00	7.2	1.4687	5.1	1,460,203	Open	15.5	318
8/27/2026	14:15:00	7.2	1.4460	3.5	1,460,224	Open	15.5	318
8/27/2026	14:30:00	7.2	0.0000	6.3	1,460,239	Closed	15.7	323
8/27/2026	14:45:00	7.2	0.0000	2.1	1,460,239	Closed	16.2	323
8/27/2026	15:00:00	7.2	1.4612	4.2	1,460,260	Open	15.6	321
8/27/2026	15:15:00	7.2	0.0000	3.6	1,460,275	Closed	15.8	325
8/27/2026	15:30:00	7.2	1.4801	6.9	1,460,281	Open	15.7	323
8/27/2026	15:45:00	7.2	1.3362	3.5	1,460,289	Closed	15.7	324



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	16:00:00	7.2	0.0000	2.1	1,460,302	Closed	15.9	326
8/27/2026	16:15:00	7.2	1.4915	5.6	1,460,314	Open	15.7	324
8/27/2026	16:30:00	7.2	1.4763	5.1	1,460,336	Open	15.7	321
8/27/2026	16:45:00	7.2	0.9577	7.8	1,460,355	Open	15.7	319
8/27/2026	17:00:00	7.2	1.4650	5	1,460,360	Open	15.8	318
8/27/2026	17:15:00	7.2	1.4877	9	1,460,382	Open	15.7	316
8/27/2026	17:30:00	7.2	0.6170	17.6	1,460,401	Open	15.6	314
8/27/2026	17:45:00	7.2	1.5444	12.2	1,460,421	Open	15.6	314
8/27/2026	18:00:00	7.2	1.4915	17	1,460,443	Open	15.5	314
8/27/2026	18:15:00	7.2	0.8517	9	1,460,462	Open	15.5	314
8/27/2026	18:30:00	7.2	1.3287	14.9	1,460,464	Open	15.8	313
8/27/2026	18:45:00	7.2	1.2984	6.4	1,460,483	Open	15.4	313
8/27/2026	19:00:00	7.2	0.8744	8.1	1,460,501	Open	15.3	313
8/27/2026	19:15:00	7.2	0.0000	7.1	1,460,503	Closed	15.7	107
8/27/2026	19:30:00	7.2	0.0000	2.3	1,460,503	Open	15.7	311
8/27/2026	19:45:00	7.2	0.0000	2.5	1,460,503	Closed	15.4	309
8/27/2026	20:00:00	7.2	1.7413	2.7	1,460,516	Open	15.3	313
8/27/2026	20:30:00	7.2	1.6769	1.9	1,460,567	Open	15	313
8/27/2026	20:45:00	7.2	0.0000	0.2	1,460,578	Closed	15.4	312
8/27/2026	21:00:00	7.2	1.7375	1.1	1,460,588	Open	15.3	312
8/27/2026	21:15:00	7.2	1.5672	0.6	1,460,612	Open	15.4	309
8/27/2026	21:30:00	7.2	1.6164	3.6	1,460,619	Open	15.7	309
8/27/2026	21:45:00	7.2	1.1886	1.5	1,460,638	Open	15.4	310
8/27/2026	22:00:00	7.2	1.6088	4.5	1,460,661	Open	15.3	313
8/27/2026	22:15:00	7.1	0.0000	3.2	1,460,682	Closed	15.3	316
8/27/2026	22:30:00	7.1	1.6088	3.7	1,460,684	Open	15.6	316
8/27/2026	22:45:00	7.1	1.5974	3.1	1,460,708	Open	15.4	313
8/27/2026	23:00:00	7.2	0.0000	7.8	1,460,713	Open	15.5	313
8/27/2026	23:15:00	7.2	1.3098	4.8	1,460,724	Open	15.4	312
8/27/2026	23:30:00	7.2	1.3287	35.9	1,460,733	Open	15.6	313
8/27/2026	23:45:00	7.2	1.4271	0.8	1,460,754	Open	15.3	309
8/28/2026	0:00:00	7.2	1.3855	0.5	1,460,775	Open	15.2	309



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	0:15:00	7.1	1.4650	4.6	1,460,775	Closed	15.7	311
8/28/2026	0:30:00	7.1	1.0864	0.7	1,460,793	Open	15.3	311
8/28/2026	0:45:00	7.1	1.4309	0.8	1,460,796	Open	15.3	313
8/28/2026	1:00:00	7.2	1.4195	1	1,460,817	Open	15	313
8/28/2026	1:15:00	7.2	1.4044	0.9	1,460,838	Open	15	313
8/28/2026	1:30:00	7.2	0.0000	10.4	1,460,845	Closed	15	107
8/28/2026	1:45:00	7.2	1.6542	0.4	1,460,859	Open	14.8	309
8/28/2026	2:00:00	7.2	1.6164	0.1	1,460,883	Open	14.9	310
8/28/2026	2:15:00	7.1	0.0000	0	1,460,885	Closed	16	110
8/28/2026	2:30:00	7.2	1.7072	0	1,460,897	Open	15.2	312
8/28/2026	2:45:00	7.1	0.0000	0	1,460,905	Closed	15.8	314
8/28/2026	3:00:00	7.2	1.6921	0	1,460,927	Open	15.1	310
8/28/2026	3:15:00	7.1	0.0000	5.8	1,460,939	Closed	15.7	111
8/28/2026	3:30:00	7.1	1.6921	0.3	1,460,943	Open	15.5	304
8/28/2026	3:45:00	7.1	1.6807	0.9	1,460,968	Open	15	310
8/28/2026	4:00:00	7.1	0.0000	402.2	1,460,974	Closed	15.4	109
8/28/2026	4:15:00	7.1	0.0000	1	1,460,974	Closed	17.5	109
8/28/2026	4:30:00	7.1	0.0000	1.6	1,460,974	Closed	15.1	315
8/28/2026	4:45:00	7.1	0.9615	0.7	1,460,987	Open	14.9	314
8/28/2026	5:00:00	7.1	1.5407	0.7	1,461,006	Open	14.7	312
8/28/2026	5:15:00	7.1	1.5142	0.7	1,461,029	Open	14.6	312
8/28/2026	5:30:00	7.1	0.0000	6.3	1,461,043	Closed	14.9	108
8/28/2026	5:45:00	7.1	1.1205	41.3	1,461,047	Open	14.7	310
8/28/2026	6:00:00	7.1	1.6012	2.7	1,461,069	Open	14.6	299
8/28/2026	6:15:00	7.1	1.6202	4.8	1,461,071	Closed	15.2	298
8/28/2026	6:30:00	7.1	1.5634	2.8	1,461,095	Open	14.6	298
8/28/2026	6:45:00	7.1	0.0000	7.2	1,461,108	Closed	14.9	107
8/28/2026	7:00:00	7.1	0.0000	1.2	1,461,117	Closed	14.6	296
8/28/2026	7:15:00	7.1	1.5709	1.4	1,461,134	Open	14.5	296
8/28/2026	7:30:00	7.1	0.0000	1.5	1,461,156	Closed	14.4	309
8/28/2026	7:45:00	7.1	0.0000	1.1	1,461,156	Closed	14.9	296
8/28/2026	8:00:00	7.1	1.6429	1.2	1,461,156	Open	14.8	297



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	8:15:00	7.1	1.5861	1.6	1,461,180	Open	14.5	296
8/28/2026	8:30:00	7.1	0.0000	1	1,461,188	Closed	15.1	296
8/28/2026	8:45:00	7.1	1.1167	5.4	1,461,205	Open	14.5	296
8/28/2026	9:00:00	7.1	0.0000	2.9	1,461,216	Closed	14.8	107
8/28/2026	9:15:00	7.1	1.4687	1.1	1,461,231	Open	14.6	294
8/28/2026	9:30:00	7.2	1.4536	1.5	1,461,253	Open	14.7	307
8/28/2026	9:45:00	7.2	0.9577	5.8	1,461,274	Open	14.8	309
8/28/2026	10:15:00	7.1	0.9880	4.8	1,461,295	Open	15	307
8/28/2026	10:30:00	7.2	1.4309	4.2	1,461,313	Open	15	306
8/28/2026	10:45:00	7.2	0.9918	10.3	1,461,317	Open	15.2	306
8/28/2026	11:00:00	7.2	1.2795	7	1,461,334	Open	15.1	309
8/28/2026	11:15:00	7.2	0.8517	12.2	1,461,352	Open	15.1	309
8/28/2026	11:30:00	7.2	1.4385	3.9	1,461,369	Open	15.1	306
8/28/2026	11:45:00	7.2	0.0000	4.4	1,461,389	Closed	15.1	108
8/28/2026	12:00:00	7.2	1.4385	4.5	1,461,392	Open	15.4	306
8/28/2026	12:15:00	7.2	0.6246	10.8	1,461,413	Open	15.2	308
8/28/2026	12:30:00	7.2	1.3627	5.8	1,461,426	Open	15.2	308
8/28/2026	12:45:00	7.2	0.9161	5.5	1,461,446	Open	15.2	308
8/28/2026	13:00:00	7.2	0.0000	3.9	1,461,449	Closed	16.2	109
8/28/2026	13:15:00	7.2	0.9388	6.6	1,461,458	Open	15.3	306
8/28/2026	13:30:00	7.2	1.3779	3.4	1,461,475	Open	15.3	306
8/28/2026	13:45:00	7.2	0.9199	6.6	1,461,495	Open	15.3	306
8/28/2026	14:00:00	7.2	1.3287	5.3	1,461,512	Open	15.3	306
8/28/2026	14:15:00	7.2	0.9009	8.2	1,461,532	Open	15.4	306
8/28/2026	14:30:00	7.2	0.0000	3.1	1,461,542	Closed	15.7	108
8/28/2026	14:45:00	7.2	0.9161	6.4	1,461,553	Open	15.4	304
8/28/2026	15:00:00	7.2	1.3325	13.6	1,461,570	Open	15.4	304
8/28/2026	15:15:00	7.2	0.8934	15.1	1,461,589	Open	15.4	304
8/28/2026	15:30:00	7.2	1.3060	10.9	1,461,605	Open	15.4	304
8/28/2026	15:45:00	7.2	0.0000	14.5	1,461,623	Closed	15.4	262
8/28/2026	16:00:00	7.1	0.0000	4	1,461,623	Closed	17	108
8/28/2026	16:15:00	7.1	0.8820	4.5	1,461,629	Open	15.7	301



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	16:30:00	7.2	1.2908	7.9	1,461,646	Open	15.5	303
8/28/2026	16:45:00	7.2	0.8858	5.3	1,461,664	Open	15.4	304
8/28/2026	17:00:00	7.2	1.2946	6.7	1,461,680	Open	15.4	304
8/28/2026	17:15:00	7.2	0.8706	5	1,461,699	Open	15.3	309
8/28/2026	17:30:00	7.2	0.5413	38.3	1,461,714	Closed	15.3	311
8/28/2026	17:45:00	7.2	0.3899	17	1,461,715	Open	15.8	311
8/28/2026	18:00:00	7.2	1.5104	2.7	1,461,728	Open	15.2	313
8/28/2026	18:15:00	7.2	1.0334	1.9	1,461,750	Open	15.2	313
8/28/2026	18:30:00	7.2	0.0000	0.8	1,461,763	Closed	15.4	108
8/28/2026	18:45:00	7.2	1.0675	1	1,461,768	Open	15.3	311
8/28/2026	19:00:00	7.2	1.5709	1.3	1,461,788	Open	15.1	311
8/28/2026	19:15:00	7.2	0.0000	1.2	1,461,802	Closed	15.4	107
8/28/2026	19:30:00	7.2	1.5709	1.1	1,461,803	Open	16	306
8/28/2026	19:45:00	7.2	1.0599	11.8	1,461,826	Open	15.1	309
8/28/2026	20:00:00	7.2	0.0000	1	1,461,830	Closed	16.8	111
8/28/2026	20:15:00	7.2	0.6473	2	1,461,846	Open	15.2	305
8/28/2026	20:30:00	7.2	0.0000	6.3	1,461,852	Open	15	308
8/28/2026	20:45:00	7.2	0.0000	4.3	1,461,852	Open	15.1	306
8/28/2026	21:00:00	7.2	1.3627	3	1,461,857	Open	14.9	309
8/28/2026	21:15:00	7.2	0.0000	2.4	1,461,875	Closed	14.8	107
8/28/2026	21:30:00	7.2	1.4650	7.7	1,461,883	Open	14.9	306
8/28/2026	21:45:00	7.2	0.4883	0	1,461,901	Open	15.4	112
8/28/2026	22:00:00	7.2	1.3892	0.7	1,461,919	Open	15.2	307
8/28/2026	22:15:00	7.2	0.0000	6.2	1,461,935	Open	15.1	303
8/28/2026	22:30:00	7.2	2.0744	39.4	1,461,936	Closed	15.1	308
8/28/2026	22:45:00	7.2	0.0000	34	1,461,936	Closed	15.1	309
8/28/2026	23:00:00	7.2	1.6239	76.6	1,461,945	Open	15.1	311
8/28/2026	23:15:00	7.2	1.5520	1.2	1,461,968	Open	15.3	313
8/28/2026	23:30:00	7.2	0.0000	0.8	1,461,982	Closed	15.3	107
8/28/2026	23:45:00	7.2	1.4422	1.2	1,461,993	Open	15.1	313
8/29/2026	0:00:00	7.2	1.3968	1.4	1,462,014	Open	15	314
8/29/2026	0:15:00	7.2	1.4120	1.4	1,462,036	Open	15	314



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	0:30:00	7.2	1.4195	1.9	1,462,052	Open	15.1	314
8/29/2026	0:45:00	7.2	1.4082	1.9	1,462,073	Open	15.1	316
8/29/2026	1:00:00	7.2	0.0000	1.7	1,462,078	Closed	16.7	108
8/29/2026	1:15:00	7.3	1.3968	1.8	1,462,099	Open	15.1	318
8/29/2026	1:30:00	7.3	0.9766	1.1	1,462,116	Open	15.2	323
8/29/2026	1:45:00	7.2	0.0000	1.3	1,462,123	Closed	16.1	108
8/29/2026	2:00:00	7.3	0.0000	40.6	1,462,137	Closed	15.2	319
8/29/2026	2:15:00	7.3	0.0000	9.6	1,462,137	Open	15.3	322
8/29/2026	2:30:00	7.3	0.0000	19.2	1,462,138	Closed	15.4	108
8/29/2026	2:45:00	7.3	1.6050	5.3	1,462,156	Open	15	319
8/29/2026	3:00:00	7.3	1.6277	6.2	1,462,180	Open	14.9	317
8/29/2026	3:15:00	7.3	1.5217	5.7	1,462,201	Open	14.8	315
8/29/2026	3:30:00	7.3	0.3104	2.8	1,462,205	Closed	14.8	314
8/29/2026	3:45:00	7.3	1.2870	3.3	1,462,205	Closed	14.7	315
8/29/2026	4:00:00	7.3	1.5747	5.6	1,462,218	Open	14.7	317
8/29/2026	4:15:00	7.2	1.5331	4.8	1,462,240	Open	14.7	320
8/29/2026	4:30:00	7.3	1.5217	4.3	1,462,262	Open	14.7	320
8/29/2026	4:45:00	7.3	0.5489	2.7	1,462,271	Closed	15	322
8/29/2026	5:00:00	7.3	1.5293	5.3	1,462,293	Open	15	322
8/29/2026	5:15:00	7.3	1.4347	6.4	1,462,314	Open	15.1	324
8/29/2026	5:30:00	7.2	0.0000	5.8	1,462,321	Closed	15.7	324
8/29/2026	5:45:00	7.3	1.4271	5.1	1,462,336	Open	15.2	320
8/29/2026	6:00:00	7.3	0.0000	12.8	1,462,351	Closed	15.5	255
8/29/2026	6:15:00	7.2	1.4725	11.9	1,462,352	Open	16.4	319
8/29/2026	6:30:00	7.3	1.4120	6.2	1,462,374	Open	15.4	324
8/29/2026	6:45:00	7.2	0.0000	9.2	1,462,381	Closed	15.8	325
8/29/2026	7:00:00	7.2	1.0978	6	1,462,388	Open	15.3	322
8/29/2026	7:15:00	7.2	1.4195	5.6	1,462,408	Open	15.3	324
8/29/2026	7:30:00	7.2	0.0000	4.5	1,462,414	Closed	16.3	323
8/29/2026	7:45:00	7.3	1.4271	4.7	1,462,425	Open	15.6	318
8/29/2026	8:00:00	7.2	1.1129	5.4	1,462,446	Open	15.4	319
8/29/2026	8:15:00	7.2	1.3741	32.1	1,462,446	Closed	15.8	322



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	8:30:00	7.2	1.2038	8.8	1,462,449	Closed	14.9	317
8/29/2026	8:45:00	7.2	1.5293	5	1,462,457	Open	14.8	317
8/29/2026	9:00:00	7.2	1.1394	2.5	1,462,479	Open	14.8	317
8/29/2026	9:15:00	7.2	1.4574	2.5	1,462,492	Closed	14.8	318
8/29/2026	9:30:00	7.2	1.2189	1.9	1,462,505	Open	14.9	317
8/29/2026	9:45:00	7.2	1.5444	6.3	1,462,525	Open	15	321
8/29/2026	10:00:00	7.2	1.1546	4.7	1,462,547	Open	15	319
8/29/2026	10:15:00	7.2	0.0000	3.9	1,462,559	Closed	15.1	321
8/29/2026	10:30:00	7.2	1.2303	4.8	1,462,564	Open	15.2	319
8/29/2026	10:45:00	7.3	0.2120	4.5	1,462,579	Closed	15.1	318
8/29/2026	11:00:00	7.2	1.1053	2.1	1,462,590	Open	15.2	318
8/29/2026	11:15:00	7.2	1.4725	4.5	1,462,609	Open	15.2	318
8/29/2026	11:30:00	7.2	1.1205	5.4	1,462,631	Open	15.2	318
8/29/2026	11:45:00	7.2	0.0000	5.5	1,462,641	Closed	15.6	108
8/29/2026	12:00:00	7.2	1.1243	7.4	1,462,653	Open	15.4	316
8/29/2026	12:15:00	7.2	1.4801	6	1,462,673	Open	15.5	316
8/29/2026	12:30:00	7.2	1.0713	7.3	1,462,694	Open	15.5	316
8/29/2026	12:45:00	7.2	1.4650	7.5	1,462,713	Open	15.6	316
8/29/2026	13:00:00	7.2	1.0826	12.8	1,462,734	Open	15.6	313
8/29/2026	13:15:00	7.3	1.2643	5.3	1,462,748	Closed	15.6	311
8/29/2026	13:30:00	7.2	1.0221	8.2	1,462,756	Open	15.7	311
8/29/2026	13:45:00	7.2	1.3665	2.3	1,462,774	Open	15.7	311
8/29/2026	14:00:00	7.3	1.0221	4.9	1,462,794	Open	15.8	311
8/29/2026	14:15:00	7.2	0.0000	1.5	1,462,798	Closed	16.3	108
8/29/2026	14:30:00	7.2	1.0334	6.8	1,462,812	Open	15.9	309
8/29/2026	14:45:00	7.3	1.4044	5.6	1,462,831	Open	15.9	309
8/29/2026	15:00:00	7.3	0.6624	20.4	1,462,851	Closed	15.9	310
8/29/2026	15:15:00	7.4	1.3173	5.4	1,462,851	Closed	16.1	309
8/29/2026	15:30:00	7.4	0.9918	7.7	1,462,872	Open	15.9	313
8/29/2026	15:45:00	7.4	1.4460	3.8	1,462,891	Open	15.8	313
8/29/2026	16:00:00	7.4	0.9880	4.1	1,462,912	Open	15.8	313
8/29/2026	16:15:00	7.4	1.4120	4.1	1,462,929	Open	15.8	313



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	16:30:00	7.4	0.9312	11.8	1,462,949	Open	15.8	313
8/29/2026	16:45:00	7.4	0.0000	9.9	1,462,963	Closed	16	108
8/29/2026	17:00:00	7.4	0.9350	13.5	1,462,966	Open	16.3	311
8/29/2026	17:15:00	7.4	1.4385	3.5	1,462,983	Open	16	313
8/29/2026	17:30:00	7.3	0.9501	10.3	1,463,003	Open	15.9	314
8/29/2026	17:45:00	7.3	1.3703	6.2	1,463,021	Open	15.9	314
8/29/2026	18:00:00	7.3	0.9539	8.6	1,463,041	Open	15.9	313
8/29/2026	18:15:00	7.3	1.3362	3.9	1,463,058	Open	16	313
8/29/2026	18:30:00	7.4	0.8934	9.3	1,463,078	Open	15.9	316
8/29/2026	18:45:00	7.3	1.3665	3.8	1,463,081	Open	16	311
8/29/2026	19:00:00	7.3	0.9539	9.6	1,463,101	Open	15.8	313
8/29/2026	19:15:00	7.4	0.0000	7.1	1,463,105	Open	15.6	311
8/29/2026	19:30:00	7.3	0.0000	5	1,463,107	Closed	15.5	298
8/29/2026	19:45:00	7.3	1.5293	8.5	1,463,118	Open	15.3	309
8/29/2026	20:00:00	7.3	1.5293	6.9	1,463,141	Open	15.1	306
8/29/2026	20:15:00	7.3	1.5217	8.5	1,463,164	Open	15.2	308
8/29/2026	20:30:00	7.4	1.5293	9.6	1,463,181	Open	15.4	304
8/29/2026	20:45:00	7.4	1.4725	6.1	1,463,204	Open	15.5	304
8/29/2026	21:00:00	7.3	0.8139	3.3	1,463,224	Open	15.7	304
8/29/2026	21:15:00	7.3	1.1924	4.6	1,463,231	Open	15.9	302
8/29/2026	21:30:00	7.3	1.1659	0.8	1,463,248	Open	15.8	300
8/29/2026	21:45:00	7.3	0.0000	72.4	1,463,264	Closed	15.7	304
8/29/2026	22:00:00	7.3	0.7949	18.1	1,463,271	Open	15.6	304
8/29/2026	22:15:00	7.3	1.3135	2.4	1,463,289	Open	15.5	304
8/29/2026	22:30:00	7.3	1.2605	2.7	1,463,308	Open	15.4	304
8/29/2026	22:45:00	7.3	0.8669	1.9	1,463,325	Open	15.4	304
8/29/2026	23:00:00	7.3	0.9804	0.9	1,463,343	Open	15.3	304
8/29/2026	23:15:00	7.3	1.3325	1.4	1,463,362	Open	15.2	304
8/29/2026	23:30:00	7.3	0.0000	0.5	1,463,376	Closed	15.6	109
8/29/2026	23:45:00	7.4	1.4195	1.9	1,463,380	Open	15.9	300
8/30/2026	0:00:00	7.4	1.0637	0.5	1,463,400	Open	15.8	300
8/30/2026	0:15:00	7.3	1.4309	0.3	1,463,405	Open	16.3	302



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	0:30:00	7.4	1.4195	2.2	1,463,426	Open	15.8	302
8/30/2026	0:45:00	7.4	1.4006	2.3	1,463,447	Open	15.8	300
8/30/2026	1:00:00	7.4	0.0000	2.2	1,463,466	Closed	15.9	300
8/30/2026	1:15:00	7.4	1.4044	2.2	1,463,472	Open	15.8	300
8/30/2026	1:30:00	7.4	0.0000	0.3	1,463,478	Closed	17.3	113
8/30/2026	1:45:00	7.4	1.4157	0	1,463,492	Open	15.9	297
8/30/2026	2:00:00	7.4	1.0864	0	1,463,512	Open	16	300
8/30/2026	2:15:00	7.4	0.9804	0	1,463,516	Open	16.2	299
8/30/2026	2:30:00	7.5	1.4195	0	1,463,535	Open	16.1	302
8/30/2026	2:45:00	7.5	1.4195	0	1,463,556	Open	16.2	302
8/30/2026	3:00:00	7.4	0.0000	0	1,463,573	Closed	16.6	300
8/30/2026	3:15:00	7.4	1.4347	0	1,463,577	Open	17	297
8/30/2026	3:30:00	7.5	1.4157	0	1,463,598	Open	16.3	302
8/30/2026	3:45:00	7.4	0.0000	0	1,463,611	Closed	16.9	300
8/30/2026	4:00:00	7.5	1.1016	0	1,463,623	Open	16.2	300
8/30/2026	4:15:00	7.5	1.4233	0	1,463,644	Open	16	300
8/30/2026	4:30:00	7.5	1.4195	0	1,463,665	Open	16.1	304
8/30/2026	4:45:00	7.5	0.0000	0.8	1,463,667	Closed	16.5	113
8/30/2026	5:00:00	7.5	1.4952	4.4	1,463,681	Open	16	305
8/30/2026	5:15:00	7.5	1.4763	5	1,463,703	Open	16	309
8/30/2026	5:30:00	7.5	1.4612	5.5	1,463,725	Open	16	308
8/30/2026	5:45:00	7.5	0.0000	6.9	1,463,734	Closed	16.6	112
8/30/2026	6:00:00	7.5	1.4612	7.2	1,463,748	Open	15.5	312
8/30/2026	6:15:00	7.5	1.4347	8.6	1,463,770	Open	15.2	309
8/30/2026	6:30:00	7.4	0.0000	9.1	1,463,786	Closed	15.3	307
8/30/2026	6:45:00	7.4	1.4460	10.4	1,463,790	Open	15	305
8/30/2026	7:00:00	7.4	1.4612	10.4	1,463,811	Open	14.9	305
8/30/2026	7:15:00	7.6	1.3590	35.5	1,463,824	Closed	15.6	107
8/30/2026	7:30:00	7.4	0.6700	7.5	1,463,829	Open	14.8	304
8/30/2026	7:45:00	7.5	0.0000	9.2	1,463,838	Open	14.7	302
8/30/2026	8:00:00	7.4	1.2757	1.6	1,463,854	Open	14.7	306
8/30/2026	8:15:00	7.4	1.2454	2.1	1,463,873	Open	14.7	304



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	8:30:00	7.4	0.8820	2.7	1,463,890	Open	14.7	301
8/30/2026	8:45:00	7.4	1.3249	2.4	1,463,909	Open	14.7	301
8/30/2026	9:00:00	7.4	1.3098	4.1	1,463,929	Open	14.7	300
8/30/2026	9:15:00	7.4	0.7798	3.5	1,463,948	Open	14.8	303
8/30/2026	9:30:00	7.5	0.8744	4	1,463,957	Open	14.8	306
8/30/2026	9:45:00	7.5	0.9350	2.2	1,463,979	Open	14.9	304
8/30/2026	10:00:00	7.4	1.4801	1.4	1,463,985	Open	15	309
8/30/2026	10:15:00	7.4	0.9842	1.8	1,464,007	Open	15	304
8/30/2026	10:30:00	7.4	1.4725	1.1	1,464,025	Open	15	306
8/30/2026	10:45:00	7.4	0.9426	3.6	1,464,047	Open	15	303
8/30/2026	11:00:00	7.4	0.0000	1.2	1,464,062	Closed	15.1	303
8/30/2026	11:15:00	7.4	0.0000	1.3	1,464,062	Closed	16	299
8/30/2026	11:30:00	7.4	1.4347	3	1,464,079	Open	15	301
8/30/2026	11:45:00	7.4	0.9123	6.7	1,464,100	Open	14.9	301
8/30/2026	12:00:00	7.4	1.3892	2.3	1,464,117	Open	15	301
8/30/2026	12:15:00	7.4	0.8820	7.3	1,464,137	Open	15	301
8/30/2026	12:30:00	7.4	1.3930	2.6	1,464,141	Open	15.1	299
8/30/2026	12:45:00	7.4	0.8896	5.6	1,464,161	Open	15	299
8/30/2026	13:00:00	7.4	1.3438	1.7	1,464,178	Open	15	303
8/30/2026	13:15:00	7.4	0.9312	6.1	1,464,198	Open	15.1	303
8/30/2026	13:30:00	7.4	1.4044	3.2	1,464,216	Open	15.1	303
8/30/2026	13:45:00	7.4	0.9161	7	1,464,221	Open	15.1	304
8/30/2026	14:00:00	7.4	1.4347	5.8	1,464,227	Open	15.2	306
8/30/2026	14:15:00	7.4	0.9274	9.5	1,464,248	Open	15.1	306
8/30/2026	14:30:00	7.4	1.4120	7	1,464,266	Open	15.2	308
8/30/2026	14:45:00	7.4	0.9161	21.5	1,464,286	Open	15.2	311
8/30/2026	15:00:00	7.4	1.3930	8.8	1,464,304	Open	15.2	309
8/30/2026	15:15:00	7.4	0.0000	7.1	1,464,307	Closed	16.9	108
8/30/2026	15:30:00	7.4	1.4271	6.7	1,464,319	Open	15.3	309
8/30/2026	15:45:00	7.4	0.4505	9.8	1,464,334	Open	15.2	311
8/30/2026	16:00:00	7.4	1.4195	5.4	1,464,349	Open	15.2	309
8/30/2026	16:15:00	7.4	0.9426	10.4	1,464,368	Open	15.2	309



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	16:30:00	7.4	1.4233	11.3	1,464,388	Open	15.2	309
8/30/2026	16:45:00	7.4	0.9501	13.6	1,464,406	Open	15.3	309
8/30/2026	17:00:00	7.4	1.3968	7.7	1,464,426	Open	15.2	309
8/30/2026	17:15:00	7.4	0.0000	8.2	1,464,442	Closed	15.3	309
8/30/2026	17:30:00	7.4	0.0000	4.2	1,464,442	Closed	16.4	306
8/30/2026	17:45:00	7.4	0.9577	7.9	1,464,455	Open	15.3	308
8/30/2026	18:00:00	7.4	1.4271	8.6	1,464,476	Open	15.3	306
8/30/2026	18:15:00	7.4	0.7117	9.2	1,464,492	Open	15.2	306
8/30/2026	18:30:00	7.4	1.3968	7.4	1,464,512	Open	15.2	306
8/30/2026	18:45:00	7.4	0.0000	9.2	1,464,528	Closed	15.3	306
8/30/2026	19:00:00	7.3	1.3362	9	1,464,536	Open	15.3	303
8/30/2026	19:15:00	7.3	0.9009	14.2	1,464,553	Open	15.3	303
8/30/2026	19:30:00	7.3	1.3892	8.6	1,464,574	Open	15.2	303
8/30/2026	19:45:00	7.7	0.1325	401	1,464,583	Open	16.5	108
8/30/2026	20:00:00	7.4	1.4044	10	1,464,594	Open	15.2	297
8/30/2026	20:15:00	7.3	0.0000	12.9	1,464,610	Open	15.2	277
8/30/2026	20:30:00	7.3	0.6965	1.5	1,464,620	Open	15	298
8/30/2026	20:45:00	7.3	1.2303	9.2	1,464,627	Open	15.2	293
8/30/2026	21:00:00	7.3	1.4044	7.9	1,464,636	Open	15.2	296
8/30/2026	21:15:00	7.3	1.3968	2.7	1,464,657	Open	14.8	294
8/30/2026	21:30:00	7.3	0.9577	2.6	1,464,675	Open	14.9	296
8/30/2026	21:45:00	7.3	0.0000	16.1	1,464,689	Open	14.8	296
8/30/2026	22:00:00	7.3	1.4233	1.4	1,464,704	Open	14.8	298
8/30/2026	22:15:00	7.3	1.4952	1	1,464,726	Open	14.8	298
8/30/2026	22:30:00	7.3	1.4650	1	1,464,748	Open	14.8	298
8/30/2026	22:45:00	7.3	0.0000	0.9	1,464,762	Closed	15.4	107
8/30/2026	23:00:00	7.3	1.5255	1.6	1,464,763	Open	15.7	294
8/30/2026	23:15:00	7.3	1.4990	1.4	1,464,786	Open	14.8	296
8/30/2026	23:30:00	7.3	1.0788	1.2	1,464,807	Closed	14.8	293
8/30/2026	23:45:00	7.3	1.5179	0.6	1,464,810	Open	15	294

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

Appendix B: CP2 WTP Data Logs



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	0:00:00	6.93	1.5407	0	269180	ON	14.2	229
8/24/2026	0:15:00	6.93	1.5444	0	269204	ON	14.2	228
8/24/2026	0:30:00	6.93	1.8397	0	269229	ON	14.1	229
8/24/2026	0:45:00	6.95	0.5678	0	269246	ON	14.3	231
8/24/2026	1:00:00	6.94	0.3710	0	269250	ON	15.2	229
8/24/2026	1:15:00	6.94	0.9426	0	269261	ON	14.3	231
8/24/2026	1:30:00	6.94	1.7943	0	269283	ON	14	233
8/24/2026	1:45:00	6.95	0.9539	0	269305	ON	14.2	233
8/24/2026	2:00:00	6.95	0.9993	0	269321	ON	14.2	235
8/24/2026	2:15:00	6.96	0.0000	0	269326	ON	15.3	0
8/24/2026	2:30:00	6.92	0.0227	0	269326	ON	16	221
8/24/2026	2:45:00	6.93	1.3098	0	269327	ON	16.3	235
8/24/2026	3:00:00	6.96	0.0303	0	269335	ON	14.9	238
8/24/2026	3:15:00	6.94	1.2870	0	269343	ON	14.3	234
8/24/2026	3:30:00	6.95	0.0189	0	269349	ON	15	237
8/24/2026	3:45:00	6.94	1.2605	0	269356	ON	14.3	233
8/24/2026	4:00:00	6.95	0.4050	0	269372	ON	14.5	234
8/24/2026	4:15:00	6.93	0.2120	0	269373	ON	15.5	236
8/24/2026	4:30:00	6.95	0.6095	0	269389	ON	14.2	236
8/24/2026	4:45:00	6.95	1.2492	0	269402	ON	14.2	232
8/24/2026	5:00:00	6.96	1.2643	0	269423	ON	14.2	236
8/24/2026	5:15:00	6.96	0.7874	0	269435	ON	14.3	236
8/24/2026	5:30:00	6.95	1.5444	0	269452	ON	14.3	236
8/24/2026	5:45:00	6.96	0.6927	0	269469	ON	14.4	237
8/24/2026	6:00:00	6.95	0.8441	0	269481	ON	14.3	239
8/24/2026	6:15:00	6.96	0.0265	0	269494	ON	14.5	240
8/24/2026	6:30:00	6.93	0.0265	0	269494	ON	15.4	240
8/24/2026	6:45:00	6.94	0.7798	0	269499	ON	14.6	239
8/24/2026	7:00:00	6.94	0.5905	0	269509	ON	15.1	241
8/24/2026	7:15:00	6.93	1.5974	0	269527	ON	14.2	241
8/24/2026	7:30:00	6.92	1.6996	0	269550	ON	14.2	241
8/24/2026	7:45:00	6.93	1.6542	0	269574	ON	14.2	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	8:00:00	6.95	0.6057	0	269588	ON	14.6	242
8/24/2026	8:15:00	6.93	0.0265	0	269589	ON	15.7	69
8/24/2026	8:30:00	6.94	1.7299	0	269606	ON	14.5	241
8/24/2026	8:45:00	6.95	1.6618	0	269630	ON	14.4	240
8/24/2026	9:00:00	6.96	1.6618	1	269653	ON	14.4	237
8/24/2026	9:15:00	6.97	0.3748	0	269671	ON	14.8	237
8/24/2026	9:30:00	6.81	0.0000	0	269672	ON	0	0
8/24/2026	9:45:00	6.94	1.8927	1	269678	ON	15	233
8/24/2026	10:00:00	6.96	0.2612	0	269686	ON	15.9	236
8/24/2026	10:15:00	6.94	0.2650	0	269690	ON	16.4	237
8/24/2026	10:30:00	6.97	0.1514	1	269694	ON	16.1	232
8/24/2026	10:45:00	6.96	1.8889	0	269703	ON	15.2	230
8/24/2026	11:00:00	6.97	0.0189	0	269712	ON	16.2	0
8/24/2026	11:15:00	6.96	0.0000	0	269712	ON	16.7	230
8/24/2026	11:30:00	7	0.5186	0	269728	ON	15.7	233
8/24/2026	11:45:00	6.98	0.0303	1	269729	ON	16.9	234
8/24/2026	12:00:00	6.95	0.1476	1	269729	ON	17.6	234
8/24/2026	12:15:00	7.01	1.6202	1	269749	ON	15.8	233
8/24/2026	12:30:00	7	1.9381	1	269774	ON	15.7	232
8/24/2026	12:45:00	6.98	1.6164	1	269800	ON	15.5	228
8/24/2026	13:00:00	6.98	0.5754	0	269823	ON	15.6	233
8/24/2026	13:15:00	6.99	0.0379	1	269825	ON	16.8	171
8/24/2026	13:30:00	6.97	0.0303	1	269826	ON	17.7	0
8/24/2026	13:45:00	6.93	1.2833	1	269826	ON	18.3	235
8/24/2026	14:00:00	6.97	1.6467	1	269850	ON	15.5	255
8/24/2026	14:15:00	6.98	1.9041	0	269874	ON	15.3	257
8/24/2026	14:30:00	6.99	1.6239	0	269902	ON	15.2	257
8/24/2026	14:45:00	7	1.7716	0	269930	ON	15.1	256
8/24/2026	15:00:00	7.01	1.9306	0	269954	ON	15.2	252
8/24/2026	15:15:00	7.02	0.5867	0	269977	ON	15.6	253
8/24/2026	15:30:00	6.99	0.0265	1	269979	ON	17	252
8/24/2026	15:45:00	7	1.8889	0	269994	ON	15.5	246



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/24/2026	16:00:00	7.03	0.6889	0	270018	ON	15.8	248
8/24/2026	16:15:00	6.99	0.0189	0	270021	ON	17.5	251
8/24/2026	16:30:00	7.02	0.2763	0	270028	ON	16.5	246
8/24/2026	16:45:00	7.02	0.0227	1	270028	ON	18.1	0
8/24/2026	17:00:00	6.99	0.2309	1	270030	ON	18.8	248
8/24/2026	17:15:00	6.96	0.2385	1	270034	ON	19.2	248
8/24/2026	17:30:00	7.02	0.6700	1	270043	ON	16.8	244
8/24/2026	17:45:00	7.01	1.9571	0	270068	ON	15.4	244
8/24/2026	18:00:00	7	1.6239	0	270092	ON	15.3	244
8/24/2026	18:15:00	6.99	1.6315	0	270118	ON	15.3	244
8/24/2026	18:30:00	7	0.7987	0	270136	ON	15.5	243
8/24/2026	18:45:00	7.02	0.0265	0	270140	ON	16.8	0
8/24/2026	19:00:00	6.99	1.4801	1	270145	ON	15.8	242
8/24/2026	19:15:00	7.01	1.6429	0	270173	ON	15.1	244
8/24/2026	19:30:00	7.01	1.8473	0	270195	ON	15	246
8/24/2026	19:45:00	7.03	1.6088	0	270222	ON	14.9	246
8/24/2026	20:00:00	7.03	1.6050	0	270244	ON	15	246
8/24/2026	20:15:00	7.04	0.0681	0	270254	ON	16.1	248
8/24/2026	20:30:00	7.04	1.2265	0	270263	ON	15.2	244
8/24/2026	20:45:00	7.04	1.1470	0	270285	ON	14.9	245
8/24/2026	21:00:00	7.04	0.0303	0	270291	ON	16.2	155
8/24/2026	21:15:00	7.02	0.0227	0	270291	ON	17.2	245
8/24/2026	21:30:00	7	0.0151	1	270292	ON	17.9	241
8/24/2026	21:45:00	7.01	1.4271	0	270297	ON	15.6	240
8/24/2026	22:00:00	7.01	1.5937	0	270320	ON	14.8	242
8/24/2026	22:15:00	6.99	1.5596	0	270342	ON	14.7	241
8/24/2026	22:30:00	7.01	0.1855	0	270363	ON	15	243
8/24/2026	22:45:00	6.98	1.4385	0	270369	ON	14.8	241
8/24/2026	23:00:00	6.99	1.5937	0	270394	ON	14.4	242
8/24/2026	23:15:00	6.99	1.8927	0	270418	ON	14.4	241
8/24/2026	23:30:00	7	0.5035	0	270438	ON	14.6	242
8/24/2026	23:45:00	7.02	0.0379	1	270440	ON	15.2	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	0:00:00	6.99	1.6012	0	270460	ON	14.3	243
8/25/2026	0:15:00	7.01	0.5905	0	270481	ON	14.6	245
8/25/2026	0:30:00	6.99	0.0303	0	270483	ON	15.9	246
8/25/2026	0:45:00	6.99	1.5482	0	270501	ON	14.4	245
8/25/2026	1:00:00	7.01	0.5640	0	270517	ON	14.6	244
8/25/2026	1:15:00	7.02	0.0189	0	270520	ON	14.9	244
8/25/2026	1:30:00	7.01	1.4460	0	270532	ON	14.3	247
8/25/2026	1:45:00	7.02	1.6050	0	270556	ON	14.3	248
8/25/2026	2:00:00	7.03	0.2385	0	270563	ON	15	249
8/25/2026	2:15:00	7.04	1.6012	1	270582	ON	14.2	251
8/25/2026	2:30:00	7.04	1.6088	0	270606	ON	14.2	250
8/25/2026	2:45:00	7.04	1.9192	0	270633	ON	14.1	251
8/25/2026	3:00:00	7.05	0.8555	0	270656	ON	14.2	249
8/25/2026	3:15:00	7.06	0.0151	0	270660	ON	15	251
8/25/2026	3:30:00	7.03	0.0265	0	270660	ON	15.4	250
8/25/2026	3:45:00	7.02	0.0000	0	270660	ON	16.1	249
8/25/2026	4:00:00	7.01	0.0000	0	270660	ON	16.4	249
8/25/2026	4:15:00	7	0.0000	1	270663	ON	16.7	250
8/25/2026	4:30:00	7.01	0.0114	0	270663	ON	17.4	0
8/25/2026	4:45:00	7.02	1.8284	0	270670	ON	14.7	242
8/25/2026	5:00:00	7.04	0.3407	0	270690	ON	14.6	246
8/25/2026	5:15:00	7.02	0.0000	0	270691	ON	15.2	246
8/25/2026	5:30:00	7.03	0.1893	0	270697	ON	14.9	244
8/25/2026	5:45:00	6.97	1.9192	0	270715	ON	14.1	243
8/25/2026	6:00:00	6.97	1.9192	0	270742	ON	13.9	245
8/25/2026	6:15:00	6.99	0.1779	0	270759	ON	14.2	249
8/25/2026	6:30:00	7	0.4505	0	270765	ON	14.3	248
8/25/2026	6:45:00	6.98	0.9426	0	270773	ON	14.2	250
8/25/2026	7:00:00	6.96	1.9268	0	270798	ON	13.9	251
8/25/2026	7:15:00	6.96	1.7148	0	270826	ON	13.9	252
8/25/2026	7:30:00	6.97	0.6927	0	270847	ON	14.1	253
8/25/2026	7:45:00	6.98	0.0492	0	270849	ON	15.1	0



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	8:00:00	6.98	1.4385	0	270856	ON	14.3	255
8/25/2026	8:15:00	7.01	1.5747	0	270879	ON	14.1	258
8/25/2026	8:30:00	7.03	1.5672	0	270903	ON	14.1	260
8/25/2026	8:45:00	7.06	1.5785	0	270927	ON	14.2	259
8/25/2026	9:00:00	7.07	1.5520	0	270951	ON	14.3	259
8/25/2026	9:15:00	7.08	0.7495	0	270975	ON	14.3	260
8/25/2026	9:30:00	7.08	0.0189	0	270978	ON	15.3	0
8/25/2026	9:45:00	7.06	0.0265	0	270978	ON	16.3	0
8/25/2026	10:00:00	7.07	1.4498	0	270988	ON	14.8	255
8/25/2026	10:15:00	7.08	1.8473	0	271012	ON	14.6	253
8/25/2026	10:30:00	7.08	0.0265	0	271027	ON	15	255
8/25/2026	10:45:00	7.06	0.0341	0	271027	ON	16.3	85
8/25/2026	11:00:00	7.05	0.0189	1	271027	ON	17.2	255
8/25/2026	11:15:00	7.03	0.1703	0	271030	ON	17.6	255
8/25/2026	11:30:00	7.01	0.1703	0	271033	ON	18.1	257
8/25/2026	11:45:00	7.02	1.5369	0	271047	ON	15.5	254
8/25/2026	12:00:00	7.01	1.5444	0	271071	ON	15.4	257
8/25/2026	12:15:00	7	1.5331	0	271095	ON	15.5	256
8/25/2026	12:30:00	6.99	1.5028	0	271118	ON	15.6	256
8/25/2026	12:45:00	6.99	1.5672	0	271143	ON	15.5	255
8/25/2026	13:00:00	7	0.7230	0	271161	ON	16.1	256
8/25/2026	13:15:00	6.99	0.0265	0	271166	ON	18.2	260
8/25/2026	13:30:00	6.98	1.3287	1	271168	ON	18.4	251
8/25/2026	13:45:00	7.03	1.4385	0	271189	ON	16.1	255
8/25/2026	14:00:00	7.02	1.3855	0	271209	ON	16.1	255
8/25/2026	14:15:00	7.04	1.3362	0	271232	ON	16	259
8/25/2026	14:30:00	7.06	1.2757	0	271252	ON	16.2	259
8/25/2026	14:45:00	7.07	1.1886	0	271274	ON	16.2	258
8/25/2026	15:00:00	7.08	1.1281	1	271291	ON	16.5	258
8/25/2026	15:15:00	7.09	0.3180	0	271304	ON	17.2	261
8/25/2026	15:30:00	7.08	0.0076	1	271306	ON	18.3	117
8/25/2026	15:45:00	7.06	0.5224	0	271311	ON	17.6	256



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/25/2026	16:00:00	7.05	0.4656	0	271318	ON	17.8	260
8/25/2026	16:15:00	7.05	0.0871	0	271326	ON	17.6	261
8/25/2026	16:30:00	7.07	1.9608	1	271346	ON	15.9	264
8/25/2026	16:45:00	7.08	1.4650	1	271359	ON	16.1	263
8/25/2026	17:00:00	7.06	0.9766	1	271370	ON	16.7	265
8/25/2026	17:15:00	7.04	0.9729	1	271384	ON	17.7	265
8/25/2026	17:30:00	7.04	1.9873	1	271401	ON	16	262
8/25/2026	17:45:00	7.06	1.9836	1	271432	ON	15.5	268
8/25/2026	18:00:00	7.06	1.6921	1	271460	ON	15.6	265
8/25/2026	18:15:00	7.07	1.9684	1	271490	ON	15.5	265
8/25/2026	18:30:00	7.08	1.6845	1	271520	ON	15.5	266
8/25/2026	18:45:00	7.08	1.9722	1	271547	ON	15.4	263
8/25/2026	19:00:00	7.09	0.8025	1	271569	ON	15.7	266
8/25/2026	19:15:00	7.1	0.6322	2	271577	ON	16.2	265
8/25/2026	19:30:00	7.09	1.9684	1	271604	ON	15.3	264
8/25/2026	19:45:00	7.08	1.6921	1	271632	ON	15.3	263
8/25/2026	20:00:00	7.08	0.5943	1	271646	ON	16.1	266
8/25/2026	20:15:00	7.08	1.5520	0	271657	ON	15.5	260
8/25/2026	20:30:00	7.05	1.9608	0	271684	ON	15.2	264
8/25/2026	20:45:00	7.05	1.6542	0	271711	ON	15.1	257
8/25/2026	21:00:00	7.04	0.8479	0	271732	ON	15.3	255
8/25/2026	21:15:00	7.02	0.0000	0	271737	ON	16.8	256
8/25/2026	21:30:00	7.01	0.0227	0	271737	ON	18.1	0
8/25/2026	21:45:00	7.02	1.8284	1	271746	ON	15.5	250
8/25/2026	22:00:00	7.01	1.8927	0	271773	ON	14.8	245
8/25/2026	22:15:00	7	1.6315	0	271800	ON	14.7	244
8/25/2026	22:30:00	7	0.5186	0	271818	ON	15.1	244
8/25/2026	22:45:00	7	1.2416	0	271827	ON	14.9	240
8/25/2026	23:00:00	6.97	1.6126	0	271849	ON	14.8	242
8/25/2026	23:15:00	6.99	0.0265	0	271855	ON	16.2	0
8/25/2026	23:30:00	6.96	1.7602	0	271869	ON	14.8	241
8/25/2026	23:45:00	6.96	1.7564	0	271899	ON	14.5	239



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	0:00:00	6.95	2.1690	0	271929	ON	14.5	240
8/26/2026	0:15:00	6.95	1.8208	0	271958	ON	14.5	241
8/26/2026	0:30:00	6.95	1.8208	0	271989	ON	14.5	238
8/26/2026	0:45:00	6.98	0.0265	0	271996	ON	15.3	241
8/26/2026	1:00:00	6.96	1.6807	0	272007	ON	14.7	239
8/26/2026	1:15:00	6.95	2.1501	0	272036	ON	14.4	240
8/26/2026	1:30:00	6.95	2.1463	0	272063	ON	14.4	241
8/26/2026	1:45:00	6.96	1.8056	0	272092	ON	14.4	239
8/26/2026	2:00:00	6.96	2.1350	0	272121	ON	14.3	240
8/26/2026	2:15:00	6.98	1.7791	0	272150	ON	14.4	240
8/26/2026	2:30:00	6.99	1.7943	0	272178	ON	14.4	239
8/26/2026	2:45:00	6.99	2.1236	0	272206	ON	14.3	241
8/26/2026	3:00:00	7	0.8404	0	272232	ON	14.5	245
8/26/2026	3:15:00	7.02	0.0265	0	272239	ON	15.5	0
8/26/2026	3:30:00	7	1.8473	0	272252	ON	14.5	238
8/26/2026	3:45:00	7.02	0.1855	0	272267	ON	14.8	238
8/26/2026	4:00:00	7.02	0.0265	0	272267	ON	15.2	237
8/26/2026	4:15:00	7.01	2.0706	0	272289	ON	14.3	238
8/26/2026	4:30:00	7.03	1.8056	0	272316	ON	14.3	241
8/26/2026	4:45:00	7.04	0.3104	0	272335	ON	14.7	243
8/26/2026	5:00:00	7.04	1.7451	0	272348	ON	14.4	244
8/26/2026	5:15:00	7.06	0.0341	0	272361	ON	15.1	0
8/26/2026	5:30:00	7.05	1.7905	0	272371	ON	14.5	246
8/26/2026	5:45:00	7.06	1.8132	0	272398	ON	14.3	247
8/26/2026	6:00:00	7.08	0.0189	0	272412	ON	14.8	247
8/26/2026	6:15:00	7.08	0.0416	1	272412	ON	15.3	247
8/26/2026	6:30:00	7.07	1.8094	0	272436	ON	14.4	247
8/26/2026	6:45:00	7.08	1.8208	0	272467	ON	14.3	248
8/26/2026	7:00:00	7.07	2.1615	1	272497	ON	14.3	247
8/26/2026	7:15:00	7.07	2.1350	1	272526	ON	14.3	247
8/26/2026	7:30:00	7.07	0.7457	0	272551	ON	14.4	247
8/26/2026	7:45:00	7.08	0.0000	0	272554	ON	15.3	243



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	8:00:00	7.06	0.0227	0	272554	ON	16.1	0
8/26/2026	8:15:00	7.06	0.2271	0	272555	ON	16.5	249
8/26/2026	8:30:00	7.04	0.0341	0	272556	ON	17	247
8/26/2026	8:45:00	7.04	0.5186	1	272557	ON	17.4	247
8/26/2026	9:00:00	7.03	0.5905	0	272566	ON	16.4	248
8/26/2026	9:15:00	7.02	0.5678	0	272576	ON	16.5	252
8/26/2026	9:30:00	7.03	0.6359	0	272586	ON	16.2	247
8/26/2026	9:45:00	7.04	1.7791	0	272606	ON	14.9	198
8/26/2026	10:00:00	7.05	2.1085	0	272634	ON	14.8	244
8/26/2026	10:15:00	7.06	0.3483	0	272653	ON	15.3	241
8/26/2026	10:30:00	7.07	0.0265	1	272654	ON	16.3	243
8/26/2026	10:45:00	7.04	2.0101	1	272662	ON	15.5	241
8/26/2026	11:00:00	7.05	2.0971	0	272691	ON	15.2	239
8/26/2026	11:15:00	7.07	0.3520	0	272709	ON	15.6	240
8/26/2026	11:30:00	7.06	0.0227	0	272711	ON	16.8	0
8/26/2026	11:45:00	7.04	1.7224	0	272730	ON	15.6	241
8/26/2026	12:00:00	7.05	1.7413	1	272759	ON	15.5	243
8/26/2026	12:15:00	7.05	2.0895	1	272788	ON	15.5	245
8/26/2026	12:30:00	7.06	1.0372	1	272814	ON	15.8	245
8/26/2026	12:45:00	7.06	0.0265	1	272820	ON	16.7	245
8/26/2026	13:00:00	7.04	2.0933	1	272832	ON	16	245
8/26/2026	13:15:00	7.05	0.1022	0	272848	ON	16.4	247
8/26/2026	13:30:00	7.04	0.1666	1	272852	ON	17	250
8/26/2026	13:45:00	7.04	0.0189	1	272852	ON	17.8	94
8/26/2026	14:00:00	7.01	0.0265	1	272852	ON	18.5	170
8/26/2026	14:15:00	7.02	1.6429	0	272868	ON	16.4	246
8/26/2026	14:30:00	7.04	1.6391	1	272892	ON	16.1	247
8/26/2026	14:45:00	7.05	1.6467	1	272916	ON	16.1	248
8/26/2026	15:00:00	7.05	0.6435	1	272941	ON	16.3	246
8/26/2026	15:15:00	7.06	0.4542	1	272944	ON	17.5	246
8/26/2026	15:30:00	7.04	0.2574	1	272951	ON	17.3	246
8/26/2026	15:45:00	7.02	0.7041	0	272956	ON	17.1	245



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/26/2026	16:00:00	7	0.2461	0	272963	ON	17.6	246
8/26/2026	16:15:00	7	1.9646	0	272978	ON	16.1	241
8/26/2026	16:30:00	7.01	1.8738	0	273003	ON	16.1	242
8/26/2026	16:45:00	7.03	0.0681	0	273020	ON	16.6	242
8/26/2026	17:00:00	7.03	0.9842	2	273023	ON	17.4	239
8/26/2026	17:15:00	7.03	0.0416	1	273030	ON	18.1	242
8/26/2026	17:30:00	7.01	1.4801	0	273035	ON	16.7	238
8/26/2026	17:45:00	6.98	1.8965	0	273060	ON	15.8	238
8/26/2026	18:00:00	6.97	1.0902	0	273085	ON	15.9	238
8/26/2026	18:15:00	6.96	1.5520	0	273108	ON	15.8	237
8/26/2026	18:30:00	6.96	1.7981	0	273133	ON	15.4	237
8/26/2026	18:45:00	6.97	1.0031	0	273150	ON	15.6	237
8/26/2026	19:00:00	6.98	0.0189	0	273155	ON	16.6	52
8/26/2026	19:15:00	6.99	0.7533	0	273167	ON	15.6	235
8/26/2026	19:30:00	6.98	1.4157	0	273186	ON	15.2	235
8/26/2026	19:45:00	7	1.2340	0	273208	ON	15.2	234
8/26/2026	20:00:00	7	1.2340	0	273224	ON	15.2	233
8/26/2026	20:15:00	7	1.6126	0	273244	ON	15.1	234
8/26/2026	20:30:00	7.02	0.6397	0	273258	ON	15.7	233
8/26/2026	20:45:00	7.02	0.1628	0	273269	ON	15.3	233
8/26/2026	21:00:00	7.01	1.5104	0	273272	ON	15.6	230
8/26/2026	21:15:00	7.02	2.0214	0	273299	ON	14.7	231
8/26/2026	21:30:00	7.02	0.3028	1	273306	ON	15.4	232
8/26/2026	21:45:00	7	2.0933	0	273320	ON	14.6	230
8/26/2026	22:00:00	7	1.5444	0	273350	ON	14.5	229
8/26/2026	22:15:00	6.98	2.0971	0	273377	ON	14.4	229
8/26/2026	22:30:00	6.97	2.0176	0	273405	ON	14.3	228
8/26/2026	22:45:00	6.98	1.7375	0	273432	ON	14.3	228
8/26/2026	23:00:00	7	1.1318	0	273460	ON	14.3	227
8/26/2026	23:15:00	7	0.0303	0	273465	ON	15.5	141
8/26/2026	23:30:00	7	0.1628	1	273469	ON	16.1	228
8/26/2026	23:45:00	6.98	0.7306	1	273472	ON	16.6	228



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	0:00:00	7	1.5255	0	273500	ON	14.3	227
8/27/2026	0:15:00	6.99	2.0858	0	273527	ON	14.2	227
8/27/2026	0:30:00	6.99	2.0744	0	273555	ON	14.1	225
8/27/2026	0:45:00	6.99	1.7564	0	273581	ON	14.1	226
8/27/2026	1:00:00	7	2.0328	0	273611	ON	14.1	227
8/27/2026	1:15:00	7.01	1.7110	0	273640	ON	14.1	227
8/27/2026	1:30:00	7.02	1.0145	0	273667	ON	14.1	228
8/27/2026	1:45:00	7.05	0.0000	0	273672	ON	14.8	153
8/27/2026	2:00:00	7.01	0.0265	0	273672	ON	15.7	170
8/27/2026	2:15:00	7.02	0.0795	0	273675	ON	16	226
8/27/2026	2:30:00	7	0.4391	0	273678	ON	16.3	228
8/27/2026	2:45:00	7.02	2.0138	0	273696	ON	14.2	228
8/27/2026	3:00:00	7.03	1.4801	0	273723	ON	14.1	228
8/27/2026	3:15:00	7.04	0.5224	0	273735	ON	14.4	227
8/27/2026	3:30:00	7.04	0.0227	0	273737	ON	15.3	0
8/27/2026	3:45:00	7.03	0.3369	1	273738	ON	15.6	228
8/27/2026	4:00:00	7.01	1.9987	1	273761	ON	14	227
8/27/2026	4:15:00	7	2.0366	0	273788	ON	13.9	227
8/27/2026	4:30:00	7.02	0.8479	0	273810	ON	14	227
8/27/2026	4:45:00	7.03	0.6435	1	273817	ON	14.2	226
8/27/2026	5:00:00	7.02	0.0303	0	273822	ON	14.9	226
8/27/2026	5:15:00	7.01	0.8176	1	273829	ON	15.2	226
8/27/2026	5:30:00	7.02	0.8101	2	273844	ON	14.1	224
8/27/2026	5:45:00	7.03	1.6050	1	273860	ON	14	227
8/27/2026	6:00:00	7.05	2.0214	1	273887	ON	13.9	228
8/27/2026	6:15:00	7.07	2.0593	1	273917	ON	13.8	230
8/27/2026	6:30:00	7.08	0.7912	1	273938	ON	14	230
8/27/2026	6:45:00	7.09	0.4883	1	273945	ON	14.5	232
8/27/2026	7:00:00	7.09	0.5413	2	273952	ON	14.5	230
8/27/2026	7:15:00	7.11	2.0517	2	273979	ON	13.9	236
8/27/2026	7:30:00	7.12	1.6959	1	274007	ON	13.9	238
8/27/2026	7:45:00	7.14	0.0151	2	274023	ON	14.2	237



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	8:00:00	7.11	0.0303	1	274023	ON	14.9	39
8/27/2026	8:15:00	7.1	0.0265	2	274023	ON	15.4	184
8/27/2026	8:30:00	7.1	0.1022	2	274023	ON	15.9	238
8/27/2026	8:45:00	7.11	0.0833	1	274026	ON	15.6	237
8/27/2026	9:00:00	7.08	0.1136	1	274028	ON	15.8	238
8/27/2026	9:15:00	7.1	0.5905	1	274032	ON	15.6	233
8/27/2026	9:30:00	7.14	1.6769	1	274054	ON	14.2	234
8/27/2026	9:45:00	7.14	1.9987	1	274083	ON	14.1	235
8/27/2026	10:00:00	7.15	0.0946	1	274098	ON	14.4	234
8/27/2026	10:15:00	7.15	0.4807	1	274104	ON	14.6	234
8/27/2026	10:30:00	7.11	1.8927	1	274110	ON	14.4	232
8/27/2026	10:45:00	7.1	1.6732	1	274137	ON	14.2	233
8/27/2026	11:00:00	7.09	0.9993	0	274162	ON	14.3	233
8/27/2026	11:15:00	7.1	0.3710	1	274166	ON	14.9	234
8/27/2026	11:30:00	7.11	0.0189	1	274173	ON	15.4	0
8/27/2026	11:45:00	7.09	0.0189	1	274173	ON	15.9	45
8/27/2026	12:00:00	7.07	0.0227	1	274173	ON	16.2	233
8/27/2026	12:15:00	7.05	1.5974	1	274176	ON	15.2	232
8/27/2026	12:30:00	7.04	1.6769	1	274200	ON	14.4	233
8/27/2026	12:45:00	7.05	1.9684	0	274224	ON	14.3	235
8/27/2026	13:00:00	7.06	1.6921	0	274254	ON	14.3	236
8/27/2026	13:15:00	7.09	1.0902	1	274280	ON	14.5	238
8/27/2026	13:30:00	7.08	0.4315	1	274286	ON	15	235
8/27/2026	13:45:00	7.07	0.5035	1	274293	ON	15.6	237
8/27/2026	14:00:00	7.06	0.0908	1	274295	ON	16.1	238
8/27/2026	14:15:00	7.09	1.6391	1	274315	ON	14.7	238
8/27/2026	14:30:00	7.11	0.4883	1	274336	ON	14.9	239
8/27/2026	14:45:00	7.09	0.0000	1	274337	ON	15.9	241
8/27/2026	15:00:00	7.08	0.0000	1	274337	ON	16.4	239
8/27/2026	15:15:00	7.05	0.0000	1	274340	ON	16.8	240
8/27/2026	15:30:00	7.08	0.0000	1	274340	ON	17.4	242
8/27/2026	15:45:00	7.05	0.0151	1	274340	ON	17.6	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/27/2026	16:00:00	7.05	0.0341	1	274340	ON	17.8	241
8/27/2026	16:15:00	7.04	0.0114	1	274340	ON	18	241
8/27/2026	16:30:00	7.04	0.2574	1	274343	ON	16.8	242
8/27/2026	16:45:00	7.04	2.0820	1	274365	ON	14.9	239
8/27/2026	17:00:00	7.04	2.2069	0	274395	ON	14.7	244
8/27/2026	17:15:00	7.07	0.5981	0	274414	ON	14.9	245
8/27/2026	17:30:00	7.05	0.0341	1	274417	ON	16	246
8/27/2026	17:45:00	7.02	2.0441	0	274444	ON	14.5	253
8/27/2026	18:00:00	7.03	2.0441	0	274472	ON	14.4	254
8/27/2026	18:15:00	7.04	1.7224	0	274501	ON	14.4	253
8/27/2026	18:30:00	7.05	2.0403	0	274531	ON	14.4	255
8/27/2026	18:45:00	7.07	2.0214	0	274558	ON	14.4	255
8/27/2026	19:00:00	7.1	0.6852	0	274582	ON	14.6	255
8/27/2026	19:15:00	7.1	0.0227	1	274590	ON	15	252
8/27/2026	19:30:00	7.08	2.0290	0	274611	ON	14.4	255
8/27/2026	19:45:00	7.09	1.9873	0	274638	ON	14.4	256
8/27/2026	20:00:00	7.09	1.6580	0	274667	ON	14.3	255
8/27/2026	20:15:00	7.1	0.6624	0	274685	ON	14.5	255
8/27/2026	20:30:00	7.09	0.0265	0	274686	ON	15.4	252
8/27/2026	20:45:00	7.08	0.0114	0	274686	ON	16.1	0
8/27/2026	21:00:00	7.08	0.0341	0	274686	ON	16.4	252
8/27/2026	21:15:00	7.07	1.5066	0	274693	ON	14.9	250
8/27/2026	21:30:00	7.08	0.3861	0	274705	ON	14.8	252
8/27/2026	21:45:00	7.18	0.0189	779	274709	ON	15.3	0
8/27/2026	22:00:00	7.05	0.7230	0	274716	ON	14.8	248
8/27/2026	22:15:00	7.03	1.9646	0	274730	ON	14.4	247
8/27/2026	22:30:00	7.03	1.6580	0	274757	ON	14.3	246
8/27/2026	22:45:00	7.03	1.6126	0	274784	ON	14.3	245
8/27/2026	23:00:00	7.02	2.0479	1	274812	ON	14.2	244
8/27/2026	23:15:00	7.02	1.8549	0	274839	ON	14.3	241
8/27/2026	23:30:00	7.04	0.2006	0	274858	ON	14.4	242
8/27/2026	23:45:00	7.03	0.0265	0	274858	ON	15.1	242



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	0:00:00	7.01	0.1855	0	274858	ON	15.6	243
8/28/2026	0:15:00	7.05	0.5678	0	274871	ON	14.6	241
8/28/2026	0:30:00	7.04	0.1211	0	274872	ON	15.3	243
8/28/2026	0:45:00	7.03	1.6202	0	274895	ON	14.2	243
8/28/2026	1:00:00	7.02	1.5747	0	274921	ON	14.1	241
8/28/2026	1:15:00	7.02	1.8321	0	274947	ON	14.1	241
8/28/2026	1:30:00	7.02	1.7299	0	274970	ON	14.2	242
8/28/2026	1:45:00	7.04	1.4082	0	274996	ON	14.2	243
8/28/2026	2:00:00	7.05	0.0000	0	275001	ON	15	0
8/28/2026	2:15:00	7.04	0.0189	1	275001	ON	15.3	164
8/28/2026	2:30:00	7.05	0.3634	0	275005	ON	15.2	243
8/28/2026	2:45:00	7.04	0.0303	0	275007	ON	15.7	246
8/28/2026	3:00:00	7.01	1.1470	0	275015	ON	14.5	243
8/28/2026	3:15:00	6.99	1.8132	1	275032	ON	14.2	243
8/28/2026	3:30:00	6.97	2.2031	0	275063	ON	13.9	243
8/28/2026	3:45:00	7	0.9085	0	275087	ON	14	244
8/28/2026	4:00:00	7.01	0.4240	0	275095	ON	14.5	244
8/28/2026	4:15:00	7	2.2485	1	275120	ON	13.9	242
8/28/2026	4:30:00	7.04	0.0151	1	275129	ON	14.3	242
8/28/2026	4:45:00	7.02	1.8208	0	275141	ON	14	241
8/28/2026	5:00:00	7.02	1.1356	1	275167	ON	14	242
8/28/2026	5:15:00	7.03	0.5489	0	275179	ON	14.3	242
8/28/2026	5:30:00	6.99	2.0025	1	275200	ON	13.9	244
8/28/2026	5:45:00	7.02	0.6776	0	275217	ON	14.1	242
8/28/2026	6:00:00	7.02	0.0227	1	275221	ON	14.4	242
8/28/2026	6:15:00	6.99	2.2410	0	275247	ON	13.9	243
8/28/2026	6:30:00	6.99	2.2258	0	275278	ON	13.8	244
8/28/2026	6:45:00	6.99	2.2296	0	275309	ON	13.9	243
8/28/2026	7:00:00	7.02	0.4050	0	275330	ON	14.1	244
8/28/2026	7:15:00	7.02	0.7192	1	275335	ON	14.2	243
8/28/2026	7:30:00	7.01	0.0000	0	275347	ON	14.4	245
8/28/2026	7:45:00	7.01	0.0227	0	275347	ON	14.9	244



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	8:00:00	7.01	0.0189	1	275348	ON	15.6	244
8/28/2026	8:15:00	7	0.0227	1	275348	ON	15.9	244
8/28/2026	8:30:00	7	0.2120	1	275349	ON	16.1	245
8/28/2026	8:45:00	6.98	0.2536	1	275353	ON	16.3	246
8/28/2026	9:00:00	7.02	0.3483	2	275361	ON	14.8	243
8/28/2026	9:15:00	7.01	1.5899	1	275372	ON	14.3	243
8/28/2026	9:30:00	7.02	1.6921	1	275400	ON	14.2	244
8/28/2026	9:45:00	7.01	2.0101	1	275425	ON	14.2	244
8/28/2026	10:00:00	7.02	1.6883	0	275452	ON	14.3	242
8/28/2026	10:15:00	7.04	0.1060	1	275465	ON	14.8	242
8/28/2026	10:30:00	7.01	1.9192	1	275472	ON	14.5	241
8/28/2026	10:45:00	7	1.6845	0	275500	ON	14.3	242
8/28/2026	11:00:00	6.99	1.7526	0	275528	ON	14.2	242
8/28/2026	11:15:00	6.98	1.7375	1	275555	ON	14.2	239
8/28/2026	11:30:00	7.01	0.4126	0	275575	ON	14.5	241
8/28/2026	11:45:00	6.99	0.0227	1	275576	ON	15.4	240
8/28/2026	12:00:00	6.98	0.0265	1	275576	ON	15.8	241
8/28/2026	12:15:00	6.97	0.0227	1	275576	ON	16.3	241
8/28/2026	12:30:00	6.98	1.7678	1	275601	ON	14.3	240
8/28/2026	12:45:00	6.99	1.7451	1	275628	ON	14.2	242
8/28/2026	13:00:00	6.99	1.7564	0	275655	ON	14.2	243
8/28/2026	13:15:00	7	2.0668	0	275684	ON	14.2	242
8/28/2026	13:30:00	7.04	0.1741	1	275697	ON	14.7	242
8/28/2026	13:45:00	7.02	0.0189	1	275697	ON	15.5	242
8/28/2026	14:00:00	7.02	1.6202	1	275706	ON	14.6	241
8/28/2026	14:15:00	7.03	0.6662	0	275725	ON	14.6	244
8/28/2026	14:30:00	7.03	0.2725	1	275730	ON	15.1	242
8/28/2026	14:45:00	7.01	0.7230	1	275736	ON	14.7	239
8/28/2026	15:00:00	7.02	0.9161	1	275745	ON	14.6	241
8/28/2026	15:15:00	7.02	0.0227	1	275748	ON	15.5	202
8/28/2026	15:30:00	7	0.0416	1	275748	ON	16.1	240
8/28/2026	15:45:00	7	1.6239	1	275757	ON	14.8	240



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/28/2026	16:00:00	6.99	1.7186	1	275784	ON	14.3	241
8/28/2026	16:15:00	6.99	1.6921	1	275810	ON	14.3	243
8/28/2026	16:30:00	7	1.6883	1	275834	ON	14.2	242
8/28/2026	16:45:00	7.02	0.3975	1	275851	ON	14.6	242
8/28/2026	17:00:00	7.02	0.0189	1	275852	ON	15.7	245
8/28/2026	17:15:00	7.02	0.6473	1	275861	ON	14.7	241
8/28/2026	17:30:00	7.04	0.0341	1	275869	ON	15.5	0
8/28/2026	17:45:00	7.02	0.1855	1	275870	ON	15.9	243
8/28/2026	18:00:00	7.03	2.0138	1	275886	ON	14.4	246
8/28/2026	18:15:00	7.04	1.6845	1	275914	ON	14.2	250
8/28/2026	18:30:00	7.04	1.6996	1	275943	ON	14.1	250
8/28/2026	18:45:00	7.03	1.9911	1	275969	ON	14.1	247
8/28/2026	19:00:00	7.05	0.0871	1	275982	ON	14.6	248
8/28/2026	19:15:00	7.04	1.9533	1	275990	ON	14.4	246
8/28/2026	19:30:00	7.04	1.6883	1	276017	ON	14.2	245
8/28/2026	19:45:00	7.03	1.9987	1	276042	ON	14.1	246
8/28/2026	20:00:00	7.04	1.6845	1	276067	ON	14.1	243
8/28/2026	20:15:00	7.05	1.9873	1	276093	ON	14.1	245
8/28/2026	20:30:00	7.08	0.0946	1	276106	ON	14.4	246
8/28/2026	20:45:00	7.07	0.0151	1	276108	ON	14.9	246
8/28/2026	21:00:00	7.06	0.1363	1	276108	ON	15.3	246
8/28/2026	21:15:00	7.05	0.1666	1	276111	ON	15.6	247
8/28/2026	21:30:00	7.04	0.0227	1	276113	ON	15.9	246
8/28/2026	21:45:00	7.04	0.3445	1	276113	ON	16.1	248
8/28/2026	22:00:00	7.07	0.3710	1	276121	ON	14.9	248
8/28/2026	22:15:00	7.03	1.9381	1	276127	ON	15.2	250
8/28/2026	22:30:00	7.05	1.7034	1	276154	ON	13.9	243
8/28/2026	22:45:00	7.04	1.6996	1	276180	ON	13.9	242
8/28/2026	23:00:00	7.04	1.6694	1	276207	ON	13.9	241
8/28/2026	23:15:00	7.03	1.6618	0	276231	ON	13.9	241
8/28/2026	23:30:00	7.05	0.1287	0	276247	ON	14.2	239
8/28/2026	23:45:00	7.06	0.6587	1	276249	ON	14.3	239



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	0:00:00	7.06	0.0303	1	276255	ON	14.9	242
8/29/2026	0:15:00	7.04	1.5407	1	276262	ON	14.3	244
8/29/2026	0:30:00	7.06	0.6776	1	276283	ON	14	250
8/29/2026	0:45:00	7.07	0.0341	1	276286	ON	15.2	252
8/29/2026	1:00:00	7.06	0.4013	1	276287	ON	15.7	251
8/29/2026	1:15:00	7.06	1.6088	1	276302	ON	14	253
8/29/2026	1:30:00	7.09	1.6656	1	276326	ON	13.9	259
8/29/2026	1:45:00	7.08	1.6732	1	276353	ON	13.8	257
8/29/2026	2:00:00	7.08	1.6467	1	276377	ON	13.9	256
8/29/2026	2:15:00	7.09	0.7912	1	276402	ON	13.9	256
8/29/2026	2:30:00	7.1	0.2915	1	276407	ON	14.2	254
8/29/2026	2:45:00	7.09	0.0000	1	276407	ON	15.2	255
8/29/2026	3:00:00	7.08	0.0189	2	276407	ON	15.8	233
8/29/2026	3:15:00	7.07	0.0227	1	276407	ON	16.3	0
8/29/2026	3:30:00	7.08	0.0416	1	276407	ON	16	255
8/29/2026	3:45:00	7.07	0.2082	1	276409	ON	16.2	255
8/29/2026	4:00:00	7.06	0.7117	1	276417	ON	14.3	252
8/29/2026	4:15:00	7.07	1.6959	1	276443	ON	13.8	254
8/29/2026	4:30:00	7.06	1.9684	1	276468	ON	13.8	256
8/29/2026	4:45:00	7.06	1.6467	1	276494	ON	13.8	254
8/29/2026	5:00:00	7.05	1.6126	1	276521	ON	13.7	254
8/29/2026	5:15:00	7.07	0.0341	1	276529	ON	14.2	252
8/29/2026	5:30:00	7.07	0.7382	2	276531	ON	14.3	252
8/29/2026	5:45:00	7.05	1.8624	1	276556	ON	13.8	253
8/29/2026	6:00:00	7.06	1.5899	1	276581	ON	13.8	254
8/29/2026	6:15:00	7.08	0.0946	1	276596	ON	13.9	254
8/29/2026	6:30:00	7.07	1.4157	1	276604	ON	13.8	255
8/29/2026	6:45:00	7.07	1.5596	1	276629	ON	13.7	256
8/29/2026	7:00:00	7.06	1.8284	1	276653	ON	13.7	260
8/29/2026	7:15:00	7.07	1.5066	1	276679	ON	13.7	260
8/29/2026	7:30:00	7.07	1.4877	1	276704	ON	13.7	259
8/29/2026	7:45:00	7.07	1.7413	1	276727	ON	13.8	261



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	8:00:00	7.08	1.3855	1	276752	ON	13.8	262
8/29/2026	8:15:00	7.1	0.2082	1	276762	ON	13.8	261
8/29/2026	8:30:00	7.1	0.0341	1	276764	ON	14.1	261
8/29/2026	8:45:00	7.09	0.0416	1	276764	ON	14.2	261
8/29/2026	9:00:00	7.08	0.0227	1	276764	ON	14.3	262
8/29/2026	9:15:00	7.07	0.0379	1	276764	ON	14.5	262
8/29/2026	9:30:00	7.07	1.3968	1	276772	ON	14.1	259
8/29/2026	9:45:00	7.08	1.7564	1	276795	ON	14	255
8/29/2026	10:00:00	7.07	1.7640	1	276824	ON	14	253
8/29/2026	10:15:00	7.07	0.3785	1	276844	ON	14.2	252
8/29/2026	10:30:00	7.05	0.8971	1	276854	ON	14.3	250
8/29/2026	10:45:00	7.05	0.3785	1	276866	ON	14.5	248
8/29/2026	11:00:00	7.03	0.4202	1	276873	ON	14.6	248
8/29/2026	11:15:00	7.02	1.6996	1	276886	ON	14.4	246
8/29/2026	11:30:00	7.03	1.7489	1	276913	ON	14.4	247
8/29/2026	11:45:00	0	0.0000	0	276919	ON	0	0
8/29/2026	12:00:00	0	0.0000	0	276919	ON	0	0
8/29/2026	12:30:00	7.04	0.0189	2	276919	OFF	15.6	0
8/29/2026	12:45:00	7.04	0.0265	1	276919	OFF	15.8	247
8/29/2026	13:00:00	7.04	0.0151	1	276919	OFF	15.9	246
8/29/2026	13:15:00	7.04	0.0189	2	276919	OFF	16.4	247
8/29/2026	13:30:00	7.01	0.0454	2	276919	OFF	17.2	248
8/29/2026	13:45:00	7.03	1.7564	2	276945	ON	15.3	251
8/29/2026	14:00:00	7.02	1.7489	2	276974	ON	15.1	253
8/29/2026	14:15:00	7.01	1.7905	1	277004	ON	15.1	254
8/29/2026	14:30:00	7.02	1.1659	1	277031	ON	15.2	255
8/29/2026	14:45:00	7.04	0.0265	1	277037	ON	16.2	257
8/29/2026	15:00:00	7.01	0.0341	1	277037	ON	16.9	0
8/29/2026	15:15:00	7.01	0.4807	1	277040	ON	17.3	257
8/29/2026	15:30:00	6.99	0.4467	1	277047	ON	17.6	256
8/29/2026	15:45:00	6.98	0.2044	1	277052	ON	17.9	256
8/29/2026	16:00:00	6.99	0.0303	1	277054	ON	18.5	0



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/29/2026	16:15:00	6.99	0.1211	1	277055	ON	18.5	258
8/29/2026	16:30:00	7.01	0.0341	2	277055	ON	17.8	262
8/29/2026	16:45:00	6.98	2.1577	2	277055	ON	18.1	262
8/29/2026	17:00:00	7.08	1.7754	2	277082	ON	15.2	262
8/29/2026	17:15:00	7.08	0.8669	2	277103	ON	15.4	262
8/29/2026	17:30:00	7.07	0.0189	2	277106	ON	16.5	262
8/29/2026	17:45:00	7.08	1.7451	2	277124	ON	15.3	261
8/29/2026	18:00:00	7.09	0.0946	2	277139	ON	15.6	261
8/29/2026	18:15:00	7.08	2.1009	2	277148	ON	15.3	260
8/29/2026	18:30:00	7.07	2.0858	1	277177	ON	15	260
8/29/2026	18:45:00	7.06	1.7829	2	277206	ON	15	259
8/29/2026	19:00:00	7.06	0.6624	1	277232	ON	14.9	259
8/29/2026	19:15:00	7.08	0.4618	2	277238	ON	15.2	259
8/29/2026	19:30:00	7.07	0.0000	2	277240	ON	16	261
8/29/2026	19:45:00	7.05	0.0114	2	277240	ON	16.9	0
8/29/2026	20:00:00	7.04	0.0341	2	277240	ON	17	257
8/29/2026	20:15:00	7.06	0.7533	1	277257	ON	14.8	255
8/29/2026	20:30:00	7.07	0.3937	1	277264	ON	15	253
8/29/2026	20:45:00	7.04	2.0138	2	277277	ON	14.5	252
8/29/2026	21:00:00	7.05	1.7526	1	277306	ON	14.2	253
8/29/2026	21:15:00	7.06	0.8063	1	277326	ON	14.3	249
8/29/2026	21:30:00	7.08	0.0151	1	277328	ON	15.2	0
8/29/2026	21:45:00	7.06	0.0227	1	277328	ON	15.8	0
8/29/2026	22:00:00	7.05	0.0341	1	277328	ON	16.3	0
8/29/2026	22:15:00	7.05	1.6504	1	277335	ON	14.5	246
8/29/2026	22:30:00	7.04	2.0858	1	277364	ON	14	247
8/29/2026	22:45:00	7.04	1.1583	1	277394	ON	14	244
8/29/2026	23:00:00	7.06	0.4353	1	277403	ON	14.2	243
8/29/2026	23:15:00	7.06	0.2763	1	277408	ON	14.4	243
8/29/2026	23:30:00	7.05	0.2801	1	277411	ON	14.9	242
8/29/2026	23:45:00	7.03	0.0265	1	277418	ON	14.6	243
8/30/2026	0:00:00	7	1.7526	2	277422	ON	14.5	241



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	0:15:00	7.09	0.4770	1	277442	ON	14.2	245
8/30/2026	0:30:00	7.09	0.0265	2	277443	ON	15.1	0
8/30/2026	0:45:00	7.07	0.0151	1	277443	ON	15.7	0
8/30/2026	1:00:00	7.08	0.3710	2	277443	ON	16	245
8/30/2026	1:15:00	7.1	1.7640	2	277470	ON	14	250
8/30/2026	1:30:00	7.1	2.0971	1	277497	ON	14	251
8/30/2026	1:45:00	7.11	0.9312	2	277525	ON	14	254
8/30/2026	2:00:00	7.1	0.2763	1	277532	ON	14.4	253
8/30/2026	2:15:00	7.09	0.2233	1	277536	ON	14.9	253
8/30/2026	2:30:00	7.09	0.0341	2	277536	ON	15.7	0
8/30/2026	2:45:00	7.08	0.0303	1	277536	ON	16.1	0
8/30/2026	3:00:00	7.08	0.2650	1	277536	ON	15.8	251
8/30/2026	3:15:00	7.09	0.3520	1	277561	ON	14.1	255
8/30/2026	3:30:00	7.08	0.3748	1	277568	ON	14.3	256
8/30/2026	3:45:00	7.08	0.3899	1	277574	ON	14.3	255
8/30/2026	4:00:00	7.08	1.7716	2	277597	ON	14	257
8/30/2026	4:15:00	7.09	1.7564	1	277625	ON	13.9	259
8/30/2026	4:30:00	7.11	0.0151	2	277632	ON	14.4	259
8/30/2026	4:45:00	7.1	1.6807	1	277643	ON	14	257
8/30/2026	5:00:00	7.11	0.5640	2	277664	ON	14.1	260
8/30/2026	5:15:00	7.11	0.0000	2	277665	ON	14.8	259
8/30/2026	5:30:00	7.1	0.0303	2	277665	ON	15.4	260
8/30/2026	5:45:00	7.09	0.0151	2	277665	ON	15.9	260
8/30/2026	6:00:00	7.07	0.1401	2	277667	ON	16.3	260
8/30/2026	6:15:00	7.11	1.7602	2	277688	ON	14	263
8/30/2026	6:30:00	7.11	1.7905	2	277717	ON	13.9	266
8/30/2026	6:45:00	7.11	2.1009	1	277746	ON	13.9	263
8/30/2026	7:00:00	7.13	0.6246	2	277770	ON	14	263
8/30/2026	7:15:00	7.11	0.1628	1	277776	ON	14.5	265
8/30/2026	7:30:00	7.11	2.0858	1	277798	ON	14	262
8/30/2026	7:45:00	7.12	0.0341	1	277814	ON	14.2	262
8/30/2026	8:00:00	7.11	0.2877	1	277815	ON	14.7	262



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	8:15:00	7.11	0.1476	1	277816	ON	15.2	261
8/30/2026	8:30:00	7.1	2.0782	1	277844	ON	14	261
8/30/2026	8:45:00	7.12	0.1552	5	277850	ON	14.3	259
8/30/2026	9:00:00	7.11	0.6019	1	277857	ON	14.3	255
8/30/2026	9:15:00	7.11	0.4467	2	277862	ON	14.4	256
8/30/2026	9:30:00	7.14	0.4921	1	277869	ON	14.5	255
8/30/2026	9:45:00	7.11	0.0341	1	277873	ON	14.8	255
8/30/2026	10:00:00	7.1	1.7829	1	277891	ON	14.2	254
8/30/2026	10:15:00	7.1	1.6429	1	277917	ON	14.2	252
8/30/2026	10:30:00	7.11	0.0227	1	277922	ON	14.6	251
8/30/2026	10:45:00	7.08	1.8056	1	277936	ON	14.3	250
8/30/2026	11:00:00	7.06	1.6353	1	277961	ON	14.1	247
8/30/2026	11:15:00	7.07	1.3476	2	277984	ON	14.2	247
8/30/2026	11:30:00	7.08	0.4694	1	277999	ON	14.4	245
8/30/2026	11:45:00	7.08	0.1628	2	278003	ON	14.6	244
8/30/2026	12:00:00	7.08	0.0379	2	278004	ON	15.2	242
8/30/2026	12:15:00	7.06	0.0379	2	278004	ON	15.4	243
8/30/2026	12:30:00	7.08	0.0303	1	278014	ON	15	245
8/30/2026	12:45:00	7.08	1.5558	1	278019	ON	14.6	241
8/30/2026	13:00:00	7.09	1.6996	1	278045	ON	14.3	241
8/30/2026	13:15:00	7.08	2.0138	1	278070	ON	14.3	242
8/30/2026	13:30:00	7.08	1.9949	1	278101	ON	14.2	242
8/30/2026	13:45:00	7.09	0.3823	1	278112	ON	14.6	242
8/30/2026	14:00:00	7.09	0.0189	1	278117	ON	15.3	2
8/30/2026	14:15:00	7.1	0.2006	1	278119	ON	15.8	242
8/30/2026	14:30:00	7.08	0.2309	2	278122	ON	16.2	244
8/30/2026	14:45:00	7.06	0.2271	1	278126	ON	16.8	245
8/30/2026	15:00:00	7.09	0.8176	1	278132	ON	15.2	243
8/30/2026	15:15:00	7.07	0.0795	1	278135	ON	16.3	231
8/30/2026	15:30:00	7.07	0.0341	1	278135	ON	16.5	249
8/30/2026	15:45:00	7.07	1.5407	1	278139	ON	15.4	242
8/30/2026	16:00:00	7.08	1.6353	1	278163	ON	14.5	246



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Date	Time	Discharge pH	Discharge Flow Rate (m3PM)	Discharge NTU	Flow Total (m3)	Discharge Valve Status	Discharge Temperature (°C)	Discharge Conductivity (uS/cm)
8/30/2026	16:15:00	7.08	1.6315	1	278189	ON	14.4	244
8/30/2026	16:30:00	7.08	1.8246	1	278213	ON	14.4	245
8/30/2026	16:45:00	7.1	0.0265	1	278223	ON	15	244
8/30/2026	17:00:00	7.09	0.7192	1	278224	ON	15.7	245
8/30/2026	17:15:00	7.1	0.0227	2	278237	ON	15	243
8/30/2026	17:30:00	7.09	0.1211	1	278237	ON	15.6	244
8/30/2026	17:45:00	7.09	2.0328	2	278260	ON	14.5	243
8/30/2026	18:00:00	7.1	1.7564	1	278289	ON	14.4	244
8/30/2026	18:15:00	7.11	0.2650	2	278307	ON	14.7	245
8/30/2026	18:30:00	7.09	2.0025	2	278314	ON	14.6	242
8/30/2026	18:45:00	7.1	1.7489	2	278342	ON	14.5	243
8/30/2026	19:00:00	7.1	1.7602	1	278372	ON	14.4	244
8/30/2026	19:15:00	7.1	1.0599	1	278398	ON	14.5	244
8/30/2026	19:30:00	7.1	0.0189	1	278403	ON	15.3	245
8/30/2026	19:45:00	7.1	1.8246	2	278422	ON	14.5	244
8/30/2026	20:00:00	7.11	0.0000	1	278436	ON	15.2	40
8/30/2026	20:15:00	7.09	0.7949	2	278438	ON	15.9	245
8/30/2026	20:30:00	7.11	0.0908	1	278449	ON	15.2	244
8/30/2026	20:45:00	7.09	0.4013	1	278449	ON	15.6	246
8/30/2026	21:00:00	7.08	0.0000	1	278453	ON	16.3	246
8/30/2026	21:15:00	7.09	0.0227	2	278453	ON	17	0
8/30/2026	21:30:00	7.08	0.1022	2	278456	ON	16.8	244
8/30/2026	21:45:00	7.11	2.0858	2	278473	ON	14.4	243
8/30/2026	22:00:00	7.11	1.7299	2	278502	ON	14.1	242
8/30/2026	22:15:00	7.11	1.7413	1	278531	ON	14.1	241
8/30/2026	22:30:00	7.11	1.3590	1	278560	ON	14	238
8/30/2026	22:45:00	7.12	0.0151	1	278567	ON	14.6	238
8/30/2026	23:00:00	7.11	0.2763	1	278571	ON	14.6	234
8/30/2026	23:15:00	7.11	0.0000	1	278576	ON	14.6	234
8/30/2026	23:30:00	7.08	2.0517	1	278594	ON	14	231
8/30/2026	23:45:00	7.11	0.5489	1	278617	ON	14.2	232

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

Appendix C: Photos




Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Photo 1: No visible sheen observed in the Portal WTP water, August 24




		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

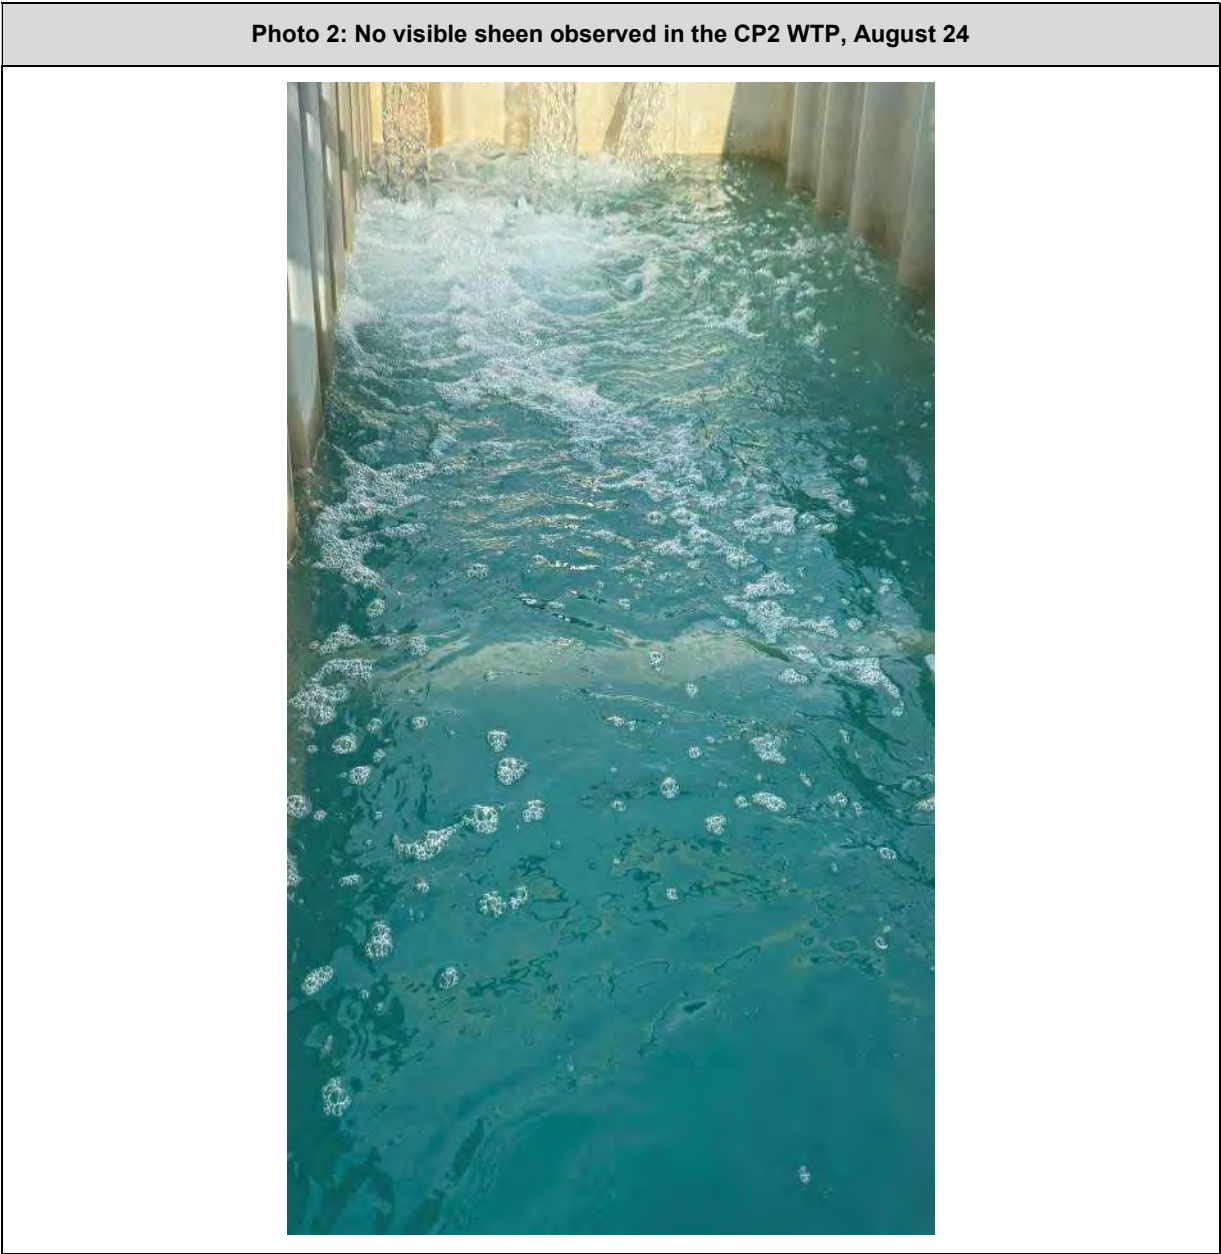


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026




		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

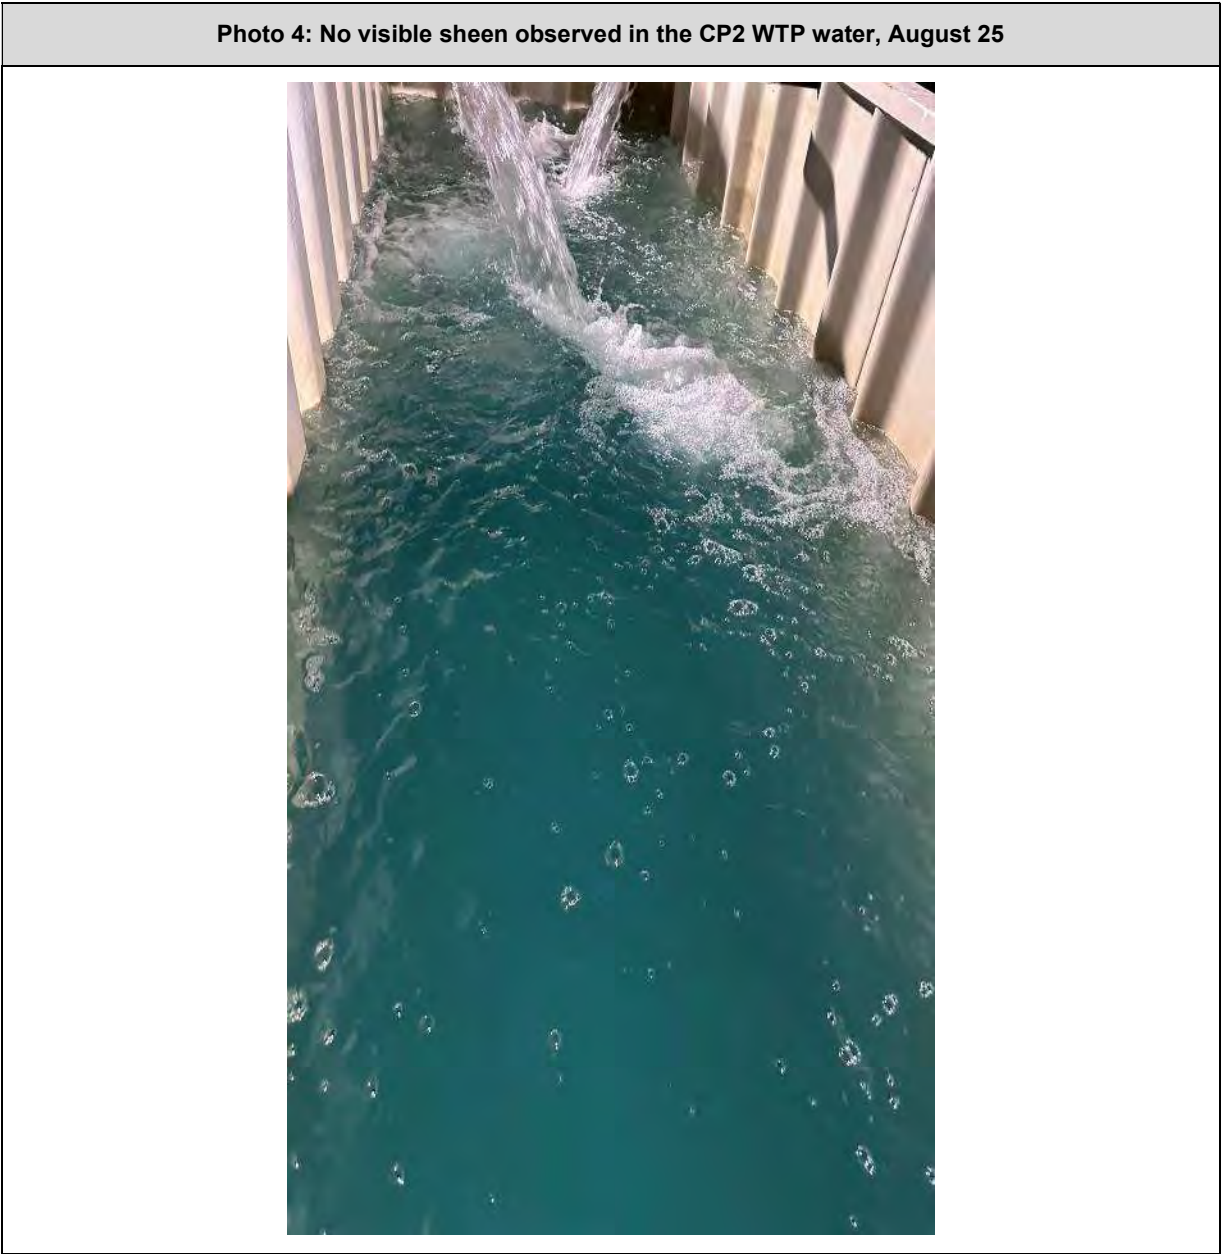


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

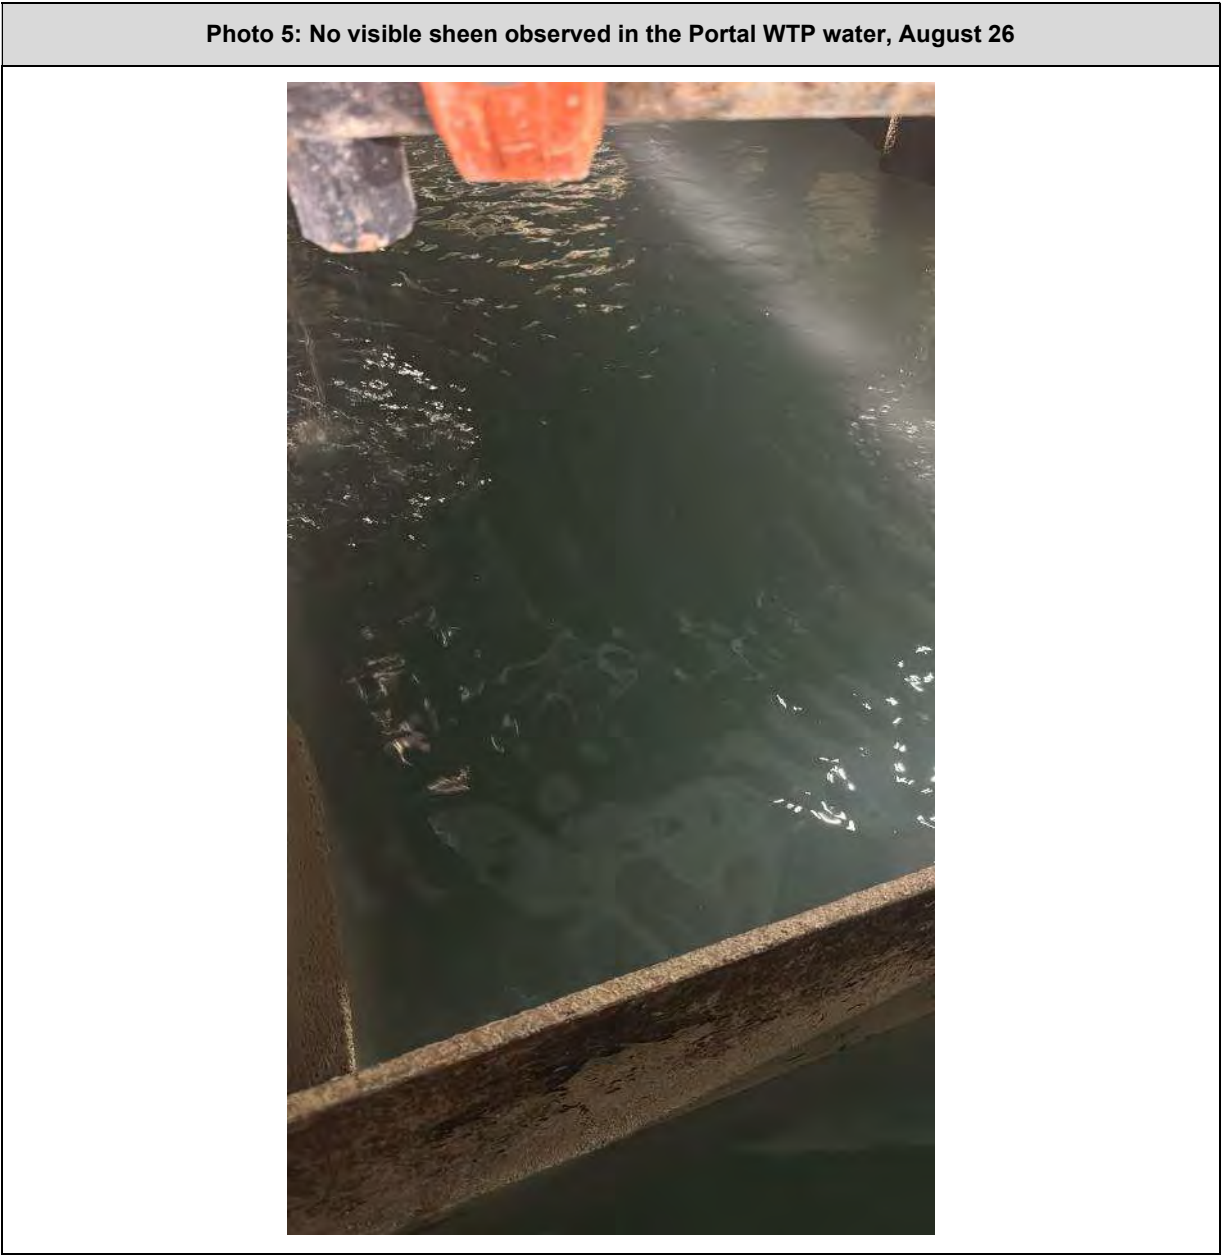


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

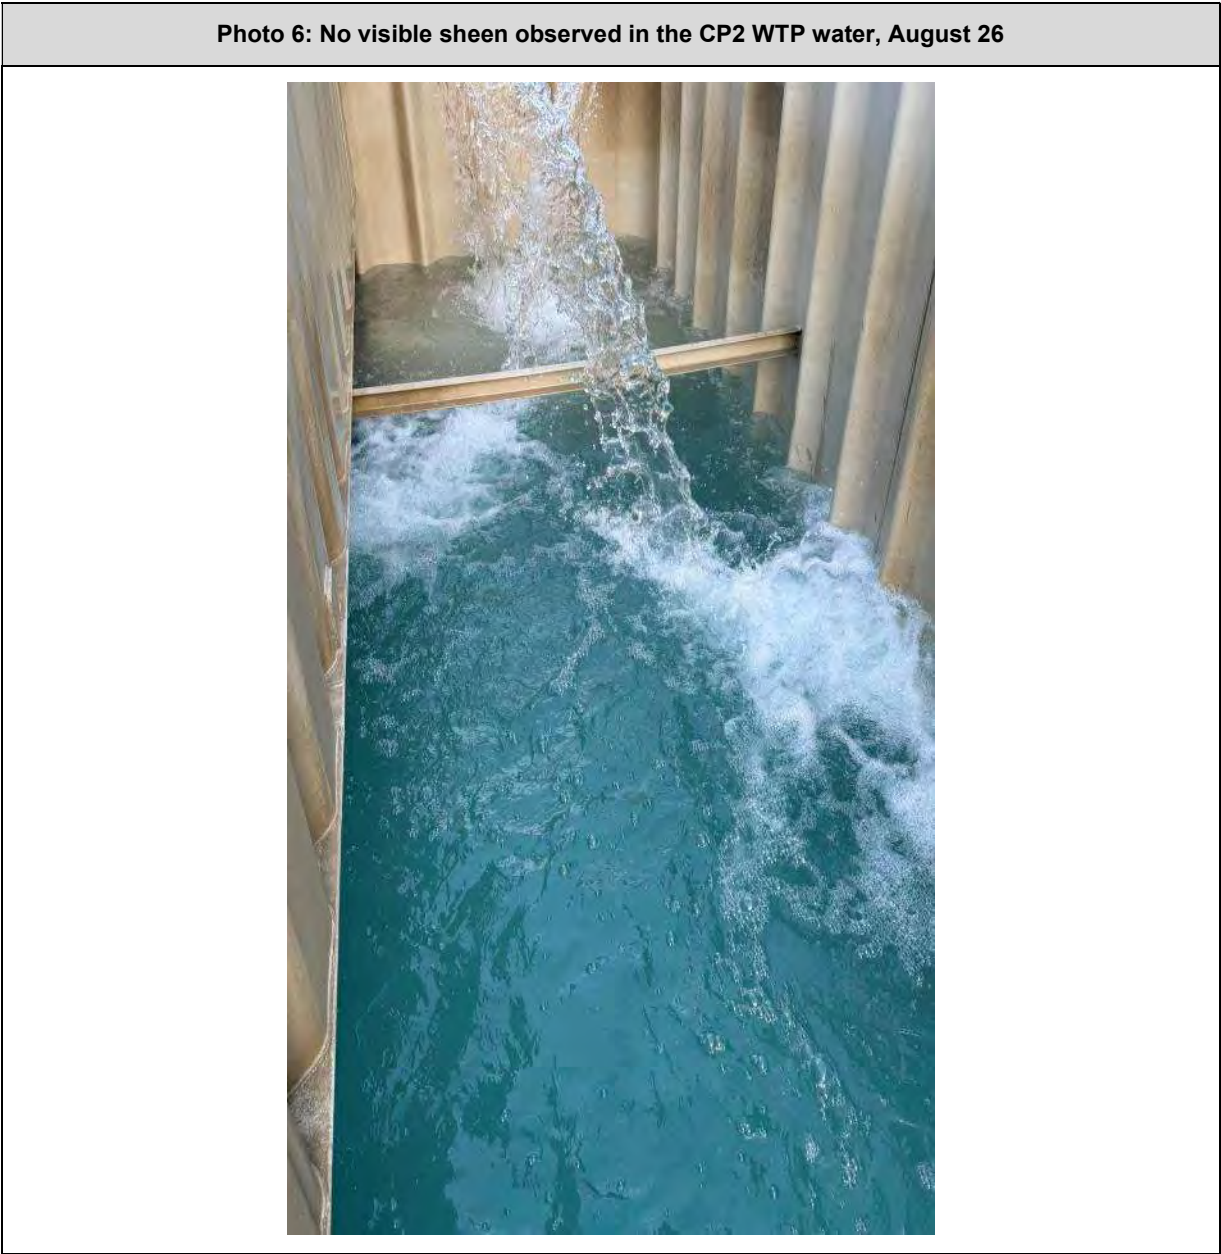


		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

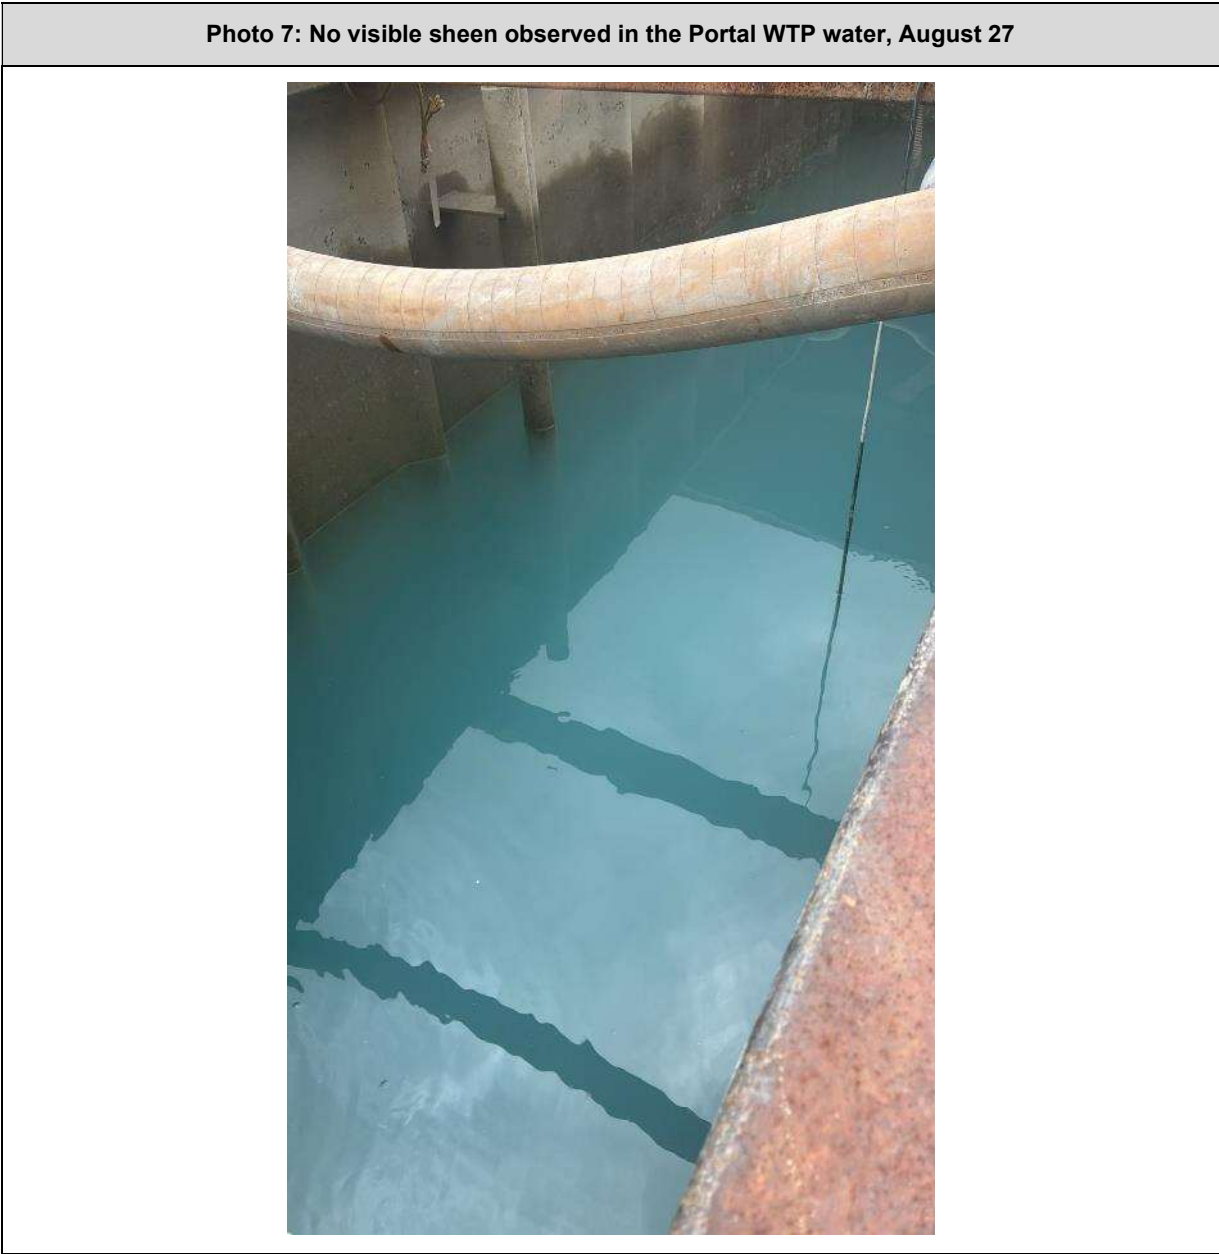

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: BC1 Approved by: BC2 Date: September 6, 2026	

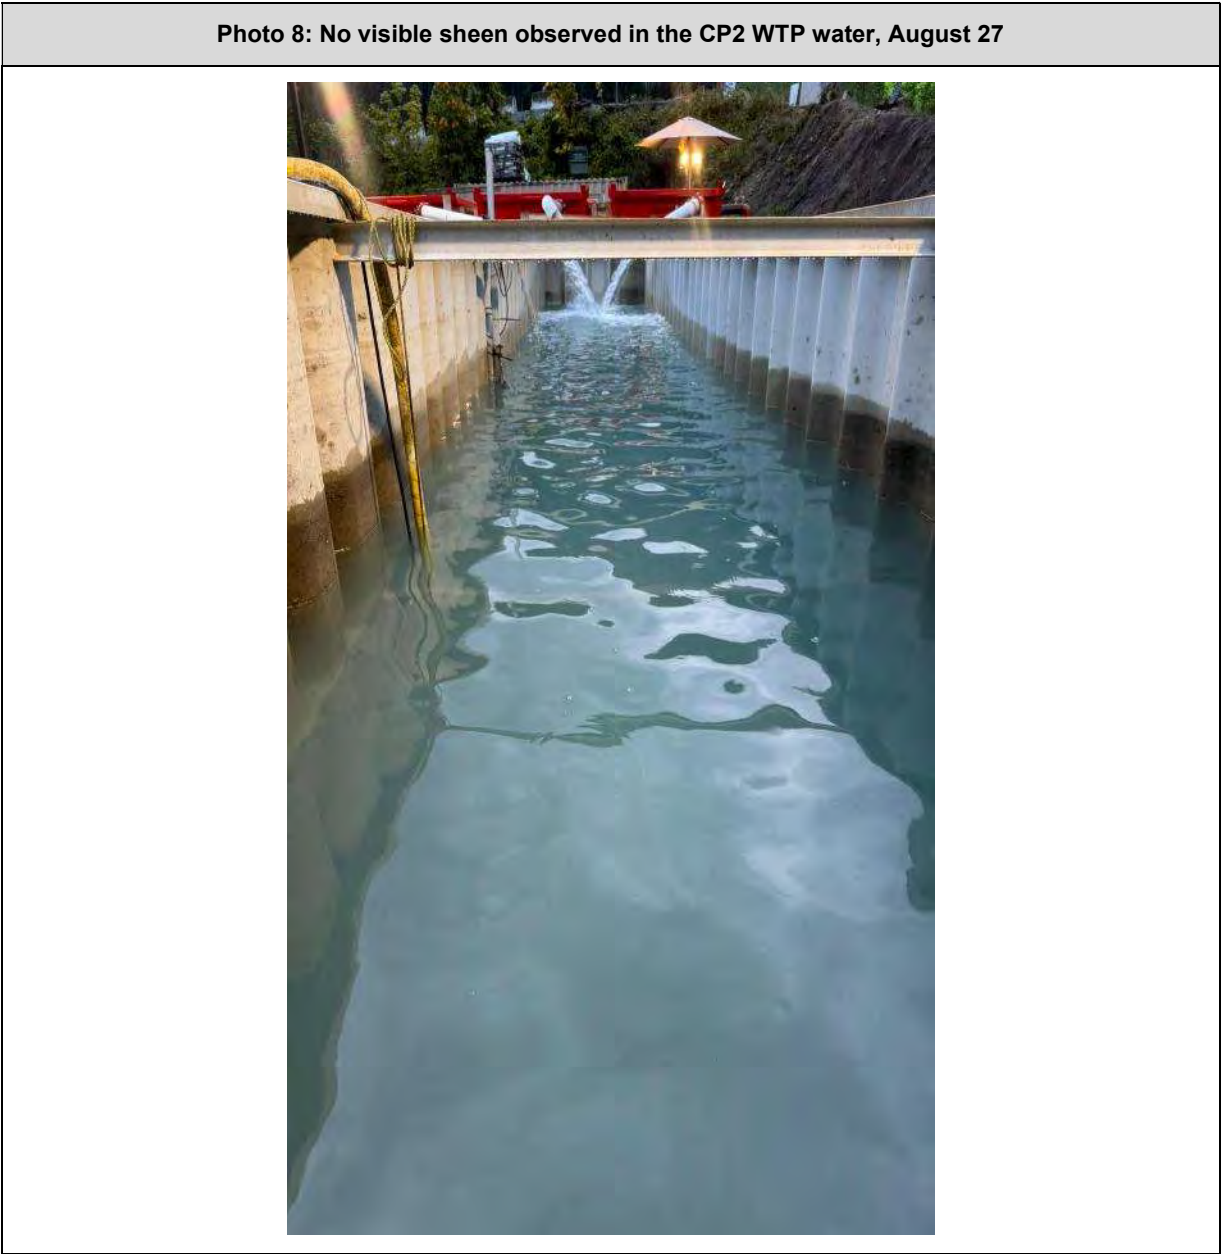

		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

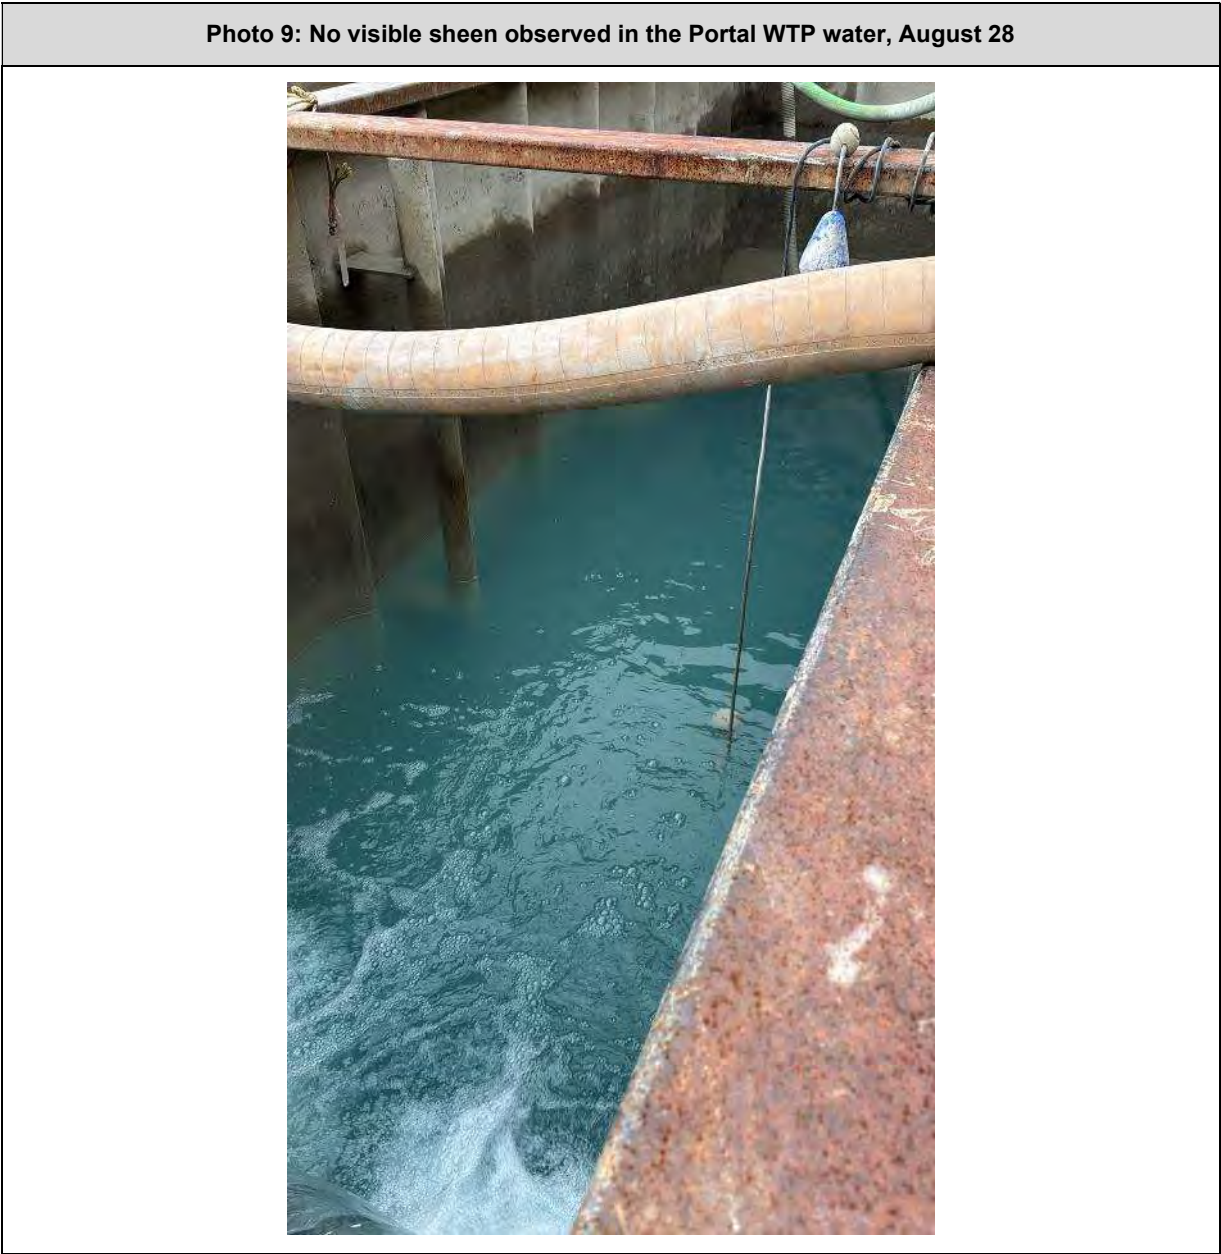



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Photo 10: No visible sheen observed in the CP2 WTP water, August 28






Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Photo 11: No visible sheen observed in the Portal WTP water, August 29



		Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope	
Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

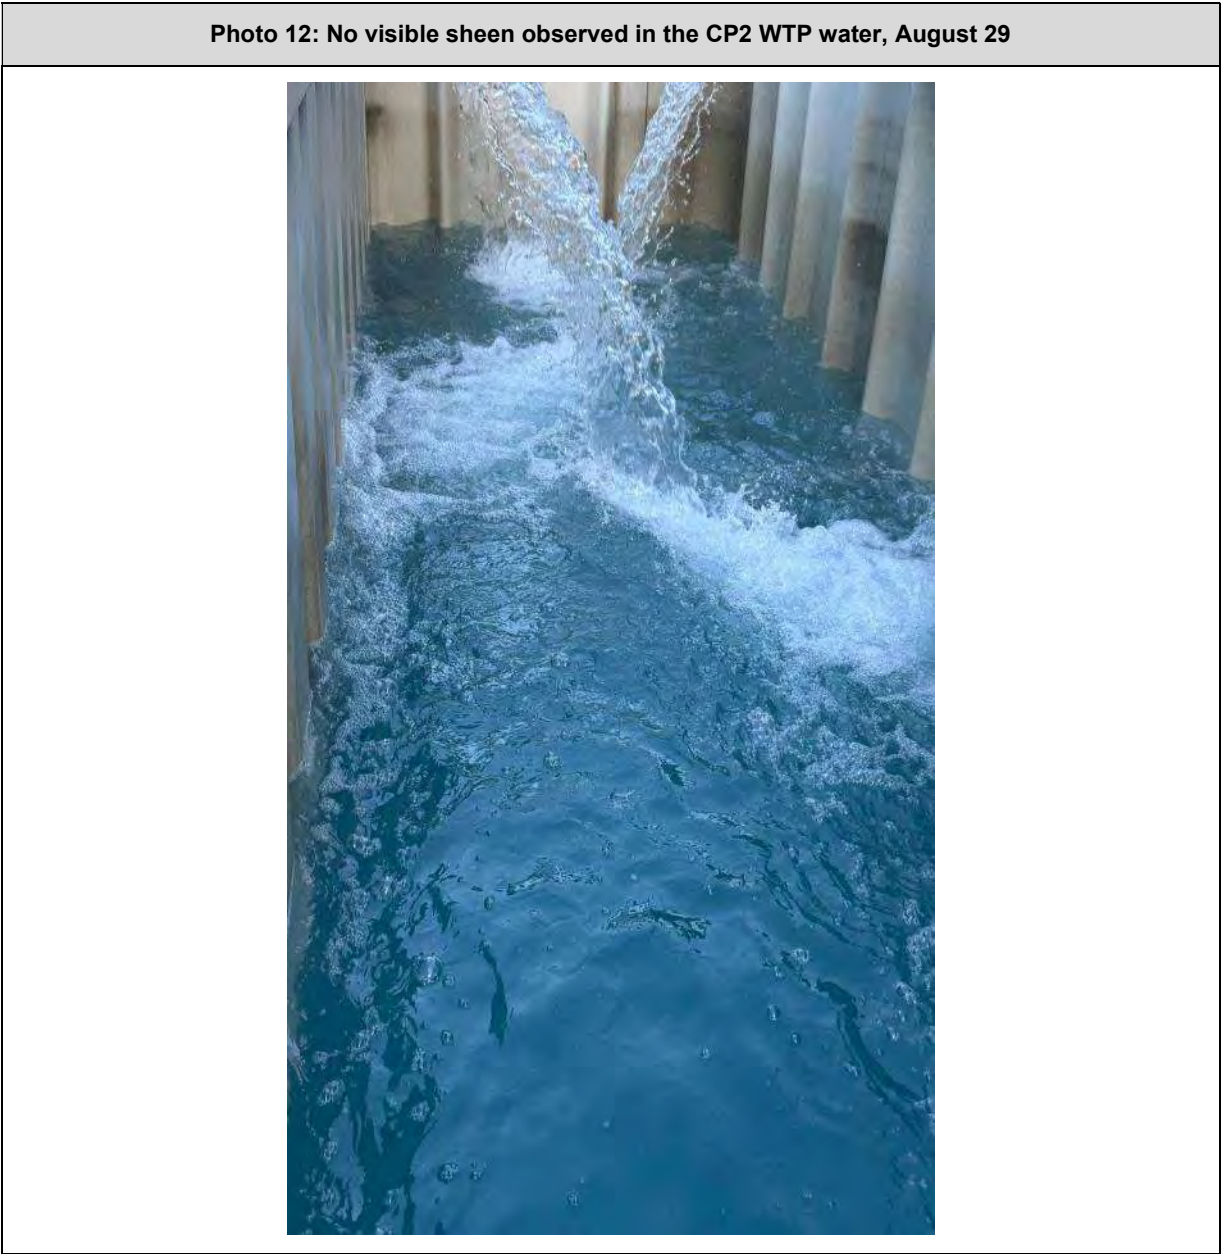



Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Photo 13: No visible sheen observed in the Portal WTP water, August 30






Eagle Mountain- Woodfibre Gas Pipeline Project- Tunnel Scope

Title	Woodfibre Weekly Water Discharge Report	Revision:	0
Data Range	August 24, 2026 to August 30, 2026	Prepared by: Approved by: Date:	BC1 BC2 September 6, 2026

Photo 14: No visible sheen observed in the CP2 WTP water, August 30

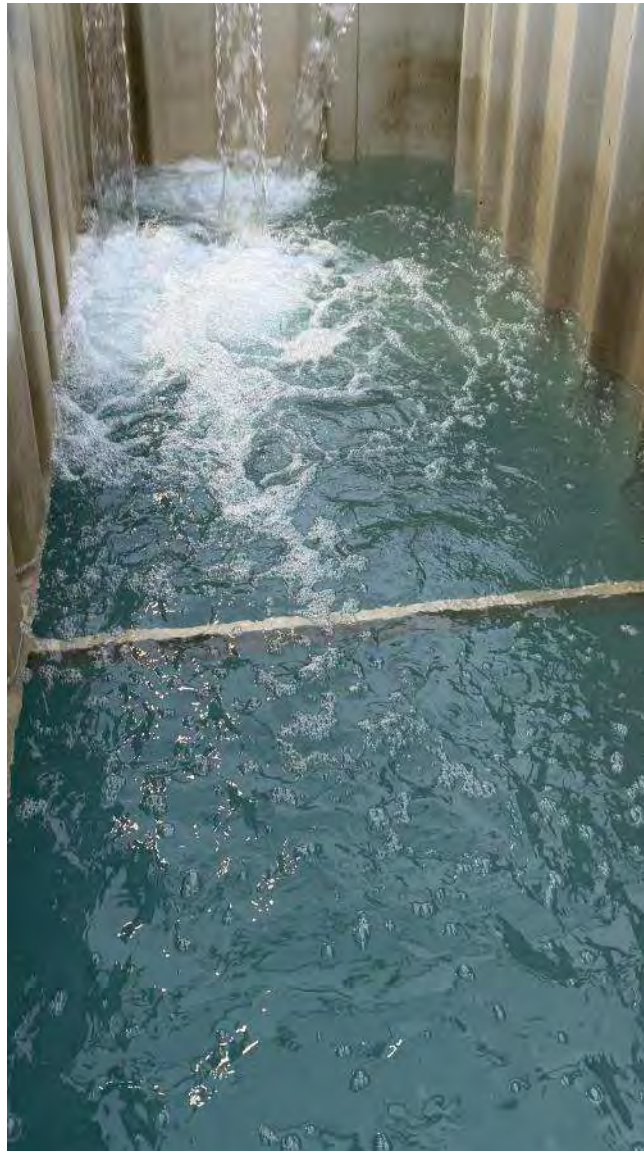

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix D	D-1

Appendix D:
Woodfibre Site Receiving Environment
Documentation

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix D	D-2

Woodfibre Site Receiving Environment Sample Analysis



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-25 09:47:00	WLNG DS 2026-08-25 09:17:00
In situ Parameters									
Field pH	pH Units		6.5 - 9			7 - 8.7		7.45	7.6
Field Temperature	°C	18	19					16.2	14
General Parameters									
pH	pH Units							6.54	7.38
Alkalinity (Total as CaCO ₃)	mg/L							9.7	55
Alkalinity (PP as CaCO ₃)	mg/L							<1	<1
Hardness (CaCO ₃)-Total	mg/L							9.28	65.8
Hardness (CaCO ₃)-Dissolved	mg/L							9.51	69
Sulphide-Total	mg/L							<0.0018	<0.0018
Sulphide (as H ₂ S)	mg/L			0.002				<0.002	<0.002
Un-ionized Hydrogen Sulfide as H ₂ S-Total	mg/L							<0.0019	<0.0019
Un-ionized Hydrogen Sulfide as S-Total	mg/L							<0.0018	<0.0018
Anions and Nutrients									
Ammonia (N)-Total	mg/L	1.54	10.8		5	33		<0.015	<0.015
Bicarbonate (HCO ₃)	mg/L							12	67
Carbonate (CO ₃)	mg/L							<1	<1
Hydroxide (OH)	mg/L							<1	<1
Nitrate (N)	mg/L	3	32.8		3.7			<0.02	<0.02
Nitrite (N)	mg/L	0.02	0.06					<0.005	<0.005
Nitrate plus Nitrite (N)	mg/L							<0.02	<0.02
Nitrogen (N)-Total	mg/L							0.106	0.188
Phosphorus (P)-Total (4500-P)	mg/L							0.016	0.0024
Bromide (Br)	mg/L							<0.01	<0.01
Chloride (Cl)	mg/L	150	600					<1	16
Fluoride (F)	mg/L		0.4			1.5		<0.05	0.35
Sulphate (SO ₄)-Dissolved	mg/L	128						1.8	15
Total Metals									
Aluminum (Al)-Total	mg/L	0.0738331						0.0388	0.0542
Antimony (Sb)-Total	mg/L	0.074	0.25					0.000021	0.00077
Arsenic (As)-Total	mg/L	0.005			0.0125			0.000141	0.000845
Barium (Ba)-Total	mg/L			1				0.00417	0.00465
Beryllium (Be)-Total	mg/L			0.00013			0.1	<0.00001	<0.00001
Bismuth (Bi)-Total	mg/L							<0.00001	<0.00001
Boron (B)-Total	mg/L	1.2			1.2			<0.01	0.013
Cadmium (Cd)-Total	mg/L						0.00012	0.0000055	<0.000005
Calcium (Ca)-Total	mg/L							3.15	24.1
Cesium (Cs)-Total	mg/L							<0.00005	<0.00005
Chromium (Cr)-Total	mg/L							<0.0001	<0.0001

¹ Guideline calculated using the in-situ measurements (pH (field),Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-25 09:47:00	WLNG DS 2026-08-25 09:17:00
Total Metals (Cont'd.)									
Chromium (Cr III)-Total	mg/L			0.0089			0.056	<0.00099	<0.00099
Chromium (Cr VI)-Total	mg/L			0.0025			0.0015	<0.00099	<0.00099
Cobalt (Co)-Total	mg/L							0.000023	0.000025
Copper (Cu)-Total	mg/L				0.002	0.003		0.00071	0.00034
Iron (Fe)-Total	mg/L	0.055	1					0.0543	0.0102
Lead (Pb)-Total	mg/L				0.002	0.14		0.000024	<0.00002
Lithium (Li)-Total	mg/L							<0.0005	0.00759
Magnesium (Mg)-Total	mg/L							0.34	1.37
Manganese (Mn)-Total	mg/L						0.1	0.00141	0.0177
Mercury (Hg)-Total	mg/L	0.00002			0.0001			<0.0000019	<0.0000019
Molybdenum (Mo)-Total	mg/L	7.6	46					0.000717	0.0472
Nickel (Ni)-Total	mg/L						0.0083	0.00021	0.00018
Phosphorus (P)-Total (ICPMS)	mg/L							0.0142	<0.005
Potassium (K)-Total	mg/L							<0.25	1.85
Rubidium (Rb)-Total	mg/L							0.000394	0.00391
Selenium (Se)-Total	mg/L	0.002			0.002			<0.00004	<0.00004
Silicon (Si)-Total	mg/L							4.8	6.04
Silver (Ag)-Total	mg/L	0.00012			0.0005	0.0037	0.0005	<0.00001	<0.00001
Sodium (Na)-Total	mg/L							1.82	8.47
Strontium (Sr)-Total	mg/L							0.0149	0.0467
Sulphur (S)-Total	mg/L							<3	5.6
Tellurium (Te)-Total	mg/L							<0.00002	<0.00002
Thallium (Tl)-Total	mg/L			0.00003				<0.000002	0.0000083
Thorium (Th)-Total	mg/L							<0.00005	<0.00005
Tin (Sn)-Total	mg/L							<0.0002	<0.0002
Titanium (Ti)-Total	mg/L							<0.002	<0.002
Uranium (U)-Total	mg/L		0.0165	0.0075				0.000058	0.00056
Vanadium (V)-Total	mg/L			0.06			0.005	0.00021	<0.0002
Zinc (Zn)-Total	mg/L				0.01	0.055		0.0011	0.0023
Zirconium (Zr)-Total	mg/L							<0.0001	<0.0001
Dissolved Metals									
Aluminum (Al)-Dissolved	mg/L							0.0361	0.0406
Antimony (Sb)-Dissolved	mg/L							0.000021	0.000791
Arsenic (As)-Dissolved	mg/L							0.000141	0.00086
Barium (Ba)-Dissolved	mg/L							0.00448	0.00507
Beryllium (Be)-Dissolved	mg/L							<0.00001	<0.00001
Bismuth (Bi)-Dissolved	mg/L							<0.000005	<0.000005
Boron (B)-Dissolved	mg/L							<0.01	0.013
Cadmium (Cd)-Dissolved	mg/L	0.0000368	0.0000508					<0.000005	<0.000005

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).



Analyte	Unit	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Freshwater Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Freshwater Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Long Term Average	BC Approved Water Quality Guideline - Marine Aquatic Life - Short Term Max	BC Working Water Quality Guideline - Marine Aquatic Life - Long Term Average	WLNG US 2026-08-25 09:47:00	WLNG DS 2026-08-25 09:17:00
Dissolved Metals (Cont'd.)									
Calcium (Ca)-Dissolved	mg/L							3.22	25.2
Cesium (Cs)-Dissolved	mg/L							<0.00005	<0.00005
Chromium (Cr)-Dissolved	mg/L							<0.0001	<0.0001
Cobalt (Co)-Dissolved	mg/L	0.0003889						0.0000152	0.0000165
Copper (Cu)-Dissolved	mg/L	0.00036	0.00213					0.000737	0.000065
Iron (Fe)-Dissolved	mg/L							0.0418	0.0011
Lead (Pb)-Dissolved	mg/L	0.001529						0.0000172	<0.000005
Lithium (Li)-Dissolved	mg/L							<0.0005	0.00844
Manganese (Mn)-Dissolved	mg/L	0.13	0.4407697					0.000909	0.0174
Magnesium (Mg)-Dissolved	mg/L							0.355	1.47
Mercury (Hg)-Dissolved	mg/L							<0.0000019	<0.0000019
Molybdenum (Mo)-Dissolved	mg/L							0.000785	0.0493
Nickel (Ni)-Dissolved	mg/L	0.0009	0.0127					0.000277	0.000125
Phosphorus (P)-Dissolved	mg/L							0.0119	0.0028
Potassium (K)-Dissolved	mg/L							0.19	1.92
Rubidium (Rb)-Dissolved	mg/L							0.000409	0.00418
Selenium (Se)-Dissolved	mg/L							<0.00004	<0.00004
Silicon (Si)-Dissolved	mg/L							5.18	6.54
Silver (Ag)-Dissolved	mg/L							<0.000005	<0.000005
Sodium (Na)-Dissolved	mg/L							1.89	9.06
Strontium (Sr)-Dissolved	mg/L			1.25				0.0162	0.053
Sulphur (S)-Dissolved	mg/L							<3	5.5
Tellurium (Te)-Dissolved	mg/L							<0.00002	<0.00002
Thallium (Tl)-Dissolved	mg/L							<0.000002	0.0000074
Thorium (Th)-Dissolved	mg/L							0.0000116	<0.000005
Tin (Sn)-Dissolved	mg/L							<0.0002	<0.0002
Titanium (Ti)-Dissolved	mg/L							<0.0005	<0.0005
Uranium (U)-Dissolved	mg/L							0.0000532	0.000575
Vanadium (V)-Dissolved	mg/L							0.00022	<0.0002
Zinc (Zn)-Dissolved	mg/L	0.0030078	0.0087868					0.00051	0.0017
Zirconium (Zr)-Dissolved	mg/L							<0.0001	<0.0001
Inorganics									
Organic Carbon (C)-Total	mg/L							1.9	0.69
Organic Carbon (C)-Dissolved	mg/L							1.9	0.66
Solids-Total Dissolved	mg/L							<10	52
Solids-Total Suspended	mg/L	6	26					<1	1.2

¹ Guideline calculated using the in-situ measurements (pH (field), Temperature (field), Turbidity (field), Hardness (as CaCO₃) – total, Dissolved Organic Carbon (DOC), Total Alkalinity (CaCO₃), and Chloride).

² Guideline values presented represent the lower of the co-factor dependent guidelines for the upstream and downstream stations when they differ, but exceedance bolding is dependent on guidelines calculated using in situ co-factor considerations.

³ **Bold text** denotes value exceeding guidelines, except in cases where they are below a station-specific guideline that isn't displayed as per ¹ and ² above. Given that application of chronic BC water quality guidelines for protection of aquatic life in the receiving environment downstream of the discharge does not represent a regulatory requirement and instead data are intended to be assessed relative to monthly average concentrations, exceedances of these guidelines are highlighted for information purposes, but detailed interpretation of guideline exceedances are not provided given that an interpretation of monthly trends and consideration of background influences and discharge chemistry is required.

⁴ **Bold and shaded text** outlines a reportable exceedance given that it exceeds the applicable BC water quality guideline (i.e., the short-term acute freshwater aquatic life guideline), or discharge concentration limit, consistent with recommendations outlined in Hatfield (2024).

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix D	D-3

Woodfibre Site Receiving Environment
Field Notes and Logs

Water Quality Field Data Sheet



Hatfield

Project: FORTIS11234

Location Information

Site ID:	<u>WLNG (EAS) DS</u>	Date:	<u>August 25, 2026</u>
Site Name:	<u>East Creek</u>	Time:	<u>9:19</u>
Site UTM:	Zone: 10U E: <u>482092</u>	Crew:	<u>BG</u>
(NAD83)	N: <u>5501875</u>	Weather:	<u>20°C, Clear skies</u>

In Situ Parameters

pH:	<u>7.6</u>	DO:	<u>10.21</u> (mg/L)
Temp:	<u>14</u> (°C)	Cond:	<u>251.1</u> (us/cm)
Turbidity:	<u>0</u> FNRU	Salinity:	<u>0.12</u> (ppt)
Visible Sheen:	No	ORP:	<u>76.9</u> (mV)
Water Surface Condition:	Clear		

Photo Record



Observations

No notable observations.

Water Quality Field Data Sheet



Project: FORTIS11234

Location Information

Site ID:	WLNG (EAS) US	Date:	August 25, 2026
Site Name:	East Creek	Time:	8:25
Site UTM:	Zone: 10U E: 481908	Crew:	BG
(NAD83)	N: 5501909	Weather:	20°C, Clear skies

In Situ Parameters

pH:	7.45	DO:	9.14 (mg/L)
Temp:	16.2 (°C)	Cond:	80.8 (us/cm)
Turbidity:	0 FNRU	Salinity:	0.04 (ppt)
Visible Sheen:	No	ORP:	50 (mV)

Water Surface Condition:

Photo Record



Observations

No notable observations.

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-24 00:00:00	14.19	226.17	0.07	7.81	9.78	0.00	0.12
EAS-DS	2026-08-24 00:15:00	14.12	225.43	0.07	7.79	9.77	0.10	0.12
EAS-DS	2026-08-24 00:30:00	13.82	222.39	0.08	7.76	9.89	0.00	0.12
EAS-DS	2026-08-24 00:45:00	14.11	227.82	-0.01	7.78	9.79	0.03	0.12
EAS-DS	2026-08-24 01:00:00	14.37	230.38	0.06	7.81	9.71	0.32	0.12
EAS-DS	2026-08-24 01:15:00	14.31	226.69	0.05	7.80	9.56	0.00	0.12
EAS-DS	2026-08-24 01:30:00	13.97	227.69	0.06	7.79	9.86	0.00	0.12
EAS-DS	2026-08-24 01:45:00	14.13	230.78	-0.02	7.79	9.83	0.12	0.12
EAS-DS	2026-08-24 02:00:00	14.19	231.70	0.05	7.80	9.76	9.31	0.12
EAS-DS	2026-08-24 02:15:00	13.99	226.86	0.03	7.73	9.70	0.00	0.12
EAS-DS	2026-08-24 02:30:00	14.43	234.47	0.04	7.85	9.76	0.79	0.13
EAS-DS	2026-08-24 02:45:00	14.52	235.25	-0.03	7.85	9.66	0.74	0.13
EAS-DS	2026-08-24 03:00:00	14.29	232.56	0.05	7.76	9.62	0.16	0.12
EAS-DS	2026-08-24 03:15:00	14.24	230.24	0.06	7.68	9.24	0.00	0.12
EAS-DS	2026-08-24 03:30:00	14.34	234.90	0.06	7.85	9.69	0.35	0.13
EAS-DS	2026-08-24 03:45:00	14.47	235.79	-0.03	7.82	9.66	2.07	0.13
EAS-DS	2026-08-24 04:00:00	13.99	227.88	0.05	7.74	9.59	0.00	0.12
EAS-DS	2026-08-24 04:15:00	14.25	234.81	0.05	7.84	9.73	0.75	0.13
EAS-DS	2026-08-24 04:30:00	14.19	233.25	0.05	7.81	9.75	0.28	0.12
EAS-DS	2026-08-24 04:45:00	14.04	226.66	-0.03	7.72	9.59	0.00	0.12
EAS-DS	2026-08-24 05:00:00	13.87	226.57	0.05	7.77	9.78	0.00	0.12
EAS-DS	2026-08-24 05:15:00	14.17	234.46	0.05	7.83	9.79	1.09	0.13
EAS-DS	2026-08-24 05:30:00	14.18	234.26	0.05	7.82	9.77	0.26	0.13
EAS-DS	2026-08-24 05:45:00	13.95	228.66	-0.03	7.75	9.73	0.01	0.12
EAS-DS	2026-08-24 06:00:00	14.17	235.30	0.05	7.84	9.80	50.29	0.13
EAS-DS	2026-08-24 06:15:00	14.17	235.11	0.05	7.82	9.78	0.81	0.13
EAS-DS	2026-08-24 06:30:00	14.37	235.07	0.04	7.79	9.61	0.96	0.13
EAS-DS	2026-08-24 06:45:00	14.33	233.08	-0.03	7.66	9.19	0.17	0.12
EAS-DS	2026-08-24 07:00:00	14.33	234.69	0.04	7.83	9.73	0.70	0.13
EAS-DS	2026-08-24 07:15:00	14.25	234.81	0.04	7.82	9.75	0.74	0.13
EAS-DS	2026-08-24 07:30:00	14.18	234.96	0.05	7.82	9.75	0.75	0.13
EAS-DS	2026-08-24 07:45:00	13.96	232.39	-0.04	7.74	9.72	0.52	0.12
EAS-DS	2026-08-24 08:00:00	14.19	234.61	0.05	7.80	9.70	1.56	0.13
EAS-DS	2026-08-24 08:15:00	14.47	237.40	0.04	7.81	9.60	0.71	0.13
EAS-DS	2026-08-24 08:30:00	14.41	233.44	0.04	7.78	9.59	0.55	0.12
EAS-DS	2026-08-24 08:45:00	14.12	231.33	-0.03	7.75	9.75	0.03	0.12
EAS-DS	2026-08-24 09:00:00	14.29	234.60	0.05	7.81	9.74	0.39	0.13
EAS-DS	2026-08-24 09:15:00	14.43	236.35	0.04	7.83	9.75	0.61	0.13
EAS-DS	2026-08-24 09:30:00	14.54	236.55	0.05	7.79	9.50	0.37	0.13
EAS-DS	2026-08-24 09:45:00	14.50	233.81	-0.04	7.64	8.93	1.56	0.13
EAS-DS	2026-08-24 10:00:00	14.64	233.75	0.04	7.83	9.53	0.63	0.13
EAS-DS	2026-08-24 10:15:00	14.66	231.85	0.04	7.72	9.21	0.22	0.12
EAS-DS	2026-08-24 10:30:00	14.75	227.70	0.02	7.75	9.39	0.32	0.12
EAS-DS	2026-08-24 10:45:00	15.04	239.56	-0.04	7.82	9.50	0.72	0.13
EAS-DS	2026-08-24 11:00:00	14.97	236.16	0.04	7.81	9.57	0.59	0.13
EAS-DS	2026-08-24 11:15:00	14.99	236.40	0.04	7.73	9.11	0.20	0.13
EAS-DS	2026-08-24 11:30:00	15.16	234.42	0.03	7.82	9.55	0.60	0.13
EAS-DS	2026-08-24 11:45:00	15.46	246.76	-0.05	7.79	9.38	0.39	0.13
EAS-DS	2026-08-24 12:00:00	15.64	250.14	0.03	7.77	9.24	0.37	0.13
EAS-DS	2026-08-24 12:15:00	15.81	245.59	0.03	7.82	9.37	0.42	0.13
EAS-DS	2026-08-24 12:30:00	15.72	238.73	0.03	7.83	9.43	0.70	0.13
EAS-DS	2026-08-24 12:45:00	15.70	236.84	-0.04	7.82	9.43	0.43	0.13
EAS-DS	2026-08-24 13:00:00	15.48	227.40	0.03	7.82	9.45	0.50	0.12
EAS-DS	2026-08-24 13:15:00	15.48	228.34	0.01	7.74	9.14	0.44	0.12
EAS-DS	2026-08-24 13:30:00	15.99	240.73	0.02	7.81	9.10	1.10	0.13
EAS-DS	2026-08-24 13:45:00	16.16	244.06	-0.05	7.80	9.17	1.20	0.13

Woodfibre LNG (East Creek)□								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-24 14:00:00	15.92	239.36	0.02	7.79	9.30	0.21	0.13
EAS-DS	2026-08-24 14:15:00	15.66	247.19	0.02	7.85	9.42	0.37	0.13
EAS-DS	2026-08-24 14:30:00	15.52	247.08	0.03	7.86	9.47	6.30	0.13
EAS-DS	2026-08-24 14:45:00	15.52	246.61	-0.04	7.84	9.44	1.49	0.13
EAS-DS	2026-08-24 15:00:00	15.46	245.14	0.03	7.86	9.47	0.59	0.13
EAS-DS	2026-08-24 15:15:00	15.49	244.15	0.03	7.87	9.46	0.36	0.13
EAS-DS	2026-08-24 15:30:00	15.76	242.98	0.04	7.82	9.15	0.33	0.13
EAS-DS	2026-08-24 15:45:00	15.82	237.25	-0.06	7.76	9.03	0.23	0.13
EAS-DS	2026-08-24 16:00:00	15.60	241.71	0.02	7.86	9.46	0.31	0.13
EAS-DS	2026-08-24 16:15:00	15.96	243.61	0.03	7.86	9.28	0.40	0.13
EAS-DS	2026-08-24 16:30:00	16.05	242.62	0.01	7.88	9.35	4.88	0.13
EAS-DS	2026-08-24 16:45:00	15.89	240.01	-0.05	7.68	8.82	1.36	0.13
EAS-DS	2026-08-24 17:00:00	16.13	241.42	0.02	7.79	8.98	1.03	0.13
EAS-DS	2026-08-24 17:15:00	16.28	244.84	0.03	7.91	9.37	0.92	0.13
EAS-DS	2026-08-24 17:30:00	16.05	242.32	0.03	7.92	9.43	0.82	0.13
EAS-DS	2026-08-24 17:45:00	15.81	241.83	-0.05	7.85	9.36	1.28	0.13
EAS-DS	2026-08-24 18:00:00	15.61	240.36	0.02	7.85	9.44	1.74	0.13
EAS-DS	2026-08-24 18:15:00	15.63	241.02	0.03	7.84	9.44	1.30	0.13
EAS-DS	2026-08-24 18:30:00	15.20	236.34	0.03	7.80	9.46	0.35	0.13
EAS-DS	2026-08-24 18:45:00	15.83	243.60	-0.05	7.91	9.48	1.03	0.13
EAS-DS	2026-08-24 19:00:00	16.03	242.88	0.03	7.84	9.21	1.02	0.13
EAS-DS	2026-08-24 19:15:00	15.21	238.10	0.03	7.82	9.44	0.37	0.13
EAS-DS	2026-08-24 19:30:00	15.01	238.40	0.03	7.83	9.46	2.07	0.13
EAS-DS	2026-08-24 19:45:00	14.83	238.45	-0.06	7.79	9.48	1.79	0.13
EAS-DS	2026-08-24 20:00:00	14.88	238.20	0.02	7.80	9.48	0.54	0.13
EAS-DS	2026-08-24 20:15:00	15.03	241.10	0.03	7.85	9.61	3.90	0.13
EAS-DS	2026-08-24 20:30:00	15.40	241.12	0.04	7.81	9.37	11.10	0.13
EAS-DS	2026-08-24 20:45:00	14.87	239.81	-0.04	7.81	9.61	0.72	0.13
EAS-DS	2026-08-24 21:00:00	15.12	238.99	0.04	7.87	9.52	2.22	0.13
EAS-DS	2026-08-24 21:15:00	15.27	238.45	0.04	7.78	9.22	0.88	0.13
EAS-DS	2026-08-24 21:30:00	15.33	233.99	0.03	7.82	9.48	1.68	0.12
EAS-DS	2026-08-24 21:45:00	15.36	240.57	-0.05	7.85	9.50	1.24	0.13
EAS-DS	2026-08-24 22:00:00	14.98	239.90	0.03	7.84	9.58	1.42	0.13
EAS-DS	2026-08-24 22:15:00	14.52	234.38	0.04	7.81	9.59	0.45	0.13
EAS-DS	2026-08-24 22:30:00	14.45	236.47	0.03	7.80	9.72	0.75	0.13
EAS-DS	2026-08-24 22:45:00	15.06	242.50	-0.05	7.84	9.53	4.15	0.13
EAS-DS	2026-08-24 23:00:00	14.70	238.75	0.03	7.85	9.67	0.86	0.13
EAS-DS	2026-08-24 23:15:00	14.31	233.59	0.02	7.79	9.64	0.57	0.13
EAS-DS	2026-08-24 23:30:00	14.58	239.55	0.03	7.85	9.68	0.79	0.13
EAS-DS	2026-08-24 23:45:00	14.87	240.28	-0.05	7.82	9.46	1.26	0.13
EAS-DS	2026-08-25 00:00:00	14.50	233.74	0.00	7.78	9.61	0.56	0.13
EAS-DS	2026-08-25 00:15:00	14.36	238.93	0.04	7.82	9.73	0.65	0.13
EAS-DS	2026-08-25 00:30:00	14.74	237.33	0.04	7.89	9.67	1.11	0.13
EAS-DS	2026-08-25 00:45:00	14.52	236.99	-0.04	7.83	9.73	1.30	0.13
EAS-DS	2026-08-25 01:00:00	14.21	235.89	0.04	7.81	9.70	1.02	0.13
EAS-DS	2026-08-25 01:15:00	14.57	236.93	0.04	7.91	9.77	1.43	0.13
EAS-DS	2026-08-25 01:30:00	14.53	237.35	0.04	7.86	9.65	1.34	0.13
EAS-DS	2026-08-25 01:45:00	14.07	237.02	-0.04	7.83	9.85	2.10	0.13
EAS-DS	2026-08-25 02:00:00	14.43	239.00	0.04	7.89	9.80	1.70	0.13
EAS-DS	2026-08-25 02:15:00	14.36	241.22	0.04	7.84	9.75	1.38	0.13
EAS-DS	2026-08-25 02:30:00	14.27	241.84	0.04	7.86	9.79	1.82	0.13
EAS-DS	2026-08-25 02:45:00	13.94	240.35	-0.03	7.85	9.89	1.15	0.13
EAS-DS	2026-08-25 03:00:00	13.88	239.15	0.04	7.86	9.90	1.37	0.13
EAS-DS	2026-08-25 03:15:00	14.29	241.69	0.05	7.88	9.75	1.25	0.13
EAS-DS	2026-08-25 03:30:00	14.33	239.66	0.04	7.75	9.29	0.97	0.13
EAS-DS	2026-08-25 03:45:00	14.55	241.96	-0.05	7.89	9.75	1.52	0.13

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-25 04:00:00	14.55	241.46	0.02	7.79	9.57	1.14	0.13
EAS-DS	2026-08-25 04:15:00	14.52	236.73	0.02	7.73	9.06	1.49	0.13
EAS-DS	2026-08-25 04:30:00	14.59	241.80	0.02	7.82	9.51	0.93	0.13
EAS-DS	2026-08-25 04:45:00	14.72	247.74	-0.06	7.88	9.68	7.81	0.13
EAS-DS	2026-08-25 05:00:00	14.32	244.76	0.02	7.86	9.83	3.12	0.13
EAS-DS	2026-08-25 05:15:00	14.55	247.08	0.02	7.84	9.60	1.81	0.13
EAS-DS	2026-08-25 05:30:00	14.49	237.05	0.02	7.79	9.24	1.62	0.13
EAS-DS	2026-08-25 05:45:00	14.29	240.46	-0.06	7.83	9.79	2.25	0.13
EAS-DS	2026-08-25 06:00:00	14.14	239.00	0.00	7.81	9.80	1.74	0.13
EAS-DS	2026-08-25 06:15:00	13.95	236.82	0.02	7.79	9.81	1.78	0.13
EAS-DS	2026-08-25 06:30:00	14.06	235.44	0.02	7.85	9.86	8.90	0.13
EAS-DS	2026-08-25 06:45:00	14.31	240.87	-0.05	7.87	9.83	2.42	0.13
EAS-DS	2026-08-25 07:00:00	14.12	241.54	0.03	7.84	9.80	4.54	0.13
EAS-DS	2026-08-25 07:15:00	13.80	240.27	0.03	7.85	9.94	3.46	0.13
EAS-DS	2026-08-25 07:30:00	13.76	240.81	0.04	7.84	9.92	1.98	0.13
EAS-DS	2026-08-25 07:45:00	14.25	243.31	-0.05	7.85	9.85	1.93	0.13
EAS-DS	2026-08-25 08:00:00	14.43	246.22	0.03	7.86	9.78	2.60	0.13
EAS-DS	2026-08-25 08:15:00	14.06	248.74	0.04	7.84	9.84	2.21	0.13
EAS-DS	2026-08-25 08:30:00	14.08	250.75	0.04	7.85	9.83	2.57	0.13
EAS-DS	2026-08-25 08:45:00	13.92	248.16	-0.04	7.87	9.91	2.30	0.13
EAS-DS	2026-08-25 09:00:00	13.87	248.45	0.04	7.87	9.92	1.73	0.13
EAS-DS	2026-08-25 09:15:00	14.09	250.39	0.00	7.86	9.82	2.75	0.13
EAS-DS	2026-08-25 09:30:00	14.41	249.69	-0.06	7.89	9.82	0.75	0.13
EAS-DS	2026-08-25 09:45:00	14.44	248.38	0.05	7.72	9.43	0.00	0.13
EAS-DS	2026-08-25 10:00:00	14.44	248.17	0.00	7.68	9.25	0.00	0.13
EAS-DS	2026-08-25 10:15:00	14.43	248.65	0.03	7.90	9.87	0.00	0.13
EAS-DS	2026-08-25 10:30:00	14.61	252.11	-0.05	7.90	9.81	0.00	0.14
EAS-DS	2026-08-25 10:45:00	14.87	256.20	0.02	7.93	9.72	0.00	0.14
EAS-DS	2026-08-25 11:00:00	15.03	260.66	0.02	7.93	9.71	0.00	0.14
EAS-DS	2026-08-25 11:15:00	15.14	260.48	0.04	7.96	9.68	0.00	0.14
EAS-DS	2026-08-25 11:30:00	15.25	262.23	-0.03	7.93	9.64	0.56	0.14
EAS-DS	2026-08-25 11:45:00	15.32	248.14	0.06	7.89	9.62	0.00	0.13
EAS-DS	2026-08-25 12:00:00	15.14	256.73	0.08	7.88	9.55	0.00	0.14
EAS-DS	2026-08-25 12:15:00	15.15	255.15	0.08	7.88	9.54	0.00	0.14
EAS-DS	2026-08-25 12:30:00	15.18	252.64	0.00	7.84	9.59	0.00	0.14
EAS-DS	2026-08-25 12:45:00	15.26	251.29	0.09	7.91	9.57	0.00	0.13
EAS-DS	2026-08-25 13:00:00	15.17	247.82	0.10	7.82	9.39	0.00	0.13
EAS-DS	2026-08-25 13:15:00	15.61	259.80	0.11	7.93	9.55	0.36	0.14
EAS-DS	2026-08-25 13:30:00	15.67	261.73	0.00	7.79	9.15	0.00	0.14
EAS-DS	2026-08-25 13:45:00	15.71	251.28	0.09	7.84	9.42	0.00	0.13
EAS-DS	2026-08-25 14:00:00	15.57	248.24	0.09	7.85	9.50	0.00	0.13
EAS-DS	2026-08-25 14:15:00	15.72	258.26	0.08	7.89	9.41	0.61	0.14
EAS-DS	2026-08-25 14:30:00	15.75	251.87	0.00	7.92	9.51	0.00	0.13
EAS-DS	2026-08-25 14:45:00	15.94	262.77	0.10	7.91	9.37	0.00	0.14
EAS-DS	2026-08-25 15:00:00	16.06	264.29	0.12	7.95	9.44	0.00	0.14
EAS-DS	2026-08-25 15:15:00	15.97	253.45	0.13	7.83	9.21	0.00	0.14
EAS-DS	2026-08-25 15:30:00	16.34	268.43	0.00	7.93	9.36	0.00	0.14
EAS-DS	2026-08-25 15:45:00	16.49	263.07	0.10	8.00	9.36	0.00	0.14
EAS-DS	2026-08-25 16:00:00	16.35	260.42	0.10	7.86	9.07	0.00	0.14
EAS-DS	2026-08-25 16:15:00	16.37	262.69	0.09	8.02	9.38	0.00	0.14
EAS-DS	2026-08-25 16:30:00	16.19	261.96	-0.01	7.89	9.25	0.00	0.14
EAS-DS	2026-08-25 16:45:00	16.13	278.30	0.15	7.93	9.43	0.01	0.15
EAS-DS	2026-08-25 17:00:00	16.07	278.20	0.12	7.93	9.44	0.00	0.15
EAS-DS	2026-08-25 17:15:00	15.93	255.54	0.16	7.79	9.24	0.00	0.14
EAS-DS	2026-08-25 17:30:00	15.74	252.54	-0.03	7.83	9.06	0.00	0.13
EAS-DS	2026-08-25 17:45:00	15.71	264.42	0.13	7.88	9.37	0.00	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-25 18:00:00	15.46	252.55	0.13	7.95	9.45	0.00	0.13
EAS-DS	2026-08-25 18:15:00	15.57	266.43	0.12	7.91	9.41	0.00	0.14
EAS-DS	2026-08-25 18:30:00	15.54	266.31	0.01	7.81	9.39	0.22	0.14
EAS-DS	2026-08-25 18:45:00	15.33	247.95	0.08	7.95	9.58	0.00	0.13
EAS-DS	2026-08-25 19:00:00	15.25	246.79	0.08	7.98	9.52	0.00	0.13
EAS-DS	2026-08-25 19:15:00	15.42	255.62	0.07	7.89	9.20	0.00	0.14
EAS-DS	2026-08-25 19:30:00	15.25	255.08	0.01	7.95	9.60	0.00	0.14
EAS-DS	2026-08-25 19:45:00	15.14	254.96	0.11	7.86	9.53	0.00	0.14
EAS-DS	2026-08-25 20:00:00	15.27	268.92	0.12	7.80	9.44	0.00	0.14
EAS-DS	2026-08-25 20:15:00	15.44	280.82	0.11	7.89	9.37	0.00	0.15
EAS-DS	2026-08-25 20:30:00	15.17	257.62	0.03	7.82	9.48	0.00	0.14
EAS-DS	2026-08-25 20:45:00	14.98	245.95	0.15	7.84	9.51	0.00	0.13
EAS-DS	2026-08-25 21:00:00	14.90	242.55	0.08	7.91	9.50	0.00	0.13
EAS-DS	2026-08-25 21:15:00	15.35	274.95	0.09	7.86	9.53	0.00	0.15
EAS-DS	2026-08-25 21:30:00	15.44	288.17	0.03	7.70	9.13	1.80	0.15
EAS-DS	2026-08-25 21:45:00	15.40	284.97	0.12	7.60	8.67	0.00	0.15
EAS-DS	2026-08-25 22:00:00	15.01	261.34	0.13	7.81	9.54	0.00	0.14
EAS-DS	2026-08-25 22:15:00	15.09	263.60	0.12	7.79	9.51	0.00	0.14
EAS-DS	2026-08-25 22:30:00	14.77	236.36	0.02	7.83	9.48	0.00	0.13
EAS-DS	2026-08-25 22:45:00	14.83	242.88	0.13	7.76	9.22	0.00	0.13
EAS-DS	2026-08-25 23:00:00	14.60	236.16	0.11	7.83	9.64	0.00	0.13
EAS-DS	2026-08-25 23:15:00	15.27	270.19	0.09	7.81	9.48	0.00	0.14
EAS-DS	2026-08-25 23:30:00	15.41	260.57	0.01	7.77	9.39	0.00	0.14
EAS-DS	2026-08-25 23:45:00	14.53	230.32	0.10	7.83	9.68	0.00	0.12
EAS-DS	2026-08-26 00:00:00	14.38	227.42	0.08	7.82	9.75	0.00	0.12
EAS-DS	2026-08-26 00:15:00	14.39	227.59	0.12	7.90	9.63	0.00	0.12
EAS-DS	2026-08-26 00:30:00	14.34	233.07	0.02	7.73	9.69	0.00	0.12
EAS-DS	2026-08-26 00:45:00	14.40	232.60	0.10	7.73	9.47	0.00	0.12
EAS-DS	2026-08-26 01:00:00	15.29	269.91	0.17	7.89	9.51	0.00	0.14
EAS-DS	2026-08-26 01:15:00	14.54	237.03	0.16	7.80	9.73	0.00	0.13
EAS-DS	2026-08-26 01:30:00	14.37	234.13	0.01	7.83	9.63	0.00	0.13
EAS-DS	2026-08-26 01:45:00	14.31	232.68	0.11	7.87	9.64	0.00	0.12
EAS-DS	2026-08-26 02:00:00	14.28	237.31	0.12	7.88	9.75	0.00	0.13
EAS-DS	2026-08-26 02:15:00	14.63	254.97	0.11	7.85	9.65	0.00	0.14
EAS-DS	2026-08-26 02:30:00	14.31	235.30	0.03	7.76	9.62	0.00	0.13
EAS-DS	2026-08-26 02:45:00	14.21	233.22	0.14	7.83	9.78	0.00	0.12
EAS-DS	2026-08-26 03:00:00	14.49	256.31	0.13	7.80	9.69	0.00	0.13
EAS-DS	2026-08-26 03:15:00	14.75	270.06	0.16	7.75	9.59	0.00	0.14
EAS-DS	2026-08-26 03:30:00	14.80	269.00	0.01	7.80	9.37	0.00	0.14
EAS-DS	2026-08-26 03:45:00	14.36	239.46	0.13	7.74	9.56	0.00	0.13
EAS-DS	2026-08-26 04:00:00	14.43	236.17	0.13	7.71	9.19	0.00	0.13
EAS-DS	2026-08-26 04:15:00	14.60	256.38	0.11	7.76	9.60	0.00	0.14
EAS-DS	2026-08-26 04:30:00	14.53	258.13	0.02	7.73	9.70	0.00	0.14
EAS-DS	2026-08-26 04:45:00	14.25	237.13	0.14	7.77	9.63	0.00	0.13
EAS-DS	2026-08-26 05:00:00	14.35	233.91	0.14	7.78	9.47	0.00	0.13
EAS-DS	2026-08-26 05:15:00	14.53	266.65	0.14	7.76	9.73	0.00	0.14
EAS-DS	2026-08-26 05:30:00	14.70	284.02	0.02	7.66	9.51	0.00	0.15
EAS-DS	2026-08-26 05:45:00	14.27	242.10	0.11	7.80	9.60	0.00	0.13
EAS-DS	2026-08-26 06:00:00	14.22	240.57	0.12	7.76	9.60	0.00	0.13
EAS-DS	2026-08-26 06:15:00	14.40	253.69	0.11	7.74	9.51	0.00	0.14
EAS-DS	2026-08-26 06:30:00	14.39	256.16	0.00	7.81	9.70	0.00	0.14
EAS-DS	2026-08-26 06:45:00	14.22	237.19	0.08	7.89	9.78	0.00	0.13
EAS-DS	2026-08-26 07:00:00	14.15	233.95	0.09	7.92	9.84	0.09	0.13
EAS-DS	2026-08-26 07:15:00	14.22	249.92	0.09	7.86	9.76	0.00	0.13
EAS-DS	2026-08-26 07:30:00	14.22	260.73	0.03	7.75	9.73	0.00	0.14
EAS-DS	2026-08-26 07:45:00	14.27	266.41	0.13	7.68	9.51	0.00	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-26 08:00:00	14.31	262.15	0.12	7.65	9.28	0.00	0.14
EAS-DS	2026-08-26 08:15:00	14.41	279.90	0.11	7.68	9.49	0.00	0.15
EAS-DS	2026-08-26 08:30:00	14.40	284.45	0.03	7.65	9.53	0.00	0.15
EAS-DS	2026-08-26 08:45:00	14.39	287.79	0.14	7.63	9.42	0.00	0.15
EAS-DS	2026-08-26 09:00:00	14.49	261.40	0.12	7.71	9.38	0.00	0.14
EAS-DS	2026-08-26 09:15:00	14.46	270.78	0.13	7.76	9.73	0.00	0.15
EAS-DS	2026-08-26 09:30:00	14.49	275.87	0.03	7.76	9.80	0.00	0.15
EAS-DS	2026-08-26 09:45:00	14.53	262.99	0.12	7.78	9.66	0.00	0.14
EAS-DS	2026-08-26 10:00:00	14.53	244.64	0.12	7.82	9.79	0.00	0.13
EAS-DS	2026-08-26 10:15:00	14.65	258.50	0.12	7.81	9.76	0.00	0.14
EAS-DS	2026-08-26 10:30:00	14.81	279.98	0.03	7.70	9.46	0.00	0.15
EAS-DS	2026-08-26 10:45:00	15.00	280.21	0.14	7.74	9.42	0.00	0.15
EAS-DS	2026-08-26 11:00:00	15.02	260.88	0.14	7.82	9.56	0.00	0.14
EAS-DS	2026-08-26 11:15:00	14.94	238.68	0.14	7.82	9.51	0.00	0.13
EAS-DS	2026-08-26 11:30:00	15.18	271.00	0.02	7.74	9.42	0.00	0.15
EAS-DS	2026-08-26 11:45:00	15.37	258.60	0.11	7.81	9.55	0.00	0.14
EAS-DS	2026-08-26 12:00:00	15.35	258.69	0.11	7.82	9.49	0.00	0.14
EAS-DS	2026-08-26 12:15:00	15.38	244.20	0.10	7.87	9.56	0.00	0.13
EAS-DS	2026-08-26 12:30:00	15.40	238.43	0.02	7.82	9.40	0.00	0.13
EAS-DS	2026-08-26 12:45:00	15.60	267.24	0.13	7.79	9.38	0.00	0.14
EAS-DS	2026-08-26 13:00:00	15.75	278.66	0.06	7.88	9.35	0.00	0.15
EAS-DS	2026-08-26 13:15:00	15.75	241.89	0.06	7.90	9.32	0.00	0.13
EAS-DS	2026-08-26 13:30:00	15.73	243.55	0.01	7.69	8.91	0.00	0.13
EAS-DS	2026-08-26 13:45:00	16.01	274.51	0.10	7.76	9.24	0.00	0.15
EAS-DS	2026-08-26 14:00:00	16.07	283.04	0.12	7.77	9.41	0.00	0.15
EAS-DS	2026-08-26 14:15:00	16.19	267.52	0.11	7.83	9.28	0.00	0.14
EAS-DS	2026-08-26 14:30:00	15.91	261.46	0.01	7.82	9.33	0.00	0.14
EAS-DS	2026-08-26 14:45:00	15.86	260.39	0.13	7.84	9.36	0.00	0.14
EAS-DS	2026-08-26 15:00:00	15.78	242.17	0.13	7.84	9.30	0.00	0.13
EAS-DS	2026-08-26 15:15:00	16.04	267.68	0.13	7.83	9.19	0.00	0.14
EAS-DS	2026-08-26 15:30:00	16.16	263.50	0.01	7.76	9.07	0.00	0.14
EAS-DS	2026-08-26 15:45:00	16.24	269.79	0.10	7.76	9.08	0.00	0.14
EAS-DS	2026-08-26 16:00:00	16.17	259.64	0.11	7.71	8.88	0.00	0.14
EAS-DS	2026-08-26 16:15:00	16.23	243.27	0.11	7.79	9.01	0.00	0.13
EAS-DS	2026-08-26 16:30:00	16.07	253.58	0.01	7.82	9.30	0.00	0.14
EAS-DS	2026-08-26 16:45:00	16.08	255.70	0.13	7.83	9.37	0.00	0.14
EAS-DS	2026-08-26 17:00:00	16.22	264.55	0.12	7.78	9.31	0.00	0.14
EAS-DS	2026-08-26 17:15:00	16.15	259.00	0.12	7.76	9.38	0.00	0.14
EAS-DS	2026-08-26 17:30:00	16.13	262.08	0.01	7.67	8.92	0.00	0.14
EAS-DS	2026-08-26 17:45:00	15.88	240.63	0.11	7.81	9.25	0.00	0.13
EAS-DS	2026-08-26 18:00:00	15.75	244.29	0.11	7.83	9.34	0.00	0.13
EAS-DS	2026-08-26 18:15:00	15.68	246.95	0.11	7.82	9.40	0.00	0.13
EAS-DS	2026-08-26 18:30:00	15.51	242.70	0.01	7.80	9.40	0.00	0.13
EAS-DS	2026-08-26 18:45:00	15.51	247.62	0.13	7.81	9.46	0.00	0.13
EAS-DS	2026-08-26 19:00:00	15.53	248.86	0.13	7.77	9.27	0.00	0.13
EAS-DS	2026-08-26 19:15:00	15.52	236.31	0.13	7.78	9.13	0.00	0.13
EAS-DS	2026-08-26 19:30:00	15.15	231.05	0.01	7.78	9.35	0.00	0.12
EAS-DS	2026-08-26 19:45:00	14.94	229.97	0.10	7.81	9.38	0.00	0.12
EAS-DS	2026-08-26 20:00:00	14.87	229.09	0.11	7.79	9.41	0.00	0.12
EAS-DS	2026-08-26 20:15:00	14.84	228.55	0.10	7.78	9.37	0.00	0.12
EAS-DS	2026-08-26 20:30:00	15.06	243.39	0.02	7.78	9.47	0.00	0.13
EAS-DS	2026-08-26 20:45:00	15.05	251.47	0.14	7.82	9.61	0.00	0.13
EAS-DS	2026-08-26 21:00:00	15.18	258.56	0.14	7.75	9.31	0.00	0.14
EAS-DS	2026-08-26 21:15:00	14.71	227.75	0.13	7.83	9.65	0.00	0.12
EAS-DS	2026-08-26 21:30:00	14.71	229.49	0.02	7.73	9.28	0.00	0.12
EAS-DS	2026-08-26 21:45:00	14.82	239.93	0.11	7.80	9.50	0.00	0.13

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-26 22:00:00	14.65	239.98	0.11	7.82	9.62	0.00	0.13
EAS-DS	2026-08-26 22:15:00	14.40	225.49	0.11	7.83	9.63	0.00	0.12
EAS-DS	2026-08-26 22:30:00	14.27	224.42	0.02	7.82	9.69	0.00	0.12
EAS-DS	2026-08-26 22:45:00	14.47	237.68	0.12	7.82	9.69	0.00	0.13
EAS-DS	2026-08-26 23:00:00	14.48	239.23	0.14	7.81	9.69	0.00	0.13
EAS-DS	2026-08-26 23:15:00	14.59	242.28	0.14	7.74	9.44	0.00	0.13
EAS-DS	2026-08-26 23:30:00	14.60	235.77	0.03	7.68	9.14	0.00	0.13
EAS-DS	2026-08-26 23:45:00	14.72	251.64	0.10	7.75	9.53	0.00	0.13
EAS-DS	2026-08-27 00:00:00	14.26	225.90	0.12	7.81	9.81	1.92	0.12
EAS-DS	2026-08-27 00:15:00	14.09	223.85	0.12	7.81	9.79	0.00	0.12
EAS-DS	2026-08-27 00:30:00	14.31	238.78	0.03	7.78	9.72	0.00	0.13
EAS-DS	2026-08-27 00:45:00	14.27	235.04	0.14	7.79	9.66	0.00	0.13
EAS-DS	2026-08-27 01:00:00	13.97	222.02	0.14	7.83	9.85	0.00	0.12
EAS-DS	2026-08-27 01:15:00	13.94	221.18	0.14	7.81	9.74	0.00	0.12
EAS-DS	2026-08-27 01:30:00	13.95	226.39	0.03	7.78	9.81	0.00	0.12
EAS-DS	2026-08-27 01:45:00	14.33	245.08	0.13	7.75	9.68	0.00	0.13
EAS-DS	2026-08-27 02:00:00	14.47	253.14	0.15	7.69	9.55	0.00	0.14
EAS-DS	2026-08-27 02:15:00	14.43	251.44	0.13	7.64	9.16	0.00	0.13
EAS-DS	2026-08-27 02:30:00	14.44	239.62	0.03	7.63	9.06	0.00	0.13
EAS-DS	2026-08-27 02:45:00	14.25	222.93	0.15	7.77	9.39	0.00	0.12
EAS-DS	2026-08-27 03:00:00	14.08	239.13	0.15	7.77	9.77	0.00	0.13
EAS-DS	2026-08-27 03:15:00	14.10	246.17	0.15	7.78	9.76	0.00	0.13
EAS-DS	2026-08-27 03:30:00	14.15	237.65	0.03	7.67	9.36	0.00	0.13
EAS-DS	2026-08-27 03:45:00	14.19	234.37	0.14	7.63	9.16	0.00	0.13
EAS-DS	2026-08-27 04:00:00	14.06	238.26	0.14	7.78	9.73	0.00	0.13
EAS-DS	2026-08-27 04:15:00	13.83	222.49	0.15	7.81	9.77	0.00	0.12
EAS-DS	2026-08-27 04:30:00	13.95	242.15	0.03	7.78	9.80	0.00	0.13
EAS-DS	2026-08-27 04:45:00	14.13	250.86	0.18	7.78	9.72	0.00	0.13
EAS-DS	2026-08-27 05:00:00	14.12	253.48	0.17	7.76	9.70	0.00	0.14
EAS-DS	2026-08-27 05:15:00	14.11	237.97	0.17	7.77	9.38	0.00	0.13
EAS-DS	2026-08-27 05:30:00	13.98	235.65	0.05	7.75	9.63	0.00	0.13
EAS-DS	2026-08-27 05:45:00	13.99	248.59	0.16	7.76	9.73	0.00	0.13
EAS-DS	2026-08-27 06:00:00	13.87	243.53	0.16	7.77	9.80	0.00	0.13
EAS-DS	2026-08-27 06:15:00	13.71	227.15	0.16	7.82	9.90	0.00	0.12
EAS-DS	2026-08-27 06:30:00	13.70	224.66	0.04	7.77	9.71	0.00	0.12
EAS-DS	2026-08-27 06:45:00	13.89	251.60	0.17	7.80	9.80	0.00	0.14
EAS-DS	2026-08-27 07:00:00	13.97	257.70	0.17	7.79	9.78	0.00	0.14
EAS-DS	2026-08-27 07:15:00	13.77	229.38	0.17	7.85	9.82	0.00	0.12
EAS-DS	2026-08-27 07:30:00	13.71	228.86	0.04	7.81	9.81	0.00	0.12
EAS-DS	2026-08-27 07:45:00	13.86	252.27	0.15	7.79	9.83	0.00	0.14
EAS-DS	2026-08-27 08:00:00	13.93	256.63	0.17	7.71	9.46	0.00	0.14
EAS-DS	2026-08-27 08:15:00	13.97	253.82	0.16	7.64	9.20	0.00	0.14
EAS-DS	2026-08-27 08:30:00	13.97	268.25	0.01	7.69	9.61	0.00	0.14
EAS-DS	2026-08-27 08:45:00	13.94	265.78	0.18	7.72	9.66	0.00	0.14
EAS-DS	2026-08-27 09:00:00	13.97	265.61	0.17	7.70	9.44	0.00	0.14
EAS-DS	2026-08-27 09:15:00	14.05	267.44	0.18	7.75	9.63	0.00	0.14
EAS-DS	2026-08-27 09:30:00	14.02	249.70	0.00	7.77	9.76	0.00	0.13
EAS-DS	2026-08-27 09:45:00	14.02	247.43	0.17	7.79	9.76	1.75	0.13
EAS-DS	2026-08-27 10:00:00	14.09	253.37	0.17	7.77	9.76	0.00	0.14
EAS-DS	2026-08-27 10:15:00	14.15	246.60	0.17	7.75	9.55	0.00	0.13
EAS-DS	2026-08-27 10:30:00	14.24	258.26	0.03	7.73	9.56	0.00	0.14
EAS-DS	2026-08-27 10:45:00	14.17	245.49	0.19	7.82	9.74	0.88	0.13
EAS-DS	2026-08-27 11:00:00	14.11	236.78	0.19	7.83	9.74	0.00	0.13
EAS-DS	2026-08-27 11:15:00	14.21	250.74	0.19	7.79	9.64	0.00	0.13
EAS-DS	2026-08-27 11:30:00	14.32	254.37	0.04	7.77	9.64	0.00	0.14
EAS-DS	2026-08-27 11:45:00	14.38	262.39	0.17	7.78	9.48	0.00	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-27 12:00:00	14.42	266.47	0.17	7.74	9.34	0.00	0.14
EAS-DS	2026-08-27 12:15:00	14.42	265.95	0.18	7.70	9.28	0.00	0.14
EAS-DS	2026-08-27 12:30:00	14.34	249.26	0.04	7.76	9.67	0.00	0.13
EAS-DS	2026-08-27 12:45:00	14.27	250.14	0.18	7.83	9.70	0.00	0.13
EAS-DS	2026-08-27 13:00:00	14.27	246.44	0.19	7.84	9.75	0.00	0.13
EAS-DS	2026-08-27 13:15:00	14.22	230.50	0.19	7.84	9.80	0.00	0.12
EAS-DS	2026-08-27 13:30:00	14.42	261.55	0.04	7.79	9.60	0.00	0.14
EAS-DS	2026-08-27 13:45:00	14.53	266.64	0.18	7.78	9.55	0.00	0.14
EAS-DS	2026-08-27 14:00:00	14.54	251.91	0.19	7.76	9.33	0.00	0.14
EAS-DS	2026-08-27 14:15:00	14.59	259.64	0.19	7.84	9.65	0.00	0.14
EAS-DS	2026-08-27 14:30:00	14.55	258.59	0.04	7.82	9.62	2.66	0.14
EAS-DS	2026-08-27 14:45:00	14.56	249.68	0.19	7.76	9.29	0.00	0.13
EAS-DS	2026-08-27 15:00:00	14.70	269.64	0.19	7.77	9.36	0.00	0.15
EAS-DS	2026-08-27 15:15:00	14.79	283.00	0.19	7.78	9.38	0.00	0.15
EAS-DS	2026-08-27 15:30:00	14.77	278.83	0.04	7.68	8.97	0.52	0.15
EAS-DS	2026-08-27 15:45:00	14.88	287.21	0.19	7.74	9.29	0.00	0.15
EAS-DS	2026-08-27 16:00:00	14.92	287.03	0.18	7.73	9.12	0.00	0.15
EAS-DS	2026-08-27 16:15:00	14.90	288.71	0.18	7.69	9.02	0.00	0.16
EAS-DS	2026-08-27 16:30:00	15.03	285.66	0.03	7.74	9.28	0.00	0.15
EAS-DS	2026-08-27 16:45:00	14.89	261.12	0.19	7.84	9.51	3.74	0.14
EAS-DS	2026-08-27 17:00:00	14.66	240.33	0.19	7.87	9.54	0.00	0.13
EAS-DS	2026-08-27 17:15:00	14.68	260.37	0.19	7.86	9.59	0.00	0.14
EAS-DS	2026-08-27 17:30:00	14.76	268.98	0.05	7.77	9.46	0.00	0.14
EAS-DS	2026-08-27 17:45:00	14.62	261.13	0.19	7.83	9.59	50.11	0.14
EAS-DS	2026-08-27 18:00:00	14.50	261.88	0.20	7.85	9.63	0.00	0.14
EAS-DS	2026-08-27 18:15:00	14.44	260.73	0.19	7.78	9.66	0.00	0.14
EAS-DS	2026-08-27 18:30:00	14.34	247.05	0.02	7.87	9.59	0.00	0.13
EAS-DS	2026-08-27 18:45:00	14.37	255.35	0.19	7.87	9.65	0.00	0.14
EAS-DS	2026-08-27 19:00:00	14.38	257.51	0.21	7.89	9.61	0.00	0.14
EAS-DS	2026-08-27 19:15:00	14.41	256.64	0.20	7.89	9.51	0.00	0.14
EAS-DS	2026-08-27 19:30:00	14.37	237.55	0.08	7.90	9.49	0.00	0.13
EAS-DS	2026-08-27 19:45:00	14.25	238.05	0.17	7.93	9.62	0.00	0.13
EAS-DS	2026-08-27 20:00:00	14.21	240.29	0.18	7.93	9.70	0.00	0.13
EAS-DS	2026-08-27 20:15:00	14.31	253.68	0.17	7.91	9.69	0.00	0.14
EAS-DS	2026-08-27 20:30:00	14.34	261.86	0.04	7.82	9.53	0.00	0.14
EAS-DS	2026-08-27 20:45:00	14.34	271.40	0.19	7.82	9.55	0.00	0.15
EAS-DS	2026-08-27 21:00:00	14.36	270.40	0.19	7.77	9.21	0.00	0.15
EAS-DS	2026-08-27 21:15:00	14.36	271.36	0.19	7.74	9.25	0.00	0.15
EAS-DS	2026-08-27 21:30:00	14.28	251.12	0.07	7.83	9.45	0.00	0.13
EAS-DS	2026-08-27 21:45:00	14.28	251.64	0.18	7.87	9.64	0.00	0.13
EAS-DS	2026-08-27 22:00:00	14.27	259.91	0.19	7.82	9.73	0.00	0.14
EAS-DS	2026-08-27 22:15:00	14.27	259.63	0.19	7.86	9.71	0.00	0.14
EAS-DS	2026-08-27 22:30:00	14.13	243.54	0.05	7.89	9.68	0.00	0.13
EAS-DS	2026-08-27 22:45:00	14.18	254.26	0.20	7.87	9.64	0.00	0.14
EAS-DS	2026-08-27 23:00:00	14.16	241.66	0.20	7.90	9.68	0.00	0.13
EAS-DS	2026-08-27 23:15:00	14.07	238.29	0.20	7.89	9.74	0.00	0.13
EAS-DS	2026-08-27 23:30:00	14.18	242.66	0.07	7.85	9.69	0.00	0.13
EAS-DS	2026-08-27 23:45:00	14.22	239.04	0.18	7.87	9.62	0.00	0.13
EAS-DS	2026-08-28 00:00:00	14.40	256.51	0.18	7.83	9.59	0.00	0.14
EAS-DS	2026-08-28 00:15:00	14.39	256.50	0.19	7.85	9.47	0.00	0.14
EAS-DS	2026-08-28 00:30:00	14.26	250.37	-0.02	7.80	9.55	0.00	0.13
EAS-DS	2026-08-28 00:45:00	14.16	242.92	0.20	7.84	9.58	0.00	0.13
EAS-DS	2026-08-28 01:00:00	14.07	250.79	0.20	7.83	9.76	0.00	0.13
EAS-DS	2026-08-28 01:15:00	14.04	250.91	0.20	7.78	9.76	0.00	0.13
EAS-DS	2026-08-28 01:30:00	14.02	239.86	0.08	7.85	9.69	0.00	0.13
EAS-DS	2026-08-28 01:45:00	13.91	229.90	0.19	7.90	9.79	0.00	0.12

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-28 02:00:00	14.04	247.36	0.18	7.85	9.71	0.00	0.13
EAS-DS	2026-08-28 02:15:00	14.14	255.56	0.19	7.81	9.48	0.00	0.14
EAS-DS	2026-08-28 02:30:00	14.17	262.94	0.03	7.71	9.36	0.62	0.14
EAS-DS	2026-08-28 02:45:00	14.15	267.65	0.22	7.70	9.50	0.00	0.14
EAS-DS	2026-08-28 03:00:00	14.18	267.73	0.22	7.78	9.69	0.00	0.14
EAS-DS	2026-08-28 03:15:00	14.02	255.54	0.21	7.77	9.66	0.00	0.14
EAS-DS	2026-08-28 03:30:00	13.84	237.82	-0.01	7.79	9.74	0.00	0.13
EAS-DS	2026-08-28 03:45:00	13.87	252.98	0.20	7.77	9.80	0.00	0.14
EAS-DS	2026-08-28 04:00:00	13.97	262.25	0.22	7.72	9.67	0.00	0.14
EAS-DS	2026-08-28 04:15:00	13.86	229.30	0.21	7.89	9.81	0.00	0.12
EAS-DS	2026-08-28 04:30:00	13.80	235.90	0.00	7.72	9.60	0.00	0.13
EAS-DS	2026-08-28 04:45:00	13.88	246.69	0.22	7.77	9.59	0.00	0.13
EAS-DS	2026-08-28 05:00:00	13.83	250.06	0.22	7.85	9.82	0.00	0.13
EAS-DS	2026-08-28 05:15:00	13.90	259.48	0.23	7.84	9.81	0.00	0.14
EAS-DS	2026-08-28 05:30:00	13.90	254.58	0.05	7.75	9.77	0.00	0.14
EAS-DS	2026-08-28 05:45:00	13.78	234.04	0.22	7.82	9.66	0.00	0.13
EAS-DS	2026-08-28 06:00:00	13.87	245.16	0.22	7.81	9.65	0.00	0.13
EAS-DS	2026-08-28 06:15:00	13.85	238.77	0.22	7.90	9.74	0.00	0.13
EAS-DS	2026-08-28 06:30:00	13.81	250.27	0.07	7.83	9.84	0.00	0.13
EAS-DS	2026-08-28 06:45:00	13.80	251.49	0.21	7.84	9.72	0.00	0.14
EAS-DS	2026-08-28 07:00:00	13.72	238.13	0.22	7.88	9.74	0.00	0.13
EAS-DS	2026-08-28 07:15:00	13.85	253.63	0.22	7.81	9.50	0.00	0.14
EAS-DS	2026-08-28 07:30:00	13.84	258.63	0.01	7.72	9.76	0.00	0.14
EAS-DS	2026-08-28 07:45:00	13.89	263.82	0.21	7.68	9.37	2.96	0.14
EAS-DS	2026-08-28 08:00:00	13.90	259.84	0.22	7.70	9.05	0.00	0.14
EAS-DS	2026-08-28 08:15:00	13.98	252.98	0.11	7.80	9.30	0.00	0.14
EAS-DS	2026-08-28 08:30:00	13.95	268.94	0.01	7.64	9.50	50.60	0.14
EAS-DS	2026-08-28 08:45:00	14.01	259.28	0.16	7.74	9.52	0.00	0.14
EAS-DS	2026-08-28 09:00:00	13.95	252.27	0.20	7.83	9.70	0.00	0.14
EAS-DS	2026-08-28 09:15:00	13.99	252.83	0.24	7.75	9.10	0.00	0.14
EAS-DS	2026-08-28 09:30:00	13.98	252.51	0.03	7.72	9.74	0.00	0.14
EAS-DS	2026-08-28 09:45:00	14.03	245.26	0.22	7.85	9.76	0.00	0.13
EAS-DS	2026-08-28 10:00:00	14.02	228.78	-0.07	7.87	9.86	0.00	0.12
EAS-DS	2026-08-28 10:15:00	14.18	258.43	0.16	7.88	9.88	0.00	0.14
EAS-DS	2026-08-28 10:30:00	14.32	267.35	0.18	7.85	9.82	0.00	0.14
EAS-DS	2026-08-28 10:45:00	14.11	234.39	0.18	7.94	9.91	0.00	0.13
EAS-DS	2026-08-28 11:00:00	14.13	239.82	0.02	7.85	9.91	1.79	0.13
EAS-DS	2026-08-28 11:15:00	14.14	241.78	0.18	7.87	9.90	0.32	0.13
EAS-DS	2026-08-28 11:30:00	14.12	241.31	0.19	7.88	9.90	1.02	0.13
EAS-DS	2026-08-28 11:45:00	14.35	261.06	0.19	7.85	9.81	0.78	0.14
EAS-DS	2026-08-28 12:00:00	14.32	266.41	0.02	7.74	9.45	0.00	0.14
EAS-DS	2026-08-28 12:15:00	14.45	271.51	0.18	7.83	9.79	0.00	0.15
EAS-DS	2026-08-28 12:30:00	14.25	249.92	0.18	7.89	9.87	0.00	0.13
EAS-DS	2026-08-28 12:45:00	14.18	250.51	0.18	7.89	9.89	4.03	0.13
EAS-DS	2026-08-28 13:00:00	14.09	227.72	0.01	7.90	9.89	0.00	0.12
EAS-DS	2026-08-28 13:15:00	14.05	227.24	0.17	7.90	9.94	0.00	0.12
EAS-DS	2026-08-28 13:30:00	14.25	244.14	0.17	7.92	9.88	0.51	0.13
EAS-DS	2026-08-28 13:45:00	14.47	257.57	0.18	7.87	9.79	0.00	0.14
EAS-DS	2026-08-28 14:00:00	14.54	251.72	-0.03	7.79	9.79	0.32	0.13
EAS-DS	2026-08-28 14:15:00	14.36	252.36	0.17	7.86	9.84	0.11	0.14
EAS-DS	2026-08-28 14:30:00	14.44	257.36	0.18	7.86	9.80	0.00	0.14
EAS-DS	2026-08-28 14:45:00	14.47	243.08	0.18	7.86	9.61	0.00	0.13
EAS-DS	2026-08-28 15:00:00	14.43	249.54	0.02	7.85	9.81	0.00	0.13
EAS-DS	2026-08-28 15:15:00	14.47	253.93	0.18	7.85	9.77	0.02	0.14
EAS-DS	2026-08-28 15:30:00	14.51	255.95	0.18	7.81	9.42	0.00	0.14
EAS-DS	2026-08-28 15:45:00	14.57	254.93	0.18	7.86	9.78	2.26	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-28 16:00:00	14.15	233.76	0.02	7.87	9.87	0.00	0.13
EAS-DS	2026-08-28 16:15:00	14.02	232.37	0.17	7.92	9.90	0.00	0.12
EAS-DS	2026-08-28 16:30:00	14.16	246.70	0.18	7.89	9.89	1.78	0.13
EAS-DS	2026-08-28 16:45:00	14.23	252.13	0.18	7.90	9.86	0.18	0.14
EAS-DS	2026-08-28 17:00:00	14.38	264.08	0.02	7.79	9.64	0.00	0.14
EAS-DS	2026-08-28 17:15:00	14.36	253.62	0.19	7.88	9.83	0.43	0.14
EAS-DS	2026-08-28 17:30:00	14.30	250.55	0.19	7.92	9.83	0.00	0.13
EAS-DS	2026-08-28 17:45:00	14.39	258.78	0.19	7.82	9.43	0.00	0.14
EAS-DS	2026-08-28 18:00:00	14.28	247.90	-0.06	7.83	9.82	0.43	0.13
EAS-DS	2026-08-28 18:15:00	14.18	260.15	0.08	7.87	9.87	1.77	0.14
EAS-DS	2026-08-28 18:30:00	14.12	257.63	0.21	7.86	9.88	2.81	0.14
EAS-DS	2026-08-28 18:45:00	13.96	239.75	0.20	7.93	9.92	0.31	0.13
EAS-DS	2026-08-28 19:00:00	14.18	256.12	0.07	7.86	9.87	0.02	0.14
EAS-DS	2026-08-28 19:15:00	14.29	263.02	0.17	7.90	9.82	0.49	0.14
EAS-DS	2026-08-28 19:30:00	13.98	230.55	0.19	7.94	9.90	2.06	0.12
EAS-DS	2026-08-28 19:45:00	14.04	253.54	0.10	7.88	9.90	1.79	0.14
EAS-DS	2026-08-28 20:00:00	13.91	237.23	0.00	7.92	9.90	0.00	0.13
EAS-DS	2026-08-28 20:15:00	13.96	243.58	0.19	7.92	9.92	0.23	0.13
EAS-DS	2026-08-28 20:30:00	13.96	250.19	0.20	7.95	9.83	0.00	0.13
EAS-DS	2026-08-28 20:45:00	14.00	242.52	0.20	7.86	9.46	0.00	0.13
EAS-DS	2026-08-28 21:00:00	14.05	232.57	-0.02	7.70	9.29	0.00	0.12
EAS-DS	2026-08-28 21:15:00	14.03	254.31	0.19	7.86	9.88	0.13	0.14
EAS-DS	2026-08-28 21:30:00	14.02	246.70	0.20	7.81	9.54	0.00	0.13
EAS-DS	2026-08-28 21:45:00	13.99	251.59	0.20	7.85	9.88	0.00	0.14
EAS-DS	2026-08-28 22:00:00	13.96	258.52	0.05	7.86	9.90	0.91	0.14
EAS-DS	2026-08-28 22:15:00	13.99	260.59	0.19	7.86	9.89	0.23	0.14
EAS-DS	2026-08-28 22:30:00	13.77	233.65	0.20	7.93	9.96	0.00	0.13
EAS-DS	2026-08-28 22:45:00	13.70	231.56	0.20	7.95	9.95	0.00	0.12
EAS-DS	2026-08-28 23:00:00	13.72	232.61	0.05	7.92	9.96	0.37	0.12
EAS-DS	2026-08-28 23:15:00	14.02	251.02	0.19	7.87	9.89	1.37	0.13
EAS-DS	2026-08-28 23:30:00	14.00	251.08	0.19	7.92	9.88	0.00	0.13
EAS-DS	2026-08-28 23:45:00	14.00	251.64	0.19	7.85	9.52	0.00	0.14
EAS-DS	2026-08-29 00:00:00	14.07	268.85	-0.03	7.87	9.86	0.00	0.14
EAS-DS	2026-08-29 00:15:00	14.12	266.29	0.20	7.90	9.86	2.78	0.14
EAS-DS	2026-08-29 00:30:00	13.81	253.39	0.20	7.92	9.94	0.00	0.14
EAS-DS	2026-08-29 00:45:00	14.02	278.66	0.20	7.91	9.88	0.03	0.15
EAS-DS	2026-08-29 01:00:00	14.09	278.74	-0.02	7.82	9.56	0.00	0.15
EAS-DS	2026-08-29 01:15:00	13.90	260.07	0.20	7.89	9.91	2.43	0.14
EAS-DS	2026-08-29 01:30:00	13.82	256.75	0.21	7.95	9.94	1.67	0.14
EAS-DS	2026-08-29 01:45:00	13.72	248.51	0.20	7.97	9.93	0.00	0.13
EAS-DS	2026-08-29 02:00:00	13.74	260.78	0.02	7.93	9.96	0.91	0.14
EAS-DS	2026-08-29 02:15:00	13.55	246.06	0.18	7.96	9.99	0.47	0.13
EAS-DS	2026-08-29 02:30:00	13.62	246.47	0.19	7.89	9.62	0.00	0.13
EAS-DS	2026-08-29 02:45:00	13.87	274.76	0.19	7.90	9.88	0.97	0.15
EAS-DS	2026-08-29 03:00:00	14.00	280.68	0.00	7.91	9.87	2.48	0.15
EAS-DS	2026-08-29 03:15:00	13.98	274.99	0.19	7.89	9.75	0.00	0.15
EAS-DS	2026-08-29 03:30:00	13.96	274.52	0.20	7.83	9.59	0.00	0.15
EAS-DS	2026-08-29 03:45:00	13.92	274.15	0.20	7.75	9.24	0.00	0.15
EAS-DS	2026-08-29 04:00:00	13.72	244.49	0.00	7.88	9.81	0.45	0.13
EAS-DS	2026-08-29 04:15:00	13.69	259.16	0.19	7.93	9.97	0.31	0.14
EAS-DS	2026-08-29 04:30:00	13.72	262.36	0.20	7.93	9.96	1.75	0.14
EAS-DS	2026-08-29 04:45:00	13.67	248.83	0.20	7.96	9.95	0.63	0.13
EAS-DS	2026-08-29 05:00:00	13.70	261.08	0.02	7.87	9.97	1.48	0.14
EAS-DS	2026-08-29 05:15:00	13.82	271.72	0.20	7.94	9.90	0.43	0.15
EAS-DS	2026-08-29 05:30:00	13.94	283.94	0.20	7.88	9.78	0.00	0.15
EAS-DS	2026-08-29 05:45:00	13.66	259.87	0.20	7.95	9.97	1.05	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-29 06:00:00	13.69	268.06	0.00	7.89	9.97	1.79	0.14
EAS-DS	2026-08-29 06:15:00	13.55	247.30	0.19	7.90	9.78	0.00	0.13
EAS-DS	2026-08-29 06:30:00	13.82	287.92	0.20	7.91	9.92	6.95	0.16
EAS-DS	2026-08-29 06:45:00	13.54	251.46	0.20	7.97	9.96	0.21	0.14
EAS-DS	2026-08-29 07:00:00	13.42	238.38	-0.05	7.96	10.02	2.51	0.13
EAS-DS	2026-08-29 07:15:00	13.59	254.52	0.19	7.92	10.00	1.81	0.14
EAS-DS	2026-08-29 07:30:00	13.49	238.03	0.21	7.96	9.98	0.31	0.13
EAS-DS	2026-08-29 07:45:00	13.46	244.99	0.21	7.94	10.05	3.06	0.13
EAS-DS	2026-08-29 08:00:00	13.52	258.54	0.02	7.90	10.04	4.06	0.14
EAS-DS	2026-08-29 08:15:00	13.50	256.43	0.18	7.92	9.80	0.00	0.14
EAS-DS	2026-08-29 08:30:00	13.48	249.69	0.19	7.88	9.57	0.00	0.13
EAS-DS	2026-08-29 08:45:00	13.50	254.48	0.19	7.85	9.41	0.16	0.14
EAS-DS	2026-08-29 09:00:00	13.61	271.33	0.01	7.86	9.97	1.71	0.15
EAS-DS	2026-08-29 09:15:00	13.69	267.76	0.18	7.90	9.96	2.03	0.14
EAS-DS	2026-08-29 09:30:00	13.69	257.59	0.19	7.84	9.78	2.48	0.14
EAS-DS	2026-08-29 09:45:00	13.81	253.53	0.19	7.93	9.94	0.64	0.14
EAS-DS	2026-08-29 10:00:00	13.88	263.01	0.03	7.91	9.94	2.50	0.14
EAS-DS	2026-08-29 10:15:00	13.97	265.97	0.18	7.92	9.91	2.57	0.14
EAS-DS	2026-08-29 10:30:00	13.88	252.81	0.18	7.90	9.57	0.00	0.14
EAS-DS	2026-08-29 10:45:00	14.15	267.02	0.18	7.93	9.87	0.38	0.14
EAS-DS	2026-08-29 11:00:00	14.11	241.11	0.02	7.85	9.51	0.34	0.13
EAS-DS	2026-08-29 11:15:00	14.31	252.05	0.17	7.91	9.83	4.85	0.14
EAS-DS	2026-08-29 11:30:00	14.29	245.78	0.19	7.91	9.83	1.21	0.13
EAS-DS	2026-08-29 11:45:00	14.37	246.77	0.18	7.97	9.81	0.29	0.13
EAS-DS	2026-08-29 12:00:00	14.35	251.29	0.02	7.79	9.26	1.09	0.13
EAS-DS	2026-08-29 12:15:00	14.64	276.18	0.20	7.90	9.71	0.29	0.15
EAS-DS	2026-08-29 12:30:00	14.70	277.83	0.21	7.89	9.74	0.29	0.15
EAS-DS	2026-08-29 12:45:00	14.74	275.38	0.20	7.88	9.67	1.83	0.15
EAS-DS	2026-08-29 13:00:00	14.83	271.86	0.10	7.87	9.67	0.21	0.15
EAS-DS	2026-08-29 13:15:00	14.76	260.24	0.20	7.88	9.47	0.00	0.14
EAS-DS	2026-08-29 13:30:00	14.71	267.53	0.21	7.83	9.16	0.00	0.14
EAS-DS	2026-08-29 13:45:00	15.15	252.25	0.22	7.97	9.67	0.00	0.13
EAS-DS	2026-08-29 14:00:00	14.96	252.69	0.22	7.97	9.66	0.00	0.14
EAS-DS	2026-08-29 14:15:00	14.97	244.24	0.15	7.93	9.72	0.00	0.13
EAS-DS	2026-08-29 14:30:00	15.01	245.45	0.24	7.95	9.64	0.00	0.13
EAS-DS	2026-08-29 14:45:00	15.01	252.41	0.25	7.94	9.63	0.00	0.14
EAS-DS	2026-08-29 15:00:00	15.07	260.30	0.25	7.93	9.52	0.00	0.14
EAS-DS	2026-08-29 15:15:00	15.02	268.87	0.21	7.88	9.25	0.00	0.14
EAS-DS	2026-08-29 15:30:00	15.14	267.49	0.22	7.98	9.64	0.00	0.14
EAS-DS	2026-08-29 15:45:00	15.04	267.99	0.23	7.96	9.65	0.00	0.14
EAS-DS	2026-08-29 16:00:00	15.03	272.67	0.22	7.97	9.65	0.00	0.15
EAS-DS	2026-08-29 16:15:00	15.03	268.07	0.22	7.86	9.34	0.00	0.14
EAS-DS	2026-08-29 16:30:00	15.02	267.99	0.20	7.92	9.52	0.00	0.14
EAS-DS	2026-08-29 16:45:00	15.01	267.51	0.24	7.90	9.35	0.00	0.14
EAS-DS	2026-08-29 17:00:00	14.97	244.99	0.23	7.96	9.58	0.00	0.13
EAS-DS	2026-08-29 17:15:00	14.92	264.31	0.21	7.98	9.72	0.00	0.14
EAS-DS	2026-08-29 17:30:00	14.99	270.84	0.23	7.94	9.56	0.00	0.15
EAS-DS	2026-08-29 17:45:00	15.03	264.05	0.23	7.98	9.63	0.00	0.14
EAS-DS	2026-08-29 18:00:00	14.92	266.55	0.23	7.99	9.70	0.00	0.14
EAS-DS	2026-08-29 18:15:00	14.99	273.21	0.15	7.93	9.63	0.00	0.15
EAS-DS	2026-08-29 18:30:00	14.88	263.27	0.25	7.91	9.73	6.49	0.14
EAS-DS	2026-08-29 18:45:00	14.73	249.40	0.26	7.93	9.74	0.33	0.13
EAS-DS	2026-08-29 19:00:00	14.70	247.97	0.26	7.93	9.77	0.05	0.13
EAS-DS	2026-08-29 19:15:00	14.74	264.18	0.22	7.91	9.50	0.00	0.14
EAS-DS	2026-08-29 19:30:00	14.73	254.88	0.24	7.88	9.27	0.00	0.14
EAS-DS	2026-08-29 19:45:00	14.73	252.58	0.24	7.84	9.07	0.00	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-29 20:00:00	14.55	266.31	0.24	7.91	9.76	0.00	0.14
EAS-DS	2026-08-29 20:15:00	14.38	246.83	0.23	7.92	9.84	1.13	0.13
EAS-DS	2026-08-29 20:30:00	14.35	249.23	0.25	7.96	9.81	0.00	0.13
EAS-DS	2026-08-29 20:45:00	14.29	248.00	0.25	7.92	9.84	1.35	0.13
EAS-DS	2026-08-29 21:00:00	14.15	242.44	0.25	7.95	9.89	0.00	0.13
EAS-DS	2026-08-29 21:15:00	14.08	242.76	0.21	7.94	9.81	0.00	0.13
EAS-DS	2026-08-29 21:30:00	14.22	255.27	0.23	7.93	9.76	0.00	0.14
EAS-DS	2026-08-29 21:45:00	14.34	260.75	0.23	7.88	9.36	0.00	0.14
EAS-DS	2026-08-29 22:00:00	14.37	261.84	0.23	7.85	9.22	0.00	0.14
EAS-DS	2026-08-29 22:15:00	14.43	252.41	0.23	7.86	9.66	0.14	0.14
EAS-DS	2026-08-29 22:30:00	14.08	237.70	0.24	7.93	9.91	0.00	0.13
EAS-DS	2026-08-29 22:45:00	14.01	235.74	0.25	7.95	9.90	0.00	0.13
EAS-DS	2026-08-29 23:00:00	14.13	242.29	0.25	7.92	9.86	0.00	0.13
EAS-DS	2026-08-29 23:15:00	14.22	255.62	0.20	7.90	9.85	0.00	0.14
EAS-DS	2026-08-29 23:30:00	14.23	257.12	0.22	7.92	9.86	1.25	0.14
EAS-DS	2026-08-29 23:45:00	14.06	246.79	0.22	7.91	9.54	0.00	0.13
EAS-DS	2026-08-30 00:00:00	14.23	259.55	0.22	7.93	9.83	0.00	0.14
EAS-DS	2026-08-30 00:15:00	13.90	232.68	0.22	7.95	9.90	0.00	0.12
EAS-DS	2026-08-30 00:30:00	14.11	248.43	0.24	7.87	9.73	0.00	0.13
EAS-DS	2026-08-30 00:45:00	14.12	249.12	0.24	7.88	9.66	0.00	0.13
EAS-DS	2026-08-30 01:00:00	14.06	248.26	0.25	7.86	9.62	0.00	0.13
EAS-DS	2026-08-30 01:15:00	13.73	238.87	0.20	7.94	9.99	0.00	0.13
EAS-DS	2026-08-30 01:30:00	13.75	242.20	0.22	7.96	9.98	0.00	0.13
EAS-DS	2026-08-30 01:45:00	13.75	249.05	0.22	7.95	9.99	0.43	0.13
EAS-DS	2026-08-30 02:00:00	13.88	256.37	0.22	7.95	9.95	0.00	0.14
EAS-DS	2026-08-30 02:15:00	13.92	257.09	0.15	7.80	9.50	0.00	0.14
EAS-DS	2026-08-30 02:30:00	13.92	257.95	0.19	7.82	9.55	0.00	0.14
EAS-DS	2026-08-30 02:45:00	13.99	264.51	0.20	7.91	9.83	0.00	0.14
EAS-DS	2026-08-30 03:00:00	13.98	263.87	0.25	7.91	9.82	0.00	0.14
EAS-DS	2026-08-30 03:15:00	13.70	245.00	0.20	7.94	9.99	0.00	0.13
EAS-DS	2026-08-30 03:30:00	13.89	251.86	0.20	7.92	9.93	0.00	0.14
EAS-DS	2026-08-30 03:45:00	13.91	259.74	0.22	7.95	9.92	0.00	0.14
EAS-DS	2026-08-30 04:00:00	13.78	252.89	0.22	7.94	9.96	0.00	0.14
EAS-DS	2026-08-30 04:15:00	13.79	250.80	0.21	7.94	9.89	0.00	0.13
EAS-DS	2026-08-30 04:30:00	13.88	256.45	0.24	7.94	9.87	0.00	0.14
EAS-DS	2026-08-30 04:45:00	13.97	261.50	0.25	7.90	9.53	0.00	0.14
EAS-DS	2026-08-30 05:00:00	13.75	250.65	0.25	7.95	9.94	0.00	0.13
EAS-DS	2026-08-30 05:15:00	14.00	267.66	0.17	7.96	9.87	0.00	0.14
EAS-DS	2026-08-30 05:30:00	14.10	278.81	0.20	7.96	9.87	0.00	0.15
EAS-DS	2026-08-30 05:45:00	14.09	277.18	0.22	7.93	9.56	0.00	0.15
EAS-DS	2026-08-30 06:00:00	14.04	273.23	0.22	7.88	9.14	0.00	0.15
EAS-DS	2026-08-30 06:15:00	13.88	248.13	0.22	7.92	9.89	0.70	0.13
EAS-DS	2026-08-30 06:30:00	13.83	245.82	0.24	7.93	9.85	0.00	0.13
EAS-DS	2026-08-30 06:45:00	13.70	237.00	0.24	7.96	9.97	0.00	0.13
EAS-DS	2026-08-30 07:00:00	13.80	244.49	0.24	7.93	9.93	0.25	0.13
EAS-DS	2026-08-30 07:15:00	13.86	261.21	0.20	7.98	9.94	0.55	0.14
EAS-DS	2026-08-30 07:30:00	13.73	249.56	0.22	7.99	10.03	0.00	0.13
EAS-DS	2026-08-30 07:45:00	13.81	256.85	0.22	7.99	9.96	0.00	0.14
EAS-DS	2026-08-30 08:00:00	13.85	256.51	0.22	7.93	9.79	0.00	0.14
EAS-DS	2026-08-30 08:15:00	13.86	249.58	0.22	7.92	9.78	0.00	0.13
EAS-DS	2026-08-30 08:30:00	13.81	245.17	0.24	7.94	9.92	0.00	0.13
EAS-DS	2026-08-30 08:45:00	13.86	247.57	0.24	7.93	9.92	0.00	0.13
EAS-DS	2026-08-30 09:00:00	13.89	246.47	0.24	7.91	9.95	0.00	0.13
EAS-DS	2026-08-30 09:15:00	13.92	257.13	0.17	7.89	9.93	4.87	0.14
EAS-DS	2026-08-30 09:30:00	13.93	253.11	0.21	7.89	9.81	0.00	0.14
EAS-DS	2026-08-30 09:45:00	14.05	253.46	0.21	7.92	9.91	0.92	0.14

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-DS	2026-08-30 10:00:00	14.02	247.05	0.21	7.98	9.92	0.00	0.13
EAS-DS	2026-08-30 10:15:00	14.04	248.44	0.21	7.91	9.96	0.00	0.13
EAS-DS	2026-08-30 10:30:00	14.09	248.51	0.24	7.92	9.76	0.00	0.13
EAS-DS	2026-08-30 10:45:00	14.10	245.23	0.24	7.94	9.85	0.00	0.13
EAS-DS	2026-08-30 11:00:00	14.00	240.12	0.24	7.92	9.89	0.47	0.13
EAS-DS	2026-08-30 11:15:00	13.88	229.65	0.19	7.94	9.98	0.68	0.12
EAS-DS	2026-08-30 11:30:00	14.00	246.33	0.21	7.96	9.96	0.09	0.13
EAS-DS	2026-08-30 11:45:00	14.15	253.28	0.21	7.95	9.91	0.00	0.14
EAS-DS	2026-08-30 12:00:00	14.16	252.42	0.21	7.95	9.70	0.00	0.14
EAS-DS	2026-08-30 12:15:00	14.21	253.97	0.21	7.90	9.76	0.00	0.14
EAS-DS	2026-08-30 12:30:00	14.14	240.10	0.24	7.90	9.54	0.00	0.13
EAS-DS	2026-08-30 12:45:00	14.20	250.38	0.24	7.90	9.60	0.00	0.13
EAS-DS	2026-08-30 13:00:00	14.09	237.93	0.24	7.91	9.91	0.00	0.13
EAS-DS	2026-08-30 13:15:00	14.09	244.90	0.20	7.95	9.91	0.00	0.13
EAS-DS	2026-08-30 13:30:00	14.06	242.81	0.21	7.95	9.90	0.00	0.13
EAS-DS	2026-08-30 13:45:00	14.07	241.40	0.22	7.91	9.60	0.00	0.13
EAS-DS	2026-08-30 14:00:00	14.16	249.58	0.22	7.89	9.58	0.00	0.13
EAS-DS	2026-08-30 14:15:00	14.27	251.35	0.22	7.93	9.79	0.84	0.13
EAS-DS	2026-08-30 14:30:00	14.27	249.65	0.24	7.90	9.66	1.56	0.13
EAS-DS	2026-08-30 14:45:00	14.30	254.92	0.23	7.93	9.81	1.26	0.14
EAS-DS	2026-08-30 15:00:00	14.29	255.09	0.23	7.93	9.71	2.43	0.14
EAS-DS	2026-08-30 15:15:00	14.24	257.37	0.19	7.87	9.45	0.00	0.14
EAS-DS	2026-08-30 15:30:00	14.24	259.11	0.21	7.85	9.20	0.00	0.14
EAS-DS	2026-08-30 15:45:00	14.33	270.46	0.21	7.94	9.59	0.00	0.15
EAS-DS	2026-08-30 16:00:00	14.19	252.29	0.21	7.93	9.92	5.19	0.14
EAS-DS	2026-08-30 16:15:00	14.16	247.54	0.21	7.91	9.86	0.99	0.13
EAS-DS	2026-08-30 16:30:00	14.16	245.37	0.23	7.94	9.85	1.15	0.13
EAS-DS	2026-08-30 16:45:00	14.23	249.67	0.23	7.94	9.84	0.80	0.13
EAS-DS	2026-08-30 17:00:00	14.33	259.30	0.23	7.93	9.72	0.92	0.14
EAS-DS	2026-08-30 17:15:00	14.27	248.22	0.19	7.92	9.87	4.64	0.13
EAS-DS	2026-08-30 17:30:00	14.28	256.08	0.21	7.88	9.24	0.00	0.14
EAS-DS	2026-08-30 17:45:00	14.29	248.99	0.22	7.91	9.81	0.83	0.13
EAS-DS	2026-08-30 18:00:00	14.25	249.31	0.22	7.91	9.87	4.44	0.13
EAS-DS	2026-08-30 18:15:00	14.27	248.49	0.19	7.91	9.84	0.48	0.13
EAS-DS	2026-08-30 18:30:00	14.35	252.85	0.21	7.91	9.73	1.97	0.14
EAS-DS	2026-08-30 18:45:00	14.24	238.37	0.22	7.91	9.70	1.84	0.13
EAS-DS	2026-08-30 19:00:00	14.16	226.65	0.21	7.96	9.89	0.36	0.12
EAS-DS	2026-08-30 19:15:00	14.20	238.16	0.19	7.90	9.76	5.44	0.13
EAS-DS	2026-08-30 19:30:00	14.25	253.28	0.21	7.93	9.86	1.17	0.14
EAS-DS	2026-08-30 19:45:00	14.18	239.33	0.22	7.93	9.89	0.60	0.13
EAS-DS	2026-08-30 20:00:00	14.12	236.53	0.22	7.93	9.82	0.92	0.13
EAS-DS	2026-08-30 20:15:00	14.20	248.20	0.19	7.90	9.77	1.28	0.13
EAS-DS	2026-08-30 20:30:00	14.18	238.57	0.22	7.88	9.75	0.00	0.13
EAS-DS	2026-08-30 20:45:00	14.21	242.43	0.22	7.88	9.21	0.00	0.13
EAS-DS	2026-08-30 21:00:00	14.14	239.71	0.22	7.90	9.11	1.98	0.13
EAS-DS	2026-08-30 21:15:00	14.11	241.56	0.19	7.86	9.75	0.40	0.13
EAS-DS	2026-08-30 21:30:00	14.08	246.55	0.22	7.94	9.89	0.00	0.13
EAS-DS	2026-08-30 21:45:00	14.03	244.51	0.22	7.89	9.92	2.65	0.13
EAS-DS	2026-08-30 22:00:00	13.95	242.05	0.22	7.91	9.95	0.00	0.13
EAS-DS	2026-08-30 22:15:00	13.94	236.50	0.20	7.86	9.87	0.37	0.13
EAS-DS	2026-08-30 22:30:00	13.92	229.97	0.22	7.90	9.84	0.00	0.12
EAS-DS	2026-08-30 22:45:00	13.98	235.70	0.21	7.94	9.88	0.00	0.13
EAS-DS	2026-08-30 23:00:00	14.01	235.09	0.22	7.85	9.42	0.00	0.13
EAS-DS	2026-08-30 23:15:00	13.96	238.57	0.20	7.90	9.82	0.57	0.13
EAS-DS	2026-08-30 23:30:00	13.84	238.25	0.21	7.92	9.98	1.19	0.13
EAS-DS	2026-08-30 23:45:00	13.68	226.36	0.22	7.94	9.96	0.00	0.12

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-24 00:00:00	16.56	30.55	0.49	7.21	8.94	8.57	0.01
EAS-US	2026-08-24 00:15:00							
EAS-US	2026-08-24 00:30:00							
EAS-US	2026-08-24 00:45:00							
EAS-US	2026-08-24 01:00:00	16.50	30.95	0.49	7.20	8.93	8.48	0.01
EAS-US	2026-08-24 01:15:00							
EAS-US	2026-08-24 01:30:00							
EAS-US	2026-08-24 01:45:00							
EAS-US	2026-08-24 02:00:00	16.44	30.67	0.49	7.21	8.94	8.63	0.01
EAS-US	2026-08-24 02:15:00							
EAS-US	2026-08-24 02:30:00							
EAS-US	2026-08-24 02:45:00							
EAS-US	2026-08-24 03:00:00	16.39	30.58	0.49	7.20	8.96	8.56	0.01
EAS-US	2026-08-24 03:15:00							
EAS-US	2026-08-24 03:30:00							
EAS-US	2026-08-24 03:45:00							
EAS-US	2026-08-24 04:00:00	16.33	30.30	0.49	7.21	8.98	8.48	0.01
EAS-US	2026-08-24 04:15:00							
EAS-US	2026-08-24 04:30:00							
EAS-US	2026-08-24 04:45:00							
EAS-US	2026-08-24 05:00:00	16.28	30.15	0.49	7.20	8.99	8.57	0.01
EAS-US	2026-08-24 05:15:00							
EAS-US	2026-08-24 05:30:00							
EAS-US	2026-08-24 05:45:00							
EAS-US	2026-08-24 06:00:00	16.23	29.96	0.49	7.20	9.02	8.52	0.01
EAS-US	2026-08-24 06:15:00							
EAS-US	2026-08-24 06:30:00							
EAS-US	2026-08-24 06:45:00							
EAS-US	2026-08-24 07:00:00	16.19	29.74	0.49	7.21	9.09	8.62	0.01
EAS-US	2026-08-24 07:15:00							
EAS-US	2026-08-24 07:30:00							
EAS-US	2026-08-24 07:45:00							
EAS-US	2026-08-24 08:00:00	16.24	29.43	0.48	7.25	9.28	8.61	0.01
EAS-US	2026-08-24 08:15:00							
EAS-US	2026-08-24 08:30:00							
EAS-US	2026-08-24 08:45:00							
EAS-US	2026-08-24 09:00:00	16.30	29.22	0.47	7.28	9.36	8.62	0.01
EAS-US	2026-08-24 09:15:00							
EAS-US	2026-08-24 09:30:00							
EAS-US	2026-08-24 09:45:00							
EAS-US	2026-08-24 10:00:00	16.43	29.03	0.47	7.30	9.41	8.78	0.01
EAS-US	2026-08-24 10:15:00							
EAS-US	2026-08-24 10:30:00							
EAS-US	2026-08-24 10:45:00							
EAS-US	2026-08-24 11:00:00	17.38	28.41	0.42	7.41	9.92	8.86	0.01
EAS-US	2026-08-24 11:15:00							
EAS-US	2026-08-24 11:30:00							
EAS-US	2026-08-24 11:45:00							
EAS-US	2026-08-24 12:00:00	18.43	28.37	0.41	7.46	9.75	8.98	0.01
EAS-US	2026-08-24 12:15:00							
EAS-US	2026-08-24 12:30:00							
EAS-US	2026-08-24 12:45:00							
EAS-US	2026-08-24 13:00:00	18.76	28.42	0.41	7.44	9.56	8.88	0.01
EAS-US	2026-08-24 13:15:00							
EAS-US	2026-08-24 13:30:00							
EAS-US	2026-08-24 13:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-24 14:00:00	19.02	28.46	0.42	7.43	9.39	8.84	0.01
EAS-US	2026-08-24 14:15:00							
EAS-US	2026-08-24 14:30:00							
EAS-US	2026-08-24 14:45:00							
EAS-US	2026-08-24 15:00:00	19.39	28.46	0.43	7.41	9.21	9.03	0.01
EAS-US	2026-08-24 15:15:00							
EAS-US	2026-08-24 15:30:00							
EAS-US	2026-08-24 15:45:00							
EAS-US	2026-08-24 16:00:00	19.68	28.56	0.43	7.41	9.12	8.94	0.01
EAS-US	2026-08-24 16:15:00							
EAS-US	2026-08-24 16:30:00							
EAS-US	2026-08-24 16:45:00							
EAS-US	2026-08-24 17:00:00	19.22	29.03	0.45	7.33	8.80	8.87	0.01
EAS-US	2026-08-24 17:15:00							
EAS-US	2026-08-24 17:30:00							
EAS-US	2026-08-24 17:45:00							
EAS-US	2026-08-24 18:00:00	18.92	29.50	0.46	7.27	8.62	8.80	0.01
EAS-US	2026-08-24 18:15:00							
EAS-US	2026-08-24 18:30:00							
EAS-US	2026-08-24 18:45:00							
EAS-US	2026-08-24 19:00:00	18.57	29.89	0.47	7.23	8.54	8.65	0.01
EAS-US	2026-08-24 19:15:00							
EAS-US	2026-08-24 19:30:00							
EAS-US	2026-08-24 19:45:00							
EAS-US	2026-08-24 20:00:00	18.23	30.09	0.47	7.21	8.50	8.49	0.01
EAS-US	2026-08-24 20:15:00							
EAS-US	2026-08-24 20:30:00							
EAS-US	2026-08-24 20:45:00							
EAS-US	2026-08-24 21:00:00	17.96	30.20	0.48	7.19	8.49	8.40	0.01
EAS-US	2026-08-24 21:15:00							
EAS-US	2026-08-24 21:30:00							
EAS-US	2026-08-24 21:45:00							
EAS-US	2026-08-24 22:00:00	17.72	30.19	0.48	7.18	8.54	8.39	0.01
EAS-US	2026-08-24 22:15:00							
EAS-US	2026-08-24 22:30:00							
EAS-US	2026-08-24 22:45:00							
EAS-US	2026-08-24 23:00:00	17.51	30.06	0.49	7.18	8.59	8.40	0.01
EAS-US	2026-08-24 23:15:00							
EAS-US	2026-08-24 23:30:00							
EAS-US	2026-08-24 23:45:00							
EAS-US	2026-08-25 00:00:00	17.30	29.87	0.49	7.18	8.64	9.73	0.01
EAS-US	2026-08-25 00:15:00							
EAS-US	2026-08-25 00:30:00							
EAS-US	2026-08-25 00:45:00							
EAS-US	2026-08-25 01:00:00	17.12	29.68	0.49	7.18	8.70	8.49	0.01
EAS-US	2026-08-25 01:15:00							
EAS-US	2026-08-25 01:30:00							
EAS-US	2026-08-25 01:45:00							
EAS-US	2026-08-25 02:00:00	16.97	29.53	0.49	7.18	8.74	8.41	0.01
EAS-US	2026-08-25 02:15:00							
EAS-US	2026-08-25 02:30:00							
EAS-US	2026-08-25 02:45:00							
EAS-US	2026-08-25 03:00:00	16.81	29.39	0.49	7.18	8.78	8.49	0.01
EAS-US	2026-08-25 03:15:00							
EAS-US	2026-08-25 03:30:00							
EAS-US	2026-08-25 03:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-25 04:00:00	16.67	29.24	0.50	7.19	8.83	8.37	0.01
EAS-US	2026-08-25 04:15:00							
EAS-US	2026-08-25 04:30:00							
EAS-US	2026-08-25 04:45:00							
EAS-US	2026-08-25 05:00:00	16.52	29.09	0.50	7.19	8.89	8.41	0.01
EAS-US	2026-08-25 05:15:00							
EAS-US	2026-08-25 05:30:00							
EAS-US	2026-08-25 05:45:00							
EAS-US	2026-08-25 06:00:00	16.39	28.97	0.50	7.19	8.92	8.44	0.01
EAS-US	2026-08-25 06:15:00							
EAS-US	2026-08-25 06:30:00							
EAS-US	2026-08-25 06:45:00							
EAS-US	2026-08-25 07:00:00	16.28	28.85	0.49	7.20	8.99	8.46	0.01
EAS-US	2026-08-25 07:15:00							
EAS-US	2026-08-25 07:30:00							
EAS-US	2026-08-25 07:45:00							
EAS-US	2026-08-25 08:00:00	16.26	28.57	0.49	7.23	9.17	8.51	0.01
EAS-US	2026-08-25 08:15:00							
EAS-US	2026-08-25 08:30:00							
EAS-US	2026-08-25 08:45:00							
EAS-US	2026-08-25 09:00:00	16.35	28.25	0.48	7.27	9.37	8.58	0.01
EAS-US	2026-08-25 09:15:00							
EAS-US	2026-08-25 09:30:00							
EAS-US	2026-08-25 09:45:00							
EAS-US	2026-08-25 10:00:00	16.53	27.99	0.47	7.31	9.55	8.60	0.01
EAS-US	2026-08-25 10:15:00							
EAS-US	2026-08-25 10:30:00							
EAS-US	2026-08-25 10:45:00							
EAS-US	2026-08-25 11:00:00	17.25	27.46	0.44	7.41	9.95	8.68	0.01
EAS-US	2026-08-25 11:15:00							
EAS-US	2026-08-25 11:30:00							
EAS-US	2026-08-25 11:45:00							
EAS-US	2026-08-25 12:00:00	18.28	27.56	0.43	7.47	9.83	8.87	0.01
EAS-US	2026-08-25 12:15:00							
EAS-US	2026-08-25 12:30:00							
EAS-US	2026-08-25 12:45:00							
EAS-US	2026-08-25 13:00:00	18.79	27.63	0.43	7.47	9.70	8.88	0.01
EAS-US	2026-08-25 13:15:00							
EAS-US	2026-08-25 13:30:00							
EAS-US	2026-08-25 13:45:00							
EAS-US	2026-08-25 14:00:00	19.09	27.67	0.43	7.48	9.54	8.93	0.01
EAS-US	2026-08-25 14:15:00							
EAS-US	2026-08-25 14:30:00							
EAS-US	2026-08-25 14:45:00							
EAS-US	2026-08-25 15:00:00	19.39	27.68	0.43	7.46	9.39	8.91	0.01
EAS-US	2026-08-25 15:15:00							
EAS-US	2026-08-25 15:30:00							
EAS-US	2026-08-25 15:45:00							
EAS-US	2026-08-25 16:00:00	19.66	27.90	0.44	7.44	9.27	8.83	0.01
EAS-US	2026-08-25 16:15:00							
EAS-US	2026-08-25 16:30:00							
EAS-US	2026-08-25 16:45:00							
EAS-US	2026-08-25 17:00:00	19.45	28.36	0.45	7.37	8.99	8.84	0.01
EAS-US	2026-08-25 17:15:00							
EAS-US	2026-08-25 17:30:00							
EAS-US	2026-08-25 17:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-25 18:00:00	19.18	28.84	0.46	7.30	8.76	8.62	0.01
EAS-US	2026-08-25 18:15:00							
EAS-US	2026-08-25 18:30:00							
EAS-US	2026-08-25 18:45:00							
EAS-US	2026-08-25 19:00:00	18.88	29.32	0.47	7.25	8.60	8.61	0.01
EAS-US	2026-08-25 19:15:00							
EAS-US	2026-08-25 19:30:00							
EAS-US	2026-08-25 19:45:00							
EAS-US	2026-08-25 20:00:00	18.60	29.73	0.48	7.20	8.47	8.50	0.01
EAS-US	2026-08-25 20:15:00							
EAS-US	2026-08-25 20:30:00							
EAS-US	2026-08-25 20:45:00							
EAS-US	2026-08-25 21:00:00	18.34	30.03	0.48	7.18	8.39	8.50	0.01
EAS-US	2026-08-25 21:15:00							
EAS-US	2026-08-25 21:30:00							
EAS-US	2026-08-25 21:45:00							
EAS-US	2026-08-25 22:00:00	18.15	30.08	0.49	7.18	8.39	8.41	0.01
EAS-US	2026-08-25 22:15:00							
EAS-US	2026-08-25 22:30:00							
EAS-US	2026-08-25 22:45:00							
EAS-US	2026-08-25 23:00:00	17.99	30.03	0.49	7.17	8.43	8.34	0.01
EAS-US	2026-08-25 23:15:00							
EAS-US	2026-08-25 23:30:00							
EAS-US	2026-08-25 23:45:00							
EAS-US	2026-08-26 00:00:00	17.82	29.85	0.49	7.17	8.49	8.46	0.01
EAS-US	2026-08-26 00:15:00							
EAS-US	2026-08-26 00:30:00							
EAS-US	2026-08-26 00:45:00							
EAS-US	2026-08-26 01:00:00	17.65	29.62	0.49	7.17	8.56	8.49	0.01
EAS-US	2026-08-26 01:15:00							
EAS-US	2026-08-26 01:30:00							
EAS-US	2026-08-26 01:45:00							
EAS-US	2026-08-26 02:00:00	17.49	29.42	0.49	7.17	8.62	8.53	0.01
EAS-US	2026-08-26 02:15:00							
EAS-US	2026-08-26 02:30:00							
EAS-US	2026-08-26 02:45:00							
EAS-US	2026-08-26 03:00:00	17.33	29.26	0.49	7.17	8.66	8.47	0.01
EAS-US	2026-08-26 03:15:00							
EAS-US	2026-08-26 03:30:00							
EAS-US	2026-08-26 03:45:00							
EAS-US	2026-08-26 04:00:00	17.17	29.09	0.49	7.17	8.69	8.45	0.01
EAS-US	2026-08-26 04:15:00							
EAS-US	2026-08-26 04:30:00							
EAS-US	2026-08-26 04:45:00							
EAS-US	2026-08-26 05:00:00	17.02	28.95	0.49	7.17	8.73	8.41	0.01
EAS-US	2026-08-26 05:15:00							
EAS-US	2026-08-26 05:30:00							
EAS-US	2026-08-26 05:45:00							
EAS-US	2026-08-26 06:00:00	16.88	28.82	0.50	7.18	8.78	8.45	0.01
EAS-US	2026-08-26 06:15:00							
EAS-US	2026-08-26 06:30:00							
EAS-US	2026-08-26 06:45:00							
EAS-US	2026-08-26 07:00:00	16.76	28.68	0.49	7.18	8.86	8.70	0.01
EAS-US	2026-08-26 07:15:00							
EAS-US	2026-08-26 07:30:00							
EAS-US	2026-08-26 07:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-26 08:00:00	16.69	28.57	0.49	7.20	8.98	8.53	0.01
EAS-US	2026-08-26 08:15:00							
EAS-US	2026-08-26 08:30:00							
EAS-US	2026-08-26 08:45:00							
EAS-US	2026-08-26 09:00:00	16.71	28.31	0.48	7.23	9.10	8.46	0.01
EAS-US	2026-08-26 09:15:00							
EAS-US	2026-08-26 09:30:00							
EAS-US	2026-08-26 09:45:00							
EAS-US	2026-08-26 10:00:00	16.85	27.86	0.47	7.30	9.36	8.50	0.01
EAS-US	2026-08-26 10:15:00							
EAS-US	2026-08-26 10:30:00							
EAS-US	2026-08-26 10:45:00							
EAS-US	2026-08-26 11:00:00	17.50	27.07	0.44	7.43	9.88	8.69	0.01
EAS-US	2026-08-26 11:15:00							
EAS-US	2026-08-26 11:30:00							
EAS-US	2026-08-26 11:45:00							
EAS-US	2026-08-26 12:00:00	18.73	26.99	0.42	7.50	9.83	8.70	0.01
EAS-US	2026-08-26 12:15:00							
EAS-US	2026-08-26 12:30:00							
EAS-US	2026-08-26 12:45:00							
EAS-US	2026-08-26 13:00:00	19.08	27.19	0.42	7.48	9.68	8.78	0.01
EAS-US	2026-08-26 13:15:00							
EAS-US	2026-08-26 13:30:00							
EAS-US	2026-08-26 13:45:00							
EAS-US	2026-08-26 14:00:00	19.35	27.37	0.43	7.47	9.44	8.80	0.01
EAS-US	2026-08-26 14:15:00							
EAS-US	2026-08-26 14:30:00							
EAS-US	2026-08-26 14:45:00							
EAS-US	2026-08-26 15:00:00	19.72	27.47	0.43	7.45	9.27	8.79	0.01
EAS-US	2026-08-26 15:15:00							
EAS-US	2026-08-26 15:30:00							
EAS-US	2026-08-26 15:45:00							
EAS-US	2026-08-26 16:00:00	19.93	27.83	0.44	7.42	9.20	8.65	0.01
EAS-US	2026-08-26 16:15:00							
EAS-US	2026-08-26 16:30:00							
EAS-US	2026-08-26 16:45:00							
EAS-US	2026-08-26 17:00:00	19.49	27.99	0.45	7.35	8.81	8.63	0.01
EAS-US	2026-08-26 17:15:00							
EAS-US	2026-08-26 17:30:00							
EAS-US	2026-08-26 17:45:00							
EAS-US	2026-08-26 18:00:00	19.13	28.33	0.47	7.29	8.63	8.47	0.01
EAS-US	2026-08-26 18:15:00							
EAS-US	2026-08-26 18:30:00							
EAS-US	2026-08-26 18:45:00							
EAS-US	2026-08-26 19:00:00	18.78	28.63	0.48	7.25	8.53	8.37	0.01
EAS-US	2026-08-26 19:15:00							
EAS-US	2026-08-26 19:30:00							
EAS-US	2026-08-26 19:45:00							
EAS-US	2026-08-26 20:00:00	18.42	28.92	0.48	7.22	8.47	8.35	0.01
EAS-US	2026-08-26 20:15:00							
EAS-US	2026-08-26 20:30:00							
EAS-US	2026-08-26 20:45:00							
EAS-US	2026-08-26 21:00:00	18.10	29.15	0.49	7.18	8.40	8.29	0.01
EAS-US	2026-08-26 21:15:00							
EAS-US	2026-08-26 21:30:00							
EAS-US	2026-08-26 21:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-26 22:00:00	17.82	29.24	0.49	7.18	8.42	8.15	0.01
EAS-US	2026-08-26 22:15:00							
EAS-US	2026-08-26 22:30:00							
EAS-US	2026-08-26 22:45:00							
EAS-US	2026-08-26 23:00:00	17.57	29.23	0.50	7.17	8.46	8.24	0.01
EAS-US	2026-08-26 23:15:00							
EAS-US	2026-08-26 23:30:00							
EAS-US	2026-08-26 23:45:00							
EAS-US	2026-08-27 00:00:00	17.31	29.05	0.50	7.18	8.56	8.26	0.01
EAS-US	2026-08-27 00:15:00							
EAS-US	2026-08-27 00:30:00							
EAS-US	2026-08-27 00:45:00							
EAS-US	2026-08-27 01:00:00	17.11	28.87	0.50	7.18	8.64	8.28	0.01
EAS-US	2026-08-27 01:15:00							
EAS-US	2026-08-27 01:30:00							
EAS-US	2026-08-27 01:45:00							
EAS-US	2026-08-27 02:00:00	16.93	28.75	0.50	7.18	8.70	8.09	0.01
EAS-US	2026-08-27 02:15:00							
EAS-US	2026-08-27 02:30:00							
EAS-US	2026-08-27 02:45:00							
EAS-US	2026-08-27 03:00:00	16.77	28.66	0.50	7.18	8.75	8.21	0.01
EAS-US	2026-08-27 03:15:00							
EAS-US	2026-08-27 03:30:00							
EAS-US	2026-08-27 03:45:00							
EAS-US	2026-08-27 04:00:00	16.66	28.53	0.50	7.18	8.80	8.26	0.01
EAS-US	2026-08-27 04:15:00							
EAS-US	2026-08-27 04:30:00							
EAS-US	2026-08-27 04:45:00							
EAS-US	2026-08-27 05:00:00	16.54	28.42	0.50	7.18	8.84	8.18	0.01
EAS-US	2026-08-27 05:15:00							
EAS-US	2026-08-27 05:30:00							
EAS-US	2026-08-27 05:45:00							
EAS-US	2026-08-27 06:00:00	16.44	28.29	0.50	7.18	8.88	8.22	0.01
EAS-US	2026-08-27 06:15:00							
EAS-US	2026-08-27 06:30:00							
EAS-US	2026-08-27 06:45:00							
EAS-US	2026-08-27 07:00:00	16.35	28.24	0.50	7.19	8.94	8.23	0.01
EAS-US	2026-08-27 07:15:00							
EAS-US	2026-08-27 07:30:00							
EAS-US	2026-08-27 07:45:00							
EAS-US	2026-08-27 08:00:00	16.30	28.06	0.50	7.21	9.04	8.28	0.01
EAS-US	2026-08-27 08:15:00							
EAS-US	2026-08-27 08:30:00							
EAS-US	2026-08-27 08:45:00							
EAS-US	2026-08-27 09:00:00	16.29	27.89	0.49	7.23	9.17	8.21	0.01
EAS-US	2026-08-27 09:15:00							
EAS-US	2026-08-27 09:30:00							
EAS-US	2026-08-27 09:45:00							
EAS-US	2026-08-27 10:00:00	16.26	27.76	0.44	7.18	9.20	8.07	0.01
EAS-US	2026-08-27 10:15:00							
EAS-US	2026-08-27 10:30:00							
EAS-US	2026-08-27 10:45:00							
EAS-US	2026-08-27 11:00:00	16.32	27.49	0.44	7.23	9.29	8.06	0.01
EAS-US	2026-08-27 11:15:00							
EAS-US	2026-08-27 11:30:00							
EAS-US	2026-08-27 11:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-27 12:00:00	16.36	27.49	0.45	7.22	9.28	8.16	0.01
EAS-US	2026-08-27 12:15:00							
EAS-US	2026-08-27 12:30:00							
EAS-US	2026-08-27 12:45:00							
EAS-US	2026-08-27 13:00:00	16.43	27.86	0.44	7.26	9.37	8.11	0.01
EAS-US	2026-08-27 13:15:00							
EAS-US	2026-08-27 13:30:00							
EAS-US	2026-08-27 13:45:00							
EAS-US	2026-08-27 14:00:00	16.58	27.76	0.44	7.29	9.37	8.12	0.01
EAS-US	2026-08-27 14:15:00							
EAS-US	2026-08-27 14:30:00							
EAS-US	2026-08-27 14:45:00							
EAS-US	2026-08-27 15:00:00	16.65	27.61	0.44	7.28	9.36	8.53	0.01
EAS-US	2026-08-27 15:15:00							
EAS-US	2026-08-27 15:30:00							
EAS-US	2026-08-27 15:45:00							
EAS-US	2026-08-27 16:00:00	16.71	27.45	0.44	7.23	9.31	8.14	0.01
EAS-US	2026-08-27 16:15:00							
EAS-US	2026-08-27 16:30:00							
EAS-US	2026-08-27 16:45:00							
EAS-US	2026-08-27 17:00:00	16.71	27.62	0.44	7.20	9.17	8.26	0.01
EAS-US	2026-08-27 17:15:00							
EAS-US	2026-08-27 17:30:00							
EAS-US	2026-08-27 17:45:00							
EAS-US	2026-08-27 18:00:00	16.65	27.79	0.44	7.23	9.16	8.30	0.01
EAS-US	2026-08-27 18:15:00							
EAS-US	2026-08-27 18:30:00							
EAS-US	2026-08-27 18:45:00							
EAS-US	2026-08-27 19:00:00	16.54	28.09	0.45	7.19	9.07	8.29	0.01
EAS-US	2026-08-27 19:15:00							
EAS-US	2026-08-27 19:30:00							
EAS-US	2026-08-27 19:45:00							
EAS-US	2026-08-27 20:00:00	16.46	28.40	0.44	7.18	9.04	8.53	0.01
EAS-US	2026-08-27 20:15:00							
EAS-US	2026-08-27 20:30:00							
EAS-US	2026-08-27 20:45:00							
EAS-US	2026-08-27 21:00:00	16.36	28.77	0.45	7.17	9.04	8.31	0.01
EAS-US	2026-08-27 21:15:00							
EAS-US	2026-08-27 21:30:00							
EAS-US	2026-08-27 21:45:00							
EAS-US	2026-08-27 22:00:00	16.30	28.91	0.45	7.17	9.07	8.28	0.01
EAS-US	2026-08-27 22:15:00							
EAS-US	2026-08-27 22:30:00							
EAS-US	2026-08-27 22:45:00							
EAS-US	2026-08-27 23:00:00	16.23	28.68	0.45	7.20	9.13	8.37	0.01
EAS-US	2026-08-27 23:15:00							
EAS-US	2026-08-27 23:30:00							
EAS-US	2026-08-27 23:45:00							
EAS-US	2026-08-28 00:00:00	16.16	28.40	0.46	7.18	9.14	8.22	0.01
EAS-US	2026-08-28 00:15:00							
EAS-US	2026-08-28 00:30:00							
EAS-US	2026-08-28 00:45:00							
EAS-US	2026-08-28 01:00:00	16.09	28.19	0.46	7.20	9.15	8.26	0.01
EAS-US	2026-08-28 01:15:00							
EAS-US	2026-08-28 01:30:00							
EAS-US	2026-08-28 01:45:00							


Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-28 02:00:00	16.02	28.11	0.46	7.19	9.16	8.28	0.01
EAS-US	2026-08-28 02:15:00							
EAS-US	2026-08-28 02:30:00							
EAS-US	2026-08-28 02:45:00							
EAS-US	2026-08-28 03:00:00	15.97	27.99	0.46	7.17	9.18	8.31	0.01
EAS-US	2026-08-28 03:15:00							
EAS-US	2026-08-28 03:30:00							
EAS-US	2026-08-28 03:45:00							
EAS-US	2026-08-28 04:00:00	15.91	27.97	0.46	7.18	9.18	8.34	0.01
EAS-US	2026-08-28 04:15:00							
EAS-US	2026-08-28 04:30:00							
EAS-US	2026-08-28 04:45:00							
EAS-US	2026-08-28 05:00:00	15.86	27.90	0.46	7.19	9.19	8.34	0.01
EAS-US	2026-08-28 05:15:00							
EAS-US	2026-08-28 05:30:00							
EAS-US	2026-08-28 05:45:00							
EAS-US	2026-08-28 06:00:00	15.82	27.91	0.46	7.21	9.19	8.27	0.01
EAS-US	2026-08-28 06:15:00							
EAS-US	2026-08-28 06:30:00							
EAS-US	2026-08-28 06:45:00							
EAS-US	2026-08-28 07:00:00	15.79	27.82	0.47	7.18	9.22	8.40	0.01
EAS-US	2026-08-28 07:15:00							
EAS-US	2026-08-28 07:30:00							
EAS-US	2026-08-28 07:45:00							
EAS-US	2026-08-28 08:00:00	15.80	27.72	0.47	7.19	9.30	8.33	0.01
EAS-US	2026-08-28 08:15:00							
EAS-US	2026-08-28 08:30:00							
EAS-US	2026-08-28 08:45:00							
EAS-US	2026-08-28 09:00:00	15.87	27.44	0.47	7.24	9.40	8.37	0.01
EAS-US	2026-08-28 09:15:00							
EAS-US	2026-08-28 09:30:00							
EAS-US	2026-08-28 09:45:00							
EAS-US	2026-08-28 10:00:00	16.04	27.08	0.46	7.31	9.53	8.39	0.01
EAS-US	2026-08-28 10:15:00							
EAS-US	2026-08-28 10:30:00							
EAS-US	2026-08-28 10:45:00							
EAS-US	2026-08-28 11:00:00	16.09	27.15	0.47	7.22	9.39	8.51	0.01
EAS-US	2026-08-28 11:15:00							
EAS-US	2026-08-28 11:30:00							
EAS-US	2026-08-28 11:45:00							
EAS-US	2026-08-28 12:00:00	16.13	27.24	0.47	7.27	9.46	8.51	0.01
EAS-US	2026-08-28 12:15:00							
EAS-US	2026-08-28 12:30:00							
EAS-US	2026-08-28 12:45:00							
EAS-US	2026-08-28 13:00:00	16.22	27.15	0.46	7.26	9.46	8.39	0.01
EAS-US	2026-08-28 13:15:00							
EAS-US	2026-08-28 13:30:00							
EAS-US	2026-08-28 13:45:00							
EAS-US	2026-08-28 14:00:00	16.36	27.15	0.46	7.31	9.47	9.31	0.01
EAS-US	2026-08-28 14:15:00							
EAS-US	2026-08-28 14:30:00							
EAS-US	2026-08-28 14:45:00							
EAS-US	2026-08-28 15:00:00	16.40	27.37	0.47	7.25	9.32	8.50	0.01
EAS-US	2026-08-28 15:15:00							
EAS-US	2026-08-28 15:30:00							
EAS-US	2026-08-28 15:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-28 16:00:00	16.42	27.55	0.47	7.23	9.28	8.54	0.01
EAS-US	2026-08-28 16:15:00							
EAS-US	2026-08-28 16:30:00							
EAS-US	2026-08-28 16:45:00							
EAS-US	2026-08-28 17:00:00	16.40	27.71	0.47	7.22	9.22	8.49	0.01
EAS-US	2026-08-28 17:15:00							
EAS-US	2026-08-28 17:30:00							
EAS-US	2026-08-28 17:45:00							
EAS-US	2026-08-28 18:00:00	16.35	27.99	0.47	7.23	9.13	8.52	0.01
EAS-US	2026-08-28 18:15:00							
EAS-US	2026-08-28 18:30:00							
EAS-US	2026-08-28 18:45:00							
EAS-US	2026-08-28 19:00:00	16.31	28.11	0.47	7.21	9.12	8.51	0.01
EAS-US	2026-08-28 19:15:00							
EAS-US	2026-08-28 19:30:00							
EAS-US	2026-08-28 19:45:00							
EAS-US	2026-08-28 20:00:00	16.19	28.38	0.44	7.22	9.08	8.69	0.01
EAS-US	2026-08-28 20:15:00							
EAS-US	2026-08-28 20:30:00							
EAS-US	2026-08-28 20:45:00							
EAS-US	2026-08-28 21:00:00	15.95	28.80	0.45	7.17	9.25	8.96	0.01
EAS-US	2026-08-28 21:15:00							
EAS-US	2026-08-28 21:30:00							
EAS-US	2026-08-28 21:45:00							
EAS-US	2026-08-28 22:00:00	15.87	116.13	0.46	7.34	9.24	9.67	0.05
EAS-US	2026-08-28 22:15:00							
EAS-US	2026-08-28 22:30:00							
EAS-US	2026-08-28 22:45:00							
EAS-US	2026-08-28 23:00:00	15.77	71.26	0.44	7.37	9.33	9.82	0.03
EAS-US	2026-08-28 23:15:00							
EAS-US	2026-08-28 23:30:00							
EAS-US	2026-08-28 23:45:00							
EAS-US	2026-08-29 00:00:00	15.61	47.11	0.45	7.31	9.36	9.22	0.02
EAS-US	2026-08-29 00:15:00							
EAS-US	2026-08-29 00:30:00							
EAS-US	2026-08-29 00:45:00							
EAS-US	2026-08-29 01:00:00	15.50	38.26	0.46	7.25	9.35	8.64	0.02
EAS-US	2026-08-29 01:15:00							
EAS-US	2026-08-29 01:30:00							
EAS-US	2026-08-29 01:45:00							
EAS-US	2026-08-29 02:00:00	15.34	34.09	0.46	7.21	9.37	8.57	0.01
EAS-US	2026-08-29 02:15:00							
EAS-US	2026-08-29 02:30:00							
EAS-US	2026-08-29 02:45:00							
EAS-US	2026-08-29 03:00:00	15.20	32.15	0.46	7.21	9.38	8.61	0.01
EAS-US	2026-08-29 03:15:00							
EAS-US	2026-08-29 03:30:00							
EAS-US	2026-08-29 03:45:00							
EAS-US	2026-08-29 04:00:00	15.06	31.18	0.46	7.24	9.41	8.47	0.01
EAS-US	2026-08-29 04:15:00							
EAS-US	2026-08-29 04:30:00							
EAS-US	2026-08-29 04:45:00							
EAS-US	2026-08-29 05:00:00	14.91	30.45	0.46	7.22	9.43	8.54	0.01
EAS-US	2026-08-29 05:15:00							
EAS-US	2026-08-29 05:30:00							
EAS-US	2026-08-29 05:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-29 06:00:00	14.75	29.98	0.47	7.20	9.46	8.51	0.01
EAS-US	2026-08-29 06:15:00							
EAS-US	2026-08-29 06:30:00							
EAS-US	2026-08-29 06:45:00							
EAS-US	2026-08-29 07:00:00	14.57	29.13	0.47	7.22	9.51	8.53	0.01
EAS-US	2026-08-29 07:15:00							
EAS-US	2026-08-29 07:30:00							
EAS-US	2026-08-29 07:45:00							
EAS-US	2026-08-29 08:00:00	14.42	28.95	0.46	7.21	9.60	8.56	0.01
EAS-US	2026-08-29 08:15:00							
EAS-US	2026-08-29 08:30:00							
EAS-US	2026-08-29 08:45:00							
EAS-US	2026-08-29 09:00:00	14.37	28.48	0.46	7.23	9.69	8.48	0.01
EAS-US	2026-08-29 09:15:00							
EAS-US	2026-08-29 09:30:00							
EAS-US	2026-08-29 09:45:00							
EAS-US	2026-08-29 10:00:00	14.49	28.16	0.45	7.28	9.78	8.49	0.01
EAS-US	2026-08-29 10:15:00							
EAS-US	2026-08-29 10:30:00							
EAS-US	2026-08-29 10:45:00							
EAS-US	2026-08-29 11:00:00	15.47	27.56	0.43	7.36	9.90	8.74	0.01
EAS-US	2026-08-29 11:15:00							
EAS-US	2026-08-29 11:30:00							
EAS-US	2026-08-29 11:45:00							
EAS-US	2026-08-29 12:00:00	15.86	27.50	0.43	7.32	9.72	8.58	0.01
EAS-US	2026-08-29 12:15:00							
EAS-US	2026-08-29 12:30:00							
EAS-US	2026-08-29 12:45:00							
EAS-US	2026-08-29 13:00:00	16.36	27.34	0.44	7.31	9.52	8.84	0.01
EAS-US	2026-08-29 13:15:00							
EAS-US	2026-08-29 13:30:00							
EAS-US	2026-08-29 13:45:00							
EAS-US	2026-08-29 14:00:00	16.84	27.39	0.44	7.33	9.35	9.03	0.01
EAS-US	2026-08-29 14:15:00							
EAS-US	2026-08-29 14:30:00							
EAS-US	2026-08-29 14:45:00							
EAS-US	2026-08-29 15:00:00	17.11	27.24	0.44	7.30	9.29	9.00	0.01
EAS-US	2026-08-29 15:15:00							
EAS-US	2026-08-29 15:30:00							
EAS-US	2026-08-29 15:45:00							
EAS-US	2026-08-29 16:00:00	16.98	27.43	0.45	7.29	9.27	8.99	0.01
EAS-US	2026-08-29 16:15:00							
EAS-US	2026-08-29 16:30:00							
EAS-US	2026-08-29 16:45:00							
EAS-US	2026-08-29 17:00:00	16.92	27.51	0.45	7.26	9.20	8.85	0.01
EAS-US	2026-08-29 17:15:00							
EAS-US	2026-08-29 17:30:00							
EAS-US	2026-08-29 17:45:00							
EAS-US	2026-08-29 18:00:00	16.77	27.73	0.45	7.25	9.14	9.10	0.01
EAS-US	2026-08-29 18:15:00							
EAS-US	2026-08-29 18:30:00							
EAS-US	2026-08-29 18:45:00							
EAS-US	2026-08-29 19:00:00	16.58	28.11	0.46	7.20	9.05	8.94	0.01
EAS-US	2026-08-29 19:15:00							
EAS-US	2026-08-29 19:30:00							
EAS-US	2026-08-29 19:45:00							

Woodfibre LNG (East Creek) □								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-29 20:00:00	16.32	28.54	0.46	7.20	9.03	9.12	0.01
EAS-US	2026-08-29 20:15:00							
EAS-US	2026-08-29 20:30:00							
EAS-US	2026-08-29 20:45:00							
EAS-US	2026-08-29 21:00:00	16.08	28.62	0.46	7.18	9.06	8.90	0.01
EAS-US	2026-08-29 21:15:00							
EAS-US	2026-08-29 21:30:00							
EAS-US	2026-08-29 21:45:00							
EAS-US	2026-08-29 22:00:00	15.87	28.60	0.47	7.15	9.13	8.81	0.01
EAS-US	2026-08-29 22:15:00							
EAS-US	2026-08-29 22:30:00							
EAS-US	2026-08-29 22:45:00							
EAS-US	2026-08-29 23:00:00	15.68	28.27	0.47	7.16	9.18	8.89	0.01
EAS-US	2026-08-29 23:15:00							
EAS-US	2026-08-29 23:30:00							
EAS-US	2026-08-29 23:45:00							
EAS-US	2026-08-30 00:00:00	15.52	28.35	0.46	7.15	9.22	8.85	0.01
EAS-US	2026-08-30 00:15:00							
EAS-US	2026-08-30 00:30:00							
EAS-US	2026-08-30 00:45:00							
EAS-US	2026-08-30 01:00:00	15.38	28.23	0.46	7.16	9.26	8.72	0.01
EAS-US	2026-08-30 01:15:00							
EAS-US	2026-08-30 01:30:00							
EAS-US	2026-08-30 01:45:00							
EAS-US	2026-08-30 02:00:00	15.23	28.12	0.47	7.15	9.32	8.79	0.01
EAS-US	2026-08-30 02:15:00							
EAS-US	2026-08-30 02:30:00							
EAS-US	2026-08-30 02:45:00							
EAS-US	2026-08-30 03:00:00	15.10	27.97	0.46	7.16	9.35	8.82	0.01
EAS-US	2026-08-30 03:15:00							
EAS-US	2026-08-30 03:30:00							
EAS-US	2026-08-30 03:45:00							
EAS-US	2026-08-30 04:00:00	15.04	27.92	0.47	7.16	9.37	8.89	0.01
EAS-US	2026-08-30 04:15:00							
EAS-US	2026-08-30 04:30:00							
EAS-US	2026-08-30 04:45:00							
EAS-US	2026-08-30 05:00:00	14.99	27.83	0.47	7.16	9.39	8.93	0.01
EAS-US	2026-08-30 05:15:00							
EAS-US	2026-08-30 05:30:00							
EAS-US	2026-08-30 05:45:00							
EAS-US	2026-08-30 06:00:00	14.93	27.79	0.47	7.16	9.42	9.46	0.01
EAS-US	2026-08-30 06:15:00							
EAS-US	2026-08-30 06:30:00							
EAS-US	2026-08-30 06:45:00							
EAS-US	2026-08-30 07:00:00	14.88	27.65	0.47	7.16	9.44	9.09	0.01
EAS-US	2026-08-30 07:15:00							
EAS-US	2026-08-30 07:30:00							
EAS-US	2026-08-30 07:45:00							
EAS-US	2026-08-30 08:00:00	14.84	27.64	0.47	7.17	9.46	8.86	0.01
EAS-US	2026-08-30 08:15:00							
EAS-US	2026-08-30 08:30:00							
EAS-US	2026-08-30 08:45:00							
EAS-US	2026-08-30 09:00:00	14.84	27.32	0.47	7.18	9.56	8.92	0.01
EAS-US	2026-08-30 09:15:00							
EAS-US	2026-08-30 09:30:00							
EAS-US	2026-08-30 09:45:00							

Woodfibre LNG (East Creek)□								
Station	Date/Time	Temperature (C)	Specific Conductivity (µS/cm)	ORP (V)	pH (pH units)	Dissolved Oxygen (mg/L)	Turbidity (NTU)	Salinity (PSU)
EAS-US	2026-08-30 10:00:00	14.90	27.12	0.46	7.23	9.64	8.86	0.01
EAS-US	2026-08-30 10:15:00							
EAS-US	2026-08-30 10:30:00							
EAS-US	2026-08-30 10:45:00							
EAS-US	2026-08-30 11:00:00	14.94	26.95	0.46	7.21	9.66	8.89	0.01
EAS-US	2026-08-30 11:15:00							
EAS-US	2026-08-30 11:30:00							
EAS-US	2026-08-30 11:45:00							
EAS-US	2026-08-30 12:00:00	15.00	26.84	0.46	7.25	9.68	8.96	0.01
EAS-US	2026-08-30 12:15:00							
EAS-US	2026-08-30 12:30:00							
EAS-US	2026-08-30 12:45:00							
EAS-US	2026-08-30 13:00:00	15.08	26.68	0.44	7.26	9.73	8.96	0.01
EAS-US	2026-08-30 13:15:00							
EAS-US	2026-08-30 13:30:00							
EAS-US	2026-08-30 13:45:00							
EAS-US	2026-08-30 14:00:00	15.18	26.65	0.44	7.27	9.71	8.89	0.01
EAS-US	2026-08-30 14:15:00							
EAS-US	2026-08-30 14:30:00							
EAS-US	2026-08-30 14:45:00							
EAS-US	2026-08-30 15:00:00	15.24	26.81	0.44	7.23	9.60	8.97	0.01
EAS-US	2026-08-30 15:15:00							
EAS-US	2026-08-30 15:30:00							
EAS-US	2026-08-30 15:45:00							
EAS-US	2026-08-30 16:00:00	15.29	27.01	0.45	7.24	9.58	9.06	0.01
EAS-US	2026-08-30 16:15:00							
EAS-US	2026-08-30 16:30:00							
EAS-US	2026-08-30 16:45:00							
EAS-US	2026-08-30 17:00:00	15.36	26.91	0.44	7.24	9.62	9.00	0.01
EAS-US	2026-08-30 17:15:00							
EAS-US	2026-08-30 17:30:00							
EAS-US	2026-08-30 17:45:00							
EAS-US	2026-08-30 18:00:00	15.40	27.19	0.46	7.26	9.52	8.96	0.01
EAS-US	2026-08-30 18:15:00							
EAS-US	2026-08-30 18:30:00							
EAS-US	2026-08-30 18:45:00							
EAS-US	2026-08-30 19:00:00	15.40	27.47	0.46	7.20	9.41	9.09	0.01
EAS-US	2026-08-30 19:15:00							
EAS-US	2026-08-30 19:30:00							
EAS-US	2026-08-30 19:45:00							
EAS-US	2026-08-30 20:00:00	15.36	27.81	0.46	7.20	9.35	9.04	0.01
EAS-US	2026-08-30 20:15:00							
EAS-US	2026-08-30 20:30:00							
EAS-US	2026-08-30 20:45:00							
EAS-US	2026-08-30 21:00:00	15.29	27.96	0.46	7.16	9.33	9.21	0.01
EAS-US	2026-08-30 21:15:00							
EAS-US	2026-08-30 21:30:00							
EAS-US	2026-08-30 21:45:00							
EAS-US	2026-08-30 22:00:00	15.24	28.02	0.46	7.18	9.33	9.07	0.01
EAS-US	2026-08-30 22:15:00							
EAS-US	2026-08-30 22:30:00							
EAS-US	2026-08-30 22:45:00							
EAS-US	2026-08-30 23:00:00	15.15	27.92	0.46	7.18	9.36	9.09	0.01
EAS-US	2026-08-30 23:15:00							
EAS-US	2026-08-30 23:30:00							
EAS-US	2026-08-30 23:45:00							

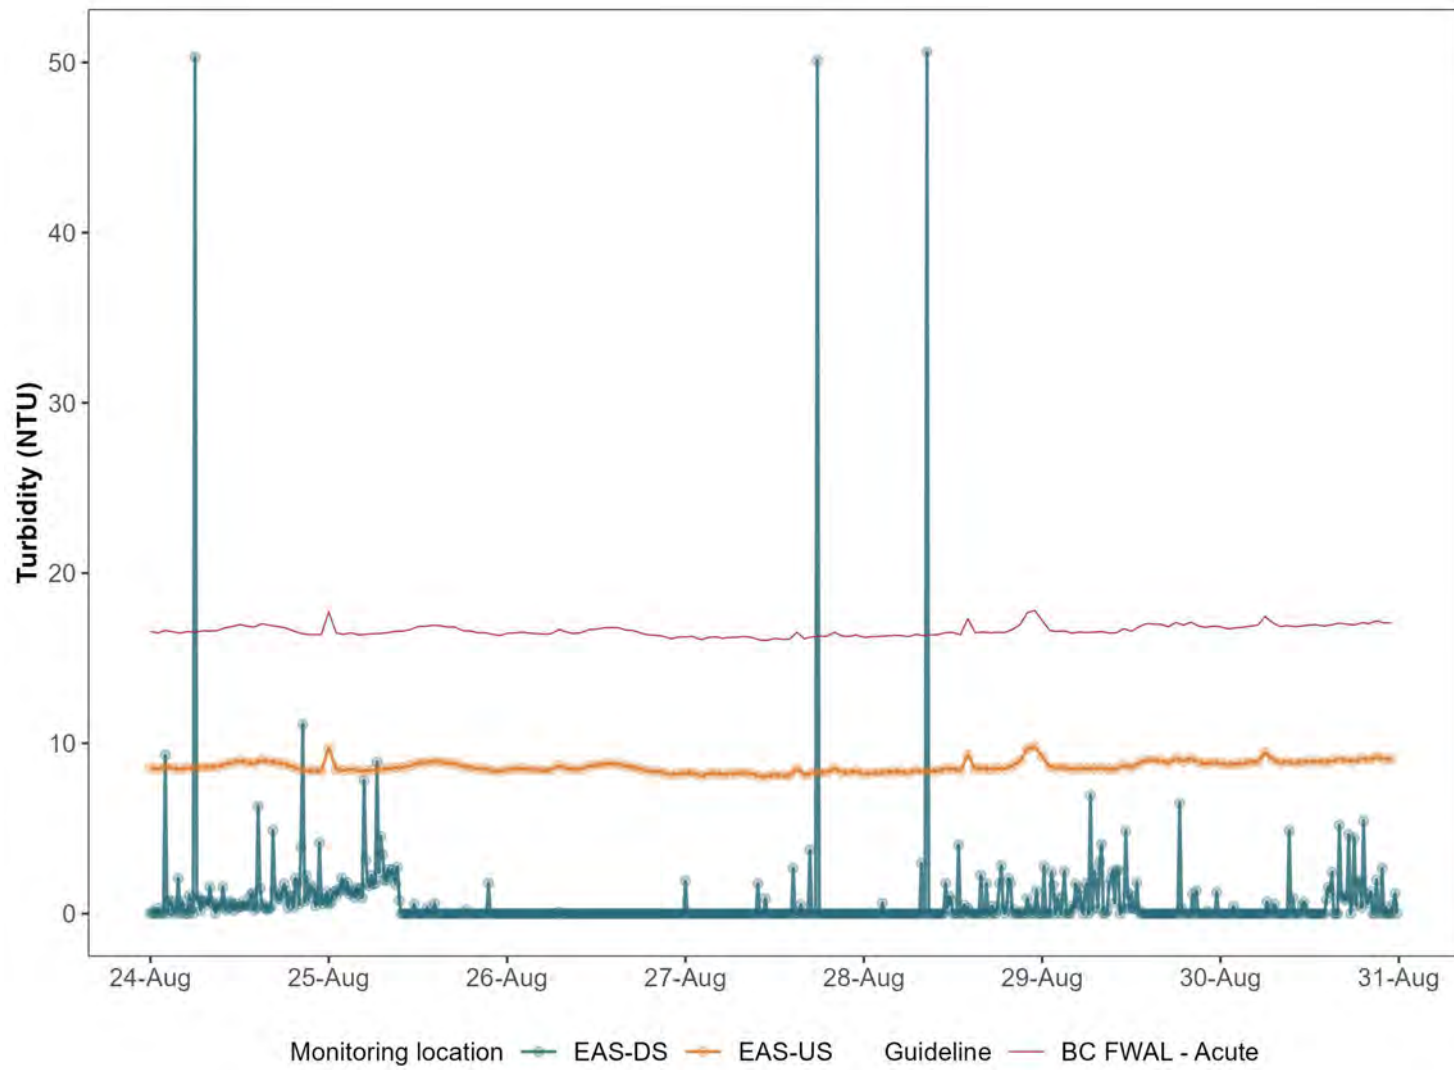

 Eagle Mountain – Woodfibre Gas Pipeline Project Waste Discharge Permit PE-110163 Report	Reporting Week	August 24 to August 30, 2026
	Report #	127
	Appendix E	E-1

Appendix E:
Lab Documentation



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 139719

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/09/09
 Report #: R3826118
 Version: 3 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C654848

Received: 2026/08/25, 14:10

Sample Matrix: Water
 # Samples Received: 6

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
Alkalinity @25C (pp, total), CO ₃ ,HCO ₃ ,OH	6	N/A	2026/08/27	BBY6SOP-00026	SM 24 2320 B m
Chloride/Sulphate by Auto Colourimetry	6	N/A	2026/08/26	BBY6SOP-00011 / BBY6SOP-00017	SM24-4500-Cl/SO ₄ -E m
Chromium III (Calc'd)	2	N/A	2026/08/28		
Chromium III (Calc'd)	4	N/A	2026/08/31		
Total Hexavalent Chromium	6	N/A	2026/08/26	BBY6SOP-00054	SM 24 3500-Cr B m
Daphnia Magna LC50 Multi-concentration	1	N/A	2026/08/26	BBY2SOP-00007	EC EPS 1/RM/14 R2
Carbon (DOC) -Lab Filtered (2)	6	N/A	2026/08/29	BBY6SOP-00053	SM 24 5310 B m
Fluoride	6	N/A	2026/08/26	BBY6SOP-00037	SM 24 4500-F C m
Glycols in Water by GC/FID (1)	2	N/A	2026/08/27	CAL SOP-00093	BCMOE Glycols 09/17
Sulphide (as H ₂ S) (1)	6	N/A	2026/08/28		Auto Calc
Un-ionized Hydrogen Sulphide as S Calc	4	N/A	2026/08/28	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	2	N/A	2026/08/28	BBY WI-00033	Auto Calc
Hardness Total (calculated as CaCO ₃) (3)	4	N/A	2026/08/31	BBY WI-00033	Auto Calc
Hardness (calculated as CaCO ₃)	6	N/A	2026/08/31	BBY WI-00033	Auto Calc
Mercury (Dissolved) by CV-Lab Filtered	6	2026/08/31	2026/08/31	BBY7SOP-00032	BCMOE LMAug2023 C m
Mercury (Total) by CV	6	2026/08/28	2026/08/28	BBY7SOP-00032	BCMOE LMAug2023 C m
Bromide as Bromine (Br) by ICPMS	6	N/A	2026/08/27	BBY7SOP-00002	EPA 6020B R2 m
EPH in Water when PAH required	2	2026/08/27	2026/08/28	BBY8SOP-00029	BCMOE BCLM Sep2017 m
Na, K, Ca, Mg, S by CRC ICPMS (diss.)	6	N/A	2026/08/31	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (lab filter) (4)	6	N/A	2026/08/28	BBY7SOP-00002	EPA 6020b R2 m
Elements by ICPMS Digested LL (total)	2	2026/08/27	2026/08/27	BBY7SOP-00003 / BBY7SOP-00002	EPA 6020b R2 m
Na, K, Ca, Mg, S by CRC ICPMS (total)	2	N/A	2026/08/28	BBY WI-00033	Auto Calc
Na, K, Ca, Mg, S by CRC ICPMS (total)	4	N/A	2026/08/31	BBY WI-00033	Auto Calc
Elements by ICPMS Low Level (total)	4	N/A	2026/08/28	BBY7SOP-00002	EPA 6020b R2 m
Nitrogen (Total)	6	N/A	2026/08/28	BBY6SOP-00016	SM 24 4500-N C m
Ammonia-N (Total)	6	N/A	2026/08/26	AB SOP-00007	SM 24 4500 NH ₃ A G m
Nitrate + Nitrite (N)	6	N/A	2026/08/26	BBY6SOP-00010	SM 24 4500-NO ₃ - H m
Nitrite (N) Regular Level Water	6	N/A	2026/08/26	BBY6SOP-00010	SM 24 4500-NO ₂ - m
Nitrogen - Nitrate (as N)	6	N/A	2026/08/27	BBY WI-00033	Auto Calc



Your P.O. #: 4800010213
 Your Project #: FORTIS11234/PE110163
 Site Location: WOODFIBRE PIPELINE PROJECT
 Your C.O.C. #: 139719

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
 N. VANCOUVER
 200-850 Harbourside Dr
 North Vancouver, BC
 Canada V7P 0A3

Report Date: 2026/09/09
 Report #: R3826118
 Version: 3 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C654848

Received: 2026/08/25, 14:10

Sample Matrix: Water
 # Samples Received: 6

Analyses	Quantity	Date Extracted	Date Analyzed	Laboratory Method	Analytical Method
PAH in Water by GC/MS (SIM)	2	2026/08/27	2026/08/27	BBY8SOP-00021	BCMOE BCLM Jul2017m
Total LMW, HMW, Total PAH Calc (5)	2	N/A	2026/08/31	BBY WI-00033	Auto Calc
pH @25°C (6)	6	N/A	2026/08/27	BBY6SOP-00026	SM 24 4500-H+ B m
Phenols (4-AAP) (1)	2	N/A	2026/08/28	AB SOP-00088	EPA 9066 R0 m
Rainbow Trout LC50 Multi-concentration	1	N/A	2026/08/27	BBY2SOP-00004	EPS1/RM/13(2nd)&RM/9
Total Sulphide (1)	6	2026/08/27	2026/08/28	AB SOP-00080	SM 24 4500 S2-A D Fm
Total Dissolved Solids (Filt. Residue)	6	2026/08/26	2026/08/27	BBY6SOP-00033	SM 24 2540 C m
EPH less PAH in Water by GC/FID (7)	2	N/A	2026/08/31	BBY WI-00033	Auto Calc
Carbon (Total Organic) (8)	2	N/A	2026/08/28	BBY6SOP-00053	SM 24 5310 B m
Carbon (Total Organic) (8)	4	N/A	2026/08/29	BBY6SOP-00053	SM 24 5310 B m
Total Phosphorus Low Level Total	6	2026/08/27	2026/08/29	BBY6SOP-00013	SM 24 4500-P E m
Total Suspended Solids (NFR)	5	2026/08/26	2026/08/27	BBY6SOP-00034	SM 24 2540 D m
Total Suspended Solids (NFR)	1	2026/08/27	2026/08/28	BBY6SOP-00034	SM 24 2540 D m
Field pH	4	N/A	2026/08/26	Field Test	Field Test
Field Temperature	4	N/A	2026/08/26	Field Test	Field Test
VOCs, VH, F1, LH in Water by HS GC/MS	1	N/A	2026/08/28	BBY8SOP-00009 / BBY8SOP-00011 / BBY8SOP-00012	BCMOE BCLM Jul2017 m
VOCs, VH, F1, LH in Water by HS GC/MS	1	N/A	2026/08/29	BBY8SOP-00009 / BBY8SOP-00011 / BBY8SOP-00012	BCMOE BCLM Jul2017 m
Volatile HC-BTEX (9)	2	N/A	2026/08/31	BBY WI-00033	Auto Calc

Remarks:

Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation. Unless otherwise noted, procedures used by Bureau Veritas are based upon recognized Provincial, Federal or US method compendia such as CCME, EPA, APHA or the Quebec Ministry of Environment.

All work recorded herein has been done in accordance with procedures and practices ordinarily exercised by professionals in Bureau Veritas' profession using accepted testing methodologies, quality assurance and quality control procedures (except where otherwise agreed by the client and Bureau Veritas in writing). All data is in statistical control and has met quality control and method performance criteria unless otherwise noted. All method blanks are reported; unless indicated otherwise, associated sample data are not blank corrected. Where applicable, unless otherwise noted, Measurement Uncertainty has not been accounted for when stating conformity to the referenced standard.



Your P.O. #: 4800010213
Your Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your C.O.C. #: 139719

Attention: Saeesh Mangwani

HATFIELD CONSULTANTS
N. VANCOUVER
200-850 Harbourside Dr
North Vancouver, BC
Canada V7P 0A3

Report Date: 2026/09/09

Report #: R3826118

Version: 3 - Final

CERTIFICATE OF ANALYSIS

BUREAU VERITAS JOB #: C654848

Received: 2026/08/25, 14:10

Bureau Veritas liability is limited to the actual cost of the requested analyses, unless otherwise agreed in writing. There is no other warranty expressed or implied. Bureau Veritas has been retained to provide analysis of samples provided by the Client using the testing methodology referenced in this report. Interpretation and use of test results are the sole responsibility of the Client and are not within the scope of services provided by Bureau Veritas, unless otherwise agreed in writing. Bureau Veritas is not responsible for the accuracy or any data impacts, that result from the information provided by the customer or their agent.

Solid sample results, except biota, are based on dry weight unless otherwise indicated. Organic analyses are not recovery corrected except for isotope dilution methods.

Results relate to samples tested. When sampling is not conducted by Bureau Veritas, results relate to the supplied samples tested.

This Certificate shall not be reproduced except in full, without the written approval of the laboratory.

Reference Method suffix "m" indicates test methods incorporate validated modifications from specific reference methods to improve performance.

* RPDs calculated using raw data. The rounding of final results may result in the apparent difference.

(1) This test was performed by Bureau Veritas Calgary, 4000 - 19 St. , Calgary, AB, T2E 6P8

(2) DOC present in the sample should be considered as non-purgeable DOC. Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(3) "Total Hardness" was calculated from Total Ca and Mg concentrations and may be biased high (Hardness, or Dissolved Hardness, calculated from Dissolved Ca and Mg, should be used for compliance if available).

(4) Samples were filtered and preserved at the lab. Values may not reflect concentrations at the time of sampling.

For Dissolved > Total Imbalance: When applicable, Dissolved and Total results were reviewed and data quality meets acceptable levels unless otherwise noted.

(5) Total PAHs in Water include: Quinoline, Naphthalene, 1-Methylnaphthalene, 2-Methylnaphthalene, Acenaphthylene, Acenaphthene, Fluorene, Phenanthrene, Anthracene, Acridine, Fluoranthene, Pyrene, Benzo(a)anthracene, Chrysene, Benzo(b&j)fluoranthene, Benzo(k)fluoranthene, Benzo(a)pyrene, Indeno(1,2,3-cd)pyrene, Dibenz(a,h)anthracene, and Benzo(g,h,i)perylene.

(6) The CCME method requires pH to be analysed within 15 minutes of sampling and therefore field analysis is required for compliance. All Laboratory pH analyses in this report are reported past the CCME holding time. Bureau Veritas endeavours to analyze samples as soon as possible after receipt.

(7) LEPH = EPH (C10 to C19) - (Acenaphthene + Acridine + Anthracene + Fluorene + Naphthalene + Phenanthrene)

HEPH = EPH (C19 to C32) - (Benzo(a)anthracene + Benzo(a)pyrene + Fluoranthene + Pyrene)

(8) TOC present in the sample should be considered as non-purgeable TOC.

(9) VPH = VH - (Benzene + Toluene + Ethylbenzene + m & p-Xylene + o-Xylene + Styrene)

Encryption Key

Please direct all questions regarding this Certificate of Analysis to:

Levi Manchak, Senior Project Manager

Email: Levi.MANCHAK@bureauveritas.com

Phone# (780)862-5634

=====

Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports. For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.

Total Cover Pages : 3

Page 3 of 46



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM801			ELM802			ELM803		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG -EOP	RDL	QC Batch	WLNG-US	RDL	QC Batch

ANIONS

Nitrite (N)	mg/L	ND	0.0050	C390406	ND	0.0050	C390406	ND	0.0050	C390406
-------------	------	----	--------	---------	----	--------	---------	----	--------	---------

Calculated Parameters

Total Chromium III	mg/L	ND	0.00099	C389836	ND	0.00099	C389836	ND	0.00099	C389836
Dissolved Hardness (CaCO ₃)	mg/L	69.0	0.50	C389846	69.9	0.50	C389297	9.51	0.50	C389297
Total Hardness (CaCO ₃)	mg/L	65.8	0.50	C388997	68.7	0.50	C388997	9.28	0.50	C388997
Nitrate (N)	mg/L	ND	0.020	C389000	ND	0.020	C389000	ND	0.020	C389000
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C389728	ND	0.0020	C389728	ND	0.0020	C389728

Daphnia Magna

LC50	% vol/vol				ATTACHED	N/A	C390976			
------	-----------	--	--	--	----------	-----	---------	--	--	--

Field Parameters

Field pH	pH	7.60	N/A	ONSITE	7.22	N/A	ONSITE	7.45	N/A	ONSITE
Field Temperature	°C	14	N/A	ONSITE	14.6	N/A	ONSITE	16.2	N/A	ONSITE

Misc. Inorganics

pH	pH	7.38	N/A	C390734	7.42	N/A	C390734	6.54	N/A	C390734
Total Organic Carbon (C)	mg/L	0.69	0.50	C393648	0.66	0.50	C393648	1.9	0.50	C394095
Total Dissolved Solids	mg/L	52	10	C390447	64	10	C390447	ND	10	C390447
Total Suspended Solids	mg/L	1.2	1.0	C392250	1.6	1.0	C390608	ND	1.0	C390608

Lab Filtered Inorganics

Dissolved Organic Carbon (C)	mg/L	0.66	0.50	C394071	0.69	0.50	C394071	1.9	0.50	C394071
------------------------------	------	------	------	---------	------	------	---------	-----	------	---------

Anions

Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C390732	ND	1.0	C390732	ND	1.0	C390732
Alkalinity (Total as CaCO ₃)	mg/L	55	1.0	C390732	56	1.0	C390732	9.7	1.0	C390732
Bicarbonate (HCO ₃)	mg/L	67	1.0	C390732	68	1.0	C390732	12	1.0	C390732
Carbonate (CO ₃)	mg/L	ND	1.0	C390732	ND	1.0	C390732	ND	1.0	C390732
Fluoride (F)	mg/L	0.35	0.050	C390334	0.35	0.050	C390334	ND	0.050	C390334
Hydroxide (OH)	mg/L	ND	1.0	C390732	ND	1.0	C390732	ND	1.0	C390732
Total Sulphide	mg/L	ND	0.0018	C392160	ND	0.0018	C392160	ND	0.0018	C392160
Chloride (Cl)	mg/L	16	1.0	C390388	17	1.0	C390388	ND	1.0	C390388
Sulphate (SO ₄)	mg/L	15	1.0	C390388	15	1.0	C390388	1.8	1.0	C390388

RDL = Reportable Detection Limit

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.

N/A = Not Applicable



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM801			ELM802			ELM803		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG -EOP	RDL	QC Batch	WLNG-US	RDL	QC Batch
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.00099	C390373	ND	0.00099	C390373	ND	0.00099	C390373
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C390523	ND	0.015	C390523	ND	0.015	C390523
Total Phosphorus (P)	mg/L	0.0024	0.0010	C391669	0.0019	0.0010	C391669	0.016	0.0010	C391669
Nitrate plus Nitrite (N)	mg/L	ND	0.020	C390403	ND	0.020	C390403	ND	0.020	C390403
Total Nitrogen (N)	mg/L	0.188	0.020	C391569	0.185	0.020	C391569	0.106	0.020	C391569
Misc. Organics										
Phenols	mg/L				ND	0.0015	C393198			
Rainbow Trout										
LC50	% vol/vol				ATTACHED	N/A	C392541			
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM803			ELM804			ELM804		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L				ND	0.0050	C390406			
Calculated Parameters										
Total Chromium III	mg/L				ND	0.00099	C389836			
Dissolved Hardness (CaCO ₃)	mg/L				ND	0.50	C389297			
Total Hardness (CaCO ₃)	mg/L				ND	0.50	C388997			
Nitrate (N)	mg/L				ND	0.020	C389000			
Sulphide (as H ₂ S)	mg/L				ND	0.0020	C389728			
Misc. Inorganics										
pH	pH				5.99	N/A	C390734			
Total Organic Carbon (C)	mg/L				ND	0.50	C394095			
Total Dissolved Solids	mg/L				ND	10	C390447			
Total Suspended Solids	mg/L				ND	1.0	C390608			
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L				ND	0.50	C394071			
Anions										
Alkalinity (PP as CaCO ₃)	mg/L				ND	1.0	C390732			
Alkalinity (Total as CaCO ₃)	mg/L				ND	1.0	C390732			
Bicarbonate (HCO ₃)	mg/L				ND	1.0	C390732			
Carbonate (CO ₃)	mg/L				ND	1.0	C390732			
Fluoride (F)	mg/L	ND	0.050	C390334	ND	0.050	C390334			
Hydroxide (OH)	mg/L				ND	1.0	C390732			
Total Sulphide	mg/L				ND	0.0018	C392160			
Chloride (Cl)	mg/L				ND	1.0	C390388			
Sulphate (SO ₄)	mg/L				ND	1.0	C390388			
Metals										
Total Hex. Chromium (Cr 6+)	mg/L				ND	0.00099	C390373	ND	0.00099	C390373
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM803			ELM804			ELM804		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-US Lab-Dup	RDL	QC Batch	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch
Nutrients										
Total Ammonia (N)	mg/L				ND	0.015	C390523			
Total Phosphorus (P)	mg/L				ND	0.0010	C391669	ND	0.0010	C391669
Nitrate plus Nitrite (N)	mg/L				ND	0.020	C390403			
Total Nitrogen (N)	mg/L				ND	0.020	C391569	ND	0.020	C391569
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM805			ELM805			ELM806		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch	DUP	RDL	QC Batch
ANIONS										
Nitrite (N)	mg/L	ND	0.0050	C390406				ND	0.0050	C390406
Calculated Parameters										
Total Chromium III	mg/L	ND	0.00099	C389836				ND	0.00099	C389836
Dissolved Hardness (CaCO ₃)	mg/L	ND	0.50	C389297				71.0	0.50	C389297
Total Hardness (CaCO ₃)	mg/L	ND	0.50	C388997				68.3	0.50	C388997
Nitrate (N)	mg/L	ND	0.020	C389000				ND	0.020	C389000
Sulphide (as H ₂ S)	mg/L	ND	0.0020	C389728				ND	0.0020	C389728
Field Parameters										
Field pH	pH							7.22	N/A	ONSITE
Field Temperature	°C							14.6	N/A	ONSITE
Misc. Inorganics										
pH	pH	5.82	N/A	C390734				7.28	N/A	C390734
Total Organic Carbon (C)	mg/L	ND	0.50	C394095				0.61	0.50	C394095
Total Dissolved Solids	mg/L	ND	10	C390447	ND	10	C390447	72	10	C390447
Total Suspended Solids	mg/L	ND	1.0	C390608	ND	1.0	C390608	ND	1.0	C390608
Lab Filtered Inorganics										
Dissolved Organic Carbon (C)	mg/L	ND	0.50	C394071				0.54	0.50	C394071
Anions										
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C390732				ND	1.0	C390732
Alkalinity (Total as CaCO ₃)	mg/L	ND	1.0	C390732				55	1.0	C390732
Bicarbonate (HCO ₃)	mg/L	ND	1.0	C390732				67	1.0	C390732
Carbonate (CO ₃)	mg/L	ND	1.0	C390732				ND	1.0	C390732
Fluoride (F)	mg/L	ND	0.050	C390334				0.32	0.050	C390334
Hydroxide (OH)	mg/L	ND	1.0	C390732				ND	1.0	C390732
Total Sulphide	mg/L	ND	0.0018	C392160				ND	0.0018	C392160
Chloride (Cl)	mg/L	ND	1.0	C390388				17	1.0	C390388
Sulphate (SO ₄)	mg/L	ND	1.0	C390388				15	1.0	C390388
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit. N/A = Not Applicable										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM805			ELM805			ELM806		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	Trip Blank	RDL	QC Batch	Trip Blank Lab-Dup	RDL	QC Batch	DUP	RDL	QC Batch
Metals										
Total Hex. Chromium (Cr 6+)	mg/L	ND	0.00099	C390373				ND	0.00099	C390373
Nutrients										
Total Ammonia (N)	mg/L	ND	0.015	C390523				ND	0.015	C390523
Total Phosphorus (P)	mg/L	ND	0.0010	C391669				0.0012	0.0010	C391669
Nitrate plus Nitrite (N)	mg/L	ND	0.020	C390403				ND	0.020	C390403
Total Nitrogen (N)	mg/L	ND	0.020	C391569				0.174	0.020	C391569
Misc. Organics										
Phenols	mg/L							ND	0.0015	C393198
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

RESULTS OF CHEMICAL ANALYSES OF WATER

Bureau Veritas ID		ELM806		
Sampling Date		2026/08/25		
COC Number		139719		
	UNITS	DUP Lab-Dup	RDL	QC Batch
Misc. Inorganics				
pH	pH	7.41	N/A	C390734
Anions				
Alkalinity (PP as CaCO ₃)	mg/L	ND	1.0	C390732
Alkalinity (Total as CaCO ₃)	mg/L	55	1.0	C390732
Bicarbonate (HCO ₃)	mg/L	67	1.0	C390732
Carbonate (CO ₃)	mg/L	ND	1.0	C390732
Hydroxide (OH)	mg/L	ND	1.0	C390732
Nutrients				
Total Ammonia (N)	mg/L	ND	0.015	C390523
Misc. Organics				
Phenols	mg/L	ND	0.0015	C393198
RDL = Reportable Detection Limit Lab-Dup = Laboratory Initiated Duplicate N/A = Not Applicable ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.				



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

GLYCOLS BY GC-FID (WATER)

Bureau Veritas ID		ELM802	ELM806		
Sampling Date		2026/08/25	2026/08/25		
COC Number		139719	139719		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Glycols					
Ethylene Glycol	mg/L	ND	ND	3.0	C392159
Diethylene Glycol	mg/L	ND	ND	5.0	C392159
Triethylene Glycol	mg/L	ND	ND	5.0	C392159
Propylene Glycol	mg/L	ND	ND	5.0	C392159
Surrogate Recovery (%)					
Methyl Sulfone (sur.)	%	97	99		C392159
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

MERCURY BY COLD VAPOR (WATER)

Bureau Veritas ID		ELM801			ELM801			ELM802		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG-DS Lab-Dup	RDL	QC Batch	WLNG -EOP	RDL	QC Batch

Elements										
Total Mercury (Hg)	ug/L	ND	0.0019	C393252				ND	0.0019	C393998
Lab Filtered Elements										
Dissolved Mercury (Hg)	ug/L	ND	0.0019	C395272	ND	0.0019	C395272	ND	0.0019	C395272
RDL = Reportable Detection Limit										
Lab-Dup = Laboratory Initiated Duplicate										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										

Bureau Veritas ID		ELM803		ELM804		ELM805	ELM806		
Sampling Date		2026/08/25		2026/08/25		2026/08/25	2026/08/25		
COC Number		139719		139719		139719	139719		
	UNITS	WLNG-US	QC Batch	Field Blank	QC Batch	Trip Blank	DUP	RDL	QC Batch

Elements									
Total Mercury (Hg)	ug/L	ND	C393252	ND	C393998	ND	ND	0.0019	C393252
Lab Filtered Elements									
Dissolved Mercury (Hg)	ug/L	ND	C395272	ND	C395272	ND	ND	0.0019	C395272
RDL = Reportable Detection Limit									
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.									



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM801			ELM802			ELM803		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG -EOP	RDL	QC Batch	WLNG-US	RDL	QC Batch

ANIONS

Bromide (Br)	mg/L	ND	0.010	C391476	ND	0.010	C391476	ND	0.010	C391476
--------------	------	----	-------	---------	----	-------	---------	----	-------	---------

Dissolved Metals by ICPMS

Dissolved Calcium (Ca)	mg/L	25.2	0.050	C389305	25.6	0.050	C389305	3.22	0.050	C389305
Dissolved Magnesium (Mg)	mg/L	1.47	0.050	C389305	1.44	0.050	C389305	0.355	0.050	C389305
Dissolved Potassium (K)	mg/L	1.92	0.050	C389305	1.70	0.050	C389305	0.190	0.050	C389305
Dissolved Sodium (Na)	mg/L	9.06	0.050	C389305	9.27	0.050	C389305	1.89	0.050	C389305
Dissolved Sulphur (S)	mg/L	5.5	3.0	C389305	5.2	3.0	C389305	ND	3.0	C389305

Lab Filtered Metals

Dissolved Aluminum (Al)	ug/L	40.6	0.50	C393094	26.7	0.50	C393094	36.1	0.50	C393094
Dissolved Antimony (Sb)	ug/L	0.791	0.020	C393094	0.720	0.020	C393094	0.021	0.020	C393094
Dissolved Arsenic (As)	ug/L	0.860	0.020	C393094	1.01	0.020	C393094	0.141	0.020	C393094
Dissolved Barium (Ba)	ug/L	5.07	0.020	C393094	4.21	0.020	C393094	4.48	0.020	C393094
Dissolved Beryllium (Be)	ug/L	ND	0.010	C393094	ND	0.010	C393094	ND	0.010	C393094
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	0.0050	C393094
Dissolved Boron (B)	ug/L	13	10	C393094	14	10	C393094	ND	10	C393094
Dissolved Cadmium (Cd)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	0.0050	C393094
Dissolved Cesium (Cs)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	0.050	C393094
Dissolved Chromium (Cr)	ug/L	ND	0.10	C393094	ND	0.10	C393094	ND	0.10	C393094
Dissolved Cobalt (Co)	ug/L	0.0165	0.0050	C393094	0.0270	0.0050	C393094	0.0152	0.0050	C393094
Dissolved Copper (Cu)	ug/L	0.065	0.050	C393094	0.058	0.050	C393094	0.737	0.050	C393094
Dissolved Iron (Fe)	ug/L	1.1	1.0	C393094	ND	1.0	C393094	41.8	1.0	C393094
Dissolved Lead (Pb)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	0.0172	0.0050	C393094
Dissolved Lithium (Li)	ug/L	8.44	0.50	C393094	8.26	0.50	C393094	ND	0.50	C393094
Dissolved Manganese (Mn)	ug/L	17.4	0.050	C393094	24.5	0.050	C393094	0.909	0.050	C393094
Dissolved Molybdenum (Mo)	ug/L	49.3	0.050	C393094	48.2	0.050	C393094	0.785	0.050	C393094
Dissolved Nickel (Ni)	ug/L	0.125	0.020	C393094	0.173	0.020	C393094	0.277	0.020	C393094
Dissolved Phosphorus (P)	ug/L	2.8	2.0	C393094	3.2	2.0	C393094	11.9	2.0	C393094
Dissolved Rubidium (Rb)	ug/L	4.18	0.050	C393094	3.89	0.050	C393094	0.409	0.050	C393094
Dissolved Selenium (Se)	ug/L	ND	0.040	C393094	ND	0.040	C393094	ND	0.040	C393094
Dissolved Silicon (Si)	ug/L	6540	50	C393094	6800	50	C393094	5180	50	C393094
Dissolved Silver (Ag)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	0.0050	C393094

RDL = Reportable Detection Limit

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM801			ELM802			ELM803		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG -EOP	RDL	QC Batch	WLNG-US	RDL	QC Batch
Dissolved Strontium (Sr)	ug/L	53.0	0.050	C393094	53.7	0.050	C393094	16.2	0.050	C393094
Dissolved Tellurium (Te)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	0.020	C393094
Dissolved Thallium (Tl)	ug/L	0.0074	0.0020	C393094	0.0085	0.0020	C393094	ND	0.0020	C393094
Dissolved Thorium (Th)	ug/L	ND	0.0050	C393094	0.0050	0.0050	C393094	0.0116	0.0050	C393094
Dissolved Tin (Sn)	ug/L	ND	0.20	C393094	ND	0.20	C393094	ND	0.20	C393094
Dissolved Titanium (Ti)	ug/L	ND	0.50	C393094	ND	0.50	C393094	ND	0.50	C393094
Dissolved Uranium (U)	ug/L	0.575	0.0020	C393094	0.254	0.0020	C393094	0.0532	0.0020	C393094
Dissolved Vanadium (V)	ug/L	ND	0.20	C393094	ND	0.20	C393094	0.22	0.20	C393094
Dissolved Zinc (Zn)	ug/L	1.70	0.10	C393094	2.77	0.10	C393094	0.51	0.10	C393094
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C393094	ND	0.10	C393094	ND	0.10	C393094
Total Metals by ICPMS										
Total Aluminum (Al)	ug/L	54.2	3.0	C391177	38.1	0.50	C391403	38.8	3.0	C391177
Total Antimony (Sb)	ug/L	0.770	0.020	C391177	0.735	0.020	C391403	0.021	0.020	C391177
Total Arsenic (As)	ug/L	0.845	0.020	C391177	0.997	0.020	C391403	0.141	0.020	C391177
Total Barium (Ba)	ug/L	4.65	0.050	C391177	4.14	0.020	C391403	4.17	0.050	C391177
Total Beryllium (Be)	ug/L	ND	0.010	C391177	ND	0.010	C391403	ND	0.010	C391177
Total Bismuth (Bi)	ug/L	ND	0.010	C391177	ND	0.0050	C391403	ND	0.010	C391177
Total Boron (B)	ug/L	13	10	C391177	11	10	C391403	ND	10	C391177
Total Cadmium (Cd)	ug/L	ND	0.0050	C391177	ND	0.0050	C391403	0.0055	0.0050	C391177
Total Cesium (Cs)	ug/L	ND	0.050	C391177	ND	0.050	C391403	ND	0.050	C391177
Total Chromium (Cr)	ug/L	ND	0.10	C391177	ND	0.10	C391403	ND	0.10	C391177
Total Cobalt (Co)	ug/L	0.025	0.010	C391177	0.0290	0.0050	C391403	0.023	0.010	C391177
Total Copper (Cu)	ug/L	0.34	0.10	C391177	ND	0.050	C391403	0.71	0.10	C391177
Total Iron (Fe)	ug/L	10.2	5.0	C391177	9.8	1.0	C391403	54.3	5.0	C391177
Total Lead (Pb)	ug/L	ND	0.020	C391177	0.0051	0.0050	C391403	0.024	0.020	C391177
Total Lithium (Li)	ug/L	7.59	0.50	C391177	7.29	0.50	C391403	ND	0.50	C391177
Total Manganese (Mn)	ug/L	17.7	0.10	C391177	25.3	0.050	C391403	1.41	0.10	C391177
Total Molybdenum (Mo)	ug/L	47.2	0.050	C391177	48.5	0.050	C391403	0.717	0.050	C391177
Total Nickel (Ni)	ug/L	0.18	0.10	C391177	0.155	0.020	C391403	0.21	0.10	C391177
Total Phosphorus (P)	ug/L	ND	5.0	C391177	ND	2.0	C391403	14.2	5.0	C391177
Total Rubidium (Rb)	ug/L	3.91	0.050	C391177	3.81	0.050	C391403	0.394	0.050	C391177
Total Selenium (Se)	ug/L	ND	0.040	C391177	0.046	0.040	C391403	ND	0.040	C391177
RDL = Reportable Detection Limit										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM801			ELM802			ELM803		
Sampling Date		2026/08/25			2026/08/25			2026/08/25		
COC Number		139719			139719			139719		
	UNITS	WLNG-DS	RDL	QC Batch	WLNG -EOP	RDL	QC Batch	WLNG-US	RDL	QC Batch
Total Silicon (Si)	ug/L	6040	50	C391177	6650	50	C391403	4800	50	C391177
Total Silver (Ag)	ug/L	ND	0.010	C391177	ND	0.0050	C391403	ND	0.010	C391177
Total Strontium (Sr)	ug/L	46.7	0.050	C391177	51.6	0.050	C391403	14.9	0.050	C391177
Total Tellurium (Te)	ug/L	ND	0.020	C391177	ND	0.020	C391403	ND	0.020	C391177
Total Thallium (Tl)	ug/L	0.0083	0.0020	C391177	0.0077	0.0020	C391403	ND	0.0020	C391177
Total Thorium (Th)	ug/L	ND	0.050	C391177	ND	0.050	C391403	ND	0.050	C391177
Total Tin (Sn)	ug/L	ND	0.20	C391177	ND	0.20	C391403	ND	0.20	C391177
Total Titanium (Ti)	ug/L	ND	2.0	C391177	ND	0.50	C391403	ND	2.0	C391177
Total Uranium (U)	ug/L	0.560	0.0050	C391177	0.281	0.0020	C391403	0.0580	0.0050	C391177
Total Vanadium (V)	ug/L	ND	0.20	C391177	ND	0.20	C391403	0.21	0.20	C391177
Total Zinc (Zn)	ug/L	2.3	1.0	C391177	2.83	0.10	C391403	1.1	1.0	C391177
Total Zirconium (Zr)	ug/L	ND	0.10	C391177	ND	0.10	C391403	ND	0.10	C391177
Total Calcium (Ca)	mg/L	24.1	0.25	C389307	25.3	0.050	C389307	3.15	0.25	C389307
Total Magnesium (Mg)	mg/L	1.37	0.25	C389307	1.37	0.050	C389307	0.34	0.25	C389307
Total Potassium (K)	mg/L	1.85	0.25	C389307	1.75	0.050	C389307	ND	0.25	C389307
Total Sodium (Na)	mg/L	8.47	0.25	C389307	8.80	0.050	C389307	1.82	0.25	C389307
Total Sulphur (S)	mg/L	5.6	3.0	C389307	4.9	3.0	C389307	ND	3.0	C389307
RDL = Reportable Detection Limit										
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.										



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM804			ELM804			ELM805	ELM806		
Sampling Date		2026/08/25			2026/08/25			2026/08/25	2026/08/25		
COC Number		139719			139719			139719	139719		
	UNITS	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	DUP	RDL	QC Batch

ANIONS

Bromide (Br)	mg/L	ND	0.010	C391476				ND	ND	0.010	C391476
--------------	------	----	-------	---------	--	--	--	----	----	-------	---------

Dissolved Metals by ICPMS

Dissolved Calcium (Ca)	mg/L	ND	0.050	C389305				ND	26.1	0.050	C389305
Dissolved Magnesium (Mg)	mg/L	ND	0.050	C389305				ND	1.43	0.050	C389305
Dissolved Potassium (K)	mg/L	ND	0.050	C389305				ND	1.69	0.050	C389305
Dissolved Sodium (Na)	mg/L	ND	0.050	C389305				ND	9.28	0.050	C389305
Dissolved Sulphur (S)	mg/L	ND	3.0	C389305				ND	5.0	3.0	C389305

Lab Filtered Metals

Dissolved Aluminum (Al)	ug/L	ND	0.50	C393094	ND	0.50	C393094	ND	25.7	0.50	C393094
Dissolved Antimony (Sb)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	0.725	0.020	C393094
Dissolved Arsenic (As)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	1.02	0.020	C393094
Dissolved Barium (Ba)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	4.00	0.020	C393094
Dissolved Beryllium (Be)	ug/L	ND	0.010	C393094	ND	0.010	C393094	ND	ND	0.010	C393094
Dissolved Bismuth (Bi)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	ND	0.0050	C393094
Dissolved Boron (B)	ug/L	ND	10	C393094	ND	10	C393094	ND	14	10	C393094
Dissolved Cadmium (Cd)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	ND	0.0050	C393094
Dissolved Cesium (Cs)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	ND	0.050	C393094
Dissolved Chromium (Cr)	ug/L	ND	0.10	C393094	ND	0.10	C393094	ND	ND	0.10	C393094
Dissolved Cobalt (Co)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	0.0268	0.0050	C393094
Dissolved Copper (Cu)	ug/L	0.243	0.050	C393094	0.230	0.050	C393094	ND	0.053	0.050	C393094
Dissolved Iron (Fe)	ug/L	ND	1.0	C393094	ND	1.0	C393094	ND	ND	1.0	C393094
Dissolved Lead (Pb)	ug/L	0.0063	0.0050	C393094	0.0061	0.0050	C393094	ND	ND	0.0050	C393094
Dissolved Lithium (Li)	ug/L	ND	0.50	C393094	ND	0.50	C393094	ND	8.06	0.50	C393094
Dissolved Manganese (Mn)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	24.9	0.050	C393094
Dissolved Molybdenum (Mo)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	48.0	0.050	C393094
Dissolved Nickel (Ni)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	0.161	0.020	C393094
Dissolved Phosphorus (P)	ug/L	ND	2.0	C393094	3.1	2.0	C393094	ND	3.0	2.0	C393094
Dissolved Rubidium (Rb)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	3.76	0.050	C393094
Dissolved Selenium (Se)	ug/L	ND	0.040	C393094	ND	0.040	C393094	ND	ND	0.040	C393094
Dissolved Silicon (Si)	ug/L	ND	50	C393094	ND	50	C393094	ND	6870	50	C393094

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM804			ELM804			ELM805	ELM806		
Sampling Date		2026/08/25			2026/08/25			2026/08/25	2026/08/25		
COC Number		139719			139719			139719	139719		
	UNITS	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	DUP	RDL	QC Batch
Dissolved Silver (Ag)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	ND	0.0050	C393094
Dissolved Strontium (Sr)	ug/L	ND	0.050	C393094	ND	0.050	C393094	ND	53.0	0.050	C393094
Dissolved Tellurium (Te)	ug/L	ND	0.020	C393094	ND	0.020	C393094	ND	ND	0.020	C393094
Dissolved Thallium (Tl)	ug/L	ND	0.0020	C393094	ND	0.0020	C393094	ND	0.0072	0.0020	C393094
Dissolved Thorium (Th)	ug/L	ND	0.0050	C393094	ND	0.0050	C393094	ND	ND	0.0050	C393094
Dissolved Tin (Sn)	ug/L	ND	0.20	C393094	ND	0.20	C393094	ND	ND	0.20	C393094
Dissolved Titanium (Ti)	ug/L	ND	0.50	C393094	ND	0.50	C393094	ND	ND	0.50	C393094
Dissolved Uranium (U)	ug/L	ND	0.0020	C393094	ND	0.0020	C393094	ND	0.250	0.0020	C393094
Dissolved Vanadium (V)	ug/L	ND	0.20	C393094	ND	0.20	C393094	ND	ND	0.20	C393094
Dissolved Zinc (Zn)	ug/L	0.17	0.10	C393094	0.17	0.10	C393094	ND	2.75	0.10	C393094
Dissolved Zirconium (Zr)	ug/L	ND	0.10	C393094	ND	0.10	C393094	ND	ND	0.10	C393094
Total Metals by ICPMS											
Total Aluminum (Al)	ug/L	ND	0.50	C391403	ND	0.50	C391403	ND	35.9	0.50	C391403
Total Antimony (Sb)	ug/L	ND	0.020	C391403	ND	0.020	C391403	ND	0.721	0.020	C391403
Total Arsenic (As)	ug/L	ND	0.020	C391403	ND	0.020	C391403	ND	0.977	0.020	C391403
Total Barium (Ba)	ug/L	ND	0.020	C391403	ND	0.020	C391403	ND	4.13	0.020	C391403
Total Beryllium (Be)	ug/L	ND	0.010	C391403	ND	0.010	C391403	ND	ND	0.010	C391403
Total Bismuth (Bi)	ug/L	ND	0.0050	C391403	ND	0.0050	C391403	ND	ND	0.0050	C391403
Total Boron (B)	ug/L	ND	10	C391403	ND	10	C391403	ND	11	10	C391403
Total Cadmium (Cd)	ug/L	ND	0.0050	C391403	ND	0.0050	C391403	ND	ND	0.0050	C391403
Total Cesium (Cs)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	ND	0.050	C391403
Total Chromium (Cr)	ug/L	ND	0.10	C391403	ND	0.10	C391403	ND	ND	0.10	C391403
Total Cobalt (Co)	ug/L	ND	0.0050	C391403	ND	0.0050	C391403	ND	0.0264	0.0050	C391403
Total Copper (Cu)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	ND	0.050	C391403
Total Iron (Fe)	ug/L	ND	1.0	C391403	ND	1.0	C391403	ND	9.2	1.0	C391403
Total Lead (Pb)	ug/L	ND	0.0050	C391403	ND	0.0050	C391403	ND	ND	0.0050	C391403
Total Lithium (Li)	ug/L	ND	0.50	C391403	ND	0.50	C391403	ND	7.30	0.50	C391403
Total Manganese (Mn)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	25.2	0.050	C391403
Total Molybdenum (Mo)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	48.3	0.050	C391403
Total Nickel (Ni)	ug/L	ND	0.020	C391403	ND	0.020	C391403	ND	0.173	0.020	C391403
Total Phosphorus (P)	ug/L	ND	2.0	C391403	ND	2.0	C391403	ND	2.0	2.0	C391403
RDL = Reportable Detection Limit											
Lab-Dup = Laboratory Initiated Duplicate											
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.											



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

ELEMENTS BY ATOMIC SPECTROSCOPY (WATER)

Bureau Veritas ID		ELM804			ELM804			ELM805	ELM806		
Sampling Date		2026/08/25			2026/08/25			2026/08/25	2026/08/25		
COC Number		139719			139719			139719	139719		
	UNITS	Field Blank	RDL	QC Batch	Field Blank Lab-Dup	RDL	QC Batch	Trip Blank	DUP	RDL	QC Batch
Total Rubidium (Rb)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	3.83	0.050	C391403
Total Selenium (Se)	ug/L	ND	0.040	C391403	ND	0.040	C391403	ND	0.043	0.040	C391403
Total Silicon (Si)	ug/L	ND	50	C391403	ND	50	C391403	ND	6610	50	C391403
Total Silver (Ag)	ug/L	ND	0.0050	C391403	ND	0.0050	C391403	ND	ND	0.0050	C391403
Total Strontium (Sr)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	51.9	0.050	C391403
Total Tellurium (Te)	ug/L	ND	0.020	C391403	ND	0.020	C391403	ND	ND	0.020	C391403
Total Thallium (Tl)	ug/L	ND	0.0020	C391403	ND	0.0020	C391403	ND	0.0086	0.0020	C391403
Total Thorium (Th)	ug/L	ND	0.050	C391403	ND	0.050	C391403	ND	ND	0.050	C391403
Total Tin (Sn)	ug/L	ND	0.20	C391403	ND	0.20	C391403	ND	ND	0.20	C391403
Total Titanium (Ti)	ug/L	ND	0.50	C391403	ND	0.50	C391403	ND	ND	0.50	C391403
Total Uranium (U)	ug/L	ND	0.0020	C391403	ND	0.0020	C391403	ND	0.266	0.0020	C391403
Total Vanadium (V)	ug/L	ND	0.20	C391403	ND	0.20	C391403	ND	ND	0.20	C391403
Total Zinc (Zn)	ug/L	ND	0.10	C391403	ND	0.10	C391403	ND	2.77	0.10	C391403
Total Zirconium (Zr)	ug/L	ND	0.10	C391403	ND	0.10	C391403	ND	ND	0.10	C391403
Total Calcium (Ca)	mg/L	ND	0.050	C389307				ND	25.1	0.050	C389307
Total Magnesium (Mg)	mg/L	ND	0.050	C389307				ND	1.37	0.050	C389307
Total Potassium (K)	mg/L	ND	0.050	C389307				ND	1.74	0.050	C389307
Total Sodium (Na)	mg/L	ND	0.050	C389307				ND	8.92	0.050	C389307
Total Sulphur (S)	mg/L	ND	3.0	C389307				ND	5.0	3.0	C389307

RDL = Reportable Detection Limit

Lab-Dup = Laboratory Initiated Duplicate

ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

MISCELLANEOUS (WATER)

Bureau Veritas ID		ELM801	ELM802	ELM803	ELM806		
Sampling Date		2026/08/25	2026/08/25	2026/08/25	2026/08/25		
COC Number		139719	139719	139719	139719		
	UNITS	WLNG-DS	WLNG -EOP	WLNG-US	DUP	RDL	QC Batch
Calculated Parameters							
Total Un-ionized Hydrogen Sulfide as S	mg/L	ND	ND	ND	ND	0.0018	C389844
Total Un-ionized Hydrogen Sulfide as H2S	mg/L	ND	ND	ND	ND	0.0019	C389844
RDL = Reportable Detection Limit							
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.							

**LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)**

Bureau Veritas ID		ELM802	ELM806		
Sampling Date		2026/08/25	2026/08/25		
COC Number		139719	139719		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Calculated Parameters					
Low Molecular Weight PAH's	ug/L	ND	ND	0.10	C389316
High Molecular Weight PAH's	ug/L	ND	ND	0.050	C389316
Total PAH	ug/L	ND	ND	0.10	C389316
Polycyclic Aromatics					
Quinoline	ug/L	ND	ND	0.020	C391315
Naphthalene	ug/L	ND	ND	0.10	C391315
1-Methylnaphthalene	ug/L	ND	ND	0.050	C391315
2-Methylnaphthalene	ug/L	ND	ND	0.10	C391315
Acenaphthylene	ug/L	ND	ND	0.050	C391315
Acenaphthene	ug/L	ND	ND	0.050	C391315
Fluorene	ug/L	ND	ND	0.050	C391315
Phenanthrene	ug/L	ND	ND	0.050	C391315
Anthracene	ug/L	ND	ND	0.010	C391315
Acridine	ug/L	ND	ND	0.050	C391315
Fluoranthene	ug/L	ND	ND	0.020	C391315
Pyrene	ug/L	ND	ND	0.020	C391315
Benzo(a)anthracene	ug/L	ND	ND	0.010	C391315
Chrysene	ug/L	ND	ND	0.020	C391315
Benzo(b&j)fluoranthene	ug/L	ND	ND	0.030	C391315
Benzo(k)fluoranthene	ug/L	ND	ND	0.050	C391315
Benzo(a)pyrene	ug/L	ND	ND	0.0050	C391315
Indeno(1,2,3-cd)pyrene	ug/L	ND	ND	0.050	C391315
Dibenz(a,h)anthracene	ug/L	ND	0.0049 (1)	0.0030	C391315
Benzo(g,h,i)perylene	ug/L	ND	ND	0.050	C391315
Calculated Parameters					
LEPH (C10-C19 less PAH)	mg/L	ND	ND	0.20	C389330
HEPH (C19-C32 less PAH)	mg/L	ND	ND	0.20	C389330
Ext. Pet. Hydrocarbon					
EPH (C10-C19)	mg/L	ND	ND	0.20	C391320
RDL = Reportable Detection Limit					
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					
(1) Tentatively identified result and may be potentially biased high due to matrix interference.					



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

LEPH & HEPH WITH CSR/CCME PAH IN WATER (WATER)

Bureau Veritas ID		ELM802	ELM806		
Sampling Date		2026/08/25	2026/08/25		
COC Number		139719	139719		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
EPH (C19-C32)	mg/L	ND	ND	0.20	C391320
Surrogate Recovery (%)					
O-TERPHENYL (sur.)	%	113	111		C391320
D10-ANTHRACENE (sur.)	%	103	104		C391315
D8-ACENAPHTHYLENE (sur.)	%	102	101		C391315
D8-NAPHTHALENE (sur.)	%	85	83		C391315
TERPHENYL-D14 (sur.)	%	92	90		C391315
RDL = Reportable Detection Limit					
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		ELM802	ELM806		
Sampling Date		2026/08/25	2026/08/25		
COC Number		139719	139719		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Calculated Parameters					
VPH (VH6 to 10 - BTEX)	ug/L	ND	ND	300	C389008
Volatiles					
VH C6-C10	ug/L	ND	ND	300	C391711
1,1,1,2-tetrachloroethane	ug/L	ND	ND	0.50	C391711
1,1,1-trichloroethane	ug/L	ND	ND	0.50	C391711
1,1,2,2-tetrachloroethane	ug/L	ND	ND	0.50	C391711
1,1,2Trichloro-1,2,2Trifluoroethane	ug/L	ND	ND	2.0	C391711
1,1,2-trichloroethane	ug/L	ND	ND	0.50	C391711
1,1-dichloroethane	ug/L	ND	ND	0.50	C391711
1,1-dichloroethene	ug/L	ND	ND	0.50	C391711
1,2,3-trichlorobenzene	ug/L	ND	ND	2.0	C391711
1,2,4-trichlorobenzene	ug/L	ND	ND	2.0	C391711
1,2-dibromoethane	ug/L	ND	ND	0.20	C391711
1,2-dichlorobenzene	ug/L	ND	ND	0.50	C391711
1,2-dichloroethane	ug/L	ND	ND	0.50	C391711
1,2-dichloropropane	ug/L	ND	ND	0.50	C391711
1,3,5-trimethylbenzene	ug/L	ND	ND	2.0	C391711
1,3-Butadiene	ug/L	ND	ND	0.50	C391711
1,3-dichlorobenzene	ug/L	ND	ND	0.50	C391711
1,3-dichloropropane	ug/L	ND	ND	1.0	C391711
1,4-dichlorobenzene	ug/L	ND	ND	0.50	C391711
Benzene	ug/L	ND	ND	0.40	C391711
Bromobenzene	ug/L	ND	ND	2.0	C391711
Bromodichloromethane	ug/L	ND	ND	1.0	C391711
Bromoform	ug/L	ND	ND	1.0	C391711
Bromomethane	ug/L	ND	ND	1.0	C391711
Carbon tetrachloride	ug/L	ND	ND	0.50	C391711
Chlorobenzene	ug/L	ND	ND	0.50	C391711
Dibromochloromethane	ug/L	ND	ND	1.0	C391711
Chloroethane	ug/L	ND	ND	1.0	C391711
Chloroform	ug/L	ND	ND	1.0	C391711
RDL = Reportable Detection Limit					
ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

CSR VOC + VPH IN WATER (WATER)

Bureau Veritas ID		ELM802	ELM806		
Sampling Date		2026/08/25	2026/08/25		
COC Number		139719	139719		
	UNITS	WLNG -EOP	DUP	RDL	QC Batch
Chloromethane	ug/L	ND	ND	1.0	C391711
cis-1,2-dichloroethene	ug/L	ND	ND	1.0	C391711
cis-1,3-dichloropropene	ug/L	ND	ND	1.0	C391711
Dichlorodifluoromethane	ug/L	ND	ND	2.0	C391711
Dichloromethane	ug/L	ND	ND	2.0	C391711
Ethylbenzene	ug/L	ND	ND	0.40	C391711
Hexachlorobutadiene	ug/L	ND	ND	0.50	C391711
Isopropylbenzene	ug/L	ND	ND	2.0	C391711
Methyl-tert-butylether (MTBE)	ug/L	ND	ND	4.0	C391711
Styrene	ug/L	ND	ND	0.50	C391711
Tetrachloroethene	ug/L	ND	ND	0.50	C391711
Toluene	ug/L	ND	ND	0.40	C391711
trans-1,2-dichloroethene	ug/L	ND	ND	1.0	C391711
trans-1,3-dichloropropene	ug/L	ND	ND	1.0	C391711
Trichloroethene	ug/L	ND	ND	0.50	C391711
Trichlorofluoromethane	ug/L	ND	ND	4.0	C391711
Vinyl chloride	ug/L	ND	ND	0.50	C391711
m & p-Xylene	ug/L	ND	ND	0.40	C391711
o-Xylene	ug/L	ND	ND	0.40	C391711
Xylenes (Total)	ug/L	ND	ND	0.40	C391711
Surrogate Recovery (%)					
1,4-Difluorobenzene (sur.)	%	104	101		C391711
4-Bromofluorobenzene (sur.)	%	66	67		C391711
D4-1,2-Dichloroethane (sur.)	%	105	107		C391711
RDL = Reportable Detection Limit ND = Not Detected at a concentration equal or greater than the indicated Detection Limit.					



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

GENERAL COMMENTS

Results relate only to the items tested.



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C390334	BTM	Matrix Spike	Dissolved Fluoride (F)	2026/08/26		NC	%	80 - 120
C390334	BTM	Spiked Blank	Dissolved Fluoride (F)	2026/08/26		100	%	80 - 120
C390334	BTM	Method Blank	Dissolved Fluoride (F)	2026/08/26	ND, RDL=0.050		mg/L	
C390334	BTM	RPD [ELM803-02]	Fluoride (F)	2026/08/26	NC		%	20
C390373	JGL	Matrix Spike [ELM804-12]	Total Hex. Chromium (Cr 6+)	2026/08/26		99	%	80 - 120
C390373	JGL	Spiked Blank	Total Hex. Chromium (Cr 6+)	2026/08/26		112	%	80 - 120
C390373	JGL	Method Blank	Total Hex. Chromium (Cr 6+)	2026/08/26	ND, RDL=0.00099		mg/L	
C390373	JGL	RPD [ELM804-12]	Total Hex. Chromium (Cr 6+)	2026/08/26	NC		%	20
C390388	JAV	Matrix Spike	Chloride (Cl)	2026/08/26		114	%	80 - 120
			Sulphate (SO4)	2026/08/26		NC	%	80 - 120
C390388	JAV	Spiked Blank	Chloride (Cl)	2026/08/26		101	%	80 - 120
			Sulphate (SO4)	2026/08/26		96	%	80 - 120
C390388	JAV	Method Blank	Chloride (Cl)	2026/08/26	ND, RDL=1.0		mg/L	
			Sulphate (SO4)	2026/08/26	ND, RDL=1.0		mg/L	
C390388	JAV	RPD	Sulphate (SO4)	2026/08/26	3.1		%	20
C390403	RLZ	Matrix Spike	Nitrate plus Nitrite (N)	2026/08/26		111	%	80 - 120
C390403	RLZ	Spiked Blank	Nitrate plus Nitrite (N)	2026/08/26		105	%	80 - 120
C390403	RLZ	Method Blank	Nitrate plus Nitrite (N)	2026/08/26	ND, RDL=0.020		mg/L	
C390406	RLZ	Matrix Spike	Nitrite (N)	2026/08/26		108	%	80 - 120
C390406	RLZ	Spiked Blank	Nitrite (N)	2026/08/26		102	%	80 - 120
C390406	RLZ	Method Blank	Nitrite (N)	2026/08/26	ND, RDL=0.0050		mg/L	
C390447	SPP	Matrix Spike [ELM806-03]	Total Dissolved Solids	2026/08/27		97	%	80 - 120
C390447	SPP	Spiked Blank	Total Dissolved Solids	2026/08/27		102	%	80 - 120
C390447	SPP	Method Blank	Total Dissolved Solids	2026/08/27	ND, RDL=10		mg/L	
C390447	SPP	RPD [ELM805-03]	Total Dissolved Solids	2026/08/27	NC		%	20
C390523	BB3	Matrix Spike [ELM806-10]	Total Ammonia (N)	2026/08/26		103	%	80 - 120
C390523	BB3	Spiked Blank	Total Ammonia (N)	2026/08/26		103	%	80 - 120
C390523	BB3	Method Blank	Total Ammonia (N)	2026/08/26	ND, RDL=0.015		mg/L	
C390523	BB3	RPD [ELM806-10]	Total Ammonia (N)	2026/08/26	NC		%	20
C390608	SPP	Matrix Spike [ELM806-01]	Total Suspended Solids	2026/08/27		106	%	80 - 120
C390608	SPP	Spiked Blank	Total Suspended Solids	2026/08/27		101	%	80 - 120
C390608	SPP	Method Blank	Total Suspended Solids	2026/08/27	ND, RDL=1.0		mg/L	
C390608	SPP	RPD [ELM805-01]	Total Suspended Solids	2026/08/27	NC		%	20
C390732	BTM	Spiked Blank	Alkalinity (Total as CaCO3)	2026/08/27		99	%	80 - 120
C390732	BTM	Method Blank	Alkalinity (PP as CaCO3)	2026/08/27	ND, RDL=1.0		mg/L	
			Alkalinity (Total as CaCO3)	2026/08/27	ND, RDL=1.0		mg/L	
			Bicarbonate (HCO3)	2026/08/27	ND, RDL=1.0		mg/L	
			Carbonate (CO3)	2026/08/27	ND, RDL=1.0		mg/L	
			Hydroxide (OH)	2026/08/27	ND, RDL=1.0		mg/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C390732	BTM	RPD [ELM806-02]	Alkalinity (PP as CaCO3)	2026/08/27	NC		%	20
			Alkalinity (Total as CaCO3)	2026/08/27	0.23		%	20
			Bicarbonate (HCO3)	2026/08/27	0.23		%	20
			Carbonate (CO3)	2026/08/27	NC		%	20
			Hydroxide (OH)	2026/08/27	NC		%	20
C390734	BTM	Spiked Blank	pH	2026/08/27		100	%	97 - 103
C390734	BTM	RPD [ELM806-02]	pH	2026/08/27	1.8		%	N/A
C391177	AA1	Matrix Spike	Total Aluminum (Al)	2026/08/27		102	%	80 - 120
			Total Antimony (Sb)	2026/08/27		101	%	80 - 120
			Total Arsenic (As)	2026/08/27		104	%	80 - 120
			Total Barium (Ba)	2026/08/27		99	%	80 - 120
			Total Beryllium (Be)	2026/08/27		98	%	80 - 120
			Total Bismuth (Bi)	2026/08/27		100	%	80 - 120
			Total Boron (B)	2026/08/27		98	%	80 - 120
			Total Cadmium (Cd)	2026/08/27		102	%	80 - 120
			Total Cesium (Cs)	2026/08/27		100	%	80 - 120
			Total Chromium (Cr)	2026/08/27		97	%	80 - 120
			Total Cobalt (Co)	2026/08/27		99	%	80 - 120
			Total Copper (Cu)	2026/08/27		98	%	80 - 120
			Total Iron (Fe)	2026/08/27		104	%	80 - 120
			Total Lead (Pb)	2026/08/27		98	%	80 - 120
			Total Lithium (Li)	2026/08/27		97	%	80 - 120
			Total Manganese (Mn)	2026/08/27		100	%	80 - 120
			Total Molybdenum (Mo)	2026/08/27		105	%	80 - 120
			Total Nickel (Ni)	2026/08/27		97	%	80 - 120
			Total Phosphorus (P)	2026/08/27		102	%	80 - 120
			Total Rubidium (Rb)	2026/08/27		102	%	80 - 120
			Total Selenium (Se)	2026/08/27		102	%	80 - 120
			Total Silicon (Si)	2026/08/27		106	%	80 - 120
			Total Silver (Ag)	2026/08/27		101	%	80 - 120
			Total Strontium (Sr)	2026/08/27		101	%	80 - 120
			Total Tellurium (Te)	2026/08/27		105	%	80 - 120
			Total Thallium (Tl)	2026/08/27		101	%	80 - 120
			Total Thorium (Th)	2026/08/27		104	%	80 - 120
			Total Tin (Sn)	2026/08/27		99	%	80 - 120
			Total Titanium (Ti)	2026/08/27		99	%	80 - 120
			Total Uranium (U)	2026/08/27		88	%	80 - 120
			Total Vanadium (V)	2026/08/27		100	%	80 - 120
			Total Zinc (Zn)	2026/08/27		100	%	80 - 120
			Total Zirconium (Zr)	2026/08/27		102	%	80 - 120
C391177	AA1	Spiked Blank	Total Aluminum (Al)	2026/08/27		103	%	80 - 120
			Total Antimony (Sb)	2026/08/27		102	%	80 - 120
			Total Arsenic (As)	2026/08/27		104	%	80 - 120
			Total Barium (Ba)	2026/08/27		102	%	80 - 120
			Total Beryllium (Be)	2026/08/27		100	%	80 - 120
			Total Bismuth (Bi)	2026/08/27		102	%	80 - 120
			Total Boron (B)	2026/08/27		101	%	80 - 120
			Total Cadmium (Cd)	2026/08/27		102	%	80 - 120
			Total Cesium (Cs)	2026/08/27		104	%	80 - 120
			Total Chromium (Cr)	2026/08/27		101	%	80 - 120
			Total Cobalt (Co)	2026/08/27		100	%	80 - 120
			Total Copper (Cu)	2026/08/27		98	%	80 - 120
			Total Iron (Fe)	2026/08/27		105	%	80 - 120



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C391177	AA1	Method Blank	Total Lead (Pb)	2026/08/27		99	%	80 - 120
			Total Lithium (Li)	2026/08/27		97	%	80 - 120
			Total Manganese (Mn)	2026/08/27		101	%	80 - 120
			Total Molybdenum (Mo)	2026/08/27		107	%	80 - 120
			Total Nickel (Ni)	2026/08/27		99	%	80 - 120
			Total Phosphorus (P)	2026/08/27		102	%	80 - 120
			Total Rubidium (Rb)	2026/08/27		102	%	80 - 120
			Total Selenium (Se)	2026/08/27		101	%	80 - 120
			Total Silicon (Si)	2026/08/27		109	%	80 - 120
			Total Silver (Ag)	2026/08/27		101	%	80 - 120
			Total Strontium (Sr)	2026/08/27		104	%	80 - 120
			Total Tellurium (Te)	2026/08/27		103	%	80 - 120
			Total Thallium (Tl)	2026/08/27		101	%	80 - 120
			Total Thorium (Th)	2026/08/27		106	%	80 - 120
			Total Tin (Sn)	2026/08/27		104	%	80 - 120
			Total Titanium (Ti)	2026/08/27		101	%	80 - 120
			Total Uranium (U)	2026/08/27		89	%	80 - 120
			Total Vanadium (V)	2026/08/27		100	%	80 - 120
			Total Zinc (Zn)	2026/08/27		100	%	80 - 120
			Total Zirconium (Zr)	2026/08/27		102	%	80 - 120
			Total Aluminum (Al)	2026/08/27	ND, RDL=3.0		ug/L	
			Total Antimony (Sb)	2026/08/27	ND, RDL=0.020		ug/L	
			Total Arsenic (As)	2026/08/27	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/08/27	ND, RDL=0.050		ug/L	
			Total Beryllium (Be)	2026/08/27	ND, RDL=0.010		ug/L	
			Total Bismuth (Bi)	2026/08/27	ND, RDL=0.010		ug/L	
			Total Boron (B)	2026/08/27	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/08/27	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/08/27	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/08/27	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/08/27	ND, RDL=0.010		ug/L	
			Total Copper (Cu)	2026/08/27	ND, RDL=0.10		ug/L	
			Total Iron (Fe)	2026/08/27	ND, RDL=5.0		ug/L	
			Total Lead (Pb)	2026/08/27	ND, RDL=0.020		ug/L	
			Total Lithium (Li)	2026/08/27	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/08/27	ND, RDL=0.10		ug/L	
			Total Molybdenum (Mo)	2026/08/27	ND, RDL=0.050		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C391177	AA1	RPD	Total Nickel (Ni)	2026/08/27	ND, RDL=0.10		ug/L	
			Total Phosphorus (P)	2026/08/27	ND, RDL=5.0		ug/L	
			Total Rubidium (Rb)	2026/08/27	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/08/27	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/08/27	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/08/27	ND, RDL=0.010		ug/L	
			Total Strontium (Sr)	2026/08/27	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/08/27	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/08/27	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/08/27	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/08/27	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/08/27	ND, RDL=2.0		ug/L	
			Total Uranium (U)	2026/08/27	ND, RDL=0.0050		ug/L	
			Total Vanadium (V)	2026/08/27	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/08/27	ND, RDL=1.0		ug/L	
			Total Zirconium (Zr)	2026/08/27	ND, RDL=0.10		ug/L	
			Total Aluminum (Al)	2026/08/27	4.9		%	20
			Total Antimony (Sb)	2026/08/27	12		%	20
			Total Arsenic (As)	2026/08/27	2.7		%	20
			Total Barium (Ba)	2026/08/27	0.65		%	20
			Total Beryllium (Be)	2026/08/27	NC		%	20
			Total Bismuth (Bi)	2026/08/27	NC		%	20
			Total Boron (B)	2026/08/27	NC		%	20
			Total Cadmium (Cd)	2026/08/27	NC		%	20
			Total Chromium (Cr)	2026/08/27	4.6		%	20
			Total Cobalt (Co)	2026/08/27	1.2		%	20
			Total Copper (Cu)	2026/08/27	4.1		%	20
			Total Iron (Fe)	2026/08/27	0.74		%	20
			Total Lead (Pb)	2026/08/27	0.14		%	20
			Total Lithium (Li)	2026/08/27	NC		%	20
			Total Manganese (Mn)	2026/08/27	0.65		%	20
			Total Molybdenum (Mo)	2026/08/27	6.1		%	20
			Total Nickel (Ni)	2026/08/27	0.58		%	20
			Total Phosphorus (P)	2026/08/27	7.1		%	20
			Total Selenium (Se)	2026/08/27	NC		%	20
			Total Silicon (Si)	2026/08/27	1.4		%	20
			Total Silver (Ag)	2026/08/27	NC		%	20
			Total Strontium (Sr)	2026/08/27	1.0		%	20



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C391315	JST	Spiked Blank	Total Thallium (Tl)	2026/08/27	NC		%	20
			Total Tin (Sn)	2026/08/27	NC		%	20
			Total Titanium (Ti)	2026/08/27	NC		%	20
			Total Uranium (U)	2026/08/27	NC		%	20
			Total Vanadium (V)	2026/08/27	NC		%	20
			Total Zinc (Zn)	2026/08/27	5.1		%	20
			Total Zirconium (Zr)	2026/08/27	NC		%	20
			D10-ANTHRACENE (sur.)	2026/08/27		101	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/08/27		100	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/08/27		91	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/08/27		90	%	50 - 140
			Quinoline	2026/08/27		93	%	50 - 140
			Naphthalene	2026/08/27		84	%	50 - 140
			1-Methylnaphthalene	2026/08/27		84	%	50 - 140
			2-Methylnaphthalene	2026/08/27		86	%	50 - 140
			Acenaphthylene	2026/08/27		85	%	50 - 140
			Acenaphthene	2026/08/27		86	%	50 - 140
			Fluorene	2026/08/27		84	%	50 - 140
			Phenanthrene	2026/08/27		84	%	50 - 140
			Anthracene	2026/08/27		89	%	50 - 140
			Acridine	2026/08/27		89	%	50 - 140
			Fluoranthene	2026/08/27		69	%	50 - 140
			Pyrene	2026/08/27		68	%	50 - 140
			Benzo(a)anthracene	2026/08/27		92	%	50 - 140
			Chrysene	2026/08/27		96	%	50 - 140
			Benzo(b&j)fluoranthene	2026/08/27		94	%	50 - 140
			Benzo(k)fluoranthene	2026/08/27		104	%	50 - 140
			Benzo(a)pyrene	2026/08/27		87	%	50 - 140
			Indeno(1,2,3-cd)pyrene	2026/08/27		96	%	50 - 140
			Dibenz(a,h)anthracene	2026/08/27		95	%	50 - 140
			Benzo(g,h,i)perylene	2026/08/27		98	%	50 - 140
C391315	JST	Method Blank	D10-ANTHRACENE (sur.)	2026/08/27		101	%	50 - 140
			D8-ACENAPHTHYLENE (sur.)	2026/08/27		97	%	50 - 140
			D8-NAPHTHALENE (sur.)	2026/08/27		85	%	50 - 140
			TERPHENYL-D14 (sur.)	2026/08/27		91	%	50 - 140
			Quinoline	2026/08/27	ND, RDL=0.020		ug/L	
			Naphthalene	2026/08/27	ND, RDL=0.10		ug/L	
			1-Methylnaphthalene	2026/08/27	ND, RDL=0.050		ug/L	
			2-Methylnaphthalene	2026/08/27	ND, RDL=0.10		ug/L	
			Acenaphthylene	2026/08/27	ND, RDL=0.050		ug/L	
			Acenaphthene	2026/08/27	ND, RDL=0.050		ug/L	
			Fluorene	2026/08/27	ND, RDL=0.050		ug/L	
			Phenanthrene	2026/08/27	ND, RDL=0.050		ug/L	
			Anthracene	2026/08/27	ND, RDL=0.010		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Acridine	2026/08/27	ND, RDL=0.050		ug/L	
			Fluoranthene	2026/08/27	ND, RDL=0.020		ug/L	
			Pyrene	2026/08/27	ND, RDL=0.020		ug/L	
			Benzo(a)anthracene	2026/08/27	ND, RDL=0.010		ug/L	
			Chrysene	2026/08/27	ND, RDL=0.020		ug/L	
			Benzo(b&j)fluoranthene	2026/08/27	ND, RDL=0.030		ug/L	
			Benzo(k)fluoranthene	2026/08/27	ND, RDL=0.050		ug/L	
			Benzo(a)pyrene	2026/08/27	ND, RDL=0.0050		ug/L	
			Indeno(1,2,3-cd)pyrene	2026/08/27	ND, RDL=0.050		ug/L	
			Dibenz(a,h)anthracene	2026/08/27	ND, RDL=0.0030		ug/L	
			Benzo(g,h,i)perylene	2026/08/27	ND, RDL=0.050		ug/L	
C391320	RYA	Spiked Blank	O-TERPHENYL (sur.)	2026/08/27		113	%	60 - 140
			EPH (C10-C19)	2026/08/27		88	%	70 - 130
			EPH (C19-C32)	2026/08/27		98	%	70 - 130
C391320	RYA	Method Blank	O-TERPHENYL (sur.)	2026/08/27		108	%	60 - 140
			EPH (C10-C19)	2026/08/27	ND, RDL=0.20		mg/L	
			EPH (C19-C32)	2026/08/27	ND, RDL=0.20		mg/L	
C391403	AA1	Matrix Spike [ELM804-05]	Total Aluminum (Al)	2026/08/28		95	%	80 - 120
			Total Antimony (Sb)	2026/08/28		101	%	80 - 120
			Total Arsenic (As)	2026/08/28		97	%	80 - 120
			Total Barium (Ba)	2026/08/28		94	%	80 - 120
			Total Beryllium (Be)	2026/08/28		86	%	80 - 120
			Total Bismuth (Bi)	2026/08/28		95	%	80 - 120
			Total Boron (B)	2026/08/28		90	%	80 - 120
			Total Cadmium (Cd)	2026/08/28		98	%	80 - 120
			Total Cesium (Cs)	2026/08/28		95	%	80 - 120
			Total Chromium (Cr)	2026/08/28		96	%	80 - 120
			Total Cobalt (Co)	2026/08/28		95	%	80 - 120
			Total Copper (Cu)	2026/08/28		94	%	80 - 120
			Total Iron (Fe)	2026/08/28		98	%	80 - 120
			Total Lead (Pb)	2026/08/28		91	%	80 - 120
			Total Lithium (Li)	2026/08/28		90	%	80 - 120
			Total Manganese (Mn)	2026/08/28		95	%	80 - 120
			Total Molybdenum (Mo)	2026/08/28		101	%	80 - 120
			Total Nickel (Ni)	2026/08/28		94	%	80 - 120
			Total Phosphorus (P)	2026/08/28		97	%	80 - 120
			Total Rubidium (Rb)	2026/08/28		94	%	80 - 120
			Total Selenium (Se)	2026/08/28		93	%	80 - 120
			Total Silicon (Si)	2026/08/28		101	%	80 - 120
			Total Silver (Ag)	2026/08/28		97	%	80 - 120



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C391403	AA1	Spiked Blank	Total Strontium (Sr)	2026/08/28		94	%	80 - 120
			Total Tellurium (Te)	2026/08/28		101	%	80 - 120
			Total Thallium (Tl)	2026/08/28		96	%	80 - 120
			Total Thorium (Th)	2026/08/28		101	%	80 - 120
			Total Tin (Sn)	2026/08/28		103	%	80 - 120
			Total Titanium (Ti)	2026/08/28		97	%	80 - 120
			Total Uranium (U)	2026/08/28		85	%	80 - 120
			Total Vanadium (V)	2026/08/28		96	%	80 - 120
			Total Zinc (Zn)	2026/08/28		98	%	80 - 120
			Total Zirconium (Zr)	2026/08/28		99	%	80 - 120
			Total Aluminum (Al)	2026/08/28		102	%	80 - 120
			Total Antimony (Sb)	2026/08/28		106	%	80 - 120
			Total Arsenic (As)	2026/08/28		105	%	80 - 120
			Total Barium (Ba)	2026/08/28		103	%	80 - 120
			Total Beryllium (Be)	2026/08/28		93	%	80 - 120
			Total Bismuth (Bi)	2026/08/28		102	%	80 - 120
			Total Boron (B)	2026/08/28		96	%	80 - 120
			Total Cadmium (Cd)	2026/08/28		105	%	80 - 120
			Total Cesium (Cs)	2026/08/28		105	%	80 - 120
			Total Chromium (Cr)	2026/08/28		102	%	80 - 120
			Total Cobalt (Co)	2026/08/28		101	%	80 - 120
			Total Copper (Cu)	2026/08/28		100	%	80 - 120
			Total Iron (Fe)	2026/08/28		107	%	80 - 120
			Total Lead (Pb)	2026/08/28		99	%	80 - 120
			Total Lithium (Li)	2026/08/28		96	%	80 - 120
			Total Manganese (Mn)	2026/08/28		101	%	80 - 120
			Total Molybdenum (Mo)	2026/08/28		106	%	80 - 120
			Total Nickel (Ni)	2026/08/28		100	%	80 - 120
			Total Phosphorus (P)	2026/08/28		104	%	80 - 120
			Total Rubidium (Rb)	2026/08/28		103	%	80 - 120
			Total Selenium (Se)	2026/08/28		103	%	80 - 120
			Total Silicon (Si)	2026/08/28		112	%	80 - 120
			Total Silver (Ag)	2026/08/28		104	%	80 - 120
			Total Strontium (Sr)	2026/08/28		103	%	80 - 120
			Total Tellurium (Te)	2026/08/28		108	%	80 - 120
			Total Thallium (Tl)	2026/08/28		104	%	80 - 120
			Total Thorium (Th)	2026/08/28		106	%	80 - 120
			Total Tin (Sn)	2026/08/28		106	%	80 - 120
			Total Titanium (Ti)	2026/08/28		102	%	80 - 120
			Total Uranium (U)	2026/08/28		90	%	80 - 120
			Total Vanadium (V)	2026/08/28		101	%	80 - 120
			Total Zinc (Zn)	2026/08/28		103	%	80 - 120
			Total Zirconium (Zr)	2026/08/28		104	%	80 - 120
C391403	AA1	Method Blank	Total Aluminum (Al)	2026/08/28	ND, RDL=0.50		ug/L	
			Total Antimony (Sb)	2026/08/28	ND, RDL=0.020		ug/L	
			Total Arsenic (As)	2026/08/28	ND, RDL=0.020		ug/L	
			Total Barium (Ba)	2026/08/28	ND, RDL=0.020		ug/L	
			Total Beryllium (Be)	2026/08/28	ND, RDL=0.010		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Bismuth (Bi)	2026/08/28	ND, RDL=0.0050		ug/L	
			Total Boron (B)	2026/08/28	ND, RDL=10		ug/L	
			Total Cadmium (Cd)	2026/08/28	ND, RDL=0.0050		ug/L	
			Total Cesium (Cs)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Chromium (Cr)	2026/08/28	ND, RDL=0.10		ug/L	
			Total Cobalt (Co)	2026/08/28	ND, RDL=0.0050		ug/L	
			Total Copper (Cu)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Iron (Fe)	2026/08/28	ND, RDL=1.0		ug/L	
			Total Lead (Pb)	2026/08/28	ND, RDL=0.0050		ug/L	
			Total Lithium (Li)	2026/08/28	ND, RDL=0.50		ug/L	
			Total Manganese (Mn)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Molybdenum (Mo)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Nickel (Ni)	2026/08/28	ND, RDL=0.020		ug/L	
			Total Phosphorus (P)	2026/08/28	ND, RDL=2.0		ug/L	
			Total Rubidium (Rb)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Selenium (Se)	2026/08/28	ND, RDL=0.040		ug/L	
			Total Silicon (Si)	2026/08/28	ND, RDL=50		ug/L	
			Total Silver (Ag)	2026/08/28	ND, RDL=0.0050		ug/L	
			Total Strontium (Sr)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Tellurium (Te)	2026/08/28	ND, RDL=0.020		ug/L	
			Total Thallium (Tl)	2026/08/28	ND, RDL=0.0020		ug/L	
			Total Thorium (Th)	2026/08/28	ND, RDL=0.050		ug/L	
			Total Tin (Sn)	2026/08/28	ND, RDL=0.20		ug/L	
			Total Titanium (Ti)	2026/08/28	ND, RDL=0.50		ug/L	
			Total Uranium (U)	2026/08/28	ND, RDL=0.0020		ug/L	
			Total Vanadium (V)	2026/08/28	ND, RDL=0.20		ug/L	
			Total Zinc (Zn)	2026/08/28	ND, RDL=0.10		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Total Zirconium (Zr)	2026/08/28	ND, RDL=0.10		ug/L	
C391403	AA1	RPD [ELM804-05]	Total Aluminum (Al)	2026/08/28	NC		%	20
			Total Antimony (Sb)	2026/08/28	NC		%	20
			Total Arsenic (As)	2026/08/28	NC		%	20
			Total Barium (Ba)	2026/08/28	NC		%	20
			Total Beryllium (Be)	2026/08/28	NC		%	20
			Total Bismuth (Bi)	2026/08/28	NC		%	20
			Total Boron (B)	2026/08/28	NC		%	20
			Total Cadmium (Cd)	2026/08/28	NC		%	20
			Total Cesium (Cs)	2026/08/28	NC		%	20
			Total Chromium (Cr)	2026/08/28	NC		%	20
			Total Cobalt (Co)	2026/08/28	NC		%	20
			Total Copper (Cu)	2026/08/28	NC		%	20
			Total Iron (Fe)	2026/08/28	NC		%	20
			Total Lead (Pb)	2026/08/28	NC		%	20
			Total Lithium (Li)	2026/08/28	NC		%	20
			Total Manganese (Mn)	2026/08/28	NC		%	20
			Total Molybdenum (Mo)	2026/08/28	NC		%	20
			Total Nickel (Ni)	2026/08/28	NC		%	20
			Total Phosphorus (P)	2026/08/28	NC		%	20
			Total Rubidium (Rb)	2026/08/28	NC		%	20
			Total Selenium (Se)	2026/08/28	NC		%	20
			Total Silicon (Si)	2026/08/28	NC		%	20
			Total Silver (Ag)	2026/08/28	NC		%	20
			Total Strontium (Sr)	2026/08/28	NC		%	20
			Total Tellurium (Te)	2026/08/28	NC		%	20
			Total Thallium (Tl)	2026/08/28	NC		%	20
			Total Thorium (Th)	2026/08/28	NC		%	20
			Total Tin (Sn)	2026/08/28	NC		%	20
			Total Titanium (Ti)	2026/08/28	NC		%	20
			Total Uranium (U)	2026/08/28	NC		%	20
			Total Vanadium (V)	2026/08/28	NC		%	20
			Total Zinc (Zn)	2026/08/28	NC		%	20
			Total Zirconium (Zr)	2026/08/28	NC		%	20
C391476	LRT	Matrix Spike	Bromide (Br)	2026/08/27		91	%	78 - 120
C391476	LRT	Spiked Blank	Bromide (Br)	2026/08/27		102	%	80 - 120
C391476	LRT	Method Blank	Bromide (Br)	2026/08/27	ND, RDL=0.010		mg/L	
C391476	LRT	RPD	Bromide (Br)	2026/08/27	7.6		%	20
C391569	BB3	Matrix Spike [ELM804-09]	Total Nitrogen (N)	2026/08/28		113	%	80 - 120
C391569	BB3	Spiked Blank	Total Nitrogen (N)	2026/08/28		101	%	80 - 120
C391569	BB3	Method Blank	Total Nitrogen (N)	2026/08/28	ND, RDL=0.020		mg/L	
C391569	BB3	RPD [ELM804-09]	Total Nitrogen (N)	2026/08/28	NC		%	20
C391669	JGL	Matrix Spike [ELM804-09]	Total Phosphorus (P)	2026/08/29		115	%	N/A
C391669	JGL	Spiked Blank	Total Phosphorus (P)	2026/08/29		116	%	80 - 120
C391669	JGL	Method Blank	Total Phosphorus (P)	2026/08/29	0.0014, RDL=0.0010		mg/L	
C391669	JGL	RPD [ELM804-09]	Total Phosphorus (P)	2026/08/29	NC		%	20
C391711	AC2	Matrix Spike	1,4-Difluorobenzene (sur.)	2026/08/28		100	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/28		89	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/28		111	%	50 - 140



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C391711	AC2	Spiked Blank	1,1,1,2-tetrachloroethane	2026/08/28		108	%	50 - 140
			1,1,1-trichloroethane	2026/08/28		111	%	50 - 140
			1,1,2,2-tetrachloroethane	2026/08/28		110	%	50 - 140
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/28		97	%	50 - 140
			1,1,2-trichloroethane	2026/08/28		102	%	50 - 140
			1,1-dichloroethane	2026/08/28		114	%	50 - 140
			1,1-dichloroethene	2026/08/28		97	%	50 - 140
			1,2,3-trichlorobenzene	2026/08/28		104	%	50 - 140
			1,2,4-trichlorobenzene	2026/08/28		99	%	50 - 140
			1,2-dibromoethane	2026/08/28		98	%	50 - 140
			1,2-dichlorobenzene	2026/08/28		106	%	50 - 140
			1,2-dichloroethane	2026/08/28		112	%	50 - 140
			1,2-dichloropropane	2026/08/28		110	%	50 - 140
			1,3,5-trimethylbenzene	2026/08/28		112	%	50 - 140
			1,3-Butadiene	2026/08/28		87	%	50 - 140
			1,3-dichlorobenzene	2026/08/28		108	%	50 - 140
			1,3-dichloropropane	2026/08/28		100	%	50 - 140
			1,4-dichlorobenzene	2026/08/28		106	%	50 - 140
			Benzene	2026/08/28		105	%	50 - 140
			Bromobenzene	2026/08/28		98	%	50 - 140
			Bromodichloromethane	2026/08/28		110	%	50 - 140
			Bromoform	2026/08/28		100	%	50 - 140
			Bromomethane	2026/08/28		102	%	50 - 140
			Carbon tetrachloride	2026/08/28		111	%	50 - 140
			Chlorobenzene	2026/08/28		95	%	50 - 140
			Dibromochloromethane	2026/08/28		103	%	50 - 140
			Chloroethane	2026/08/28		102	%	50 - 140
			Chloroform	2026/08/28		110	%	50 - 140
			Chloromethane	2026/08/28		86	%	50 - 140
			cis-1,2-dichloroethene	2026/08/28		95	%	50 - 140
			cis-1,3-dichloropropene	2026/08/28		108	%	50 - 140
			Dichlorodifluoromethane	2026/08/28		56	%	50 - 140
			Dichloromethane	2026/08/28		101	%	50 - 140
			Ethylbenzene	2026/08/28		105	%	50 - 140
			Hexachlorobutadiene	2026/08/28		110	%	50 - 140
			Isopropylbenzene	2026/08/28		97	%	50 - 140
			Methyl-tert-butylether (MTBE)	2026/08/28		82	%	50 - 140
			Styrene	2026/08/28		104	%	50 - 140
			Tetrachloroethene	2026/08/28		92	%	50 - 140
			Toluene	2026/08/28		96	%	50 - 140
			trans-1,2-dichloroethene	2026/08/28		102	%	50 - 140
			trans-1,3-dichloropropene	2026/08/28		112	%	50 - 140
			Trichloroethene	2026/08/28		96	%	50 - 140
			Trichlorofluoromethane	2026/08/28		103	%	50 - 140
			Vinyl chloride	2026/08/28		92	%	50 - 140
			m & p-Xylene	2026/08/28		114	%	50 - 140
			o-Xylene	2026/08/28		103	%	50 - 140
			1,4-Difluorobenzene (sur.)	2026/08/28		97	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/28		88	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/28		105	%	50 - 140
			VH C6-C10	2026/08/28		110	%	70 - 130
			1,1,1,2-tetrachloroethane	2026/08/28		97	%	60 - 130
			1,1,1-trichloroethane	2026/08/28		107	%	60 - 130



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			1,1,2,2-tetrachloroethane	2026/08/28		108	%	60 - 130
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/28		93	%	60 - 130
			1,1,2-trichloroethane	2026/08/28		96	%	60 - 130
			1,1-dichloroethane	2026/08/28		111	%	60 - 130
			1,1-dichloroethene	2026/08/28		96	%	60 - 130
			1,2,3-trichlorobenzene	2026/08/28		102	%	60 - 130
			1,2,4-trichlorobenzene	2026/08/28		99	%	60 - 130
			1,2-dibromoethane	2026/08/28		96	%	60 - 130
			1,2-dichlorobenzene	2026/08/28		106	%	60 - 130
			1,2-dichloroethane	2026/08/28		108	%	60 - 130
			1,2-dichloropropane	2026/08/28		106	%	60 - 130
			1,3,5-trimethylbenzene	2026/08/28		114	%	60 - 130
			1,3-Butadiene	2026/08/28		85	%	50 - 140
			1,3-dichlorobenzene	2026/08/28		109	%	60 - 130
			1,3-dichloropropane	2026/08/28		97	%	60 - 130
			1,4-dichlorobenzene	2026/08/28		107	%	60 - 130
			Benzene	2026/08/28		106	%	60 - 130
			Bromobenzene	2026/08/28		99	%	60 - 130
			Bromodichloromethane	2026/08/28		107	%	60 - 130
			Bromoform	2026/08/28		96	%	60 - 130
			Bromomethane	2026/08/28		96	%	50 - 140
			Carbon tetrachloride	2026/08/28		106	%	60 - 130
			Chlorobenzene	2026/08/28		95	%	60 - 130
			Dibromochloromethane	2026/08/28		98	%	60 - 130
			Chloroethane	2026/08/28		92	%	50 - 140
			Chloroform	2026/08/28		106	%	60 - 130
			Chloromethane	2026/08/28		85	%	50 - 140
			cis-1,2-dichloroethene	2026/08/28		93	%	60 - 130
			cis-1,3-dichloropropene	2026/08/28		101	%	50 - 140
			Dichlorodifluoromethane	2026/08/28		55	%	50 - 140
			Dichloromethane	2026/08/28		97	%	60 - 130
			Ethylbenzene	2026/08/28		103	%	60 - 130
			Hexachlorobutadiene	2026/08/28		108	%	60 - 130
			Isopropylbenzene	2026/08/28		99	%	60 - 130
			Methyl-tert-butylether (MTBE)	2026/08/28		83	%	60 - 130
			Styrene	2026/08/28		103	%	60 - 130
			Tetrachloroethene	2026/08/28		92	%	60 - 130
			Toluene	2026/08/28		95	%	60 - 130
			trans-1,2-dichloroethene	2026/08/28		102	%	60 - 130
			trans-1,3-dichloropropene	2026/08/28		100	%	50 - 140
			Trichloroethene	2026/08/28		93	%	60 - 130
			Trichlorofluoromethane	2026/08/28		100	%	60 - 130
			Vinyl chloride	2026/08/28		91	%	50 - 140
			m & p-Xylene	2026/08/28		113	%	60 - 130
			o-Xylene	2026/08/28		103	%	60 - 130
C391711	AC2	Method Blank	1,4-Difluorobenzene (sur.)	2026/08/28		101	%	50 - 140
			4-Bromofluorobenzene (sur.)	2026/08/28		77	%	50 - 140
			D4-1,2-Dichloroethane (sur.)	2026/08/28		104	%	50 - 140
			VH C6-C10	2026/08/28	ND, RDL=300		ug/L	
			1,1,1,2-tetrachloroethane	2026/08/28	ND, RDL=0.50		ug/L	



QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			1,1,1-trichloroethane	2026/08/28	ND, RDL=0.50		ug/L	
			1,1,2,2-tetrachloroethane	2026/08/28	ND, RDL=0.50		ug/L	
			1,1,2Trichloro-1,2,2Trifluoroethane	2026/08/28	ND, RDL=2.0		ug/L	
			1,1,2-trichloroethane	2026/08/28	ND, RDL=0.50		ug/L	
			1,1-dichloroethane	2026/08/28	ND, RDL=0.50		ug/L	
			1,1-dichloroethene	2026/08/28	ND, RDL=0.50		ug/L	
			1,2,3-trichlorobenzene	2026/08/28	ND, RDL=2.0		ug/L	
			1,2,4-trichlorobenzene	2026/08/28	ND, RDL=2.0		ug/L	
			1,2-dibromoethane	2026/08/28	ND, RDL=0.20		ug/L	
			1,2-dichlorobenzene	2026/08/28	ND, RDL=0.50		ug/L	
			1,2-dichloroethane	2026/08/28	ND, RDL=0.50		ug/L	
			1,2-dichloropropane	2026/08/28	ND, RDL=0.50		ug/L	
			1,3,5-trimethylbenzene	2026/08/28	ND, RDL=2.0		ug/L	
			1,3-Butadiene	2026/08/28	ND, RDL=0.50		ug/L	
			1,3-dichlorobenzene	2026/08/28	ND, RDL=0.50		ug/L	
			1,3-dichloropropane	2026/08/28	ND, RDL=1.0		ug/L	
			1,4-dichlorobenzene	2026/08/28	ND, RDL=0.50		ug/L	
			Benzene	2026/08/28	ND, RDL=0.40		ug/L	
			Bromobenzene	2026/08/28	ND, RDL=2.0		ug/L	
			Bromodichloromethane	2026/08/28	ND, RDL=1.0		ug/L	
			Bromoform	2026/08/28	ND, RDL=1.0		ug/L	
			Bromomethane	2026/08/28	ND, RDL=1.0		ug/L	
			Carbon tetrachloride	2026/08/28	ND, RDL=0.50		ug/L	
			Chlorobenzene	2026/08/28	ND, RDL=0.50		ug/L	
			Dibromochloromethane	2026/08/28	ND, RDL=1.0		ug/L	
			Chloroethane	2026/08/28	ND, RDL=1.0		ug/L	
			Chloroform	2026/08/28	ND, RDL=1.0		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Chloromethane	2026/08/28	ND, RDL=1.0		ug/L	
			cis-1,2-dichloroethene	2026/08/28	ND, RDL=1.0		ug/L	
			cis-1,3-dichloropropene	2026/08/28	ND, RDL=1.0		ug/L	
			Dichlorodifluoromethane	2026/08/28	ND, RDL=2.0		ug/L	
			Dichloromethane	2026/08/28	ND, RDL=2.0		ug/L	
			Ethylbenzene	2026/08/28	ND, RDL=0.40		ug/L	
			Hexachlorobutadiene	2026/08/28	ND, RDL=0.50		ug/L	
			Isopropylbenzene	2026/08/28	ND, RDL=2.0		ug/L	
			Methyl-tert-butylether (MTBE)	2026/08/28	ND, RDL=4.0		ug/L	
			Styrene	2026/08/28	ND, RDL=0.50		ug/L	
			Tetrachloroethene	2026/08/28	ND, RDL=0.50		ug/L	
			Toluene	2026/08/28	ND, RDL=0.40		ug/L	
			trans-1,2-dichloroethene	2026/08/28	ND, RDL=1.0		ug/L	
			trans-1,3-dichloropropene	2026/08/28	ND, RDL=1.0		ug/L	
			Trichloroethene	2026/08/28	ND, RDL=0.50		ug/L	
			Trichlorofluoromethane	2026/08/28	ND, RDL=4.0		ug/L	
			Vinyl chloride	2026/08/28	ND, RDL=0.50		ug/L	
			m & p-Xylene	2026/08/28	ND, RDL=0.40		ug/L	
			o-Xylene	2026/08/28	ND, RDL=0.40		ug/L	
			Xylenes (Total)	2026/08/28	ND, RDL=0.40		ug/L	
C391711	AC2	RPD	1,2-dichloroethane	2026/08/28	NC		%	30
			Benzene	2026/08/28	NC		%	30
C392159	AAX	Matrix Spike	Methyl Sulfone (sur.)	2026/08/27		135	%	50 - 140
			Ethylene Glycol	2026/08/27		122	%	60 - 140
			Diethylene Glycol	2026/08/27		139	%	60 - 140
			Triethylene Glycol	2026/08/27		134	%	60 - 140
			Propylene Glycol	2026/08/27		122	%	60 - 140
C392159	AAX	Spiked Blank	Methyl Sulfone (sur.)	2026/08/28		96	%	50 - 140
			Ethylene Glycol	2026/08/28		72	%	70 - 130
			Diethylene Glycol	2026/08/28		97	%	70 - 130
			Triethylene Glycol	2026/08/28		89	%	70 - 130
			Propylene Glycol	2026/08/28		78	%	70 - 130
C392159	AAX	Method Blank	Methyl Sulfone (sur.)	2026/08/27		160 (1)	%	50 - 140



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
			Ethylene Glycol	2026/08/27	ND, RDL=3.0		mg/L	
			Diethylene Glycol	2026/08/27	ND, RDL=5.0		mg/L	
			Triethylene Glycol	2026/08/27	ND, RDL=5.0		mg/L	
			Propylene Glycol	2026/08/27	ND, RDL=5.0		mg/L	
C392159	AAX	RPD	Ethylene Glycol	2026/08/27	NC		%	30
			Diethylene Glycol	2026/08/27	NC		%	30
			Triethylene Glycol	2026/08/27	NC		%	30
			Propylene Glycol	2026/08/27	NC		%	30
C392160	DSX	Matrix Spike	Total Sulphide	2026/08/28		35 (1)	%	80 - 120
C392160	DSX	Spiked Blank	Total Sulphide	2026/08/28		99	%	80 - 120
C392160	DSX	Method Blank	Total Sulphide	2026/08/28	ND, RDL=0.0018		mg/L	
C392160	DSX	RPD	Total Sulphide	2026/08/28	NC		%	20
C392250	SPP	Matrix Spike	Total Suspended Solids	2026/08/28		103	%	80 - 120
C392250	SPP	Spiked Blank	Total Suspended Solids	2026/08/28		102	%	80 - 120
C392250	SPP	Method Blank	Total Suspended Solids	2026/08/28	ND, RDL=1.0		mg/L	
C392250	SPP	RPD	Total Suspended Solids	2026/08/28	0		%	20
C393094	AA1	Matrix Spike	Dissolved Aluminum (Al)	2026/08/28		99	%	80 - 120
			Dissolved Antimony (Sb)	2026/08/28		102	%	80 - 120
			Dissolved Arsenic (As)	2026/08/28		102	%	80 - 120
			Dissolved Barium (Ba)	2026/08/28		99	%	80 - 120
			Dissolved Beryllium (Be)	2026/08/28		101	%	80 - 120
			Dissolved Bismuth (Bi)	2026/08/28		98	%	80 - 120
			Dissolved Boron (B)	2026/08/28		102	%	80 - 120
			Dissolved Cadmium (Cd)	2026/08/28		101	%	80 - 120
			Dissolved Cesium (Cs)	2026/08/28		98	%	80 - 120
			Dissolved Chromium (Cr)	2026/08/28		97	%	80 - 120
			Dissolved Cobalt (Co)	2026/08/28		95	%	80 - 120
			Dissolved Copper (Cu)	2026/08/28		93	%	80 - 120
			Dissolved Iron (Fe)	2026/08/28		100	%	80 - 120
			Dissolved Lead (Pb)	2026/08/28		93	%	80 - 120
			Dissolved Lithium (Li)	2026/08/28		96	%	80 - 120
			Dissolved Manganese (Mn)	2026/08/28		NC	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/08/28		106	%	80 - 120
			Dissolved Nickel (Ni)	2026/08/28		94	%	80 - 120
			Dissolved Phosphorus (P)	2026/08/28		102	%	80 - 120
			Dissolved Rubidium (Rb)	2026/08/28		103	%	80 - 120
			Dissolved Selenium (Se)	2026/08/28		101	%	80 - 120
			Dissolved Silicon (Si)	2026/08/28		96	%	80 - 120
			Dissolved Silver (Ag)	2026/08/28		101	%	80 - 120
			Dissolved Strontium (Sr)	2026/08/28		NC	%	80 - 120
			Dissolved Tellurium (Te)	2026/08/28		105	%	80 - 120
			Dissolved Thallium (Tl)	2026/08/28		98	%	80 - 120
			Dissolved Thorium (Th)	2026/08/28		103	%	80 - 120
			Dissolved Tin (Sn)	2026/08/28		100	%	80 - 120
			Dissolved Titanium (Ti)	2026/08/28		100	%	80 - 120
			Dissolved Uranium (U)	2026/08/28		90	%	80 - 120
			Dissolved Vanadium (V)	2026/08/28		99	%	80 - 120



QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C393094	AA1	Spiked Blank	Dissolved Zinc (Zn)	2026/08/28		97	%	80 - 120
			Dissolved Zirconium (Zr)	2026/08/28		105	%	80 - 120
			Dissolved Aluminum (Al)	2026/08/28		106	%	80 - 120
			Dissolved Antimony (Sb)	2026/08/28		106	%	80 - 120
			Dissolved Arsenic (As)	2026/08/28		106	%	80 - 120
			Dissolved Barium (Ba)	2026/08/28		104	%	80 - 120
			Dissolved Beryllium (Be)	2026/08/28		109	%	80 - 120
			Dissolved Bismuth (Bi)	2026/08/28		104	%	80 - 120
			Dissolved Boron (B)	2026/08/28		111	%	80 - 120
			Dissolved Cadmium (Cd)	2026/08/28		104	%	80 - 120
			Dissolved Cesium (Cs)	2026/08/28		105	%	80 - 120
			Dissolved Chromium (Cr)	2026/08/28		104	%	80 - 120
			Dissolved Cobalt (Co)	2026/08/28		102	%	80 - 120
			Dissolved Copper (Cu)	2026/08/28		100	%	80 - 120
			Dissolved Iron (Fe)	2026/08/28		105	%	80 - 120
			Dissolved Lead (Pb)	2026/08/28		99	%	80 - 120
			Dissolved Lithium (Li)	2026/08/28		103	%	80 - 120
			Dissolved Manganese (Mn)	2026/08/28		102	%	80 - 120
			Dissolved Molybdenum (Mo)	2026/08/28		109	%	80 - 120
			Dissolved Nickel (Ni)	2026/08/28		101	%	80 - 120
			Dissolved Phosphorus (P)	2026/08/28		107	%	80 - 120
			Dissolved Rubidium (Rb)	2026/08/28		106	%	80 - 120
			Dissolved Selenium (Se)	2026/08/28		103	%	80 - 120
			Dissolved Silicon (Si)	2026/08/28		112	%	80 - 120
			Dissolved Silver (Ag)	2026/08/28		104	%	80 - 120
			Dissolved Strontium (Sr)	2026/08/28		108	%	80 - 120
			Dissolved Tellurium (Te)	2026/08/28		105	%	80 - 120
			Dissolved Thallium (Tl)	2026/08/28		103	%	80 - 120
			Dissolved Thorium (Th)	2026/08/28		104	%	80 - 120
			Dissolved Tin (Sn)	2026/08/28		105	%	80 - 120
			Dissolved Titanium (Ti)	2026/08/28		107	%	80 - 120
			Dissolved Uranium (U)	2026/08/28		91	%	80 - 120
			Dissolved Vanadium (V)	2026/08/28		103	%	80 - 120
			Dissolved Zinc (Zn)	2026/08/28		104	%	80 - 120
			Dissolved Zirconium (Zr)	2026/08/28		107	%	80 - 120
C393094	AA1	Method Blank	Dissolved Aluminum (Al)	2026/08/28	ND, RDL=0.50		ug/L	
			Dissolved Antimony (Sb)	2026/08/28	ND, RDL=0.020		ug/L	
			Dissolved Arsenic (As)	2026/08/28	ND, RDL=0.020		ug/L	
			Dissolved Barium (Ba)	2026/08/28	ND, RDL=0.020		ug/L	
			Dissolved Beryllium (Be)	2026/08/28	ND, RDL=0.010		ug/L	
			Dissolved Bismuth (Bi)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Boron (B)	2026/08/28	ND, RDL=10		ug/L	
			Dissolved Cadmium (Cd)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Cesium (Cs)	2026/08/28	ND, RDL=0.050		ug/L	



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C393094	AA1	RPD	Dissolved Chromium (Cr)	2026/08/28	ND, RDL=0.10		ug/L	
			Dissolved Cobalt (Co)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Copper (Cu)	2026/08/28	ND, RDL=0.050		ug/L	
			Dissolved Iron (Fe)	2026/08/28	ND, RDL=1.0		ug/L	
			Dissolved Lead (Pb)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Lithium (Li)	2026/08/28	ND, RDL=0.50		ug/L	
			Dissolved Manganese (Mn)	2026/08/28	ND, RDL=0.050		ug/L	
			Dissolved Molybdenum (Mo)	2026/08/28	ND, RDL=0.050		ug/L	
			Dissolved Nickel (Ni)	2026/08/28	ND, RDL=0.020		ug/L	
			Dissolved Phosphorus (P)	2026/08/28	ND, RDL=2.0		ug/L	
			Dissolved Rubidium (Rb)	2026/08/28	ND, RDL=0.050		ug/L	
			Dissolved Selenium (Se)	2026/08/28	ND, RDL=0.040		ug/L	
			Dissolved Silicon (Si)	2026/08/28	ND, RDL=50		ug/L	
			Dissolved Silver (Ag)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Strontium (Sr)	2026/08/28	ND, RDL=0.050		ug/L	
			Dissolved Tellurium (Te)	2026/08/28	ND, RDL=0.020		ug/L	
			Dissolved Thallium (Tl)	2026/08/28	ND, RDL=0.0020		ug/L	
			Dissolved Thorium (Th)	2026/08/28	ND, RDL=0.0050		ug/L	
			Dissolved Tin (Sn)	2026/08/28	ND, RDL=0.20		ug/L	
			Dissolved Titanium (Ti)	2026/08/28	ND, RDL=0.50		ug/L	
			Dissolved Uranium (U)	2026/08/28	ND, RDL=0.0020		ug/L	
			Dissolved Vanadium (V)	2026/08/28	ND, RDL=0.20		ug/L	
			Dissolved Zinc (Zn)	2026/08/28	ND, RDL=0.10		ug/L	
			Dissolved Zirconium (Zr)	2026/08/28	ND, RDL=0.10		ug/L	
			Dissolved Aluminum (Al)	2026/08/28	9.8		%	20
			Dissolved Antimony (Sb)	2026/08/28	9.7		%	20
			Dissolved Arsenic (As)	2026/08/28	1.8		%	20
			Dissolved Barium (Ba)	2026/08/28	0.16		%	20
			Dissolved Beryllium (Be)	2026/08/28	NC		%	20
			Dissolved Bismuth (Bi)	2026/08/28	NC		%	20



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C393094	AA1	RPD [ELM804-07]	Dissolved Boron (B)	2026/08/28	NC		%	20
			Dissolved Cadmium (Cd)	2026/08/28	NC		%	20
			Dissolved Chromium (Cr)	2026/08/28	NC		%	20
			Dissolved Cobalt (Co)	2026/08/28	0.58		%	20
			Dissolved Copper (Cu)	2026/08/28	0.26		%	20
			Dissolved Iron (Fe)	2026/08/28	4.1		%	20
			Dissolved Lead (Pb)	2026/08/28	13		%	20
			Dissolved Lithium (Li)	2026/08/28	7.8		%	20
			Dissolved Manganese (Mn)	2026/08/28	0.75		%	20
			Dissolved Molybdenum (Mo)	2026/08/28	2.7		%	20
			Dissolved Nickel (Ni)	2026/08/28	12		%	20
			Dissolved Phosphorus (P)	2026/08/28	11		%	20
			Dissolved Selenium (Se)	2026/08/28	NC		%	20
			Dissolved Silicon (Si)	2026/08/28	1.9		%	20
			Dissolved Silver (Ag)	2026/08/28	NC		%	20
			Dissolved Strontium (Sr)	2026/08/28	0.28		%	20
			Dissolved Thallium (Tl)	2026/08/28	NC		%	20
			Dissolved Tin (Sn)	2026/08/28	NC		%	20
			Dissolved Titanium (Ti)	2026/08/28	NC		%	20
			Dissolved Uranium (U)	2026/08/28	2.0		%	20
			Dissolved Vanadium (V)	2026/08/28	0.38		%	20
			Dissolved Zinc (Zn)	2026/08/28	6.1		%	20
			Dissolved Zirconium (Zr)	2026/08/28	NC		%	20
			Dissolved Aluminum (Al)	2026/08/28	NC		%	20
			Dissolved Antimony (Sb)	2026/08/28	NC		%	20
			Dissolved Arsenic (As)	2026/08/28	NC		%	20
			Dissolved Barium (Ba)	2026/08/28	NC		%	20
			Dissolved Beryllium (Be)	2026/08/28	NC		%	20
			Dissolved Bismuth (Bi)	2026/08/28	NC		%	20
			Dissolved Boron (B)	2026/08/28	NC		%	20
			Dissolved Cadmium (Cd)	2026/08/28	NC		%	20
			Dissolved Cesium (Cs)	2026/08/28	NC		%	20
			Dissolved Chromium (Cr)	2026/08/28	NC		%	20
			Dissolved Cobalt (Co)	2026/08/28	NC		%	20
			Dissolved Copper (Cu)	2026/08/28	5.5		%	20
			Dissolved Iron (Fe)	2026/08/28	NC		%	20
			Dissolved Lead (Pb)	2026/08/28	3.2		%	20
			Dissolved Lithium (Li)	2026/08/28	NC		%	20
			Dissolved Manganese (Mn)	2026/08/28	NC		%	20
			Dissolved Molybdenum (Mo)	2026/08/28	NC		%	20
			Dissolved Nickel (Ni)	2026/08/28	NC		%	20
			Dissolved Phosphorus (P)	2026/08/28	NC		%	20
			Dissolved Rubidium (Rb)	2026/08/28	NC		%	20
			Dissolved Selenium (Se)	2026/08/28	NC		%	20
			Dissolved Silicon (Si)	2026/08/28	NC		%	20
			Dissolved Silver (Ag)	2026/08/28	NC		%	20
			Dissolved Strontium (Sr)	2026/08/28	NC		%	20
			Dissolved Tellurium (Te)	2026/08/28	NC		%	20
			Dissolved Thallium (Tl)	2026/08/28	NC		%	20
			Dissolved Thorium (Th)	2026/08/28	NC		%	20
			Dissolved Tin (Sn)	2026/08/28	NC		%	20
			Dissolved Titanium (Ti)	2026/08/28	NC		%	20
			Dissolved Uranium (U)	2026/08/28	NC		%	20



Bureau Veritas Job #: C654848

Report Date: 2026/09/09

HATFIELD CONSULTANTS

Client Project #: FORTIS11234/PE110163

Site Location: WOODFIBRE PIPELINE PROJECT

Your P.O. #: 4800010213

QUALITY ASSURANCE REPORT(CONT'D)

QA/QC Batch	Init	QC Type	Parameter	Date Analyzed	Value	Recovery	UNITS	QC Limits
C393198	JLD	Matrix Spike [ELM806-13]	Dissolved Vanadium (V)	2026/08/28	NC		%	20
			Dissolved Zinc (Zn)	2026/08/28	0.35		%	20
			Dissolved Zirconium (Zr)	2026/08/28	NC		%	20
			Phenols	2026/08/28		102	%	80 - 120
			Phenols	2026/08/28		100	%	80 - 120
C393198	JLD	Method Blank	Phenols	2026/08/28	ND, RDL=0.0015		mg/L	
C393198	JLD	RPD [ELM806-13]	Phenols	2026/08/28	NC		%	20
C393252	C2L	Matrix Spike	Total Mercury (Hg)	2026/08/28		112	%	80 - 120
C393252	C2L	Spiked Blank	Total Mercury (Hg)	2026/08/28		89	%	80 - 120
C393252	C2L	Method Blank	Total Mercury (Hg)	2026/08/28	ND, RDL=0.0019		ug/L	
C393252	C2L	RPD	Total Mercury (Hg)	2026/08/28	NC		%	20
C393648	CJY	Matrix Spike	Total Organic Carbon (C)	2026/08/28		104	%	80 - 120
C393648	CJY	Spiked Blank	Total Organic Carbon (C)	2026/08/28		96	%	80 - 120
C393648	CJY	Method Blank	Total Organic Carbon (C)	2026/08/28	ND, RDL=0.50		mg/L	
C393648	CJY	RPD	Total Organic Carbon (C)	2026/08/28	9.3		%	20
C393998	C2L	Matrix Spike	Total Mercury (Hg)	2026/08/28		107	%	80 - 120
C393998	C2L	Spiked Blank	Total Mercury (Hg)	2026/08/28		96	%	80 - 120
C393998	C2L	Method Blank	Total Mercury (Hg)	2026/08/28	ND, RDL=0.0019		ug/L	
C393998	C2L	RPD	Total Mercury (Hg)	2026/08/28	NC		%	20
C394071	CJY	Spiked Blank	Dissolved Organic Carbon (C)	2026/08/29		96	%	80 - 120
C394071	CJY	Method Blank	Dissolved Organic Carbon (C)	2026/08/29	ND, RDL=0.50		mg/L	
C394095	CJY	Matrix Spike	Total Organic Carbon (C)	2026/08/29		111	%	80 - 120
C394095	CJY	Spiked Blank	Total Organic Carbon (C)	2026/08/29		96	%	80 - 120
C394095	CJY	Method Blank	Total Organic Carbon (C)	2026/08/29	ND, RDL=0.50		mg/L	
C394095	CJY	RPD	Total Organic Carbon (C)	2026/08/29	NC		%	20
C395272	MEM	Matrix Spike [ELM801-08]	Dissolved Mercury (Hg)	2026/08/31		110	%	80 - 120
C395272	MEM	Spiked Blank	Dissolved Mercury (Hg)	2026/08/31		91	%	80 - 120
C395272	MEM	Method Blank	Dissolved Mercury (Hg)	2026/08/31	ND, RDL=0.0019		ug/L	
C395272	MEM	RPD [ELM801-08]	Dissolved Mercury (Hg)	2026/08/31	NC		%	20

N/A = Not Applicable

Duplicate: Paired analysis of a separate portion of the same sample. Used to evaluate the variance in the measurement.

Matrix Spike: A sample to which a known amount of the analyte of interest has been added. Used to evaluate sample matrix interference.

Spiked Blank: A blank matrix sample to which a known amount of the analyte, usually from a second source, has been added. Used to evaluate method accuracy.

Method Blank: A blank matrix containing all reagents used in the analytical procedure. Used to identify laboratory contamination.

Surrogate: A pure or isotopically labeled compound whose behavior mirrors the analytes of interest. Used to evaluate extraction efficiency.

NC (Matrix Spike): The recovery in the matrix spike was not calculated. The relative difference between the concentration in the parent sample and the spike amount was too small to permit a reliable recovery calculation (matrix spike concentration was less than the native sample concentration)

NC (Duplicate RPD): The duplicate RPD was not calculated. The concentration in the sample and/or duplicate was too low to permit a reliable RPD calculation (absolute difference <= 2x RDL).

(1) Recovery or RPD for this parameter is outside control limits. The overall quality control for this analysis meets acceptability criteria.



Bureau Veritas Job #: C654848
Report Date: 2026/09/09

HATFIELD CONSULTANTS
Client Project #: FORTIS11234/PE110163
Site Location: WOODFIBRE PIPELINE PROJECT
Your P.O. #: 4800010213

VALIDATION SIGNATURE PAGE

The analytical data and all QC contained in this report were reviewed and validated by:

David Huang, M.Sc., P.Chem., QP, Scientific Services Manager

Levi Manchak, Senior Project Manager

Melissa Thompson, Scientist

Pushpa Gurung, Laboratory Supervisor

Suwan (Sze Yeung) Fock, B.Sc., Scientific Specialist

Bureau Veritas Certified by Ghayasuddin Khan, M.Sc., P.Chem., QP, Scientific Specialist, Inorganics

Bureau Veritas has procedures in place to guard against improper use of the electronic signature and have the required "signatories", as per ISO/IEC 17025, signing the reports. For Service Group specific validation, please refer to the Validation Signatures page if included, otherwise available by request. For Department specific Analyst/Supervisor validation names, please refer to the Test Summary section if included, otherwise available by request. This report is authorized by Rob Gilbert, BBY General Manager responsible for British Columbia Environmental laboratory operations.



Custody Tracking Form

eCOC Number
W 139719

Please use this form for custody tracking when submitting the work instructions via eCOC (electronic Chain of Custody). Please ensure your form has a barcode or a Bureau Veritas eCOC confirmation number in the top right hand side. This number links your electronic submission to your samples. This form should be placed in the cooler with your samples.

Relinquished By			Received By		
Brandon Garrett		Date: 2026/08/25 Time (24 HR): 14:06	Nadia Lawora		Date: 2026/08/25 Time (24 HR): 14:10
		Date:			Date:
		Time (24 HR):			Time (24 HR):
		Date:			Date:
		Time (24 HR):			Time (24 HR):

Unless otherwise agreed to, submissions and use of services are governed by Bureau Veritas' standard terms and conditions which can be found at www.bvna.com.



Trace Information																																	
Sampled By (Print):	# of Coolers/Plugs:	Immediate Test: ☐	Rush: ☐																														
			Micro: ☐																														
*** Laboratory Use Only ***																																	
Received At:	Lab Comments:	<table border="1"> <thead> <tr> <th colspan="2">Custody Seal</th> <th>Cooling Media</th> <th colspan="3">Temperature °C</th> </tr> <tr> <th>Present (Y/N)</th> <th>Intact (Y/N)</th> <th>Present (Y/N)</th> <th>1</th> <th>2</th> <th>3</th> </tr> </thead> <tbody> <tr> <td>N</td> <td>N</td> <td>Y</td> <td>14</td> <td>14</td> <td>15</td> </tr> <tr> <td>N</td> <td>N</td> <td>Y</td> <td>16</td> <td>17</td> <td>15</td> </tr> <tr> <td>N</td> <td>N</td> <td>Y</td> <td>16</td> <td>17</td> <td>17</td> </tr> </tbody> </table>		Custody Seal		Cooling Media	Temperature °C			Present (Y/N)	Intact (Y/N)	Present (Y/N)	1	2	3	N	N	Y	14	14	15	N	N	Y	16	17	15	N	N	Y	16	17	17
Custody Seal		Cooling Media	Temperature °C																														
Present (Y/N)	Intact (Y/N)	Present (Y/N)	1	2	3																												
N	N	Y	14	14	15																												
N	N	Y	16	17	15																												
N	N	Y	16	17	17																												



MVAN-2026-08-1832



COR FCD-00340 / 7
PAGE 1 of 1

EPH in Water when PAH required Chromatogram

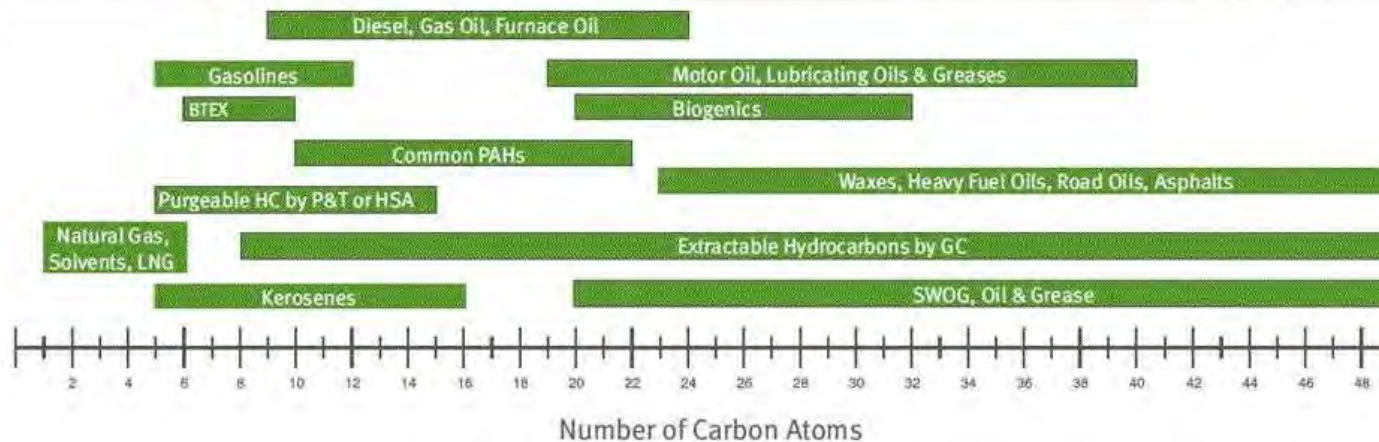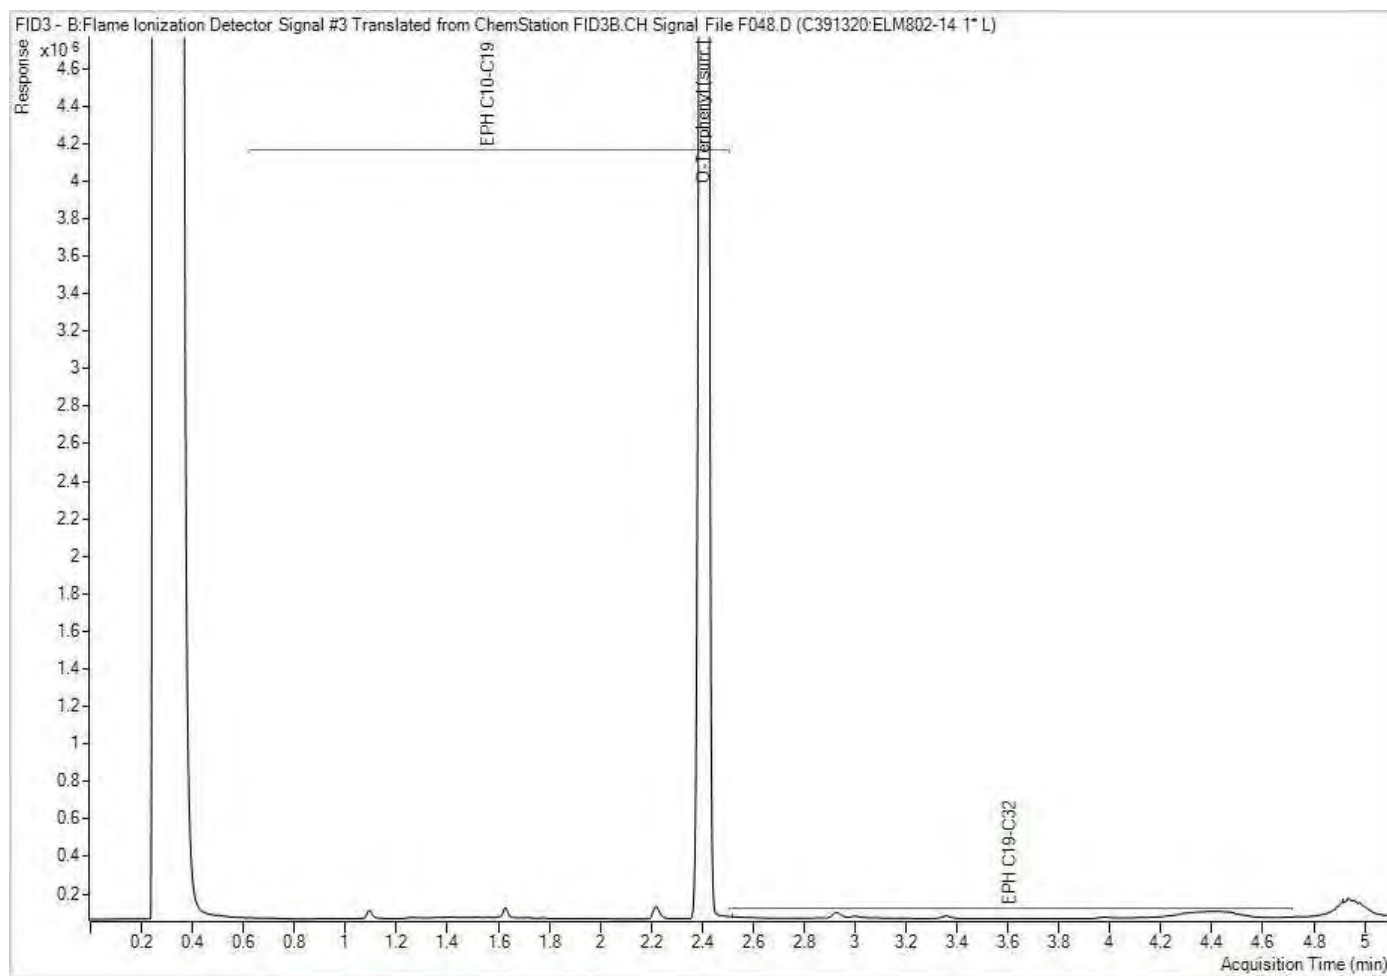

Note: This information is provided for reference purposes only. Should detailed chemist interpretation or fingerprinting be required, please contact the laboratory.


EPH in Water when PAH required Chromatogram

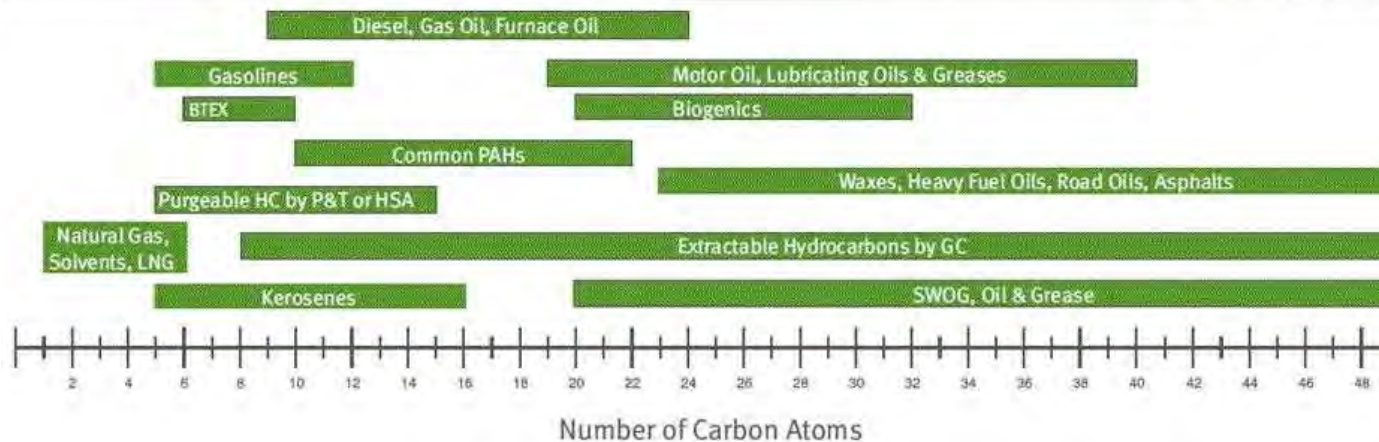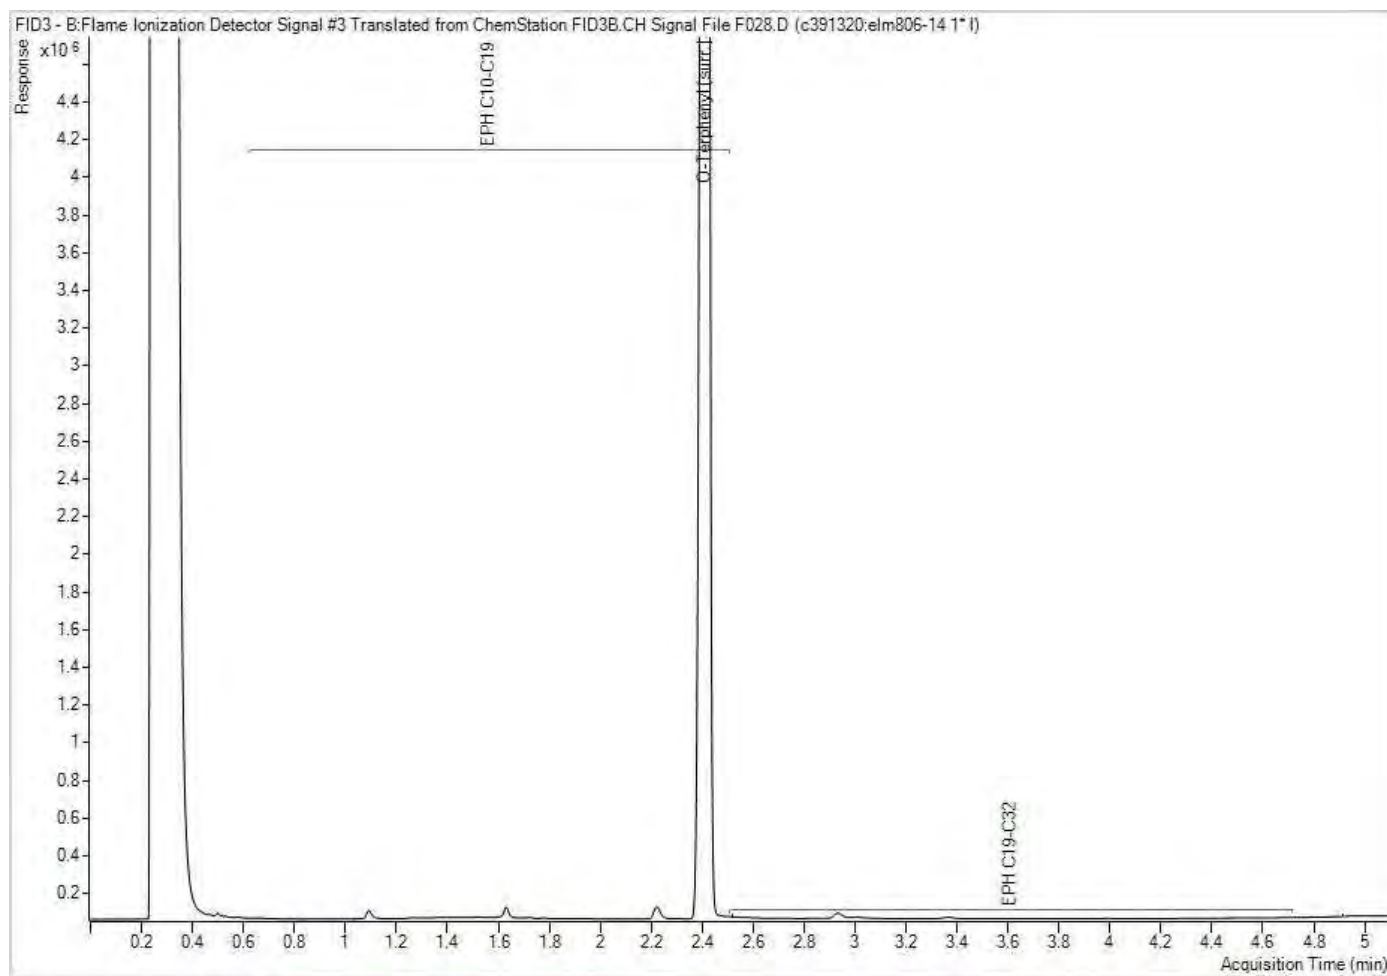

Note: This information is provided for reference purposes only. Should detailed chemist interpretation or fingerprinting be required, please contact the laboratory.



eCOC: W139719



Project Information: C654848
Job Received: 2026/08/25 14:10
Expected TAT: Standard TAT
Expected Arrival: 2026/08/25 15:30
Submitted By: Sam Wolf
Submitted To: Burnaby ENV: 4606
Canada Way

Invoice Information

Attn: Accounts Payable
Fortis BC Energy Inc
16705 Fraser Hwy
Surrey , BC , V4N 0E8
Email to:
einvoices@fortisbc.com

Report Information

Attn: Brett Lucas
HATFIELD CONSULTANTS
200-850 Harbourside Dr
North Vancouver , BC , V7P 0A3
Email to:
blucas@hatfieldgroup.com
danielle.samels@fortisbc.com
smangwani@hatfieldgroup.com
swolf@hatfieldgroup.com

Project Information

Quote #: C50083
PO/AFE#: 4800010213
Project #: Fortis11234/PE-110163
Site Location: Woodfibre Pipeline Project

Analytical Summary

A: Standard TAT

Client Sample ID	Clnt Ref	Sampling Date/Time	Matrix	#Cont	Woodfibre	Woodfibre Additional	Woodfibre Blank	Daphnia Magna LC50 Multi-concentration	Rainbow Trout LC50 Multi-concentration	Set Number
WLNG-DS	1	2026/08/25	WATER	14	A					1
WLNG -EOP	2	2026/08/25	WATER	24	A	A		A	A	2
WLNG-US	3	2026/08/25	WATER	14	A					1
Field Blank	4	2026/08/25	WATER	14			A			3
Trip Blank	5	2026/08/25	WATER	14			A			3
DUP	6	2026/08/25	WATER	18	A	A				4

Deadlines are estimates only and are subject to change. Please refer to your Job Confirmation report for final due dates.

Submission Information

of Samples: 6

Sample Set Listing

Set 1 (2 samples)	Set 2 (1 sample)	Set 3 (2 samples)	Set 4 (1 sample)
WLNG-DS WLNG-US	WLNG -EOP	Field Blank Trip Blank	DUP



RESULTS OF RAINBOW TROUT LC50 MULTI-CONCENTRATION

Client : 12239 Fortis BC Energy Inc, Surrey **Job Number:** C654848
Client Project Name & Number: WOODFIBRE PIPELINE PROJECT FORTIS11234/PE110163

Test Result:

96 hrs LC50 % vol/vol (95% CL): >100% (N/A) **Statistical Method:** Visual

Sample Name : WLNG -EOP

Description: Clear and colourless **Sample Number:** ELM802-18
Sample Collected: Aug 25, 2026 **Sampling Method :** N/A **Site Collection:** N/A
Sample Collected By: N/A **Volume Received:** 4 x ECO10 **Avg Temp Arrival:** 16 °C **Storage:** 2-6°C
Sample Received: Aug 25, 2026 02:10 PM **pH:** 7.5 **Dissolved Oxygen:** 10.0 mg/L
Analysis Start : Aug 27, 2026 01:52 PM **Temperature :** 15 °C **Sample Conductance:** 209 µS/cm

Concentration	Temperature (°C)	Temperature (°C)	Dissolved Oxygen (mg/L)	Dissolved Oxygen (mg/L)	pH	pH	Conductivity (uS/cm)	Mortality (#)	Mortality (%)	Atypical Behaviour (#)
% vol/vol	Initial	96 hrs	Initial	96 hrs	Initial	96 hrs	Initial	96 hrs	96 hrs	96 hrs
0	15	15	10.1	9.9	7.7	7.8	59	0	0	0
6.25	15	15	10.1	10.0	7.7	8.0	69	0	0	0
12.5	15	15	10.1	10.0	7.7	7.9	79	0	0	0
25	15	15	10.1	10.0	7.6	7.9	97	0	0	0
50	15	15	10.1	9.6	7.6	7.7	136	0	0	0
100	15	15	10.0	9.8	7.6	8.0	209	0	0	0

Comments : All fish appeared and behaved normally at 24 hours, 48 hours, 72 hours, and 96 hours into testing.
The reference toxicant test conducted for this batch of fish was outside 2 standard deviations of the historical mean but within 3 standard deviations (0.09, 0.47) mg/L. There was nothing unusual about the reference toxicant test or with the culture prior to testing; therefore, the point was kept in the control chart.

Culture/Control/Dilution Water

Burnaby Municipal Dechlorinated Water

Hardness: 22 mg/L CaCO₃ **Other parameters available on request.**

Test Conditions

Test concentration : 0,6.25,12.5,25,50,100 (% vol/vol)

Organisms per Vessel : 10 **Test Temperature :** 15 ± 1 °C **Solution Depth :** >15 cm
Total # of Organisms Used : 60 **Pre-aeration Time :** 30 min. **Rate of Aeration** 6.5±1 mL/(min*L)
Test Volume : 15 L **Vessel Volume :** 20L **Test pH Adjusted:** No
Loading Density : 0.3 g/L **Photoperiod :** 16:8 (light: dark)

Test Organism :

Rainbow Trout (*Oncorhynchus mykiss*) **Source :** Aqua Farm

Culture Temperature : 15 ± 2 °C **Weight (Mean) +- SD :** 0.4 ± 0.2 g **Length (Mean) +- SD :** 3.78 ± 0.52 cm
Culture Water Renewal : ≥ 1L/min/kg fish **Weight (Range) :** 0.2 – 1.0 g **Length (Range) :** 3.10 – 5.00 cm
Culture Photoperiod : 16:8 (light: dark) **% Mortality within 7 days :** 0%
Feeding rate and frequency : daily: 1-5% biomass of trout. **Acclimation Time:** >14 days

Reference chemical:

Zinc

Test Date:

Aug 20, 2026

Test Endpoint 96 hrs LC50 (95% confidence interval) : 0.42 (0.33, 0.54)mg/L **Statistical Method :** Untrimmed Spearman-Kärber

Historical Mean LC50 (warning limits) : 0.21 (0.12, 0.36) mg/L **Concentration :** 0,0.04,0.08,0.16,0.32,0.64 mg/L

Test Method

BV Lab's BBY2SOP-00004 is based on the latest version of EPS 1/RM9 and EPS 1 /RM13.

Method Deviations : None.

Note: The results contained in this report refer only to the testing of the sample submitted. Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation, including the toxicity parameters reported herein. The conductivity, dissolved oxygen and pH data contained within the toxicity report are provided for information purposes and are not individually accredited parameters. This report may not be reproduced, except in its entirety, without the written approval of the laboratory.



RESULTS OF RAINBOW TROUT LC50 MULTI-CONCENTRATION

Client : 12239 Fortis BC Energy Inc, Surrey
Client Project Name & Number: WOODFIBRE PIPELINE PROJECT FORTIS11234/PE110163

Job Number: C654848
Sample Number: ELM802-18

Analyst : Dayna Lee, Donald Lai, Melanie Mazziotti, Melissa Thompson, Nayshan Blassnitz, Oscar Ma

A handwritten signature in black ink, appearing to read "Melissa Thompson", written over a horizontal line.

Verified By : Melissa Thompson, Scientist

Date: Sep 09, 2026 11:41 AM



RESULTS OF *DAPHNIA MAGNA* LC50 MULTI-CONCENTRATION

Client : 12239 Fortis BC Energy Inc, Surrey **Job Number:** C654848
Client Project Name & Number: WOODFIBRE PIPELINE PROJECT FORTIS11234/PE110163 **Sample Number:** ELM802-17

Test Result:

48 hrs LC50 % vol/vol (95% CL): >100% (N/A) **Statistical Method:** Visual

Sample Name : WLNG -EOP

Description:	Clear, colourless	<u>Sample Prior to Analysis:</u>
Sample Collected:	Aug 25, 2026	pH: 7.5
Sample Collected By:	N/A	Temperature : 20 °C
Sample Received:	Aug 25, 2026 02:10 PM	Dissolved Oxygen: 9.7 mg/L
Analysis Start :	Aug 26, 2026 02:57 PM	Sample Conductance: 204 µS/cm
End :	Aug 28, 2026 02:58 PM	Hardness: 76 mg CaCO ₃ /L

Concentration	Temperature (°C)	Temperature (°C)	Dissolved Oxygen (mg/L)	Dissolved Oxygen (mg/L)	pH	pH	Conductivity (uS/cm)	Mortality (#)	Mortality (%)	Immobility (#)
% vol/vol	Initial	48 hrs	Initial	48 hrs	Initial	48 hrs	Initial	48 hrs	48 hrs	48 hrs
0	19	19	9.0	9.0	8.2	8.2	338	0	0	0
6.25	19	19	9.0	9.0	8.1	8.2	329	0	0	0
12.5	19	19	9.1	9.0	8.1	8.2	328	0	0	0
25	19	19	9.1	9.0	8.1	8.2	311	0	0	0
50	19	19	9.1	9.0	8.0	8.2	277	0	0	0
100	19	19	9.3	9.1	7.7	8.1	206	0	0	0

Comments : All neonates appeared and behaved normally at 24 hours and 48 hours into testing

Culture/Control/Dilution Water:

Reconstituted Water-Moderately Hard

Hardness: 104 mg/L CaCO₃ Other parameters available on request.

Test Conditions

Test concentration : 0,6.25,12.5,25,50,100 (% vol/vol)

Organisms per Vessel :	10	Pre-aeration Time :	30 min	Rate of Pre-aeration :	25-50 mL/(min*L)
Total # of Organisms Used :	60	Test Temperature :	20 ± 2 °C	Test Hardness Adjusted :	No
Test Volume :	185 mL	Vessel Volume :	200 mL	Test pH Adjusted:	No
Loading Density :	18.5 mL/Daphnia	Photoperiod :	16:8 (light: dark)		

Test Organism :

Daphnia magna

Source : Aquatic Biosystems

Age at Test Initiation :	<24 hrs	Average Brood Size :	27.4
Culture Photoperiod :	16:8 (light: dark)	% Mortality within 7 days :	2.8
Culture Temperature :	20 ± 2 °C	Time To First Brood :	8 Days
Culture Diet	4 mL algae + 1 mL YCT; Sun. 2 mL algae + 0.5 mL YCT.		

Reference chemical:

Zinc

Test Date: Aug 19, 2026

Test Endpoint 48 hrs LC50 (95% confidence interval) : 0.28 (0.21, 0.38)mg/L

Statistical Method : Untrimmed Spearman-Kärber

Historical Mean LC50 (warning limits) : 0.58 (0.19, 1.78) mg/L

Concentration : 0,0.05,0.1,0.5,1,5,10 mg/L

Test Method

BV Labs' BBY2SOP-00007 is based on the latest version of EPS 1/RM/14.

Method Deviations: None.

Note: The results contained in this report refer only to the testing of the sample submitted. Bureau Veritas is accredited to ISO/IEC 17025 for specific parameters on scopes of accreditation, including the toxicity parameters reported herein. The conductivity, dissolved oxygen and pH data contained within the toxicity report are provided for information purposes and are not individually accredited parameters. This report may not be reproduced, except in its entirety, without the written approval of the laboratory.



RESULTS OF *DAPHNIA MAGNA* LC50 MULTI-CONCENTRATION

Client : 12239 Fortis BC Energy Inc, Surrey
Client Project Name & Number: WOODFIBRE PIPELINE PROJECT FORTIS11234/PE110163

Job Number: C654848
Sample Number: ELM802-17

Analyst : Jessica Hirschbold , Melanie Mazziotti

A handwritten signature in black ink, appearing to read "J. Hirschbold", written over a horizontal line.

Verified By : Melissa Thompson, Scientist

Date: Sep 09, 2026 12:31 PM
